

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
Brooklyn Public Library - Master Plan Phase II #09 May 2025					
Cashflow					
Summary					
Milestones and Make Ready Swing Space					
S-1030	Construction (All Phases)	804	620	05-Jul-24 A	05-Nov-27
S-1102	Exterior Renovations Complete	0	0		24-Jul-25
S-1118	Chiller Installation Complete	0	0		03-Dec-26
S-1221	BPL Master Plan Phase 2 Project Substantial Completion	0	0		05-Nov-27*
S-1231	Project Closeout	60	60	08-Nov-27	04-Feb-28
Areas Completion					
MILE-10	Project Area 8A Completed	0	0		05-Dec-25
MILE-10	Project Area 13 Completed	0	0		31-Dec-25
MILE-10	Project Area 12 Completed	0	0		02-Jan-26
MILE-10	Project Area 9 Completed	0	0		09-Jan-26
MILE-10	Project Area 7 Completed	0	0		27-Jul-26
MILE-10	Project Area 11 Completed	0	0		08-Sep-26
MILE-10	Project Area 10 Completed	0	0		26-Jan-27
MILE-10	Project Area 5 Completed	0	0		17-Feb-27
MILE-10	Project Area 8B Completed	0	0		30-Jul-27
MILE-10	Project Area 6 Completed	0	0		21-Oct-27
Staff and Book Collection Swing Space Schedule					
Project Area 8A					
SW-1040	Move Staff from Swing Space PA 10 to Completed PA 8A	5	5	01-Dec-25	05-Dec-25
Project Area 9					
SW-1060	MoveBook Collection & Staff into Area 9	5	5	05-Jan-26	09-Jan-26
Project Area 12 & 13					
SW-1050	Move Staff from Swing Space PA 10 to Completed PA 12	7	7	23-Dec-25	02-Jan-26
Project Area 7					
SW-1070	Move Book Collection To BC & Staff from PA 7 to Swing Space PA 10	5	5	12-Jan-26	16-Jan-26
SW-1090	Move SST Stacks back to Completed Space Area 7	5	5	21-Jul-26	27-Jul-26
Project Area 11					
SW-1080	Move Staff from PA 11 to Swing Space PA 10	7	7	05-Jan-26	13-Jan-26
SW-1100	Move Book Collection & Staff from Swing Space to Completed PA 11	10	10	25-Aug-26	08-Sep-26
Project Area 5					
SW-1110	Move Book Collection Stacks from PA 5 to Swing Space	3	3	28-Jul-26	30-Jul-26
SW-1115	Move PA 5 Book Collection Stacks from Swing Space to Completed PA 5	10	10	04-Feb-27	17-Feb-27
Project Area 8B					
SW-1135	Swing 2nd Floor Annex into Completed Area 10	5	5	20-Jan-27	26-Jan-27
SW-1140	Adult Learning Center Move In - PA8B	0	0		30-Jul-27
Project Area 10E					
SW-1145	Move In Office Staff - PA10E	5	5	20-Jan-27	26-Jan-27
Project Area 6					
SW-1120	Move Book Collection & Staff from PA 6 to Swing Space	5	5	18-Feb-27	24-Feb-27
SW-1125	Move Book Collection from Swing Space to Completed PA 6	10	10	08-Oct-27	21-Oct-27
Project Area 10W					
SW-1130	Move Staff from Adult Learning Center PA 10W to Completed PA 8B	10	10	02-Aug-27	13-Aug-27
SW-1150	Move Staff To PA10W	5	5	03-Nov-27	09-Nov-27
CP-1					
Sub Phase A					
S-1040	Construction Phase 1	335	315	02-May-25 A	24-Aug-26
S-1120	Project Area 8A - IT Office & Data Center	116	128	15-May-25 A	26-Nov-25
S-1130	Project Area 12 - Admin. Offices EPW	139	144	19-May-25 A	22-Dec-25
S-1060	Project Area 13 - Trustee's Wing	142	142	09-Jun-25	31-Dec-25
S-1070	Project Area 9 - Youth & Teen Wing	120	120	11-Jul-25	02-Jan-26
S-1235	Sub Phase A Completion	0	0		02-Jan-26
Sub Phase B					
S-1150	Project Area 7 - Society, Sciences, Technology & History	139	139	05-Jan-26	20-Jul-26
S-1160	Project Area 11 - Annex	157	157	14-Jan-26	24-Aug-26
S-1165	Sub Phase B Completion	0	0		24-Aug-26
Exterior Restoration					
S-1100	Exterior Renovations	0	0	24-Jul-25	24-Jul-25

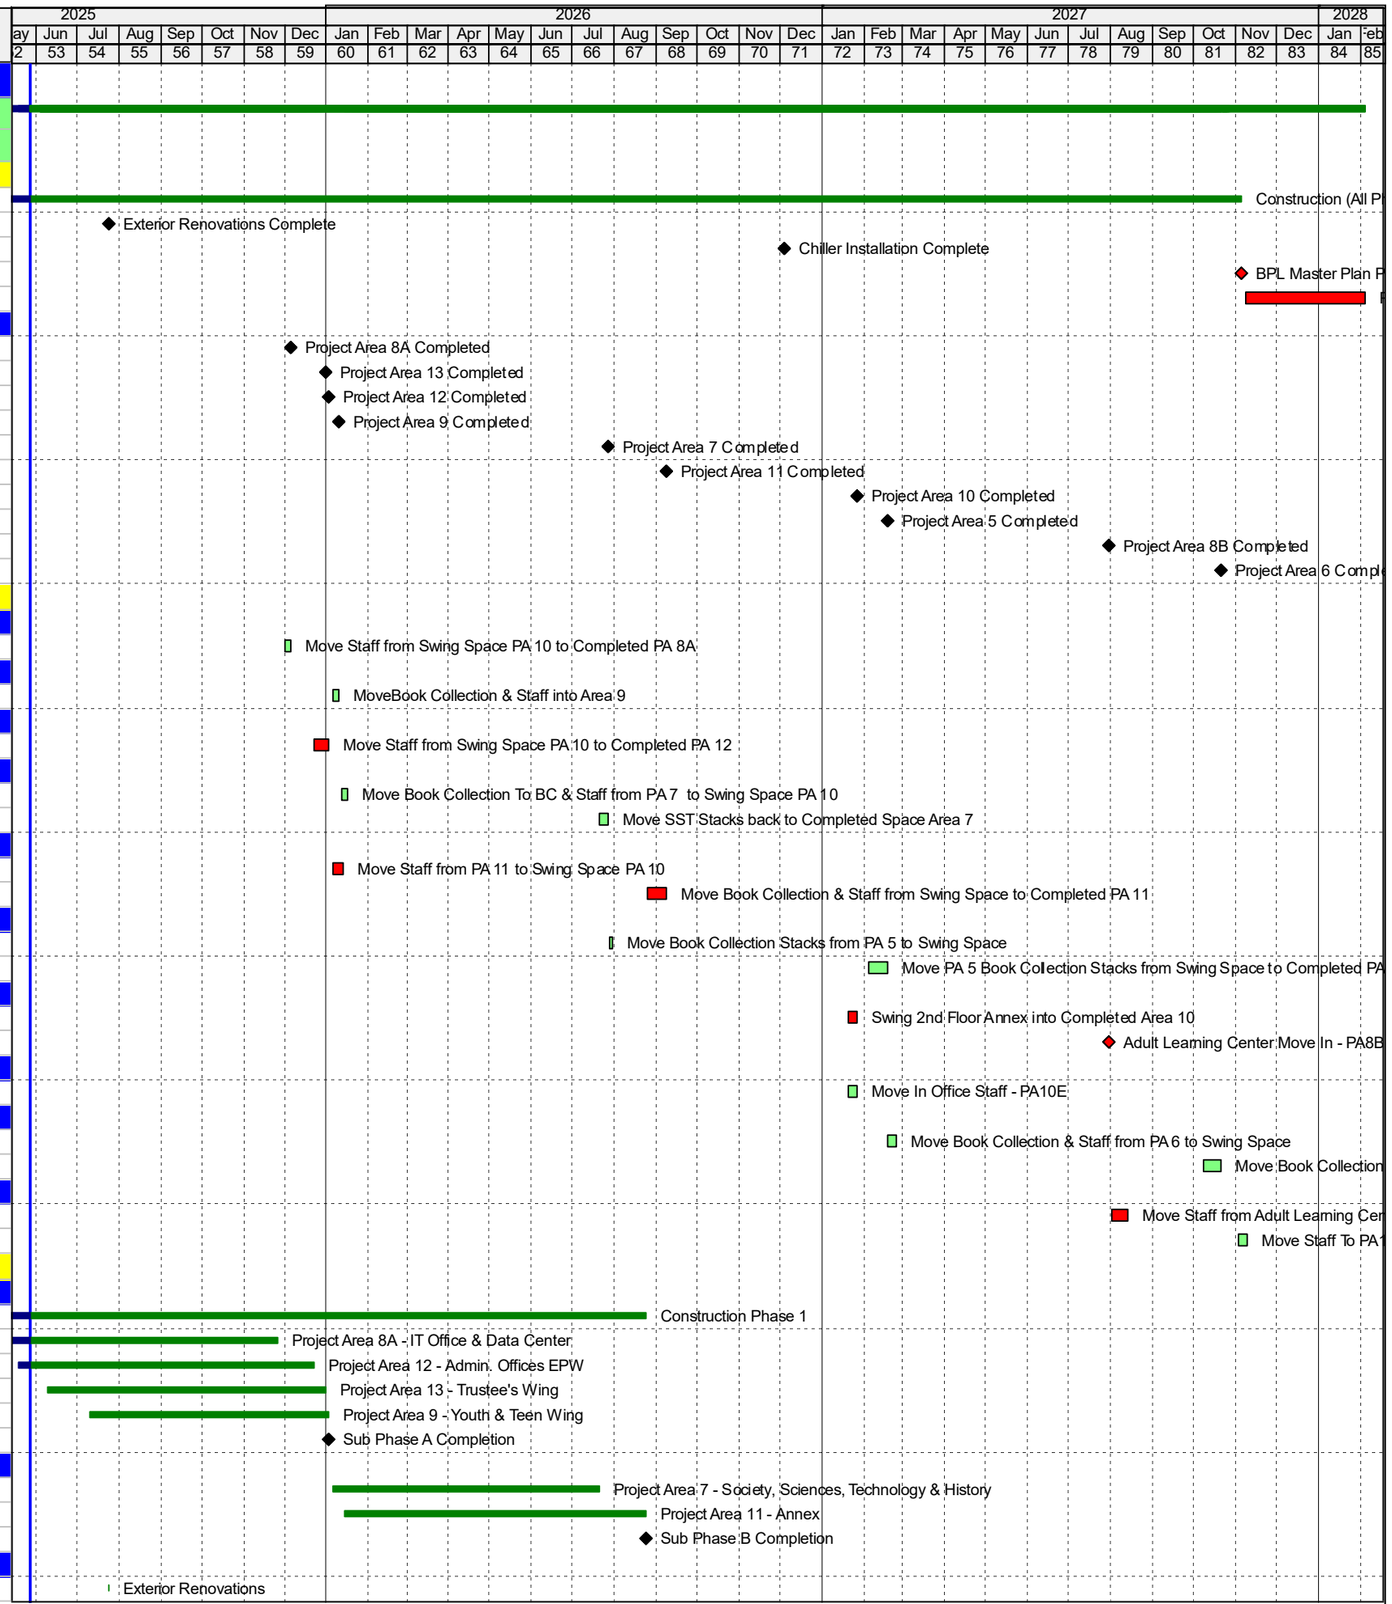

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
CP-2					
Sub Phase C					
S-1185	2nd Floor Balcony Bathrooms	135	135	22-Jul-26	03-Feb-27
S-1170	Project Area 5 - Language and Literature	128	128	31-Jul-26	03-Feb-27
SP-1060	Construction Phase 2	302	302	25-Aug-26	02-Nov-27
S-1180	Project Area 10 - Flatbush Wing Level 3 (East)	90	90	09-Sep-26	19-Jan-27
S-1240	Sub Phase C Completion	0	0		03-Feb-27
Sub Phase D					
S-1190	Project Area 8B - Adult Learning Center	131	131	27-Jan-27	30-Jul-27
S-1200	Project Area 6 - Children's Center	158	158	25-Feb-27	07-Oct-27
S-1220	Project Area 10 - Flatbush Wing Level 3 (West)	53	53	19-Aug-27	02-Nov-27
S-1230	Sub Phase D Completion	0	0		02-Nov-27
Permitting					
DOB					
CP1 & CP2					
PE1180	Issue Alt. 2 Permit CP-1 / CP-2 & Exterior	1	1	06-Jun-25	06-Jun-25
PE1210	Crane Permit Filing - CP-1	15	15	09-Jun-25	27-Jun-25
PE1230	Crane Permit Filing - CP-2	15	15	09-Jun-25	27-Jun-25
PE1220	Crane Permit Review & Approval - CP1	20	20	30-Jun-25	28-Jul-25
PE1240	Crane Permit Review & Approval - CP2	20	20	30-Jun-25	28-Jul-25
PE1250	DOB Permits Closed	20	20	08-Nov-27	08-Dec-27
FDNY					
Construction Project 1					
A4200	Roof Access FDNY Permit Rev/App	25	15	17-Feb-25 A	17-Jun-25
A4220	FDNY Welding Permit Filing Pre/Sub	5	5	28-May-25	03-Jun-25
A4230	FDNY Welding Permit Rev/App	15	15	04-Jun-25	24-Jun-25
A4610	Request FDNY Inspection - Roof Access	20	20	30-Mar-26	24-Apr-26
A4210	FDNY Inspection - Roof Access	1	1	27-Apr-26	27-Apr-26
A4620	FDNY Issue Letter of Approval - Roof Access	10	10	28-Apr-26	11-May-26
Sub Phase A					
A4260	Fire Alarm FDNY Permit Rev/App - Sub Phase A	45	10	24-Mar-25 A	10-Jun-25
A4330	Request Fire Alarm Inspection	20	20	05-Jan-26	30-Jan-26
A4340	Fire Alarm Test	1	1	02-Feb-26	02-Feb-26
A4350	FDNY Issue Notice of Defect	5	5	03-Feb-26	09-Feb-26
A4360	Address FDNY Notice of Defect	5	5	10-Feb-26	16-Feb-26
A4370	Request FDNY Re-Inspection	15	15	17-Feb-26	09-Mar-26
A4380	FDNY Re-Inspection	1	1	10-Mar-26	10-Mar-26
A4390	FDNY Issue Letter of Approval	10	10	11-Mar-26	24-Mar-26
Sub Phase B					
A4280	Fire Alarm FDNY Permit Rev/App - Sub Phase B	45	10	24-Mar-25 A	10-Jun-25
A4400	Request Fire Alarm Inspection	20	20	25-Aug-26	22-Sep-26
A4410	Fire Alarm Test	1	1	23-Sep-26	23-Sep-26
A4420	FDNY Issue Notice of Defect	5	5	24-Sep-26	30-Sep-26
A4430	Address FDNY Notice of Defect	5	5	01-Oct-26	07-Oct-26
A4440	Request FDNY Re-Inspection	15	15	08-Oct-26	28-Oct-26
A4450	FDNY Re-Inspection	1	1	29-Oct-26	29-Oct-26
A4460	FDNY Issue Letter of Approval	10	10	30-Oct-26	13-Nov-26
Construction Project 2					
A4240	FDNY Welding Permit Filing Pre/Sub	5	5	28-May-25	03-Jun-25
A4250	FDNY Welding Permit Rev/App	15	15	04-Jun-25	24-Jun-25
Sub Phase C					
A4300	Fire Alarm FDNY Permit Rev/App - Sub Phase C	45	20	24-Mar-25 A	24-Jun-25
A4470	Request Fire Alarm Inspection	20	20	04-Feb-27	03-Mar-27
A4480	Fire Alarm Test	1	1	04-Mar-27	04-Mar-27
A4490	FDNY Issue Notice of Defect	5	5	05-Mar-27	11-Mar-27
A4500	Address FDNY Notice of Defect	5	5	12-Mar-27	18-Mar-27
A4510	Request FDNY Re-Inspection	15	15	19-Mar-27	08-Apr-27
A4520	FDNY Re-Inspection	1	1	09-Apr-27	09-Apr-27
A4530	FDNY Issue Letter of Approval	10	10	12-Apr-27	23-Apr-27
Sub Phase D					
A4320	Fire Alarm FDNY Permit Rev/App - Sub Phase D	30	30	28-May-25	09-Jul-25
A4540	Request Fire Alarm Inspection	20	20	08-Oct-27	04-Nov-27

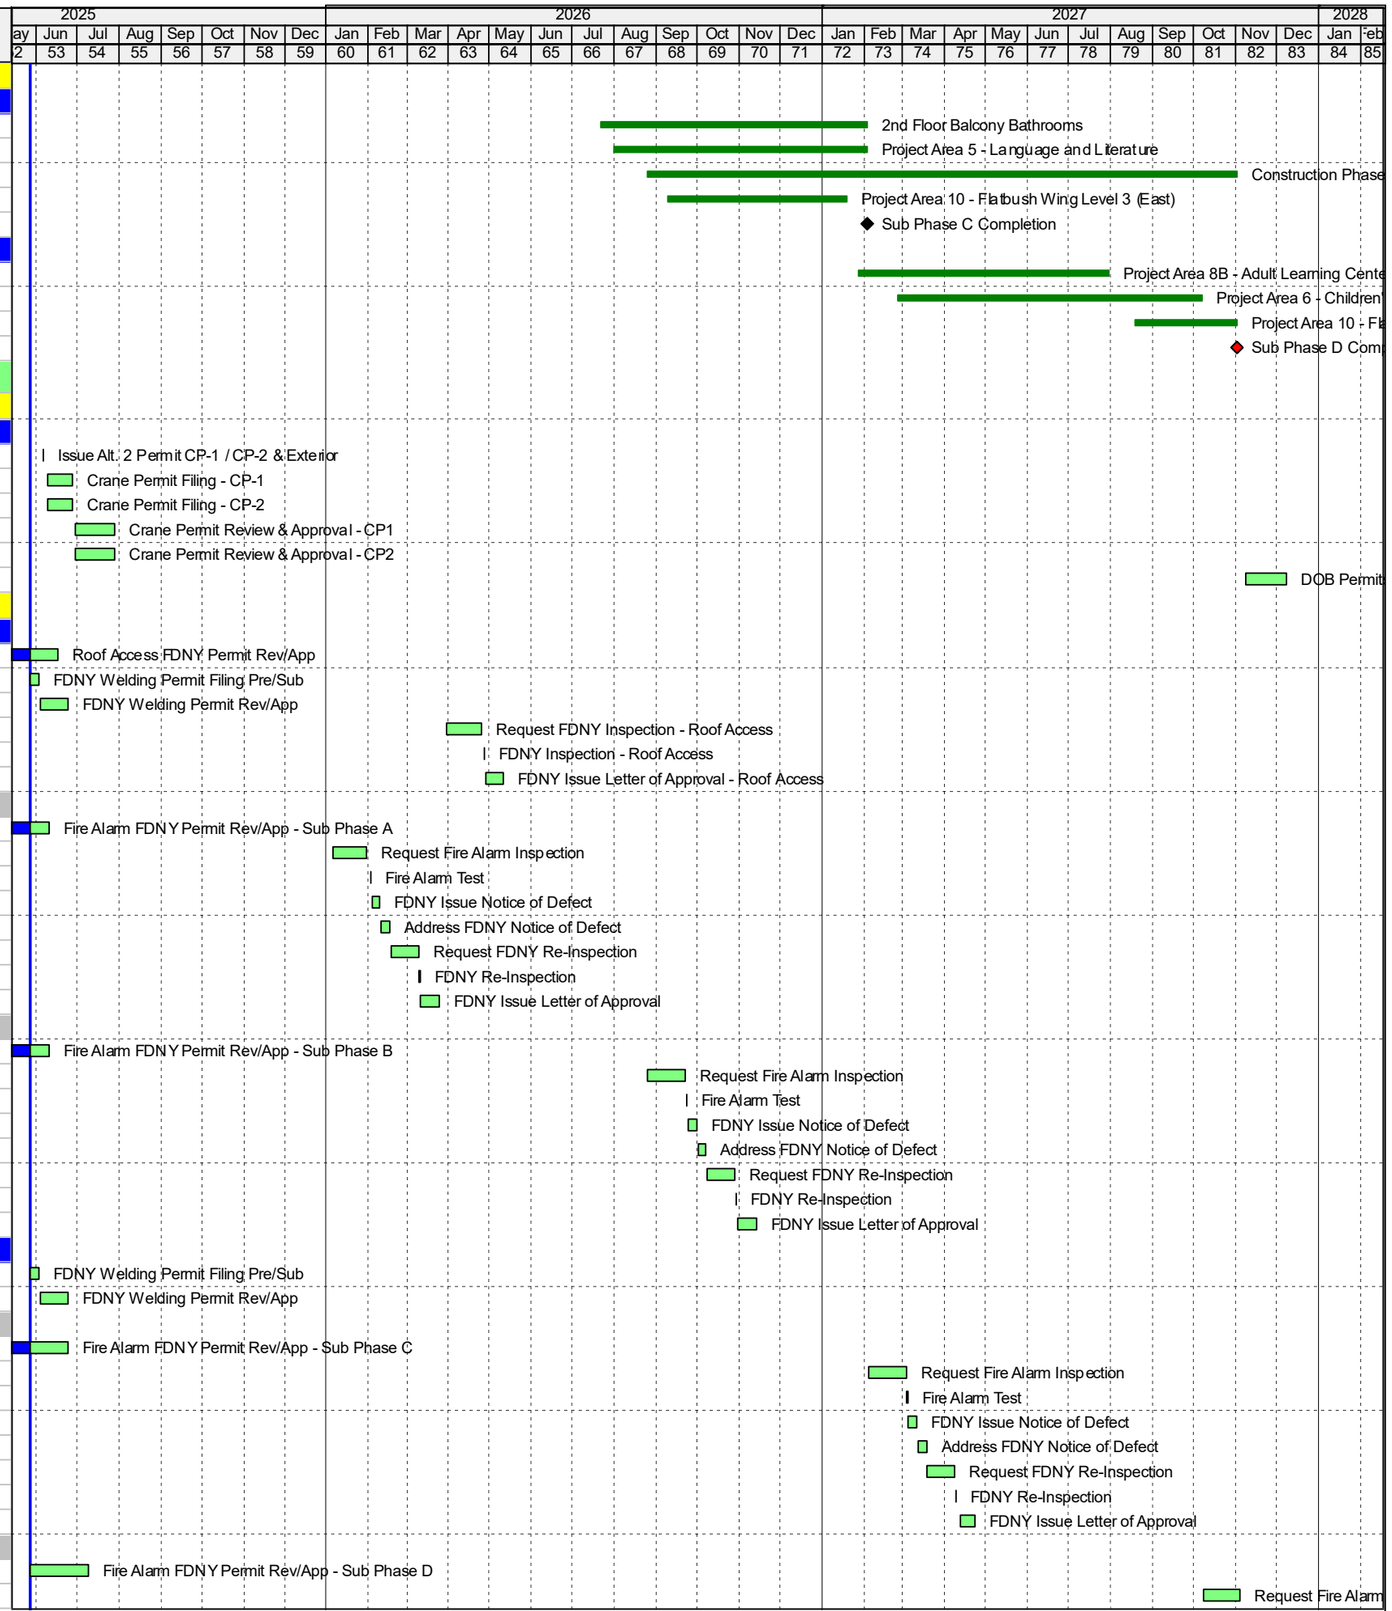


Finish Date: 04-Feb-28
Data Date: 28-May-25
Run Date: 11-Jun-25 16:20
BPL II - 09


Remaining Level of Effort · Actual Level of Effort · Actual Work · Remaining Work · Critical Remaining ... · Summary Milestone · Critical Milestone · Milestone

Gilbane


Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
A4550	Fire Alarm Test	1	1	05-Nov-27	05-Nov-27
A4560	FDNY Issue Notice of Defect	5	5	08-Nov-27	15-Nov-27
A4570	Address FDNY Notice of Defect	5	5	16-Nov-27	22-Nov-27
A4580	Request FDNY Re-Inspection	15	15	23-Nov-27	15-Dec-27
A4590	FDNY Re-Inspection	1	1	16-Dec-27	16-Dec-27
A4600	FDNY Issue Letter of Approval	10	10	17-Dec-27	31-Dec-27
DEP					
Construction Project 1					
Sub Phase A					
A4670	Rev/App V5 - Sub Phase A	40	7	11-Mar-25 A	05-Jun-25
A4890	Rev/App ATRU - Sub Phase A	30	1	07-Apr-25 A	28-May-25
A4970	ATR1 Final Inspection - Sub Phase A	1	1	05-Aug-25	05-Aug-25
A4680	File/App Project Completion ACP15 & 21 - Sub Phase A	5	5	06-Aug-25	12-Aug-25
Sub Phase B					
A4690	Onsite Pre-Filing Walkthrough - Sub Phase B	1	1	13-Aug-25	13-Aug-25
A4710	Pre/Sub ACP7 - Sub Phase B	5	5	14-Aug-25	20-Aug-25
A4720	Rev/App ACP7 - Sub Phase B	15	15	21-Aug-25	11-Sep-25
A4730	Pre/Sub V5 - Sub Phase B	10	10	12-Sep-25	25-Sep-25
A4740	Rev/App V5 - Sub Phase B	40	40	26-Sep-25	21-Nov-25
A5000	ATR1 Final Inspection - Sub Phase B	1	1	12-Mar-26	12-Mar-26
A4700	File Project Completion ACP15 & 21 - Sub Phase B	5	5	13-Mar-26	19-Mar-26
Construction Project 2					
Sub Phase C					
A4750	Onsite Pre-Filing Walkthrough - Sub Phase C	1	1	20-Mar-26	20-Mar-26
A4770	Pre/Sub ACP7- Sub Phase C	5	5	23-Mar-26	27-Mar-26
A4780	Rev/App ACP7 - Sub Phase C	15	15	30-Mar-26	17-Apr-26
A4790	Pre/Sub V5 - Sub Phase C	10	10	20-Apr-26	01-May-26
A4800	Rev/App V5 - Sub Phase C	40	40	04-May-26	29-Jun-26
A5010	ATR1 Final Inspection - Sub Phase C	1	1	24-Sep-26	24-Sep-26
A4760	File Project Completion ACP15 & 21 - Sub Phase C	5	5	25-Sep-26	01-Oct-26
Sub Phase D					
A4810	Onsite Pre-Filing Walkthrough - Sub Phase D	1	1	02-Oct-26	02-Oct-26
A4830	Pre/Sub ACP7 - Sub Phase D	5	5	05-Oct-26	09-Oct-26
A4840	Rev/App ACP7 - Sub Phase D	15	15	12-Oct-26	30-Oct-26
A4850	Pre/Sub V5 - Sub Phase D	10	10	02-Nov-26	16-Nov-26
A4860	Rev/App V5 - Sub Phase D	40	40	17-Nov-26	15-Jan-27
A5020	ATR1 Final Inspection - Sub Phase D	1	1	22-Apr-27	22-Apr-27
A4820	File Project Completion ACP15 & 21 - Sub Phase D	5	5	23-Apr-27	29-Apr-27
Procurement					
Submittals and Engineering					
Make Ready Swing Space					
BP-09A - General Trades					
DIV 10 Specialties					
A3710	Fabricate Plastic Lockers	60	35	23-Jan-25 A	16-Jul-25
CP-1 and CP-2 Procurement					
BP-03A - Concrete & Masonry (CP-1)					
A2850	Prepare / Submit SD Masonry (CP-1)	10	10	28-May-25	10-Jun-25
A2860	Review / Approve Masonry (CP-1)	10	10	11-Jun-25	24-Jun-25
A2910	Prepare / Submit SD Concrete Mix (CP-1)	10	10	19-Jun-25	02-Jul-25
A2870	Fabricate / Deliver Masonry (CP-1)	40	40	25-Jun-25	20-Aug-25
A2920	Review / Approve Concrete Mix (CP-1)	10	10	03-Jul-25	17-Jul-25
A2930	Fabricate / Deliver Concrete (CP-1)	5	5	18-Jul-25	24-Jul-25
BP-03B - Concrete & Masonry (CP-2)					
A2820	Prepare / Submit SD Masonry (CP-2)	10	10	28-May-25	10-Jun-25
A2830	Review / Approve Masonry (CP-2)	10	10	11-Jun-25	24-Jun-25
A2880	Prepare / Submit SD Concrete Mix (CP-2)	10	10	19-Jun-25	02-Jul-25
A2840	Fabricate / Deliver Masonry (CP-2)	40	40	25-Jun-25	20-Aug-25
A2890	Review / Approve Concrete Mix (CP-2)	10	10	03-Jul-25	17-Jul-25
A2900	Fabricate / Deliver Concrete (CP-2)	5	5	18-Jul-25	24-Jul-25
BP-04C - Facade / Masonry Restoration (CP-1)					
A4960	Mockup Installation	20	9	12-May-25 A	09-Jun-25
A2810	Fabricate / Deliver Facade / Masonry Restoration (CP-1)	10	10	28-May-25	10-Jun-25

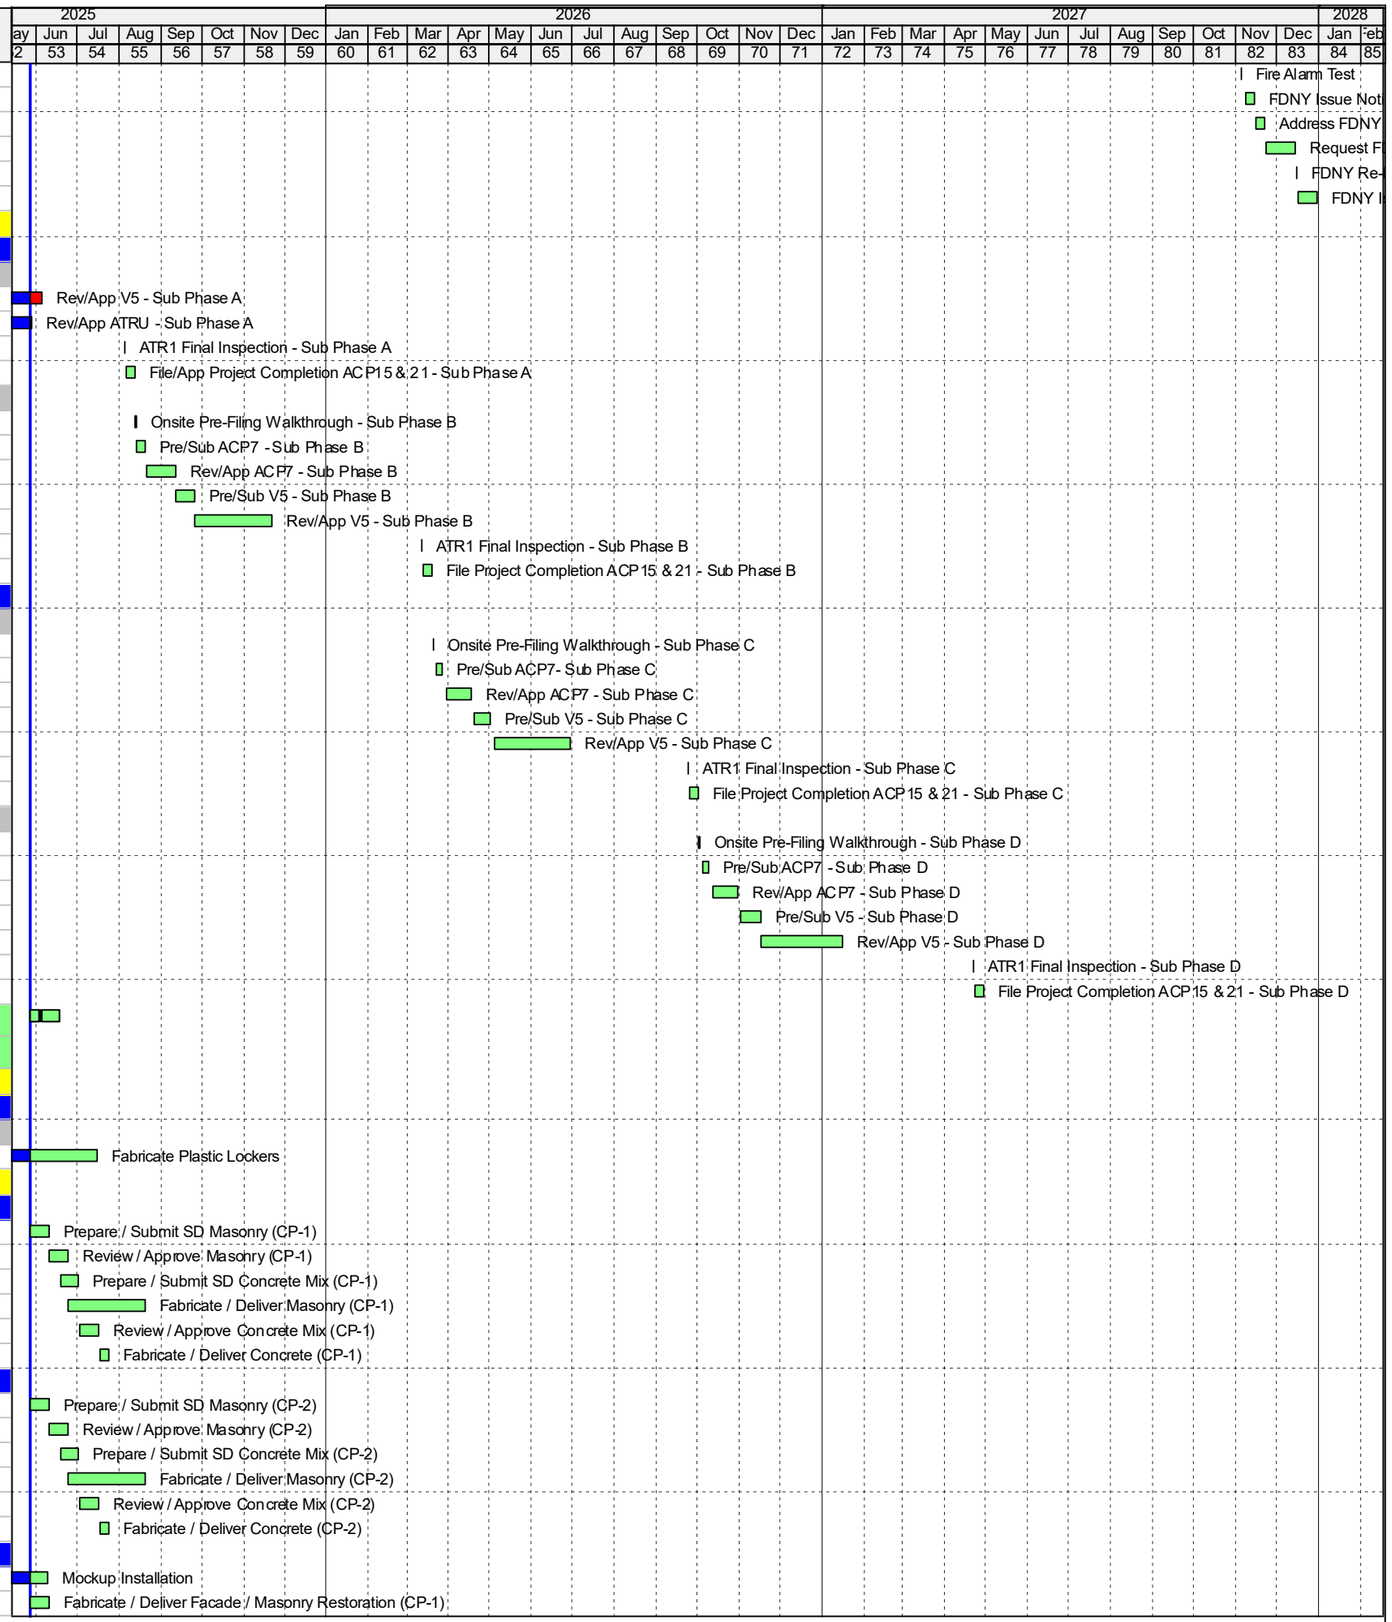


Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
A2990	Review / Approve Window Operability Survey	10	10	28-May-25	10-Jun-25
A3590	Fabricate / Deliver Glazing	30	30	28-May-25	09-Jul-25
A4930	Prepare / Submit Roof Mounted Railing (RAI)	10	10	28-May-25	10-Jun-25
A3600	Mockup Review / Approval	10	10	10-Jun-25	23-Jun-25
A4940	Review / Approve Roof Mounted Railing (RAI)	10	10	11-Jun-25	24-Jun-25
A4950	Fabricate / Deliver Roof Mounted Railing (RAI)	40	40	25-Jun-25	20-Aug-25
BP-05A - Structural Steel / Misc. Metals (CP-1)					
A2730	Prepare / Submit SD Structural Steel - Sub-Phase A	10	10	28-May-25	10-Jun-25
A3390	Prepare / Submit Crossover Platforms	10	10	28-May-25	10-Jun-25
A5200	Prepare / Submit SD Structural Steel - Sub-Phase B	10	10	28-May-25	10-Jun-25
A5140	Prepare / Submit SD Roof Ladders	10	10	28-May-25	10-Jun-25
A2770	Review / Approve SD Roof Ladders	10	10	28-May-25	10-Jun-25
A2740	Review / Approve Structural Steel - Sub-Phase A	10	10	11-Jun-25	24-Jun-25
A2760	Fabricate / Deliver Crossover Platforms	30	30	11-Jun-25	23-Jul-25
A5240	Review / Approve Structural Steel - Sub-Phase B	10	10	11-Jun-25	24-Jun-25
A2780	Fabricate / Deliver Roof Ladders	15	15	11-Jun-25	01-Jul-25
A2750	Fabricate / Deliver Structural Steel - Project Area 8A	15	15	25-Jun-25	16-Jul-25
A3030	Fabricate / Deliver Structural Steel- Project Area 9	10	10	25-Jun-25	09-Jul-25
A5210	Fabricate / Deliver Structural Steel Project Area 12	15	15	25-Jun-25	16-Jul-25
A5220	Fabricate / Deliver Structural Steel Project Area 13	15	15	25-Jun-25	16-Jul-25
A5250	Fabricate / Deliver Structural Steel Project Area 11	15	15	25-Jun-25	16-Jul-25
BP-05B - Structural Steel / Misc. Metals (CP-2)					
A2700	Prepare / Submit SD Structural Steel (CP-2)	10	10	28-May-25	10-Jun-25
A2710	Review / Approve Structural Steel (CP-2)	10	10	11-Jun-25	24-Jun-25
A2720	Fabricate / Deliver Strucutral Steel PA6 (CP-2)	15	15	25-Jun-25	16-Jul-25
A3040	Fabricate / Deliver Structural Steel PA10E (CP-2)	15	15	25-Jun-25	16-Jul-25
BP-06B - Millwork (CP-1)					
Millwork					
M1040	Review and Approve PD / Shop Drawings	10	10	28-May-25	10-Jun-25
M1050	Fabricate / Deliver Millwork - PA7	60	60	11-Jun-25	04-Sep-25
M1390	Fabricate / Deliver Millwork - PA8A	40	40	12-Aug-25	07-Oct-25
M1410	Fabricate / Deliver Millwork - PA13	40	40	18-Aug-25	13-Oct-25
M1430	Fabricate / Deliver Millwork - PA9	40	40	27-Aug-25	22-Oct-25
M1460	Fabricate / Deliver Millwork - PA12	40	40	29-Aug-25	24-Oct-25
M1420	Fabricate / Deliver Millwork - PA11	40	40	07-Apr-26	02-Jun-26
Corian Countertops					
M1230	Prepare / Submit Bathroom Countertops STN	10	10	28-May-25	10-Jun-25
M1240	Review and Approve Bathroom Countertops STN	10	10	11-Jun-25	24-Jun-25
M1250	Fabricate / Deliver Bathroom Countertops STN	15	15	25-Jun-25	16-Jul-25
Pin-Up Felt					
M1110	Prepare / Submit Pin-Up Felt ACOU5	10	10	28-May-25	10-Jun-25
M1120	Review and Approve Pin-Up Felt ACOU5	10	10	11-Jun-25	24-Jun-25
M1190	Fabricate / Deliver Pin-Up Felt ACOU5	50	50	25-Jun-25	04-Sep-25
Millwork Restoration					
M1360	Review and Approve Existing Millwork Surveys - PA 7& 9	10	10	22-Apr-25 A	10-Jun-25
M1320	Prepare / Submit Millwork Restoration PD	10	10	28-May-25	10-Jun-25
M1330	Review and Approve Millwork Restoration PD	10	10	11-Jun-25	24-Jun-25
M1340	Fabricate / Deliver Millwork Restoration Products	10	10	25-Jun-25	09-Jul-25
BP-06C - Millwork (CP-2)					
Millwork					
M1160	Prepare / Submit Millwork Shop Drawings / PD		30	28-May-25	09-Jul-25
M1170	Review and Approve PD / Shop Drawings	10	10	10-Jul-25	23-Jul-25
M1180	Fabricate / Deliver Millwork - PA6	60	60	24-Jul-25	16-Oct-25
M1440	Fabricate / Deliver Millwork - PA10W	40	40	24-Jul-25	18-Sep-25
M1470	Fabricate / Deliver Millwork - PA5	40	40	24-Jul-25	18-Sep-25
M1450	Fabricate / Deliver Millwork - PA 10E	40	40	22-Sep-26	17-Nov-26
M1400	Fabricate / Deliver Millwork - PA8B	40	40	12-Apr-27	07-Jun-27
Corian Countertops					
M1260	Prepare / Submit Bathroom Countertops STN	10	10	28-May-25	10-Jun-25
M1270	Review and Approve Bathroom Countertops STN	10	10	11-Jun-25	24-Jun-25
M1280	Fabricate / Deliver Bathroom Countertops STN	15	15	25-Jun-25	16-Jul-25
Pin-Up Felt					
M1200	Prepare / Submit Pin-Up Felt ACOU5	10	10	28-May-25	10-Jun-25

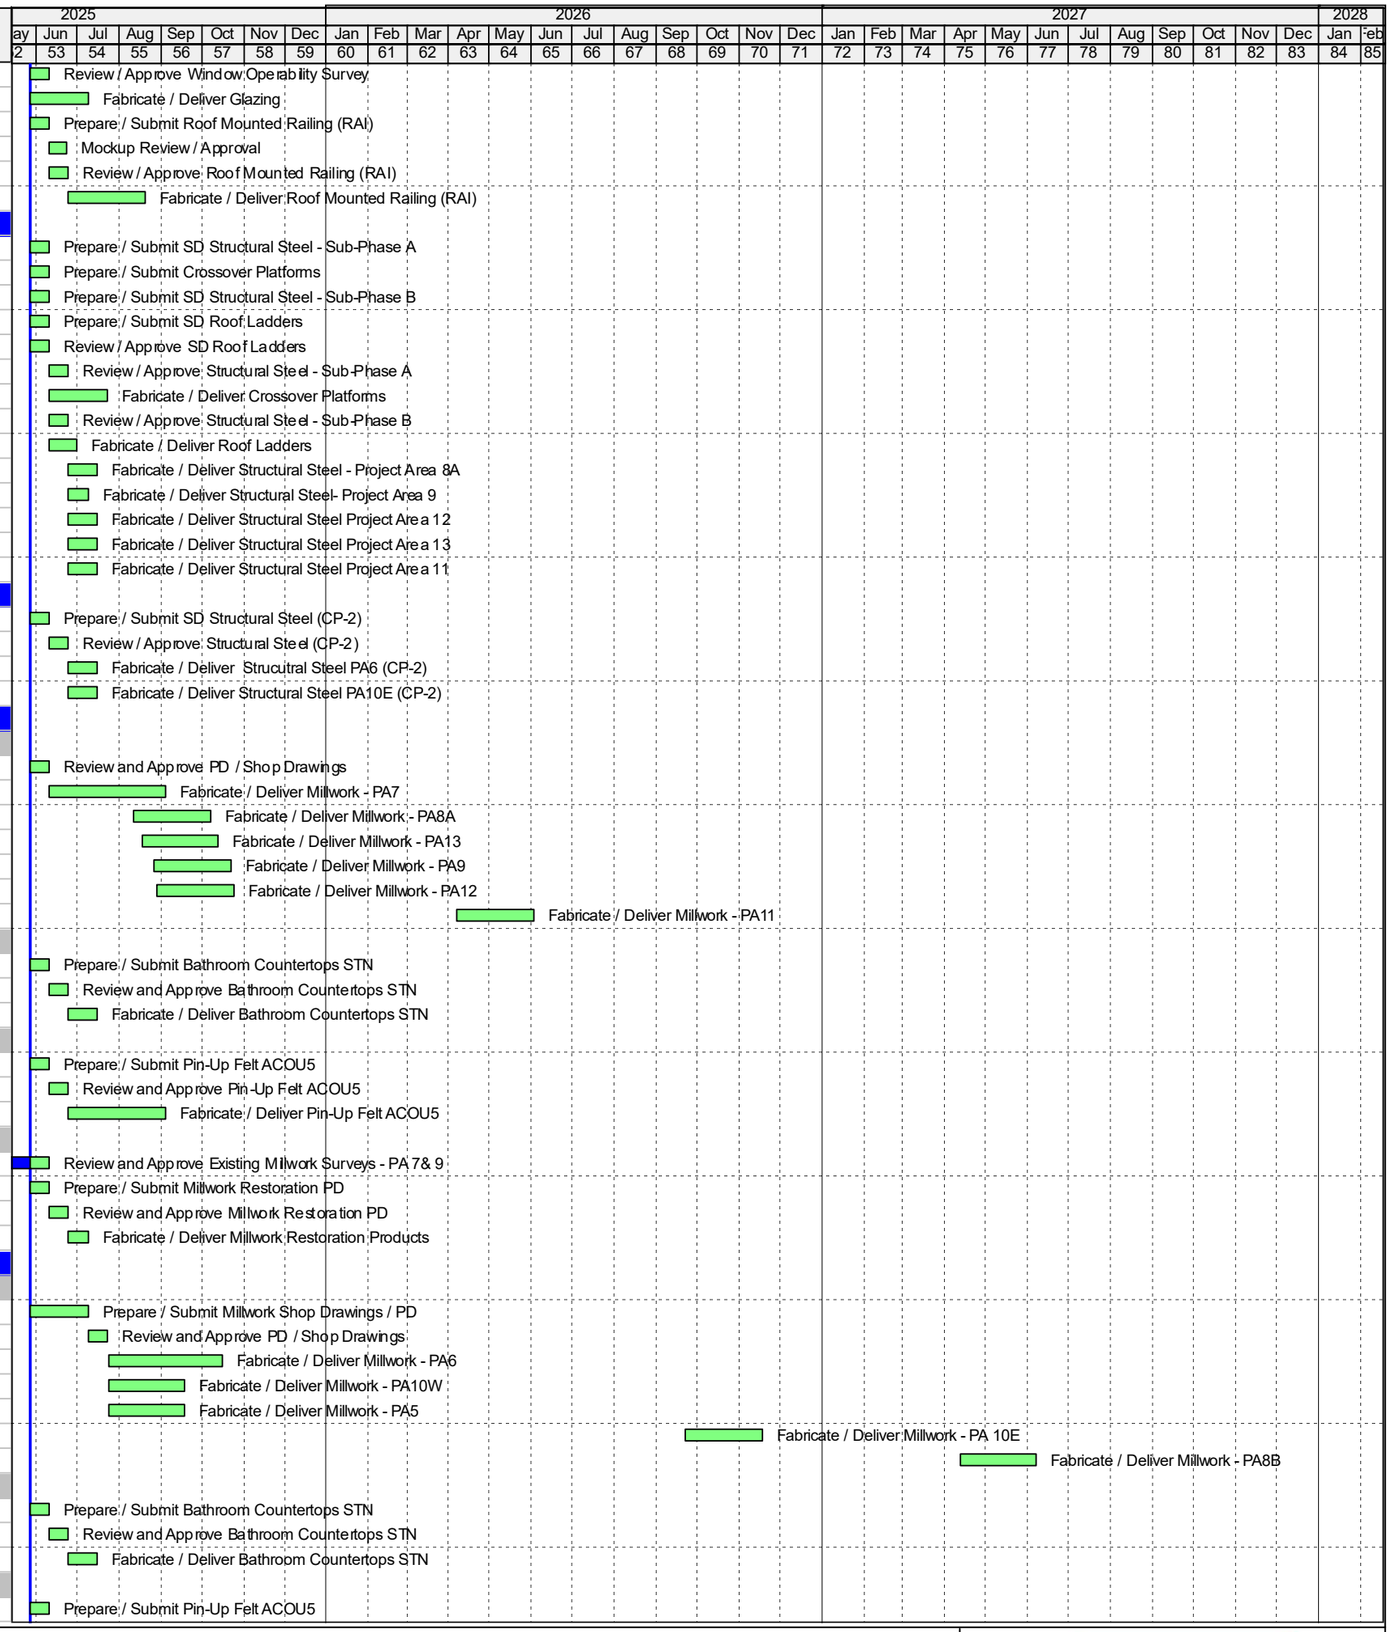

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
M1210	Review and Approve Pin-Up Felt ACOU5	10	10	11-Jun-25	24-Jun-25
M1220	Fabricate / Deliver Pin-Up Felt ACOU5	30	30	25-Jun-25	06-Aug-25
Millwork Restoration					
M1380	Review and Approve Existing Millwork Surveys - PA 5 & 6	10	10	22-Apr-25 A	10-Jun-25
A5350	New Activity	1	1	28-May-25	28-May-25
M1290	Prepare / Submit Millwork Restoration PD	10	10	28-May-25	10-Jun-25
M1300	Review and Approve Millwork Restoration PD	10	10	11-Jun-25	24-Jun-25
M1310	Fabricate / Deliver Millwork Restoration Products	10	10	25-Jun-25	09-Jul-25
BP-07A - Roofing (CP-1)					
A2580	Prepare / Submit SD Roofing (CP-1)	10	10	28-May-25	10-Jun-25
A2590	Review / Approve Roofing (CP-1)	10	10	11-Jun-25	24-Jun-25
A2600	Fabricate / Deliver Roofing (CP-1)	10	10	25-Jun-25	09-Jul-25
BP-07B - Roofing (CP-2)					
A2550	Prepare / Submit SD Roofing (CP-2)	10	10	28-May-25	10-Jun-25
A2560	Review / Approve Roofing (CP-2)	10	10	11-Jun-25	24-Jun-25
A2570	Fabricate / Deliver Roofing (CP-2)	30	30	25-Jun-25	06-Aug-25
BP-07C - Applied Fireproofing (CP-1)					
A2520	Prepare / Submit SD Applied Fireproofing (CP-1)	10	10	28-May-25	10-Jun-25
A2530	Review / Approve Applied Fireproofing (CP-1)	10	10	11-Jun-25	24-Jun-25
A2540	Fabricate / Deliver Applied Fireproofing (CP-1)	40	40	25-Jun-25	20-Aug-25
BP-07D - Applied Fireproofing (CP-2)					
A2490	Prepare / Submit SD Applied Fireproofing (CP-2)	10	10	28-May-25	10-Jun-25
A2500	Review / Approve Applied Fireproofing (CP-2)	10	10	11-Jun-25	24-Jun-25
A2510	Fabricate / Deliver Applied Fireproofing (CP-2)	40	40	25-Jun-25	20-Aug-25
BP-08A - Metal & Glazing (CP-1)					
A2460	Prepare / Submit SD Metal & Glazing (CP-1)	10	10	28-May-25	10-Jun-25
A2470	Review / Approve Metal & Glazing (CP-1)	10	10	11-Jun-25	24-Jun-25
A2480	Fabricate / Deliver Metal & Glazing (CP-1)	40	40	25-Jun-25	20-Aug-25
BP-08B - Metal & Glazing (CP-2)					
A2430	Prepare / Submit SD Metal & Glazing (CP-2)	10	10	19-Jun-25	02-Jul-25
A2440	Review / Approve Metal & Glazing (CP-2)	10	10	03-Jul-25	17-Jul-25
A2450	Fabricate / Deliver Metal & Glazing (CP-2)	40	40	18-Jul-25	12-Sep-25
BP-09D - Carpentry / Toilet Part & Accessories / Doors & Frames / Signage (CP-1)					
Carpentry / Drywall					
A2400	Prepare / Submit SD Carpentry / Drywall (CP-1)	10	10	28-May-25	10-Jun-25
A2410	Review / Approve Carpentry / Drywall (CP-1)	10	10	11-Jun-25	24-Jun-25
A2420	Fabricate / Deliver Carpentry / Drywall (CP-1)	10	10	25-Jun-25	09-Jul-25
Doors and Frames					
A3050	Prepare / Submit SD Doors / Frames (CP-1)	10	5	23-May-25 A	03-Jun-25
A3060	Review / Approve Doors / Frames (CP-1)	10	10	04-Jun-25	17-Jun-25
A3070	Fabricate / Deliver Doors / Frames (CP-1)	40	40	18-Jun-25	13-Aug-25
Wood Ceiling & Wall Panels					
A5880	Prepare / Submit SD Wood Ceiling ACOU4 (CP-1)	10	10	28-May-25	10-Jun-25
A5970	Prepare / Submit SD Wood Wall Panel ACOU2 & 7(CP-1)	10	10	28-May-25	10-Jun-25
A5890	Review / Approve Wood Ceiling ACOU3 & 4 (CP-1)	10	10	11-Jun-25	24-Jun-25
A5980	Review / Approve Wood Wall Panel ACOU2 & 7 (CP-1)	10	10	11-Jun-25	24-Jun-25
A5900	Fabricate / Deliver Wood Ceiling ACOU3 & 4 (CP-1)	70	70	25-Jun-25	02-Oct-25
A5990	Fabricate / Deliver Wood Wall Panel ACOU2 & 7 (CP-1)	70	70	25-Jun-25	02-Oct-25
Storefront Glazing System					
A5910	Prepare / Submit SD Storefront Glazing Stystem (CP-1)	10	10	28-May-25	10-Jun-25
A5920	Review / Approve Storefront Glazing Stystem (CP-1)	10	10	11-Jun-25	24-Jun-25
A5930	Fabricate / Deliver Storefront Glazing Stystem (CP-1)	50	50	25-Jun-25	04-Sep-25
Lockers & Misc Appliances					
A5940	Prepare / Submit SD Lockers MTL2 & 3 (CP-1)	10	10	28-May-25	10-Jun-25
A6000	Prepare / Submit Appliances (CP-1)	10	10	28-May-25	10-Jun-25
A5950	Review / Approve Lockers MTL2 & 3 (CP-1)	10	10	11-Jun-25	24-Jun-25
A6010	Review / Approve Appliances (CP-1)	10	10	11-Jun-25	24-Jun-25
A5960	Fabricate / Deliver Lockers MTL2 & 3 (CP-1)	40	40	25-Jun-25	20-Aug-25
A6020	Fabricate / Deliver Appliances (CP-1)	40	40	25-Jun-25	20-Aug-25
Toilet Accessories					
A3110	Prepare / Submit SD Toilet Accessories (CP-1)	10	10	28-May-25	10-Jun-25
A3120	Review / Approve Toilet Accessories (CP-1)	10	10	11-Jun-25	24-Jun-25
A3130	Fabricate / Deliver Toilet Accessories (CP-1)	30	30	25-Jun-25	06-Aug-25

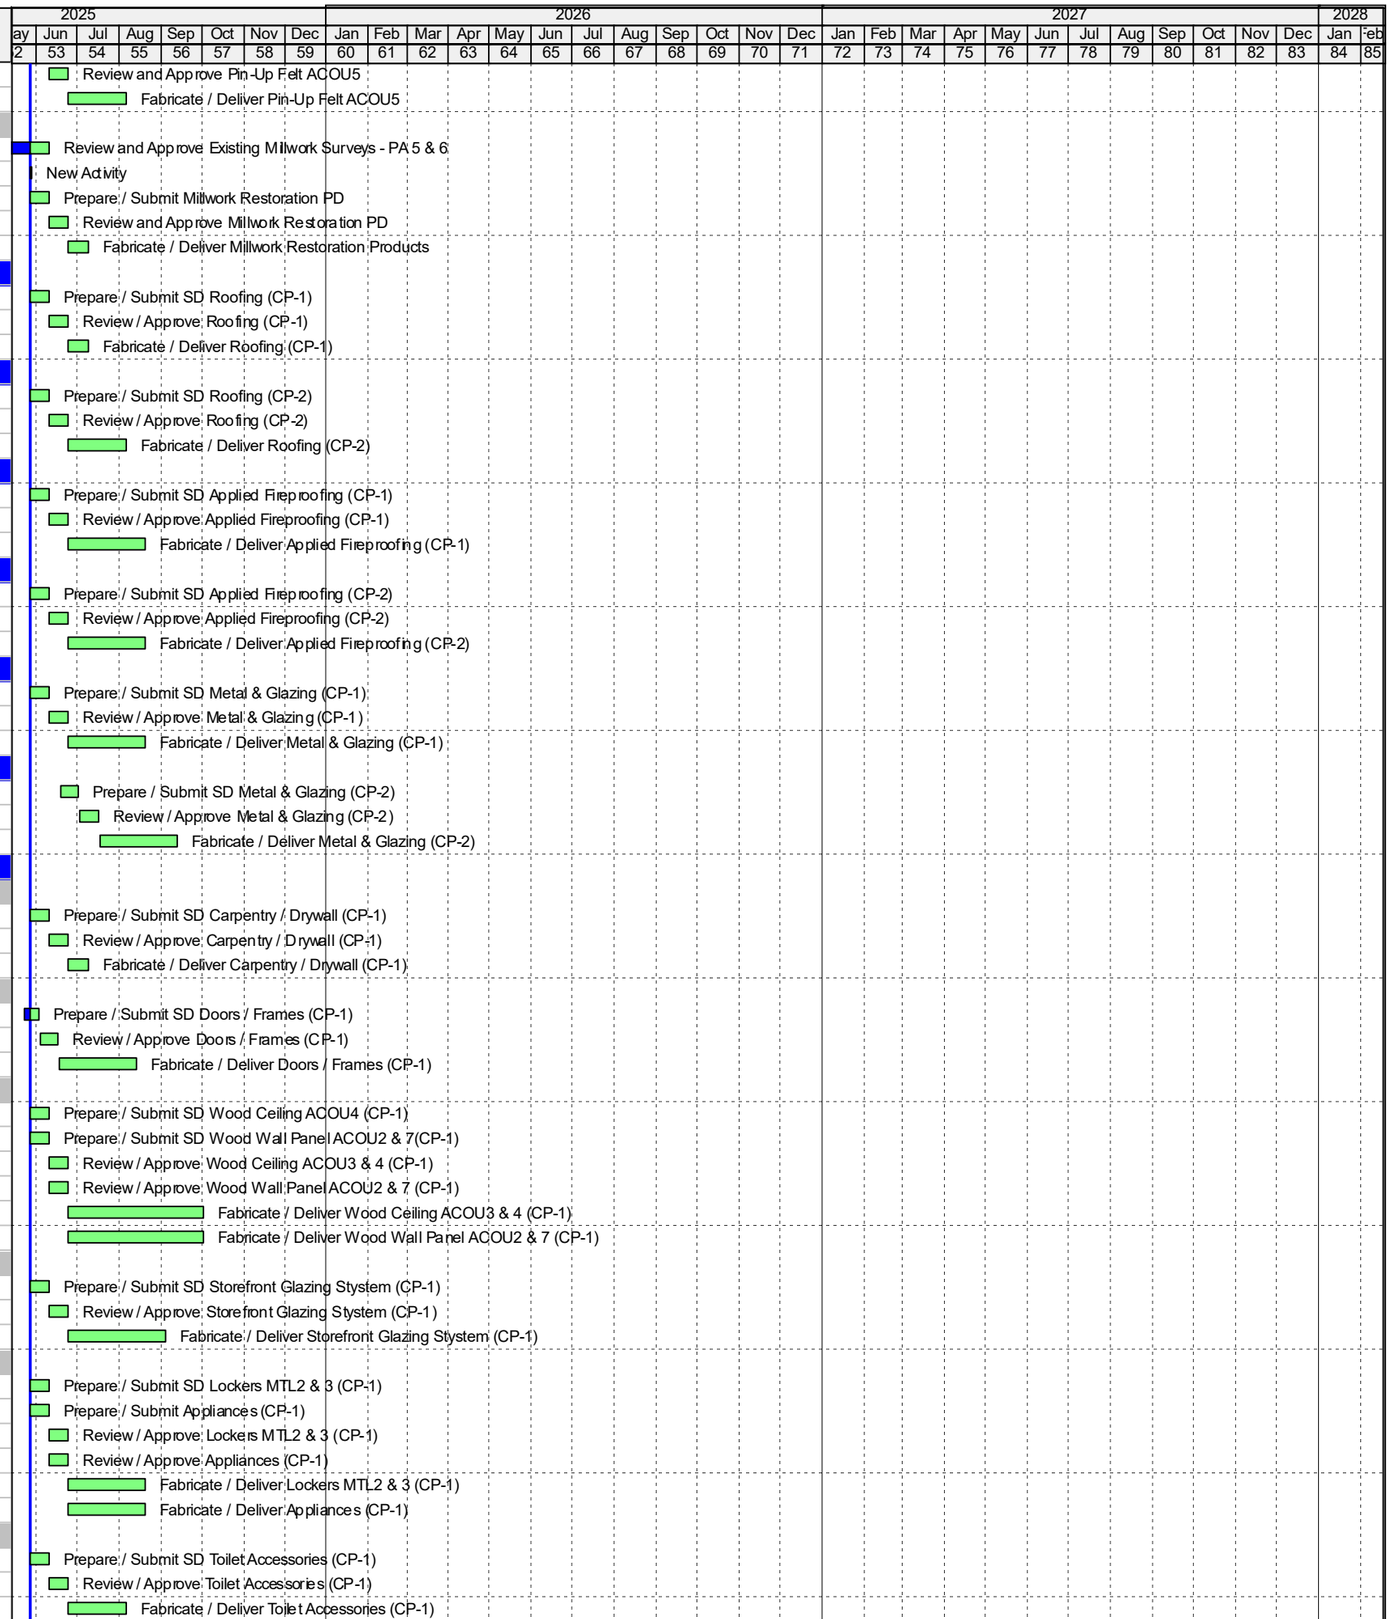

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
	Signage				
A3140	Prepare / Submit SD Signage (CP-1)	10	10	11-Jun-25	24-Jun-25
A3150	Review / Approve Signage (CP-1)	10	10	25-Jun-25	09-Jul-25
A3160	Fabricate / Deliver Signage (CP-1)	40	40	10-Jul-25	04-Sep-25
	Window Treatments				
A2160	Prepare / Submit SD Window Treatments (CP-1)	10	10	28-May-25	10-Jun-25
A2170	Review / Approve Window Treatments (CP-1)	10	10	11-Jun-25	24-Jun-25
A2180	Fabricate / Deliver Window Treatments (CP-1)	50	50	25-Jun-25	04-Sep-25
	BP-09E - Carpentry / Toilet Part & Accessories / Doors & Frames / Signage (CP-2)				
	Carpentry / Drywall				
A2370	Prepare / Submit SD Carpentry / Drywall (CP-2)	10	10	28-May-25	10-Jun-25
A2380	Review / Approve Carpentry / Drywall (CP-2)	10	10	11-Jun-25	24-Jun-25
A2390	Fabricate / Deliver Carpentry / Drywall (CP-2)	10	10	25-Jun-25	09-Jul-25
	Doors and Frames				
A3170	Prepare / Submit SD Doors / Frames (CP-2)	10	10	11-Jun-25	24-Jun-25
A3180	Review / Approve Doors / Frames (CP-2)	10	10	25-Jun-25	09-Jul-25
A3190	Fabricate / Deliver Doors / Frames (CP-2)	40	40	10-Jul-25	04-Sep-25
	Wood Ceiling & Wall Panels				
A6120	Prepare / Submit SD Wood Ceiling ACOU4 (CP-2)	10	10	28-May-25	10-Jun-25
A6130	Prepare / Submit SD Wood Wall Panel ACOU2 & 7(CP-2)	10	10	28-May-25	10-Jun-25
A6140	Review / Approve Wood Ceiling ACOU3 & 4 (CP-2)	10	10	11-Jun-25	24-Jun-25
A6150	Review / Approve Wood Wall Panel ACOU2 & 7 (CP-2)	10	10	11-Jun-25	24-Jun-25
A6160	Fabricate / Deliver Wood Ceiling ACOU3 & 4 (CP-2)	70	70	25-Jun-25	02-Oct-25
A6170	Fabricate / Deliver Wood Wall Panel ACOU2 & 7 (CP-2)	70	70	25-Jun-25	02-Oct-25
	Storefront Glazing System				
A6090	Prepare / Submit SD Storefront Glazing Stystem (CP-2)	10	10	28-May-25	10-Jun-25
A6100	Review / Approve Storefront Glazing Stystem (CP-2)	10	10	11-Jun-25	24-Jun-25
A6110	Fabricate / Deliver Storefront Glazing Stystem (CP-2)	50	50	25-Jun-25	04-Sep-25
	Lockers & Misc Appliances				
A6030	Prepare / Submit SD Lockers MTL2 & 3 (CP-2)	10	10	28-May-25	10-Jun-25
A6040	Prepare / Submit Appliances (CP-2)	10	10	28-May-25	10-Jun-25
A6050	Review / Approve Lockers MTL2 & 3 (CP-2)	10	10	11-Jun-25	24-Jun-25
A6060	Review / Approve Appliances (CP-2)	10	10	11-Jun-25	24-Jun-25
A6070	Fabricate / Deliver Lockers MTL2 & 3 (CP-2)	40	40	25-Jun-25	20-Aug-25
A6080	Fabricate / Deliver Appliances (CP-2)	40	40	25-Jun-25	20-Aug-25
	Toilet Partitions				
A3200	Prepare / Submit SD Toilet Partitions (CP-2)	10	10	25-Jun-25	09-Jul-25
A3210	Review / Approve Toilet Partitions (CP-2)	10	10	10-Jul-25	23-Jul-25
A3220	Fabricate / Deliver Toilet Partitions (CP-2)	40	40	24-Jul-25	18-Sep-25
	Toilet Accessories				
A3230	Prepare / Submit SD Toilet Accessories (CP-2)	10	10	10-Jul-25	23-Jul-25
A3240	Review / Approve Toilet Accessories (CP-2)	10	10	24-Jul-25	06-Aug-25
A3250	Fabricate / Deliver Toilet Accessories (CP-2)	30	30	07-Aug-25	18-Sep-25
	Signage				
A3260	Prepare / Submit SD Signage (CP-2)	10	10	24-Jul-25	06-Aug-25
A3270	Review / Approve Signage (CP-2)	10	10	07-Aug-25	20-Aug-25
A3280	Fabricate / Deliver Signage (CP-2)	40	40	21-Aug-25	16-Oct-25
	Window Treatments				
A2130	Prepare / Submit SD Window Treatments (CP-2)	10	10	07-Aug-25	20-Aug-25
A2140	Review / Approve Window Treatments (CP-2)	10	10	21-Aug-25	04-Sep-25
A2150	Fabricate / Deliver Window Treatments (CP-2)	50	50	05-Sep-25	14-Nov-25
	BP-09F - Resilient Flooring / Carpeting (CP-1)				
A2340	Prepare / Submit SD Resilient Flooring / Carpeting (CP-1)	10	10	28-May-25	10-Jun-25
A2350	Review / Approve Resilient Flooring / Carpeting (CP-1)	10	10	11-Jun-25	24-Jun-25
A2360	Fabricate / Deliver Resilient Flooring (MCT, VCT)	40	40	25-Jun-25	20-Aug-25
A3290	Fabricate / Deliver Carpeting (CP-1)	40	40	25-Jun-25	20-Aug-25
	BP-09G - Resilient Flooring / Carpeting (CP-2)				
A1950	Prepare / Submit SD Poured-in-Place Rubber	10	10	28-May-25	10-Jun-25
A2310	Prepare / Submit SD Resilient Flooring / Carpeting (CP-2)	10	10	28-May-25	10-Jun-25
A1960	Review / Approve Poured-in-Place Rubber	10	10	11-Jun-25	24-Jun-25
A2320	Review / Approve Resilient Flooring / Carpeting (CP-2)	10	10	11-Jun-25	24-Jun-25
A1970	Fabricate / Deliver Poured-in-Place Rubber	40	40	25-Jun-25	20-Aug-25
A2330	Fabricate / Deliver Resilient Flooring (CP-2)	40	40	25-Jun-25	20-Aug-25

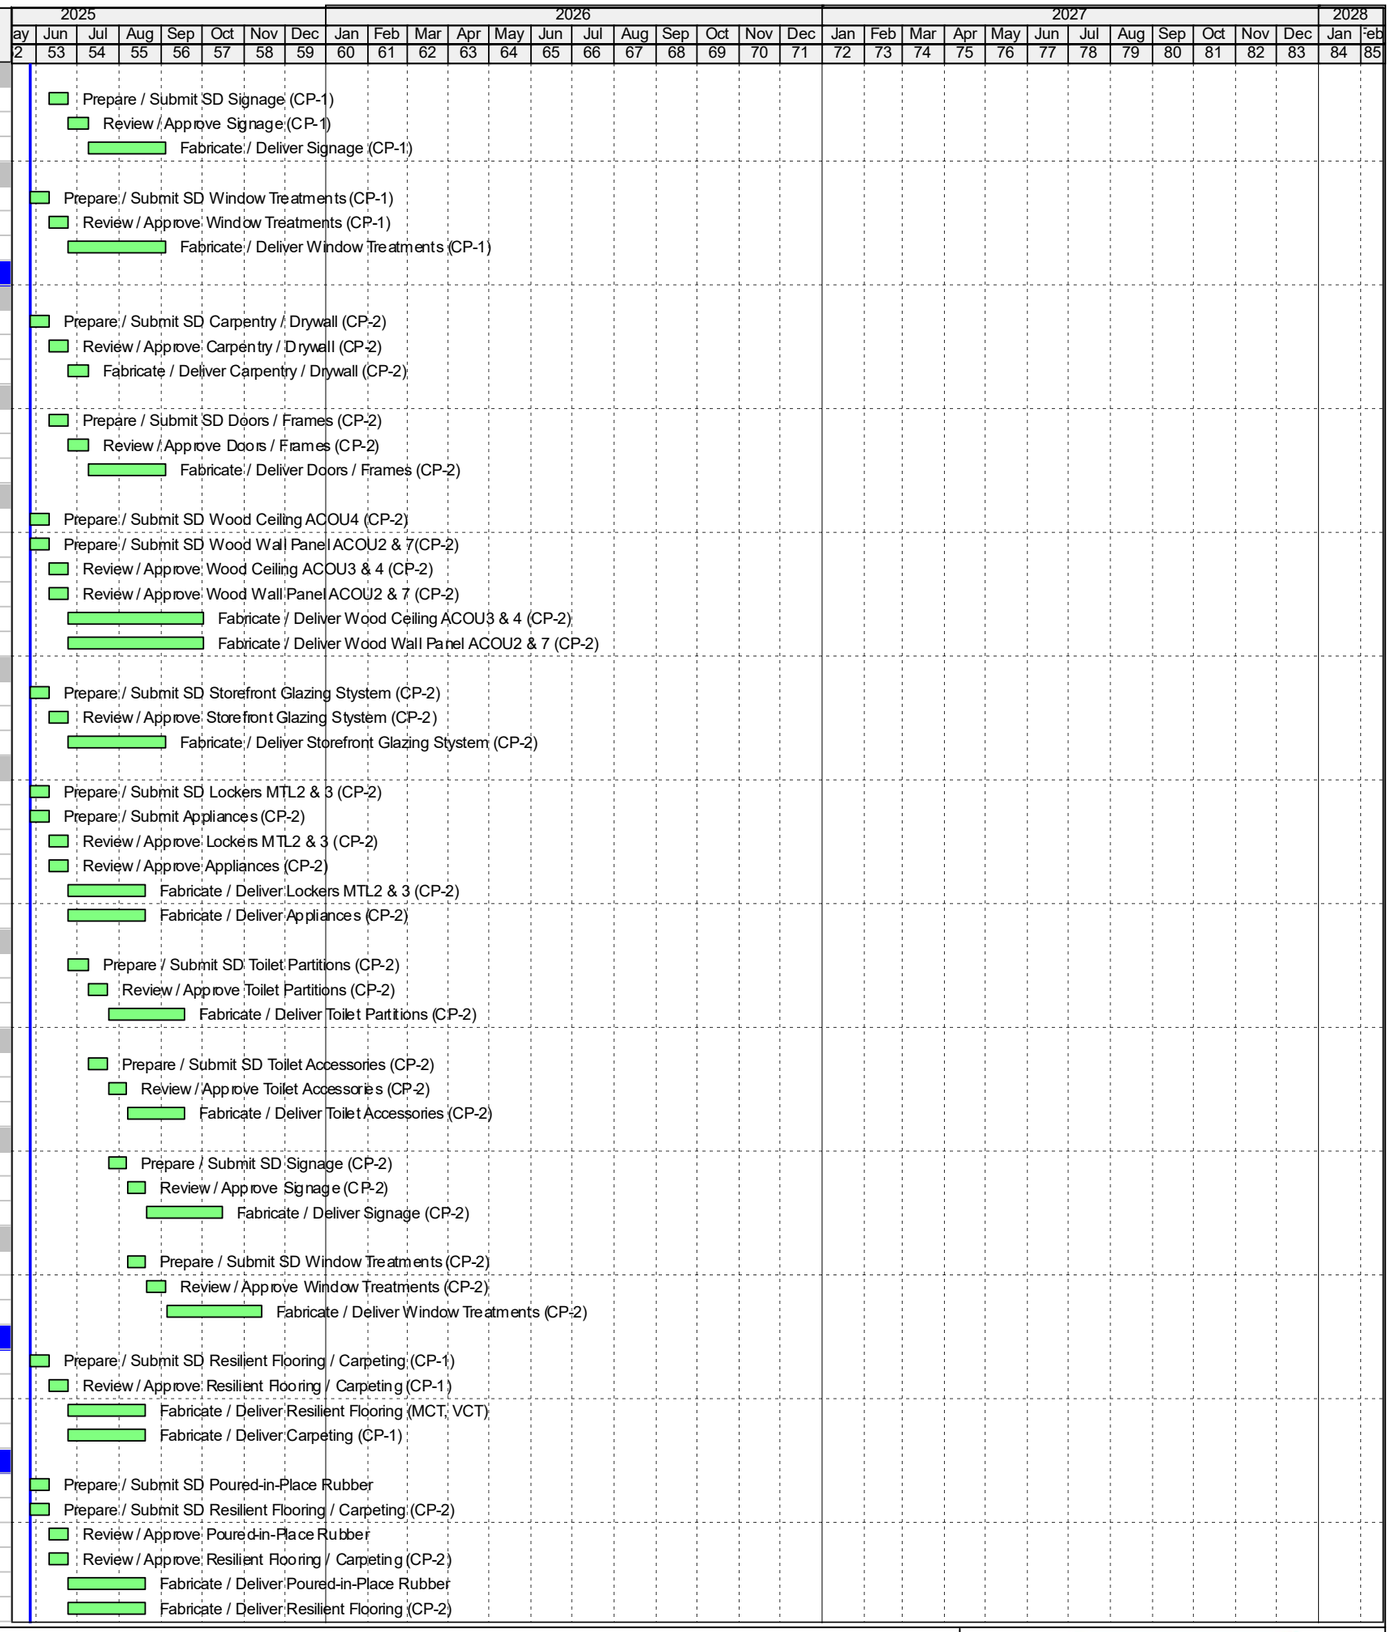


Finish Date: 04-Feb-28
Data Date: 28-May-25
Run Date: 11-Jun-25 16:20
BPL II - 09

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining ...
Summary Milestones
Critical Milestones
Milestone

Gilbane

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
A3300	Fabricate / Deliver Carpeting (CP-2)	40	40	25-Jun-25	20-Aug-25
BP09-H - Ceramic Tile / Terrazzo Tile (CP-1)					
A2300	Fabricate / Deliver Ceramic Tile (CP-1)	30	30	24-Mar-25 A	09-Jul-25
A3310	Fabricate / Deliver Terrazzo Tile Concrete Collaborative (CP-1)	70	57	24-Mar-25 A	15-Aug-25
A3960	Fabricate / Deliver Terrazzo Tile Nurrazzo (CP-1)	30	30	24-Mar-25 A	09-Jul-25
BP09-I - Ceramic Tile / Terrazzo Tile (CP-2)					
A2270	Fabricate / Deliver Ceramic Tile (CP-2)	40	40	28-May-25	23-Jul-25
A3320	Fabricate / Deliver Terrazzo Tile Nurrazzo (CP-2)	30	30	28-May-25	09-Jul-25
A5770	Fabricate / Deliver Terrazzo Tile Concrete Collaborative (CP-2)	70	70	28-May-25	04-Sep-25
BP-09J - Painting (CP-1)					
A2240	Fabricate / Deliver Painting (CP-1)	5	5	28-May-25	03-Jun-25
BP-09K - Painting (CP-2)					
A2210	Fabricate / Deliver Painting (CP-2)	5	5	28-May-25	03-Jun-25
BP-22B - Plumbing (CP-1)					
P1060	Prepare / Submit Plumbing Piping Shop Drawings / Material PD - DWV / HW / C\	25	25	04-Jun-25	09-Jul-25
P1130	Fabricate / Deliver Domestic Water Pump	1	1	04-Jun-25	04-Jun-25
P1070	Review and Approve Piping Shops Drawings / Plumbing Materials	10	10	10-Jul-25	23-Jul-25
P1100	Fabricate / Deliver Piping Materials	10	10	10-Jul-25	23-Jul-25
P1110	Fabricate / Deliver Plumbing Fixtures	15	15	24-Jul-25	13-Aug-25
Fire Protection					
A2100	Prepare / Submit SD Fire Protection (CP-1/CP-2)	10	10	28-May-25	10-Jun-25
A2110	Review / Approve Fire Protection (CP-1/CP-2)	10	10	11-Jun-25	24-Jun-25
A2120	Fabricate / Deliver Fire Protection (CP-1/CP-2)	40	40	25-Jun-25	20-Aug-25
BP-22C - Plumbing (CP-2)					
P1190	Prepare / Submit Plumbing Piping Shop Drawings / Material PD - DWV / HW / C\	25	25	28-May-25	01-Jul-25
P1240	Fabricate / Deliver Plumbing Fixtures	15	15	28-May-25	17-Jun-25
P1200	Review and Approve Piping Shops Drawings / Plumbing Materials	10	10	02-Jul-25	16-Jul-25
P1210	Fabricate / Deliver Piping Materials	10	10	02-Jul-25	16-Jul-25
BP-23B - HVAC (CP-1)					
M-1680	BIM Coordination Sub-Phase A	40	10	08-Apr-25 A	10-Jun-25
M-1150	Fabricate / Deliver CRAC Units	80	10	14-Apr-25 A	10-Jun-25
M-1180	Fabricate / Deliver VRV / HR Box / Piping	35	24	21-Apr-25 A	30-Jun-25
M-1360	Fabricate and Deliver DOAS Units	80	80	22-Apr-25 A	18-Sep-25
M-1350	Fabricate and Deliver Air Handling Units	140	80	29-Apr-25 A	18-Sep-25
M-1120	Review and Approve Grills and Diffusers	10	5	19-May-25 A	03-Jun-25
M-1160	Fabricate / Deliver RTU	85	85	28-May-25	25-Sep-25
M-1170	Fabricate / Deliver ACC Condensing Units	35	35	28-May-25	16-Jul-25
M-1200	Fabricate / Deliver Electric Heaters	45	45	28-May-25	30-Jul-25
M-1260	Review and Approve Chillers / Shop Drawings	10	10	28-May-25	10-Jun-25
M-1300	Fabricate / Deliver Roof Curbs & Equipment Rails	20	20	28-May-25	24-Jun-25
M-1430	Prepare / Submit Fans	10	5	28-May-25 A	03-Jun-25
M-1460	Prepare / Submit Louvers	10	5	28-May-25 A	03-Jun-25
M-1490	Prepare / Submit Sound Attenuator ST	10	5	28-May-25 A	03-Jun-25
M-1190	Fabricate / Deliver Grills and Diffusers	35	35	04-Jun-25	23-Jul-25
M-1420	Review and Approve Fans	10	10	04-Jun-25	17-Jun-25
M-1450	Review and Approve Louvers	10	10	04-Jun-25	17-Jun-25
M-1480	Review and Approve Sound Attenuator ST	10	10	04-Jun-25	17-Jun-25
M-1270	Fabricate / Deliver Chillers Units	85	85	11-Jun-25	09-Oct-25
M-1630	Prepare / Submit Metal Ductwork Shop Drawings PA13	5	5	11-Jun-25	17-Jun-25
M-1650	Prepare / Submit Metal Ductwork Shop Drawings PA8A	5	5	11-Jun-25	17-Jun-25
M-1640	Prepare / Submit Metal Ductwork Shop Drawings PA12	5	5	11-Jun-25	17-Jun-25
M-1670	Prepare / Submit Metal Ductwork Shop Drawings PA9	5	5	11-Jun-25	17-Jun-25
M-1690	BIM Coordination Sub-Phase B	30	30	11-Jun-25	23-Jul-25
M-1440	Fabricate / Deliver Fans	45	45	18-Jun-25	20-Aug-25
M-1470	Fabricate / Deliver Louvers	20	20	18-Jun-25	16-Jul-25
M-1500	Fabricate / Deliver Sound Attenuator ST	30	30	18-Jun-25	30-Jul-25
M-1560	Review and Approve Metal Ductwork Shop Drawings PA13	10	10	18-Jun-25	01-Jul-25
M-1580	Review and Approve Metal Ductwork Shop Drawings PA12	10	10	18-Jun-25	01-Jul-25
M-1620	Review and Approve Metal Ductwork Shop Drawings PA9	10	10	18-Jun-25	01-Jul-25
M-1610	Review and Approve Metal Ductwork Shop Drawings PA8A	10	10	18-Jun-25	01-Jul-25
M-1210	Fabricate / Deliver Metal Ductwork PA8A	20	20	02-Jul-25	30-Jul-25
M-1510	Fabricate / Deliver Metal Ductwork PA13	15	15	02-Jul-25	23-Jul-25
M-1530	Fabricate / Deliver Metal Ductwork PA12	40	40	02-Jul-25	27-Aug-25

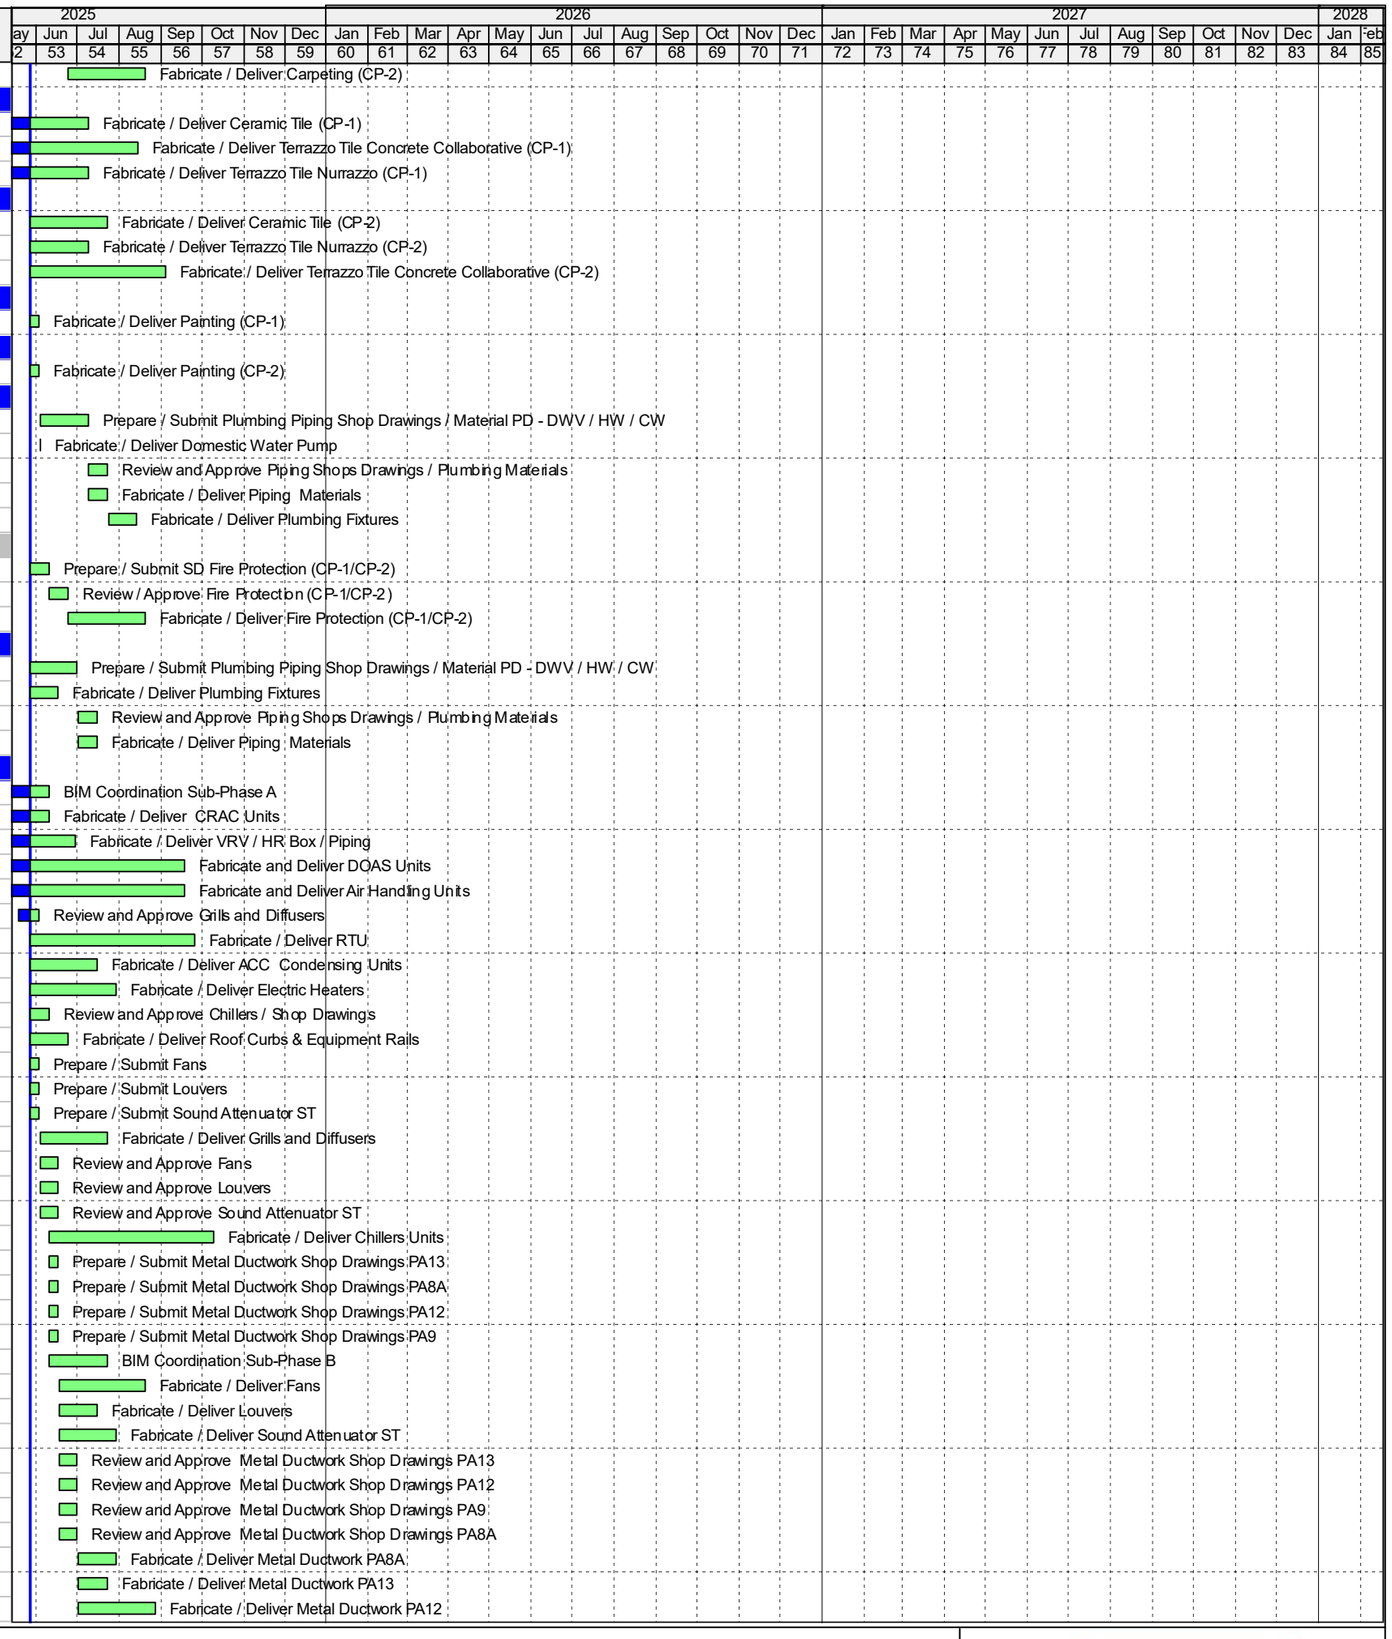


Finish Date: 04-Feb-28
Data Date: 28-May-25
Run Date: 11-Jun-25 16:20
BPL II - 09


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining ...
Summary Milestones
Critical Milestones
Milestone

Gilbane

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
M-1550	Fabricate / Deliver Metal Ductwork PA9	40	40	02-Jul-25	27-Aug-25
M-1050	Prepare / Submit Metal Ductwork Shop Drawings PA7	5	5	24-Jul-25	30-Jul-25
M-1660	Prepare / Submit Metal Ductwork Shop Drawings PA11	5	5	24-Jul-25	30-Jul-25
M-1140	Review and Approve Metal Ductwork Shop Drawings PA7	10	10	31-Jul-25	13-Aug-25
M-1570	Review and Approve Metal Ductwork Shop Drawings PA11	10	10	31-Jul-25	13-Aug-25
M-1520	Fabricate / Deliver Metal Ductwork PA11	25	25	14-Aug-25	18-Sep-25
M-1540	Fabricate / Deliver Metal Ductwork PA7	35	35	14-Aug-25	02-Oct-25
BP-23C - HVAC (CP-2)					
M-1410	Fabricate / Deliver VRV / HR Box / Piping (PA6,8B)	30	24	21-Apr-25 A	29-Jul-25
M-1220	Prepare / Submit Metal Ductwork Shop Drawings	15	15	28-May-25	17-Jun-25
M-1390	Prepare / Submit VRV / HR Box / Piping Shop Drawings (PA6,8B)	10	10	28-May-25	10-Jun-25
M-1590	Prepare / Review and Approve ACC-10D Relocation SD	25	25	28-May-25	01-Jul-25
M-1400	Review and Approve VRV / HR Box / Piping Shop Drawings (PA6,8B)	10	10	11-Jun-25	24-Jun-25
M-1230	Review and Approve Metal Ductwork Shop Drawings	10	10	18-Jun-25	01-Jul-25
M-1240	Fabricate / Deliver Metal Ductwork	20	20	02-Jul-25	30-Jul-25
BP-26B - Electrical / FA / IT / Security / AV / Projection Screens (CP-1)					
E1140	Review and Approve Light Fixtures	10	10	09-May-25 A	17-Jun-25
E1180	Prepare / Submit Electrical Devices	15	15	28-May-25	17-Jun-25
E1160	Prepare / Submit Power Panels	15	15	04-Jun-25	24-Jun-25
E1220	Prepare / Submit IT / AV / Security PD	20	20	04-Jun-25	01-Jul-25
E1150	Fabricate / Deliver Light Fixtures	60	60	18-Jun-25	11-Sep-25
E1190	Review and Approve Electrical Devices	10	10	18-Jun-25	01-Jul-25
E1170	Review and Approve Power Panels	10	10	25-Jun-25	09-Jul-25
E1200	Fabricate Electrical Devices	10	10	02-Jul-25	16-Jul-25
E1230	Review and Approve IT / AV / Security PD	20	20	02-Jul-25	30-Jul-25
E1210	Fabricate / Deliver Power Panels	50	50	10-Jul-25	18-Sep-25
E1240	Fabricate / Deliver IT / AV / Security PD	30	30	31-Jul-25	11-Sep-25
BP-26C - Electrical / FA / IT / Security / AV / Projection Screens (CP-2)					
E1470	Review and Approve Light Fixtures	10	10	09-May-25 A	10-Jun-25
E1450	Prepare / Submit Power Panels	15	15	28-May-25	17-Jun-25
E1460	Prepare / Submit Electrical Devices	15	15	28-May-25	17-Jun-25
E1500	Fabricate / Deliver Light Fixtures	60	60	11-Jun-25	04-Sep-25
E1480	Review and Approve Power Panels	10	10	18-Jun-25	01-Jul-25
E1490	Review and Approve Electrical Devices	10	10	18-Jun-25	01-Jul-25
E1510	Fabricate Electrical Devices	10	10	02-Jul-25	16-Jul-25
E1520	Fabricate / Deliver Power Panels	50	50	02-Jul-25	11-Sep-25
Master Plan Phase II Construction					
Swing Space Construction					
PA 10E Third Floor					
SP3530	Punchlist - PA10E	10	1	05-May-25 A	28-May-25
SP2320	Install Lockers	1	1	17-Jul-25	17-Jul-25
Chiller and Cooling Towers					
CHCT11	Install Heat Trace On Cooling Tower Piping	5	3	20-May-25 A	30-May-25
CHCT11	Install Ladder/Cage CT-2	1	1	28-May-25	28-May-25
CHCT11	Insulate Piping To Cooling Towers	5	5	02-Jun-25	06-Jun-25
Sub-Phase A					
Project Area 8A - 2nd Floor IT/ Data Center					
Detail					
RTU and ACC					
8A-10	Shaft Opening(s) - Wall Openings and Floor Openings	10	10	04-Jun-25	17-Jun-25
8A-21	Roofing Removal / Temporary Box Installation CU, DOAS, ACC, Duct Openings -	4	4	10-Jul-25	15-Jul-25
8A-21	Remove Concrete Slab For MEP Openings and Equipment Post - PA8A & 11	3	3	16-Jul-25	18-Jul-25
8A-20	Structural Steel Installation Above Roof - CU, DOAS, ACC Unit Area 8A	3	3	21-Jul-25	23-Jul-25
8A-10	Install SA and RA Duct Riser (Test & Insulate)	7	7	24-Jul-25	01-Aug-25
8A-10	DOAS-8A and ACC 5A and 5B Curb/Dunnage Installation	10	10	24-Jul-25	06-Aug-25
8A-20	Install CU 5A and 5B Roof Curbs	3	3	24-Jul-25	28-Jul-25
8A-22	Remove Temp Box / Patch Exisitng Roof & Waterproofing At Steel Post - Area 8A	2	2	24-Jul-25	25-Jul-25
8A-20	Rig and Install CU 5A and 5B at Roof	3	3	29-Jul-25	31-Jul-25
8A-10	New ACC 5A at Roof	2	2	07-Aug-25	08-Aug-25
8A-11	Refrigerant Piping - Roof to 2nd Floor	5	5	11-Aug-25	15-Aug-25
8A-11	Power to Equipment	5	5	18-Aug-25	22-Aug-25
8A-12	Close Shafts	5	5	25-Aug-25	29-Aug-25

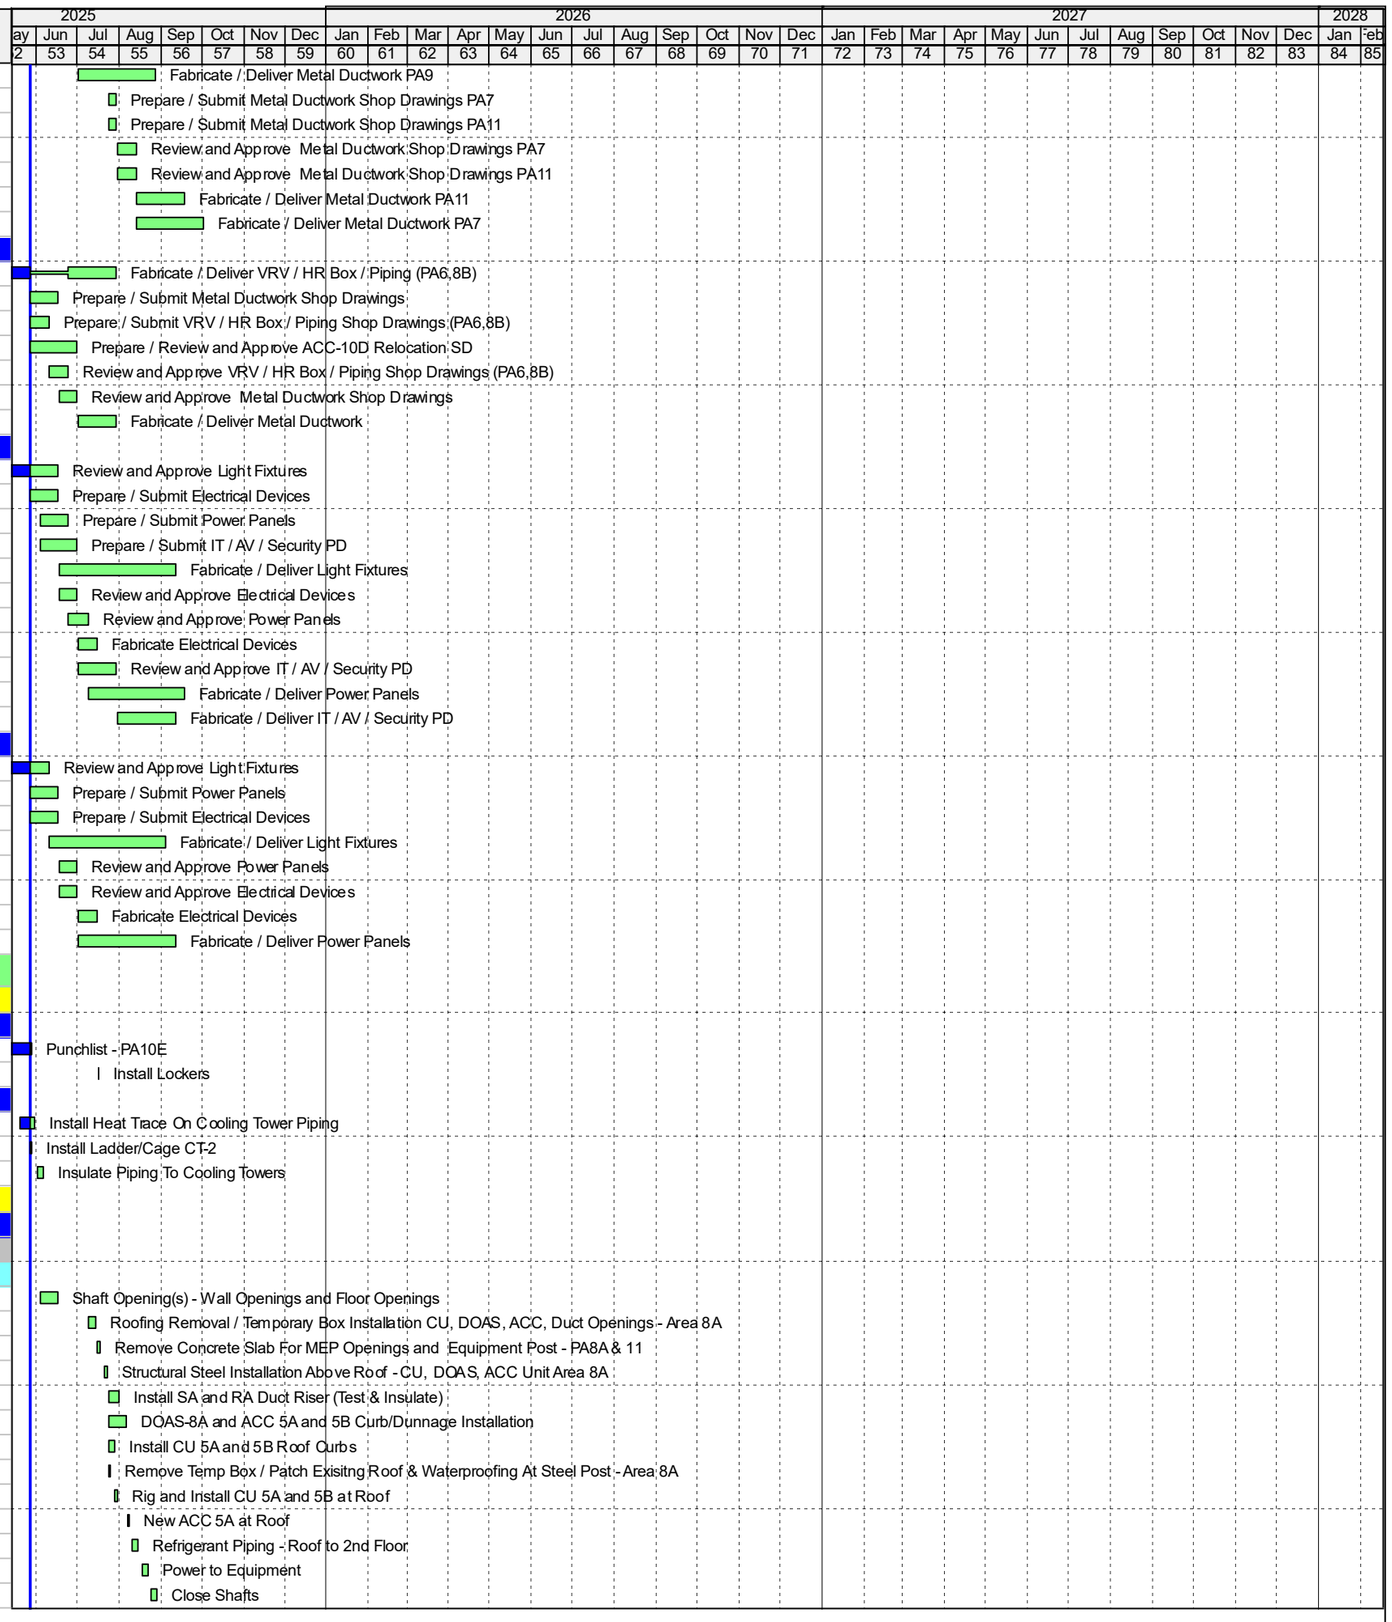

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
8A-10(	Rig New DOAS-8A / New Ductwork	4	4	19-Sep-25	24-Sep-25
8A-14'	Mechanical Equipment Final Connections	5	5	25-Sep-25	01-Oct-25
8A-14:	Mechanical Equipment Startup	2	2	02-Oct-25	03-Oct-25
8A-14:	Mechanical Equipment Testing & Balancing	5	5	06-Oct-25	10-Oct-25
Data Center					
8A-20:	Consultation & Design For Temporary Space	6	6	28-May-25	04-Jun-25
8A-20'	Prepare & Issue Construction Documents For Temporary Space - TMA	10	10	05-Jun-25	18-Jun-25
8A-20:	Construct Temporary Data Center / New Demark Wall	20	20	18-Jul-25	14-Aug-25
8A-21(	Install Temp Patch Panel For IDFs & Run New Data to Existing and New	10	10	18-Jul-25	31-Jul-25
8A-20!	Install CRAC Units and 200A Disconnect Switches	7	7	01-Aug-25	11-Aug-25
8A-20(	Relocate ECP-1 and ECP-2	5	5	01-Aug-25	07-Aug-25
8A-20(	ISPs Relocate Equipment To New Demark Location	10	10	15-Aug-25	28-Aug-25
8A-20!	Install New Racks In Temp Data Center	5	5	15-Aug-25	21-Aug-25
8A-20!	Install UPS's & Network Switches In Temp Data Center	10	10	22-Aug-25	05-Sep-25
8A-21:	Install Structural Cabling From New Demark Location To Temp Data Center	5	5	29-Aug-25	05-Sep-25
8A-20:	Relocate Existing IT Equipment to Temporary Data Center	15	15	08-Sep-25	26-Sep-25
8A-20:	Demo and Construct New Data Center / Area 8A	20	20	29-Sep-25	24-Oct-25
8A-20'	Relocate Data Center from Temporary Location to Final Location	10	10	27-Oct-25	07-Nov-25
Interior Space					
8A-16'	Remove Existing Standpipe Manifold At Roof - Area 8A	1	1	04-Jun-25	04-Jun-25
8A-10'	Demolition - Area 8A	8	8	16-Jun-25	25-Jun-25
8A-11:	ACM Testing Above Ceilings & Behind Walls - Area 8A	2	2	26-Jun-25	27-Jun-25
8A-14(	ACM Report Preperation & Issuance - Area 8A	3	3	30-Jun-25	02-Jul-25
8A-10!	Asbestos Abatement - Area 8A	10	10	03-Jul-25	17-Jul-25
8A-10:	Rough-in Overhead HVAC Ductwork - Area 8A	13	13	18-Jul-25	05-Aug-25
8A-10!	Install Indoor AC Units (AC-5A thru 5D) above Ceiling - Area 8A	3	3	18-Jul-25	22-Jul-25
8A-20'	Chip Out Concrete Encasement For Steel Installation - Area 8A	2	2	18-Jul-25	21-Jul-25
8A-16:	Remove 1st Floor Ceiling For Plumbing Installation - Area 8A	2	2	18-Jul-25	21-Jul-25
8A-11:	Install Overhead Refrigerant Piping - Area 8A	10	10	23-Jul-25	05-Aug-25
8A-111	Frame New Walls - Area 8A	3	3	06-Aug-25	08-Aug-25
8A-11'	Power to AC Units - Area 8A	5	5	06-Aug-25	12-Aug-25
8A-11(	Rough-in Overhead Electrical - Area 8A	5	5	06-Aug-25	12-Aug-25
8A-13!	Plumbing Rough In (1st Floor Ceiling) - PA 8A	7	7	06-Aug-25	14-Aug-25
8A-11'	In-Wall Electrical Rough-in - Area 8A	5	5	11-Aug-25	15-Aug-25
8A-15:	Millwork Field Measurements - Area 8A	1	1	11-Aug-25	11-Aug-25
8A-26-	Install In-Wall Countertop & Millwork Support - Area 8A	1	1	11-Aug-25	11-Aug-25
8A-11(	Set Hollow Metal Door Frames - Area 8A	1	1	14-Aug-25	14-Aug-25
8A-13:	Hang New Doors and Install Hardware - Area 8A	3	3	15-Aug-25	19-Aug-25
8A-11!	In-Wall Inspection - Area 8A	1	1	18-Aug-25	18-Aug-25
8A-12(	Sheetrock Walls (Including Taping and Sanding) - Area 8A	5	5	19-Aug-25	25-Aug-25
8A-20!	Fireproofing Installation - Area 8A	1	1	21-Aug-25	21-Aug-25
8A-16:	Install New Standpipe Manifold In Bulkhead - Area 8A	2	2	21-Aug-25	22-Aug-25
8A-12:	Frame New Gyp. Ceilings - Area 8A	5	5	26-Aug-25	02-Sep-25
8A-12:	Light Fixture Rough-in @ Gyp. Ceiling - Area 8A	5	5	03-Sep-25	09-Sep-25
8A-12-	HVAC Drops @ Gyp. Ceiling - Area 8A	5	5	03-Sep-25	09-Sep-25
8A-12(	Gypsum & ACOU1 Ceilings (Including Taping and Sanding) - Area 8A	10	10	10-Sep-25	23-Sep-25
8A-12!	Patch/Repair Existing Exposed Ceiling - Area 8A	5	5	17-Sep-25	23-Sep-25
8A-12'	Prime/1st Coat Walls and Ceilings - Area 8A	2	2	24-Sep-25	25-Sep-25
8A-27(	Install Frame for Glazing Wall System with Wood Cladding - Area 8A	3	3	24-Sep-25	26-Sep-25
8A-12!	Install Suspended Light Fixtures - Area 8A	5	5	26-Sep-25	02-Oct-25
8A-12!	Install Ceiling Mount Diffusers - Area 8A	5	5	26-Sep-25	02-Oct-25
8A-27'	Install Glazing & Doors for Glazing Wall System - Area 8A	3	3	29-Sep-25	01-Oct-25
8A-13'	Install Electrical & FA Devices and Trim - Area 8A	5	5	30-Sep-25	06-Oct-25
8A-13:	Install Resilient Flooring - Area 8A	3	3	03-Oct-25	07-Oct-25
8A-16(	Wood Ceiling Panel Installation ACOU4 - Area 8A	4	4	03-Oct-25	08-Oct-25
8A-15!	Install Acoustic Wall Panel ACOU2 - Area 8A	2	2	03-Oct-25	06-Oct-25
8A-13(	Install New Millwork - Area 8A	10	10	09-Oct-25	22-Oct-25
8A-13-	Final Paint - Area 8A	5	5	23-Oct-25	29-Oct-25
8A-15'	Owner FF&E Installation	5	5	23-Oct-25	29-Oct-25
8A-15!	Appliances Installation - Area 8A	1	1	23-Oct-25	23-Oct-25
8A-13!	Rolling Completion Work - Area 8A	5	5	30-Oct-25	05-Nov-25
8A-15!	Window Shade Installation - Area 8A	4	4	30-Oct-25	04-Nov-25
8A-15(	Signage Installation - Area 8A	2	2	30-Oct-25	31-Oct-25

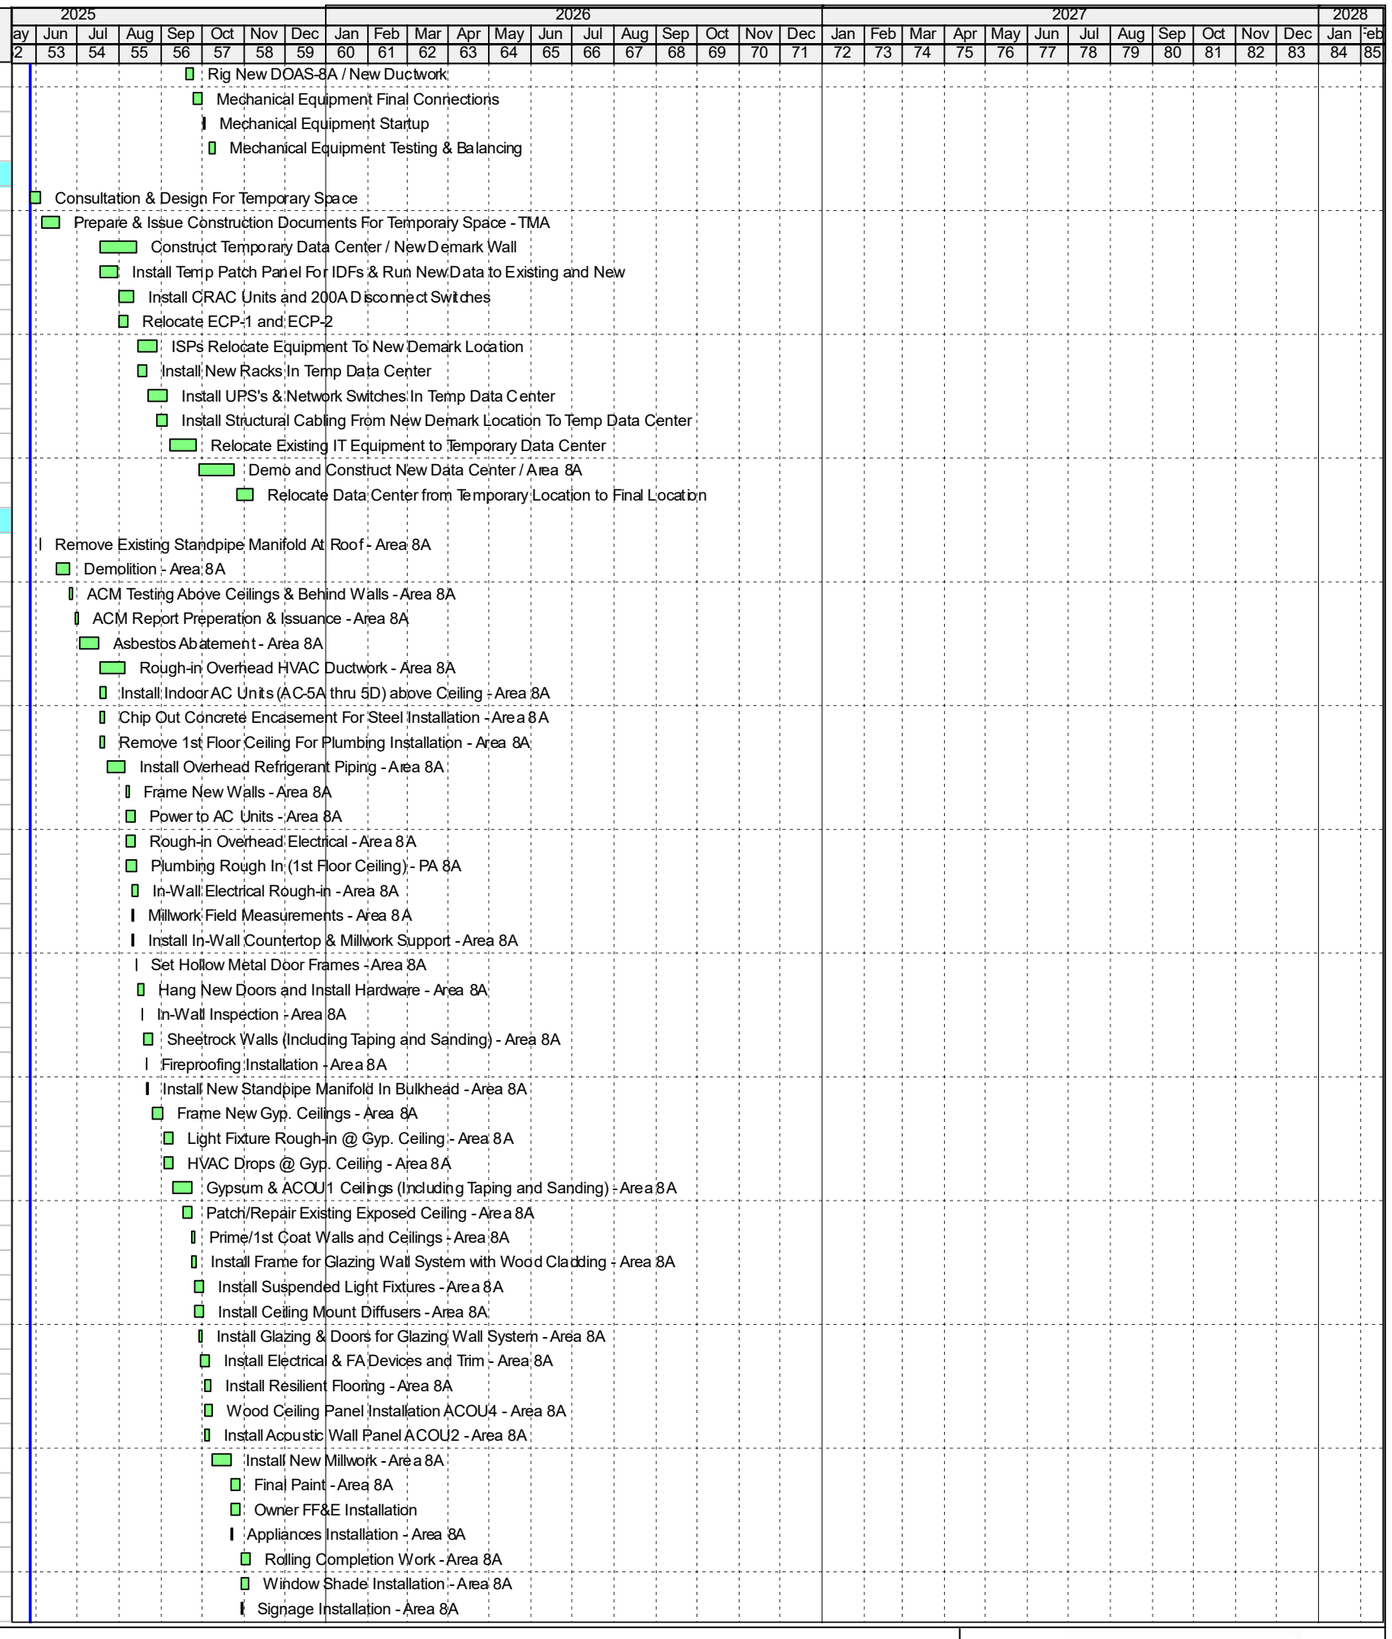


Finish Date: 04-Feb-28
Data Date: 28-May-25
Run Date: 11-Jun-25 16:20
BPL II - 09


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining ...
Summary Milestones
Critical Milestones
Milestone

Gilbane

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
8A-14	Call Center 243 Construction	10	10	10-Nov-25	24-Nov-25
8A-13	Construction Final Cleaning	2	2	25-Nov-25	26-Nov-25
8A-13	Substantial Completion - Area 8A	0	0		26-Nov-25
Bathrooms					
8A-15	Frame New Gyp. Ceilings - Area 8A	1	1	26-Aug-25	26-Aug-25
8A-14	RDG Installation Bathrooms - Area 8A	1	1	27-Aug-25	27-Aug-25
8A-14	Light Fixture Installation Bathrooms - Area 8A	1	1	12-Sep-25	12-Sep-25
8A-15	Sheetrock Gyp. Ceilngs Bathrooms (Including Taping and Sanding) - Area 8A	3	3	15-Sep-25	17-Sep-25
8A-13	Install Ceramic Tile At WC 241B - Area 8A	5	5	18-Sep-25	24-Sep-25
8A-14	Install Built-IN WC Countertop and Backsplash STN - Area 8A	1	1	25-Sep-25	25-Sep-25
8A-15	Paint Ceilings Bathrooms - Area 8A	1	1	25-Sep-25	25-Sep-25
8A-14	Install Plumbing Fixtures - Area 8A	1	1	26-Sep-25	26-Sep-25
8A-15	Install Mirrors - Area 8A	1	1	26-Sep-25	26-Sep-25
8A-14	Install Bathroom Accesories - Area 8A	1	1	29-Sep-25	29-Sep-25
Project Area 9 - 2nd Floor Youth Wing					
Detail					
AHU and ACC					
9-2141	Structural Probes - Area 9	1	1	07-Jul-25	07-Jul-25
9-2121	Roofing Removal / Curb Flashing ACC 9A - Area 9 North Penthouse	4	4	10-Jul-25	15-Jul-25
9-1190	Lintel Installation For Duct Wall Opening In Bulkhead - Area 9	1	1	10-Jul-25	10-Jul-25
9-2251	Roofing Removal & Temp Box Installation RTU-9 - Area 9	1	1	10-Jul-25	10-Jul-25
9-2151	Wall Openings For Ductwork From RTU-9 - Area 9	1	1	11-Jul-25	11-Jul-25
9-2211	Concrete Slab Removal For Steel Post RTU-9 - Area 9	1	1	16-Jul-25	16-Jul-25
9-2201	Structural Steel Installation Above Roof - RTU-9	3	3	17-Jul-25	21-Jul-25
9-2651	Remove Temp Box / Patch Exisitng Roof & Waterproofing At Steel Post - Area 9	1	1	22-Jul-25	22-Jul-25
9-1030	Install ACC-9A & RTU-9 Roof Curb (EPW Roof) - Area 9	5	5	05-Aug-25	11-Aug-25
9-2162	Chip Out Concrete Encasement For Steel Installation - Area 9 North Penthouse	2	2	05-Aug-25	06-Aug-25
9-1470	Extend Equipment Pad - Area 9	2	2	05-Aug-25	06-Aug-25
9-1060	Wall Opening In Exterior Wall For AHU-2 Rigging - Area 9	3	3	05-Aug-25	07-Aug-25
9-2171	Structural Steel Installation - ACC 9A & Area 9 North Penthouse For ACCUs	4	4	07-Aug-25	12-Aug-25
9-1070	Install AC Condensing Unit (Unit ACC-9A) mounted on Roof Curbs - Area 9	5	5	12-Aug-25	18-Aug-25
9-2181	Fireproofing Installation - Area 9 North Penthouse	1	1	21-Aug-25	21-Aug-25
9-1100	Install Power to ACC-9A & RTU-2 on Roof - Area 9	5	5	03-Sep-25	09-Sep-25
9-1195	ACC - 9A Charge and Start Up	2	2	10-Sep-25	11-Sep-25
9-1050	Rig-in and Install New AHU-2 & RTU-9 and Associated Ductwork including Tie-ins	20	20	26-Sep-25	23-Oct-25
9-1170	Replace (Install New) Exhaust and Intake Louvers - Area 9 AHU-2	3	3	24-Oct-25	28-Oct-25
9-1180	Install Power to AHU-2 - Area 9	2	2	24-Oct-25	27-Oct-25
9-2161	Exterior Wall Patching / Stucco Finish At Bulkhead- Area 9	3	3	24-Oct-25	28-Oct-25
9-1185	AHU-2 & RTU-9 - Start Up	3	3	29-Oct-25	31-Oct-25
9-2711	Mechanical Equipment Testing & Balancing	5	5	03-Nov-25	07-Nov-25
Interior Space					
9-1010	Demolition (Including Equipment Room) - Area 9	15	15	16-Jun-25	07-Jul-25
9-1550	Disconnect / Remove Existing Standpipe & FHR - Area 9	3	3	20-Jun-25	24-Jun-25
9-1000	Install Temp. Partitions - Area 9	3	3	08-Jul-25	10-Jul-25
9-1041	ACM Testing Above Ceilings & Behind Walls - Area 9	2	2	08-Jul-25	09-Jul-25
9-1042	ACM Report Preperation & Issuance - Area 9	3	3	10-Jul-25	14-Jul-25
9-0999	Asbestos Abatement (Including Windows)- Area 9	15	15	15-Jul-25	04-Aug-25
9-1040	Rough-in Overhead HVAC Ductwork - Area 9	10	10	05-Aug-25	18-Aug-25
9-1080	Install Heat Recovery Box (HR-9A) above Ceiling - Area 9	5	5	05-Aug-25	11-Aug-25
9-1090	Install Indoor AC Units (AC-9A thru AC-9F) above Ceiling - Area 9	5	5	05-Aug-25	11-Aug-25
9-1480	Exterior Window Glazing Installation / Window Restoration - Area 9	10	10	05-Aug-25	18-Aug-25
9-1500	Install Unistrut At Arcade Millwork	5	5	05-Aug-25	11-Aug-25
9-1151	Sawcut Slab for HSS Installation Under Fins	3	3	05-Aug-25	07-Aug-25
9-2691	Remove 1st Floor Ceiling For Plumbing Installation - Area 9	2	2	05-Aug-25	06-Aug-25
9-1570	Open Ceiling In PA6 For Waste Rough-In - Area 9	1	1	05-Aug-25	05-Aug-25
9-1580	Rough-In Overhead Waste PA6 - Area 9	3	3	06-Aug-25	08-Aug-25
9-1020	Rough-in Overhead Plumbing & Connect to Existing Riser P/9. - Area 9	5	5	07-Aug-25	13-Aug-25
9-1141	Install HSS Below Arch Fin	5	5	08-Aug-25	14-Aug-25
9-1590	Patch Ceiling / Tape / Spackle PA6 - Area 9	3	3	11-Aug-25	13-Aug-25
9-1130	Install Overhead Refrigerant Piping - Area 9	15	15	12-Aug-25	02-Sep-25
9-1120	Frame New Walls - Area 9	5	5	19-Aug-25	25-Aug-25
9-1110	Rough-in Overhead Electrical - Area 9	10	10	19-Aug-25	02-Sep-25
9-1510	Slab Infill After HSS Install	1	1	21-Aug-25	21-Aug-25

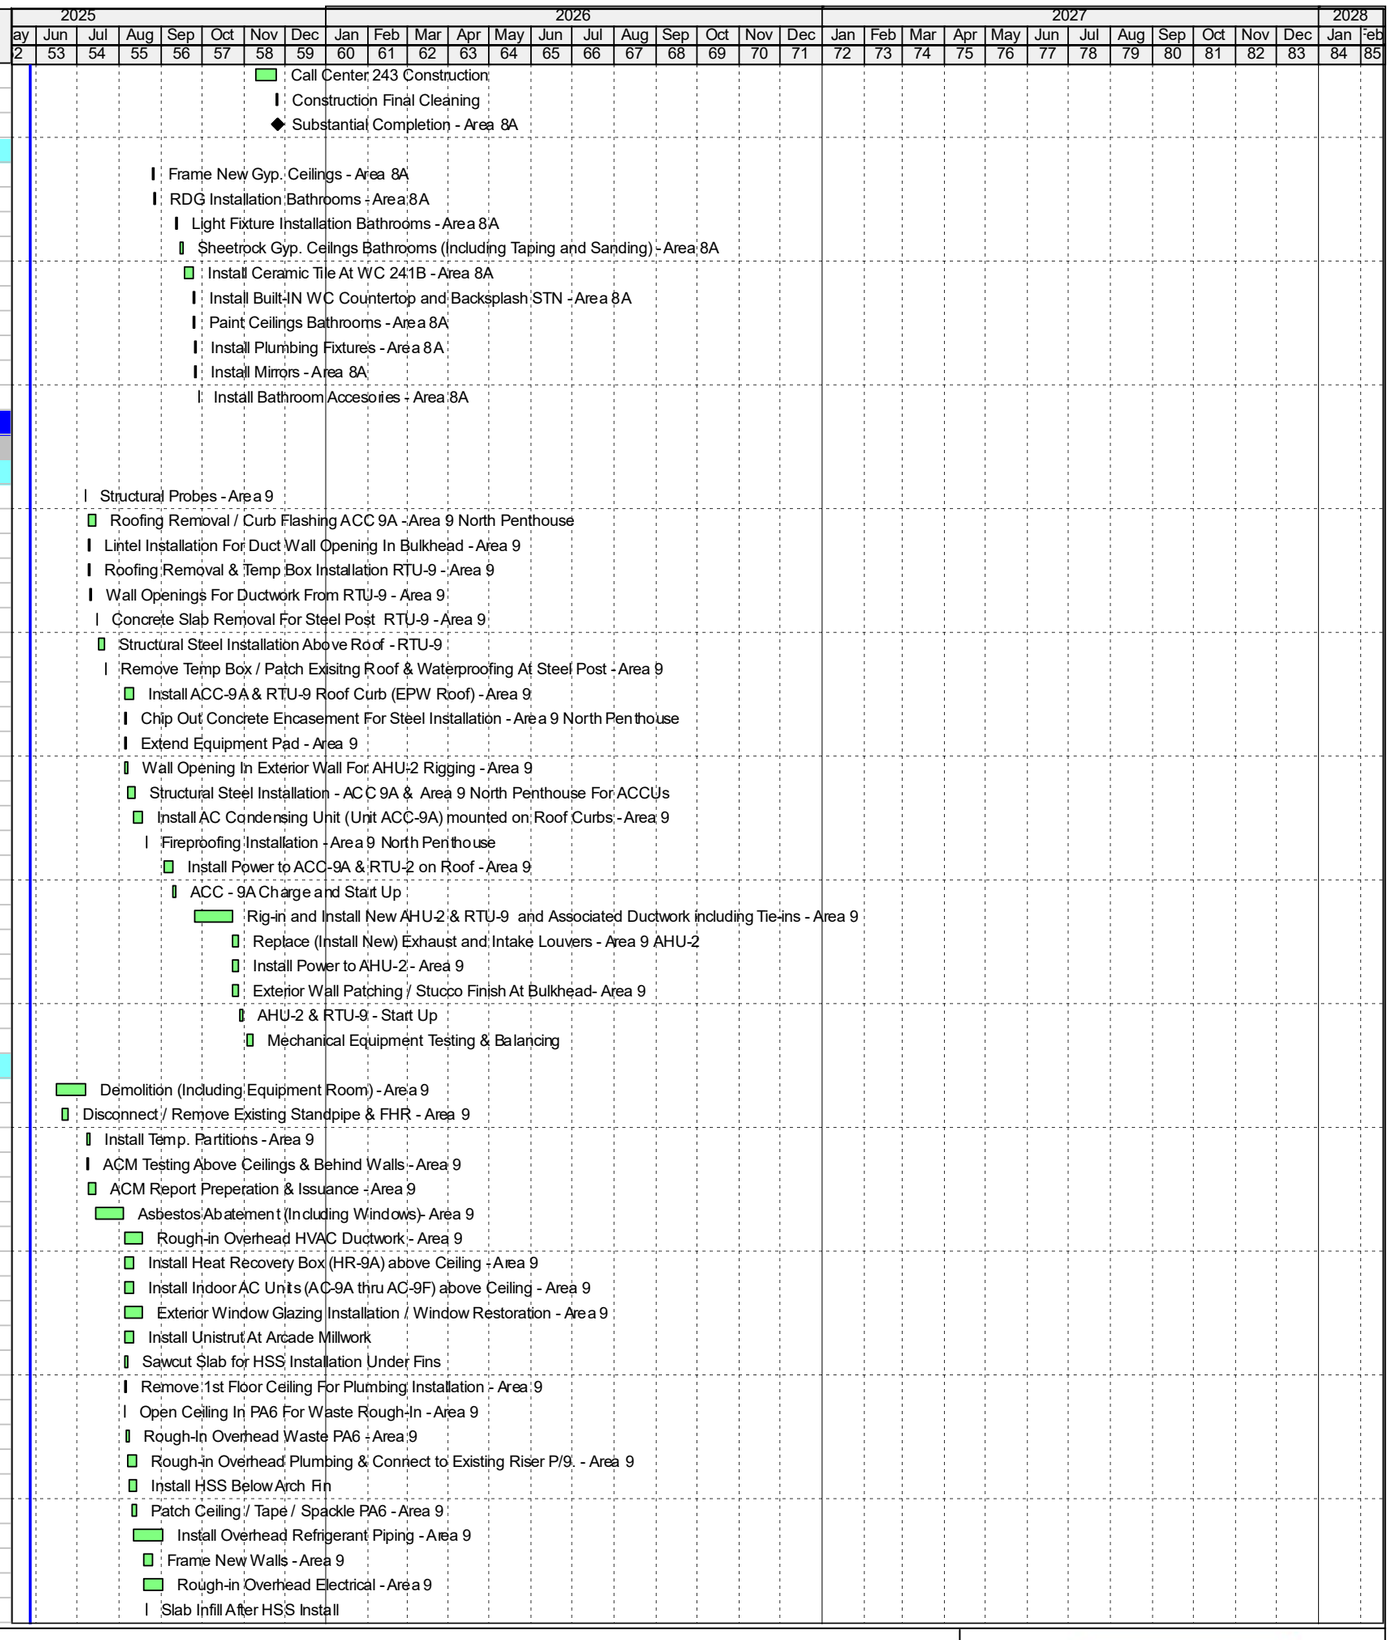

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
9-1560	Reroute Standpipe & Install New FH Cabinet - Area 9	2	2	21-Aug-25	22-Aug-25
9-1460	Slab Trenching / Poke-Thru For Elec. For Outlets & Lighting - Area 9	5	5	21-Aug-25	27-Aug-25
9-1160	In-Wall Plumbing Rough-in - Area 9	5	5	26-Aug-25	02-Sep-25
9-1200	In-Wall Electrical Rough-in - Area 9	10	10	26-Aug-25	09-Sep-25
9-1150	Set Hollow Metal Door Frames - Area 9	3	3	26-Aug-25	28-Aug-25
9-1140	Power to HR and AC Units - Area 9	5	5	26-Aug-25	02-Sep-25
9-1390	Millwork Field Measurement	1	1	26-Aug-25	26-Aug-25
9-2630	Install In-Wall Millwork Support - Area 9	1	1	26-Aug-25	26-Aug-25
9-1210	In-Wall Inspection - Area 9	1	1	10-Sep-25	10-Sep-25
9-1220	Sheetrock Walls (Including Taping and Sanding) - Area 9	7	7	11-Sep-25	19-Sep-25
9-1360	Hang New Doors and Install Hardware - Area 9	5	5	22-Sep-25	26-Sep-25
9-1230	Frame New Gyp. Ceilings - Area 9	5	5	22-Sep-25	26-Sep-25
9-1240	Light Fixture Rough-in @ Gyp. Ceiling - Area 9	7	7	29-Sep-25	07-Oct-25
9-1250	HVAC Drops @ Gyp. Ceiling - Area 9	7	7	29-Sep-25	07-Oct-25
9-1260	Gypsum & ACOU1 Ceilings (Including Taping and Sanding) - Area 9	10	10	08-Oct-25	21-Oct-25
9-1270	Patch/Repair Existing Exposed Ceiling - Area 9	5	5	15-Oct-25	21-Oct-25
9-1280	Prime/1st Coat Walls and Ceilings - Area 9	4	4	22-Oct-25	27-Oct-25
9-1421	Restore Existing Perimeter Millwork - Area 9	40	40	22-Oct-25	19-Dec-25
9-1530	Wood Ceiling Installation ACOU4 - Area 9	5	5	22-Oct-25	28-Oct-25
9-1290	Install Digital Display - Area 9	4	4	28-Oct-25	31-Oct-25
9-1310	Install Suspended Light Fixtures - Area 9	8	8	28-Oct-25	06-Nov-25
9-1320	Install Ceiling Mount Diffusers - Area 9	8	8	28-Oct-25	06-Nov-25
9-1330	Stair Finishes - Area 9	10	10	28-Oct-25	10-Nov-25
9-1490	Install Wood Frame & Caps WD6 - Area 9	3	3	28-Oct-25	30-Oct-25
9-1400	Install Glazing - Area 9	5	5	31-Oct-25	06-Nov-25
9-1340	Install Electrical & FA Devices and Trim - Area 9	5	5	31-Oct-25	06-Nov-25
9-2681	Install Acoustic Wall Panel ACOU2 - Area 9	2	2	31-Oct-25	03-Nov-25
9-1380	Install Terrazzo Tile Flooring - Area 9	10	10	07-Nov-25	21-Nov-25
9-1370	Install Projection Screens - Area 9	5	5	07-Nov-25	14-Nov-25
9-1300	Install New Millwork + Built-in Benches and Desks - Area 9	15	15	24-Nov-25	16-Dec-25
9-1540	Install Carpet At Studios - Area 9	2	2	24-Nov-25	25-Nov-25
9-1350	Install Plumbing Fixtures (Sinks) @ Millwork - Area 9	1	1	17-Dec-25	17-Dec-25
9-1410	Install Lighting At Millwork - Area 9	5	5	17-Dec-25	23-Dec-25
9-2671	Owner FF&E Installation - Area 9	5	5	17-Dec-25	23-Dec-25
9-2661	Appliances Installation - Area 9	1	1	17-Dec-25	17-Dec-25
9-1420	Final Paint - Area 9	5	5	18-Dec-25	24-Dec-25
9-1430	Rolling Completion Work - Area 9	5	5	26-Dec-25	02-Jan-26
9-1450	Construction Final Cleaning	2	2	26-Dec-25	29-Dec-25
9-2650	Window Shade Installation - Area 9	4	4	26-Dec-25	31-Dec-25
9-1520	Signage Installation - Area 9	2	2	26-Dec-25	29-Dec-25
9-1440	Substantial Completion - Area 9	0	0		02-Jan-26
Project Area 12 - 3rd Floor Eastern Parkway Wing Administration					
Detail					
AHU and ACC					
12-211	Roofing Removal / Temp Box / Curb Flashing ACC 12A, B, C, D - Area 12 North	2	2	10-Jul-25	11-Jul-25
12-211	Remove Concrete Slab For Duct Opening At Roof - PA12	1	1	14-Jul-25	14-Jul-25
12-103	Install ACC-12A, B and C Roof Curbs (EPW Roof) - Area 12	5	5	05-Aug-25	11-Aug-25
12-21(	Chip Out Concrete Encasement For Steel Installation - Area 12 North Penthouse	2	2	05-Aug-25	06-Aug-25
12-266	Wall Opening In Exterior Wall For AHU-1 Rigging - Area 9	3	3	05-Aug-25	07-Aug-25
12-211	Structural Steel Installation - ACC 12A, B, C - Area 12 North Penthouse	2	2	07-Aug-25	08-Aug-25
12-109	Install AC Condensing Unit (Unit ACC-12A, B, C, and D) mounted on Roof Curbs	5	5	12-Aug-25	18-Aug-25
12-113	Power to ACC-12A, B and C on Roof - Area 12	5	5	19-Aug-25	25-Aug-25
12-212	Fireproofing Installation - Area 12 North Penthouse	1	1	21-Aug-25	21-Aug-25
12-225	Extend Equipment Pad - Area 12	2	2	21-Aug-25	22-Aug-25
12-122	ACC-12A Charge and Start Up	2	2	26-Aug-25	27-Aug-25
12-107	Rig-in and Install New AH-1 and Associated Ductwork including Tie-ins - Area 12	20	20	19-Sep-25	16-Oct-25
12-12(	Replace (Install New) Exhaust and Intake Louvers - Area 12	5	5	17-Oct-25	23-Oct-25
12-121	Power to AHU-1 - Area 12	5	5	17-Oct-25	23-Oct-25
12-267	Exterior Wall Patching / Stucco Finish At Bulkhead- Area 9	3	3	17-Oct-25	21-Oct-25
12-121	AH-1 Start Up	3	3	24-Oct-25	28-Oct-25
12-27(	Mechanical Equipment Testing & Balancing - Area 12	5	5	29-Oct-25	04-Nov-25
Interior Space					
12-102	Demolition (Including Equipment Room) - Area 12	15	15	16-Jun-25	07-Jul-25

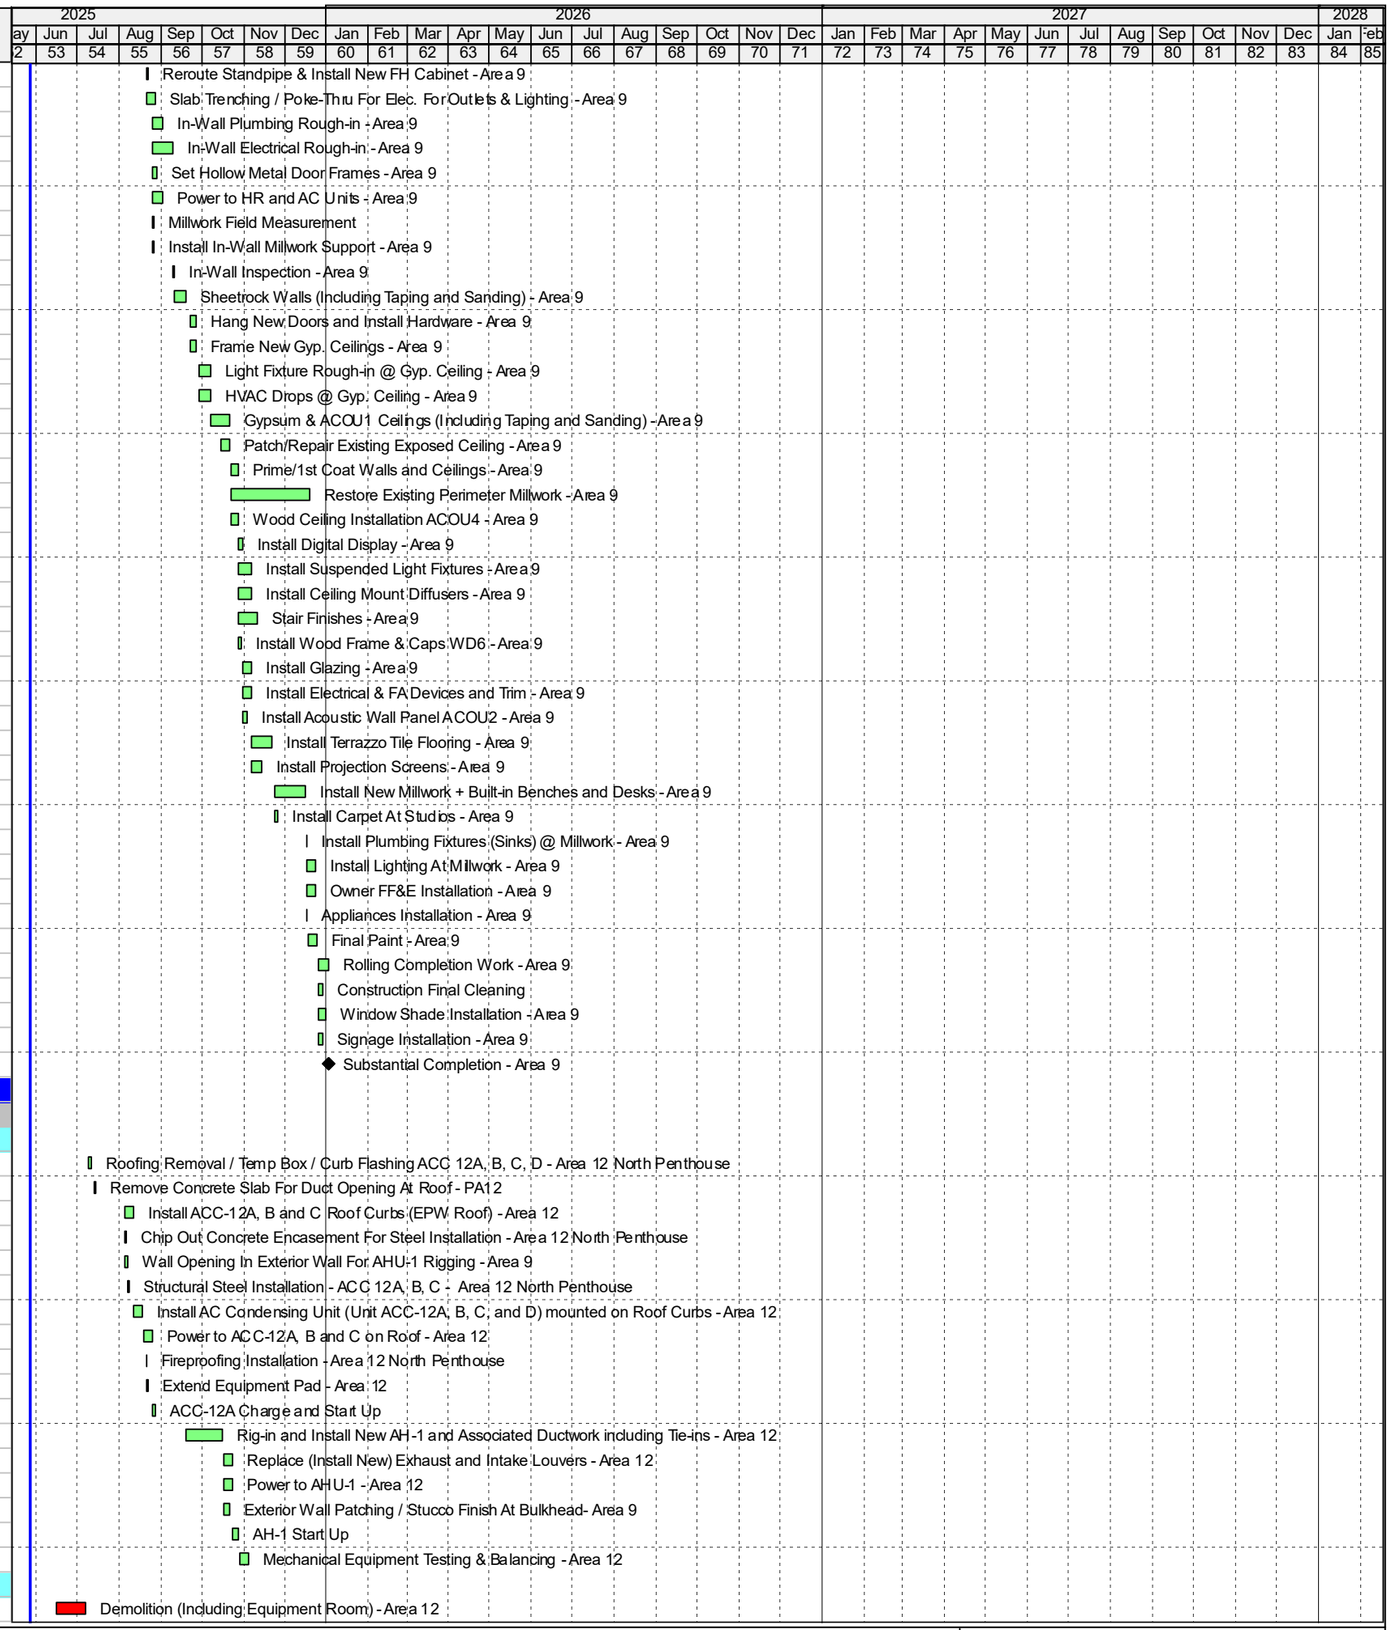


Finish Date: 04-Feb-28
Data Date: 28-May-25
Run Date: 11-Jun-25 16:20
BPL II - 09

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining ...
Summary Milestone
Critical Milestone
Milestone

Gilbane

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
12-108	Structural Probes Interior & Mech. Room - Area 12	2	2	03-Jul-25	07-Jul-25
12-228	ACM Testing Above Ceilings & Behind Walls - Area 12	2	2	08-Jul-25	09-Jul-25
12-229	ACM Report Preperation & Issuance - Area 12	3	3	10-Jul-25	14-Jul-25
12-100	Asbestos Removals - Removals Area 12	15	15	15-Jul-25	04-Aug-25
12-104	Rough-in Overhead HVAC Ductwork - Area 12	10	10	05-Aug-25	18-Aug-25
12-111	Install Heat Recovery Box (HR-9A) above Ceiling - Area 12	5	5	05-Aug-25	11-Aug-25
12-112	Install Indoor AC Units (AC-9A thru AC-9F) above Ceiling - Area 12	5	5	05-Aug-25	11-Aug-25
12-105	Rough-in Overhead Plumbing & Connect to Existing Riser P/8 and P/9. - Area 12	10	10	05-Aug-25	18-Aug-25
12-110	Install Plumbing Waste (below @ 2nd Floor Ceiling) - Area 12	5	5	05-Aug-25	11-Aug-25
12-106	Rough-in Poke Thru's for Floor Outlets from 2nd Floor Ceiling - Area 12	10	10	05-Aug-25	18-Aug-25
8A-213	Chip Out Concrete Encasement For Steel Installation - Area 12	2	2	05-Aug-25	06-Aug-25
12-152	Exterior Window Glazing Installation / Window Restoration - Area 12	15	15	05-Aug-25	25-Aug-25
8A-214	Structural Steel Installation - ACC 12D, EF-6 - Area 12	2	2	07-Aug-25	08-Aug-25
12-117	Install Overhead Refrigerant Piping - Area 12	15	15	12-Aug-25	02-Sep-25
12-115	Rough-in Overhead Electrical - Area 12	10	10	19-Aug-25	02-Sep-25
12-114	Heat Trace Water Piping - Area 12	5	5	19-Aug-25	25-Aug-25
12-116	Frame New Walls - Area 12	5	5	21-Aug-25	27-Aug-25
8A-215	Fireproofing Installation - Area 12	1	1	21-Aug-25	21-Aug-25
12-162	Install Standpipe Riser & Testing At Stair D Floor 1 - Roof	15	15	21-Aug-25	11-Sep-25
12-118	Power to HR and AC Units - Area 12	5	5	26-Aug-25	02-Sep-25
12-122	In-Wall Plumbing Rough-in - Area 12	10	10	28-Aug-25	11-Sep-25
12-124	In-Wall Electrical Rough-in - Area 12	10	10	28-Aug-25	11-Sep-25
12-119	Set Hollow Metal Door Frames - Area 12	3	3	28-Aug-25	02-Sep-25
12-145	Millwork Field Measurement	1	1	28-Aug-25	28-Aug-25
12-262	Install In-Wall Countertop & Millwork Support - Area 12	1	1	28-Aug-25	28-Aug-25
12-125	In-Wall Inspection - Area 12	1	1	12-Sep-25	12-Sep-25
12-126	Sheetrock Walls (Including Taping and Sanding) - Area 12	7	7	15-Sep-25	23-Sep-25
12-143	Hang New Doors and Install Hardware - Area 12	5	5	24-Sep-25	30-Sep-25
12-127	Frame New Gyp. Ceilings - Area 12	5	5	24-Sep-25	30-Sep-25
12-128	Light Fixture Rough-in @ Gyp. Ceiling - Area 12	7	7	01-Oct-25	09-Oct-25
12-129	HVAC Drops @ Gyp. Ceiling - Area 12	7	7	01-Oct-25	09-Oct-25
12-130	Gypsum & ACOU1 Ceilings (Including Taping and Sanding) - Area 12	7	7	10-Oct-25	20-Oct-25
12-131	Patch/Repair Existing Exposed Ceiling - Area 12	5	5	14-Oct-25	20-Oct-25
12-132	Prime/1st Coat Walls and Ceilings - Area 12	4	4	21-Oct-25	24-Oct-25
12-137	Install Frame For Glazing Wall System With Wood Cladding - Area 12	10	10	21-Oct-25	03-Nov-25
12-159	Repair Existing Wall Paneling President & CFO Office - Area 12	10	10	21-Oct-25	03-Nov-25
12-134	Install Suspended Light Fixtures - Area 12	8	8	27-Oct-25	05-Nov-25
12-135	Install Ceiling Mount Diffusers - Area 12	8	8	27-Oct-25	05-Nov-25
12-139	Install Electrical & FA Devices and Trim - Area 12	5	5	30-Oct-25	05-Nov-25
12-138	Install Glazing & Doors for Glazing Wall System - Area 12	5	5	04-Nov-25	10-Nov-25
12-144	Wood Ceiling Panel Installation ACOU4 - Area 12	10	10	04-Nov-25	18-Nov-25
12-141	Install Projection Screens - Area 12	5	5	06-Nov-25	13-Nov-25
12-149	Final Paint - Area 12	5	5	14-Nov-25	20-Nov-25
12-147	Install Terrazzo Tile Flooring - Area 12	7	7	19-Nov-25	01-Dec-25
12-150	Rolling Completion Work - Area 12	5	5	21-Nov-25	01-Dec-25
12-266	Window Shade Installation - Area 12	4	4	21-Nov-25	26-Nov-25
12-123	Signage Installation - Area 12	2	2	21-Nov-25	24-Nov-25
12-148	Install Acoustic Wall Panel ACOU2 - Area 12	5	5	21-Nov-25	01-Dec-25
12-160	Install Wood Wall Paneling WD5 - Area 12	5	5	21-Nov-25	01-Dec-25
12-136	Install New Millwork - Area 12	5	5	02-Dec-25	08-Dec-25
12-161	Install Carpet - Area 12	10	10	02-Dec-25	15-Dec-25
12-142	Lighting Installation At Millwork - Area 12	5	5	09-Dec-25	15-Dec-25
12-268	Appliances Installation - Area 12	1	1	09-Dec-25	09-Dec-25
12-151	Construction Final Cleaning	2	2	16-Dec-25	17-Dec-25
12-269	Owner FF&E Installation - Area 12	5	5	16-Dec-25	22-Dec-25
12-152	Substantial Completion - Area 12	0	0		22-Dec-25
2nd Floor Above Escalator & Stairs					
12-11	Install Scaffold For Overhead Plumbing - Area 12	5	5	05-Aug-25	11-Aug-25
12-11	Remove Ceiling For Overhead Plumbing - Area 12	2	2	12-Aug-25	13-Aug-25
12-11	Set Plumbing Carriers + Install Waste Piping @ Gang Toilets - Area 12	10	10	14-Aug-25	27-Aug-25
12-11	Patch/Tape/Spackle Ceiling - Area 12	6	6	28-Aug-25	05-Sep-25
12-11	Paint Ceiling - Area 12	2	2	08-Sep-25	09-Sep-25
12-12	Remove Scaffold & Temp Walls - Area 12	2	2	10-Sep-25	11-Sep-25

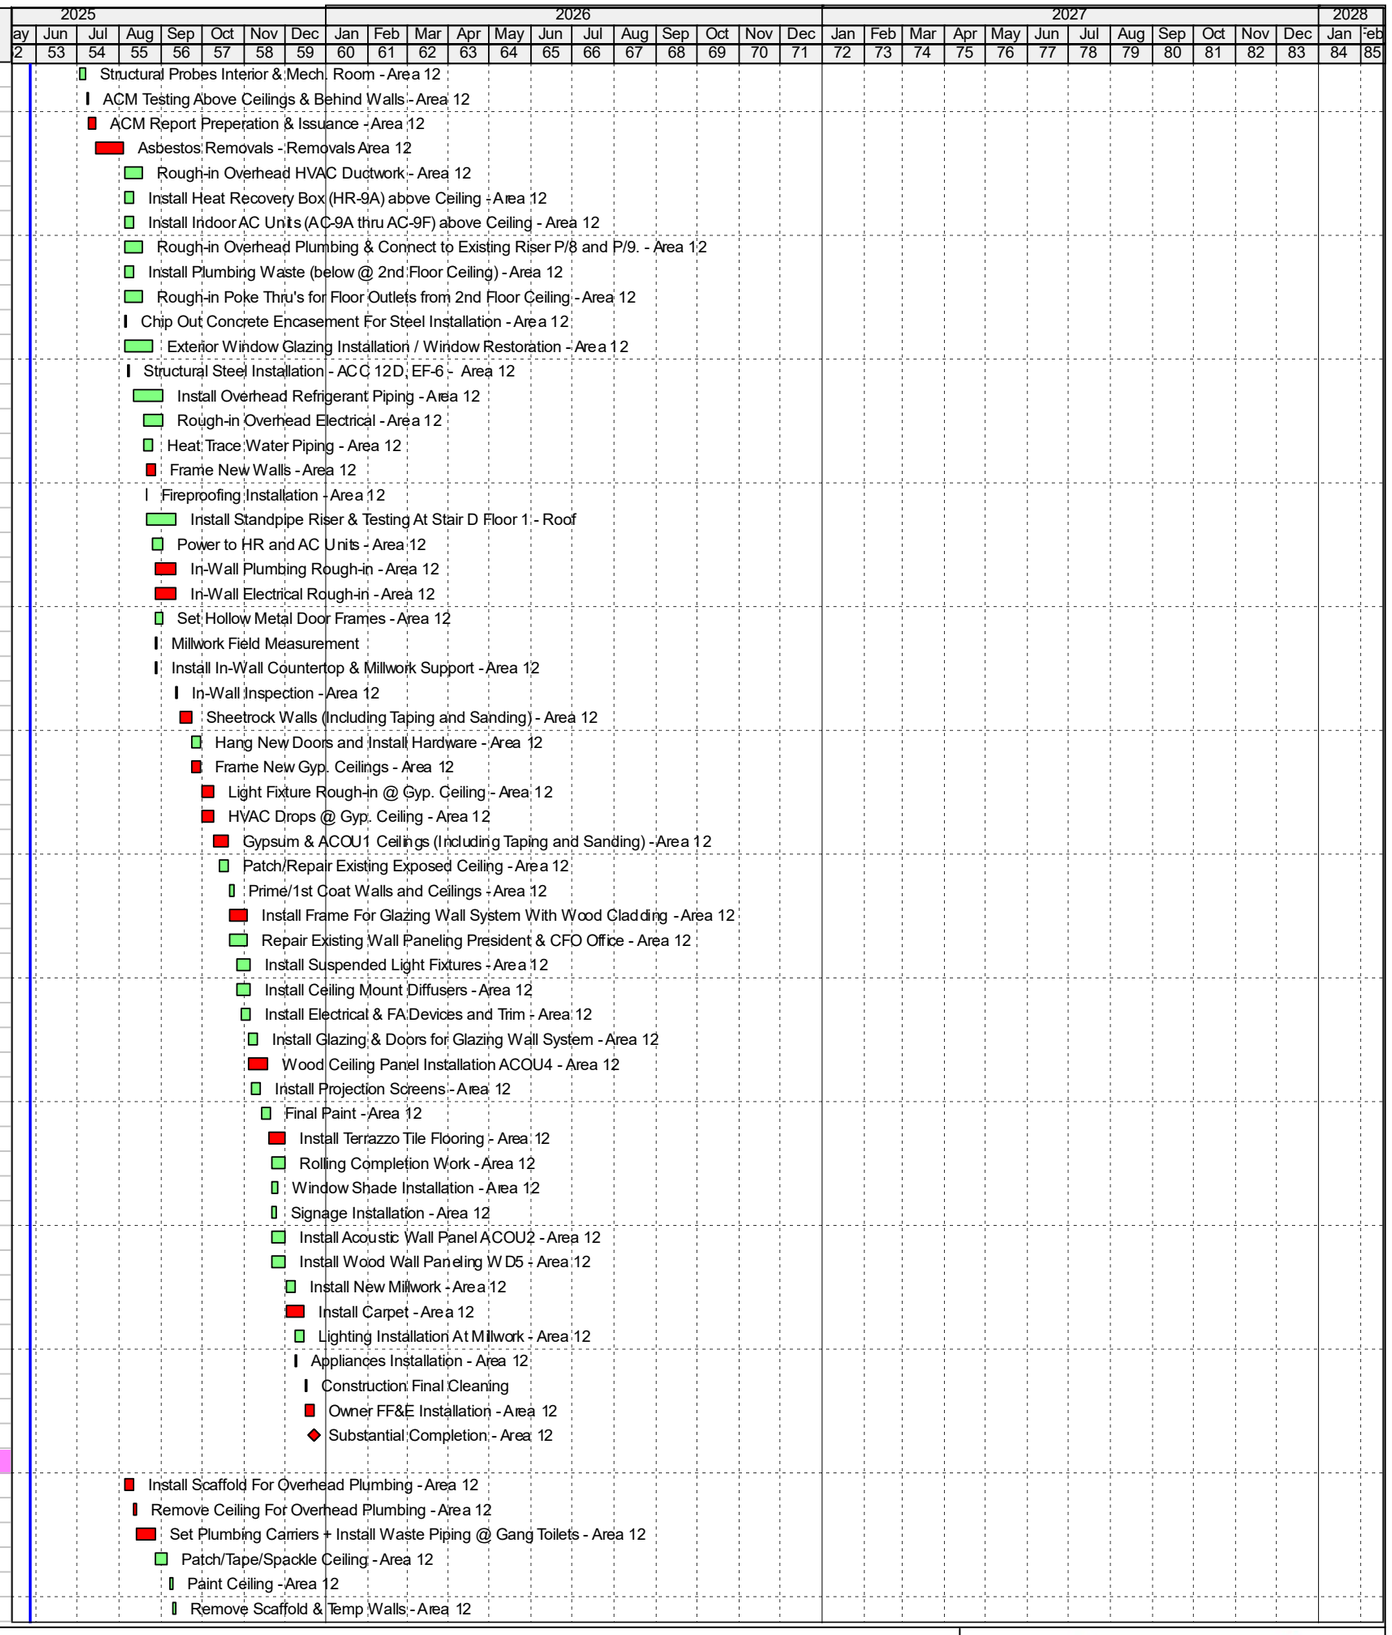


Finish Date: 04-Feb-28
Data Date: 28-May-25
Run Date: 11-Jun-25 16:20
BPL II - 09

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining ...
Summary Milestones
Critical Milestones
Milestone

Gilbane

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
	Bathrooms				
12-153	Frame New Gyp. Ceilings - Area 12	3	3	24-Sep-25	26-Sep-25
12-154	RDG Installation Bathrooms - Area 12	3	3	29-Sep-25	01-Oct-25
12-155	Light Fixture Installation Bathrooms - Area 12	3	3	29-Sep-25	01-Oct-25
12-156	Sheetrock Gyp. Ceilngs Bathrooms (Including Taping and Sanding) - Area 12	5	5	02-Oct-25	08-Oct-25
12-133	Toilet Room Finishes (Ceramic Tile) - Area 12	10	10	21-Oct-25	03-Nov-25
12-157	Install Built-IN WC Countertop and Backsplash STN - Area 12	2	2	04-Nov-25	05-Nov-25
12-158	Paint Ceilings Bathrooms - Area 8A	1	1	04-Nov-25	04-Nov-25
12-140	Install Plumbing Fixtures - Area 12	5	5	06-Nov-25	13-Nov-25
12-265	Install Mirrors - Area 12	1	1	06-Nov-25	06-Nov-25
12-146	Install Toilet Accessories - Area 12	2	2	14-Nov-25	17-Nov-25
	TR Vault IDF Closet Fitout				
IT1110	Install Conduit and Cables from Existing EDC-1 to E-IDF-N IDF Closet	10	10	05-Aug-25	18-Aug-25
IT1160	Pull All Feeders	3	3	19-Aug-25	21-Aug-25
IT1250	Frame New Walls - IDF Closet	3	3	21-Aug-25	25-Aug-25
IT1220	Tape/Spackle/Paint IDF Closet Walls	3	3	22-Aug-25	26-Aug-25
IT1260	Sheetrock Walls	3	3	26-Aug-25	28-Aug-25
IT1130	Install Plywood Backer as per Drawing TC-301 at Two Walls	1	1	29-Aug-25	29-Aug-25
IT1150	Install Panel E-IDF-N	1	1	02-Sep-25	02-Sep-25
IT1170	Install General Power and Light / Install Specified Grounding Bar	5	5	03-Sep-25	09-Sep-25
IT1180	Self Level IDF Closet	2	2	10-Sep-25	11-Sep-25
IT1210	Install VCT in IDF Closet	1	1	12-Sep-25	12-Sep-25
IT1190	Install Ladder Racks for Structured Cabling	3	3	15-Sep-25	17-Sep-25
IT1200	Install IT Data Racks	5	5	18-Sep-25	24-Sep-25
IT1230	Install Data Ports	10	10	25-Sep-25	08-Oct-25
IT1240	BPL IT Install Network Switch, UPS	5	5	25-Sep-25	01-Oct-25
	Project Area 13 - 3rd Floor Trustees Rooms				
	Detail				
	AHU and ACC				
13-161	Roofing Removal / Curb Flashing - Area 13	2	2	10-Jul-25	11-Jul-25
13-154	Install ACC-13A Roof Curbs - Area 13	5	5	29-Jul-25	04-Aug-25
13-179	Install AC Condensing Unit (Unit ACC-13A) mounted on Roof Curbs - Area 13	5	5	05-Aug-25	11-Aug-25
13-185	Power to ACC-13A - Area 13	5	5	12-Aug-25	18-Aug-25
13-186	ACC 13A Charge and Start Up	2	2	19-Aug-25	20-Aug-25
13-270	Mechanical Equipment Testing & Balancing - Area 13	5	5	21-Aug-25	27-Aug-25
	Interior Space				
13-159	Install Temp. Partitions - Area 13	3	3	04-Jun-25*	06-Jun-25
13-156	Demolition - Area 13	10	10	16-Jun-25	27-Jun-25
13-160	Chip Out Concrete Encasement For Steel Installation - Area 13	2	2	26-Jun-25	27-Jun-25
13-230	ACM Testing Above Ceilings & Behind Walls - Area 13	2	2	30-Jun-25	01-Jul-25
13-178	Open Existing Shaft For Ductwork Connection EF-13	1	1	30-Jun-25	30-Jun-25
13-231	ACM Report Preperation & Issuance - Area 13	3	3	02-Jul-25	07-Jul-25
13-155	Asbestos Removals	15	15	08-Jul-25*	28-Jul-25
13-157	Rough-in Overhead HVAC Ductwork - Area 13	10	10	29-Jul-25	11-Aug-25
13-180	Install Heat Recovery Box (HR-13A) above Ceiling - Area 13	3	3	29-Jul-25	31-Jul-25
13-181	Install Indoor AC Units (AC-13A thru AC-13D) above Ceiling - Area 13	3	3	29-Jul-25	31-Jul-25
13-170	Structural Steel Installation - ACC12A & Exhaust Duct Unit Area 13	2	2	29-Jul-25	30-Jul-25
13-182	Install Overhead Refrigerant Piping - Area 13	10	10	01-Aug-25	14-Aug-25
13-158	Frame New Walls - Area 13	3	3	12-Aug-25	14-Aug-25
13-184	Power to HR and AC Units - Area 13	5	5	12-Aug-25	18-Aug-25
13-189	Rough-in Overhead Electrical - Area 13	5	5	12-Aug-25	18-Aug-25
13-192	Slab Trenching / Poke-Thru For Elec. For Outlets	5	5	14-Aug-25	20-Aug-25
13-166	Set Hollow Metal Door Frames - Area 13	1	1	15-Aug-25	15-Aug-25
13-200	Millwork Field Measurement - Area 13	1	1	15-Aug-25	15-Aug-25
13-261	Install In-Wall Countertop & Millwork Support - Area 13	1	1	15-Aug-25	15-Aug-25
13-162	In-Wall Electrical Rough-in - Area 13	10	10	21-Aug-25	04-Sep-25
13-177	Fireproofing Installation - Area 13	1	1	21-Aug-25	21-Aug-25
13-163	In-Wall Inspection - Area 13	1	1	05-Sep-25	05-Sep-25
13-164	Sheetrock Walls (Including Taping and Sanding) - Area 13	5	5	08-Sep-25	12-Sep-25
13-174	Frame New Gyp. Ceilings - Area 13	5	5	15-Sep-25	19-Sep-25
13-175	Light Fixture Rough-in @ Gyp. Ceiling - Area 13	5	5	22-Sep-25	26-Sep-25
13-176	HVAC Drops @ Gyp. Ceiling - Area 13	5	5	22-Sep-25	26-Sep-25
13-187	Gypsum & ACOU1 Ceilings (Including Taping and Sanding) - Area 13	10	10	29-Sep-25	10-Oct-25

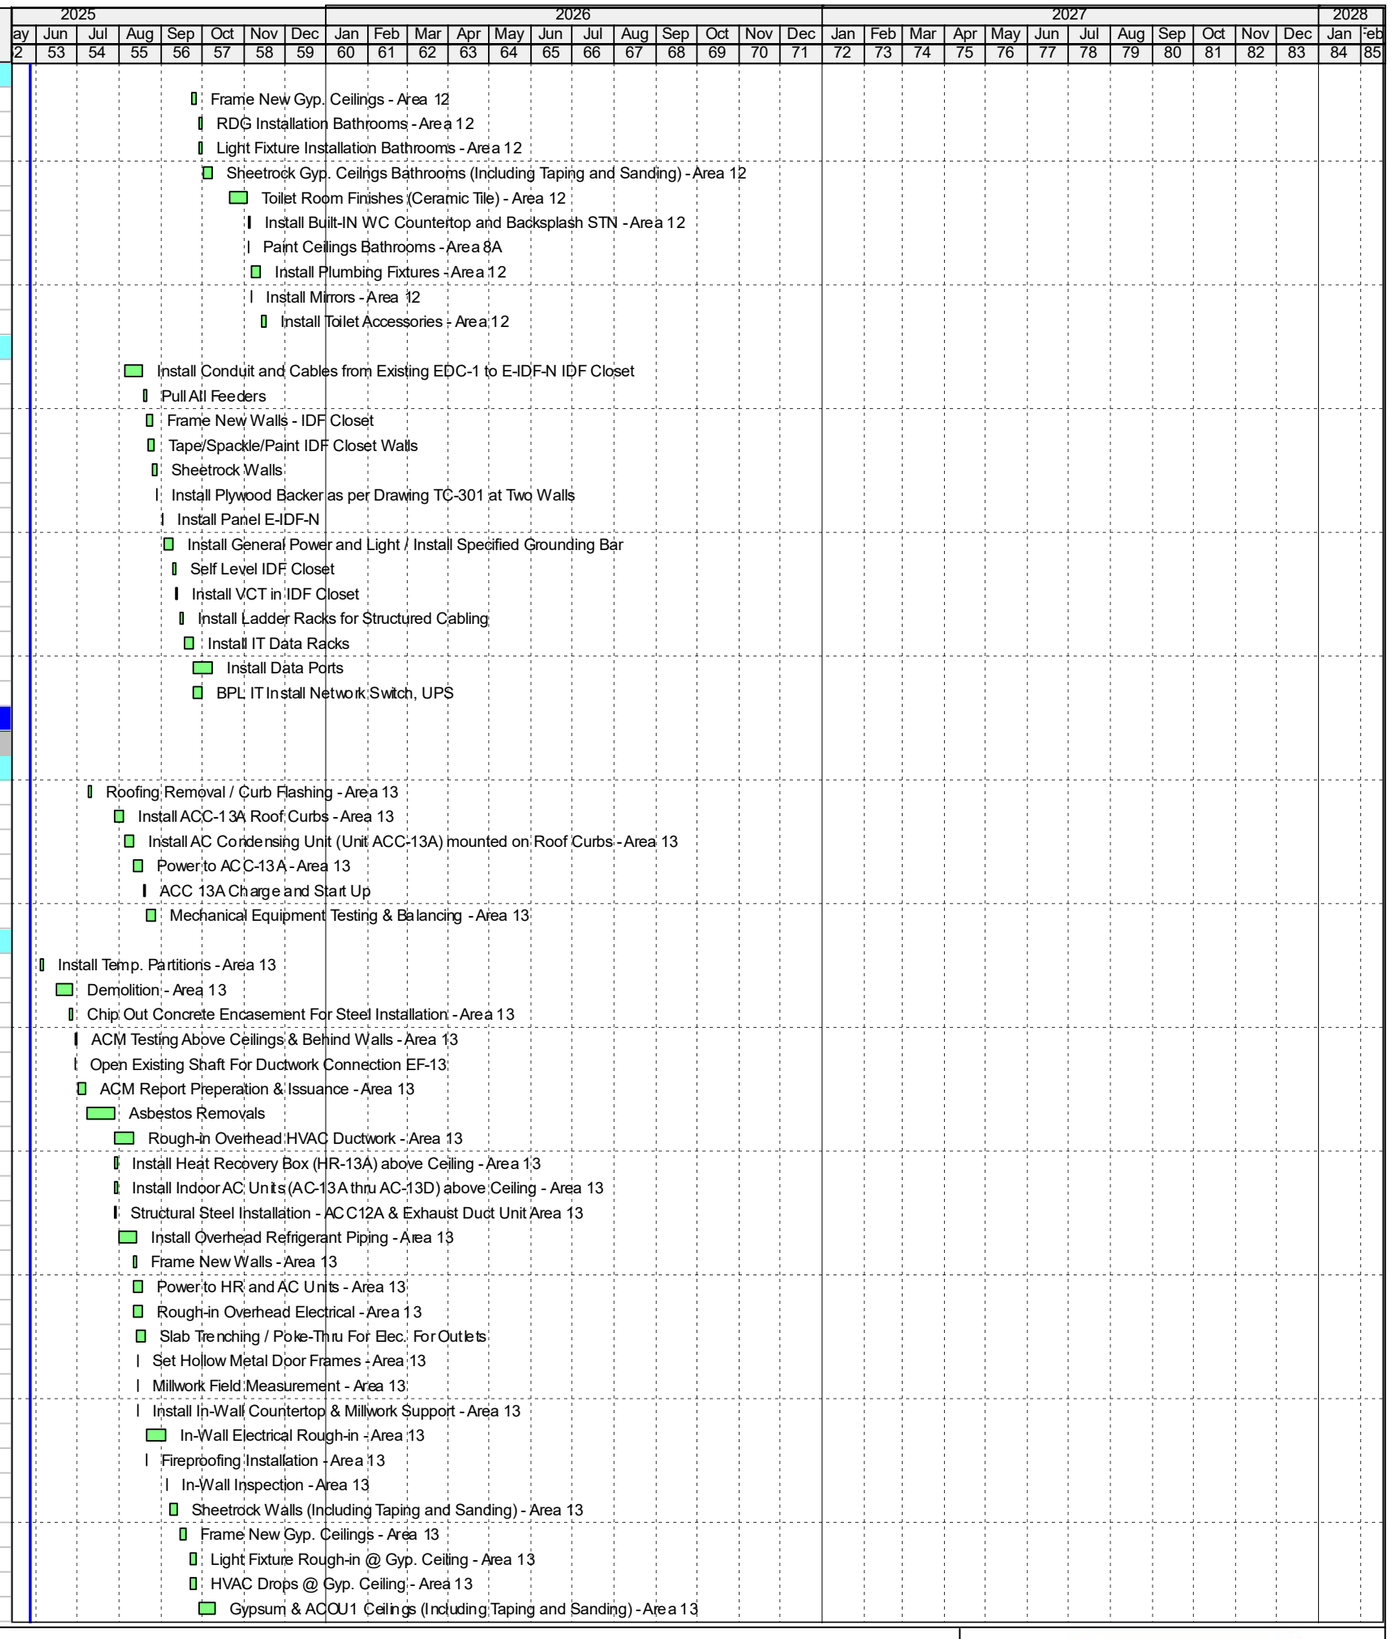


Finish Date: 04-Feb-28
Data Date: 28-May-25
Run Date: 11-Jun-25 16:20
BPL II - 09

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining ...
Summary Milestones
Critical Milestones
Milestone

Gilbane

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
13-169	Hang New Doors and Install Hardware - Area 13	2	2	13-Oct-25	14-Oct-25
13-171	Prime/1st Coat Walls and Ceilings - Area 13	2	2	13-Oct-25	14-Oct-25
13-207	Repair Existing Wall PanelingTrustees Room - Area 13	5	5	13-Oct-25	17-Oct-25
13-172	Install Suspended Light Fixtures - Area 13	8	8	15-Oct-25	24-Oct-25
13-188	Install Ceiling Mount Diffusers - Area 13	8	8	15-Oct-25	24-Oct-25
13-201	Install Frame for Glazing Wall System with Wood Paneling - Area 13	10	10	15-Oct-25	28-Oct-25
13-173	Install Projection Screens - Area 13	5	5	27-Oct-25	31-Oct-25
13-190	Install Electrical & FA Devices and Trim - Area 13	5	5	27-Oct-25	31-Oct-25
13-167	Install Terrazzo Tile Flooring - Area 13	7	7	29-Oct-25	06-Nov-25
13-165	Install New Millwork - Area 13	10	10	07-Nov-25	21-Nov-25
13-191	Install Carpet - Area 13	3	3	07-Nov-25	12-Nov-25
13-268	Owner FF&E Installation - Area 13	5	5	24-Nov-25	02-Dec-25
13-267	Appliances Installation - Area 13	1	1	24-Nov-25	24-Nov-25
13-168	Install Glazing - Area 13	5	5	10-Dec-25	16-Dec-25
13-193	Final Paint - Area 13	5	5	17-Dec-25	23-Dec-25
13-204	Rolling Completion Work - Area 13	5	5	24-Dec-25	31-Dec-25
13-196	Construction Final Cleaning	2	2	24-Dec-25	26-Dec-25
13-266	Window Shade Installation - Area 13	4	4	24-Dec-25	30-Dec-25
13-183	Signage Installation - Area 13	2	2	24-Dec-25	26-Dec-25
13-205	Substantial Completion - Area 13	0	0		31-Dec-25
Bathrooms					
13-269	Rough-in Overhead Plumbing & Connect to Existing Riser P/1. - Area 11	5	5	29-Jul-25	04-Aug-25
13-232	Frame New Gyp. Ceilings - Area 13	1	1	15-Sep-25	15-Sep-25
13-233	RDG Installation Bathrooms - Area 13	1	1	16-Sep-25	16-Sep-25
13-234	Light Fixture Installation Bathrooms - Area 13	1	1	16-Sep-25	16-Sep-25
13-235	Sheetrock Gyp. Ceilngs Bathrooms (Including Taping and Sanding) - Area 13	3	3	17-Sep-25	19-Sep-25
13-195	Toilet Room Finishes (Ceramic Tile) - Area 13	3	3	22-Sep-25	24-Sep-25
13-236	Install Built-IN WC Countertop and Backsplash STN - Area 13	1	1	25-Sep-25	25-Sep-25
13-194	Install Plumbing Fixtures (Sinks) @ Millwork - Area 13	2	2	26-Sep-25	29-Sep-25
13-266	Install Mirrors - Area 8A	1	1	26-Sep-25	26-Sep-25
13-237	Install Toilet Accessories - Area 13	1	1	30-Sep-25	30-Sep-25
Roof Areas					
Eastern Wing					
A5280	Install New Ladder - PA12 Roof Bulkhead	3	3	02-Jul-25	07-Jul-25
Flatbush Wing					
A5130	Install New Ladder - PA10E Roof Bulkhead	3	3	02-Jul-25	07-Jul-25
A3970	Crossover Platform Installation	10	10	21-Aug-25	04-Sep-25
A4090	Modify Existing Dunnage - Info Commons Chiller	7	7	13-Nov-26	23-Nov-26
A5860	Remove Existing Mechanical Equipment	5	5	19-Aug-27	25-Aug-27
A5840	Metal Deck Installation At Existing Slab Opening - Annex Roof	1	1	26-Aug-27	26-Aug-27
A5850	Concrete Infill At Existing Slab Opening - Annex Roof	1	1	27-Aug-27	27-Aug-27
A5870	Patch Roof At Units Removed - Annex Roof	2	2	30-Aug-27	31-Aug-27
Info Commons Chiller					
A4060	Demo Existing Piping / Electric to Chiller - Info Commons Chiller	3	3	02-Nov-26*	04-Nov-26
A4070	Demo Existing Chiller - Info Commons Chiller	5	5	05-Nov-26	12-Nov-26
A4080	Rough-In Electric - Info Commons Chiller	4	4	05-Nov-26	10-Nov-26
A4061	Structural Steel Installation For Buffer Tank - PA10 Equipment Room	1	1	05-Nov-26	05-Nov-26
A4062	Fireproofing Installation - PA 10 Equipment Room	1	1	06-Nov-26	06-Nov-26
A4063	Install Concrete Pad For Buffer Tank - PA 10 Equipment Room	2	2	06-Nov-26	09-Nov-26
A6190	Tnemic Paint On Existing Dunnage - Info Commons Chiller	3	3	13-Nov-26	17-Nov-26
A4100	Rig New Cooling Tower To Roof - Info Commons Chiller	1	1	24-Nov-26	24-Nov-26
A4110	Install Piping to Chiller - Info Commons Chiller	2	2	25-Nov-26	30-Nov-26
A4120	Electrical Tie-In - Info Commons Chiller	1	1	25-Nov-26	25-Nov-26
A4064	Install New Buffer Tank - PA 10 Equipment Room	2	2	25-Nov-26	30-Nov-26
A4130	Set up / Testing / Commissioning - Info Commons Chiller	3	3	01-Dec-26	03-Dec-26
Central					
A5230	Disconnect / Removal Power To Mech. Units	2	2	09-Jun-25	10-Jun-25
A5290	Remove Existing Mechanical Equipment	5	5	11-Jun-25	17-Jun-25
A5300	Patch Roof At Units Removed - Central Roof	2	2	18-Jun-25	19-Jun-25
A5260	Crossover Platform Installation - Central & Low Roof	10	10	21-Aug-25	04-Sep-25
A4000	Modify Existing Dunnage - Deck Chiller	3	3	14-Nov-25	18-Nov-25
Dweck Chiller					
A3980	Demo Existing Piping / Electric to Chiller - Dweck Chiller	3	3	03-Nov-25*	05-Nov-25

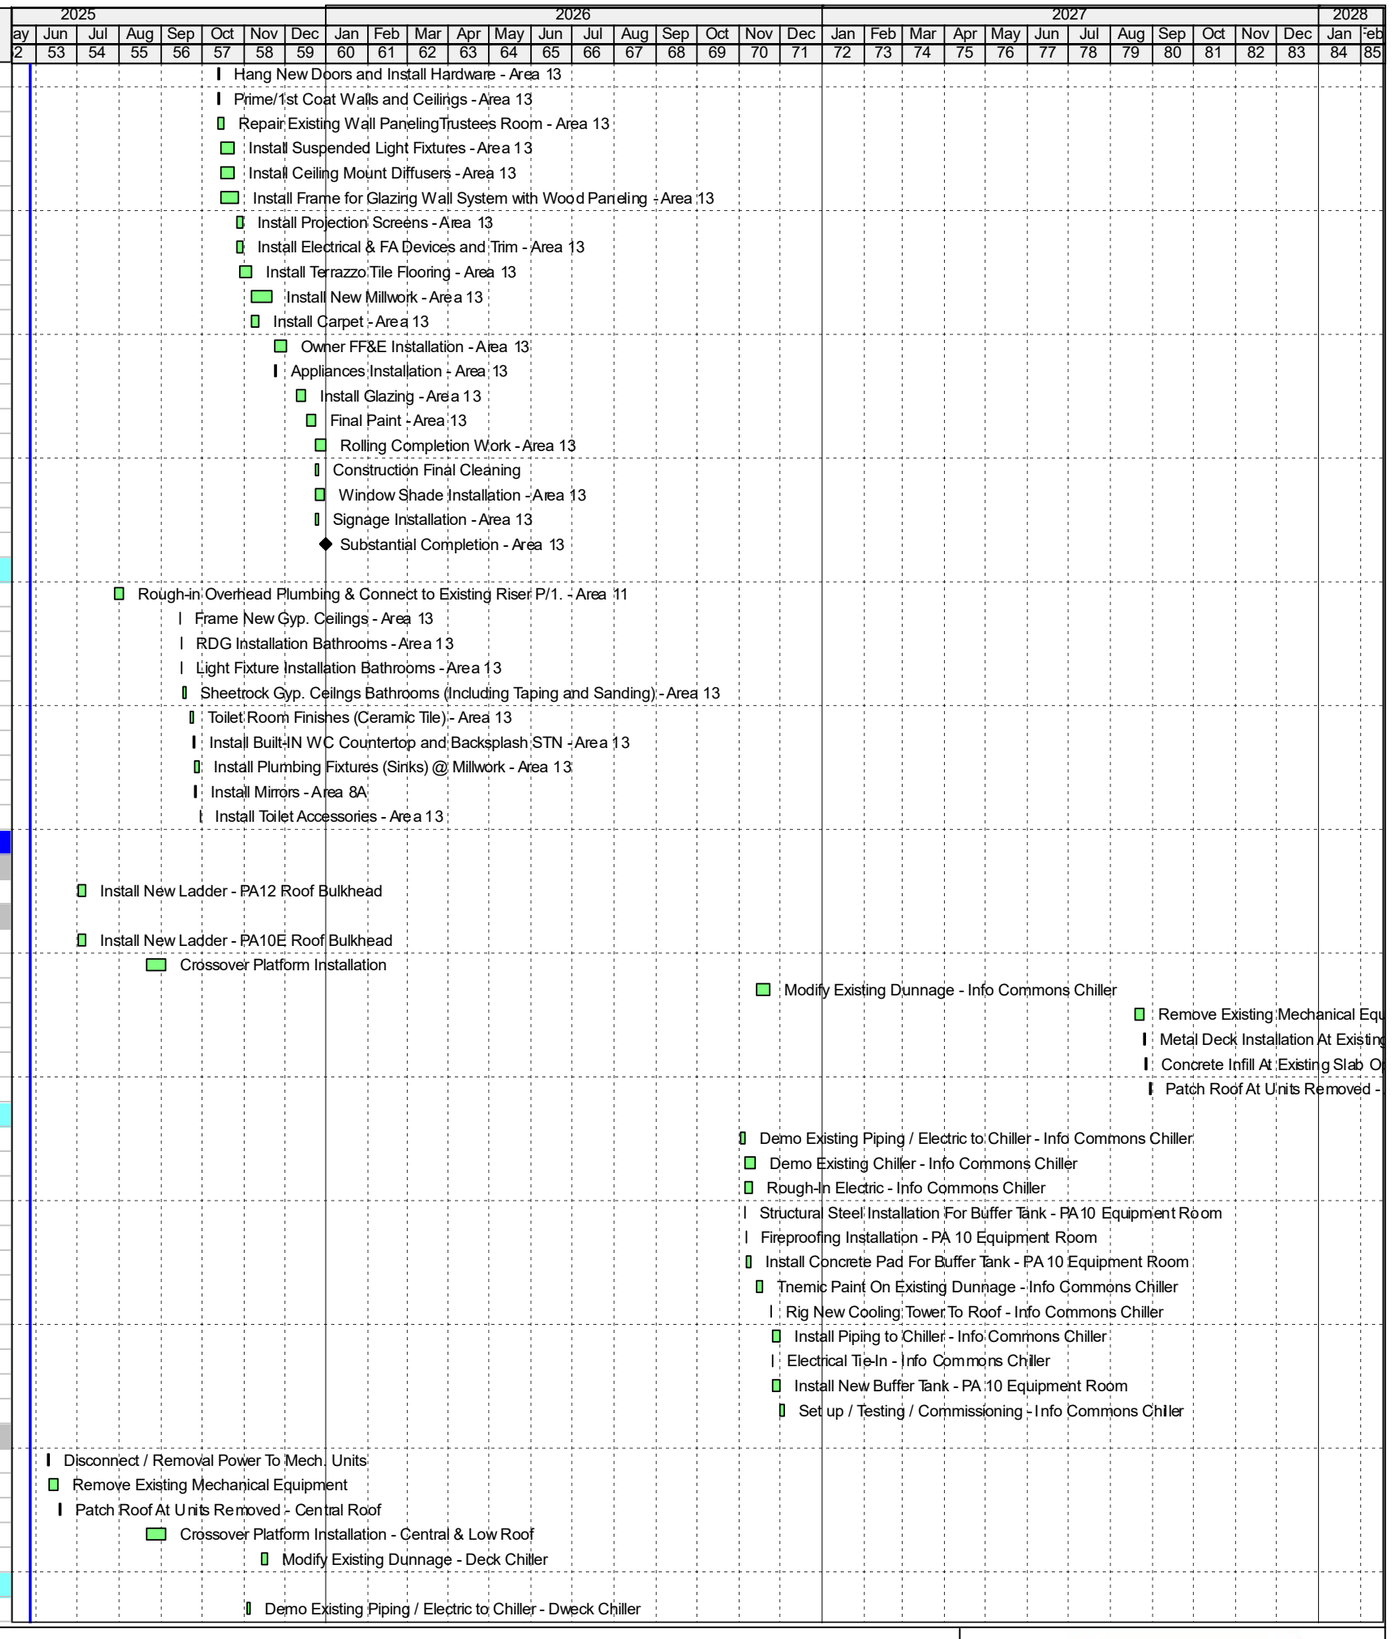


Finish Date: 04-Feb-28
Data Date: 28-May-25
Run Date: 11-Jun-25 16:20
BPL II - 09

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining ...
Summary Milestones
Critical Milestones
Milestone

Gilbane

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
A3990	Demo Existing Chiller - Dweck Chiller	5	5	06-Nov-25	13-Nov-25
A4050	Rough-In Electric - Dweck Chiller	4	4	06-Nov-25	12-Nov-25
A6180	Tnemic Paint On Existing Dunnage - Dweck Chiller	3	3	14-Nov-25	18-Nov-25
A4010	Rig New Cooling Tower To Roof - Dweck Chiller	1	1	19-Nov-25	19-Nov-25
A4020	Install Piping to Chiller - Dweck Chiller	2	2	20-Nov-25	21-Nov-25
A4030	Electrical Tie-In - Dweck Chiller	1	1	20-Nov-25	20-Nov-25
A4040	Set up / Testing / Commissioning - Dweck Chiller	3	3	24-Nov-25	26-Nov-25
Annex					
A5310	Disconnect / Removal Power To Mech. Units	2	2	19-Jan-26	20-Jan-26
A5320	Remove Existing Mechanical Equipment	5	5	21-Jan-26	27-Jan-26
A5600	Metal Deck Installation At Existing Slab Opening - Annex Roof	1	1	28-Jan-26	28-Jan-26
A5680	Concrete Infill At Existing Slab Opening - Annex Roof	1	1	29-Jan-26	29-Jan-26
A5330	Patch Roof At Units Removed - Annex Roof	2	2	30-Jan-26	02-Feb-26
A5270	Crossover Platform Installation - Central & Low Roof	10	10	16-Mar-26	27-Mar-26
Sub-Phase B					
Project Area 7 - 2nd Floor SST					
Detail					
AHU and ACC					
7-2030	Structural Probes - Area 7	1	1	11-Feb-26	11-Feb-26
7-2020	Extend Equipment Pad - Area 7	2	2	12-Mar-26	13-Mar-26
7-2681	Wall Opening In Exterior Wall For AHU-6 Rigging - Area 7	3	3	12-Mar-26	16-Mar-26
7-2000	Install New AH-6 from Basement Mech. Room - PA7	20	20	17-Mar-26	13-Apr-26
7-2010	Power to New AHU-6 / ACC / VRF - Confirm from Existing Panels	10	10	14-Apr-26	27-Apr-26
7-2691	Exterior Wall Patching / Stucco Finish At Bulkhead- Area 7	3	3	14-Apr-26	16-Apr-26
7-2721	AH-6 Charge and Start Up - Area 7	2	2	14-Apr-26	15-Apr-26
7-2731	Mechanical Equipment Testing & Balancing - Area 7	5	5	16-Apr-26	22-Apr-26
Interior Space					
7-1470	Install Temp. Partitions - Area 7	3	3	19-Jan-26	21-Jan-26
7-1450	Demolition (Including Equipment Room) - Area 7	15	15	22-Jan-26	11-Feb-26
7-1483	Fireproofing Installation - Area 7	1	1	12-Feb-26	12-Feb-26
7-2320	ACM Testing Above Ceilings & Behind Walls - Area 7	2	2	12-Feb-26	13-Feb-26
7-2330	ACM Report Preperation & Issuance - Area 7	3	3	16-Feb-26	18-Feb-26
7-1445	Asbestos Removals - Area 7	15	15	19-Feb-26	11-Mar-26
7-1460	Rough-in Overhead HVAC Ductwork - Area 7	10	10	12-Mar-26	25-Mar-26
7-1480	Exterior Window Restoration - Area 7	15	15	12-Mar-26	01-Apr-26
7-1481	Chip Out Concrete Encasement For Steel Installation - Area 7	3	3	12-Mar-26	16-Mar-26
7-1530	Slab Trenching / Poke-Thru For Elec. For Outlets & Lighting	5	5	12-Mar-26	18-Mar-26
7-1610	Rough-in Overhead Electrical - Area 7	10	10	26-Mar-26	08-Apr-26
7-1500	Patch/Repair Existing Sheetrock Walls (Including Taping and Sanding) - Area 7	7	7	09-Apr-26	17-Apr-26
7-1560	Frame New Gyp. Ceilings - Area 7	5	5	20-Apr-26	24-Apr-26
7-1570	Light Fixture Rough-in @ Gyp. Ceiling - Area 7	7	7	27-Apr-26	05-May-26
7-1580	HVAC Drops @ Gyp. Ceiling - Area 7	7	7	27-Apr-26	05-May-26
7-1590	Gypsum & ACOU1 Ceilings (Including Taping and Sanding) - Area 7	10	10	06-May-26	19-May-26
7-1540	Prime/1st Coat Walls and Ceilings - Area 7	4	4	20-May-26	26-May-26
7-1541	Restore Existing Perimeter Millwork - Area 7	40	40	20-May-26	16-Jul-26
7-1640	Wood Ceiling Panel Installation ACOU4 - Area 7	5	5	20-May-26	27-May-26
7-1550	Install Suspended Light Fixtures - Area 7	8	8	27-May-26	05-Jun-26
7-1600	Install Ceiling Mount Diffusers - Area 7	8	8	27-May-26	05-Jun-26
7-1660	Final Paint - Area 7	5	5	27-May-26	02-Jun-26
7-1620	Install Electrical Devices and Trim - Area 7	5	5	01-Jun-26	05-Jun-26
7-1630	Rolling Completion Work - Area 7	5	5	03-Jun-26	09-Jun-26
7-2661	Window Shade Installation - Area 7	4	4	03-Jun-26	08-Jun-26
7-1490	Signage Installation - Area 7	2	2	03-Jun-26	04-Jun-26
7-1520	Install Terrazzo Tile Flooring - Area 7	10	10	08-Jun-26	19-Jun-26
7-1510	Install New Millwork + Built-in Benches and Desks - Area 7	15	15	22-Jun-26	13-Jul-26
7-1551	Light Fixture Installation At Millwork - Area 7	10	10	29-Jun-26	13-Jul-26
7-2711	Owner FF&E Installation - Area 7	5	5	14-Jul-26	20-Jul-26
7-2701	Appliances Installation - Area 7	1	1	14-Jul-26	14-Jul-26
7-1680	Construction Final Cleaning	2	2	17-Jul-26	20-Jul-26
7-1665	Substantial Completion - Area 7	0	0		20-Jul-26
Project Area 11 - 3rd Floor Annex					
AHU and ACC					
11-2131	Roofing Removal / Temporary Box Installation DOAS, ACC, Duct Openings - Area	3	3	10-Jul-25	14-Jul-25

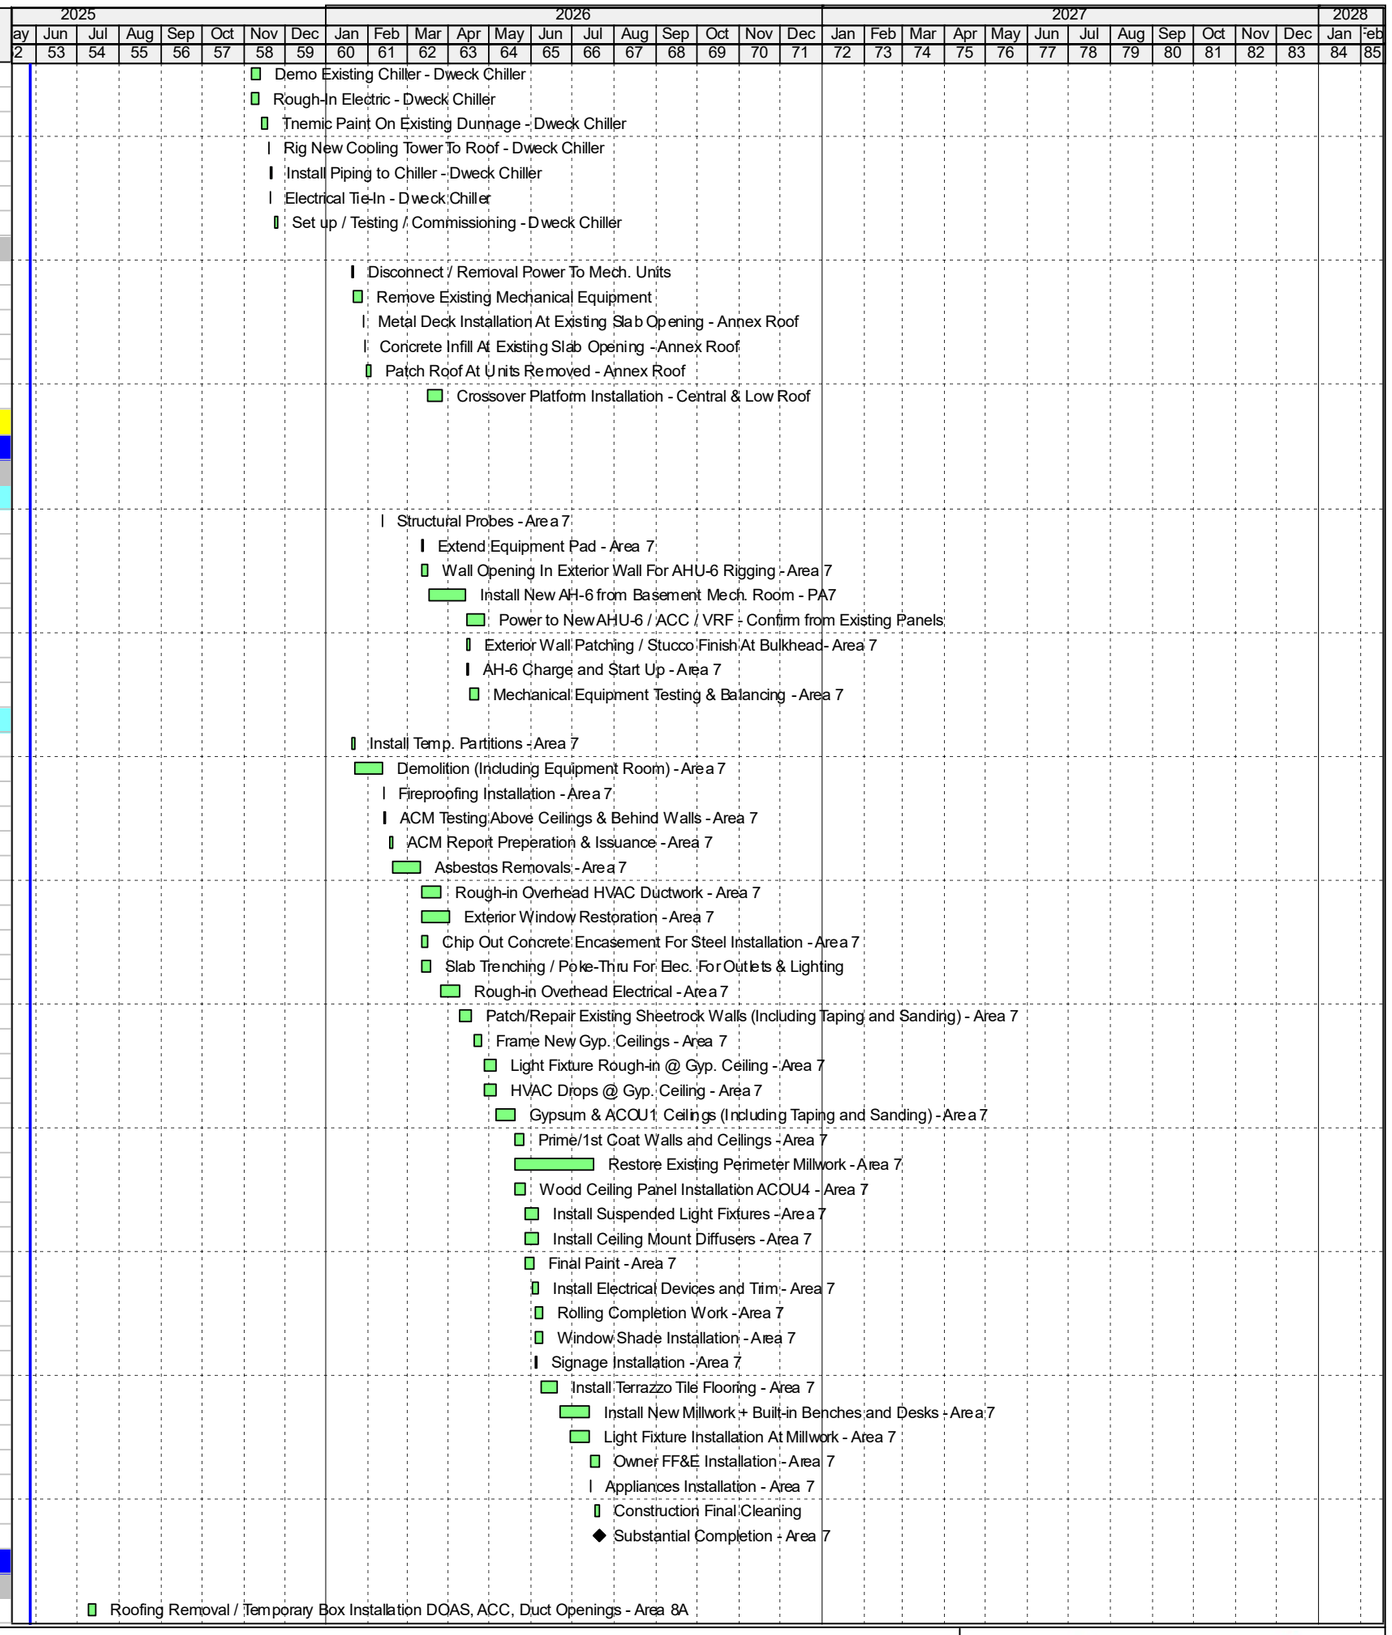


Finish Date: 04-Feb-28
Data Date: 28-May-25
Run Date: 11-Jun-25 16:20
BPL II - 09

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining ...
Summary Milestones
Critical Milestones
Milestone

Gilbane

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
11-1550	Concrete Slab Removal For MEP Steel Post - Area 11	3	3	16-Jul-25	18-Jul-25
11-2231	Structural Steel Installation Above Roof- DOAS, ACC Unit Area 11	3	3	21-Jul-25	23-Jul-25
11-1540	Install ACC-11A, B and C + DOAS -11A Roof Curbs (Annex Roof) - Area 11	5	5	09-Mar-26	13-Mar-26
11-1770	Rig-in and Install New DOAS-11A and Associated Ductwork including Tie-ins - Are	15	15	16-Mar-26	03-Apr-26
11-1790	Install AC Condensing Unit (Unit ACC-11A, B, and C) mounted on Roof Curbs - /	5	5	16-Mar-26	20-Mar-26
11-1850	Power to ACC-11A, B and C on Roof - Area 11	5	5	23-Mar-26	27-Mar-26
11-1870	Start Up and Charge - ACC A,B,C	1	1	30-Mar-26	30-Mar-26
11-1830	Power to DOAS-11A - Area 11	5	5	06-Apr-26	10-Apr-26
11-1860	Start Up and Testing DOAS-11A	1	1	13-Apr-26	13-Apr-26
11-2710	Mechanical Equipment Testing & Balancing - Area 11	5	5	14-Apr-26	20-Apr-26
Interior Space					
11-2360	Roof Slab Infill - Area 11	1	1	21-Aug-25	21-Aug-25
11-2100	Install Temp. Partitions - Area 11	3	3	14-Jan-26	16-Jan-26
11-2071	Demolition (Including Equipment Room) - Area 11	15	15	19-Jan-26	06-Feb-26
11-2341	ACM Testing Above Ceilings & Behind Walls - Area 11	2	2	09-Feb-26	10-Feb-26
11-2351	ACM Report Preperation & Issuance - Area 11	3	3	11-Feb-26	13-Feb-26
11-1010	Asbestos Abatement	15	15	16-Feb-26	06-Mar-26
11-2080	Rough-in Overhead HVAC Ductwork - Area 11	10	10	09-Mar-26	20-Mar-26
11-2260	Install Heat Recovery Box (HR-9A) above Ceiling - Area 11	5	5	09-Mar-26	13-Mar-26
11-2270	Install Indoor AC Units (AC-9A thru AC-9F) above Ceiling - Area 11	5	5	09-Mar-26	13-Mar-26
11-2300	Rough-in Overhead Plumbing & Connect to Existing Riser P/5 - Area 11	10	10	09-Mar-26	20-Mar-26
11-2410	Install Plumbing Waste (below @ 2nd Floor Ceiling) - Area 11	10	10	09-Mar-26	20-Mar-26
11-2470	Rough-in Poke Thru's for Floor Outlets from 2nd Floor Ceiling - Area 11	10	10	09-Mar-26	20-Mar-26
11-2490	Set Plumbing Carriers + Install Waste Piping @ Gang Toilets - Area 11	10	10	09-Mar-26	20-Mar-26
11-2221	Chip Out Concrete Encasement For Steel Installation - Area 11	2	2	09-Mar-26	10-Mar-26
11-2281	Structural Steel Installation - Ductwork Penetrations	2	2	09-Mar-26	10-Mar-26
11-2241	Fireproofing Installation - Area 11	1	1	11-Mar-26	11-Mar-26
11-2280	Install Overhead Refrigerant Piping - Area 11	15	15	16-Mar-26	03-Apr-26
11-2330	Rough-in Overhead Electrical - Area 11	10	10	23-Mar-26	03-Apr-26
11-2440	Heat Trace Water Piping - Area 11	5	5	23-Mar-26	27-Mar-26
11-2500	Heat Trace Hot Water Plumbing - Area 11	5	5	23-Mar-26	27-Mar-26
11-2610	Rough-In Overhead Standpipe - Area 11	4	4	23-Mar-26	26-Mar-26
11-2620	Install New FH Cabinet - Area 11	1	1	27-Mar-26	27-Mar-26
11-2630	Install 2-HR Rated Enclosure Around Standpipe - Area 11	4	4	27-Mar-26	01-Apr-26
11-2090	Frame New Walls - Area 11	5	5	30-Mar-26	03-Apr-26
11-2290	Power to HR and AC Units - Area 11	5	5	30-Mar-26	03-Apr-26
11-2095	In-Wall Plumbing Rough-in - Area 11	10	10	06-Apr-26	17-Apr-26
11-2150	Set Hollow Metal Door Frames - Area 11	3	3	06-Apr-26	08-Apr-26
11-2380	Millwork Field Measurement - Area 11	1	1	06-Apr-26	06-Apr-26
11-2600	Install In-Wall Countertop & Millwork Support - Area 11	1	1	06-Apr-26	06-Apr-26
11-2291	Install Framing / Insulation For Ramp #2 - Area 11	4	4	06-Apr-26	09-Apr-26
11-2110	In-Wall Electrical Rough-in - Area 11	10	10	09-Apr-26	22-Apr-26
11-2301	Install Steel Channel For Ramp #2 - Area 11	2	2	10-Apr-26	13-Apr-26
11-2311	Install Glass Gaurdrail System Frame Ramp #2 - Area 11	5	5	14-Apr-26	20-Apr-26
11-2321	Install Glass & Handrails Ramp #2 & Stair # 1 - Area 11	5	5	21-Apr-26	27-Apr-26
11-2120	In-Wall Inspection - Area 11	1	1	23-Apr-26	23-Apr-26
11-2130	Sheetrock Walls (Including Taping and Sanding) - Area 11	7	7	24-Apr-26	04-May-26
11-2230	Frame New Gyp. Ceilings - Area 11	5	5	05-May-26	11-May-26
11-2240	Light Fixture Rough-in @ Gyp. Ceiling - Area 11	7	7	12-May-26	20-May-26
11-2250	HVAC Drops @ Gyp. Ceiling - Area 11	7	7	12-May-26	20-May-26
11-2310	Gypsum & ACOU1 Ceilings (Including Taping and Sanding) - Area 11	7	7	21-May-26	01-Jun-26
11-2190	Patch/Repair Existing Exposed Ceiling - Area 11	5	5	26-May-26	01-Jun-26
11-2200	Prime/1st Coat Walls and Ceilings - Area 11	4	4	02-Jun-26	05-Jun-26
11-2210	Install Suspended Light Fixtures - Area 11	8	8	08-Jun-26	17-Jun-26
11-2320	Install Ceiling Mount Diffusers - Area 11	8	8	08-Jun-26	17-Jun-26
11-2450	Install Frame for Glazing Wall System With Wood Cladding - Area 11	10	10	08-Jun-26	19-Jun-26
11-2460	Install Glass & Doors for Glazing Wall System - Area 11	10	10	08-Jun-26	19-Jun-26
11-2220	Install Projection Screens - Area 11	5	5	18-Jun-26	24-Jun-26
11-2340	Install Electrical & FA Devices and Trim - Area 11	5	5	18-Jun-26	24-Jun-26
11-2480	Wood Ceiling Panel Installation ACOU4 - Area 11	10	10	22-Jun-26	06-Jul-26
11-2700	Install Acoustic Wall Panel ACOU2&7 - Area 12	5	5	22-Jun-26	26-Jun-26
11-2160	Install Terrazzo Tile Flooring - Area 11	5	5	07-Jul-26	13-Jul-26
11-2140	Install New Millwork - Area 11	5	5	14-Jul-26	20-Jul-26

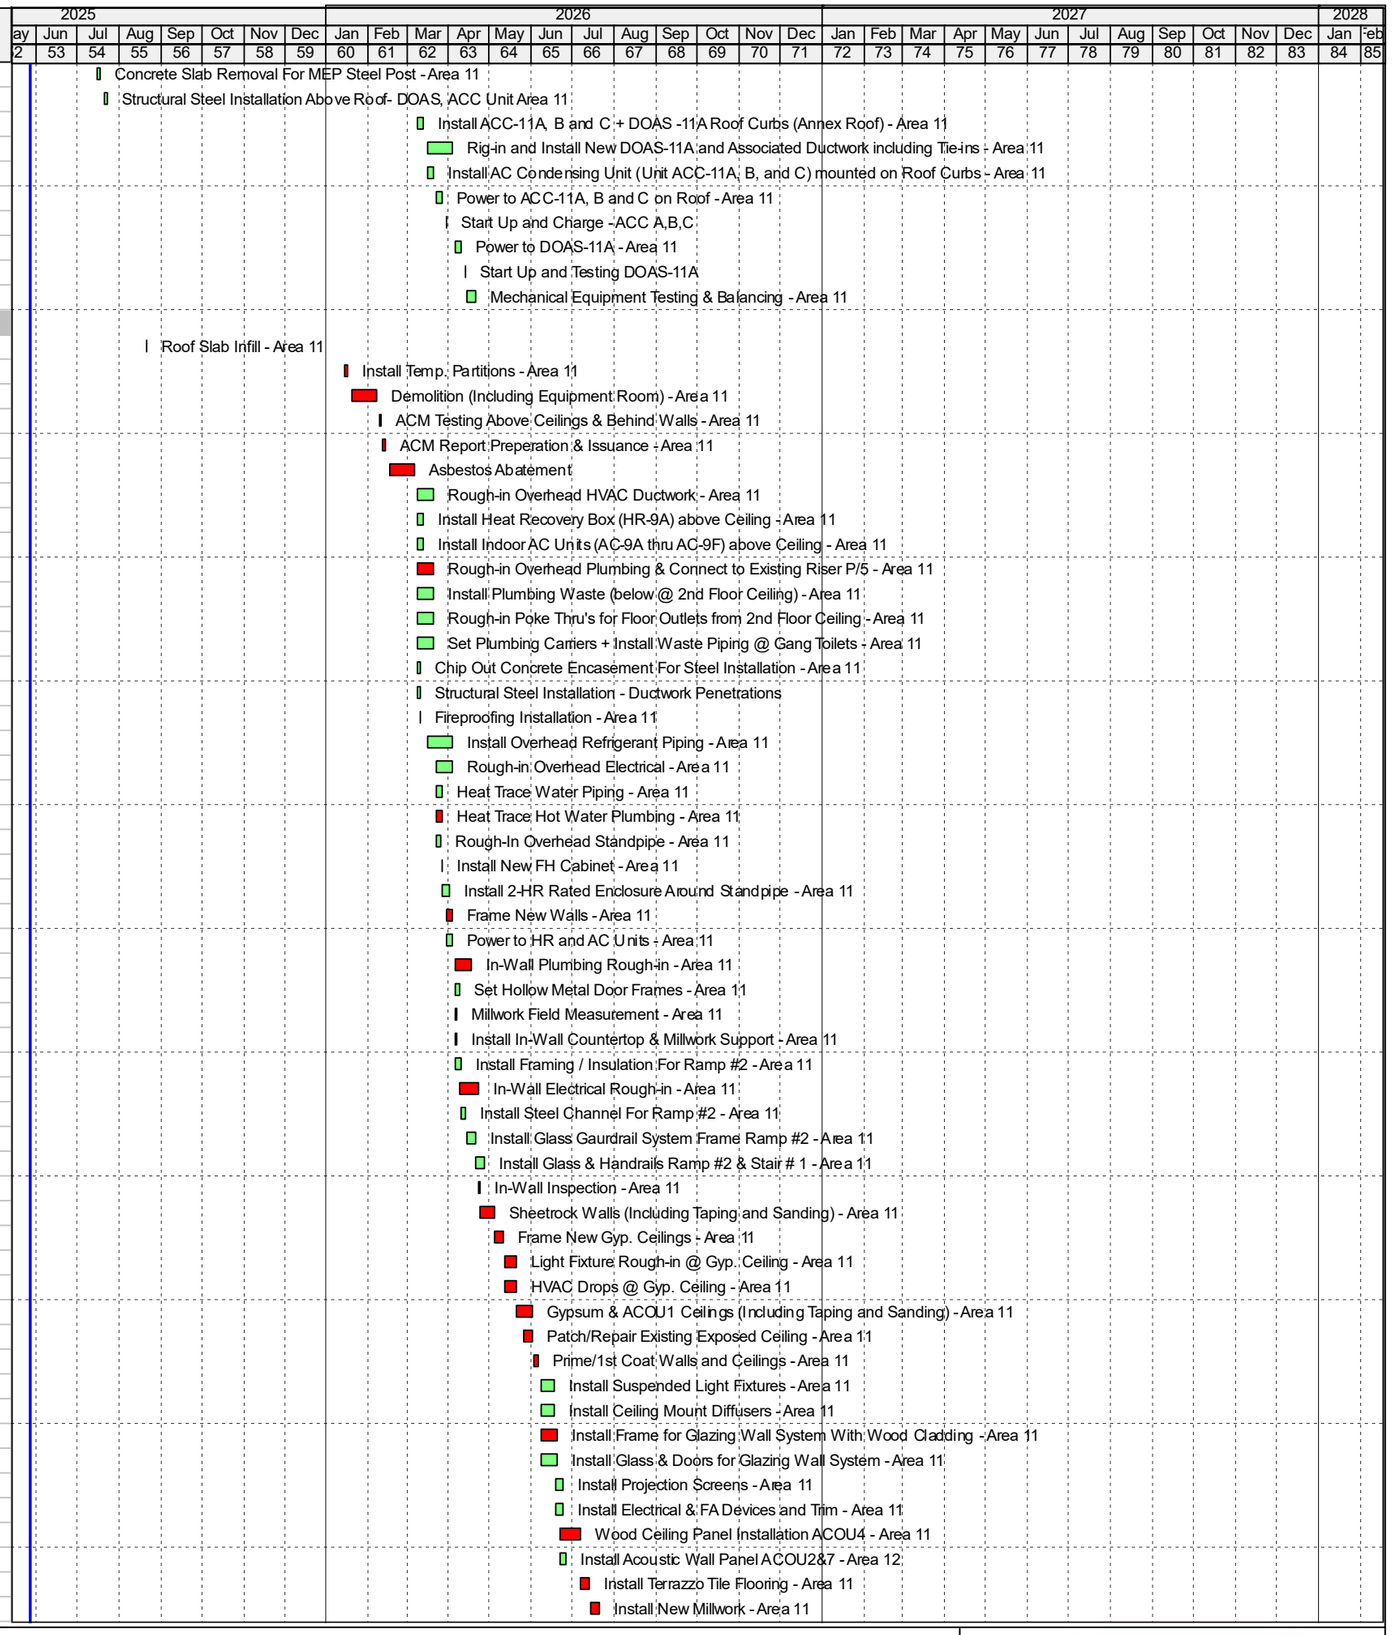

Finish Date: 04-Feb-28
Data Date: 28-May-25
Run Date: 11-Jun-25 16:20
BPL II - 09


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining ...
Summary Milestones
Critical Milestones
Milestone

Gilbane


Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
11-2180	Hang New Doors and Install Hardware - Area 11	5	5	14-Jul-26	20-Jul-26
11-2101	Install Pin-Up Felt ACOU5 - Area 11	5	5	14-Jul-26	20-Jul-26
11-2530	Install Carpet - Area 11	7	7	14-Jul-26	22-Jul-26
11-2680	Appliances Installation - Area 11	1	1	21-Jul-26	21-Jul-26
11-2690	Owner FF&E Installation - Area 11	5	5	23-Jul-26	29-Jul-26
11-2170	Install Glazing - Area 11	5	5	04-Aug-26	10-Aug-26
11-2370	Final Paint - Area 11	5	5	11-Aug-26	17-Aug-26
11-2350	Rolling Completion Work - Area 11	5	5	18-Aug-26	24-Aug-26
11-2540	Construction Final Cleaning	2	2	18-Aug-26	19-Aug-26
11-2661	Window Shade Installation - Area 11	4	4	18-Aug-26	21-Aug-26
11-2420	Signage Installation - Area 11	2	2	18-Aug-26	19-Aug-26
11-2523	Substantial Completion - Area 11	0	0		24-Aug-26
Bathrooms					
11-2550	Frame New Gyp. Ceilings - Area 11	2	2	05-May-26	06-May-26
11-2560	RDG Installation Bathrooms - Area 11	2	2	07-May-26	08-May-26
11-2570	Light Fixture Installation Bathrooms - Area 11	2	2	07-May-26	08-May-26
11-2580	Sheetrock Gyp. Ceilngs Bathrooms (Including Taping and Sanding) - Area 11	5	5	11-May-26	15-May-26
11-2390	Toilet Room Finishes (Ceramic Tile) - Area 11	5	5	18-May-26	22-May-26
11-2590	Install Built-IN WC Countertop and Backsplash STN - Area 11	1	1	26-May-26	26-May-26
11-2400	Install Plumbing Fixtures - Area 11	3	3	27-May-26	29-May-26
11-2670	Install Mirrors - Area 11	1	1	27-May-26	27-May-26
11-2430	Install Toilet Accessories - Area 11	3	3	01-Jun-26	03-Jun-26
Sub-Phase C					
Project Area 10 - 3rd Floor Open Work Spaces					
Detail					
AHU and ACC					
10-182	Remove Exisitng AC-5 / Ductwork / Piping / Louvers - PA10 Equipment Room	10	10	14-Sep-26	25-Sep-26
10-270	Wall Opening In Exterior Wall For AHU-5 Rigging - Area 10	3	3	21-Sep-26	23-Sep-26
10-184	Structural Probes - Area 10	1	1	25-Sep-26	25-Sep-26
10-179	Structural Steel Installation For Duct Slab Opening - PA10 Equipment Room	1	1	28-Sep-26	28-Sep-26
10-181	Extend Equipment Concrete Pad - PA10 Equipment Room	2	2	28-Sep-26	29-Sep-26
10-180	Fireproofing Installation - PA 10 Equipment Room	1	1	29-Sep-26	29-Sep-26
10-179	Concrete Slab Removal For Ductwork - Area 10	1	1	29-Sep-26	29-Sep-26
10-177	Rig-in and Install New AH-5 / RF-5 and Associated Ductwork including Tie-ins - An	20	20	30-Sep-26	27-Oct-26
10-178	Replace (Install New) Exhaust and Intake Louvers - Area 10	5	5	28-Oct-26	03-Nov-26
10-183	Power to AHU-5 - Area 10	5	5	28-Oct-26	03-Nov-26
10-271	Exterior Wall Patching / Stucco Finish At Bulkhead- Area 10	3	3	28-Oct-26	30-Oct-26
10-186	AH-5 Start Up	1	1	04-Nov-26	04-Nov-26
10-187	Mechanical Testing & Balancing - Area10	3	3	05-Nov-26	09-Nov-26
Interior Space					
10-159	Install Temp. Partitions - Area 10	3	3	09-Sep-26	11-Sep-26
10-160	Selective Demolition - Area 10	5	5	14-Sep-26	18-Sep-26
10-161	Exterior Window Restoration - Area 10	15	15	14-Sep-26	02-Oct-26
10-158	Frame New Walls - Area 10	5	5	21-Sep-26	25-Sep-26
10-170	Millwork Field Measurement - Area 10E	1	1	21-Sep-26	21-Sep-26
10-162	In-Wall Electrical Rough-in - Area 10	10	10	28-Sep-26	09-Oct-26
10-166	Set Hollow Metal Door Frames - Area 10	3	3	28-Sep-26	30-Sep-26
10-163	In-Wall Inspection - Area 10	1	1	12-Oct-26	12-Oct-26
10-164	Sheetrock Walls (Including Taping and Sanding) - Area 10	7	7	13-Oct-26	21-Oct-26
10-171	Prime/1st Coat Walls and Ceilings - Area 10	4	4	22-Oct-26	27-Oct-26
10-201	Install Frame For Glazing Wall System With Wood Cladding - Area 10	10	10	28-Oct-26	10-Nov-26
10-202	Install Glass & Doors For Glazing Wall System - Area 10	10	10	28-Oct-26	10-Nov-26
10-204	Acoustic Wood Ceiling Panels - Area 10	10	10	12-Nov-26	25-Nov-26
10-271	Install Acoustic Wall Panel ACOU2&7 - Area 10	5	5	12-Nov-26	18-Nov-26
10-167	Remove Existing & Install Resilient Flooring - Area 10	5	5	30-Nov-26	04-Dec-26
10-173	Install Projection Screens - Area 10	5	5	30-Nov-26	04-Dec-26
10-190	Install Electrical & FA Devices and Trim - Area 10	5	5	30-Nov-26	04-Dec-26
10-165	Install New Millwork - Area 10	10	10	07-Dec-26	18-Dec-26
10-169	Hang New Doors and Install Hardware - Area 10	5	5	07-Dec-26	11-Dec-26
10-273	Owner FF&E Installation - Area 10E	5	5	21-Dec-26	28-Dec-26
10-272	Appliances Installation - Area 10E	1	1	21-Dec-26	21-Dec-26
10-168	Install Glazing - Area 10	5	5	29-Dec-26	05-Jan-27
10-193	Final Paint - Area 10	5	5	06-Jan-27	12-Jan-27



Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
10-204	Rolling Completion Work - Area 10	5	5	13-Jan-27	19-Jan-27
10-207	Construction Final Cleaning	2	2	13-Jan-27	14-Jan-27
10-172	Signage Installation - Area 10E	2	2	13-Jan-27	14-Jan-27
10-205	Substantial Completion - Area 10	0	0		19-Jan-27
2nd Floor Balcony Bathrooms					
BB-1530	Install Temp. Partitions - 2nd Floor Balcony Bathrooms	2	2	21-Jul-26	22-Jul-26
BB-1540	Selective Demolition - 2nd Floor Balcony Bathrooms	5	5	23-Jul-26	29-Jul-26
BB-1550	Rough-in Overhead HVAC Ductwork - 2nd Floor Balcony Bathrooms	5	5	30-Jul-26	05-Aug-26
BB-1580	Install Plumbing Waste (below @ 1st Floor Ceiling) - 2nd Floor Balcony Bathroom	5	5	30-Jul-26	05-Aug-26
BB-1570	Set Plumbing Carriers + Install Waste Piping @ Gang Toilets - 2nd Floor Balcony	5	5	30-Jul-26	05-Aug-26
BB-1800	Shaft Demolition For Ductwork Connection	1	1	30-Jul-26	30-Jul-26
BB-1560	Rough-in Overhead Plumbing & Connect to Existing Riser P/8 and P/9. - 2nd Floo	5	5	31-Jul-26	06-Aug-26
BB-1600	Rough-in Overhead Electrical - 2nd Floor Balcony Bathrooms	5	5	06-Aug-26	12-Aug-26
BB-1790	Masonry Shaft Infill - 2nd Floor Balcony Bathrooms	1	1	06-Aug-26	06-Aug-26
BB-1610	Frame New Walls - 2nd Floor Balcony Bathrooms	4	4	07-Aug-26	12-Aug-26
BB-1590	Heat Trace Water Piping - 2nd Floor Balcony Bathrooms	5	5	07-Aug-26	13-Aug-26
BB-1620	In-Wall Plumbing Rough-in - 2nd Floor Balcony Bathrooms	5	5	13-Aug-26	19-Aug-26
BB-2610	Install In-Wall Countertop & Millwork Support - 2nd Floor BB	1	1	13-Aug-26	13-Aug-26
BB-1630	In-Wall Electrical Rough-in - 2nd Floor Balcony Bathrooms	4	4	19-Aug-26	24-Aug-26
BB-1640	In-Wall Inspection - 2nd Floor Balcony Bathrooms	1	1	25-Aug-26	25-Aug-26
BB-1650	Sheetrock Walls (Including Taping and Sanding) - 2nd Floor Balcony Bathrooms	4	4	26-Aug-26	31-Aug-26
BB-1660	Frame New Gyp. Ceilings - 2nd Floor Balcony Bathrooms	3	3	01-Sep-26	03-Sep-26
BB-1670	Light Fixture Rough-in @ Gyp. Ceiling - 2nd Floor Balcony Bathrooms	4	4	04-Sep-26	10-Sep-26
BB-1680	HVAC Drops @ Gyp. Ceiling - 2nd Floor Balcony Bathrooms	2	2	04-Sep-26	08-Sep-26
BB-1690	Sheetrock Gyp. Ceilings (Including Taping and Sanding) - 2nd Floor Balcony Bath	2	2	11-Sep-26	14-Sep-26
BB-1700	Prime/1st Coat Walls and Ceilings - 2nd Floor Balcony Bathrooms	2	2	15-Sep-26	16-Sep-26
BB-1710	Toilet Room Finishes (Ceramic Tile) - 2nd Floor Balcony Bathrooms	8	8	17-Sep-26	28-Sep-26
BB-1531	Install Built-IN WC Countertop and Backsplash STN - 2nd Floor BB	1	1	29-Sep-26	29-Sep-26
BB-1720	Install Plumbing Fixtures - 2nd Floor Balcony Bathrooms	5	5	30-Sep-26	06-Oct-26
BB-2680	Install Mirrors - 2nd Floor BB	1	1	30-Sep-26	30-Sep-26
BB-1730	Install Toilet Partitions - 2nd Floor Balcony Bathrooms	3	3	07-Oct-26	09-Oct-26
BB-1740	Install Toilet Accessories - 2nd Floor Balcony Bathrooms	2	2	12-Oct-26	13-Oct-26
BB-1750	Final Paint - 2nd Floor Balcony Bathrooms	2	2	14-Oct-26	15-Oct-26
BB-1760	Rolling Completion Work - 2nd Floor Balcony Bathrooms	3	3	16-Oct-26	20-Oct-26
BB-1780	Construction Final Cleaning	1	1	16-Oct-26	16-Oct-26
BB-1770	Substantial Completion - 2nd Floor Balcony Bathrooms - Beneficial Use	0	0		20-Oct-26
Project Area 5 - 1st Floor Language and Literature					
Detail					
AHU and ACC					
6-2110	Power to New AH-7 - PA5	20	20	26-Aug-26	23-Sep-26
6-2150	Extend Equipment Pad - Area 5	2	2	26-Aug-26	27-Aug-26
6-2701	Wall Opening In Exterior Wall For AHU-7 Rigging - Area 5	3	3	24-Sep-26	28-Sep-26
5-2080	Install New AH-7 from Mezzanine Mech. Room - PA5	20	20	29-Sep-26	26-Oct-26
5-2140	Start Up / Test / Charge AH-7 - PA5	4	4	27-Oct-26	30-Oct-26
6-2711	Exterior Wall Patching / Stucco Finish At Bulkhead- Area 5	3	3	27-Oct-26	29-Oct-26
5-2720	Mechanical Equipment Testing & Balancing - Area 5	5	5	27-Oct-26	02-Nov-26
Interior Space					
5-1000	Install Temp. Partitions - Area 5	3	3	31-Jul-26	04-Aug-26
5-1010	Demolition (Including Equipment Room) - Area 5	15	15	05-Aug-26	25-Aug-26
5-2550	ACM Testing Above Ceilings & Behind Walls - Area 5	2	2	26-Aug-26	27-Aug-26
5-2560	ACM Report Preperation & Issuance - Area 5	3	3	28-Aug-26	01-Sep-26
5-0960	Asbestos Abatement (including windows in Pop. Library)- Area 5	15	15	02-Sep-26	23-Sep-26
5-1040	Rough-in Overhead HVAC Ductwork - Area 5	10	10	24-Sep-26	07-Oct-26
5-2570	Exterior Window Glazing Installation / Window Restoration - Area 5	5	5	24-Sep-26	30-Sep-26
5-1020	Exterior Window Glazing Installation / Window Restoration (Night Work) - Pop. Lit	5	5	24-Sep-26	30-Sep-26
5-1120	Slab Trenching / Poke-Thru For Elec. For Outlets & Lighting	10	10	24-Sep-26	07-Oct-26
5-1110	Rough-in Overhead Electrical - Area 5	10	10	08-Oct-26	21-Oct-26
5-1400	Misc. Fireproofing Patching	1	1	08-Oct-26	08-Oct-26
5-1220	Patch/Repair Existing Sheetrock Walls (Including Taping and Sanding) - Area 5	7	7	22-Oct-26	30-Oct-26
5-1230	Frame New Gyp. Ceilings - Area 5	5	5	02-Nov-26	06-Nov-26
5-1240	Light Fixture Rough-in @ Gyp. Ceiling - Area 5	7	7	09-Nov-26	18-Nov-26
5-1250	HVAC Drops @ Gyp. Ceiling - Area 5	7	7	09-Nov-26	18-Nov-26
5-1260	Gypsum & ACOU1 Ceilings (Including Taping and Sanding) - Area 5	7	7	19-Nov-26	01-Dec-26

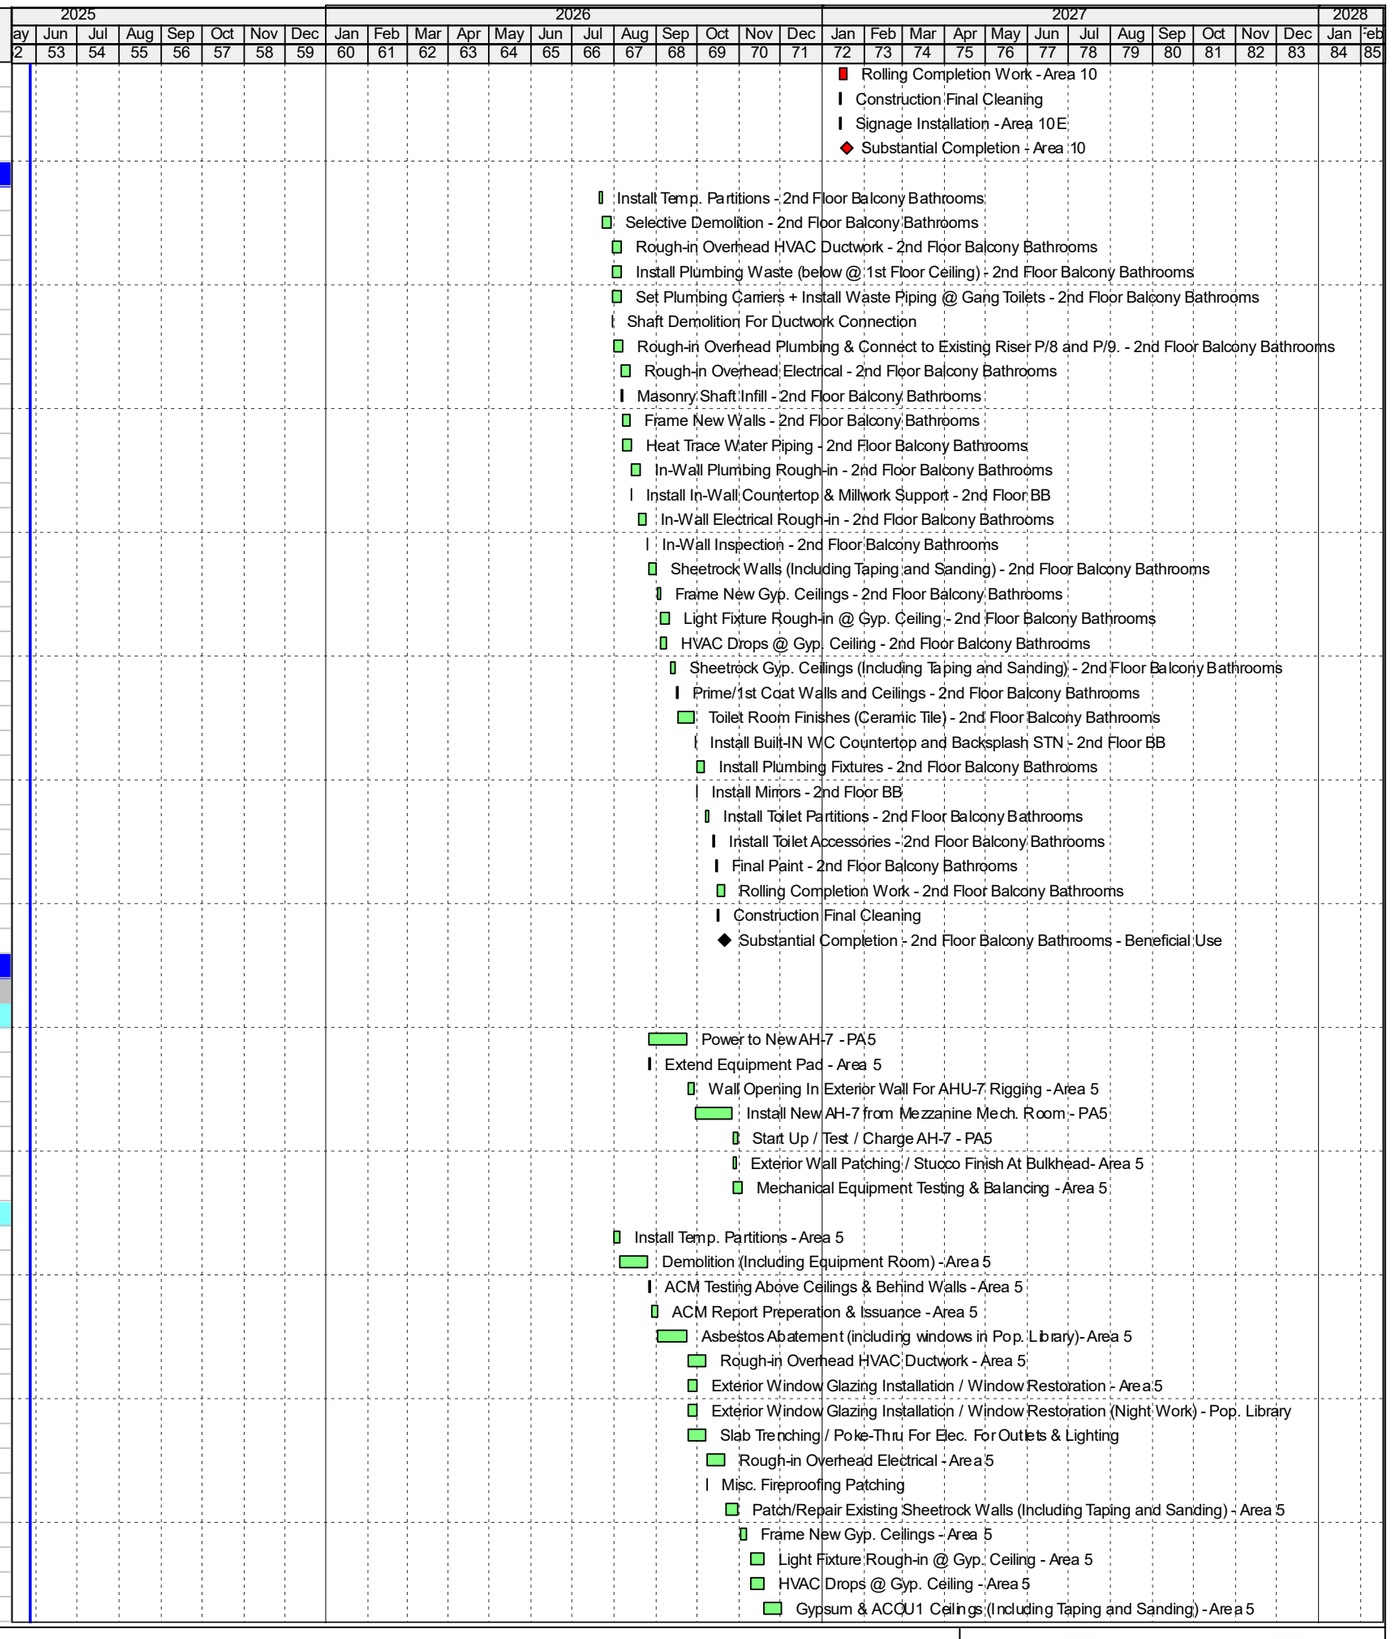

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
5-1300	Restore Existing Perimeter Millwork - Area 5	40	40	02-Dec-26	28-Jan-27
5-1280	Prime/1st Coat Walls and Ceilings - Area 5	4	4	02-Dec-26	07-Dec-26
5-1310	Install Suspended Light Fixtures - Area 5	8	8	08-Dec-26	17-Dec-26
5-1320	Install Ceiling Mount Diffusers - Area 5	8	8	08-Dec-26	17-Dec-26
5-1340	Install Electrical Devices and Trim - Area 5	5	5	11-Dec-26	17-Dec-26
5-1380	Install Terrazzo TIle Flooring - Area 5	7	7	18-Dec-26	29-Dec-26
5-1390	Install New Free Standing Millwork - Area 5	15	15	30-Dec-26	20-Jan-27
5-1410	Light Fixture Installation At Millwork - Area 5	10	10	07-Jan-27	20-Jan-27
5-1420	Final Paint - Area 5	5	5	21-Jan-27	27-Jan-27
5-2710	Owner FF&E Installation - Area 5	5	5	21-Jan-27	27-Jan-27
5-2700	Appliances Installation - Area 5	1	1	21-Jan-27	21-Jan-27
5-1430	Rolling Completion Work - Area 5	5	5	28-Jan-27	03-Feb-27
5-2661	Window Shade Installation - Area 5	4	4	28-Jan-27	02-Feb-27
5-1030	Signage Installation - Area 5	2	2	28-Jan-27	29-Jan-27
5-1460	Construction Final Cleaning	2	2	29-Jan-27	01-Feb-27
5-1440	Substantial Completion - Area 5	0	0		03-Feb-27
Bathrooms					
5-1011	Open Existing Wall For Blocking / Supports	1	1	24-Sep-26	24-Sep-26
5-1001	Install In-Wall Countertop & Millwork Support - Area 5	1	1	25-Sep-26	25-Sep-26
5-2580	Frame New Gyp. Ceilings - Area 5	1	1	02-Nov-26	02-Nov-26
5-2590	RDG Installation Bathrooms - Area 5	1	1	03-Nov-26	03-Nov-26
5-2600	Light Fixture Installation Bathrooms - Area 5	1	1	03-Nov-26	03-Nov-26
5-2610	Sheetrock Gyp. Ceilngs Bathrooms (Including Taping and Sanding) - Area 5	3	3	04-Nov-26	06-Nov-26
5-1441	Toilet Room Finishes (Ceramic Tile) - Area 5	2	2	09-Nov-26	10-Nov-26
5-2620	Install Built-IN WC Countertop and Backsplash STN - Area 5	1	1	12-Nov-26	12-Nov-26
5-2630	Install Plumbing Fixtures - Area 5	1	1	13-Nov-26	13-Nov-26
5-2690	Install Mirrors - Area 5	1	1	13-Nov-26	13-Nov-26
5-2640	Install Toilet Accessories - Area 5	1	1	16-Nov-26	16-Nov-26
Sub-Phase D					
Project Area 8B - 2nd Floor Adult Learning Center					
AHU and ACC					
8B-1540	Install ACC-5 B&C - Area 8B	5	5	07-Aug-25	13-Aug-25
8B-1828	New DOAS-8A / New Ductwork and Gas Tie-in	15	15	14-Aug-25	04-Sep-25
8B-2545	New ACC 5A and 5B at Roof	5	5	14-Aug-25	20-Aug-25
8B-2565	ACC 5A / 5B Charge and Start Up	2	2	21-Aug-25	22-Aug-25
8B-1830	Power to RTU-8A and ACC"s - Area 8B	5	5	05-Sep-25	11-Sep-25
8B-2555	RTU 8A Start Up	5	5	12-Sep-25	18-Sep-25
8B-2750	Mechanical Equipment Testing & Balancing - Area 8B	5	5	19-Sep-25	25-Sep-25
Interior Space					
8B-2670	Install Carpet - Area 8B	5	5	21-Aug-25	27-Aug-25
8B-2100	Install Temp. Partitions - Area 8B	3	3	27-Jan-27	29-Jan-27
8B-2070	Demolition (Including Equipment Room) - Area 8B	15	15	01-Feb-27	19-Feb-27
8B-2570	ACM Testing Above Ceilings & Behind Walls - Area 8B	2	2	22-Feb-27	23-Feb-27
8B-2580	ACM Report Preperation & Issuance - Area 8B	3	3	24-Feb-27	26-Feb-27
8B-2590	Asbestos Abatement - Area 8B	15	15	01-Mar-27	19-Mar-27
8B-2080	Rough-in Overhead HVAC Ductwork - Area 8B	10	10	22-Mar-27	02-Apr-27
8B-2260	Install Heat Recovery Box (HR-9A) above Ceiling - Area 8B	5	5	22-Mar-27	26-Mar-27
8B-2270	Install Indoor AC Units (AC-9A thru AC-9F) above Ceiling - Area 8B	5	5	22-Mar-27	26-Mar-27
8B-2300	Rough-in Overhead Plumbing & Connect to Existing Riser P/5 - Area 8B	10	10	22-Mar-27	02-Apr-27
8B-2410	Install Plumbing Waste (below @ 2nd Floor Ceiling) - Area 8B	10	10	22-Mar-27	02-Apr-27
8B-2470	Rough-in Poke Thru's for Floor Outlets from 2nd Floor Ceiling - Area 8B	3	3	22-Mar-27	24-Mar-27
8B-2490	Set Plumbing Carriers + Install Waste Piping @ Gang Toilets - Area 8B	10	10	22-Mar-27	02-Apr-27
8B-2280	Install Overhead Refrigerant Piping - Area 8B	15	15	29-Mar-27	16-Apr-27
8B-2090	Frame New Walls - Area 8B	4	4	05-Apr-27	08-Apr-27
8B-2330	Rough-in Overhead Electrical - Area 8B	10	10	05-Apr-27	16-Apr-27
8B-2440	Heat Trace Water Piping - Area 8B	5	5	05-Apr-27	09-Apr-27
8B-2500	Heat Trace Hot Water Plumbing - Area 8B	5	5	05-Apr-27	09-Apr-27
8B-2350	Misc. Fireproofing Patching	1	1	05-Apr-27	05-Apr-27
8B-2060	In-Wall Plumbing Rough-in - Area 8B	10	10	09-Apr-27	22-Apr-27
8B-2150	Set Hollow Metal Door Frames - Area 8B	3	3	09-Apr-27	13-Apr-27
8B-2380	Millwork Field Measurement	1	1	09-Apr-27	09-Apr-27
8B-2650	Install In-Wall Countertop & Millwork Support - Area 8B	1	1	09-Apr-27	09-Apr-27
8B-2290	Power to HR and AC Units - Area 8B	5	5	12-Apr-27	16-Apr-27

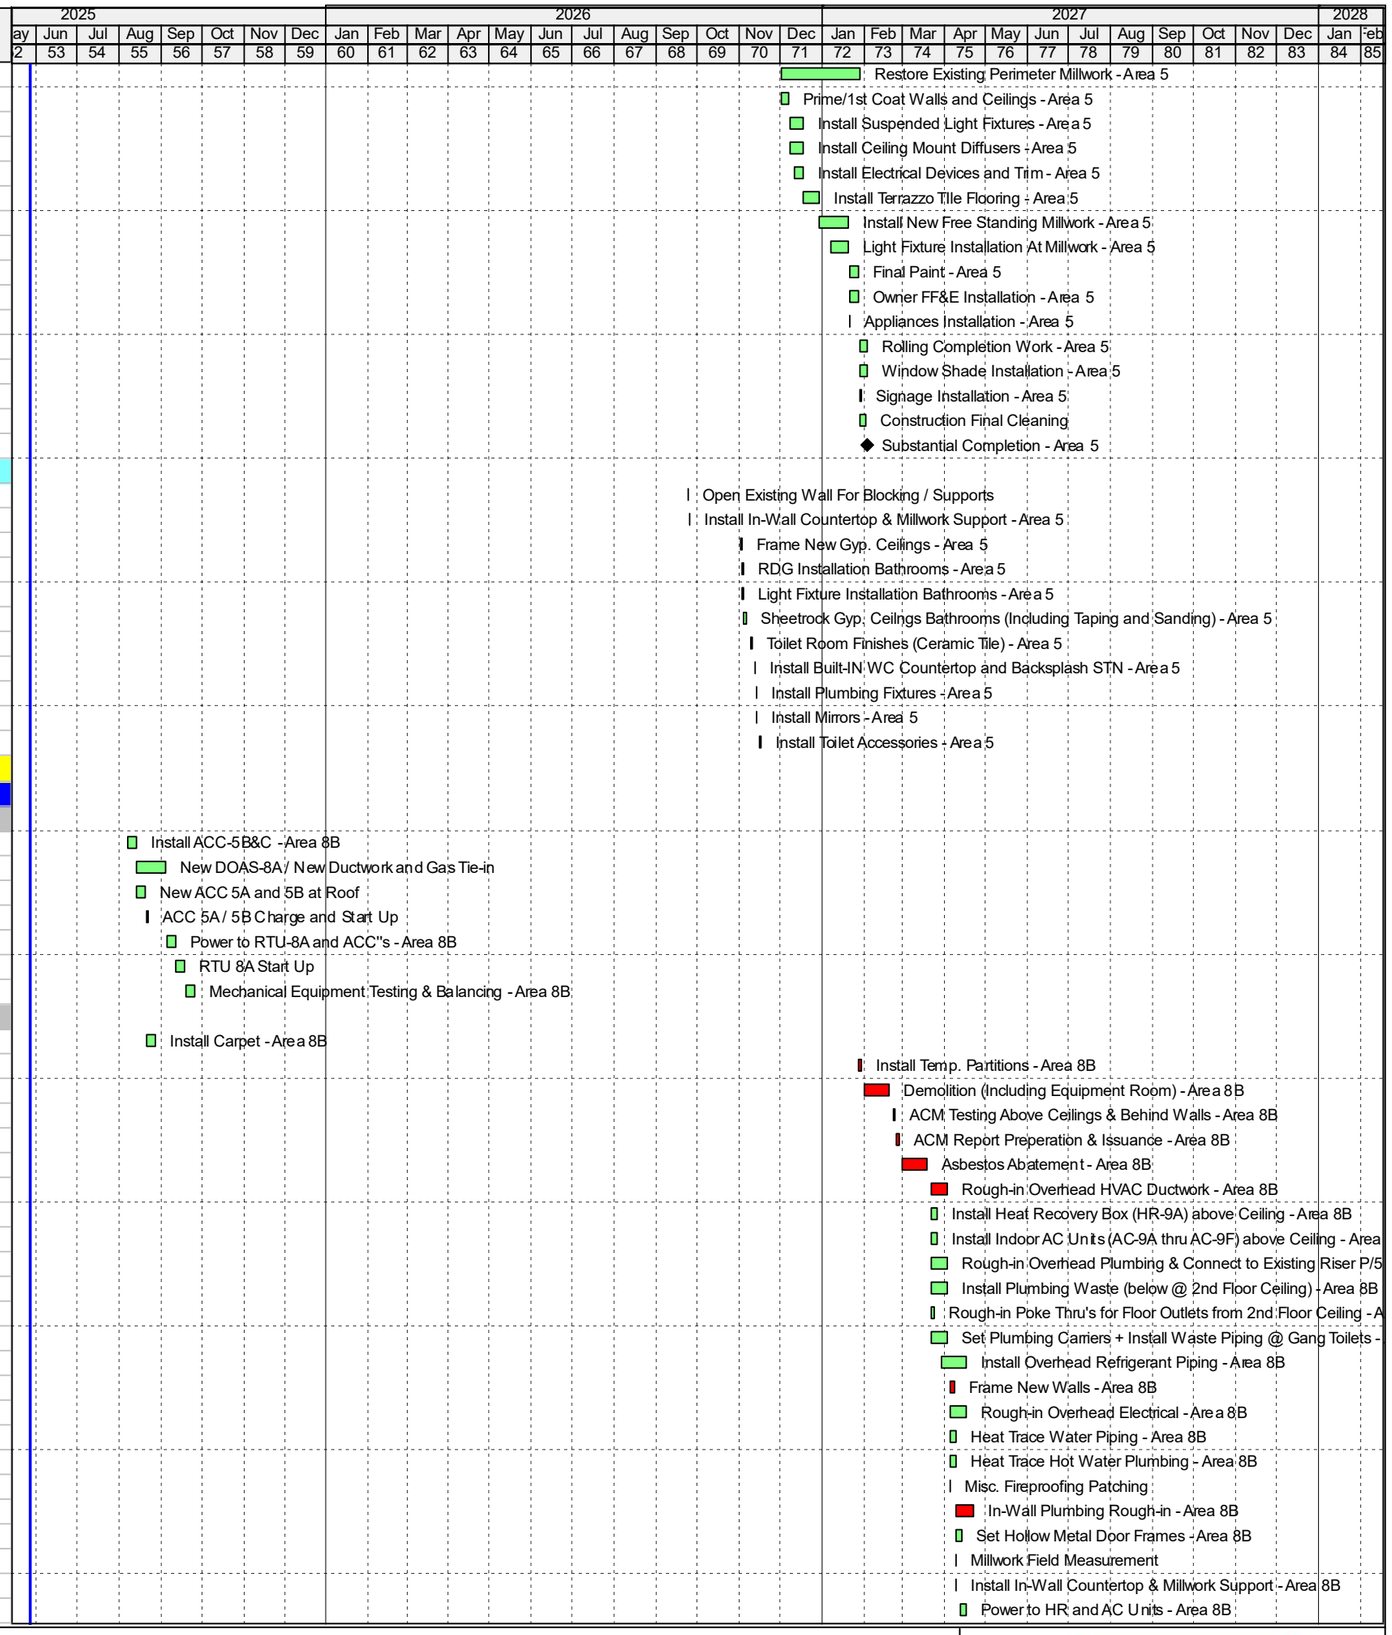


Finish Date: 04-Feb-28
Data Date: 28-May-25
Run Date: 11-Jun-25 16:20
BPL II - 09

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining ...
Summary Milestones
Critical Milestones
Milestone

Gilbane

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
8B-2110	In-Wall Electrical Rough-in - Area 8B	10	10	14-Apr-27	27-Apr-27
8B-2120	In-Wall Inspection - Area 8B	1	1	28-Apr-27	28-Apr-27
8B-2130	Sheetrock Walls (Including Taping and Sanding) - Area 8B	7	7	29-Apr-27	07-May-27
8B-2230	Frame New Gyp. Ceilings - Area 8B	5	5	10-May-27	14-May-27
8B-2240	Light Fixture Rough-in @ Gyp. Ceiling - Area 8B	7	7	17-May-27	25-May-27
8B-2250	HVAC Drops @ Gyp. Ceiling - Area 8B	7	7	17-May-27	25-May-27
8B-2310	Gypsum & ACOU1 Ceilings (Including Taping and Sanding) - Area 8B	7	7	26-May-27	04-Jun-27
8B-2190	Patch/Repair Existing Exposed Ceiling - Area 8B	5	5	28-May-27	04-Jun-27
8B-2200	Prime/1st Coat Walls and Ceilings - Area 8B	4	4	07-Jun-27	10-Jun-27
8B-2420	Wood Ceiling Panel Installation ACOU4 - Area 8B	5	5	07-Jun-27	11-Jun-27
8B-2540	Install Bathroom Accessories - Area 8B	1	1	09-Jun-27	09-Jun-27
8B-2210	Install Suspended Light Fixtures - Area 8B	8	8	11-Jun-27	22-Jun-27
8B-2320	Install Ceiling Mount Diffusers - Area 8B	8	8	11-Jun-27	22-Jun-27
8B-2450	Install Wood Frame & Caps WD6 - Area 8B	10	10	11-Jun-27	24-Jun-27
8B-2660	Install Storefront & Door 2-13	3	3	11-Jun-27	15-Jun-27
8B-2220	Install Projection Screens - Area 8B	5	5	23-Jun-27	29-Jun-27
8B-2340	Install Electrical & FA Devices and Trim - Area 8B	5	5	23-Jun-27	29-Jun-27
8B-2460	Instill Glazing In Wood Frame Systems - Area 8B	10	10	25-Jun-27	09-Jul-27
8B-2480	Acoustic Wood Ceiling Panels - Area 8B	10	10	25-Jun-27	09-Jul-27
8B-2740	Install Acoustic Wall Panel ACOU2 - Area 8A	2	2	25-Jun-27	28-Jun-27
8B-2370	Final Paint - Area 8B	5	5	30-Jun-27	07-Jul-27
8B-2525	Rolling Completion Work - Area 8B	5	5	08-Jul-27	14-Jul-27
8B-2700	Window Shade Installation - Area 8B	4	4	08-Jul-27	13-Jul-27
8B-2170	Signage Installation - Area 8B	2	2	08-Jul-27	09-Jul-27
8B-2160	Install Terrazzo Tile Flooring - Area 8B	5	5	12-Jul-27	16-Jul-27
8B-2140	Install New Millwork - Area 8B	5	5	19-Jul-27	23-Jul-27
8B-2180	Hang New Doors and Install Hardware - Area 8B	5	5	19-Jul-27	23-Jul-27
8B-2360	Install Pin-Up Felt ACOU5 - Area 8B	5	5	19-Jul-27	23-Jul-27
8B-2550	Install Handrails At Ramp R-B	2	2	19-Jul-27	20-Jul-27
8B-2730	Install Wood Wall Paneling WD5 - Area 8B	5	5	19-Jul-27	23-Jul-27
8B-2560	Construction Final Cleaning	2	2	26-Jul-27	27-Jul-27
8B-2720	Owner FF&E Installation - Area 8B	5	5	26-Jul-27	30-Jul-27
8B-2710	Appliances Installation - Area 8B	1	1	26-Jul-27	26-Jul-27
8B-2530	Substantial Completion - Area 8B	0	0		30-Jul-27
Bathrooms					
8B-2430	Install Toilet Accessories - Area 8B	3	3	19-Sep-25	23-Sep-25
8B-2600	Frame New Gyp. Ceilings - Area 8B	2	2	10-May-27	11-May-27
8B-2610	RDG Installation Bathrooms - Area 8B	2	2	12-May-27	13-May-27
8B-2620	Light Fixture Installation Bathrooms - Area 8B	2	2	12-May-27	13-May-27
8B-2630	Sheetrock Gyp. Ceilngs Bathrooms (Including Taping and Sanding) - Area 8B	5	5	14-May-27	20-May-27
8B-2390	Toilet Room Finishes (Ceramic Tile) - Area 8B	6	6	21-May-27	28-May-27
8B-2640	Install Built-IN WC Countertop and Backsplash STN - Area 8B	1	1	01-Jun-27	01-Jun-27
8B-2400	Install Plumbing Fixtures - Area 8B	5	5	02-Jun-27	08-Jun-27
8B-2690	Install Mirrors - Area 8B	1	1	02-Jun-27	02-Jun-27
Project Area 6 - 1st Floor Children's Wing					
Detail					
AHU and ACC					
6-2000	Open-up Shaft and Remove Existing Ductwork	10	10	04-Mar-27	17-Mar-27
6-2010	Install New Riser Duct - Mezzanine to 1st Floor	10	10	18-Mar-27	31-Mar-27
6-2090	Structural Probes - Area 6	1	1	24-Mar-27	24-Mar-27
6-2020	Extend Equipment Pad - Area 6	2	2	25-Mar-27	26-Mar-27
6-2702	Wall Opening In Exterior Wall For AHU-3 Rigging - Area 6	3	3	22-Apr-27	26-Apr-27
6-2040	Install New AH-3 from Mezzanine Mech. Room	20	20	27-Apr-27	24-May-27
6-2030	Rig ACC 6A on Roof - Pipe from Roof to Chase down to 1st Floor	15	15	27-Apr-27	17-May-27
6-1461	Install EF-6 on Roof - Area 6	2	2	18-May-27	19-May-27
6-2050	VRF's AC 6X at Preteen Lounge / Mezz-Loft / Classroom	15	15	25-May-27	15-Jun-27
6-2712	Exterior Wall Patching / Stucco Finish At Bulkhead- Area 6	3	3	25-May-27	27-May-27
6-2060	Power to New AHU-3 / ACC / VRF - Confirm from Existing Panels	20	20	16-Jun-27	14-Jul-27
6-2070	Start Up / Test / Charge AHU-3 / ACC 6A	4	4	15-Jul-27	20-Jul-27
6-2742	Mechanical Equipment Testing & Balancing - Area 5	5	5	21-Jul-27	27-Jul-27
Interior Space					
6-1000	Install Temp. Partitions - Area 6	5	5	25-Feb-27	03-Mar-27
6-1010	Demolition (Including Mezzanine) - Area 6	15	15	04-Mar-27	24-Mar-27

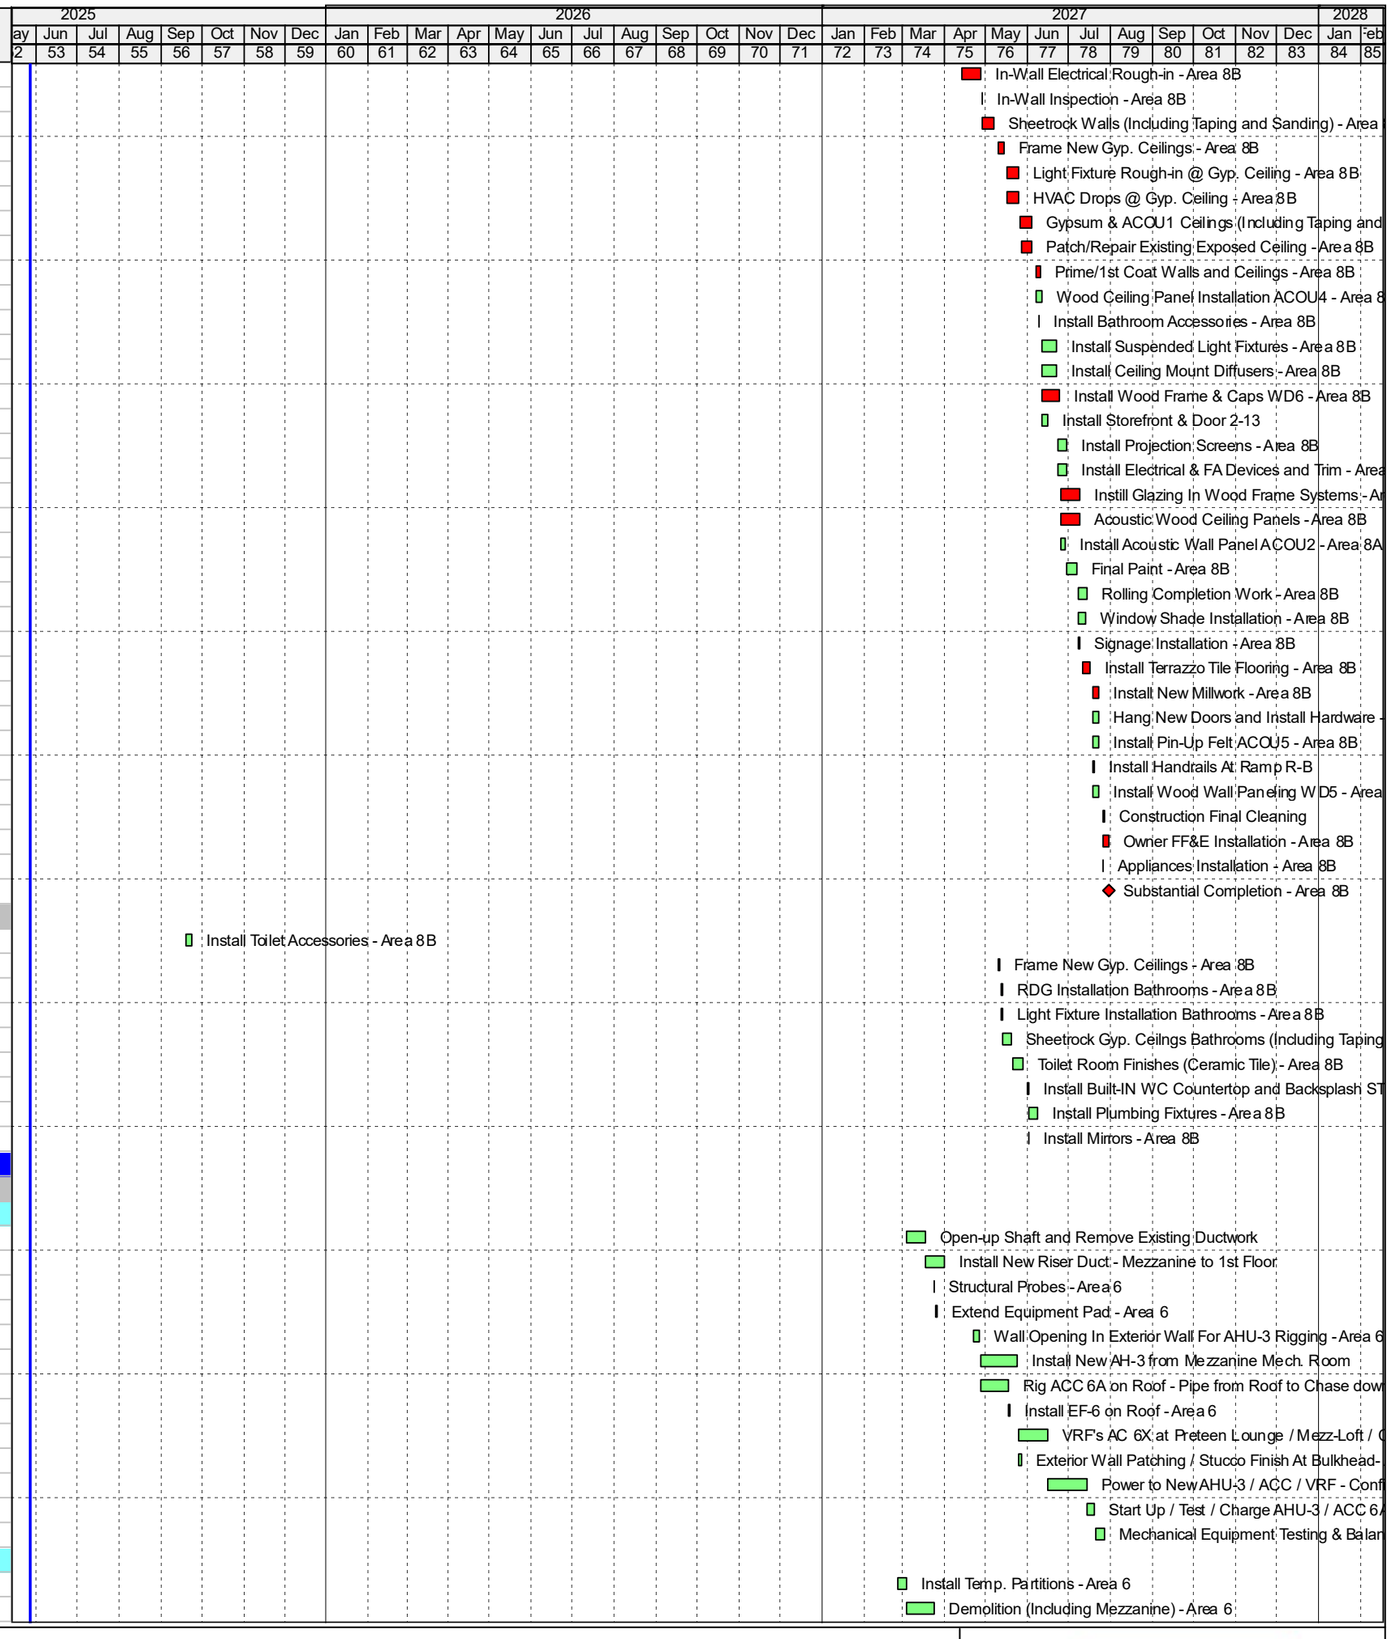


Finish Date: 04-Feb-28
Data Date: 28-May-25
Run Date: 11-Jun-25 16:20
BPL II - 09


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining ...
Summary Milestones
Critical Milestones
Milestone

Gilbane


Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
6-2600	ACM Testing Above Ceilings & Behind Walls - Area 6	2	2	25-Mar-27	26-Mar-27
6-2610	ACM Report Preperation & Issuance - Area 6	3	3	29-Mar-27	31-Mar-27
6-0960	Asbestos Abatement	15	15	01-Apr-27	21-Apr-27
6-1040	Rough-in Overhead HVAC Ductwork - Area 6	20	20	22-Apr-27	19-May-27
6-1011	Chip Out Concrete Encasement For Steel Installation - Area 6	2	2	22-Apr-27	23-Apr-27
6-1020	Exterior Window Glazing Installation / Window Restoration - Area 6	5	5	22-Apr-27	28-Apr-27
6-2661	Install In-Wall Countertop & Millwork Support - Area 6	1	1	22-Apr-27	22-Apr-27
6-2690	Frame New Walls - Area 6	5	5	22-Apr-27	28-Apr-27
6-1480	Remove Existing Ceiling Back Of House For Plumbing Rough-In - Area 6	2	2	22-Apr-27	23-Apr-27
6-1490	Remove Existing Ceiling In Brooklyn Collection For Plumbing Rough-In - Area 6	2	2	22-Apr-27	23-Apr-27
6-2710	Slab Trenching / Poke-Thru For Elec. For Outlets & Lighting - Area 6	7	7	22-Apr-27	30-Apr-27
6-1012	Structural Steel Installation - Domes Support - Area 6	5	5	26-Apr-27	30-Apr-27
6-1500	Rough-In Waste / Sanitary Piping - Area 6	5	5	26-Apr-27	30-Apr-27
6-1470	Rough-In Overhead Water & In-Wall Plumbing - Area 6	6	6	29-Apr-27	06-May-27
6-1013	Fireproofing Installation - Area 6	1	1	03-May-27	03-May-27
6-1030	Sheetrock Walls (Including Taping and Sanding) - Area 6	6	6	07-May-27	14-May-27
6-1090	Install Indoor HR and AC Units (HR-6A and AC-6A-6E) above Ceiling - Area 6	5	5	20-May-27	26-May-27
6-1110	Rough-in Overhead Electrical - Area 6	15	15	20-May-27	10-Jun-27
6-1130	Install Overhead Refrigerant Piping - Area 6	5	5	27-May-27	03-Jun-27
6-1140	Power to HR and AC Units - Area 6	5	5	04-Jun-27	10-Jun-27
6-1230	Frame New Gyp. Ceilings - Area 6	5	5	11-Jun-27	17-Jun-27
6-1240	Light Fixture Rough-in @ Gyp. Ceiling - Area 6	7	7	18-Jun-27	28-Jun-27
6-1250	HVAC Drops @ Gyp. Ceiling - Area 6	7	7	18-Jun-27	28-Jun-27
6-1220	Patch/Repair Sheetrock Walls (Including Taping and Sanding) - Area 6	7	7	29-Jun-27	08-Jul-27
6-1260	Gypsum & ACOU1 Ceilings (Including Taping and Sanding) - Area 6	15	15	29-Jun-27	20-Jul-27
6-1360	Hang New Doors and Install Hardware - Area 6	5	5	21-Jul-27	27-Jul-27
6-1280	Prime/1st Coat Walls and Ceilings - Area 6	4	4	21-Jul-27	26-Jul-27
6-2680	Restore Existing Perimeter Millwork - Area 6	40	40	21-Jul-27	15-Sep-27
6-1401	Install Storefront & Door 1-41	3	3	21-Jul-27	23-Jul-27
6-1310	Install Suspended Light Fixtures - Area 6	8	8	27-Jul-27	05-Aug-27
6-1320	Install Ceiling Mount Diffusers - Area 6	8	8	27-Jul-27	05-Aug-27
6-1340	Install Electrical & FA Devices and Trim - Area 6	5	5	30-Jul-27	05-Aug-27
6-1380	Install Terrazzo Tile Flooring - Area 6	7	7	06-Aug-27	16-Aug-27
6-1370	Install Projection Screens - Area 6	3	3	06-Aug-27	10-Aug-27
6-1300	Install New Millwork + Built-in Benches and Desks - Area 6	15	15	17-Aug-27	07-Sep-27
6-1390	Install Resilient Flooring At Mezzanine	2	2	17-Aug-27	18-Aug-27
6-1400	Install Glazing - Area 6	5	5	08-Sep-27	14-Sep-27
6-1330	Install Lighting & Power In Millwork - Area 6	5	5	08-Sep-27	14-Sep-27
6-2732	Owner FF&E Installation - Area 6	5	5	08-Sep-27	14-Sep-27
6-2722	Appliances Installation - Area 6	1	1	08-Sep-27	08-Sep-27
6-1420	Final Paint - Area 6	5	5	15-Sep-27	21-Sep-27
6-1430	Rolling Completion Work - Area 6	5	5	22-Sep-27	28-Sep-27
6-2703	Window Shade Installation - Area 6	4	4	22-Sep-27	27-Sep-27
6-1290	Signage Installation - Area 6	2	2	22-Sep-27	23-Sep-27
6-1450	Install Domes - Area 6	5	5	22-Sep-27	28-Sep-27
6-1410	Install Pour-In-Play Surface - Area 6	5	5	29-Sep-27	05-Oct-27
6-1460	Construction Final Cleaning - Area 6	2	2	06-Oct-27	07-Oct-27
6-1440	Substantial Completion - Area 6	0	0		07-Oct-27
Bathrooms					
6-2620	Frame New Gyp. Ceilings - Area 6	2	2	11-Jun-27	14-Jun-27
6-2630	RDG Installation Bathrooms - Area 6	2	2	15-Jun-27	16-Jun-27
6-2640	Light Fixture Installation Bathrooms - Area 6	2	2	15-Jun-27	16-Jun-27
6-2650	Sheetrock Gyp. Ceilngs Bathrooms (Including Taping and Sanding) - Area 6	5	5	17-Jun-27	23-Jun-27
6-1270	Toilet Room Finishes (Ceramic Tile) - Area 6	5	5	24-Jun-27	30-Jun-27
6-2660	Install Built-IN WC Countertop and Backsplash STN - Area 6	1	1	01-Jul-27	01-Jul-27
6-1350	Install Plumbing Fixtures - Area 6	5	5	02-Jul-27	09-Jul-27
6-2700	Install Mirrors - Area 6	1	1	02-Jul-27	02-Jul-27
6-2670	Install Toilet Accessories - Area 6	3	3	12-Jul-27	14-Jul-27
Project Area 10W					
AHU and ACC					
10W-45	ACC-10D Relocation	10	10	02-Jul-25	16-Jul-25
10W-10	Mechanical Equipment Testing & Balancing - Area 5	5	5	10-Sep-27	16-Sep-27
Interior Space					

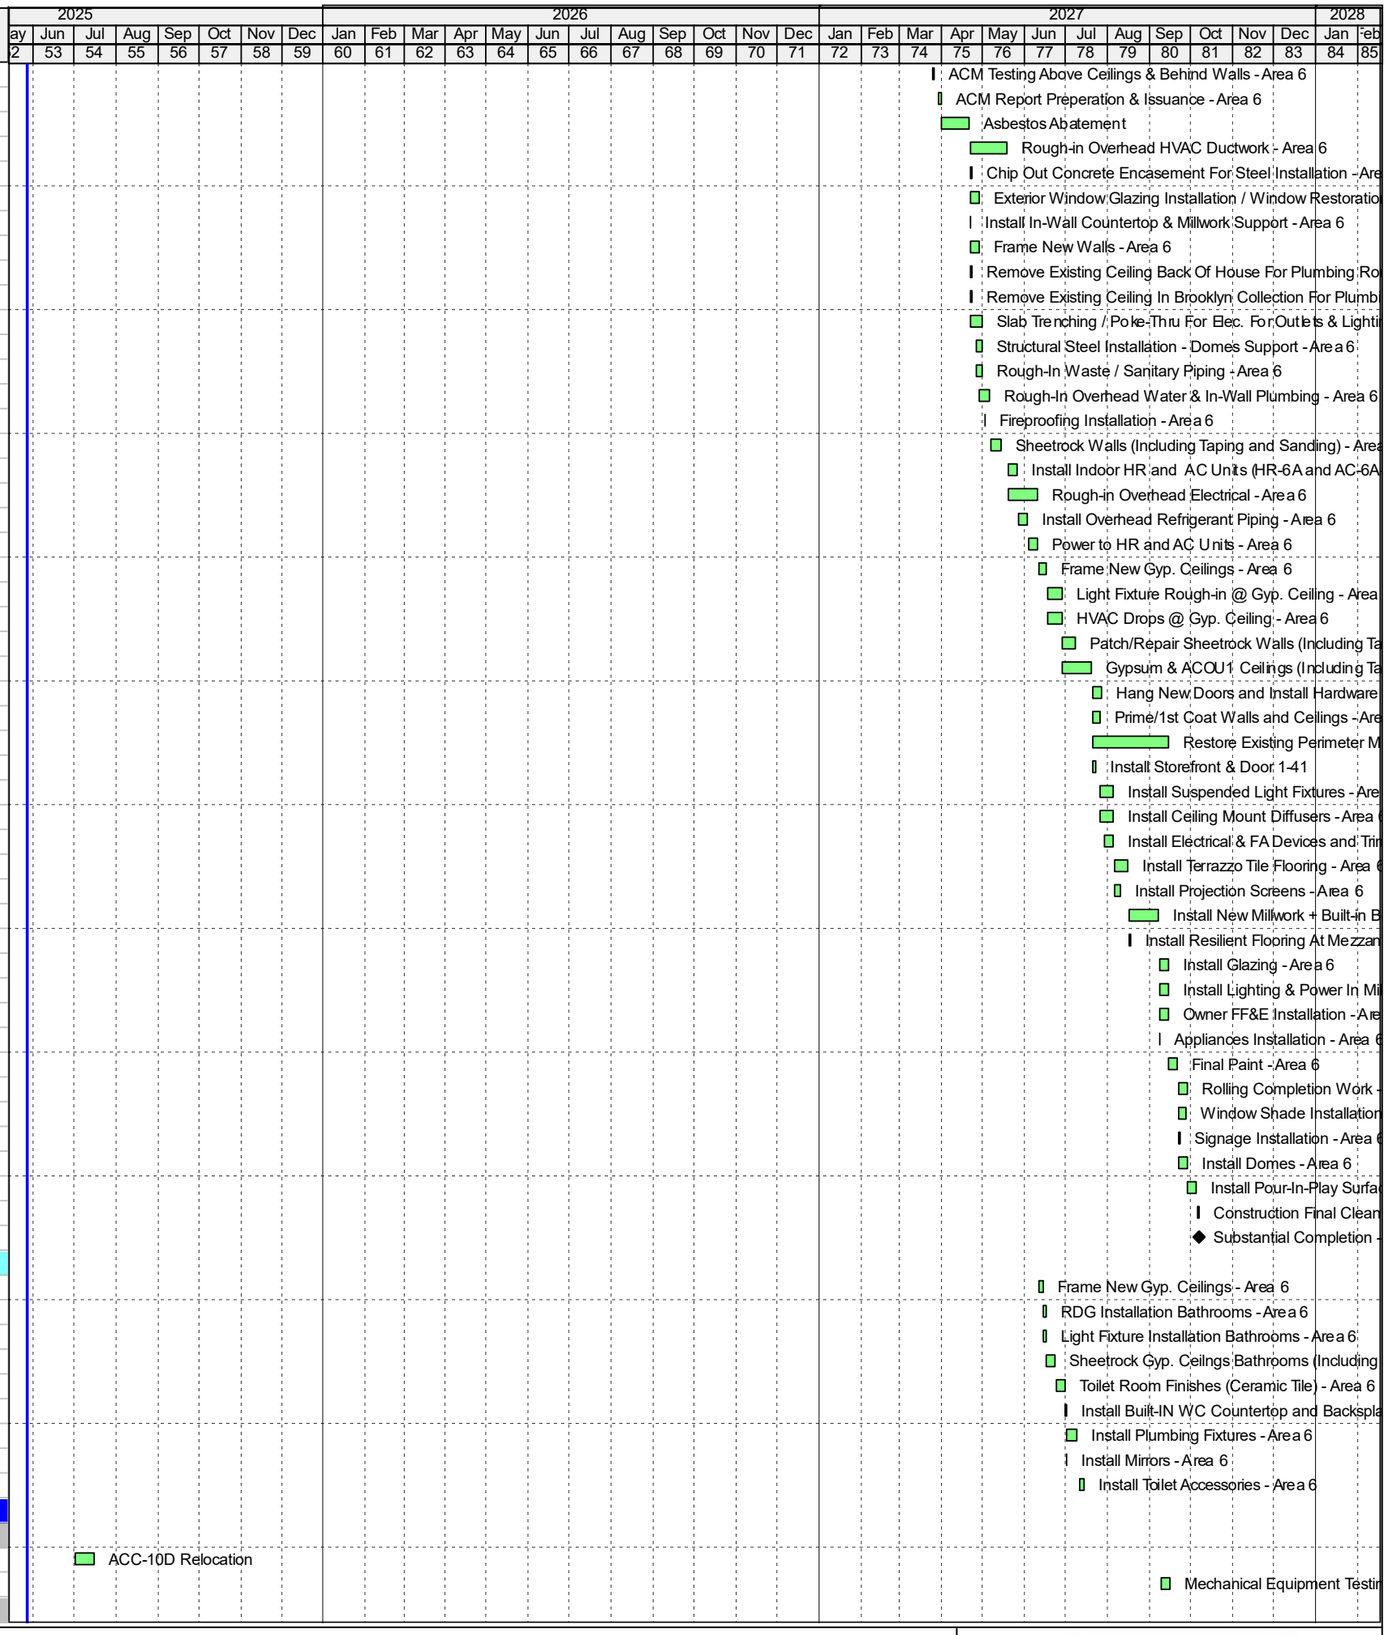

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
10-2080	Install Temp. Partitions - Area 10W	3	3	16-Aug-27	18-Aug-27
10-2090	Demolition (Including Equipment Room) - Area 10W	5	5	17-Aug-27	23-Aug-27
10-2100	ACM Testing Above Ceilings & Behind Walls - Area 10W	1	1	24-Aug-27	24-Aug-27
10-2110	ACM Report Preperation & Issuance - Area 10W	3	3	25-Aug-27	27-Aug-27
10-2120	Asbestos Abatement - Area 10W	5	5	30-Aug-27	03-Sep-27
10-1520	Structural Probes - Area 10W	1	1	07-Sep-27	07-Sep-27
10-2130	Rough-in Overhead HVAC Ductwork - Area 10W	5	5	07-Sep-27	13-Sep-27
10-2150	Install Indoor AC Units (AC-10N, M & L) above Ceiling - Area 10W	3	3	07-Sep-27	09-Sep-27
10-1530	Fireproofing - Area 10W	1	1	08-Sep-27	08-Sep-27
10-2210	Install Overhead Refrigerant Piping - Area 10W	5	5	10-Sep-27	16-Sep-27
10-2220	Frame New Walls - Area 10W	3	3	14-Sep-27	16-Sep-27
10-2320	Power to HR and AC Units - Area 10W	5	5	14-Sep-27	20-Sep-27
10-2230	Rough-in Overhead Electrical - Area 10W	5	5	14-Sep-27	20-Sep-27
10-1490	Exterior Window Restoration - Area 10W	5	5	17-Sep-27	23-Sep-27
10-2330	In-Wall Electrical Rough-in - Area 10W	3	3	17-Sep-27	21-Sep-27
10-2290	Set Hollow Metal Door Frames - Area 10W	1	1	17-Sep-27	17-Sep-27
10-2300	Millwork Field Measurement	1	1	17-Sep-27	17-Sep-27
10-2310	Install In-Wall Countertop & Millwork Support - Area 10W	1	1	17-Sep-27	17-Sep-27
10-2340	In-Wall Inspection - Area 10W	1	1	22-Sep-27	22-Sep-27
10-2350	Sheetrock Walls (Including Taping and Sanding) - Area 10W	5	5	22-Sep-27	28-Sep-27
10-2360	Frame New Gyp. Ceilings - Area 10W	3	3	29-Sep-27	01-Oct-27
10-2400	Wood Ceiling Panel Installation ACOU4 - Area 10W	3	3	29-Sep-27	01-Oct-27
10-2370	Light Fixture Rough-in @ Gyp. Ceiling - Area 10W	3	3	04-Oct-27	06-Oct-27
10-2380	HVAC Drops @ Gyp. Ceiling - Area 10W	3	3	04-Oct-27	06-Oct-27
10-2390	Gypsum & ACOU1 Ceilings (Including Taping and Sanding) - Area 10W	3	3	07-Oct-27	11-Oct-27
10-2410	Prime/1st Coat Walls and Ceilings - Area 10W	2	2	12-Oct-27	13-Oct-27
10-2430	Install Suspended Light Fixtures - Area 10W	3	3	14-Oct-27	18-Oct-27
10-2440	Install Ceiling Mount Diffusers - Area 10W	3	3	14-Oct-27	18-Oct-27
10-2450	Install Frame For Glazing Wall System With Wood Cladding - Area10W	3	3	14-Oct-27	18-Oct-27
10-2470	Install Acoustic Wall Panel ACOU2 - Area 10W	3	3	14-Oct-27	18-Oct-27
10-2490	Install Electrical & FA Devices and Trim - Area 10W	1	1	18-Oct-27	18-Oct-27
10-2510	Install Terrazzo Tile Flooring - Area 10W	3	3	19-Oct-27	21-Oct-27
10-2540	Install Glazing - Area 10W	3	3	19-Oct-27	21-Oct-27
10-2500	Acoustic Wood Ceiling Panels - Area 10W	3	3	19-Oct-27	21-Oct-27
10-1500	Millwork Installation - Area 10W	3	3	22-Oct-27	26-Oct-27
10-2530	Hang New Doors and Install Hardware - Area 10W	2	2	22-Oct-27	25-Oct-27
10-2550	Final Paint - Area 10W	3	3	22-Oct-27	26-Oct-27
10-1540	Self Level / Install Resilient Flooring - Area 10W	2	2	22-Oct-27	25-Oct-27
10-2570	Construction Final Cleaning - Area 10W	1	1	27-Oct-27	27-Oct-27
10-2700	Window Shade Installation - Area 10W	4	4	27-Oct-27	01-Nov-27
10-2140	Signage Installation - Area 10W	1	1	27-Oct-27	27-Oct-27
10-2751	Owner FF&E Installation - Area 10W	5	5	27-Oct-27	02-Nov-27
10-2741	Appliances Installation - Area 10W	1	1	27-Oct-27	27-Oct-27
10-2580	Substantial Completion - Area 10W	0	0		02-Nov-27
Exterior Renovations					
A4980	Sidewalk Shed & Fence Installation	10	10	06-Jun-25	19-Jun-25
A5340	Exterior Restoration Completion	1	1	16-Sep-25	16-Sep-25
Main Entrance Elevation					
A1370	Rigging and Installation of Scaffold Drops - Main Entrance	5	5	24-Jul-25*	30-Jul-25
A1460	Stone Crack/Spall Restoration- STN	7	7	31-Jul-25	08-Aug-25
A1480	Clean Elevation - CLN	7	7	31-Jul-25	08-Aug-25
A1750	Granite Panel Replacement - STN	5	5	31-Jul-25	06-Aug-25
A5390	Limestone Coping Restoration At Roof - COP	3	3	31-Jul-25	04-Aug-25
A1800	Sealant Joint Restoration & Repointing - JNT & PNT	5	5	31-Jul-25	06-Aug-25
A1810	Main Entrance Elevation Completion	1	1	11-Aug-25	11-Aug-25
South Entrance - Childrens Wing					
A1380	Mobilize Scaffold / Window Protection	5	5	24-Jul-25	30-Jul-25
A1490	Clean Elevation - CLN	3	3	31-Jul-25	04-Aug-25
A5810	Window Mullion Restoration - WIN 04	3	3	31-Jul-25	04-Aug-25
A5820	Sealant Joint Restoration - JNT	3	3	31-Jul-25	04-Aug-25
A5830	Childrens Wing Completion	1	1	05-Aug-25	05-Aug-25
Eastern Parkway Elevation					
A5490	Rigging and Installation of Scaffold Drops - Eastern Parkway	15	15	20-Jun-25*	11-Jul-25

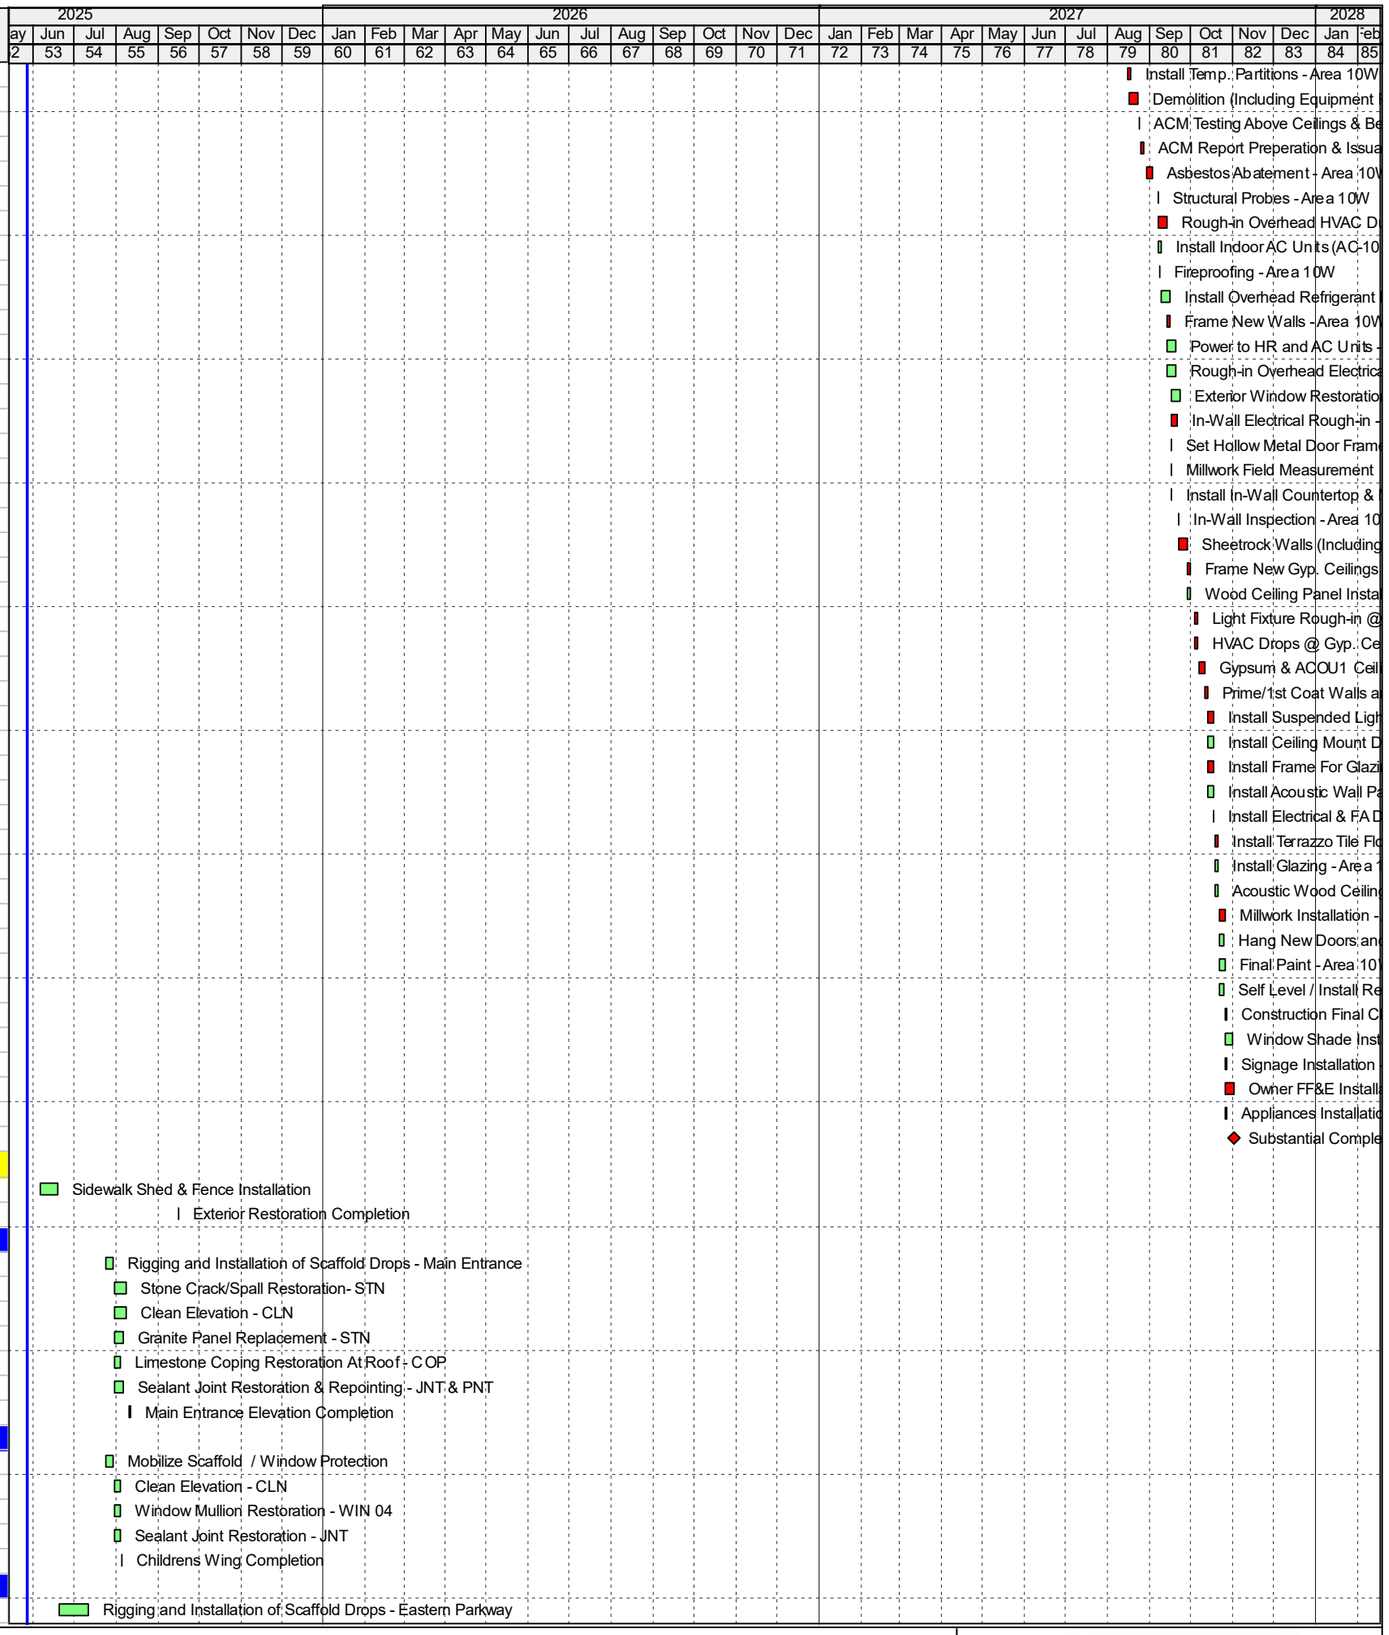

Activity ID	Activity Name	Original Duration	Remaining Duration	Actual Start	Actual Finish
A5500	Stone Crack/Spall Restoration- STN	7	7	14-Jul-25	22-Jul-25
A5510	Clean Elevation - CLN	7	7	14-Jul-25	22-Jul-25
A5520	Granite Panel Replacement - STN	5	5	14-Jul-25	18-Jul-25
A5540	Sealant Joint Restoration & Repointing - JNT & PNT	6	6	14-Jul-25	21-Jul-25
A5480	Window Mullion Restoration - WIN 04	5	5	14-Jul-25	18-Jul-25
A5550	Eastern Parkway Elevation Completion	1	1	23-Jul-25	23-Jul-25
Flatbush Avenue Elevation					
A5400	Rigging and Installation of Scaffold Drops - Flatbush Ave	15	15	20-Jun-25*	11-Jul-25
A5410	Stone Crack/Spall Restoration- STN	7	7	14-Jul-25	22-Jul-25
A5420	Clean Elevation - CLN	7	7	14-Jul-25	22-Jul-25
A5430	Granite Panel Replacement - STN	5	5	14-Jul-25	18-Jul-25
A5440	Limestone Coping Restoration At Roof - COP	3	3	14-Jul-25	16-Jul-25
A5450	Sealant Joint Restoration & Repointing - JNT & PNT	5	5	14-Jul-25	18-Jul-25
A5470	Window Sill Restoration - WIN 05	3	3	14-Jul-25	16-Jul-25
A5460	Flatbush Elevation Completion	1	1	23-Jul-25	23-Jul-25
Annex Elevation (All Annex Elevations)					
A5580	Equipment Mobilization	1	1	12-Aug-25	12-Aug-25
A5560	Stone Crack/Spall Restoration- STN	4	4	13-Aug-25	18-Aug-25
A5570	Sealant Joint Restoration - JNT	3	3	13-Aug-25	15-Aug-25
A5590	Annex Elevation Completion	1	1	19-Aug-25	19-Aug-25
Courtyard Elevations					
A1420	Equipment Mobilization	1	1	12-Aug-25	12-Aug-25
A1720	Stucco Replacement - STC	8	8	13-Aug-25	22-Aug-25
A1730	Courtyard Elevation Completion	1	1	25-Aug-25	25-Aug-25
Main Roof Elevations					
A1740	Install Railing System (RAI)	10	10	21-Aug-25	04-Sep-25
A5610	Mobilize Scaffolding (Rolling Scaffolding)	5	5	26-Aug-25*	02-Sep-25
A5650	Stucco Replacement - STC	8	8	03-Sep-25	12-Sep-25
A5620	Stone Repointing - PNT	3	3	03-Sep-25	05-Sep-25
A5640	Sealant Joint Restoration- JNT	3	3	03-Sep-25	05-Sep-25
A5630	Main Roof Elevation Completion	1	1	15-Sep-25	15-Sep-25
Eastern Parkway Roof					
A5660	Mobilize Scaffolding (Rolling Scaffolding)	5	5	26-Aug-25*	02-Sep-25
A5690	Stone Repointing - PNT	4	4	03-Sep-25	08-Sep-25
A5670	Sealant Joint Restoration- JNT	3	3	03-Sep-25	05-Sep-25
A5700	Eastern Parkway Roof Elevation Completion	1	1	09-Sep-25	09-Sep-25
Flatbush Ave Roof					
A5710	Mobilize Scaffolding (Rolling Scaffolding)	5	5	26-Aug-25*	02-Sep-25
A5730	Stone Crack Restoration - STN	8	8	03-Sep-25	12-Sep-25
A5740	Stone Repointing - PNT	4	4	03-Sep-25	08-Sep-25
A5720	Sealant Joint Restoration- JNT	3	3	03-Sep-25	05-Sep-25
A5750	Flatbush Ave Roof Elevation Completion	1	1	15-Sep-25	15-Sep-25
Annex Roof					
A5360	Install Roof-Mounted Railing	5	5	21-Aug-25	27-Aug-25
A5380	Flashing At Existing Mechanical Units	3	3	26-Aug-25	28-Aug-25
A5530	Annex Roof Completion	1	1	29-Aug-25	29-Aug-25
Terraced Roof					
A5370	Install Roof-Mounted Railing	5	5	21-Aug-25	27-Aug-25
A5760	Mobilize Scaffolding (Rolling Scaffolding)	5	5	26-Aug-25*	02-Sep-25
A5780	Stone Crack Restoration - STN	8	8	03-Sep-25	12-Sep-25
A5790	Stucco Replacement - STC	3	3	03-Sep-25	05-Sep-25
A5800	Flatbush Ave Roof Elevation Completion	1	1	15-Sep-25	15-Sep-25

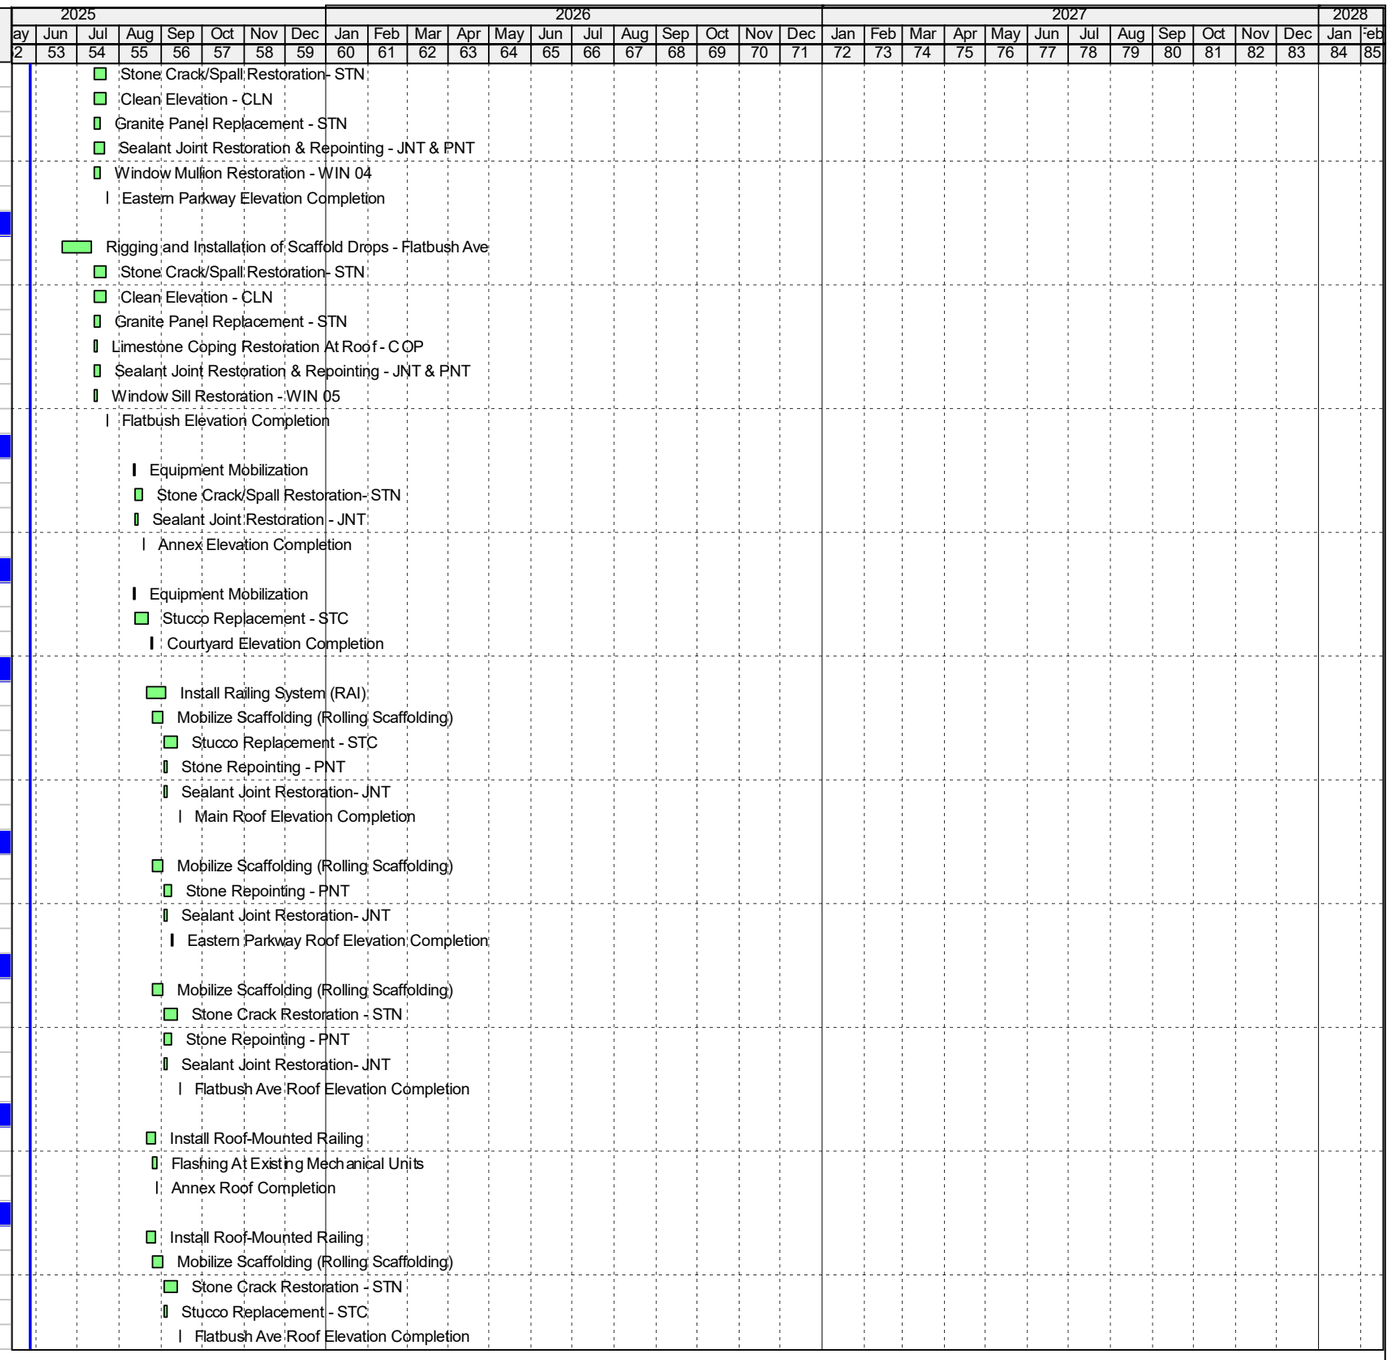

Finish Date: 04-Feb-28
Data Date: 28-May-25
Run Date: 11-Jun-25 16:20
BPL II - 09

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining ...
Summary Milestones
Critical Milestones
Milestone

Gilbane
