
Activity ID	Activity Name	Remaining Duration	Start	Finish
Turkish NTO Contract- VRH KC03042026		222	10-Nov-25 A	12-Jan-27
Turkish CIP- JFK T1		222	10-Nov-25 A	12-Jan-27
Preconstruction		115	10-Nov-25 A	12-Aug-26
3	Final Contract Negotiation	0	10-Nov-25 A	02-Dec-25 A
5	Develop M/WBE Plan	0	03-Dec-25 A	16-Dec-25 A
4	Negotiate and Issue Subcontracts	0	03-Dec-25 A	23-Dec-25 A
6	Submit M/WBE Plan	0	17-Dec-25 A	17-Dec-25 A
7	PANYNJ Conditional Approval & Scheduling Precon Meeting	0	18-Dec-25 A	24-Dec-25 A
8	Submit Critical Packages	0	24-Dec-25 A	08-Jan-26 A
11	TK Issue Notice to Proceed	0	26-Dec-25 A	26-Dec-25 A
12	Review and Accept Landlord White Box	0	29-Dec-25 A	29-Dec-25 A
9	Arch Review and Approve Critical Packages	0	09-Jan-26 A	03-Mar-26 A
13	Hold PANYNJ Precon	0	23-Feb-26 A	23-Feb-26 A
14	Mobilize to Site	0	24-Feb-26 A	24-Feb-26 A
10	Procure Long Lead Items	115	04-Mar-26*	12-Aug-26
Closeout		24	10-Dec-26	12-Jan-27
62	As-Builts/ O&Ms/ Warranties	20	10-Dec-26	06-Jan-27
63	Submit Final Payment Application and Waivers	4	07-Jan-27	12-Jan-27
Construction		191	24-Feb-26 A	30-Nov-26
16	Validate Space Layout	0	24-Feb-26 A	24-Feb-26 A
17	Slab X Ray	0	25-Feb-26 A	26-Feb-26 A
18	Wall Framing	8	02-Mar-26 A	13-Mar-26
19	Core Drill	2	05-Mar-26*	06-Mar-26
21	Place Topping Slab	3	09-Mar-26	11-Mar-26
20	Below Slab Roughin	20	09-Mar-26	03-Apr-26
22	Wall Framing	10	12-Mar-26	25-Mar-26
23	Soffit Framing	17	16-Mar-26	07-Apr-26
24	Overhead Rough In	35	26-Mar-26	13-May-26
25	In Wall Rough In	20	14-May-26	11-Jun-26
26	Install Gypsum Wall Board	13	12-Jun-26	30-Jun-26
27	Tape, Spackle & Finish	10	01-Jul-26	14-Jul-26
28	Install Column Covers	20	01-Jul-26	28-Jul-26*
29	Paint Gyp Ceilings/ Soffits	4	15-Jul-26	20-Jul-26
30	Install Ceramic Tile	15	15-Jul-26	04-Aug-26*
31	Paint Walls	4	21-Jul-26	24-Jul-26
32	Install ACT Grid	14	27-Jul-26*	13-Aug-26
33	Install Ceiling Elements	15	14-Aug-26	03-Sep-26
34	Install Access Flooring	10	04-Sep-26	18-Sep-26
37	Install Vector Wall System	30	14-Sep-26	23-Oct-26
36	Install Ornamental Elements	20	21-Sep-26	16-Oct-26
35	Install Millwork	30	21-Sep-26	30-Oct-26
39	Install Wall Covering	8	19-Oct-26	28-Oct-26
38	Install Flooring	15	19-Oct-26	06-Nov-26
44	Install Doors and Hardware	10	29-Oct-26	11-Nov-26
42	Trim Out MEP Devices & Bathrooms	15	29-Oct-26	18-Nov-26
40	Deliver Food Service Equipment	3	09-Nov-26	11-Nov-26
45	Install Carpet	2	12-Nov-26	13-Nov-26

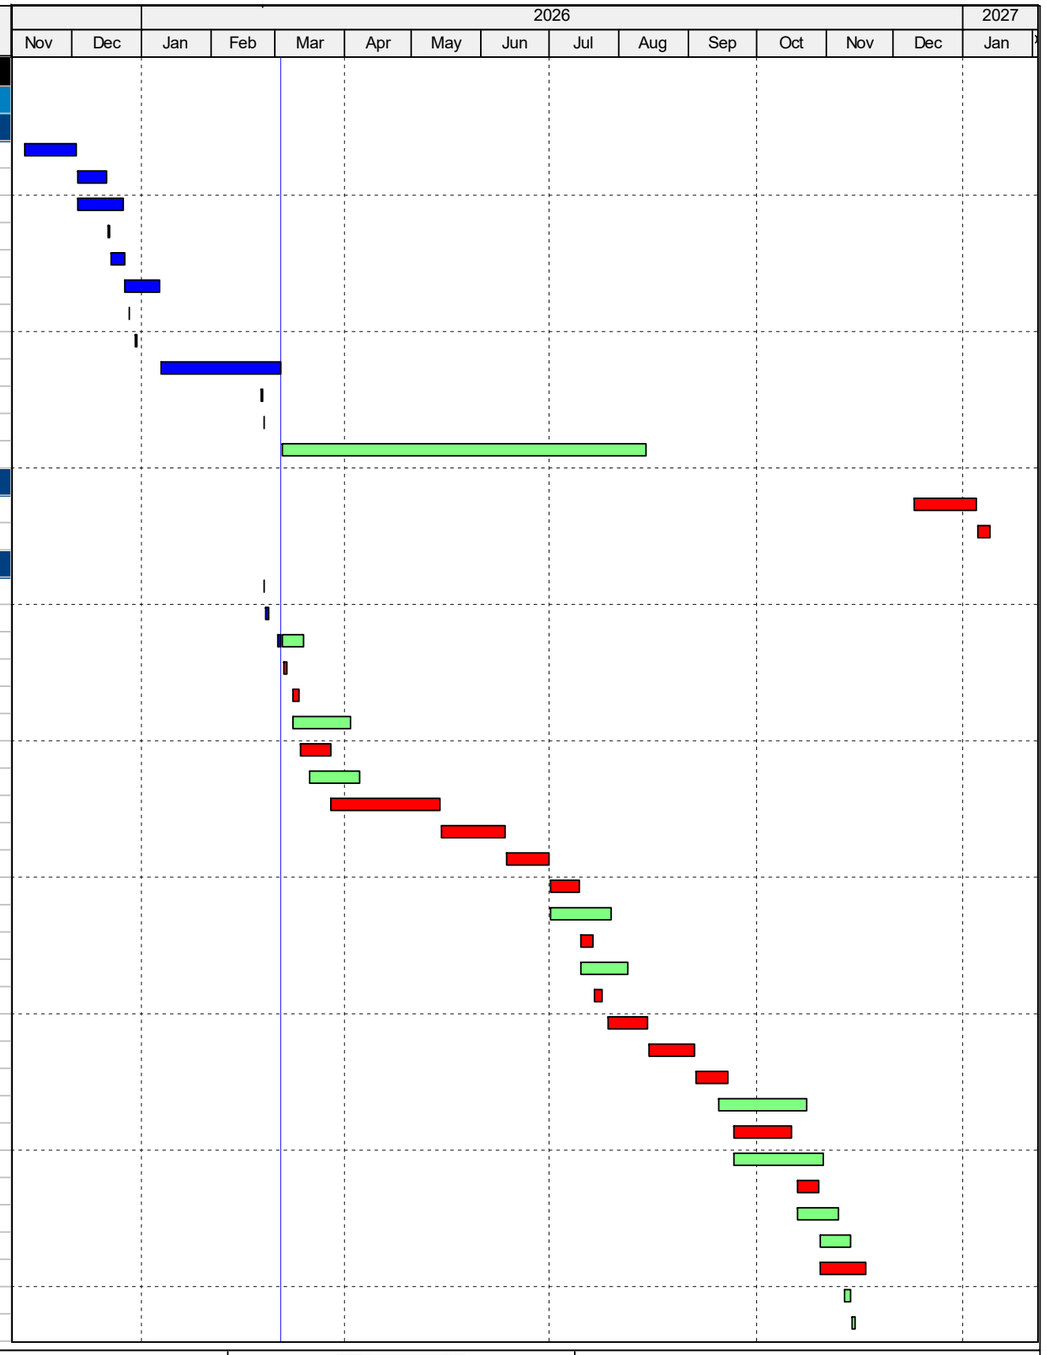

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

Turkish NTO Contract- VRH KC03042026
VRH - Baseline Comparison

Data Date: 04-Mar-26
Current Date: 04-Mar-26

Activity ID	Activity Name	Remaining Duration	Start	Finish
41	Install and Final Connect Food Service Equipment	10	12-Nov-26	25-Nov-26
46	Install Signage	3	16-Nov-26	18-Nov-26
47	Install FIDS/Video Walls	7	16-Nov-26	24-Nov-26
43	Install Security Equipment	2	19-Nov-26	20-Nov-26
48	Start up Equipment	2	23-Nov-26	24-Nov-26
49	Test FA and BMS	2	25-Nov-26	26-Nov-26
50	Substantial Completion	1	30-Nov-26	30-Nov-26
Final Completion & Handover		14	30-Nov-26	17-Dec-26
52	Prepare Punchlist	3	30-Nov-26	02-Dec-26
53	Final Cleaning- 1st Pass	2	01-Dec-26	02-Dec-26
54	Ready for Owner Loose FF&E	1	03-Dec-26	03-Dec-26
55	Resolve Punchlist	5	03-Dec-26	09-Dec-26
56	Final Inspections	2	10-Dec-26	11-Dec-26
58	Ready for Final PTO	1	14-Dec-26	14-Dec-26
59	Final Cleaning- 2nd Pass	2	14-Dec-26	15-Dec-26
57	Operational Readiness - Stock, Train, Open	4	14-Dec-26	17-Dec-26
60	Final Turnover	1	16-Dec-26	16-Dec-26

