
Korean Lounge Schedule


ID	Task Name	Duration	Start	Finish
1	**Overall Duration**	**345 days**	**Tue 2/4/25**	**Mon 6/1/26**
2	GC Award	1 day	Mon 2/10/25	Mon 2/10/25
3	90 Percent Drawing Issuance	1 day	Thu 2/27/25	Thu 2/27/25
4	GMP Pricing and Budget off 90 percent Set	20 days	Fri 2/28/25	Thu 3/27/25
5	Sub Early Procurement Package Pricing and Submission	15 days	Fri 2/28/25	Thu 3/20/25
6	Early Procurement Award Specific Trades (Millwork/HVAC/KE/Stone/Plumbing/Carpentry)	1 day	Mon 5/12/25	Mon 5/12/25
7	GMP Submission	1 day	Fri 3/28/25	Fri 3/28/25
8	GMP Drawing Budget and Review	5 days	Mon 3/31/25	Fri 4/4/25
9	GMP Approval	5 days	Mon 4/7/25	Fri 4/11/25
10	Final Sub Procurement	10 days	Mon 4/14/25	Fri 4/25/25
11	Prepare Preconstruction Docs inclusive of MBE/WBE Plan	5 days	Mon 4/28/25	Fri 5/2/25
12	Submission of Port Authority Precon Docs	1 day	Mon 5/5/25	Mon 5/5/25
13	Port Authority Approval of Preconstruction Docs	5 days	Tue 5/6/25	Mon 5/12/25
14	Port Authority Preconstruction Meeting	1 day	Tue 5/13/25	Tue 5/13/25
15	**Submittals / Shop Drawings, Fabrication and Lead-time**	**196 days**	**Fri 4/18/25**	**Fri 1/16/26**
16	**Steel**	**65 days**	**Fri 4/18/25**	**Thu 7/17/25**
17	Prepare Shop Drawings Submittals and engineering for S	15 days	Fri 4/18/25	Thu 5/8/25
18	Design Team Reviews Site Submittals	10 days	Fri 5/9/25	Thu 5/22/25
19	Field Measure as needed	5 days	Fri 5/23/25	Thu 5/29/25
20	Fabrication	40 days	Fri 5/23/25	Thu 7/17/25
21	**Carpentry**	**90 days**	**Mon 4/28/25**	**Fri 8/29/25**
22	Prepare product data and sample submittals	15 days	Mon 4/28/25	Fri 5/16/25
23	Design review and approval for samples and product da	10 days	Mon 5/19/25	Fri 5/30/25
24	Specialty Ceiling Shop Drawing	20 days	Mon 4/28/25	Fri 5/23/25
25	Specialty Ceiling Design review and Approval	10 days	Mon 5/26/25	Fri 6/6/25
26	Lead time for Specialty Ceilings	60 days	Mon 6/9/25	Fri 8/29/25
27	General Carpentry Submittal	10 days	Mon 4/28/25	Fri 5/9/25
28	Design Team Reviews Carpentry Submittals	10 days	Mon 5/19/25	Fri 5/30/25
29	Lead Time General Carpentry	10 days	Mon 6/2/25	Fri 6/13/25
30	**Millwork (Early Procurement)**	**155 days**	**Tue 5/27/25**	**Mon 12/29/25**
31	Control Sample Receipt	5 days	Tue 5/27/25	Mon 6/2/25
32	Stone Slab Selection	20 days	Tue 6/3/25	Mon 6/30/25
33	AOR Approval of stone selection and Purchase	10 days	Tue 7/1/25	Mon 7/14/25
34	Wood Walnut/OAK Product Data/Sample submission	10 days	Tue 6/3/25	Mon 6/16/25
35	Wood Walnut/OAK AOR Approval	10 days	Tue 6/17/25	Mon 6/30/25
36	Raw Material Lead Time for wood	60 days	Tue 7/1/25	Mon 9/22/25
37	Raw Material Stone Slab	60 days	Tue 7/15/25	Mon 10/6/25

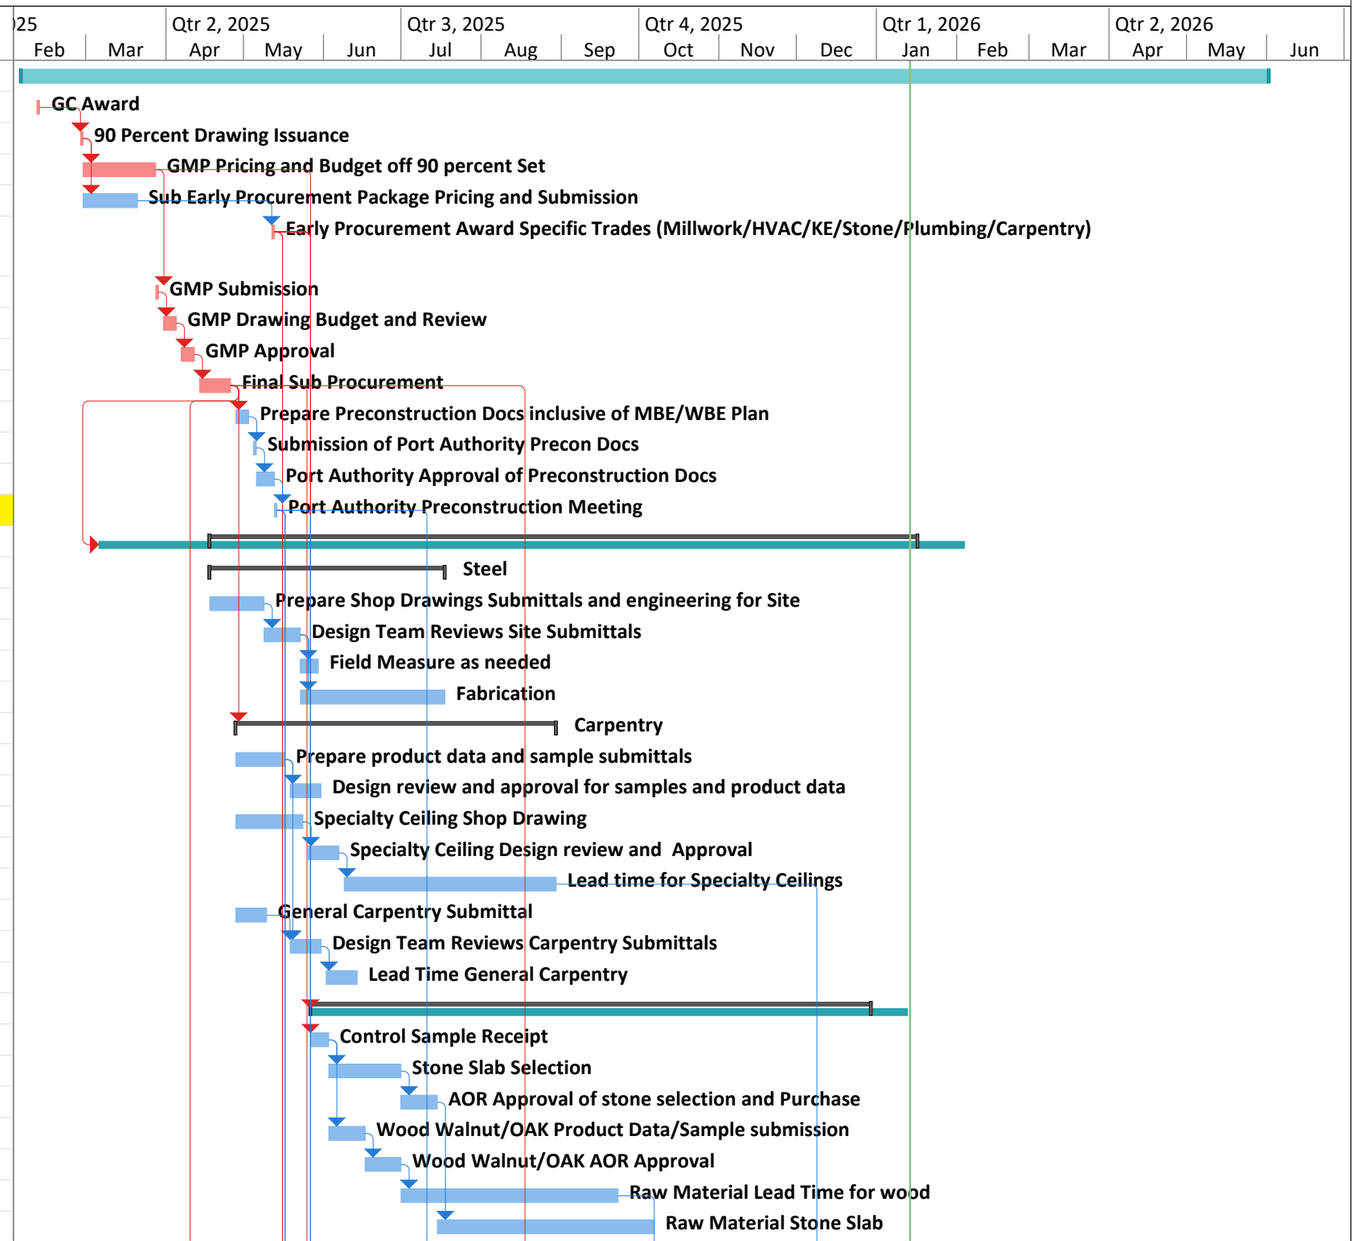

Task	External Tasks	Manual Task	Finish-only	Manual Progress
Split	External Milestone	Duration-only	Deadline
Milestone	Inactive Task	Manual Summary Rollup	Critical
Summary	Inactive Milestone	Manual Summary	Critical Split
Project Summary	Inactive Summary	Start-only	Progress

Korean Lounge Schedule


ID	Task Name	Duration	Start	Finish
38	Design Assist with Design Team to expedite shop approv	20 days	Tue 5/27/25	Mon 6/23/25
39	Formal Shop Drawing Submissions	20 days	Tue 6/24/25	Mon 7/21/25
40	Shop Drawing Approvals	10 days	Tue 7/22/25	Mon 8/4/25
41	Field Measure	25 days	Tue 8/5/25	Mon 9/8/25
42	Bar Die Fabrication	25 days	Tue 9/9/25	Mon 10/13/25
43	Millwork MEP/Trade Coordination	20 days	Tue 9/9/25	Mon 10/6/25
44	Fabrication Time for Millwork	70 days	Tue 10/7/25	Mon 1/12/26
45	**Glass and Glazing (Early Procurement)**	**181 days**	**Tue 5/27/25**	**Tue 2/3/26**
46	Control Sample receipt	5 days	Tue 5/27/25	Mon 6/2/25
47	Product Data and Sample submission MT-01/MT-02	20 days	Tue 6/3/25	Mon 6/30/25
48	Product Data and Sample submission for GL-01/GL02	20 days	Tue 6/3/25	Mon 6/30/25
49	Sample Approvals from AOR	10 days	Tue 7/1/25	Mon 7/14/25
50	Prepare Shop Drawings Submittals for Site	30 days	Tue 7/1/25	Mon 8/11/25
51	Design Team Reviews Site Submittals	10 days	Tue 9/2/25	Mon 9/15/25
52	Hold to dimensions provided based off of Millwork appr	20 days	Tue 8/5/25	Mon 9/1/25
53	lead-time	60 days	Tue 11/11/25	Mon 2/2/26
54	**Kitchen Equipment (Early Procurement)**	**121 days**	**Tue 5/27/25**	**Tue 11/11/25**
55	Submission of cutbook	20 days	Tue 5/27/25	Mon 6/23/25
56	Review of the cut book and approvals	10 days	Tue 6/24/25	Mon 7/7/25
57	Lead Time for Cooking equipment	90 days	Tue 7/8/25	Mon 11/10/25
58	Hood Submission	10 days	Tue 5/27/25	Mon 6/9/25
59	Design Team Review and Approvals	10 days	Tue 6/10/25	Mon 6/23/25
60	Lead Time for Hood	70 days	Tue 6/24/25	Mon 9/29/25
61	**Doors, Frames & Hardware**	**130 days**	**Tue 5/27/25**	**Mon 11/24/25**
62	Prepare Product data submittals	15 days	Tue 5/27/25	Mon 6/16/25
63	Prepare Shop Drawings Submittals for Site	15 days	Tue 6/17/25	Mon 7/7/25
64	Design Team Reviews Site Submittals	10 days	Tue 7/8/25	Mon 7/21/25
65	Review Site and Trade Coordination	15 days	Tue 7/22/25	Mon 8/11/25
66	Lead Time Frames	20 days	Tue 7/22/25	Mon 8/18/25
67	Lead-time Doors	75 days	Tue 8/12/25	Mon 11/24/25
68	**Painting and Wallcovering**	**111 days**	**Fri 4/18/25**	**Fri 9/19/25**
69	Control Sample Receipt	1 day	Fri 4/18/25	Fri 4/18/25
70	Prepare Product Data submittals and Samples (Wallcove	20 days	Mon 4/21/25	Fri 5/16/25
71	Prepare Product Data for special Paint (Ventian Plaster)	10 days	Mon 4/21/25	Fri 5/2/25
72	Prepare Shop Drawings Submittals for Site	20 days	Mon 5/19/25	Fri 6/13/25
73	Design Team Reviews Site Submittals	10 days	Mon 6/16/25	Fri 6/27/25
74	Review Site Condition and Trade Coordination MEP	5 days	Mon 6/30/25	Fri 7/4/25
75	Procure Site Materials Plaster	35 days	Mon 5/5/25	Fri 6/20/25

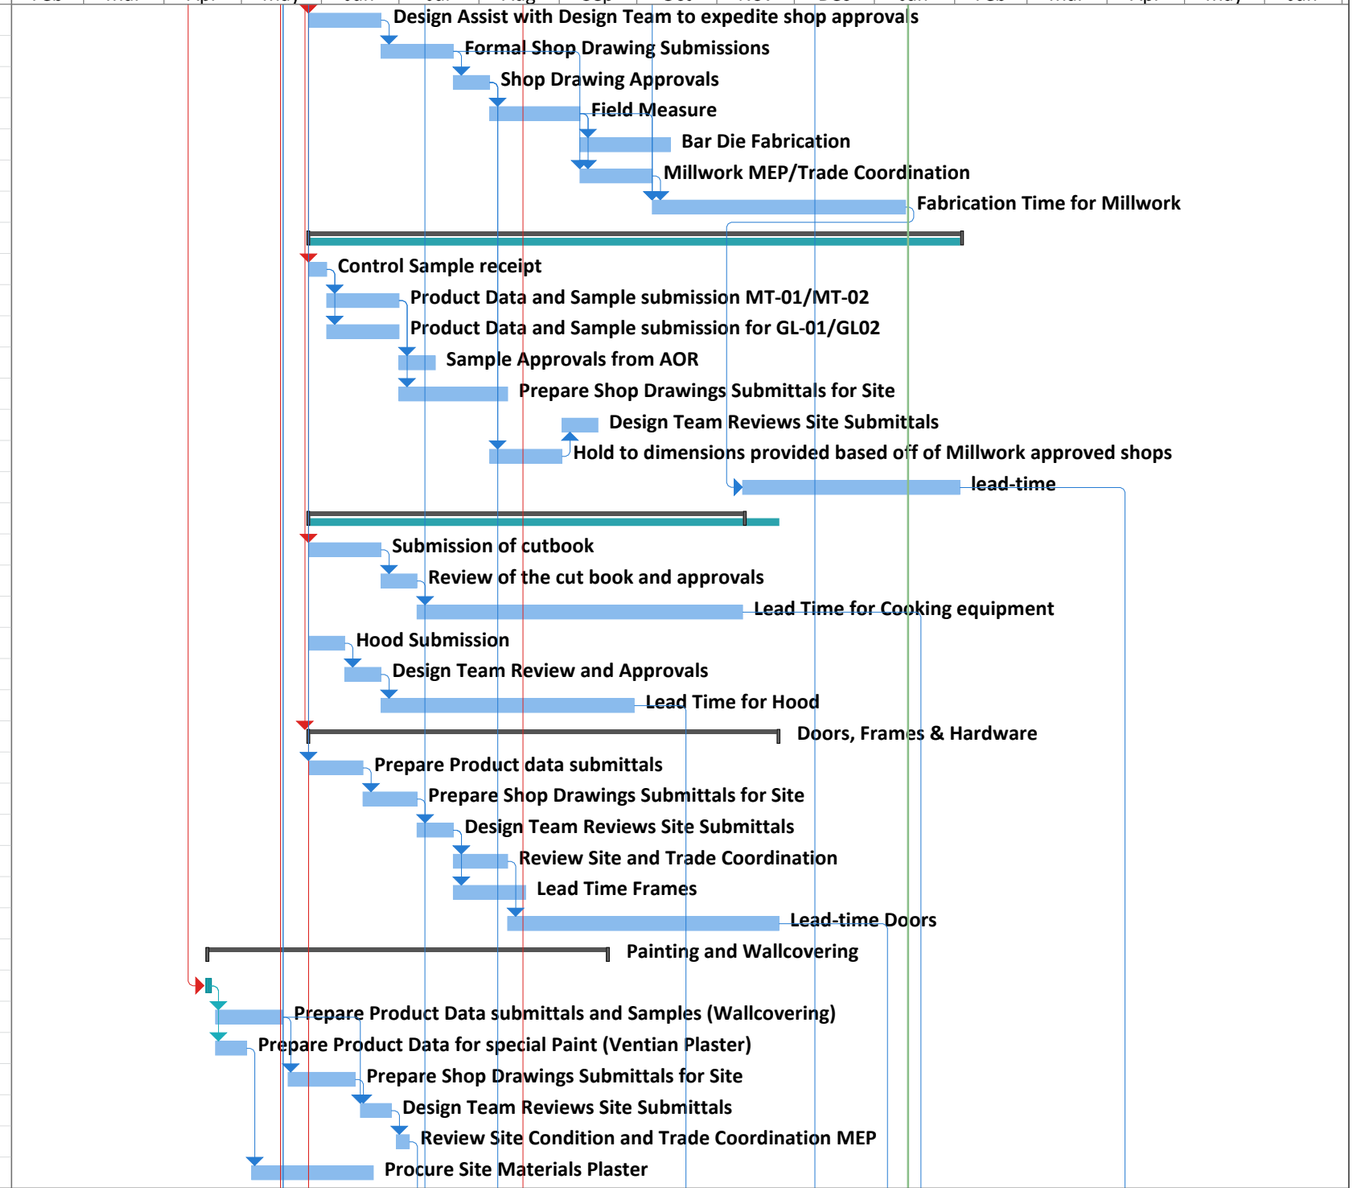

Task	External Tasks	Manual Task	Finish-only	Manual Progress
Split	External Milestone	Duration-only	Deadline	
Milestone	Inactive Task	Manual Summary Rollup	Critical	
Summary	Inactive Milestone	Manual Summary	Critical Split	
Project Summary	Inactive Summary	Start-only	Progress	

Korean Lounge Schedule

ID	Task Name	Duration	Start	Finish
76	Procure Site Materials Wallcovering	55 days	Mon 7/7/25	Fri 9/19/25
77	**Vinyl/Resilient Flooring**	**63 days**	**Fri 4/18/25**	**Tue 7/15/25**
78	Prepare and Submit Product Data/Samples	10 days	Mon 8/18/25	Fri 8/29/25
79	Design Team Reviews Site Submittals	10 days	Mon 9/1/25	Fri 9/12/25
80	Procure Site Materials	40 days	Mon 9/15/25	Fri 11/7/25
81	**Signage**	**120 days**	**Mon 8/18/25**	**Fri 1/30/26**
82	Prepare Product data submittals/samples	10 days	Mon 8/18/25	Fri 8/29/25
83	Prepare Shop Drawings Submittals for Site	25 days	Mon 9/1/25	Fri 10/3/25
84	Design Team Reviews Site Submittals	10 days	Mon 10/6/25	Fri 10/17/25
85	Coordinate associated MEP	15 days	Mon 10/20/25	Fri 11/7/25
86	Procure Site Materials	40 days	Mon 11/10/25	Fri 1/2/26
87	Fabrication	20 days	Mon 1/5/26	Fri 1/30/26
88	**Tile and Stone Flooring**	**124 days**	**Tue 3/25/25**	**Fri 9/12/25**
89	Control Sample Receipt	1 day	Tue 5/13/25	Tue 5/13/25
90	Prepare and Submit Product Data/Samples	15 days	Wed 5/14/25	Tue 6/3/25
91	Prepare Shop Drawings Submittals for Site	20 days	Wed 6/4/25	Tue 7/1/25
92	Design Team Reviews Site Submittals	40 days	Wed 7/2/25	Tue 8/26/25
93	Procure Site Materials	80 days	Wed 8/27/25	Tue 12/16/25
94	**Plumbing**	**95 days**	**Fri 4/18/25**	**Thu 8/28/25**
95	Prepare submittals for Plumbing fixtures	15 days	Fri 4/18/25	Thu 5/8/25
96	Prepare Shop Drawings Submittals for Site	25 days	Fri 5/9/25	Thu 6/12/25
97	Design Team Reviews Site Submittals	10 days	Fri 6/13/25	Thu 6/26/25
98	Procure Plumbing Equipment (Water heaters etc.)	45 days	Fri 6/27/25	Thu 8/28/25
99	Procure Site Materials	20 days	Fri 6/27/25	Thu 7/24/25
100	**HVAC (Early Procurement)**	**98 days**	**Tue 4/8/25**	**Thu 8/21/25**
101	Submission of FCU's	5 days	Tue 5/27/25	Mon 6/2/25
102	Submission of exhaust Fans	5 days	Tue 6/3/25	Mon 6/9/25
103	Early Sketching	3 days	Tue 5/27/25	Thu 5/29/25
104	Site Survey	10 days	Fri 5/30/25	Thu 6/12/25
105	Prepare Shop Drawings Submittals for Site	30 days	Fri 5/30/25	Thu 7/10/25
106	Design Team Reviews FCU	5 days	Tue 6/3/25	Mon 6/9/25
107	FCU Lead Time	35 days	Fri 7/11/25	Thu 8/28/25
108	Design Team Reviews Remaining Mechanical Equipment Submittals (Exhaust Fan/VAVS)	10 days	Tue 6/10/25	Mon 6/23/25
109	Exhaust Fan Lead Time	60 days	Tue 6/24/25	Mon 9/15/25
110	Above Ceiling Trade Coordination	10 days	Fri 7/11/25	Thu 7/24/25
111	Fabricate Ductwork	15 days	Fri 7/25/25	Thu 8/14/25
112	Procure Remaining Mechanical units	50 days	Tue 6/24/25	Mon 9/1/25

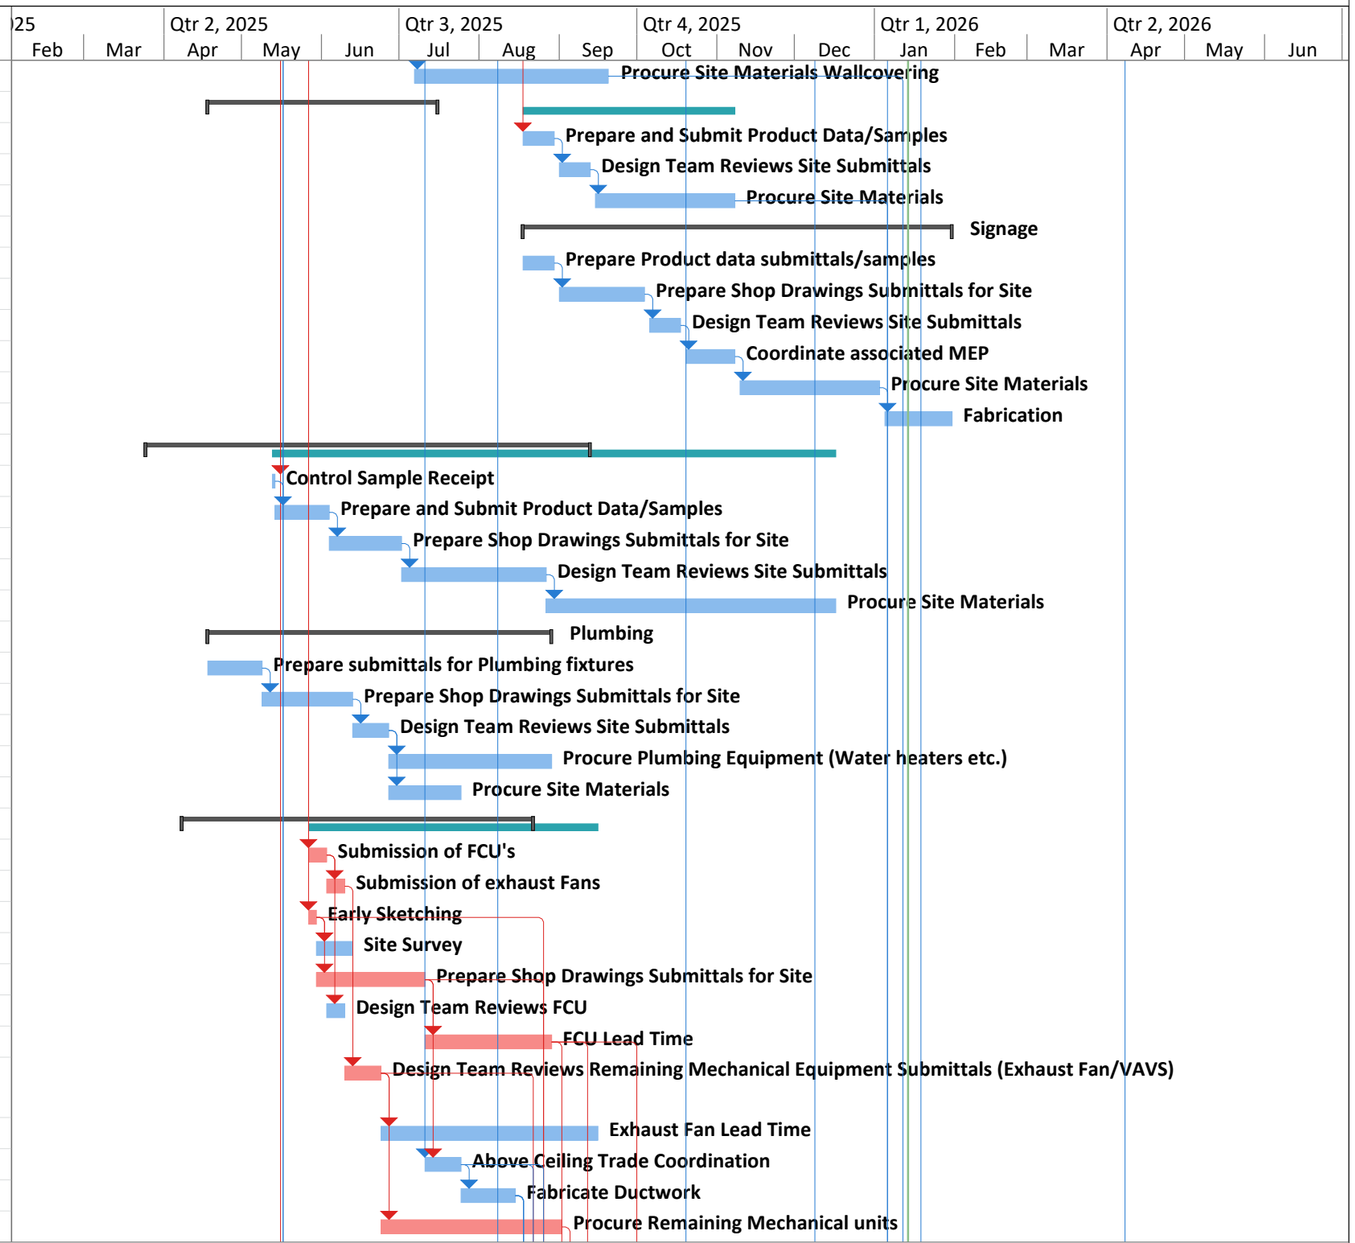

Task	External Tasks	Manual Task	Finish-only	Manual Progress
Split	External Milestone	Duration-only	Deadline
Milestone	Inactive Task	Manual Summary Rollup	Critical
Summary	Inactive Milestone	Manual Summary	Critical Split
Project Summary	Inactive Summary	Start-only	Progress

Korean Lounge Schedule


ID	Task Name	Duration	Start	Finish
113	**Fire Sprinkler**	**45 days**	**Wed 5/14/25**	**Tue 7/15/25**
114	Product Data Submittals	15 days	Wed 5/14/25	Tue 6/3/25
115	Above Ceiling Coordination for Shop Drawings	10 days	Wed 5/14/25	Tue 5/27/25
116	Prepare Shop Drawings Submittals for Site	10 days	Wed 6/11/25	Tue 6/24/25
117	Engineering and Calculations	10 days	Wed 5/28/25	Tue 6/10/25
118	Design Team Reviews Site Submittals	10 days	Wed 6/25/25	Tue 7/8/25
119	Procure Site Materials	5 days	Wed 7/9/25	Tue 7/15/25
120	**Electrical (Early Procurment)**	**131 days**	**Thu 3/6/25**	**Thu 9/4/25**
121	Product Data Submittals	10 days	Tue 5/13/25	Mon 5/26/25
122	Lighting Submittals	10 days	Tue 5/27/25	Mon 6/9/25
123	Prepare Shop Drawings Submittals for Site	20 days	Tue 6/10/25	Mon 7/7/25
124	Above Ceiling Coordination for Shop Drawings	10 days	Fri 8/22/25	Thu 9/4/25
125	Design Team Reviews Site Submittals for recessed lighti	10 days	Tue 6/10/25	Mon 6/23/25
126	Design Team Reviews Site Submittals	10 days	Tue 7/8/25	Mon 7/21/25
127	Recessed Lighting lead time	50 days	Tue 6/24/25	Mon 9/1/25
128	BOH Lighting Lead Times	30 days	Tue 7/22/25	Mon 9/1/25
129	Lead time- Lighting Coves	60 days	Tue 7/22/25	Mon 10/13/25
130	Millwork Lighting Lead time	70 days	Tue 8/5/25	Mon 11/10/25
131	**White Box Turnover**	**1 day**	**Mon 5/12/25**	**Mon 5/12/25**
132	Site Survey to review White Box turnover (Client acce	1 day	Mon 5/12/25	Mon 5/12/25
133	**Base Building Deliverables (NTO)**	**303 days**	**Fri 5/9/25**	**Tue 7/7/26**
134	Humidity Control and Dry In	2 days	Fri 8/15/25	Mon 8/18/25
135	Base Building HVAC Completion and testing	1 day	Mon 6/9/25	Mon 6/9/25
136	Base Building Fire Alarm and testing	1 day	Thu 2/26/26	Thu 2/26/26
137	Hoist in place and ready for usage on East Pier	1 day	Fri 5/9/25	Fri 5/9/25
138	Permanent Power	1 day	Fri 8/15/25	Fri 8/15/25
139	**Construction**	**232 days**	**Mon 5/12/25**	**Tue 3/31/26**
140	Mobilization	1 day	Mon 6/2/25	Mon 6/2/25
141	Install of Roof Top equipment	3 days	Mon 10/27/25	Wed 10/29/25
142	**Kitchen/BOH Storage**	**216 days**	**Fri 5/16/25**	**Fri 3/13/26**
143	Layout	5 days	Tue 6/3/25	Mon 6/9/25
144	Layout confirmation and approval by AOR	2 days	Tue 6/10/25	Wed 6/11/25
145	Scanning for Penetrations	5 days	Thu 6/12/25	Wed 6/18/25
146	Core Penetrations	15 days	Thu 6/19/25	Wed 7/9/25
147	Install Duct Trunk lines	7 days	Fri 8/15/25	Mon 8/25/25
148	Install Wall Framing	30 days	Thu 6/12/25	Wed 7/23/25
149	Underslab Plumbing and install of floor sinks and floo	20 days	Thu 7/10/25	Wed 8/6/25
150	Plumbing Rough In Walls	28 days	Wed 7/30/25	Fri 9/5/25



Task	External Tasks	Manual Task	Finish-only	Manual Progress
Split	External Milestone	Duration-only	Deadline
Milestone	Inactive Task	Manual Summary Rollup	Critical
Summary	Inactive Milestone	Manual Summary	Critical Split
Project Summary	Inactive Summary	Start-only	Progress

Korean Lounge Schedule


ID	Task Name	Duration	Start	Finish
151	Electrical Work Below Floor	16 days	Thu 6/19/25	Thu 7/10/25
152	Install Duct Distribution	18 days	Tue 8/26/25	Thu 9/18/25
153	Install controls on associated HVAC and coordination	5 days	Fri 9/12/25	Thu 9/18/25
154	Electrical Rough in Walls	30 days	Thu 7/24/25	Wed 9/3/25
155	Fire Alarm Rough In	9 days	Thu 7/24/25	Tue 8/5/25
156	One Side Sheetrock	10 days	Thu 9/4/25	Wed 9/17/25
157	PANYNJ In Wall Inspection	3 days	Mon 9/8/25	Wed 9/10/25
158	GWB Walls	6 days	Thu 9/18/25	Thu 9/25/25
159	Tape Spackle	8 days	Fri 9/26/25	Tue 10/7/25
160	Install FRP	8 days	Wed 10/8/25	Fri 10/17/25
161	Install Exhaust Hood	5 days	Mon 10/20/25	Fri 10/24/25
162	Install Sprinkler Rough	8 days	Fri 9/19/25	Tue 9/30/25
163	Install of Mechanical Units (FCU)	19 days	Wed 10/1/25	Mon 10/27/25
164	Above Ceiling Electrical rough	25 days	Fri 9/19/25	Thu 10/23/25
165	Install HVAC Connections to FCU Units	4 days	Tue 10/28/25	Fri 10/31/25
166	Installation of controls to FCU's	8 days	Mon 11/3/25	Wed 11/12/25
167	Install Ceiling Supports	6 days	Tue 10/28/25	Tue 11/4/25
168	Installation of Ceiling Grid	7 days	Thu 11/13/25	Fri 11/21/25
169	Installation of Diffusers	8 days	Mon 11/24/25	Wed 12/3/25
170	Install Lighting	21 days	Mon 11/24/25	Mon 12/22/25
171	Above Ceiling Inspection	3 days	Tue 12/23/25	Thu 12/25/25
172	Above Ceiling Punch List	5 days	Fri 12/26/25	Thu 1/1/26
173	Floor Prep	2 days	Fri 1/2/26	Mon 1/5/26
174	Install Doors and Hardware	3 days	Tue 1/6/26	Thu 1/8/26
175	Installation of BOH Flooring	4 days	Tue 1/6/26	Fri 1/9/26
176	Painting	5 days	Mon 1/12/26	Fri 1/16/26
177	Install Kitchen Equipment	13 days	Mon 1/19/26	Wed 2/4/26
178	Kitchen Equipment MEP Connections	14 days	Thu 2/5/26	Tue 2/24/26
179	Kitchen Equipment BMS Integrations	15 days	Wed 2/25/26	Tue 3/17/26
180	Equipment Start Up and Testing	10 days	Wed 3/18/26	Tue 3/31/26
181	**Bathrooms**	**198 days**	**Mon 6/9/25**	**Wed 3/11/26**
182	Layout	5 days	Mon 6/9/25	Fri 6/13/25
183	AOR Layout Approval	2 days	Mon 6/9/25	Tue 6/10/25
184	Underslab Plumbing	20 days	Mon 7/7/25	Fri 8/1/25
185	Wall Framing	20 days	Thu 6/19/25	Wed 7/16/25
186	Install Duct Trunk Lines	10 days	Fri 8/15/25	Thu 8/28/25
187	Core Layout and scanning	5 days	Mon 6/16/25	Fri 6/20/25
188	Coring Plumbing Penetrations	5 days	Mon 6/23/25	Fri 6/27/25

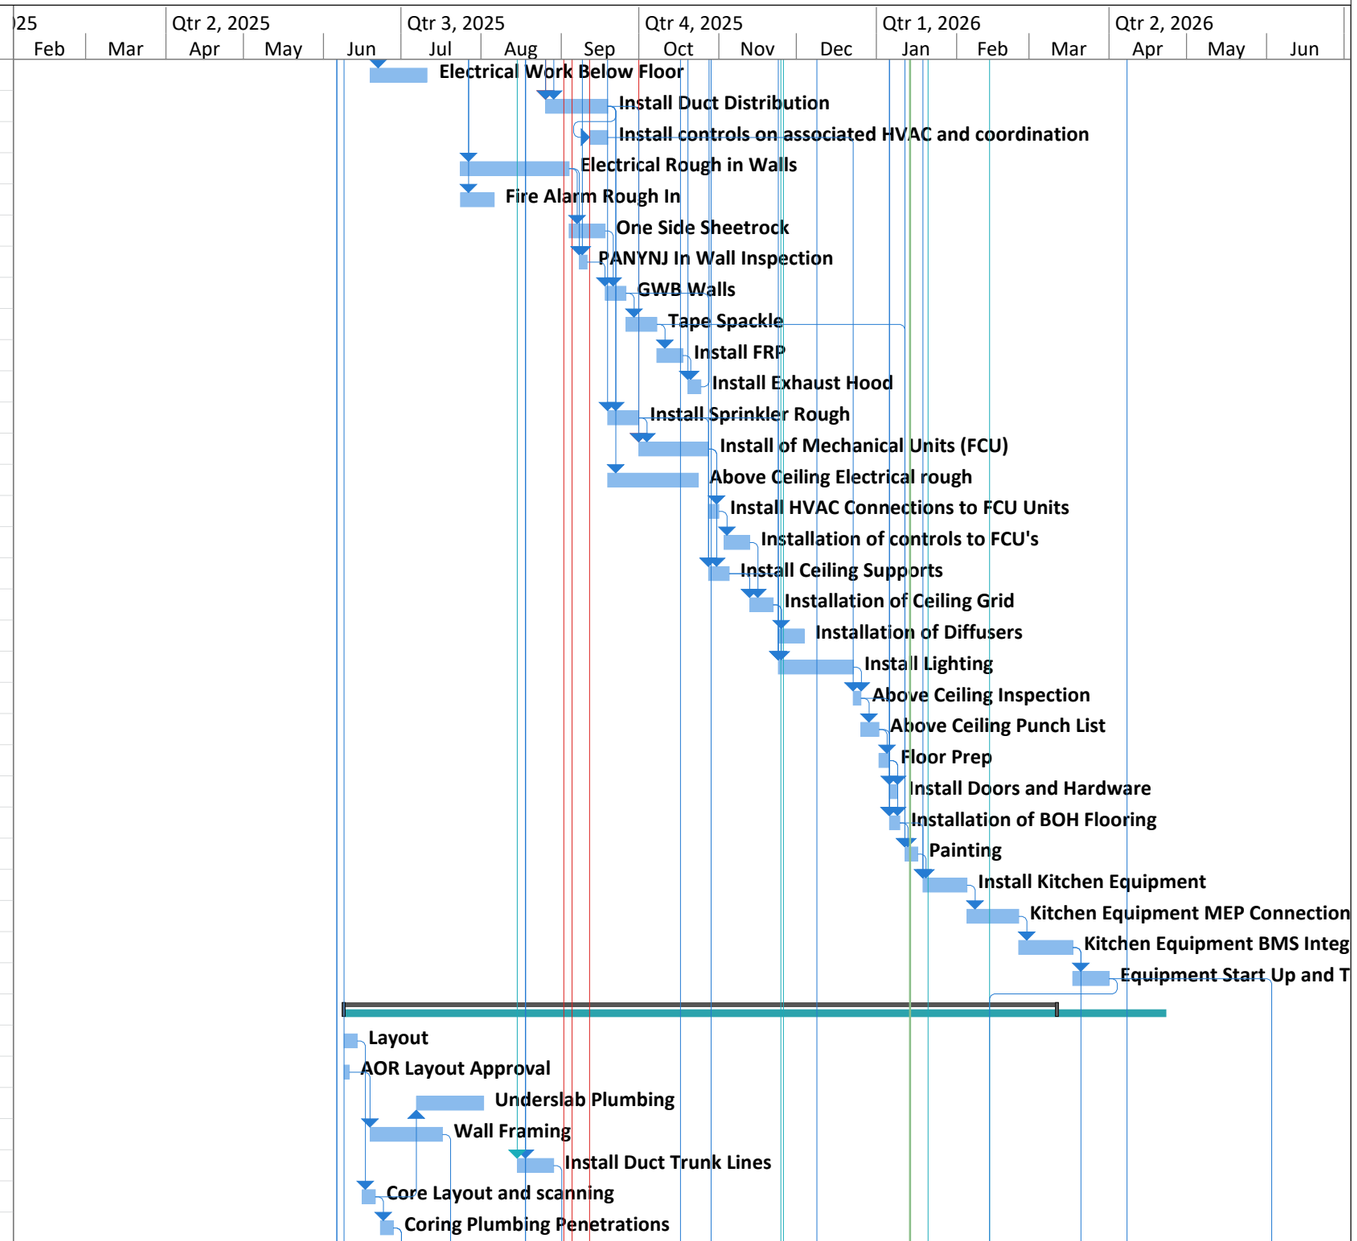

Task	External Tasks	Manual Task	Finish-only	Manual Progress
Split	External Milestone	Duration-only	Deadline
Milestone	Inactive Task	Manual Summary Rollup	Critical
Summary	Inactive Milestone	Manual Summary	Critical Split
Project Summary	Inactive Summary	Start-only	Progress

Korean Lounge Schedule


ID	Task Name	Duration	Start	Finish
189	Plumbing Stub Ups	20 days	Mon 6/30/25	Fri 7/25/25
190	Horizontal Plumbing Piping	20 days	Mon 6/30/25	Fri 7/25/25
191	Electrical In Wall Rough In	18 days	Thu 7/17/25	Mon 8/11/25
192	Fire Alarm Rough In	5 days	Tue 8/12/25	Mon 8/18/25
193	PANYNJ In Wall Inspection	5 days	Tue 8/19/25	Mon 8/25/25
194	GWB Walls	5 days	Tue 8/26/25	Mon 9/1/25
195	Above Ceiling Electrical Rough In	15 days	Fri 9/5/25	Thu 9/25/25
196	Above Ceiling Plumbing Rough	14 days	Mon 7/28/25	Thu 8/14/25
197	Above Ceiling Sprinkler Rough In	13 days	Fri 9/26/25	Tue 10/14/25
198	HVAC Branch Line Install	5 days	Fri 8/29/25	Thu 9/4/25
199	Ceiling Framing	10 days	Wed 10/15/25	Tue 10/28/25
200	Recessed Lighting Install	7 days	Wed 10/29/25	Thu 11/6/25
201	Drop Sprinkler Heads	6 days	Fri 11/7/25	Fri 11/14/25
202	Diffuser Install	4 days	Mon 11/17/25	Thu 11/20/25
203	Above Ceiling Inspection	3 days	Fri 11/21/25	Tue 11/25/25
204	Sheetrock Bathroom Ceilings	7 days	Wed 11/26/25	Thu 12/4/25
205	Cove Light Install	10 days	Fri 12/5/25	Thu 12/18/25
206	Mud Bathroom Floors	6 days	Fri 12/19/25	Fri 12/26/25
207	Flood Test	3 days	Mon 12/29/25	Wed 12/31/25
208	Floor Tile Install	18 days	Thu 1/1/26	Mon 1/26/26
209	Wall Tile Install	16 days	Tue 1/27/26	Tue 2/17/26
210	Stone Wall Install	10 days	Wed 2/18/26	Tue 3/3/26
211	Install of Bathroom Millwork Vanities	10 days	Wed 3/4/26	Tue 3/17/26
212	Install Of stone Tops at bathroom vanties	3 days	Wed 3/18/26	Fri 3/20/26
213	Plumbing Fixture Install	8 days	Wed 3/4/26	Fri 3/13/26
214	Electrical Finishes (including millwork lighting install)	8 days	Wed 3/4/26	Fri 3/13/26
215	Toilet Accessory Install	5 days	Mon 3/16/26	Fri 3/20/26
216	Plumbing Finishes at vanity	6 days	Wed 3/18/26	Wed 3/25/26
217	Metal and Glass install	10 days	Thu 3/26/26	Wed 4/8/26
218	Door and Hardware Install	5 days	Thu 4/9/26	Wed 4/15/26
219	Painting	5 days	Thu 4/16/26	Wed 4/22/26
220	**First Class Lounge**	**225 days**	**Mon 6/16/25**	**Fri 4/24/26**
221	Layout	3 days	Tue 6/3/25	Thu 6/5/25
222	AOR Approval of Layout	5 days	Fri 6/6/25	Thu 6/12/25
223	Wall Framing	20 days	Mon 6/23/25	Fri 7/18/25
224	Electrical In Wall Rough In	20 days	Mon 7/21/25	Fri 8/15/25
225	Fire Alarm In Wall Rough In	6 days	Mon 7/21/25	Mon 7/28/25
226	In Wall Inspection	5 days	Mon 8/18/25	Fri 8/22/25

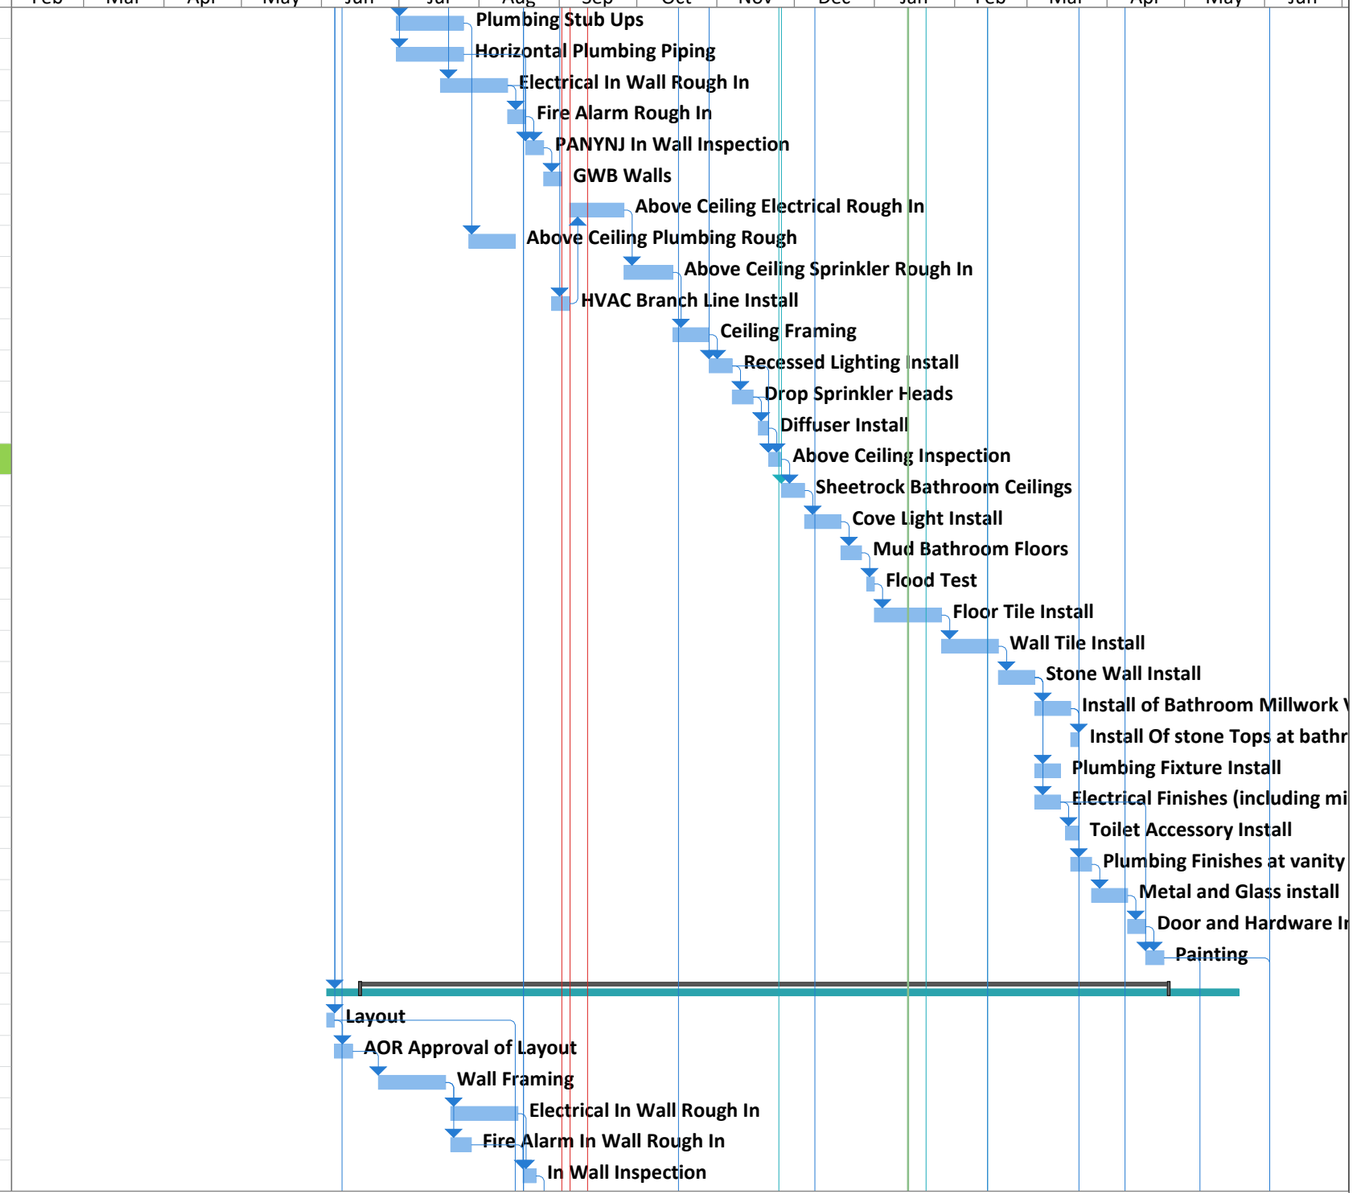

Task	External Tasks	Manual Task	Finish-only	Manual Progress
Split	External Milestone	Duration-only	Deadline	
Milestone	Inactive Task	Manual Summary Rollup	Critical	
Summary	Inactive Milestone	Manual Summary	Critical Split	
Project Summary	Inactive Summary	Start-only	Progress	

Korean Lounge Schedule


ID	Task Name	Duration	Start	Finish
227	Sheetrock Walls	7 days	Mon 8/25/25	Tue 9/2/25
228	HVAC Above Ceiling Install	20 days	Fri 8/15/25	Thu 9/11/25
229	Electrical Above Ceiling Rough In	17 days	Fri 9/12/25	Mon 10/6/25
230	Fire Alarm Above Ceiling rough in	12 days	Fri 9/12/25	Mon 9/29/25
231	Sprinkler Above Ceiling Rough In	9 days	Fri 9/12/25	Wed 9/24/25
232	FCU Install	11 days	Fri 9/12/25	Fri 9/26/25
233	Ceiling Framing (Including Light Pockets)	15 days	Mon 9/29/25	Fri 10/17/25
234	Reccessed Lighting Install	13 days	Mon 10/20/25	Wed 11/5/25
235	Sprinkler Head Drops	8 days	Thu 11/6/25	Mon 11/17/25
236	Above Ceiling Inspection	5 days	Tue 11/18/25	Mon 11/24/25
237	Sheetrock Ceiling Install	10 days	Tue 11/25/25	Mon 12/8/25
238	Prep for Paint	14 days	Tue 12/9/25	Fri 12/26/25
239	Paint includes Paint Plaster	7 days	Mon 12/29/25	Tue 1/6/26
240	Light Cove Install	17 days	Wed 1/7/26	Thu 1/29/26
241	Self Level for flooring Install	2 days	Fri 1/30/26	Mon 2/2/26
242	Stone Flooring Install	15 days	Tue 2/3/26	Mon 2/23/26
243	Wood Panel Install	15 days	Fri 2/13/26	Thu 3/5/26
244	Carpet Install	6 days	Tue 3/24/26	Tue 3/31/26
245	Millwork Install (Cabinets)	12 days	Fri 3/6/26	Mon 3/23/26
246	Stone Final Fabrication and Cuts for panels and insert	3 days	Tue 3/24/26	Thu 3/26/26
247	Stone Install	6 days	Fri 3/27/26	Fri 4/3/26
248	Glass and Metal final Measurements	3 days	Fri 3/27/26	Tue 3/31/26
249	Final Fabrication for Metal Base and Trim	10 days	Wed 4/1/26	Tue 4/14/26
250	Metal Install	15 days	Wed 4/15/26	Tue 5/5/26
251	Glass Install	9 days	Wed 5/6/26	Mon 5/18/26
252	Upholstery and banquette Install	8 days	Tue 5/12/26	Thu 5/21/26
253	**Miller-Prestige Lounge**	**240 days**	**Mon 6/9/25**	**Fri 5/8/26**
254	Layout	5 days	Mon 6/9/25	Fri 6/13/25
255	Soffit Framing	15 days	Mon 6/16/25	Fri 7/4/25
256	Ceiling Layout coordination	5 days	Mon 6/9/25	Fri 6/13/25
257	HVAC Above Ceiling Rough In	17 days	Fri 8/15/25	Mon 9/8/25
258	Electrical Above Ceiling Rough In	16 days	Fri 9/5/25	Fri 9/26/25
259	Fire Alarm Rough In	35 days	Tue 9/9/25	Mon 10/27/25
260	Sprinkler Rough In Above Ceiling	12 days	Tue 9/9/25	Wed 9/24/25
261	Wall Framing	15 days	Mon 6/16/25	Fri 7/4/25
262	In Wall Rough In	13 days	Mon 7/7/25	Wed 7/23/25
263	In Wall Inspection	4 days	Thu 7/24/25	Tue 7/29/25
264	Durock Install Following In Wall Inspection	7 days	Wed 7/30/25	Thu 8/7/25

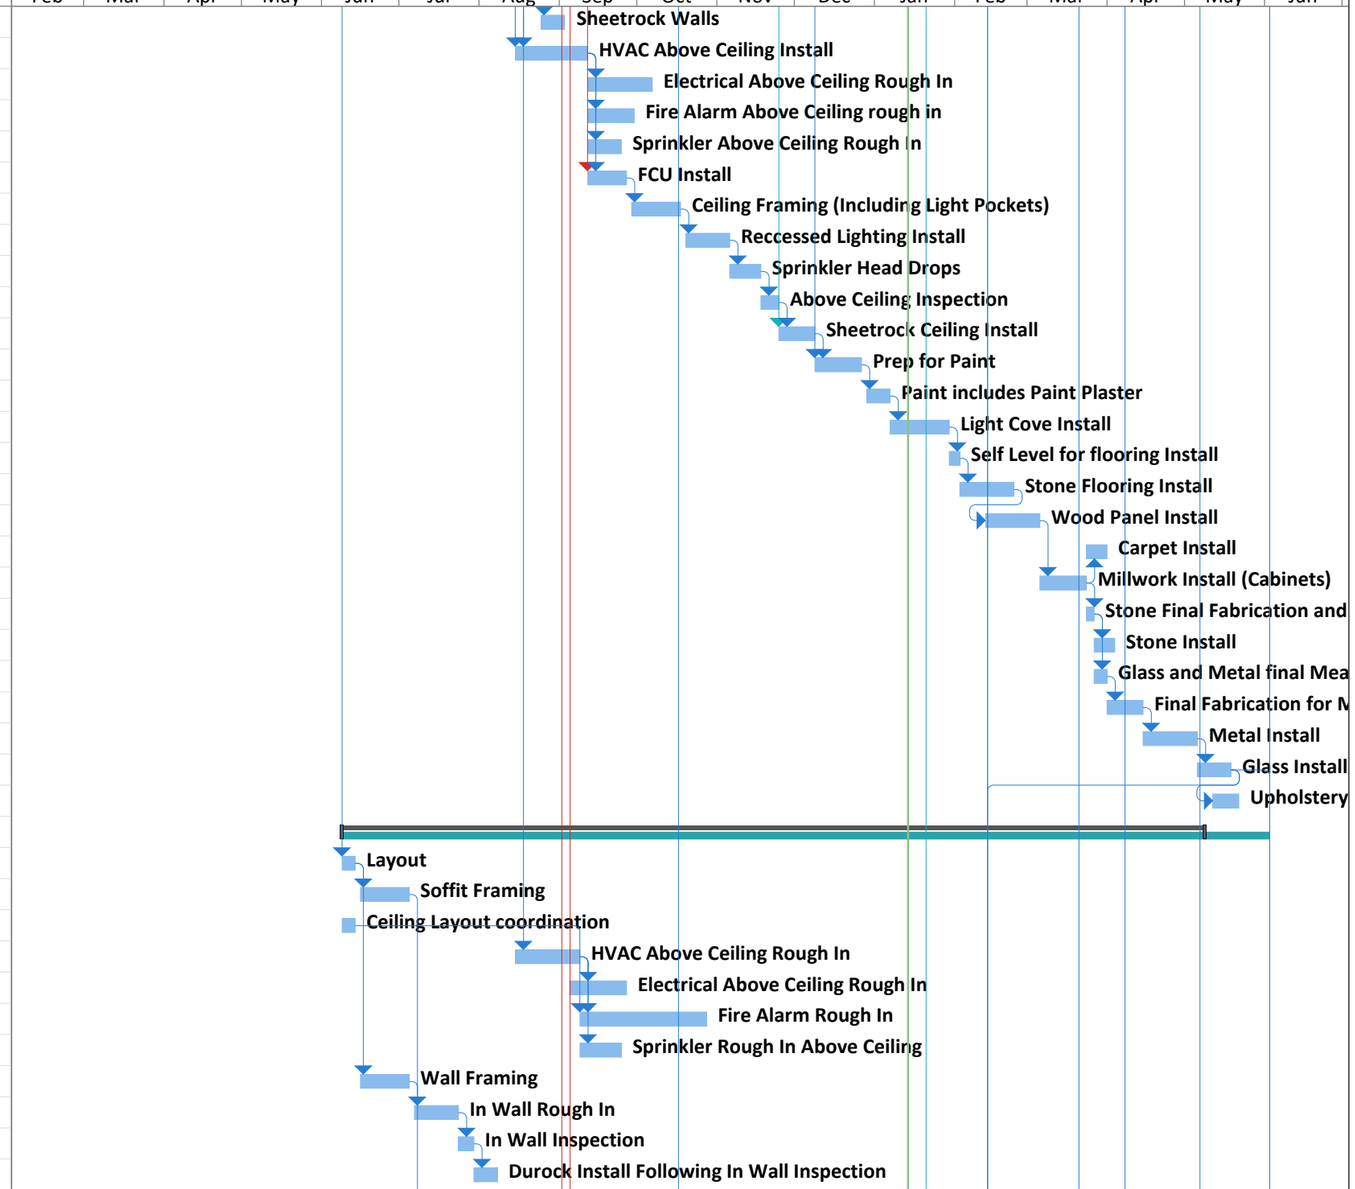

Task	External Tasks	Manual Task	Finish-only		Manual Progress
Split	External Milestone	Duration-only	Deadline		
Milestone	Inactive Task	Manual Summary Rollup	Critical		
Summary	Inactive Milestone	Manual Summary	Critical Split		
Project Summary	Inactive Summary	Start-only	Progress		

Korean Lounge Schedule

ID	Task Name	Duration	Start	Finish
265	Lighting Rough In for Cove Lights at perimeter	10 days	Mon 7/7/25	Fri 7/18/25
266	Light Cove Install	15 days	Tue 10/14/25	Mon 11/3/25
267	Installation of FCUs and VAVs	20 days	Tue 9/2/25	Mon 9/29/25
268	Electrical Connections to FCU/VAVs	15 days	Tue 9/30/25	Mon 10/20/25
269	Mechanical Piping Installation to Mechanical Units	15 days	Tue 9/30/25	Mon 10/20/25
270	Ceiling Framing	35 days	Tue 10/21/25	Mon 12/8/25
271	Recessed Lighting Install	20 days	Tue 12/9/25	Mon 1/5/26
272	Sprinkler Head Drops and Finishes	10 days	Tue 12/30/25	Mon 1/12/26
273	Diffuser Install	3 days	Tue 12/9/25	Thu 12/11/25
274	Above Ceiling Inspection	6 days	Tue 1/13/26	Tue 1/20/26
275	Ceiling Closure sheetrock	20 days	Wed 1/21/26	Tue 2/17/26
276	Stone Flooring Install and Msc Self Level	22 days	Wed 2/18/26	Thu 3/19/26
277	Millwork Install (Including screens)	15 days	Fri 3/6/26	Thu 3/26/26
278	Millwork Wall Panel Install	14 days	Thu 3/19/26	Tue 4/7/26
279	Metal and Glass Install	16 days	Wed 4/8/26	Wed 4/29/26
280	Stone Fabrication and Install for panels and Trims	11 days	Thu 4/30/26	Thu 5/14/26
281	Base Install	7 days	Fri 5/15/26	Mon 5/25/26
282	Upholstery Banquette Install behind finishes	6 days	Tue 5/26/26	Tue 6/2/26
283	Wallcovering Install and Painting	3 days	Tue 5/26/26	Thu 5/28/26
284	Inspections/General Lounge FFE	76 days	Mon 2/16/26	Mon 6/1/26
285	Deliver And Install Furniture	5 days	Wed 6/3/26	Tue 6/9/26
286	Fire Alarm Tie In	1 day	Fri 2/20/26	Fri 2/20/26
287	Fire Alarm Test	3 days	Wed 3/18/26	Fri 3/20/26
288	OSD Health Inspection	2 days	Thu 5/7/26	Fri 5/8/26
289	PANYNJ Final Inspections (Life Safety QAD comments resolved from partial inspections)	3 days	Wed 6/10/26	Fri 6/12/26
290	Punchlist	15 days	Tue 5/26/26	Mon 6/15/26
291	Certification	1 day	Tue 6/16/26	Tue 6/16/26
292	Training/Commissioning	15 days	Tue 6/16/26	Mon 7/6/26
293	Opening	1 day	Tue 7/7/26	Tue 7/7/26

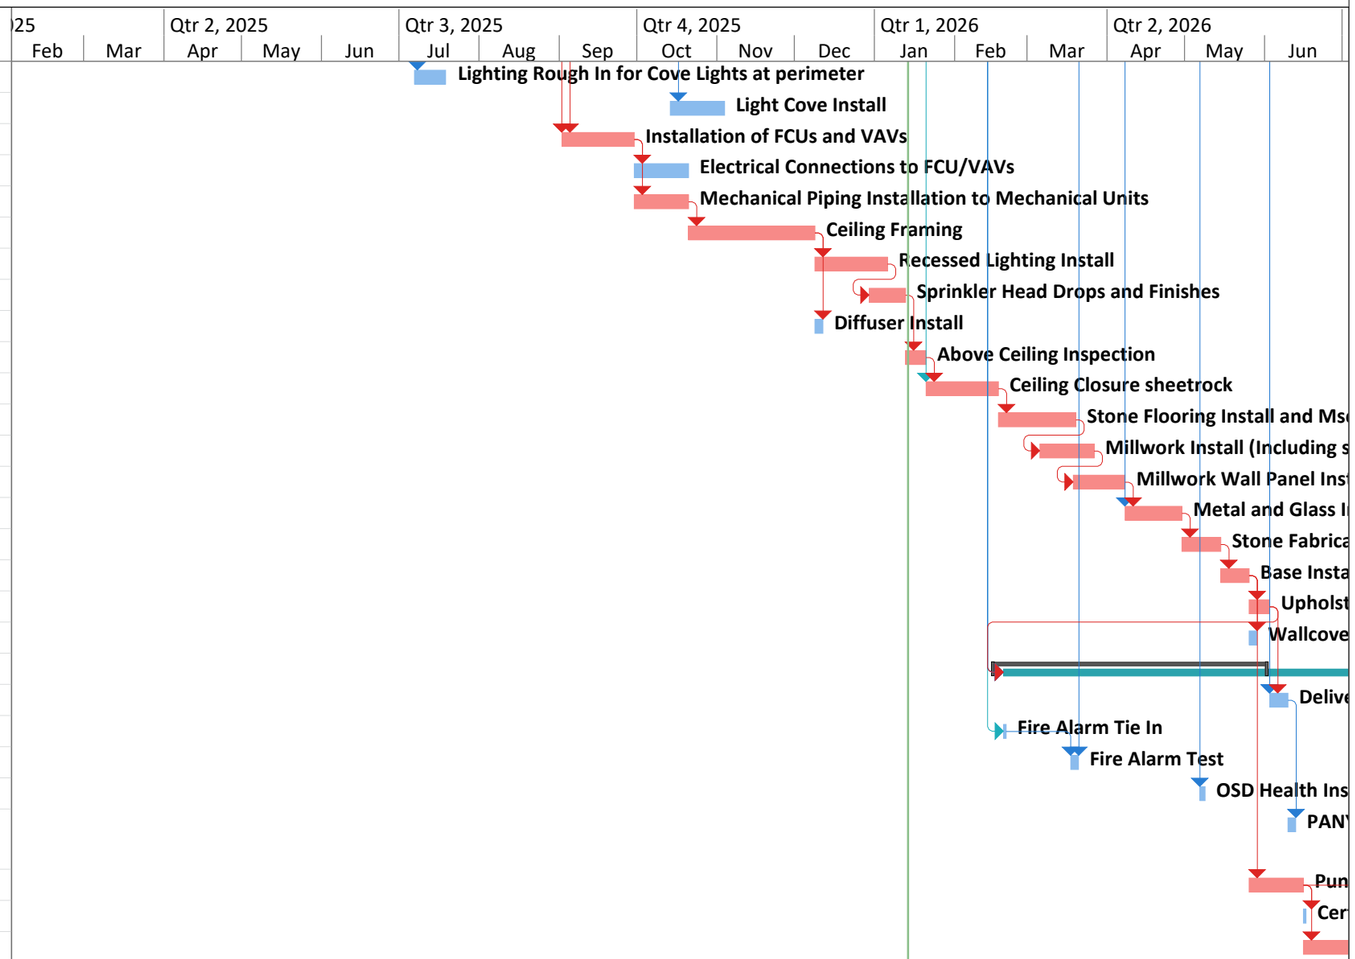

Task	External Tasks	Manual Task	Finish-only	Manual Progress
Split	External Milestone	Duration-only	Deadline	
Milestone	Inactive Task	Manual Summary Rollup	Critical	
Summary	Inactive Milestone	Manual Summary	Critical Split	
Project Summary	Inactive Summary	Start-only	Progress	

171 Above Ceiling Inspection

PANYNJ Inspections to occur within 3 day notice period

211 Install of Bathroom Millwork Vanities

PANYNJ Inspections to occur within 3 day notice period
