
Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
Eastern Parkway Library-Renovation and Expansion		579	01-Aug-25	20-Oct-27	0
ML1020	Project Duration to Final Completion	811	01-Aug-25	20-Oct-27	0
CONTRACTUAL & NON CONTRACTUAL MILESTONES		579	01-Aug-25	20-Oct-27	0
CONTRACTUAL MILESTONES		811	01-Aug-25	20-Oct-27	0
ML1000	Notice to Proceed	0		01-Aug-25	0
ML3005	Personnel Vacant Existing Library (45 CCD)	1	01-Aug-25	01-Aug-25	95
ML3010	Personnel Vacant Existing Library Milestone	0		01-Aug-25	95
ML2000	Substantial Completion	0		22-Jul-27*	0
ML3000	Final Completion Certificate of Occupancy	0		20-Oct-27	0
NON CONTRACTUAL SOFT MILESTONES		454	22-Oct-25	20-Jul-27	2
ML3065	Concrete Shop Drawings Approval Milestone	0		22-Oct-25	146
ML3095	Rebar Shop Drawings Approval Milestone	0		22-Oct-25	117
ML1010	Start Asbestos Abatement	0	27-Oct-25		51
ML3055	Start Construction	0	02-Dec-25		60
ML3115	Building Disconnects Completion Milestone	0		02-Dec-25	14
ML3295	Glazing Approval Milestone	0		08-Jan-26	144
ML3085	Curtainwall Shop Drawings Approval Milestone	0		13-Jan-26	141
ML3075	Steel Shop Drawings Approval Milestone	0		14-Jan-26	84
ML3035	Start Demolition	0	16-Jan-26		47
ML3385	Auger Pile Approval Milestone	0		26-Jan-26	52
ML3105	SOE Shop Drawings & Calculations Submission Milestone	0		02-Feb-26	17
ML3285	Aluminium Entrance & Storefront Approval Milestone	0		02-Feb-26	123
ML3335	HVAC Equipment Approval Milestone	0		18-Feb-26	84
ML3365	Fire Alarm Approval Milestone	0		18-Feb-26	347
ML3315	Sprinkler Approval Milestone	0		25-Feb-26	196
ML3325	Plumbing Approval Milestone	0		25-Feb-26	88
ML3375	Support of Excavation Approval Milestone	0		25-Feb-26	17
ML3125	Demolition of Ex'g. Building Completion Milestone	0		03-Mar-26	0
ML3045	Start Construction Excavation	0	04-Mar-26		78
ML3255	Hollow Metal Doors Approval Milestone	0		26-Mar-26	194
ML3275	Hardware Approval Milestone	0		26-Mar-26	194
ML3305	Passenger Elevator Approval Milestone	0		26-Mar-26	115
ML3355	Electrical Approval Milestone	0		26-Mar-26	283
ML3265	Architectual Woodwork Approval Milestone	0		14-Apr-26	235
ML3345	HVAC Duct Approval Milestone	0		02-Jun-26	127
ML3135	Superstructure Completion Milestone	0		09-Nov-26	10
ML3145	Exterior Enclosure Completion Milestone	0		02-Feb-27	0
ML3155	Roofing Completion Milestone	0		02-Feb-27	0
ML3400	Watertight Completion Milestone	0		02-Feb-27	0
ML3195	Power Completion Milestone	0		16-Mar-27	87
ML3235	Equipment Start-up Completion Milestone	0		23-Mar-27	59



Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
ML3175	Interior 1st Floor Completion Milestone	0		13-Apr-27	68
ML3215	Interior Cellar Completion Milestone	0		13-Apr-27	68
ML3185	Interior 2nd Floor Completion Milestone	0		17-May-27	45
ML3225	FDNY Inspection Completion Milestone	0		11-Jun-27	27
ML3395	Interior 3rd Floor Completion Milestone	0		18-Jun-27	23
ML3205	Elevator Completion Milestone	0		20-Jul-27	2
PROCUREMENT		320	01-Aug-25	22-Oct-26	259
DIVISION 1 - GENERAL REQUIREMENTS		165	01-Aug-25	10-Apr-26	267
GUARANTEES, WARRANTIES & BONDS		5	01-Aug-25	08-Aug-25	84
PR0-01-1210	Submit Bonds & Insurance	5	01-Aug-25	08-Aug-25	84
SUBCONTRACTOR "BUYOUT"		164	01-Aug-25	09-Apr-26	268
PR0-01-1000	Submit Electrical subcontractor	5	01-Aug-25	08-Aug-25	36
PR0-01-1010	Submit Mechanical (HVAC) subcontractor	5	01-Aug-25	08-Aug-25	83
PR0-01-1020	Submit Plumbing subcontractor	20	01-Aug-25	29-Aug-25	21
PR0-01-1040	Submit Painting subcontractor	84	01-Aug-25	08-Dec-25	193
PR0-01-1060	Submit Vegetated roofer subcontractor	84	01-Aug-25	08-Dec-25	154
PR0-01-1070	Submit Steel subcontractor	33	01-Aug-25	19-Sep-25	84
PR0-01-1080	Submit Carpenter subcontractor	33	01-Aug-25	19-Sep-25	149
PR0-01-1100	Submit Elevator subcontractor	20	01-Aug-25	29-Aug-25	115
PR0-01-1110	Submit Acoustical Ceiling subcontractor	33	01-Aug-25	19-Sep-25	269
PR0-01-1250	Submit Roofer subcontractor	33	01-Aug-25	19-Sep-25	154
PR0-01-1290	Submit Scaffolding subcontractor	30	01-Aug-25	15-Sep-25	0
PR0-01-1310	Submit SOE/Auger Pile subcontractor	20	01-Aug-25	29-Aug-25	17
PR0-01-1330	Submit Paving subcontractor	124	01-Aug-25	09-Feb-26	163
PR0-01-1410	Submit Metal Wall Panel subcontractor	71	01-Aug-25	14-Nov-25	170
PR0-01-1430	Submit Applied Fire Protection subcontractor	71	01-Aug-25	14-Nov-25	94
PR0-01-1450	Submit Fire Protection Fire Protection(Sprinkler) subcontractor	20	01-Aug-25	29-Aug-25	123
PR0-01-1485	Submit Geotechnical Instrumentation Monitoring & Control subcontractor	30	01-Aug-25	15-Sep-25	15
PR0-01-1505	Submit Aluminum Doors & Frames Subcontractor	52	01-Aug-25	17-Oct-25	123
PR0-01-1515	Submit Doors/ Frames & Hardware Supplier	40	01-Aug-25	30-Sep-25	194
PR0-01-1525	Submit Access Doors Supplier	40	01-Aug-25	30-Sep-25	68
PR0-01-1545	Submit Miscellaneous Metals Subcontractor	71	01-Aug-25	14-Nov-25	92
PR0-01-1555	Submit Millwork Subcontractor	52	01-Aug-25	17-Oct-25	154
PR0-01-1565	Submit Ceramic Tile Subcontractor	33	01-Aug-25	19-Sep-25	301
PR0-01-1595	Submit Signage Subcontractor	88	01-Aug-25	12-Dec-25	154
PR0-01-1605	Submit Toilet Accessories Subcontractor	105	01-Aug-25	09-Jan-26	287
PR0-01-1655	Submit Curtain & Drapes Subcontractor	100	01-Aug-25	02-Jan-26	122
PR0-01-1670	Submit Glazing Subcontractor	40	01-Aug-25	30-Sep-25	106
PR0-01-1120	Approve Electrical subcontractor	40	11-Aug-25	08-Oct-25	36
PR0-01-1160	Approve Mechanical (HVAC) subcontractor	40	11-Aug-25	08-Oct-25	84
PR0-01-1130	Approve Plumbing subcontractor	40	02-Sep-25	29-Oct-25	21

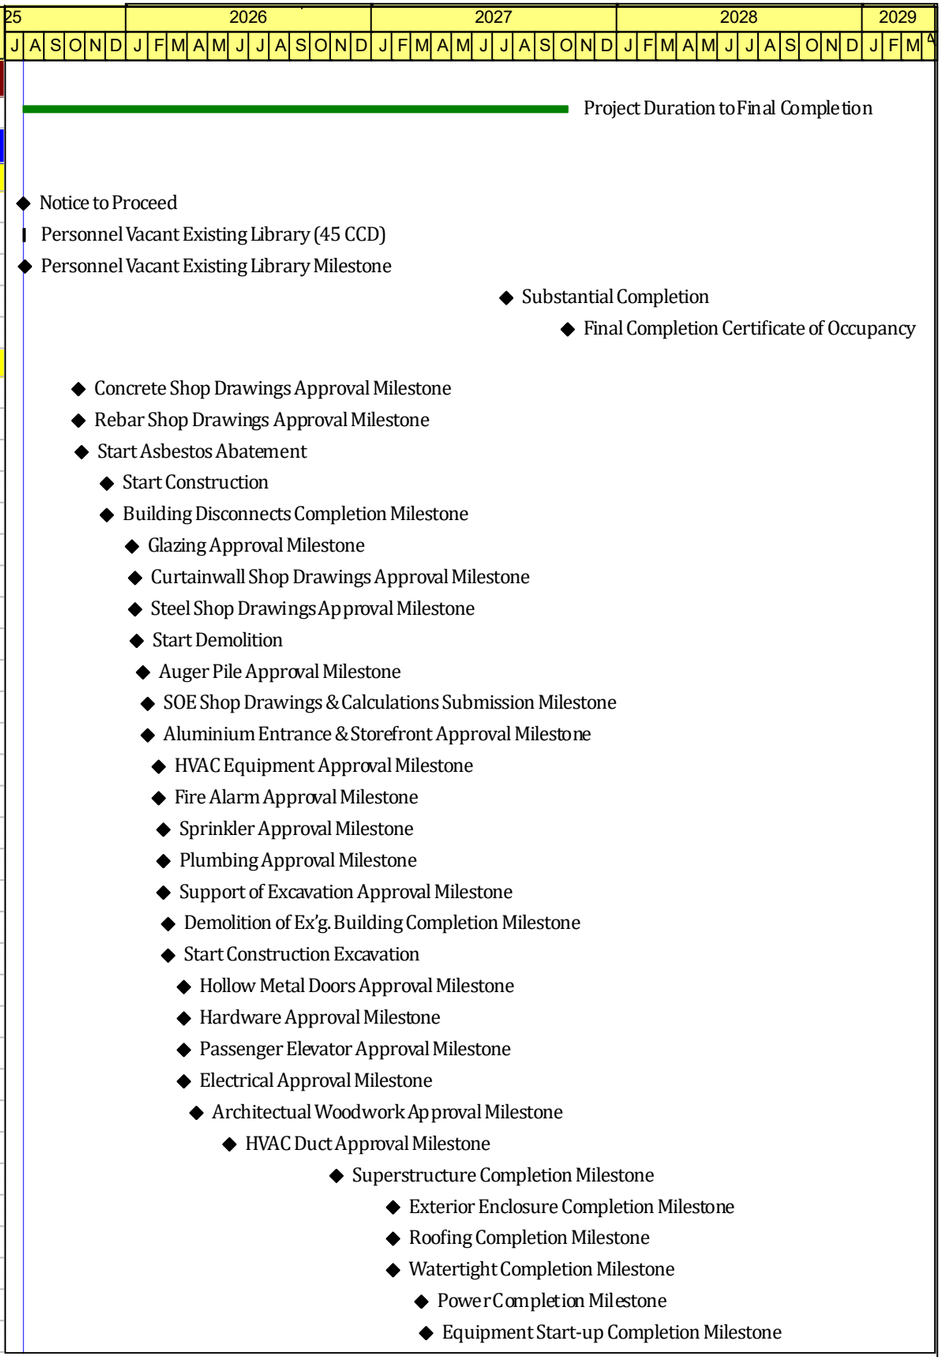

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PR0-01-1180	Approve Elevator subcontractor	40	02-Sep-25	29-Oct-25	115
PR0-01-1320	Approve SOE/Auger Pile subcontractor	40	02-Sep-25	29-Oct-25	17
PR0-01-1460	Approve Fire Protection(Sprinkler) subcontractor	40	02-Sep-25	29-Oct-25	128
PR0-01-1300	Approve Scaffolding subcontractor	40	16-Sep-25	13-Nov-25	0
PR0-01-1490	Approve Geotechnical Instrumentation Monitoring & Control subcontractor	40	16-Sep-25	13-Nov-25	15
PR0-01-1170	Approve Steel subcontractor	40	22-Sep-25	18-Nov-25	84
PR0-01-1190	Approve Carpenter subcontractor	40	22-Sep-25	18-Nov-25	149
PR0-01-1150	Approve Acoustical Ceiling subcontractor	40	22-Sep-25	18-Nov-25	269
PR0-01-1260	Approve Roofer subcontractor	40	22-Sep-25	18-Nov-25	154
PR0-01-1570	Approve Ceramic Tile Subcontractor	40	22-Sep-25	18-Nov-25	301
PR0-01-1520	Approve Doors/ Frames & Hardware Supplier	40	01-Oct-25	02-Dec-25	194
PR0-01-1530	Approve Access Doors Supplier	40	01-Oct-25	02-Dec-25	68
PR0-01-1680	Approve Glazing Subcontractor	40	01-Oct-25	02-Dec-25	106
PR0-01-1510	Approve Aluminum Doors & Frames Subcontractor	40	20-Oct-25	19-Dec-25	123
PR0-01-1560	Approve Millwork Subcontractor	40	20-Oct-25	19-Dec-25	154
PR0-01-1420	Approve Metal Wall Panel subcontractor	40	17-Nov-25	20-Jan-26	170
PR0-01-1440	Approve Applied Fire Protection subcontractor	40	17-Nov-25	20-Jan-26	94
PR0-01-1550	Approve Miscellaneous Metals Subcontractor	40	17-Nov-25	20-Jan-26	92
PR0-01-1220	Approve Painting subcontractor	40	09-Dec-25	09-Feb-26	193
PR0-01-1200	Approve Vegetated roofer subcontractor	40	09-Dec-25	09-Feb-26	154
PR0-01-1600	Approve Signage Subcontractor	40	16-Dec-25	13-Feb-26	154
PR0-01-1660	Approve Curtain & Drapes Subcontractor	40	05-Jan-26	04-Mar-26	122
PR0-01-1610	Approve Toilet Accessories Subcontractor	40	12-Jan-26	12-Mar-26	287
PR0-01-1340	Approve Paving subcontractor	40	10-Feb-26	09-Apr-26	163
013216.10 - PROJECT SCHEDULES		48	01-Aug-25	13-Oct-25	41
PRO-01-1000	Prepare and submit preliminary schedule	8	01-Aug-25	13-Aug-25	41
PRO-01-1010	Prepare and submit baseline schedule	33	01-Aug-25	19-Sep-25	41
PRO-01-1020	Review and approve preliminary schedule	15	14-Aug-25	04-Sep-25	51
PRO-01-1030	Review and approve baseline schedule	15	22-Sep-25	13-Oct-25	41
013526 - SAFETY REQUIREMENTS		16	01-Aug-25	25-Aug-25	59
PRO-01-1040	Prepare and submit safety program	1	01-Aug-25	01-Aug-25	59
PRO-01-1050	Review and approve safety program	15	05-Aug-25	25-Aug-25	59
015000 - TEMPORARY FACILITIES, SERVICES AND CONTROLS		22	01-Aug-25	03-Sep-25	51
PRO-01-1080	Prepare and submit site plan (Fencing)	7	01-Aug-25	12-Aug-25	51
PRO-01-1090	Review and approve site plan (Fencing)	15	13-Aug-25	03-Sep-25	51
017419 - CONSTRUCTION WASTE MANAGEMENT AND DISPOSAL		28	01-Aug-25	11-Sep-25	47
PRO-01-1140	Prepare and submit waste management plan	13	01-Aug-25	20-Aug-25	47
PRO-01-1150	Review and approve waste management plan	15	21-Aug-25	11-Sep-25	47
VIBRATION & MONITORING CONSTROL EQUIPMENT		30	16-Sep-25	29-Oct-25	25
PRO-01-1185	Prepare and submit Geotechnical Instrumentation Monitoring & Control	15	16-Sep-25	08-Oct-25	25
PRO-01-1190	Review and approve Geotechnical Instrumentation Monitoring & Control	15	09-Oct-25	29-Oct-25	25
COORDINATION DRAWINGS		160	11-Aug-25	10-Apr-26	127



Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
COORDINATION DRAWINGS EXISTING BUILDING		145	11-Aug-25	19-Mar-26	142
PRO-01-1470	Develop HVAC Coordination Overlay Drawings Cellar Existing Building	40	11-Aug-25	08-Oct-25	113
PRO-01-1480	Prepare Plumbing Coordination Drawings Cellar Existing Building	15	09-Oct-25	29-Oct-25	113
PRO-01-1520	Develop HVAC Coordination Overlay Drawings 1st Floor Existing Building	15	09-Oct-25	29-Oct-25	142
PRO-01-1490	Prepare Sprinkler Coordination Drawings Cellar Existing Building	15	30-Oct-25	21-Nov-25	113
PRO-01-1530	Prepare Plumbing Coordination Drawings 1st Floor Existing Building	15	30-Oct-25	21-Nov-25	172
PRO-01-1570	Develop HVAC Coordination Overlay Drawings 2nd Floor Existing Building	15	30-Oct-25	21-Nov-25	142
PRO-01-1500	Prepare Electrical Coordination Drawings Cellar Existing Building	15	24-Nov-25	17-Dec-25	113
PRO-01-1540	Prepare Sprinkler Coordination Drawings 1st Floor Existing Building	15	24-Nov-25	17-Dec-25	172
PRO-01-1580	Prepare Plumbing Coordination Drawings 2nd Floor Existing Building	15	24-Nov-25	17-Dec-25	157
PRO-01-1670	Develop HVAC Coordination Overlay Drawings Roof Existing Building	15	24-Nov-25	17-Dec-25	142
PRO-01-1510	Sign-off Coordination Drawings Cellar Existing Building	15	18-Dec-25	09-Jan-26	113
PRO-01-1550	Prepare Electrical Coordination Drawings 1st Floor Existing Building	15	18-Dec-25	09-Jan-26	172
PRO-01-1590	Prepare Sprinkler Coordination Drawings 2nd Floor Existing Building	15	18-Dec-25	09-Jan-26	157
PRO-01-1680	Prepare Plumbing Coordination Drawings Roof Existing Building	15	18-Dec-25	09-Jan-26	142
PRO-01-1560	Sign-off Coordination Drawings 1st Floor Existing Building	15	12-Jan-26	02-Feb-26	172
PRO-01-1600	Prepare Electrical Coordination Drawings 2nd Floor Existing Building	15	12-Jan-26	02-Feb-26	157
PRO-01-1690	Prepare Sprinkler Coordination Drawings Roof Existing Building	15	12-Jan-26	02-Feb-26	142
PRO-01-1610	Sign-off Coordination Drawings 2nd Floor Existing Building	15	03-Feb-26	25-Feb-26	157
PRO-01-1700	Prepare Electrical Coordination Drawings Roof Existing Building	15	03-Feb-26	25-Feb-26	142
PRO-01-1710	Sign-off Coordination Drawings Roof Existing Building	15	26-Feb-26	19-Mar-26	142
COORDINATION DRAWINGS NEW ADDITION		160	11-Aug-25	10-Apr-26	127
PRO-01-1220	Develop HVAC Coordination Overlay Drawings Cellar New Addition	40	11-Aug-25	08-Oct-25	83
PRO-01-1230	Prepare Plumbing Coordination Drawings Cellar New Addition	15	09-Oct-25	29-Oct-25	83
PRO-01-1270	Develop HVAC Coordination Overlay Drawings 1st Floor New Addition	15	09-Oct-25	29-Oct-25	127
PRO-01-1240	Prepare Sprinkler Coordination Drawings Cellar New Addition	15	30-Oct-25	21-Nov-25	83
PRO-01-1280	Prepare Plumbing Coordination Drawings 1st Floor New Addition	15	30-Oct-25	21-Nov-25	132
PRO-01-1320	Develop HVAC Coordination Overlay Drawings 2nd Floor New Addition	15	30-Oct-25	21-Nov-25	127
PRO-01-1250	Prepare Electrical Coordination Drawings Cellar New Addition	15	24-Nov-25	17-Dec-25	83
PRO-01-1290	Prepare Sprinkler Coordination Drawings 1st Floor New Addition	15	24-Nov-25	17-Dec-25	132
PRO-01-1330	Prepare Plumbing Coordination Drawings 2nd Floor New Addition	15	24-Nov-25	17-Dec-25	132
PRO-01-1370	Develop HVAC Coordination Overlay Drawings 3rd Floor New Addition	15	24-Nov-25	17-Dec-25	127
PRO-01-1260	Sign-off Coordination Drawings Cellar New Addition	15	18-Dec-25	09-Jan-26	83
PRO-01-1300	Prepare Electrical Coordination Drawings 1st Floor New Addition	15	18-Dec-25	09-Jan-26	132
PRO-01-1340	Prepare Sprinkler Coordination Drawings 2nd Floor New Addition	15	18-Dec-25	09-Jan-26	132
PRO-01-1380	Prepare Plumbing Coordination Drawings 3rd Floor New Addition	15	18-Dec-25	09-Jan-26	132
PRO-01-1420	Develop HVAC Coordination Overlay Drawings Roof New Addition	15	18-Dec-25	09-Jan-26	127
PRO-01-1310	Sign-off Coordination Drawings 1st Floor New Addition	15	12-Jan-26	02-Feb-26	132
PRO-01-1350	Prepare Electrical Coordination Drawings 2nd Floor New Addition	15	12-Jan-26	02-Feb-26	132
PRO-01-1390	Prepare Sprinkler Coordination Drawings 3rd Floor New Addition	15	12-Jan-26	02-Feb-26	132
PRO-01-1430	Prepare Plumbing Coordination Drawings Roof New Addition	15	12-Jan-26	02-Feb-26	127

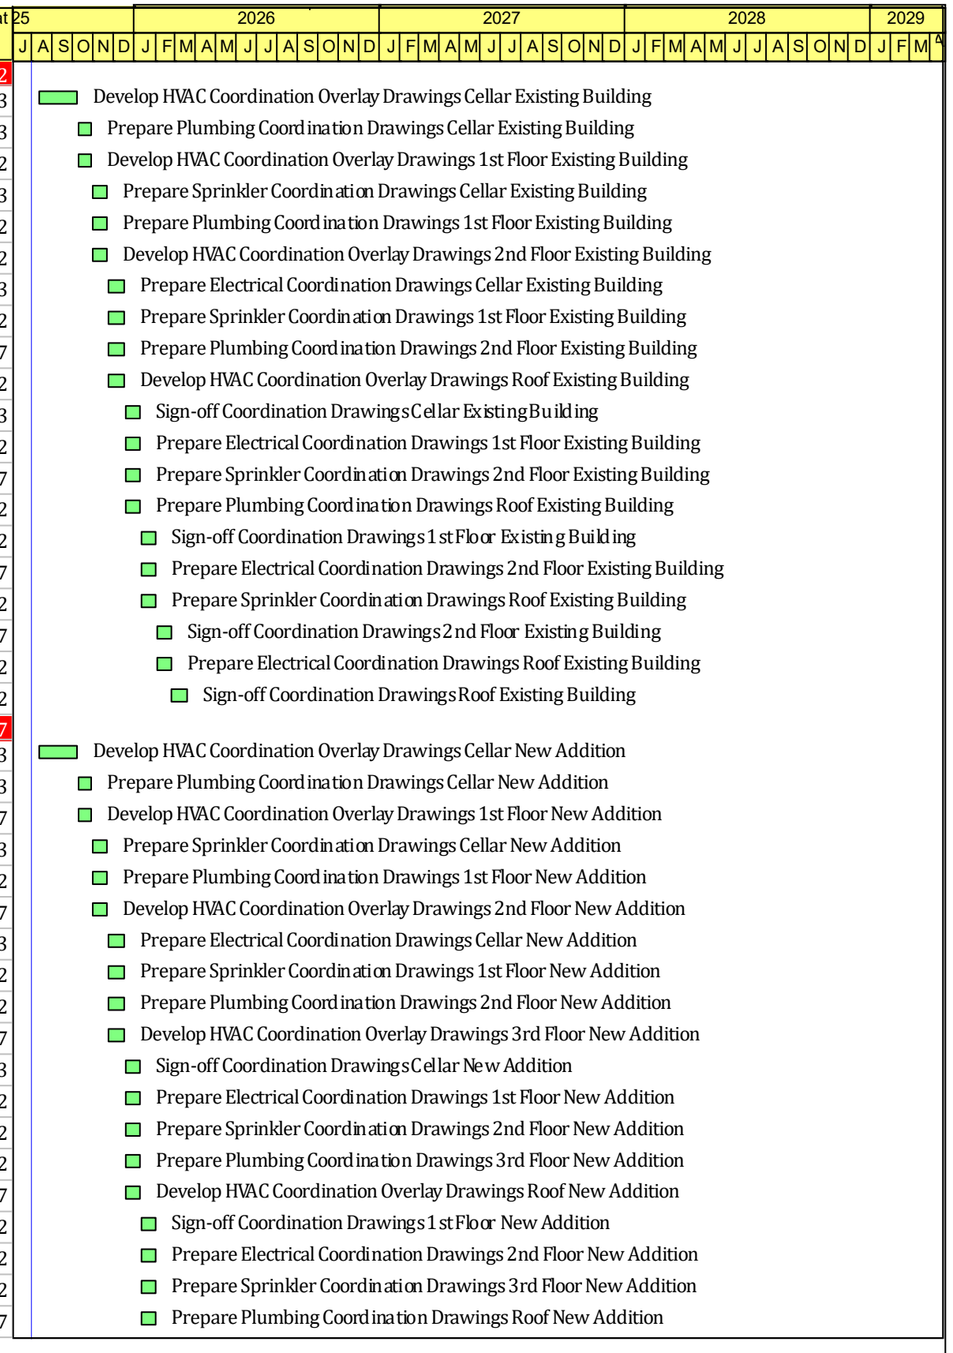

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PRO-01-1360	Sign-off Coordination Drawings 2 nd Floor New Addition	15	03-Feb-26	25-Feb-26	132
PRO-01-1400	Prepare Electrical Coordination Drawings 3rd Floor New Addition	15	03-Feb-26	25-Feb-26	132
PRO-01-1440	Prepare Sprinkler Coordination Drawings Roof New Addition	15	03-Feb-26	25-Feb-26	127
PRO-01-1410	Sign-off Coordination Drawings 3 rd Floor New Addition	15	26-Feb-26	19-Mar-26	132
PRO-01-1450	Prepare Electrical Coordination Drawings Roof New Addition	15	26-Feb-26	19-Mar-26	127
PRO-01-1460	Sign-off Coordination Drawings Roof New Addition	15	20-Mar-26	10-Apr-26	127
DIVISION 2 - EXISTING CONDITIONS		36	01-Aug-25	24-Sep-25	53
024119 SELECTIVE DEMOLITION PLANS		36	01-Aug-25	24-Sep-25	48
PRE-1070	Preparation of Structural Demolition Plans	21	01-Aug-25	02-Sep-25	48
PRE-1100	Review Structural Demolition Plans	15	03-Sep-25	24-Sep-25	48
028013 - ALLOWANCE FOR INCIDENTAL ASBESTOS ABATEMENT		36	01-Aug-25	24-Sep-25	53
PRO-02-1020	Prepare and submit Allowance Asbestos Abatement Plan	21	01-Aug-25	02-Sep-25	53
PRO-02-1080	Prepare and submit Allowance Asbestos Abatement permits and certifications	21	01-Aug-25	02-Sep-25	53
PRO-02-1030	Review and approve Allowance Asbestos Abatement Plan	15	03-Sep-25	24-Sep-25	53
PRO-02-1090	Review and approve Allowance Asbestos Abatement permits and certifications	15	03-Sep-25	24-Sep-25	53
028213 - ASBESTOS ABATEMENT		36	01-Aug-25	24-Sep-25	53
PRO-02-1100	Prepare and submit Asbestos Abatement Plan	21	01-Aug-25	02-Sep-25	53
PRO-02-1110	Prepare and submit Asbestos Abatement permits and certifications	21	01-Aug-25	02-Sep-25	53
PRO-02-1120	Review and approve Asbestos Abatement plan	15	03-Sep-25	24-Sep-25	53
PRO-02-1130	Review and approve Asbestos Abatement permits and certifications	15	03-Sep-25	24-Sep-25	53
DIVISION 3 - CONCRETE		127	01-Aug-25	26-Jan-26	216
032000 CONCRETE REINFORCING		75	01-Aug-25	21-Nov-25	117
PRO-03-1060	Prepare and submit cip reinforcement shop drawings	40	01-Aug-25	30-Sep-25	117
PRO-03-1150	Prepare and submit architectural cip reinforcement shop drawings	40	01-Aug-25	30-Sep-25	117
PRO-03-1070	Prepare and submit cip reinforcement product data	40	01-Aug-25	30-Sep-25	117
PRO-03-1100	Review and approve cip reinforcement shop drawings	15	01-Oct-25	22-Oct-25	117
PRO-03-1110	Review and approve cip reinforcement product data	15	01-Oct-25	22-Oct-25	117
PRO-03-1140	Fabrication and delivery of concrete reinforcement	20	23-Oct-25	21-Nov-25	117
033000 - CAST-IN-PLACE CONCRETE		66	01-Aug-25	06-Nov-25	136
PRO-03-1040	Prepare and submit formwork shop drawings	40	01-Aug-25	30-Sep-25	146
PRO-03-1050	Prepare and submit Cip concrete product data	33	01-Aug-25	19-Sep-25	153
PRO-03-1080	Prepare and submit concrete design mix	33	01-Aug-25	19-Sep-25	153
PRO-03-1090	Review and approve cip concrete product data	15	22-Sep-25	13-Oct-25	153
PRO-03-1120	Review and approve concrete design mix	15	22-Sep-25	13-Oct-25	153
PRO-03-1130	Review and approve formwork shop drawings	15	01-Oct-25	22-Oct-25	146
PRO-03-1190	Review and approve architectural cip reinforcement shop drawings	15	01-Oct-25	22-Oct-25	117
PRO-03-1000	Fabrication and delivery of cip concrete	1	23-Oct-25	23-Oct-25	146
PRO-03-1010	Fabrication and delivery of formwork	1	06-Nov-25	06-Nov-25	136
034500 PRECAST ARCHITECTURAL CONCRETE		115	01-Aug-25	26-Jan-26	203
PRO-03-1160	Prepare and submit Precast Architectural mock-up	50	01-Aug-25	15-Oct-25	203
PRO-03-1170	Prepare and submit Precast Architectural product data	50	01-Aug-25	15-Oct-25	203
PRO-03-1180	Prepare and submit Precast Architectural shop drawings	50	01-Aug-25	15-Oct-25	136

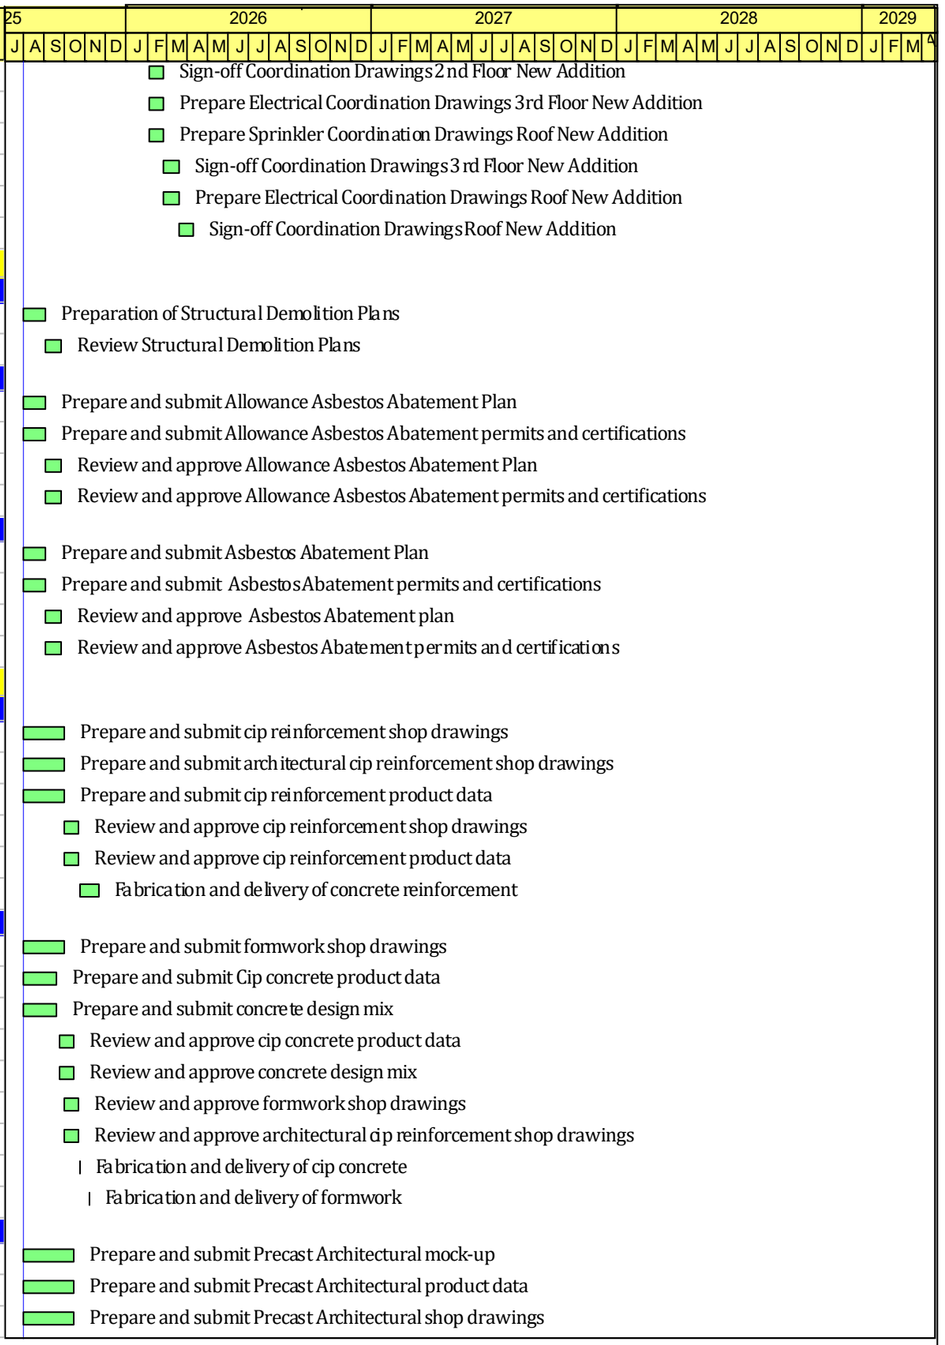

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PRO-03-1200	Review and approve Precast Architectural mock-up	15	16-Oct-25	05-Nov-25	203
PRO-03-1210	Review and approve architectural cip concrete product data	15	16-Oct-25	05-Nov-25	203
PRO-03-1220	Review and approve Precast Architectural shop drawings	15	16-Oct-25	05-Nov-25	136
PRO-03-1230	Fabrication and delivery of Precast Architectural	50	06-Nov-25	26-Jan-26	203
035319 CONCRETE OVERLAYMENT		0			0
DIVISION 4 - MASONRY		243	01-Aug-25	04-Aug-26	75
040120.52 MASONRY CLEANING		243	01-Aug-25	04-Aug-26	75
PRO-04-1140	Prepare and submit Masonry Cleaning product data	208	01-Aug-25	15-Jun-26	75
PRO-04-1170	Review and approve Masonry Cleaning product data	15	16-Jun-26	06-Jul-26	75
PRO-04-1160	Fabricate and deliver Masonry Cleaning Material	20	07-Jul-26	04-Aug-26	75
040140.91 STONE MASONRY RESTORATION		122	01-Aug-25	05-Feb-26	106
PRO-04-1070	Prepare and submit Stone Masonry product data	72	01-Aug-25	17-Nov-25	106
PRO-04-1120	Prepare and submit Stone Masonry shop drawings	72	01-Aug-25	17-Nov-25	141
PRO-04-1215	Prepare and submit Stone Masonry Samples	72	01-Aug-25	17-Nov-25	106
PRO-04-1100	Review and Stone Masonry product data	15	18-Nov-25	11-Dec-25	106
PRO-04-1130	Review and approve Stone Masonry shop drawings	15	18-Nov-25	11-Dec-25	141
PRO-04-1220	Review and approve Stone Masonry Samples	15	18-Nov-25	11-Dec-25	106
PRO-04-1080	Prepare and submit Stone Masonry mock-up	20	12-Dec-25	13-Jan-26	106
PRO-04-1110	Review and approve Stone Masonry mock-up	15	14-Jan-26	05-Feb-26	106
04200 - UNIT MASONRY		122	01-Aug-25	05-Feb-26	196
PRO-04-1010	Prepare and submit CMU product data	52	01-Aug-25	17-Oct-25	196
PRO-04-1020	Prepare and submit CMU shop drawings	52	01-Aug-25	17-Oct-25	231
PRO-04-1205	Prepare and submit CMU Design Mix	52	01-Aug-25	17-Oct-25	231
PRO-04-1030	Review and approve CMU product data	15	20-Oct-25	07-Nov-25	196
PRO-04-1040	Review and approve CMU shop drawings	15	20-Oct-25	07-Nov-25	231
PRO-04-1210	Review and approve CMU Design Mix	15	20-Oct-25	07-Nov-25	231
PRO-04-1050	Prepare and submit CMU mock-up	20	10-Nov-25	11-Dec-25	196
PRO-04-1060	Review and approve CMU mock-up	15	12-Dec-25	06-Jan-26	196
PRO-04-1000	Fabricate and deliver CMU	20	07-Jan-26	05-Feb-26	196
DIVISION 5 - METALS		73	19-Nov-25	13-Mar-26	242
051200 - STEEL STRUCTURAL FRAMING		35	19-Nov-25	14-Jan-26	84
PRO-05-1050	Prepare and submit steel structural framing shop drawings	20	19-Nov-25	22-Dec-25	84
PRO-05-1295	Prepare and submit steel structural framing Samples	20	19-Nov-25	22-Dec-25	84
PRO-05-1305	Prepare and submit steel structural framing Product Data	20	19-Nov-25	22-Dec-25	84
PRO-05-1060	Review and approve steel structural framing shop drawings	15	23-Dec-25	14-Jan-26	84
PRO-05-1300	Review and approve steel structural framing Samples	15	23-Dec-25	14-Jan-26	84
PRO-05-1310	Review and approve steel structural framing Product Data	15	23-Dec-25	14-Jan-26	84
053100 - STEEL DECK		35	19-Nov-25	14-Jan-26	84
PRO-05-1070	Prepare and submit steel deck Product Data	20	19-Nov-25	22-Dec-25	84
PRO-05-1335	Prepare and submit steel deck shop drawings	20	19-Nov-25	22-Dec-25	84
PRO-05-1080	Review and approve steel deck Product Data	15	23-Dec-25	14-Jan-26	84
PRO-05-1340	Review and approve steel deck shop drawings	15	23-Dec-25	14-Jan-26	84
054000 - COLD-FORMED METAL FRAMING		30	19-Nov-25	07-Jan-26	135

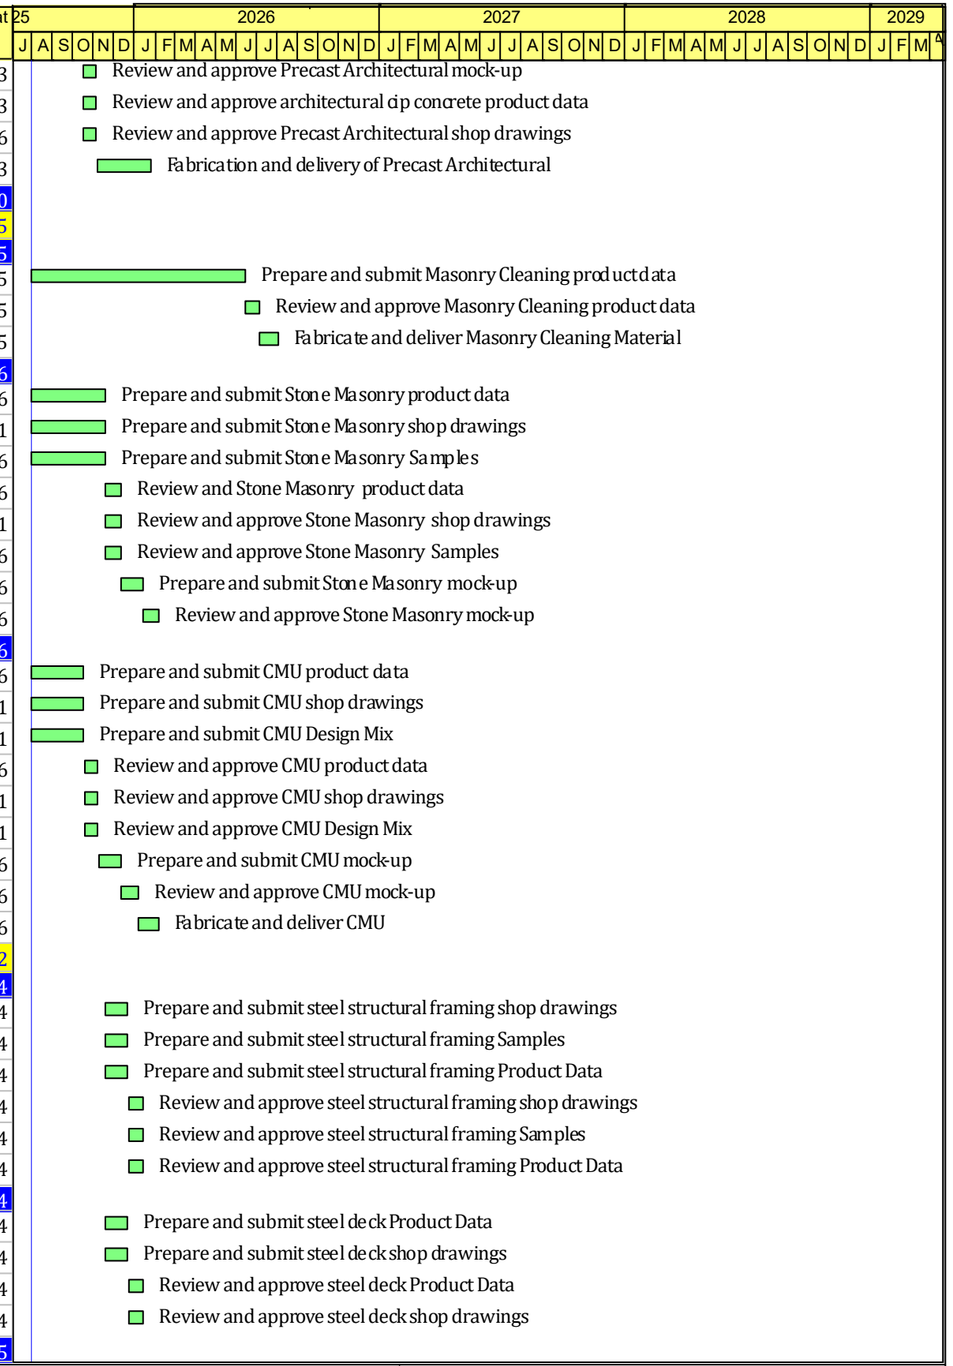

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PRO-05-1220	Prepare and submit Cold formed metal framing product data	15	19-Nov-25	12-Dec-25	135
PRO-05-1345	Prepare and submit Cold formed metal framing shop drawings	15	19-Nov-25	12-Dec-25	135
PRO-05-1215	Review and approve Cold formed metal framing product data	15	16-Dec-25	07-Jan-26	135
PRO-05-1350	Review and approve Cold formed metal framing shop drawings	15	16-Dec-25	07-Jan-26	135
055000 - METAL FABRICATIONS		35	21-Jan-26	13-Mar-26	92
PRO-05-1090	Prepare and submit assembling miscellaneous metals product data	20	21-Jan-26	19-Feb-26	92
PRO-05-1355	Prepare and submit assembling miscellaneous metals shop drawings	20	21-Jan-26	19-Feb-26	92
PRO-05-1365	Prepare and submit assembling miscellaneous metals Samples	20	21-Jan-26	19-Feb-26	92
PRO-05-1100	Review and approve assembling miscellaneous metals product data	15	20-Feb-26	13-Mar-26	92
PRO-05-1360	Review and approve assembling miscellaneous metals shop drawings	15	20-Feb-26	13-Mar-26	92
PRO-05-1370	Review and approve assembling miscellaneous metals Samples	15	20-Feb-26	13-Mar-26	92
055113 - METAL PAN STAIRS		35	21-Jan-26	13-Mar-26	236
PRO-05-1225	Prepare and submit Metal Pan Stairs shop drawings	20	21-Jan-26	19-Feb-26	236
PRO-05-1230	Prepare and submit Metal Pan Stairs product data	20	21-Jan-26	19-Feb-26	236
PRO-05-1235	Review and approve Metal Pan Stairs shop drawings	15	20-Feb-26	13-Mar-26	236
PRO-05-1240	Review and approve Metal Pan Stairs Product Data	15	20-Feb-26	13-Mar-26	236
055213 -PIPE AND TUBE RAILINGS		35	21-Jan-26	13-Mar-26	242
PRO-05-1110	Prepare and submit Metal Railings shop drawings	20	21-Jan-26	19-Feb-26	242
PRO-05-1120	Prepare and submit Metal Railings product data	20	21-Jan-26	19-Feb-26	242
PRO-05-1375	Prepare and submit Metal Railings Samples	20	21-Jan-26	19-Feb-26	242
PRO-05-1130	Review and approve Metal Railings shop drawings	15	20-Feb-26	13-Mar-26	242
PRO-05-1140	Review and approve Metal Railings product data	15	20-Feb-26	13-Mar-26	242
PRO-05-1380	Review and approve Metal Railings Samples	15	20-Feb-26	13-Mar-26	242
DIVISION 6 - WOOD, PLASTICS AND COMPOSITES		154	19-Nov-25	10-Jul-26	175
061000 - ROUGH CARPENTRY		40	19-Nov-25	22-Jan-26	185
PRO-06-1020	Prepare and submit rough carpentry Product Data	20	19-Nov-25	22-Dec-25	185
PRO-06-1355	Prepare and submit rough carpentry Mockup	20	19-Nov-25	22-Dec-25	185
PRO-06-1030	Review and approve rough carpentry Product Data	15	23-Dec-25	14-Jan-26	185
PRO-06-1360	Review and approve rough carpentry Mockup	15	23-Dec-25	14-Jan-26	185
PRO-06-1000	Fabrication and delivery of rough carpentry materials	5	15-Jan-26	22-Jan-26	185
061600 - SHEATHING		40	19-Nov-25	22-Jan-26	205
PRO-06-1095	Prepare and submit Sheathing Product Data	20	19-Nov-25	22-Dec-25	205
PRO-06-1105	Review and approve Sheathing Product Data	15	23-Dec-25	14-Jan-26	205
PRO-06-1100	Fabrication and delivery of Sheathing materials	5	15-Jan-26	22-Jan-26	205
064023 - INTERIOR ARCHITECTURAL WOODWORK		135	22-Dec-25	10-Jul-26	175
PRO-06-1300	Prepare and submit Interior Architectural Woodwork shop drawings	60	22-Dec-25	23-Mar-26	175
PRO-06-1310	Prepare and submit Architectural Woodwork data sheet	60	22-Dec-25	23-Mar-26	175
PRO-06-1320	Prepare and submit Architectural Woodwork samples	60	22-Dec-25	23-Mar-26	175
PRO-06-1295	Review and approve Architectural Woodwork shop drawings	15	24-Mar-26	14-Apr-26	235
PRO-06-1305	Review and approve Architectural Woodwork data sheet	15	24-Mar-26	14-Apr-26	235
PRO-06-1315	Review and approve Architectural Woodwork samples	15	24-Mar-26	14-Apr-26	235
PRO-06-1365	Prepare and submit Interior Architectural Woodwork Mockup	60	24-Mar-26	19-Jun-26	175

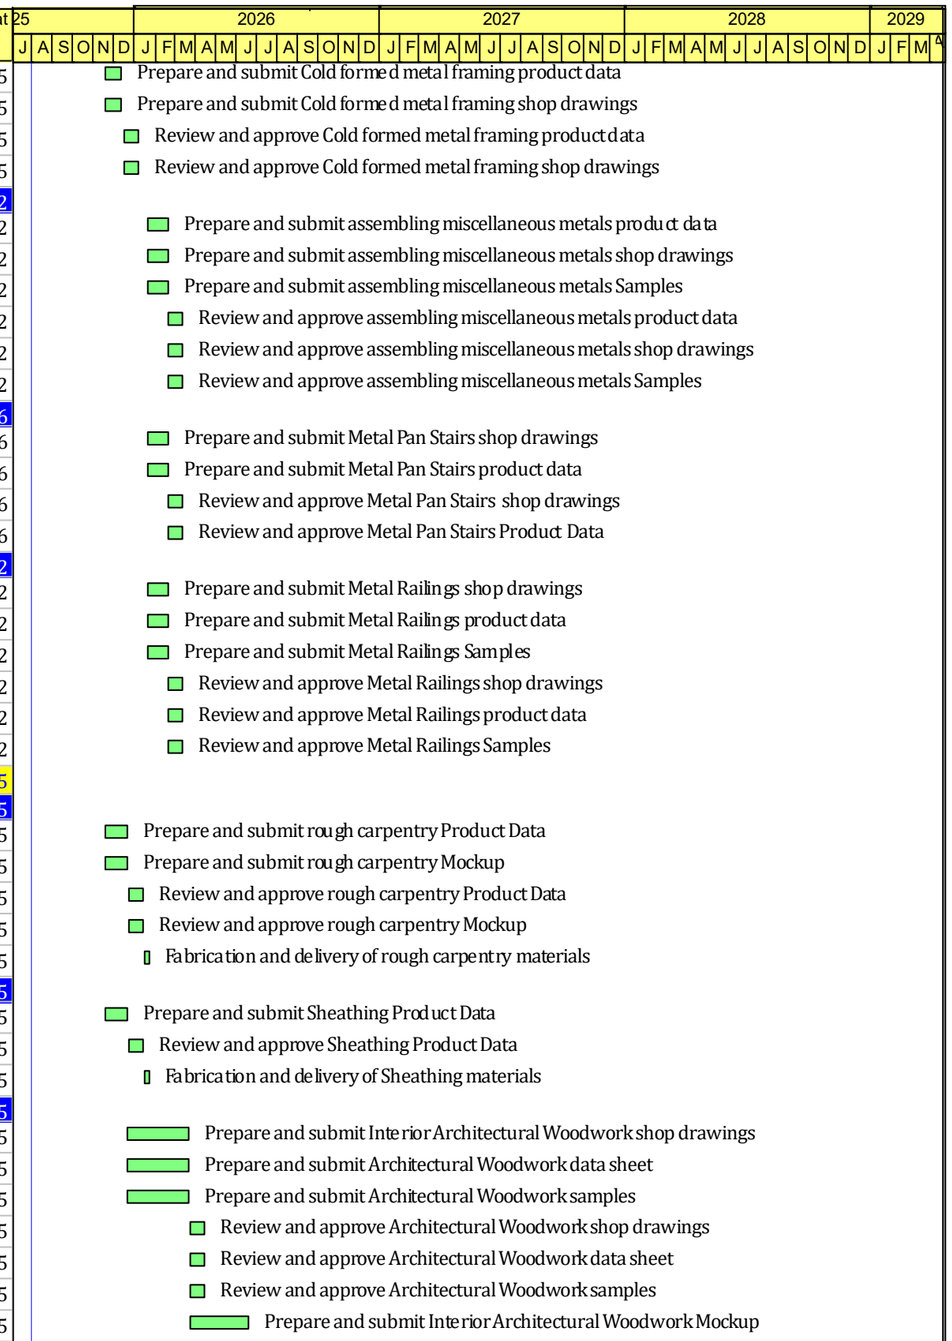

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PR0-06-1370	Review and approve Architectural Woodwork Mockup	15	22-Jun-26	10-Jul-26	175
DIVISION 7 - THERMAL AND MOISTURE PROTECTION		193	01-Aug-25	21-May-26	244
071326 - SELF-ADHERING SHEET WATERPROOFING		117	01-Aug-25	28-Jan-26	201
PR0-07-1120	Prepare and submit Self-Adhering Sheet Waterproofing product data	52	01-Aug-25	17-Oct-25	201
PR0-07-1140	Prepare and submit Self-Adhering Sheet Waterproofing sample	52	01-Aug-25	17-Oct-25	201
PR0-07-1635	Prepare and submit Self-Adhering Sheet Waterproofing Shop Drawings	52	01-Aug-25	17-Oct-25	201
PR0-07-1100	Review and approve Self-Adhering Sheet Waterproofing product data	15	20-Oct-25	07-Nov-25	201
PR0-07-1130	Review and approve Self-Adhering Sheet Waterproofing sample	15	20-Oct-25	07-Nov-25	201
PR0-07-1640	Review and approve Self-Adhering Sheet Waterproofing Shop Drawings	15	20-Oct-25	07-Nov-25	201
PR0-07-1625	Prepare and submit Self-Adhering Sheet Waterproofing Mockup	30	10-Nov-25	29-Dec-25	201
PR0-07-1630	Review and approve Self-Adhering Sheet Waterproofing Mockup	15	30-Dec-25	21-Jan-26	201
PR0-07-1000	Fabrication and delivery of Self-Adhering Sheet Waterproofing material	5	22-Jan-26	28-Jan-26	201
072100 - THERMAL INSULATION		40	19-Nov-25	22-Jan-26	205
PR0-07-1200	Prepare and submit thermal insulation product data	20	19-Nov-25	22-Dec-25	205
PR0-07-1190	Review and approve thermal insulation product data	15	23-Dec-25	14-Jan-26	205
PR0-07-1020	Fabrication and delivery of thermal insulation material	5	15-Jan-26	22-Jan-26	205
072715 - NONBITUMINOUS SELF ADHERING SHEET AIR BARRIER		85	19-Nov-25	31-Mar-26	195
PR0-07-2250	Prepare and submit Non-bituminous Self Adhering Sheet Air Barrier product data	20	19-Nov-25	22-Dec-25	195
PR0-07-2270	Prepare and submit Non-bituminous Self Adhering Sheet Air Barrier sample	20	19-Nov-25	22-Dec-25	195
PR0-07-2290	Prepare and submit Non-bituminous Self Adhering Sheet Air Barrier Shop Drawings	20	19-Nov-25	22-Dec-25	195
PR0-07-2240	Review and approve Nonbituminous Self Adhering Sheet Air Barrier product data	15	23-Dec-25	14-Jan-26	195
PR0-07-2260	Review and approve Nonbituminous Self Adhering Sheet Air Barrier sample	15	23-Dec-25	14-Jan-26	195
PR0-07-2280	Review and approve Nonbituminous Self Adhering Sheet Air Barrier Shop Drawings	15	23-Dec-25	14-Jan-26	195
PR0-07-2310	Prepare and submit Nonbituminous Self Adhering Sheet Air Barrier Mockup	30	15-Jan-26	02-Mar-26	195
PR0-07-2300	Review and approve Nonbituminous Self Adhering Sheet Air Barrier Mockup	15	03-Mar-26	24-Mar-26	195
PR0-07-1045	Fabrication and delivery Nonbituminous Self Adhering Sheet Air Barrier material	5	25-Mar-26	31-Mar-26	195
072726 - FLUID APPLIED MEMBRANE AIR BARRIER		100	19-Nov-25	22-Apr-26	180
PR0-07-1220	Prepare and submit Fluid Applied membrane air barrier shop drawings	15	19-Nov-25	12-Dec-25	170
PR0-07-1240	Prepare and submit Fluid Applied membrane air barrier product data	15	19-Nov-25	12-Dec-25	170
PR0-07-1210	Review and approve Fluid Applied membrane air barrier shop drawings	15	16-Dec-25	07-Jan-26	170
PR0-07-1230	Review and approve Fluid Applied membrane air barrier product data	15	16-Dec-25	07-Jan-26	170
PR0-07-1705	Prepare and submit Fluid Applied membrane air barrier Mockup	50	08-Jan-26	24-Mar-26	180
PR0-07-1710	Review and approve Fluid Applied membrane air barrier Mockup	15	25-Mar-26	15-Apr-26	180
PR0-07-1030	Fabrication and delivery of Fluid Applied membrane air barrier material	5	16-Apr-26	22-Apr-26	180
074213.13 -FORMED METAL WALL PANELS		45	08-Jan-26	17-Mar-26	170
PR0-07-2370	Prepare and submit Formed Metal Wall Panels Mockup	25	08-Jan-26	13-Feb-26	170
PR0-07-2330	Prepare and submit Formed Metal Wall Panels product data	17	21-Jan-26	13-Feb-26	170
PR0-07-2350	Prepare and submit Formed Metal Wall Panels sample	17	21-Jan-26	13-Feb-26	170
PR0-07-2320	Review and approve Formed Metal Wall Panels product data	15	17-Feb-26	09-Mar-26	170
PR0-07-2340	Review and approve Formed Metal Wall Panels sample	15	17-Feb-26	09-Mar-26	170
PR0-07-2360	Review and approve Formed Metal Wall Panels Mockup	15	17-Feb-26	09-Mar-26	170
PR0-07-1055	Fabrication and delivery of Formed Metal Wall Panels material	5	10-Mar-26	17-Mar-26	170

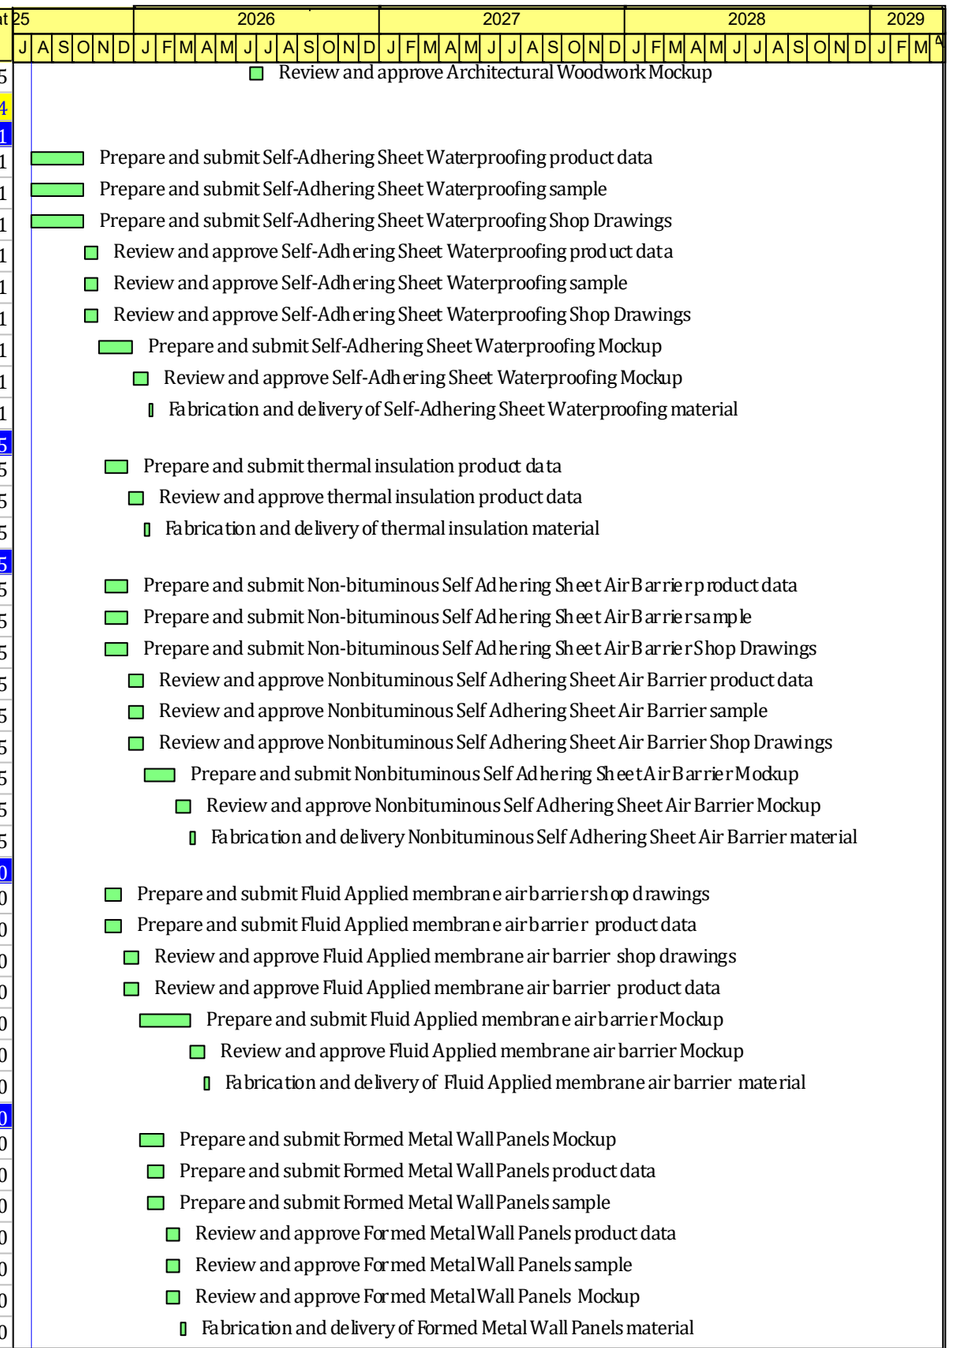

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
074213.16 - METAL PLATE WALL PANELS		45	08-Jan-26	17-Mar-26	170
PR0-07-1715	Prepare and submit Metal Plate Wall Panels Mockup	25	08-Jan-26	13-Feb-26	170
PR0-07-1535	Prepare and submit Metal Plate Wall Panels product data	17	21-Jan-26	13-Feb-26	170
PR0-07-1545	Prepare and submit Metal Plate Wall Panels sample	17	21-Jan-26	13-Feb-26	170
PR0-07-1530	Review and approve Metal Plate Wall Panels product data	15	17-Feb-26	09-Mar-26	170
PR0-07-1540	Review and approve Metal Plate Wall Panels sample	15	17-Feb-26	09-Mar-26	170
PR0-07-1720	Review and approve Metal Plate Wall Panels Mockup	15	17-Feb-26	09-Mar-26	170
PR0-07-1025	Fabrication and delivery of Metal Plate Wall Panels material	5	10-Mar-26	17-Mar-26	170
075600 - COLD FLUID APPLIED ROOFING		154	01-Aug-25	25-Mar-26	199
PR0-07-1440	Prepare and submit Cold Fluid Applied Roofing product data	89	01-Aug-25	16-Dec-25	199
PR0-07-1450	Prepare and submit Cold Fluid Applied Roofing sample	89	01-Aug-25	16-Dec-25	199
PR0-07-1645	Prepare and submit Cold Fluid Applied Roofing Shop Drawings	89	01-Aug-25	16-Dec-25	199
PR0-07-1435	Review and approve Cold Fluid Applied Roofing product data	15	17-Dec-25	08-Jan-26	199
PR0-07-1445	Review and approve Cold Fluid Applied Waterproofing sample	15	17-Dec-25	08-Jan-26	199
PR0-07-1655	Review and approve Cold Fluid Applied Roofing Shop Drawings	15	17-Dec-25	08-Jan-26	199
PR0-07-1650	Prepare and submit Cold Fluid Applied Roofing Mockup	30	09-Jan-26	24-Feb-26	199
PR0-07-1660	Review and approve Cold Fluid Applied Roofing Mockup	15	25-Feb-26	18-Mar-26	199
PR0-07-1005	Fabrication and delivery of Cold Fluid Applied Roofing material	5	19-Mar-26	25-Mar-26	199
076200 - SHEET METAL FLASHING AND TRIM		70	19-Nov-25	09-Mar-26	210
PR0-07-1300	Prepare and submit sheet metal flashing shop drawings	15	19-Nov-25	12-Dec-25	210
PR0-07-1320	Prepare and submit sheet metal flashing product data	15	19-Nov-25	12-Dec-25	210
PR0-07-1755	Prepare and submit sheet metal flashing Samples	15	19-Nov-25	12-Dec-25	210
PR0-07-1290	Review and approve sheet metal flashing shop drawings	15	16-Dec-25	07-Jan-26	210
PR0-07-1310	Review and approve sheet metal flashing product data	15	16-Dec-25	07-Jan-26	210
PR0-07-1760	Review and approve sheet metal flashing Samples	15	16-Dec-25	07-Jan-26	210
PR0-07-1745	Prepare and submit sheet metal flashing Mockup	20	08-Jan-26	06-Feb-26	210
PR0-07-1750	Review and approve sheet metal flashing Mockup	15	09-Feb-26	02-Mar-26	210
PR0-07-1050	Fabrication and delivery of sheet metal flashing material	5	03-Mar-26	09-Mar-26	210
077100 - ROOF SPECIALTIES		110	19-Nov-25	06-May-26	170
PR0-07-1340	Prepare and submit roof specialties product data	55	19-Nov-25	13-Feb-26	170
PR0-07-1765	Prepare and submit roof specialties Shop Drawings	55	19-Nov-25	13-Feb-26	170
PR0-07-1775	Prepare and submit roof specialties Samples	55	19-Nov-25	13-Feb-26	170
PR0-07-1330	Review and approve roof specialties product data	15	17-Feb-26	09-Mar-26	170
PR0-07-1770	Review and approve roof specialties Shop Drawings	15	17-Feb-26	09-Mar-26	170
PR0-07-1780	Review and approve roof specialties Samples	15	17-Feb-26	09-Mar-26	170
PR0-07-1785	Prepare and submit roof specialties Mockup	20	10-Mar-26	08-Apr-26	170
PR0-07-1790	Review and approve roof specialties Mockup	15	09-Apr-26	29-Apr-26	170
PR0-07-1060	Fabrication and delivery of roof specialties material	5	30-Apr-26	06-May-26	170
077200 - ROOF ACCESSORIES		52	19-Nov-25	10-Feb-26	228
PR0-07-1430	Prepare and submit roof accessories product data	32	19-Nov-25	09-Jan-26	228
PR0-07-1795	Prepare and submit roof accessories Shop Drawings	32	19-Nov-25	09-Jan-26	228
PR0-07-1420	Review and approve roof accessories product data	15	12-Jan-26	02-Feb-26	228

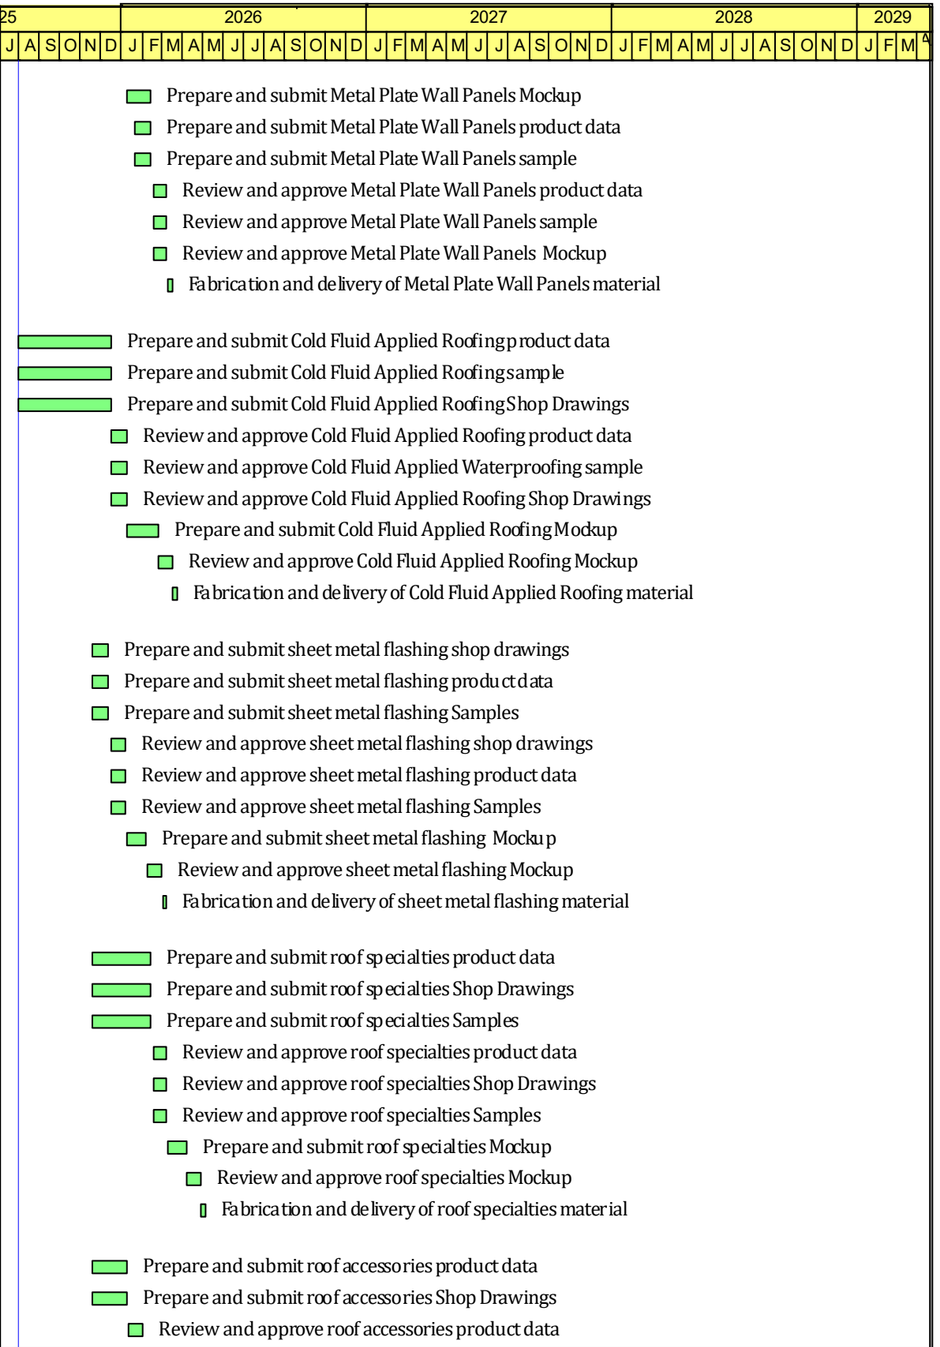

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PR0-07-1800	Review and approve roof accessories Shop Drawings	15	12-Jan-26	02-Feb-26	228
PR0-07-1410	Fabrication and delivery of roof accessories material	5	03-Feb-26	10-Feb-26	228
077273 - VEGETATED ROOF SYSTEMS		40	10-Feb-26	09-Apr-26	189
PR0-07-1555	Prepare and submit Vegetated Roof Systems product data	20	10-Feb-26	10-Mar-26	189
PR0-07-1565	Prepare and submit Vegetated Roof Systems sample	20	10-Feb-26	10-Mar-26	189
PR0-07-1805	Prepare and submit Vegetated Roof Systems Shop Drawings	20	10-Feb-26	10-Mar-26	189
PR0-07-1550	Review and approve Vegetated Roof Systems product data	15	12-Mar-26	01-Apr-26	189
PR0-07-1560	Review and approve Vegetated Roof Systems sample	15	12-Mar-26	01-Apr-26	189
PR0-07-1810	Review and approve Vegetated Roof Systems Shop Drawings	15	12-Mar-26	01-Apr-26	189
PR0-07-1030	Fabrication and delivery of Vegetated Roof Systems material	5	02-Apr-26	09-Apr-26	189
078100 - APPLIED FIRE PROTECTION		82	21-Jan-26	21-May-26	94
PR0-07-1575	Prepare and submit Applied Fire Protection product data	17	21-Jan-26	13-Feb-26	94
PR0-07-1585	Prepare and submit Applied Fire Protection sample	17	21-Jan-26	13-Feb-26	94
PR0-07-1815	Prepare and submit Applied Fire Protection Shop Drawings	17	21-Jan-26	13-Feb-26	94
PR0-07-1570	Review and approve Applied Fire Protection product data	15	17-Feb-26	09-Mar-26	94
PR0-07-1580	Review and approve Applied Fire Protection sample	15	17-Feb-26	09-Mar-26	94
PR0-07-1820	Review and approve Applied Fire Protection Shop Drawings	15	17-Feb-26	09-Mar-26	94
PR0-07-1825	Prepare and submit Applied Fire Protection Mockup	30	10-Mar-26	22-Apr-26	94
PR0-07-1830	Review and approve Applied Fire Protection Mockup	15	23-Apr-26	14-May-26	94
PR0-07-1035	Fabrication and delivery of Applied Fire Protection material	5	15-May-26	21-May-26	94
078413 - PENETRATION FIRESTOPPING		145	01-Aug-25	12-Mar-26	153
PR0-07-1945	Prepare and submit firestopping product data-Mason	129	01-Aug-25	17-Feb-26	153
PR0-07-1950	Prepare and submit firestopping product data-Concrete	129	01-Aug-25	17-Feb-26	138
PR0-07-1350	Prepare and submit firestopping product data-HVAC	84	09-Oct-25	17-Feb-26	153
PR0-07-1380	Prepare and submit firestopping product data-Electrical	84	09-Oct-25	17-Feb-26	153
PR0-07-1850	Prepare and submit firestopping product data-Plumbing	69	30-Oct-25	17-Feb-26	153
PR0-07-1865	Prepare and submit firestopping product data-Sprinkler	69	30-Oct-25	17-Feb-26	153
PR0-07-1880	Prepare and submit firestopping product data-Elevator	69	30-Oct-25	17-Feb-26	153
PR0-07-1895	Prepare and submit firestopping product data-Carpentry	55	19-Nov-25	13-Feb-26	154
PR0-07-1930	Prepare and submit firestopping product data-Roofer	55	19-Nov-25	13-Feb-26	154
PR0-07-1940	Prepare and submit firestopping product data-Steel	55	19-Nov-25	13-Feb-26	128
PR0-07-1910	Prepare and submit firestopping product data-Storefront	36	22-Dec-25	13-Feb-26	154
PR0-07-1935	Prepare and submit firestopping product data-Millwork	36	22-Dec-25	13-Feb-26	154
PR0-07-1925	Prepare and submit firestopping product data-Vegetated Garden	4	10-Feb-26	13-Feb-26	154
PR0-07-1900	Review and approve firestopping product data-Carpentry	15	17-Feb-26	09-Mar-26	154
PR0-07-1915	Review and approve firestopping product data-Storefront	15	17-Feb-26	09-Mar-26	154
PR0-07-1955	Review and approve firestopping product data-Vegetated Garden	15	17-Feb-26	09-Mar-26	154
PR0-07-1960	Review and approve firestopping product data-Roofer	15	17-Feb-26	09-Mar-26	154
PR0-07-1965	Review and approve firestopping product data-Millwork	15	17-Feb-26	09-Mar-26	154
PR0-07-1970	Review and approve firestopping product data-Steel	15	17-Feb-26	09-Mar-26	128
PR0-07-2015	Prepare and submit firestopping product data-Storefront	0	17-Feb-26	17-Feb-26	154
PR0-07-2020	Review and approve firestopping product data-Signage	15	17-Feb-26	09-Mar-26	154

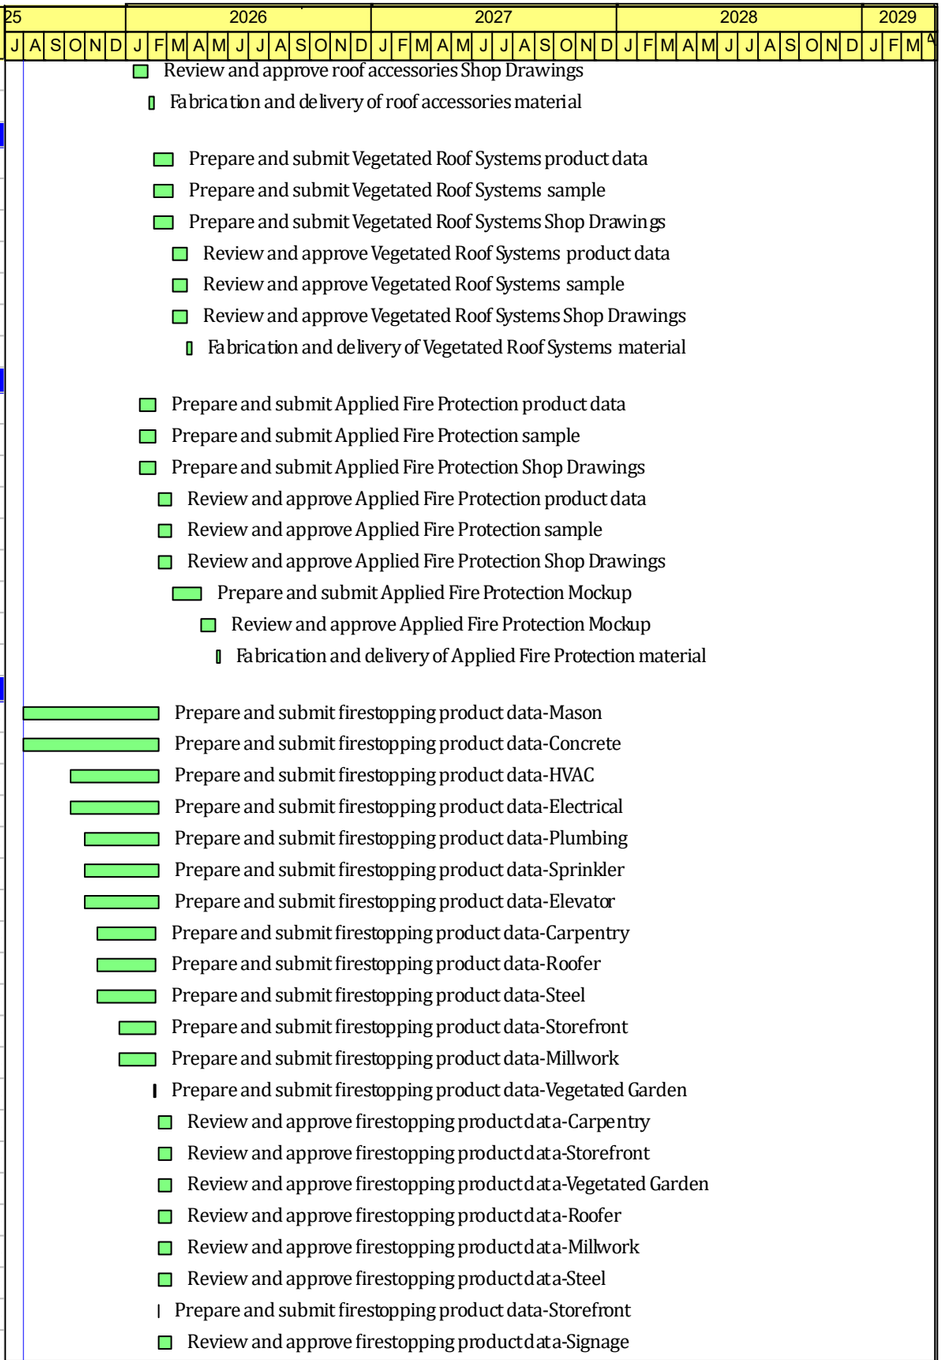

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PR0-07-1360	Review and approve firestopping product data-Electrical	15	18-Feb-26	10-Mar-26	153
PR0-07-1370	Review and approve firestopping product data-HVAC	15	18-Feb-26	10-Mar-26	153
PR0-07-1855	Review and approve firestopping product data-Plumbing	15	18-Feb-26	10-Mar-26	153
PR0-07-1870	Review and approve firestopping product data-Sprinkler	15	18-Feb-26	10-Mar-26	153
PR0-07-1885	Review and approve firestopping product data-Elevator	15	18-Feb-26	10-Mar-26	153
PR0-07-1975	Review and approve firestopping product data-Mason	15	18-Feb-26	10-Mar-26	153
PR0-07-1980	Review and approve firestopping product data-Concrete	15	18-Feb-26	10-Mar-26	138
PR0-07-1905	Fabrication and delivery of firestopping Carpentry	1	10-Mar-26	10-Mar-26	154
PR0-07-1920	Fabrication and delivery of firestopping-Storefront	1	10-Mar-26	10-Mar-26	154
PR0-07-1985	Fabrication and delivery of firestopping Vegetated Garden	1	10-Mar-26	10-Mar-26	154
PR0-07-1990	Fabrication and delivery of firestopping Roofer	1	10-Mar-26	10-Mar-26	154
PR0-07-1995	Fabrication and delivery of firestopping Millwork	1	10-Mar-26	10-Mar-26	154
PR0-07-2000	Fabrication and delivery of firestopping Steel	1	10-Mar-26	10-Mar-26	128
PR0-07-2025	Fabrication and delivery of firestopping-Signage	1	10-Mar-26	10-Mar-26	154
PR0-07-1070	Fabrication and delivery of firestopping HVAC	1	12-Mar-26	12-Mar-26	153
PR0-07-1845	Fabrication and delivery of firestopping-Electrical	1	12-Mar-26	12-Mar-26	153
PR0-07-1860	Fabrication and delivery of firestopping Plumbing	1	12-Mar-26	12-Mar-26	153
PR0-07-1875	Fabrication and delivery of firestopping Sprinkler	1	12-Mar-26	12-Mar-26	153
PR0-07-1890	Fabrication and delivery of firestopping Elevator	1	12-Mar-26	12-Mar-26	153
PR0-07-2005	Fabrication and delivery of firestopping Mason	1	12-Mar-26	12-Mar-26	153
PR0-07-2010	Fabrication and delivery of firestopping-Concrete	1	12-Mar-26	12-Mar-26	138
079200 - JOINT SEALERS		159	01-Aug-25	01-Apr-26	184
PR0-07-2400	Prepare and submit joint sealers product data-Caulking	143	01-Aug-25	09-Mar-26	184
PR0-07-2420	Prepare and submit joint sealers Samples-Caulking	143	01-Aug-25	09-Mar-26	184
PR0-07-2440	Prepare and submit joint sealers Schedule-Caulking	143	01-Aug-25	09-Mar-26	184
PR0-07-2390	Review and approve joint sealer product data-Caulking	15	10-Mar-26	31-Mar-26	184
PR0-07-2410	Review and approve joint sealer Samples-Caulking	15	10-Mar-26	31-Mar-26	184
PR0-07-2430	Review and approve joint sealer product data-Caulking	15	10-Mar-26	31-Mar-26	184
PR0-07-2380	Fabrication and delivery of joint sealer material-Caulking	1	01-Apr-26	01-Apr-26	184
079219 - ACOUSTICAL JOINT SEALANTS		159	01-Aug-25	01-Apr-26	278
PR0-07-1400	Prepare and submit Acoustical Joint sealers product data-Caulking	143	01-Aug-25	09-Mar-26	278
PR0-07-2215	Prepare and submit Acoustical Joint sealers Samples-Caulking	143	01-Aug-25	09-Mar-26	278
PR0-07-2225	Prepare and submit Acoustical Joint sealers Schedule-Caulking	143	01-Aug-25	09-Mar-26	278
PR0-07-1390	Review and approve Acoustical Joint sealer product data-Caulking	15	10-Mar-26	31-Mar-26	278
PR0-07-2220	Review and approve Acoustical Joint sealer Samples-Caulking	15	10-Mar-26	31-Mar-26	278
PR0-07-2230	Review and approve Acoustical Joint sealer product data-Caulking	15	10-Mar-26	31-Mar-26	278
PR0-07-1080	Fabrication and delivery of Acoustical Joint sealer material-Caulking	1	01-Apr-26	01-Apr-26	278
DIVISION 8 - OPENINGS		236	01-Aug-25	24-Jul-26	113
080152.91 - WOOD WINDOWS RESTORATION		104	01-Aug-25	08-Jan-26	144
PR0-08-1430	Prepare and submit Wood Window Restoration Samples	89	01-Aug-25	16-Dec-25	144
PR0-08-1440	Prepare and submit Wood Window Restoration product data	89	01-Aug-25	16-Dec-25	144
PR0-08-1425	Review and approve Wood Window Restoration samples	15	17-Dec-25	08-Jan-26	144

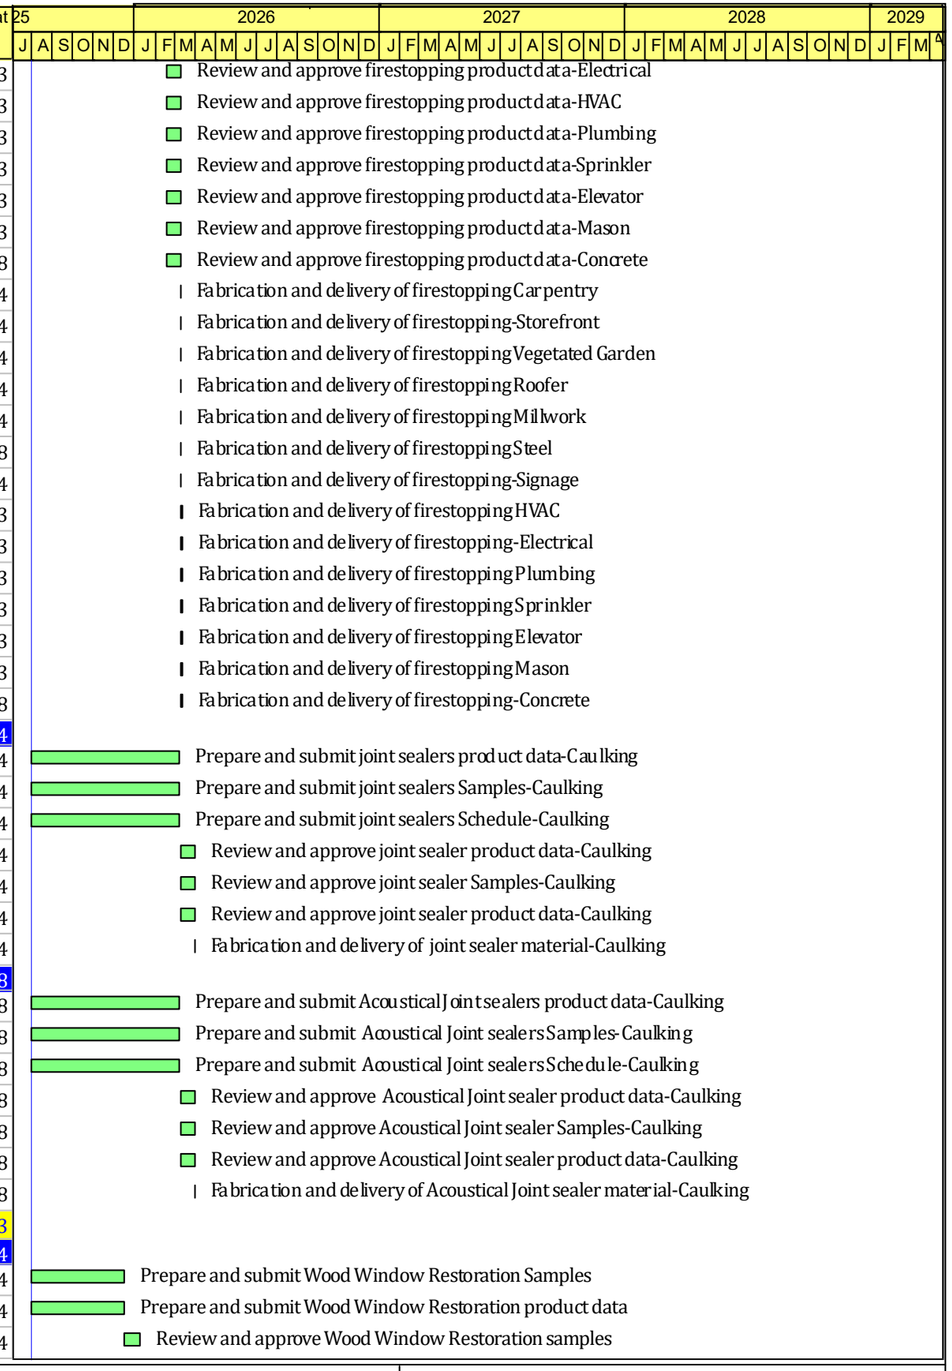

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PR0-08-1435	Review and approve Wood Window Restoration product data	15	17-Dec-25	08-Jan-26	144
081113 - HOLLOW METAL DOORS AND FRAMES		75	03-Dec-25	26-Mar-26	194
PR0-08-1020	Prepare and submit Hollow doors and frames shop drawings	60	03-Dec-25	04-Mar-26	194
PR0-08-1040	Prepare and submit Hollow doors and frames product data	60	03-Dec-25	04-Mar-26	194
PR0-08-1010	Review and approve Hollow doors and frames shop drawings	15	05-Mar-26	26-Mar-26	194
PR0-08-1030	Review and approve Hollow doors and frames product data	15	05-Mar-26	26-Mar-26	194
083113 - ACCESS DOORS AND FRAMES		75	03-Dec-25	26-Mar-26	68
PR0-08-1140	Prepare and submit access doors shop drawings	60	03-Dec-25	04-Mar-26	68
PR0-08-1160	Prepare and submit access doors product data	60	03-Dec-25	04-Mar-26	68
PR0-08-1130	Review and approve access doors shop drawings	15	05-Mar-26	26-Mar-26	68
PR0-08-1150	Review and approve access doors product data	15	05-Mar-26	26-Mar-26	68
084213 - ALUMINUM FRAMED ENTRANCE AND STOREFRONT		28	22-Dec-25	02-Feb-26	123
PR0-08-1180	Prepare and submit aluminum entrance and storefront shop drawings	13	22-Dec-25	09-Jan-26	123
PR0-08-1200	Prepare and submit aluminum entrance and storefront product data	13	22-Dec-25	09-Jan-26	123
PR0-08-1485	Prepare and submit aluminum entrance and storefront Sample	13	22-Dec-25	09-Jan-26	123
PR0-08-1170	Review and approve aluminum entrance and storefront shop drawings	15	12-Jan-26	02-Feb-26	123
PR0-08-1190	Review and approve aluminum entrance and storefront product data	15	12-Jan-26	02-Feb-26	123
PR0-08-1490	Review and approve aluminum entrance and storefront Sample	15	12-Jan-26	02-Feb-26	123
084223 - FIRE RATED ALUMINUM FRAMED ENTRANCE AND STOREFRONT		28	22-Dec-25	02-Feb-26	123
PR0-08-1650	Prepare and submit aluminum entrance and storefront shop drawings	13	22-Dec-25	09-Jan-26	123
PR0-08-1670	Prepare and submit aluminum entrance and storefront product data	13	22-Dec-25	09-Jan-26	123
PR0-08-1690	Prepare and submit aluminum entrance and storefront Sample	13	22-Dec-25	09-Jan-26	123
PR0-08-1640	Review and approve aluminum entrance and storefront shop drawings	15	12-Jan-26	02-Feb-26	123
PR0-08-1660	Review and approve aluminum entrance and storefront product data	15	12-Jan-26	02-Feb-26	123
PR0-08-1680	Review and approve aluminum entrance and storefront Sample	15	12-Jan-26	02-Feb-26	123
084225 - ALLL GLASS ENTRANCE AND STOREFRONT		28	22-Dec-25	02-Feb-26	123
PR0-08-1710	Prepare and submit aluminum entrance and storefront shop drawings	13	22-Dec-25	09-Jan-26	123
PR0-08-1730	Prepare and submit aluminum entrance and storefront product data	13	22-Dec-25	09-Jan-26	123
PR0-08-1750	Prepare and submit aluminum entrance and storefront Sample	13	22-Dec-25	09-Jan-26	123
PR0-08-1700	Review and approve aluminum entrance and storefront shop drawings	15	12-Jan-26	02-Feb-26	123
PR0-08-1720	Review and approve aluminum entrance and storefront product data	15	12-Jan-26	02-Feb-26	123
PR0-08-1740	Review and approve aluminum entrance and storefront Sample	15	12-Jan-26	02-Feb-26	123
084423 - STRUCTURAL SEALANT GLAZED CURTAIN WALLS		62	03-Dec-25	06-Mar-26	106
PR0-08-1220	Prepare and submit Structural Sealant Glazed Curtain Walls Product Data	12	03-Dec-25	19-Dec-25	106
PR0-08-1240	Prepare and submit Structural Sealant Glazed Curtain Walls Samples	12	03-Dec-25	19-Dec-25	106
PR0-08-1495	Prepare and submit Structural Sealant Glazed Curtain Walls Shop Drawings	12	03-Dec-25	19-Dec-25	106
PR0-08-1210	Review and approve Structural Sealant Glazed Curtain Walls Product Data	15	22-Dec-25	13-Jan-26	106
PR0-08-1230	Review and approve Structural Sealant Glazed Curtain Walls Samples	15	22-Dec-25	13-Jan-26	106
PR0-08-1505	Review and approve Structural Sealant Glazed Curtain Walls Shop Drawings	15	22-Dec-25	13-Jan-26	106
PR0-08-1500	Prepare and submit Structural Sealant Glazed Curtain Walls Mockup	20	14-Jan-26	12-Feb-26	106
PR0-08-1510	Review and approve Structural Sealant Glazed Curtain Walls Mockup	15	13-Feb-26	06-Mar-26	106
085113 - ALUMINUM WINDOWS		236	01-Aug-25	24-Jul-26	57

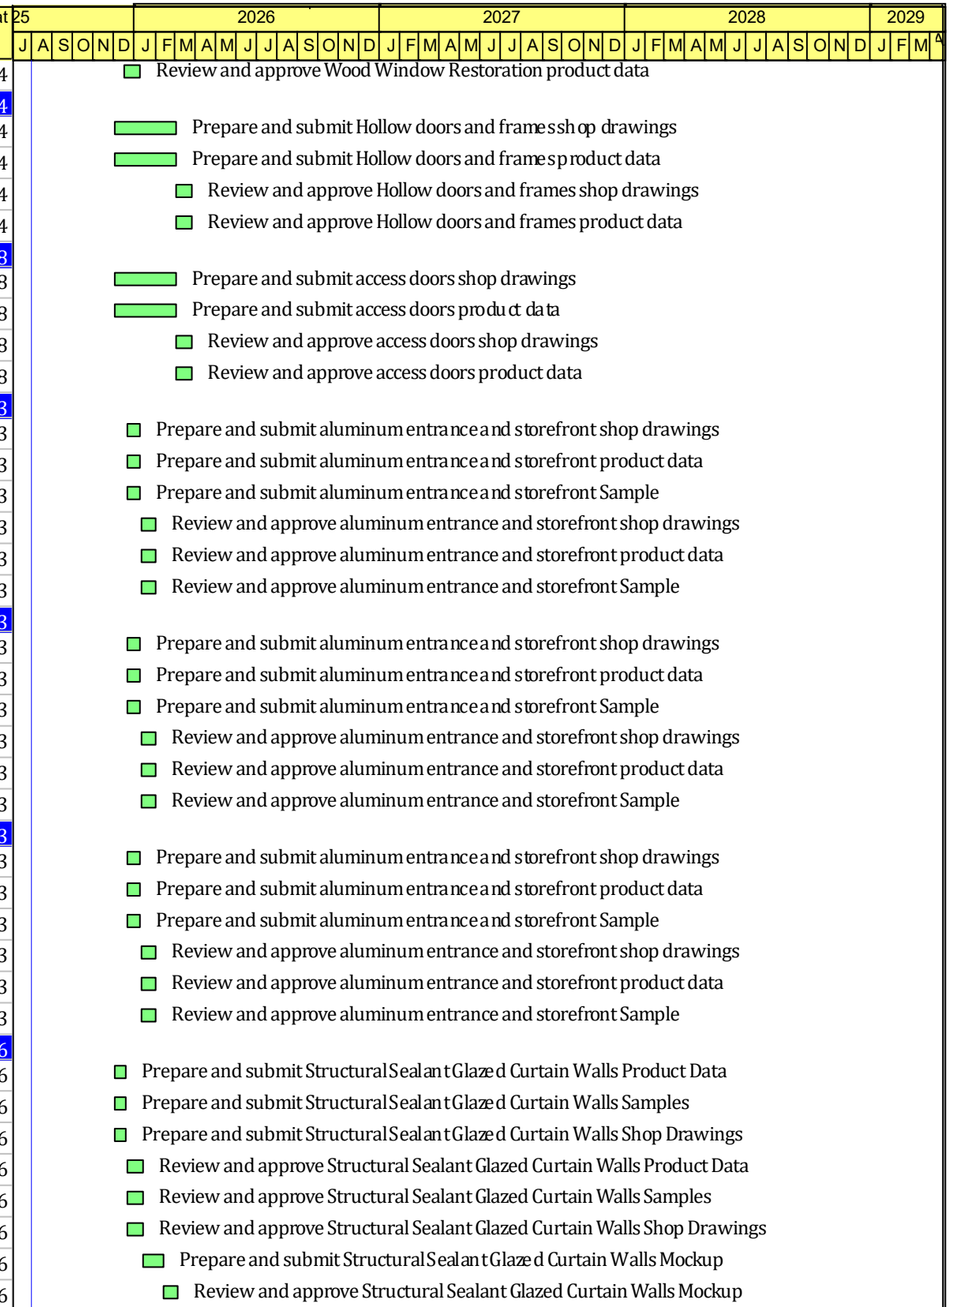

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PR0-08-1410	Prepare and submit Aluminum Windows shop drawings	106	01-Aug-25	12-Jan-26	57
PR0-08-1420	Prepare and submit Aluminum Windows product data	106	01-Aug-25	12-Jan-26	57
PR0-08-1465	Prepare and submit Aluminum Windows Samples	106	01-Aug-25	12-Jan-26	57
PR0-08-1405	Review and approve Aluminum Windows shop drawings	15	13-Jan-26	03-Feb-26	57
PR0-08-1415	Review and approve Aluminum Windows product data	15	13-Jan-26	03-Feb-26	57
PR0-08-1475	Review and approve Aluminum Windows Samples	15	13-Jan-26	03-Feb-26	57
PR0-08-1470	Prepare and submit Aluminum Windows Mockup	100	05-Feb-26	02-Jul-26	57
PR0-08-1480	Review and approve Aluminum Windows Mockup	15	03-Jul-26	24-Jul-26	57
087100 - DOOR HARDWARE		75	03-Dec-25	26-Mar-26	194
PR0-08-1340	Prepare and submit door hardware shop drawings	60	03-Dec-25	04-Mar-26	194
PR0-08-1360	Prepare and submit door hardware product data	60	03-Dec-25	04-Mar-26	194
PR0-08-1515	Prepare and submit door hardware sample	60	03-Dec-25	04-Mar-26	194
PR0-08-1330	Review and approve door hardware shop drawings	15	05-Mar-26	26-Mar-26	194
PR0-08-1350	Review and approve door hardware product data	15	05-Mar-26	26-Mar-26	194
PR0-08-1520	Review and approve door hardware sample	15	05-Mar-26	26-Mar-26	194
088000 - GLAZING		110	03-Dec-25	18-May-26	157
PR0-08-1380	Prepare and submit glass and glazing shop drawings	60	03-Dec-25	04-Mar-26	157
PR0-08-1400	Prepare and submit glass and glazing product data	60	03-Dec-25	04-Mar-26	157
PR0-08-1535	Prepare and submit glass and glazing sample	60	03-Dec-25	04-Mar-26	157
PR0-08-1370	Review and approve glass and glazing shop drawings	15	05-Mar-26	26-Mar-26	157
PR0-08-1390	Review and approve glass and glazing product data	15	05-Mar-26	26-Mar-26	157
PR0-08-1545	Review and approve glass and glazing sample	15	05-Mar-26	26-Mar-26	157
PR0-08-1540	Prepare and submit glass and glazing mockup	20	27-Mar-26	24-Apr-26	157
PR0-08-1550	Review and approve glass and glazing mockup	15	27-Apr-26	18-May-26	157
088813 - FIRE-RATED GLAZING		110	03-Dec-25	18-May-26	157
PR0-08-1570	Prepare and submit glass and glazing shop drawings	60	03-Dec-25	04-Mar-26	157
PR0-08-1590	Prepare and submit glass and glazing product data	60	03-Dec-25	04-Mar-26	157
PR0-08-1610	Prepare and submit glass and glazing sample	60	03-Dec-25	04-Mar-26	157
PR0-08-1560	Review and approve glass and glazing shop drawings	15	05-Mar-26	26-Mar-26	157
PR0-08-1580	Review and approve glass and glazing product data	15	05-Mar-26	26-Mar-26	157
PR0-08-1600	Review and approve glass and glazing sample	15	05-Mar-26	26-Mar-26	157
PR0-08-1630	Prepare and submit glass and glazing mockup	20	27-Mar-26	24-Apr-26	157
PR0-08-1620	Review and approve glass and glazing mockup	15	27-Apr-26	18-May-26	157
DIVISION 9 - FINISHES		171	19-Nov-25	05-Aug-26	203
092116,23 - GYPSUM DRYWALL SHAFT WALL ASSEMBLIES		76	19-Nov-25	18-Mar-26	149
PR0-09-1275	Prepare and submit gypsum drywall Shaft Wall Assemblies product data	60	19-Nov-25	23-Feb-26	149
PR0-09-1270	Review and approve gypsum drywall Shaft Wall Assemblies product data	15	24-Feb-26	17-Mar-26	149
PR0-09-1265	Fabrication and delivery of gypsum drywall Shaft Wall Assemblies	1	18-Mar-26	18-Mar-26	149
092216 - NON-STRUCTURAL METAL FRAMING		76	19-Nov-25	18-Mar-26	149
PR0-09-1290	Prepare and submit Non-Structural Metal Framing product data	60	19-Nov-25	23-Feb-26	149
PR0-09-1285	Review and approve Non-Structural Metal Framing product data	15	24-Feb-26	17-Mar-26	149
PR0-09-1280	Fabrication and delivery of Non-Structural Metal Framing	1	18-Mar-26	18-Mar-26	149

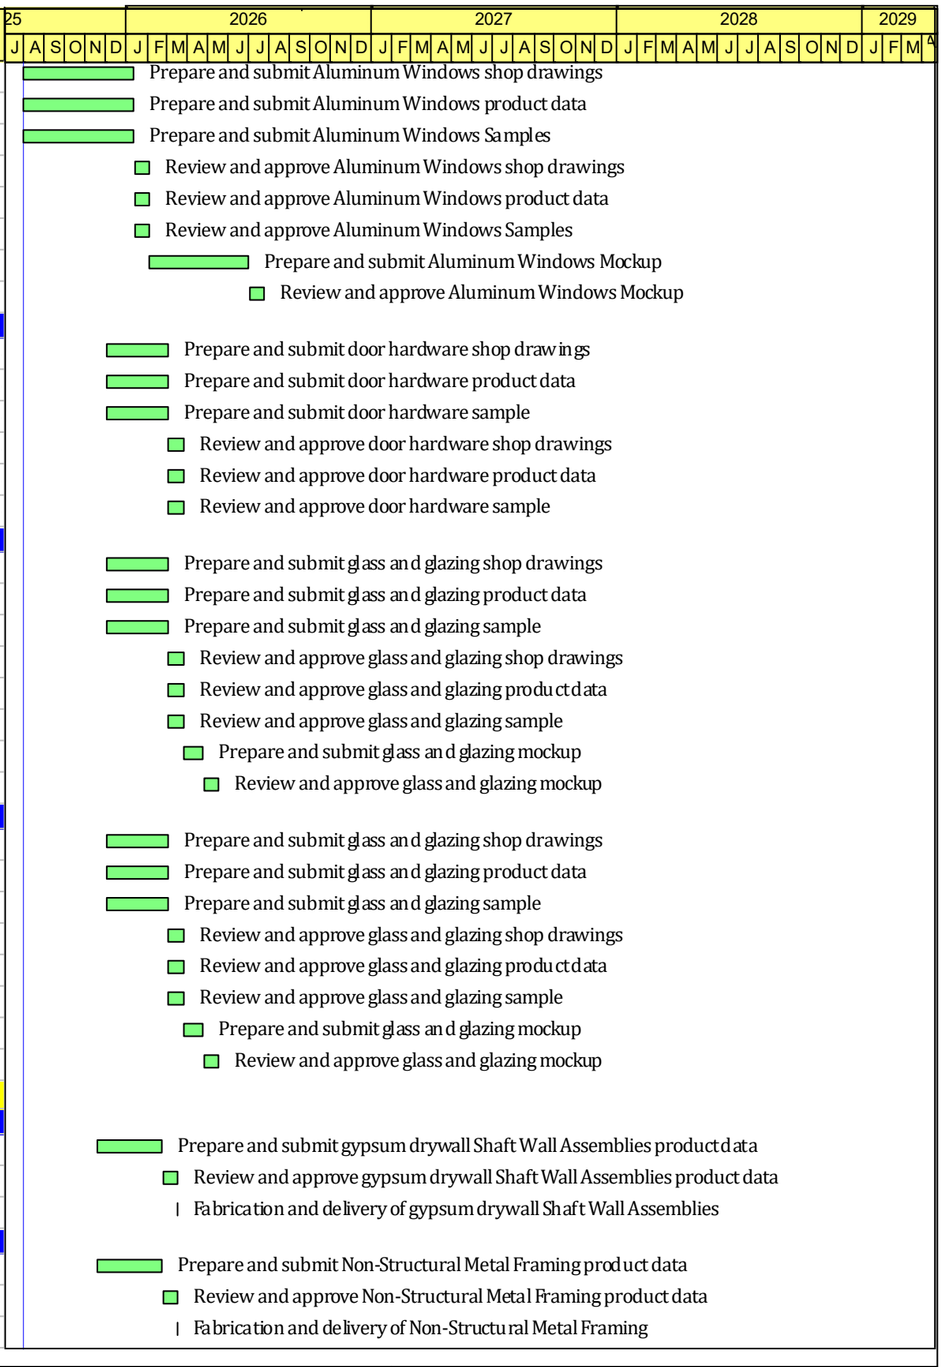

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
092313 - ACOUSTICAL GYPSUM PLASTERING		66	19-Nov-25	03-Mar-26	298
PR0-09-1100	Prepare and submit Acoustical Gypsum Plastering product data	15	19-Nov-25	12-Dec-25	298
PR0-09-1310	Prepare and submit Acoustical Gypsum Plastering sample	15	19-Nov-25	12-Dec-25	298
PR0-09-1090	Review and approve Acoustical Gypsum Plastering product data	15	16-Dec-25	07-Jan-26	298
PR0-09-1315	Review and approveAcoustical Gypsum Plastering sample	15	16-Dec-25	07-Jan-26	298
PR0-09-1320	Prepare and submit Acoustical Gypsum Plastering mockup	20	08-Jan-26	06-Feb-26	298
PR0-09-1325	Review and approve Acoustical Gypsum Plastering mockup	15	09-Feb-26	02-Mar-26	298
PR0-09-1010	Fabrication and delivery of Acoustical Gypsum Plastering	1	03-Mar-26	03-Mar-26	298
092900 - GYPSUM DRYWALL		66	19-Nov-25	03-Mar-26	228
PR0-09-1485	Prepare and submit gypsum drywall product data	15	19-Nov-25	12-Dec-25	228
PR0-09-1505	Prepare and submit gypsum drywall sample	15	19-Nov-25	12-Dec-25	228
PR0-09-1475	Review and approve gypsum drywall product data	15	16-Dec-25	07-Jan-26	228
PR0-09-1495	Review and approve gypsum drywall sample	15	16-Dec-25	07-Jan-26	228
PR0-09-1525	Prepare and submit gypsum drywall mockup	20	08-Jan-26	06-Feb-26	228
PR0-09-1515	Review and approve gypsum drywall mockup	15	09-Feb-26	02-Mar-26	228
PR0-09-1465	Fabrication and delivery of gypsum drywall	1	03-Mar-26	03-Mar-26	228
093013 - CERAMIC TILING		66	19-Nov-25	03-Mar-26	301
PR0-09-1305	Prepare and submit Ceramic Tiling product data	15	19-Nov-25	12-Dec-25	301
PR0-09-1330	Prepare and submit Ceramic Tiling Samples	15	19-Nov-25	12-Dec-25	301
PR0-09-1300	Review and approve Ceramic Tiling product data	15	16-Dec-25	07-Jan-26	301
PR0-09-1335	Review and approve Ceramic Tiling samples	15	16-Dec-25	07-Jan-26	301
PR0-09-1340	Prepare and submit Ceramic Tiling Mockup	20	08-Jan-26	06-Feb-26	301
PR0-09-1345	Review and approve Ceramic Tiling Mockup	15	09-Feb-26	02-Mar-26	301
PR0-09-1295	Fabrication and delivery of Ceramic Tiling	1	03-Mar-26	03-Mar-26	301
095113 - ACOUSTICAL PANEL CEILINGS		171	19-Nov-25	05-Aug-26	193
PR0-09-1120	Prepare and submit acoustical panel ceilings product data	27	19-Nov-25	02-Jan-26	277
PR0-09-1350	Prepare and submit acoustical panel ceilings Samples	27	19-Nov-25	02-Jan-26	277
PR0-09-1110	Review and approve acoustical panel ceilings product data	15	05-Jan-26	26-Jan-26	277
PR0-09-1355	Review and approve acoustical panel ceilings sample	15	05-Jan-26	26-Jan-26	277
PR0-09-1360	Prepare and submit acoustical panel ceilings Mockup	20	02-Jun-26	30-Jun-26	193
PR0-09-1365	Review and approve acoustical panel ceilings mockup	15	01-Jul-26	22-Jul-26	193
PR0-09-1020	Fabrication and delivery of acoustical panel ceilings	10	23-Jul-26	05-Aug-26	193
095133 - ACOUSTICAL METAL PAN CEILINGS		105	19-Nov-25	29-Apr-26	269
PR0-09-1555	Prepare and submit Acoustical Metal Pan Ceilings product data	55	19-Nov-25	13-Feb-26	269
PR0-09-1575	Prepare and submit Acoustical Metal Pan Ceilings Samples	55	19-Nov-25	13-Feb-26	269
PR0-09-1545	Review and approve Acoustical Metal Pan Ceilings product data	15	17-Feb-26	09-Mar-26	269
PR0-09-1565	Review and approve Acoustical Metal Pan Ceilings sample	15	17-Feb-26	09-Mar-26	269
PR0-09-1595	Prepare and submit Acoustical Metal Pan Ceilings Mockup	20	10-Mar-26	08-Apr-26	269
PR0-09-1585	Review and approve Acoustical Metal Pan Ceilings mockup	15	09-Apr-26	29-Apr-26	269
099123 - INTERIOR PAINTING		120	10-Feb-26	05-Aug-26	197
PR0-09-1635	Prepare and submit Interior paint product data	60	10-Feb-26	07-May-26	193
PR0-09-1645	Review and approve Interior paint product data	15	08-May-26	01-Jun-26	193



Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PR0-09-1655	Fabrication and delivery of Interior paint	10	23-Jul-26	05-Aug-26	197
DIVISION 10 - SPECIALTIES		186	01-Aug-25	11-May-26	288
101423 - PANEL SIGNAGE		39	17-Feb-26	14-Apr-26	307
PRO-10-1000	Prepare and submit signage sample	14	17-Feb-26	06-Mar-26	307
PRO-10-1010	Prepare and submit signage product data	14	17-Feb-26	06-Mar-26	307
PRO-10-1040	Prepare and submit signage shop drawings	14	17-Feb-26	06-Mar-26	307
PRO-10-1020	Review and approve signage sample	15	09-Mar-26	30-Mar-26	307
PRO-10-1030	Review and approve signage product data	15	09-Mar-26	30-Mar-26	307
PRO-10-1050	Review and approve signage shop drawings	15	09-Mar-26	30-Mar-26	307
PR0-10-1460	Fabrication and delivery of signage	10	31-Mar-26	14-Apr-26	307
102219 - DEMOUNTABLE PARTITIONS		108	30-Oct-25	15-Apr-26	236
PRO-10-1420	Prepare and submit Demountable Partitions product data	83	30-Oct-25	09-Mar-26	236
PRO-10-1440	Prepare and submit Demountable Partitions Shop Drawings	83	30-Oct-25	09-Mar-26	236
PRO-10-1410	Review and approve Demountable Partitions productdata	15	10-Mar-26	31-Mar-26	236
PRO-10-1430	Review and approveDemountable Partitions Shop Drawings	15	10-Mar-26	31-Mar-26	236
PR0-10-1540	Fabrication and delivery of Demountable Partitions	10	01-Apr-26	15-Apr-26	236
102800 - TOILET,BATH AND LAUNDRY ACCESSORIES		41	13-Mar-26	11-May-26	287
PRO-10-1240	Prepare and submit toilet, Bath and Laundry accessories product data	16	13-Mar-26	03-Apr-26	287
PRO-10-1365	Prepare and submit toilet, Bath and Laundry accessories Sample	16	13-Mar-26	03-Apr-26	287
PRO-10-1375	Prepare and submit toilet, Bath and Laundry ProductSchedule	16	13-Mar-26	03-Apr-26	287
PRO-10-1260	Review and approve toilet, Bath and Laundry product data	15	06-Apr-26	27-Apr-26	287
PRO-10-1370	Review and approve toilet, Bath and Laundry Sample	15	06-Apr-26	27-Apr-26	287
PRO-10-1380	Review and approve toilet, Bath and Laundry Product Schedule	15	06-Apr-26	27-Apr-26	287
PR0-10-1500	Fabrication and delivery of toilet, Bath and Laundry	10	28-Apr-26	11-May-26	287
104413 - FIRE PROTECTION CABINETS		53	30-Oct-25	22-Jan-26	359
PRO-10-1330	Prepare and submit fireprotection cabinets product data	28	30-Oct-25	12-Dec-25	359
PRO-10-1355	Prepare and submit fireprotection cabinets Shop Drawings	28	30-Oct-25	12-Dec-25	359
PRO-10-1320	Review and approve fire protection cabinets product data	15	16-Dec-25	07-Jan-26	359
PRO-10-1360	Review and approve fire protection cabinets Shop Drawings	15	16-Dec-25	07-Jan-26	359
PR0-10-1530	Fabrication and delivery of fire protection cabinets	10	08-Jan-26	22-Jan-26	359
108316 - BANNERS		163	01-Aug-25	08-Apr-26	180
PRO-10-1290	Prepare and submit Banners product data	143	01-Aug-25	09-Mar-26	180
PRO-10-1395	Prepare and submit Banners Shop Drawings	143	01-Aug-25	09-Mar-26	180
PRO-10-1310	Review and approve Banners product data	15	10-Mar-26	31-Mar-26	180
PRO-10-1400	Review and approve Banners Shop Drawings	15	10-Mar-26	31-Mar-26	180
PR0-10-1520	Fabrication and delivery of Banners	5	01-Apr-26	08-Apr-26	180
DIVISION 11 - EQUIPMENT		177	01-Aug-25	28-Apr-26	248
115123.13 - METAL LIBRARY SHELVING		177	01-Aug-25	28-Apr-26	248
PRO-11-1000	Prepare and submit Metal Library Shelving catalog cuts	162	01-Aug-25	06-Apr-26	248
PRO-11-1010	Review and approve Metal Library Shelving catalog cuts	15	08-Apr-26	28-Apr-26	248
DIVISION 12 - FURNISHINGS		81	05-Mar-26	02-Jul-26	132
122200 - CURTAIN AND DRAPES		81	05-Mar-26	02-Jul-26	122
PRO-12-1120	Prepare and submit Curtain and Drapes product data	21	05-Mar-26	03-Apr-26	122

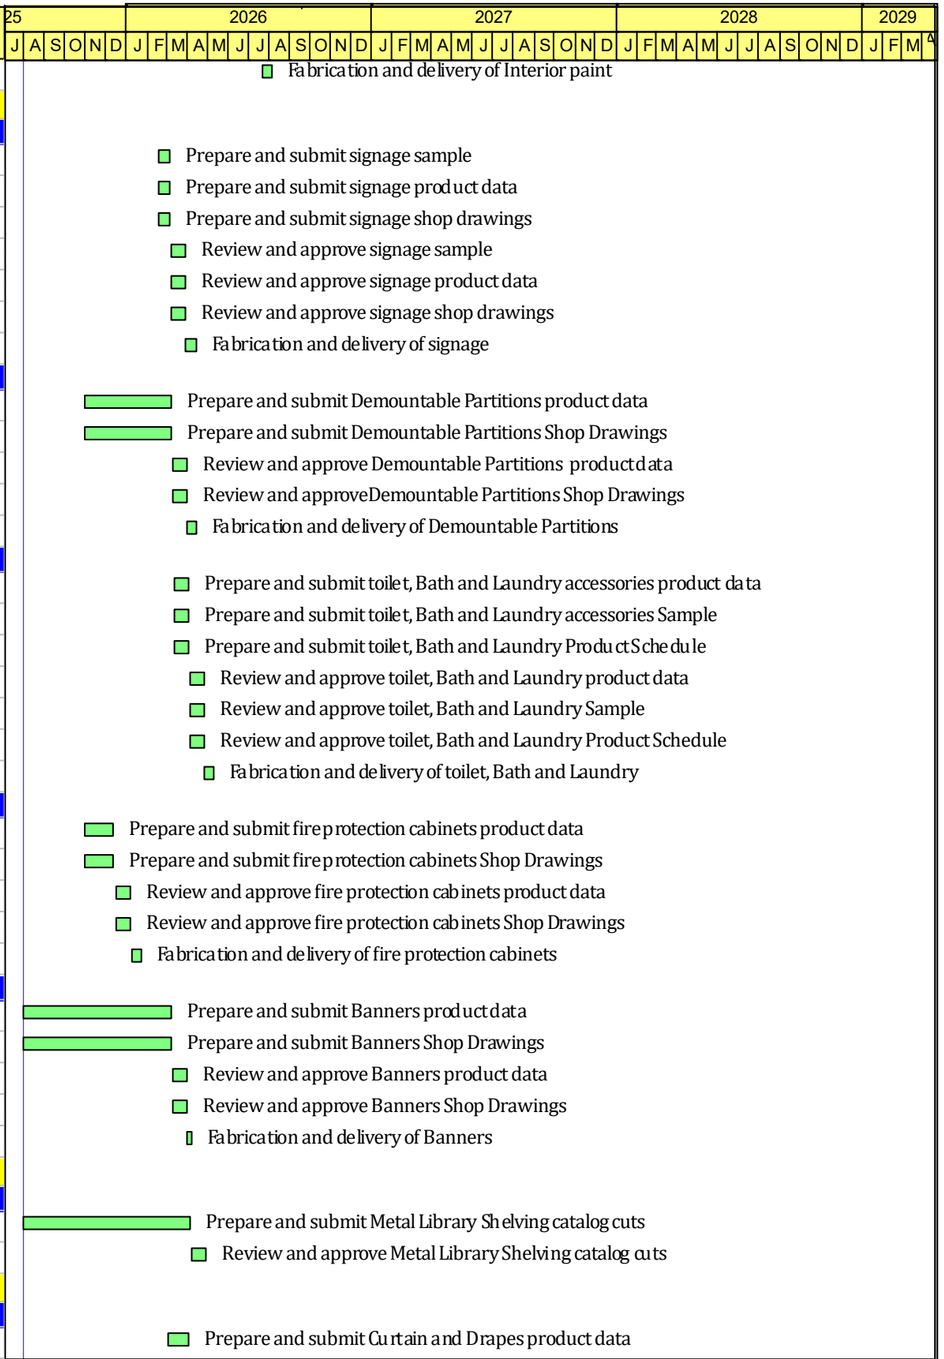

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PRO-12-1160	Prepare and submit Curtain and Drapes Samples	21	05-Mar-26	03-Apr-26	122
PRO-12-1110	Review and approve Curtain and Drapes product data	15	06-Apr-26	27-Apr-26	122
PRO-12-1150	Review and approve Curtain and Drapes Samples	15	06-Apr-26	27-Apr-26	122
PRO-12-1180	Prepare and submit Curtain and Drapes Mockup	20	28-Apr-26	27-May-26	122
PRO-12-1170	Review and approve Curtain and Drapes Mockup	15	28-May-26	18-Jun-26	122
PR0-12-1030	Fabrication and delivery Curtain and Drapes	10	19-Jun-26	02-Jul-26	122
122413 - ROLLER WINDOW SHADES		81	05-Mar-26	02-Jul-26	132
PRO-12-1030	Prepare and submit Roller Window Shades product data	21	05-Mar-26	03-Apr-26	132
PRO-12-1055	Prepare and submit Roller Window Shades Shop Drawings	21	05-Mar-26	03-Apr-26	132
PRO-12-1065	Prepare and submit Roller Window Shades Samples	21	05-Mar-26	03-Apr-26	132
PRO-12-1040	Review and approve Roller Window Shades product data	15	06-Apr-26	27-Apr-26	132
PRO-12-1060	Review and approve Roller Window Shades Shop Drawings	15	06-Apr-26	27-Apr-26	132
PRO-12-1070	Review and approve Roller Window Shades Samples	15	06-Apr-26	27-Apr-26	132
PRO-12-1075	Prepare and submit Roller Window Shades Mockup	20	28-Apr-26	27-May-26	132
PRO-12-1080	Review and approve Roller Window Shades Mockup	15	28-May-26	18-Jun-26	132
PR0-12-1000	Fabrication and delivery Roller Window Shades	10	19-Jun-26	02-Jul-26	132
DIVISION 14 - CONVEYING EQUIPMENT		95	30-Oct-25	26-Mar-26	115
142400 - HYDRAULIC ELEVATOR		95	30-Oct-25	26-Mar-26	115
PRO-14-1000	Prepare and submit Hyrdraulic Elevator product data	80	30-Oct-25	04-Mar-26	115
PRO-14-1010	Prepare and submit Hyrdraulic Elevator shop drawings	80	30-Oct-25	04-Mar-26	115
PRO-14-1020	Review and approve Hyrdraulic Elevator product data	15	05-Mar-26	26-Mar-26	115
PRO-14-1030	Review and approve Hyrdraulic Elevator shop drawings	15	05-Mar-26	26-Mar-26	115
DIVISION 21 - FIRE SUPPRESSION		95	30-Oct-25	26-Mar-26	382
210523 - GENERAL DUTY VALVES FOR FIRE SUPPRESSION PIPING		95	30-Oct-25	26-Mar-26	128
PRO-21-1240	Prepare and submit General Duty Valves for Fire Suppression product data	60	30-Oct-25	02-Feb-26	128
PRO-21-1235	Review and approve General Duty Valves for Fire Suppression product data	15	03-Feb-26	25-Feb-26	128
PR0-21-1135	Fabrication and delivery of General Duty Valves for Fire Suppression	20	26-Feb-26	26-Mar-26	128
210529 - HANGERS & SUPPORTS FOR FIRE SUPPRESSION PIPING & EQUIPMENT		67	30-Oct-25	12-Feb-26	156
PRO-21-1260	Prepare and submit Hangers & Supports for Fire Suppression product data	32	30-Oct-25	19-Dec-25	156
PRO-21-1315	Prepare and submit Hangers & Supports for Fire Suppression Shop Drawings	32	30-Oct-25	19-Dec-25	156
PRO-21-1255	Review and approve Hangers & Supports for Fire Suppression product data	15	22-Dec-25	13-Jan-26	156
PRO-21-1320	Review and approve Hangers & Supports for Fire Suppression Shop Drawings	15	22-Dec-25	13-Jan-26	156
PR0-21-1140	Fabrication and delivery of Hangers & Supports for Fire Suppression	20	14-Jan-26	12-Feb-26	156
210800 - COMMISSIONING OF FIRE SUPPRESSION SYSTEMS		65	30-Oct-25	10-Feb-26	412
PRO-21-1000	Prepare and submit Commission Procedures for Fire Suppression	30	30-Oct-25	17-Dec-25	412
PRO-21-1020	Review and approve Commission Procedures for Fire Suppression	15	18-Dec-25	09-Jan-26	412
PRO-21-1325	Submit Certificate of Completion for Fire Suppression	20	12-Jan-26	10-Feb-26	412
211313 - WET PIPE SPRINKLER SYSTEMS		95	30-Oct-25	26-Mar-26	128
PRO-21-1090	Prepare and submit Wet sprinkler system product data	60	30-Oct-25	02-Feb-26	128
PRO-21-1110	Prepare and submit Wet sprinkler system shop drawings	60	30-Oct-25	02-Feb-26	128
PRO-21-1080	Review and approve Wet sprinkler system product data	15	03-Feb-26	25-Feb-26	128
PRO-21-1100	Review and approve Wet system shop drawings	15	03-Feb-26	25-Feb-26	128

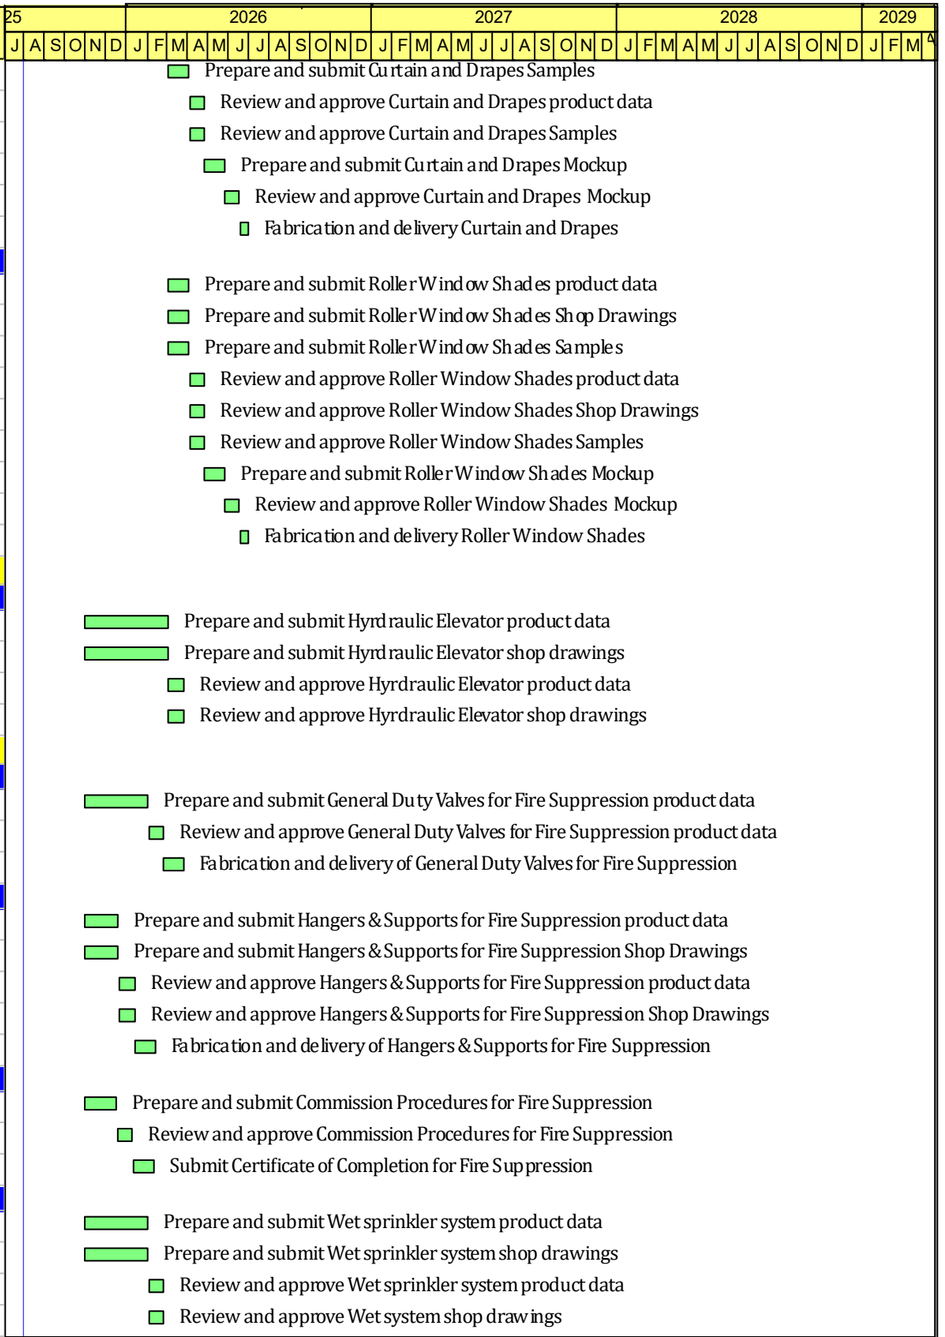

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PR0-21-1100	Fabrication and delivery of Wet sprinkler system	20	26-Feb-26	26-Mar-26	128
213213 - ELECTRIC DRIVE VERTICAL TURBINE FIRE PUMP		75	30-Oct-25	25-Feb-26	196
PRO-21-1040	Prepare and submit Fire Pump product data	60	30-Oct-25	02-Feb-26	196
PRO-21-1050	Prepare and submit Fire Pump shop drawings	60	30-Oct-25	02-Feb-26	196
PRO-21-1060	Review and approve Fire Pump product data	15	03-Feb-26	25-Feb-26	196
PRO-21-1070	Review and approve Fire Pump shop drawings	15	03-Feb-26	25-Feb-26	196
DIVISION 22 - PLUMBING		115	30-Oct-25	24-Apr-26	362
220517 - SLEEVES & SLEEVES SEALS FOR PLUMBING PIPING		75	30-Oct-25	25-Feb-26	148
PRO-22-1045	Prepare and submit Sleeves & Sleeves Seals for Plumbing Piping product data	40	30-Oct-25	02-Jan-26	148
PRO-22-1160	Review and approve Sleeves & Sleeves Seals for Plumbing Piping product data	15	05-Jan-26	26-Jan-26	148
PRO-22-1365	Fabrication and delivery of Sleeves & Sleeves Seals for Plumbing Piping Material	20	27-Jan-26	25-Feb-26	148
220519 - METERS & GUAGES FOR PLUMBING PIPING		75	30-Oct-25	25-Feb-26	148
PRO-22-1425	Prepare and submit Meters & Guages for Plumbing Piping product data	40	30-Oct-25	02-Jan-26	148
PRO-22-1420	Review and approve Meters & Guages for Plumbing Piping product data	15	05-Jan-26	26-Jan-26	148
PRO-22-1415	Fabrication and delivery of Meters & Guages for Plumbing Piping	20	27-Jan-26	25-Feb-26	148
220523.12 - BALL VALVES FOR PLUMBING PIPING		75	30-Oct-25	25-Feb-26	148
PRO-22-1055	Prepare and submit Ball Valves for Plumbing Piping product data	40	30-Oct-25	02-Jan-26	148
PRO-22-1170	Review and approve Ball Valves for Plumbing Piping product data	15	05-Jan-26	26-Jan-26	148
PRO-22-1375	Fabrication and delivery of Ball Valves for Plumbing Piping	20	27-Jan-26	25-Feb-26	148
220523.13 - BUTTERFLY VALVES FOR PLUMBING PIPING		75	30-Oct-25	25-Feb-26	148
PRO-22-1040	Prepare and submit Butterfly Valves for Plumbing Piping product data	40	30-Oct-25	02-Jan-26	148
PRO-22-1155	Review and approve Butterfly Valves for Plumbing Piping product data	15	05-Jan-26	26-Jan-26	148
PRO-22-1360	Fabrication and delivery of Butterfly Valves for Plumbing Piping	20	27-Jan-26	25-Feb-26	148
220523.14 - CHECK VALVES FOR PLUMBING PIPING		75	30-Oct-25	25-Feb-26	241
PRO-22-1075	Prepare and submit Check Valves for Plumbing Piping product data	40	30-Oct-25	02-Jan-26	241
PRO-22-1190	Review and approve Check Valves for Plumbing Piping product data	15	05-Jan-26	26-Jan-26	241
PRO-22-1390	Fabrication and delivery of Check Valves for Plumbing Piping	20	27-Jan-26	25-Feb-26	241
220523.15 - GATE VALVES FOR PLUMBING PIPING		75	30-Oct-25	25-Feb-26	148
PRO-22-1070	Prepare and submit Gate Valves for Plumbing Piping product data	40	30-Oct-25	02-Jan-26	148
PRO-22-1185	Review and approve Gate Valves for Plumbing Piping product data	15	05-Jan-26	26-Jan-26	148
PRO-22-1385	Fabrication and delivery of Gate Valves for Plumbing Piping	20	27-Jan-26	25-Feb-26	148
220529 - HANGERS & SUPPORTS FOR FIRE SUPPRESSION PIPING & EQUIPMENT		75	30-Oct-25	25-Feb-26	246
PRO-22-1080	Prepare and submit Hangers & Supports for Plumbing Piping product data	40	30-Oct-25	02-Jan-26	246
PRO-22-1430	Prepare and submit Hangers & Supports for Plumbing Piping Shop Drawings	40	30-Oct-25	02-Jan-26	246
PRO-22-1195	Review and approve Hangers & Supports for Plumbing Piping product data	15	05-Jan-26	26-Jan-26	246
PRO-22-1435	Review and approve Hangers & Supports for Plumbing Piping Shop Drawings	15	05-Jan-26	26-Jan-26	246
PRO-22-1395	Fabrication and delivery of Hangers & Supports for Plumbing Piping	20	27-Jan-26	25-Feb-26	246
220553 - IDENTIFICATION FOR FIRE SUPPRESSION PIPING		65	30-Oct-25	10-Feb-26	320
PRO-22-1085	Prepare and submit Identification for Plumbing Piping & Equipment product data	30	30-Oct-25	17-Dec-25	320
PRO-22-1450	Prepare and submit Identification for Plumbing Piping & Equipment samples	30	30-Oct-25	17-Dec-25	320
PRO-22-1200	Review and approve Identification for Plumbing Piping & Equipment product data	15	18-Dec-25	09-Jan-26	320
PRO-22-1455	Review and approve Identification for Plumbing Piping & Equipment product samples	15	18-Dec-25	09-Jan-26	320
PRO-22-1400	Fabrication and delivery of Identification for Plumbing Piping & Equipment Tags	20	12-Jan-26	10-Feb-26	320

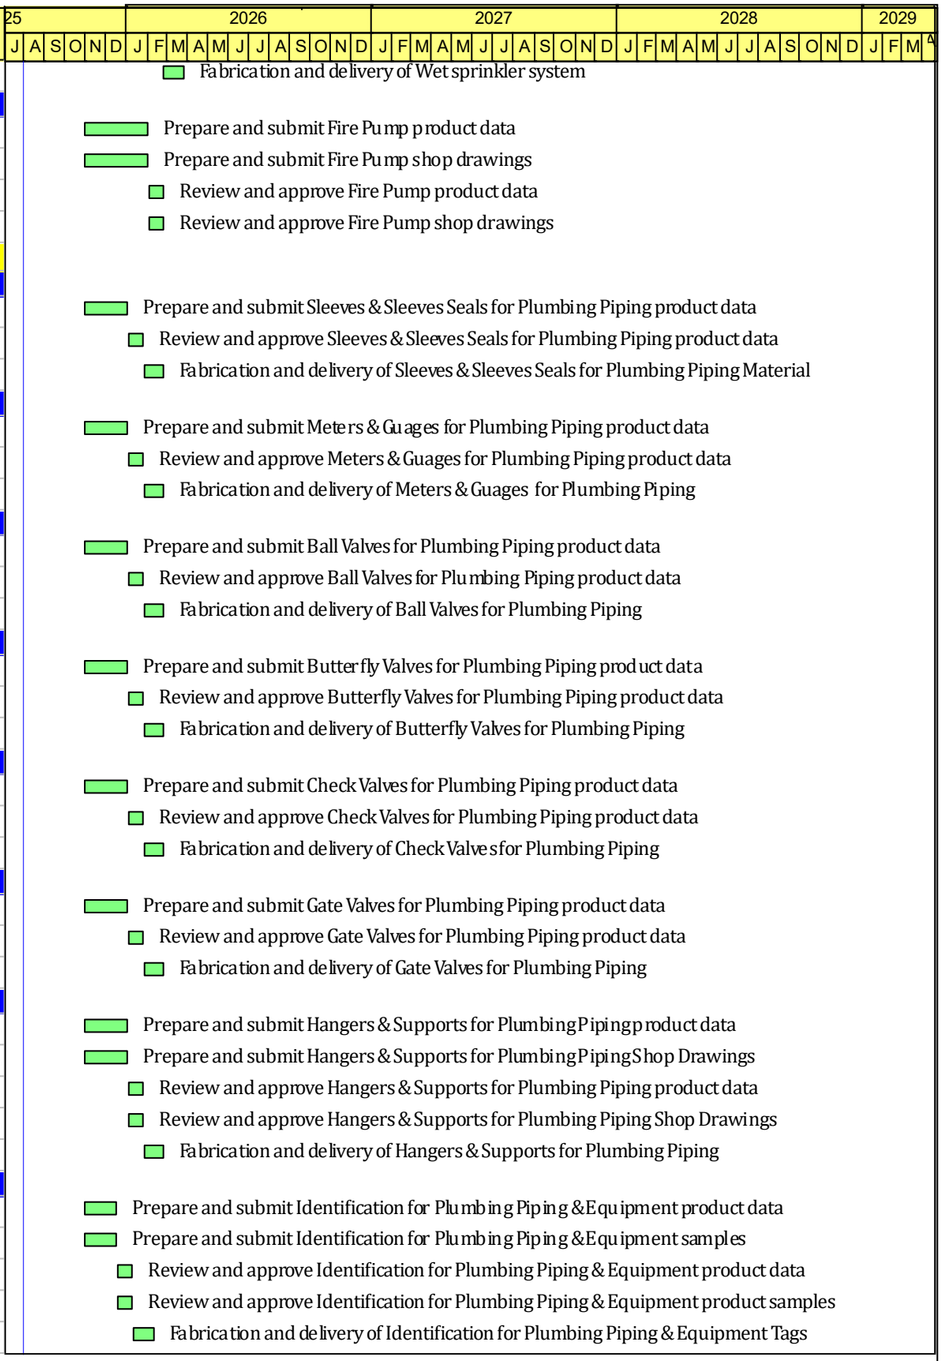

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
220593 - TESTING AND BALANCING FOR PLUMBING		45	30-Oct-25	09-Jan-26	370
PRO-22-1065	Prepare and submit Testing & Balancing Procedure for Plumbing Equipment	30	30-Oct-25	17-Dec-25	349
PRO-22-1460	Prepare and submit TAB Report for Plumbing Equipment	30	30-Oct-25	17-Dec-25	370
PRO-22-1470	Prepare and submit Check List for Plumbing Equipment	30	30-Oct-25	17-Dec-25	370
PRO-22-1480	Prepare and submit Calibration Report for Plumbing Equipment	30	30-Oct-25	17-Dec-25	370
PRO-22-1180	Review and approve Testing & Balancing Procedure for Plumbing Equipment	15	18-Dec-25	09-Jan-26	349
PRO-22-1465	Review and approve TAB Report for Plumbing Equipment	15	18-Dec-25	09-Jan-26	370
PRO-22-1475	Review and approve Check List for Plumbing Equipment	15	18-Dec-25	09-Jan-26	370
PRO-22-1485	Review and approve Calibration Report for Plumbing Equipment	15	18-Dec-25	09-Jan-26	370
220719 - PLUMBING INSULATION		85	30-Oct-25	12-Mar-26	300
PRO-22-1000	Prepare and submit plumbing insulation product data	60	30-Oct-25	02-Feb-26	300
PRO-22-1490	Prepare and submit plumbing insulation Shop Drawings	60	30-Oct-25	02-Feb-26	300
PRO-22-1345	Review and approve plumbing insulation product data	15	03-Feb-26	25-Feb-26	300
PRO-22-1495	Review and approve plumbing insulation Shop Drawings	15	03-Feb-26	25-Feb-26	300
PRO-22-1405	Fabrication and delivery of plumbing insulation	10	26-Feb-26	12-Mar-26	300
220800 - COMMISSIONING OF PLUMBING		75	30-Oct-25	25-Feb-26	402
PRO-22-1035	Prepare and submit Commissioning Procedure for Plumbing Equipment	60	30-Oct-25	02-Feb-26	319
PRO-22-1150	Review and approve Commissioning Procedure for Plumbing Equipment	15	03-Feb-26	25-Feb-26	319
PRO-22-1500	Submit Certificates of Completion for Plumbing Equipment	15	03-Feb-26	25-Feb-26	402
221116 - DOMESTIC WATER PIPING		95	30-Oct-25	26-Mar-26	226
PRO-22-1090	Prepare and submit Domestic Water Piping product data	60	30-Oct-25	02-Feb-26	88
PRO-22-1095	Prepare and submit Domestic Water Piping shop drawings	60	30-Oct-25	02-Feb-26	88
PRO-22-1225	Review and approve Domestic Water Piping product data	15	03-Feb-26	25-Feb-26	88
PRO-22-1230	Review and approve Domestic Water Piping shop drawings	15	03-Feb-26	25-Feb-26	88
PRO-22-1300	Fabrication and delivery of Domestic Water Piping	20	26-Feb-26	26-Mar-26	226
221119 - DOMESTIC WATER PIPING SPECIALTIES		95	30-Oct-25	26-Mar-26	226
PRO-22-1100	Prepare and submit Domestic Water Piping Specialities product data	60	30-Oct-25	02-Feb-26	226
PRO-22-1505	Prepare and submit Domestic Water Piping Specialities shop drawings	60	30-Oct-25	02-Feb-26	226
PRO-22-1235	Review and approve Domestic Water Piping Specialities product data	15	03-Feb-26	25-Feb-26	226
PRO-22-1510	Review and approve Domestic Water Piping Specialities shop drawings	15	03-Feb-26	25-Feb-26	226
PRO-22-1305	Fabrication and delivery of Domestic Water Piping Specialities	20	26-Feb-26	26-Mar-26	226
221123.13 - DOMESTIC WATER PACKAGE BOOSTER PUMPS		95	30-Oct-25	26-Mar-26	226
PRO-22-1690	Prepare and submit Domestic Water Package Booster Pumps product data	60	30-Oct-25	02-Feb-26	88
PRO-22-1710	Prepare and submit Domestic Water Package Booster Pumps shop drawings	60	30-Oct-25	02-Feb-26	88
PRO-22-1680	Review and approve Domestic Water Package Booster Pumps product data	15	03-Feb-26	25-Feb-26	88
PRO-22-1700	Review and approve Domestic Water Package Booster Pumps shop drawings	15	03-Feb-26	25-Feb-26	88
PRO-22-1670	Fabrication and delivery of Domestic Water Package Booster Pumps	20	26-Feb-26	26-Mar-26	226
221313 - FACILITY SANITARY SEWER PIPING		75	30-Oct-25	25-Feb-26	88
PRO-22-1640	Prepare and submit Facility Sanitary Sewer Piping product data	40	30-Oct-25	02-Jan-26	88
PRO-22-1660	Prepare and submit Facility Sanitary Sewer Piping shop drawings	40	30-Oct-25	02-Jan-26	88
PRO-22-1630	Review and approve Facility Sanitary Sewer Piping product data	15	05-Jan-26	26-Jan-26	88
PRO-22-1650	Review and approve Facility Sanitary Sewer Piping shop drawings	15	05-Jan-26	26-Jan-26	88

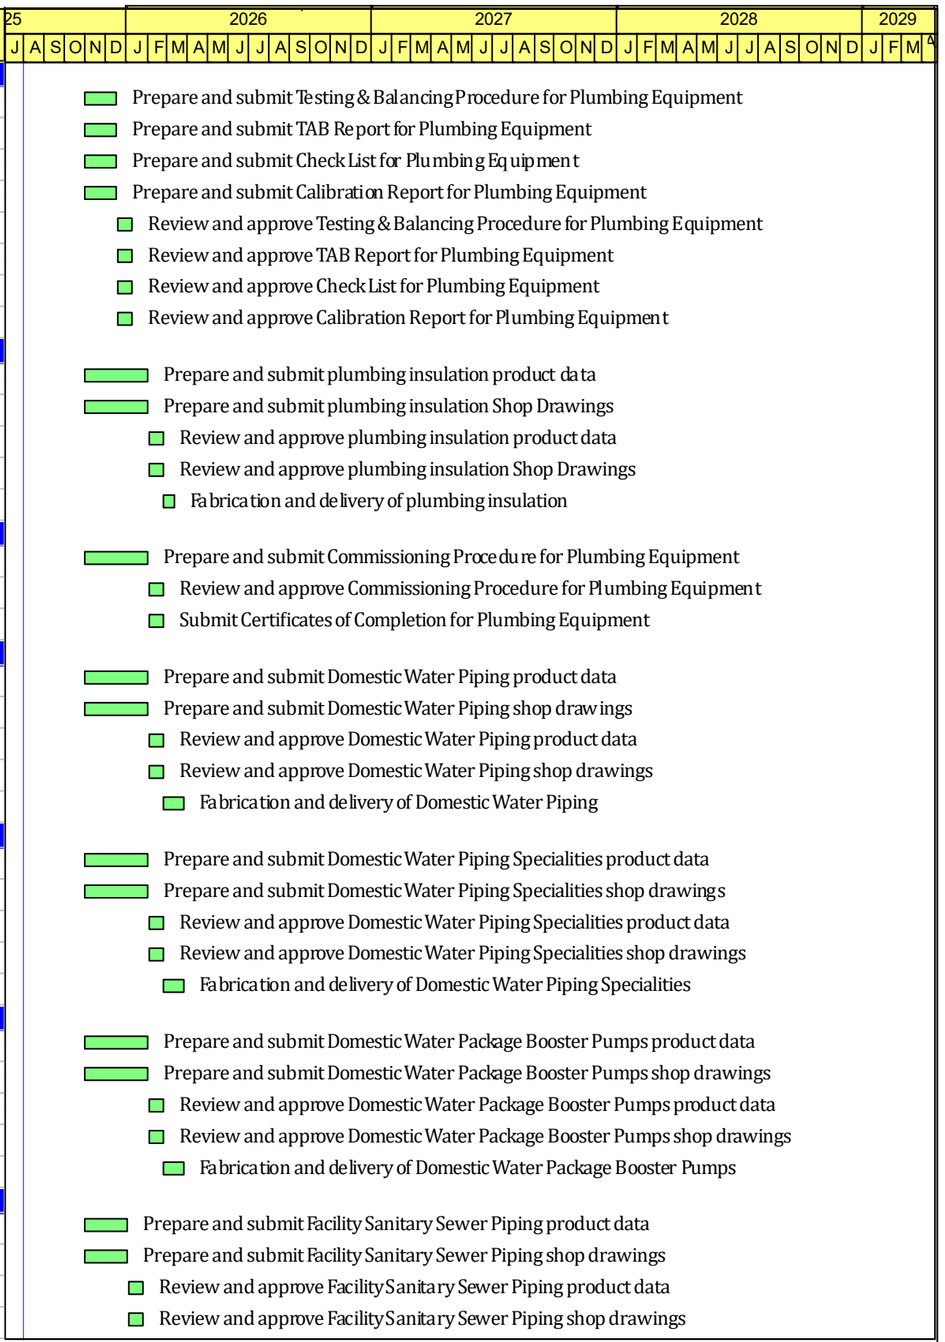

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PRO-22-1620	Fabrication and delivery of Facility Sanitary Sewer Piping	20	27-Jan-26	25-Feb-26	88
221316 - SANITARY, WASTE AND VENT PIPING		75	30-Oct-25	25-Feb-26	88
PRO-22-1015	Prepare and submit Sanitary,Waste & Vent product data	40	30-Oct-25	02-Jan-26	88
PRO-22-1020	Prepare and submit Sanitary,Waste & Vent shop drawings	40	30-Oct-25	02-Jan-26	88
PRO-22-1205	Review and approve Sanitary,Waste & Vent product data	15	05-Jan-26	26-Jan-26	88
PRO-22-1210	Review and approve Sanitary,Waste & Vent shop drawings	15	05-Jan-26	26-Jan-26	88
PRO-22-1285	Fabrication and delivery of Sanitary,Waste & Vent pipe, fittings, drains, cleanouts, valves, traps	20	27-Jan-26	25-Feb-26	88
221319 - SANITARY, WASTE AND VENT PIPING SPECIALTIES		75	30-Oct-25	25-Feb-26	88
PRO-22-1105	Prepare and submit Sanitary,Waste & Vent Piping Specialities product data	40	30-Oct-25	02-Jan-26	88
PRO-22-1515	Prepare and submit Sanitary,Waste & Vent Piping Specialities shop drawings	40	30-Oct-25	02-Jan-26	88
PRO-22-1240	Review and approve Sanitary,Waste & Vent Specialities product data	15	05-Jan-26	26-Jan-26	88
PRO-22-1520	Review and approve Sanitary,Waste & Vent Specialities shop drawings	15	05-Jan-26	26-Jan-26	88
PRO-22-1310	Fabrication and delivery of Sanitary,Waste & Vent Specialities	20	27-Jan-26	25-Feb-26	88
221319.13 - SANITARY DRAINS		75	30-Oct-25	25-Feb-26	131
PRO-22-1110	Prepare and submit Sanitary Drains product data	40	30-Oct-25	02-Jan-26	131
PRO-22-1245	Review and approve Sanitary Drains product data	15	05-Jan-26	26-Jan-26	131
PRO-22-1315	Fabrication and delivery of Sanitary Drains	20	27-Jan-26	25-Feb-26	131
221329 - SANITARY SEWAGE PUMPS (EJECTOR)		75	30-Oct-25	25-Feb-26	297
PRO-22-1115	Prepare and submit Sanitary Sewage Pumps (Ejector) product data	40	30-Oct-25	02-Jan-26	108
PRO-22-1525	Prepare and submit Sanitary Sewage Pumps (Ejector) shop drawings	40	30-Oct-25	02-Jan-26	108
PRO-22-1250	Review and approve Sanitary Sewage Pumps (Ejector) product data	15	05-Jan-26	26-Jan-26	108
PRO-22-1530	Review and approve Sanitary Sewage Pumps (Ejector) shop drawings	15	05-Jan-26	26-Jan-26	108
PRO-22-1320	Fabrication and delivery of Sanitary Sewage Pumps (Ejector)	20	27-Jan-26	25-Feb-26	297
221414 - STORM DRAINAGE PIPING		75	30-Oct-25	25-Feb-26	88
PRO-22-1120	Prepare and submit Storm Drainage Piping product data	40	30-Oct-25	02-Jan-26	88
PRO-22-1125	Prepare and submit Storm Drainage Piping shop drawings	40	30-Oct-25	02-Jan-26	88
PRO-22-1255	Review and approve Storm Drainage Piping product data	15	05-Jan-26	26-Jan-26	88
PRO-22-1260	Review and approve Storm Drainage Piping shop drawings	15	05-Jan-26	26-Jan-26	88
PRO-22-1325	Fabrication and delivery of Storm Drainage Piping	20	27-Jan-26	25-Feb-26	88
221423 - STORM DRAINAGE PIPING SPECIALITIES		75	30-Oct-25	25-Feb-26	88
PRO-22-1590	Prepare and submit Storm Drainage Piping Specialities product data	40	30-Oct-25	02-Jan-26	88
PRO-22-1610	Prepare and submit Storm Drainage Piping Specialities shop drawings	40	30-Oct-25	02-Jan-26	88
PRO-22-1580	Review and approve Storm Drainage Piping Specialities product data	15	05-Jan-26	26-Jan-26	88
PRO-22-1600	Review and approve Storm Drainage Piping Specialities shop drawings	15	05-Jan-26	26-Jan-26	88
PRO-22-1570	Fabrication and delivery of Storm Drainage Piping Specialities	20	27-Jan-26	25-Feb-26	88
221429 - SUMP PUMPS		65	30-Oct-25	10-Feb-26	318
PRO-22-1005	Prepare and submit Sump Pumps product data	40	30-Oct-25	02-Jan-26	108
PRO-22-1350	Review and approve Sump Pumps product data	15	05-Jan-26	26-Jan-26	108
PRO-22-1410	Fabrication and delivery of Sump Pumps	10	27-Jan-26	10-Feb-26	318
223300 - ELECTRIC, DOMESTIC-WATER HEATERS		115	30-Oct-25	24-Apr-26	177
PRO-22-1025	Prepare and submit Electric Domestic Water Heaters product data	40	30-Oct-25	02-Jan-26	108
PRO-22-1535	Prepare and submit Electric Domestic Water Heaters Shop Drawings	40	30-Oct-25	02-Jan-26	108
PRO-22-1215	Review and approve Electric Domestic Water Heaters product data	15	05-Jan-26	26-Jan-26	108

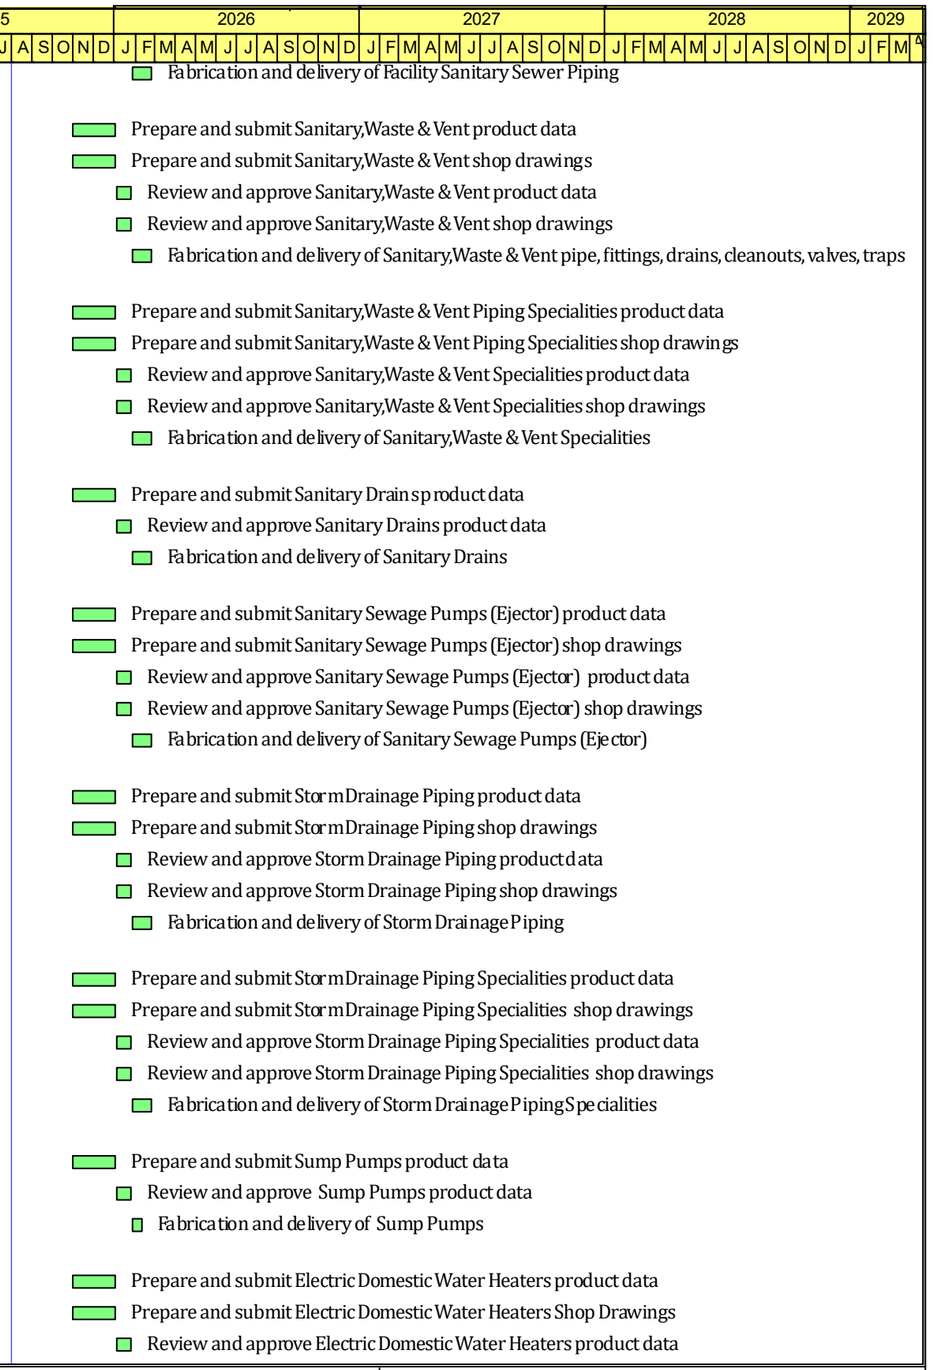

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PRO-22-1540	Review and approve Electric Domestic Water Heaters Shop Drawings	15	05-Jan-26	26-Jan-26	108
PRO-22-1290	Fabrication and delivery of Electric Domestic Water Heaters	60	27-Jan-26	24-Apr-26	177
224213.13 - COMMERCIAL WATER CLOSETS		95	30-Oct-25	26-Mar-26	300
PRO-22-1030	Prepare and submit Commercial Water Closets product data	40	30-Oct-25	02-Jan-26	108
PRO-22-1545	Prepare and submit Commercial Water Closets Shop Drawings	40	30-Oct-25	02-Jan-26	108
PRO-22-1220	Review and approve Commercial Water Closets product data	15	05-Jan-26	26-Jan-26	108
PRO-22-1550	Review and approve Commercial Water Closets Shop Drawings	15	05-Jan-26	26-Jan-26	108
PRO-22-1295	Fabrication and delivery of Commercial Water Closets	40	27-Jan-26	26-Mar-26	300
224216.13 - COMMERCIAL LAVATORIES		115	30-Oct-25	24-Apr-26	280
PRO-22-1140	Prepare and submit Commercial Lavatories product data	60	30-Oct-25	02-Feb-26	280
PRO-22-1275	Review and approve Commercial Lavatories product data	15	03-Feb-26	25-Feb-26	280
PRO-22-1335	Fabrication and delivery of Commercial Lavatories	40	26-Feb-26	24-Apr-26	280
224713 - DRINKING FOUNTAINS		115	30-Oct-25	24-Apr-26	280
PRO-22-1145	Prepare and submit Drinking Fountains product data	60	30-Oct-25	02-Feb-26	280
PRO-22-1555	Prepare and submit Drinking Fountains Shop Drawings	60	30-Oct-25	02-Feb-26	280
PRO-22-1280	Review and approve Drinking Fountains product data	15	03-Feb-26	25-Feb-26	280
PRO-22-1560	Review and approve Drinking Fountains Shop Drawings	15	03-Feb-26	25-Feb-26	280
PRO-22-1340	Fabrication and delivery of Drinking Fountains	40	26-Feb-26	24-Apr-26	280
DIVISION 23 - HEATING, VENTILATING AND AIR CONDITIONING		206	09-Oct-25	23-Jul-26	324
230513 - COMMON MOTORS REQUIREMENT FOR HVAC EQUIPMENT		65	09-Oct-25	16-Jan-26	173
PRO-23-1000	Prepare and submit hvac motor product data	50	09-Oct-25	24-Dec-25	173
PRO-23-1020	Review and approve hvac motor product data	15	26-Dec-25	16-Jan-26	173
230529 - HANGERS & SUPPORTS FOR HVAC PIPING		40	09-Oct-25	09-Dec-25	198
PRO-23-1560	Prepare and submit Hangers & Supports for HVAC product data	15	09-Oct-25	29-Oct-25	198
PRO-23-2205	Prepare and submit Hangers & Supports for HVAC Shop Drawings	15	09-Oct-25	29-Oct-25	198
PRO-23-1555	Review and approve Hangers & Supports for HVAC product data	15	30-Oct-25	21-Nov-25	198
PRO-23-2210	Review and approve Hangers & Supports for HVAC Shop Drawings	15	30-Oct-25	21-Nov-25	198
PRO-23-1530	Fabrication and delivery of Hangers & Supports for HVAC	10	24-Nov-25	09-Dec-25	198
230548.13 - VIBRATION CONTROLS FOR HVAC		75	09-Oct-25	02-Feb-26	163
PRO-23-2220	Prepare and submit Vibration Controls for HVAC product data	30	09-Oct-25	21-Nov-25	163
PRO-23-2225	Prepare and submit Vibration Controls for HVAC Shop Drawings	30	09-Oct-25	21-Nov-25	163
PRO-23-2235	Prepare and submit Vibration Controls for HVAC Wind Force Certification	30	09-Oct-25	21-Nov-25	163
PRO-23-2215	Review and approve Vibration Controls for HVAC product data	15	24-Nov-25	17-Dec-25	163
PRO-23-2230	Review and approve Vibration Controls for HVAC Shop Drawings	15	24-Nov-25	17-Dec-25	163
PRO-23-2240	Review and approve Vibration Controls for HVAC Wind Force Certification	15	24-Nov-25	17-Dec-25	163
PRO-23-1650	Fabrication and delivery of Vibration Controls for HVAC	30	18-Dec-25	02-Feb-26	163
230553 - IDENTIFICATION FOR HVAC PIPING & EQUIPMENT		75	09-Oct-25	02-Feb-26	334
PRO-23-1600	Prepare and submit Identification for HVAC product data	30	09-Oct-25	21-Nov-25	334
PRO-23-2245	Prepare and submit Identification for HVAC Samples	30	09-Oct-25	21-Nov-25	334
PRO-23-2255	Prepare and submit Identification for HVAC Schedule	30	09-Oct-25	21-Nov-25	334
PRO-23-1595	Review and approve Identification for HVAC product data	15	24-Nov-25	17-Dec-25	334
PRO-23-2250	Review and approve Identification for HVAC Samples	15	24-Nov-25	17-Dec-25	334

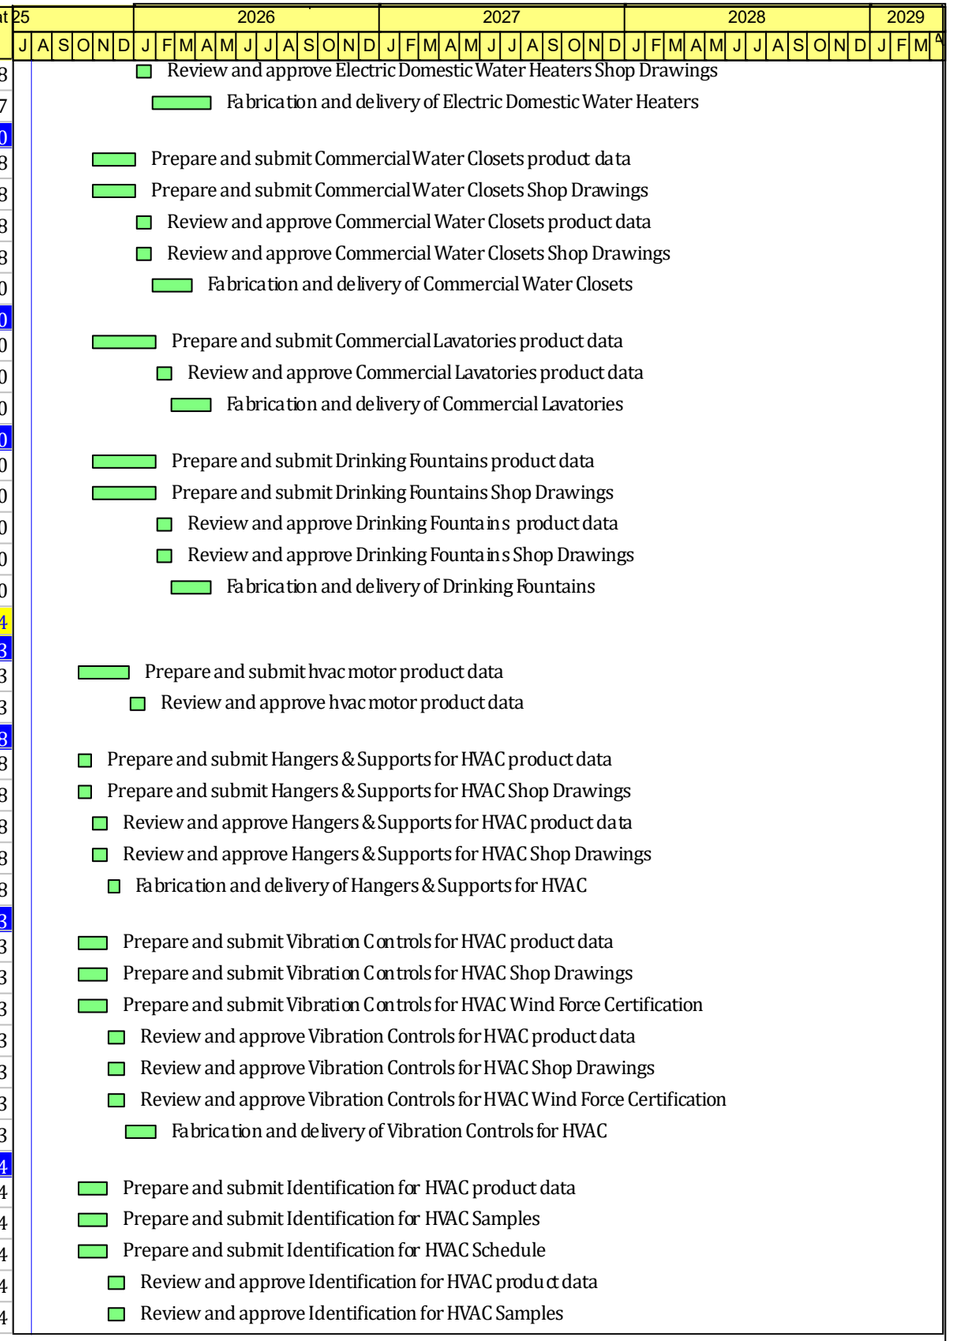

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PRO-23-2260	Review and approve Identification for HVAC Schedule	15	24-Nov-25	17-Dec-25	334
PR0-23-1540	Fabrication and delivery of Identification for HVAC tags	30	18-Dec-25	02-Feb-26	334
230593 - TESTING, ADJUSTING & BALANCING FOR HVAC		45	09-Oct-25	17-Dec-25	364
PRO-23-1130	Prepare and submit testing, adjusting & balancing procedures for HVAC	30	09-Oct-25	21-Nov-25	364
PRO-23-2265	Prepare and submit TAB Reports for HVAC	30	09-Oct-25	21-Nov-25	364
PRO-23-2275	Prepare and submit Flush Reports for HVAC	30	09-Oct-25	21-Nov-25	364
PRO-23-2285	Prepare and submit Leed requirement for HVAC	30	09-Oct-25	21-Nov-25	364
PRO-23-2295	Prepare and submit Calibration Report for HVAC	30	09-Oct-25	21-Nov-25	364
PRO-23-1150	Review and approve testing, adjusting & balancing procedures for HVAC	15	24-Nov-25	17-Dec-25	364
PRO-23-2270	Review and approve TAB Reports for HVAC	15	24-Nov-25	17-Dec-25	364
PRO-23-2280	Review and approve Flush Reports for HVAC	15	24-Nov-25	17-Dec-25	364
PRO-23-2290	Review and approve Leed requirement for HVAC	15	24-Nov-25	17-Dec-25	364
PRO-23-2300	Review and approve Calibration Report for HVAC	15	24-Nov-25	17-Dec-25	364
230713 - HVAC DUCT INSULATION		55	09-Oct-25	02-Jan-26	183
PRO-23-1160	Prepare and submit HVAC Duct Insulation product data	30	09-Oct-25	21-Nov-25	183
PRO-23-2305	Prepare and submit Leed requirement HVAC Duct Insulation	30	09-Oct-25	21-Nov-25	183
PRO-23-2315	Prepare and submit HVAC Duct Insulation Shop Drawings	30	09-Oct-25	21-Nov-25	183
PRO-23-1180	Review and approve HVAC Duct Insulation product Data	15	24-Nov-25	17-Dec-25	183
PRO-23-2310	Review and approve Leed requirement HVAC Duct Insulation	15	24-Nov-25	17-Dec-25	183
PRO-23-2320	Review and approve HVAC Duct Insulation Shop Drawings	15	24-Nov-25	17-Dec-25	183
PR0-23-1450	Fabrication and delivery of HVAC Duct Insulation	10	18-Dec-25	02-Jan-26	183
230716 - HVAC EQUIPMENT INSULATION		45	09-Oct-25	17-Dec-25	207
PRO-23-1040	Prepare and submit HVAC Equipment Insulation product Data	30	09-Oct-25	21-Nov-25	207
PRO-23-2325	Prepare and submit Leed requirement HVAC Equipment Insulation	30	09-Oct-25	21-Nov-25	207
PRO-23-2335	Prepare and submit HVAC Equipment Insulation Shop Drawings	30	09-Oct-25	21-Nov-25	207
PRO-23-2345	Prepare and submit HVAC Equipment Insulation Samples	30	09-Oct-25	21-Nov-25	207
PRO-23-1060	Review and approve HVAC Equipment Insulation product Data	15	24-Nov-25	17-Dec-25	207
PRO-23-2330	Review and approve Leed requirement HVAC Equipment Insulation	15	24-Nov-25	17-Dec-25	207
PRO-23-2340	Review and approve HVAC Equipment Insulation Shop Drawings	15	24-Nov-25	17-Dec-25	207
PRO-23-2350	Review and approve HVAC Equipment Insulation Samples	15	24-Nov-25	17-Dec-25	207
230719 - HVAC PIPING INSULATION		65	09-Oct-25	16-Jan-26	173
PRO-23-1610	Prepare and submit HVAC Piping Insulation product Data	50	09-Oct-25	24-Dec-25	173
PRO-23-2355	Prepare and submit Leed requirement HVAC Piping Insulation	50	09-Oct-25	24-Dec-25	173
PRO-23-2365	Prepare and submit HVAC Piping Insulation Shop Drawings	50	09-Oct-25	24-Dec-25	173
PRO-23-2375	Prepare and submit HVAC Piping Insulation Samples	50	09-Oct-25	24-Dec-25	173
PRO-23-1605	Review and approve HVAC Piping Insulation product Data	15	26-Dec-25	16-Jan-26	173
PRO-23-2360	Review and approve Leed requirement HVAC Piping Insulation	15	26-Dec-25	16-Jan-26	173
PRO-23-2370	Review and approve HVAC Piping Insulation Shop Drawings	15	26-Dec-25	16-Jan-26	173
PRO-23-2380	Review and approve HVAC Piping Insulation Samples	15	26-Dec-25	16-Jan-26	173
230800 - COMMISSIONING FOR HVAC SYSTEMS		190	09-Oct-25	23-Jul-26	302
PRO-23-1630	Prepare and submit Commissioning procedures for HVAC	65	09-Oct-25	16-Jan-26	334
PRO-23-2385	Prepare and submit Test Reports for HVAC	65	09-Oct-25	16-Jan-26	412



Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PRO-23-2400	Prepare and submit Commissioning Shop Drawings for HVAC	65	09-Oct-25	16-Jan-26	302
PRO-23-1625	Review and approve Commissioning procedures for HVAC	15	20-Jan-26	10-Feb-26	334
PRO-23-2390	Review and approve Test Reports for HVAC	15	20-Jan-26	10-Feb-26	412
PRO-23-2405	Review and approve Commissioning Shop Drawings for HVAC	15	20-Jan-26	10-Feb-26	302
PRO-23-2395	Prepare and submit Certificate of Completion for HVAC	110	11-Feb-26	23-Jul-26	302
230923 - DIRECT DIGITAL CONTROL (DDC) SYSTEM FOR HVAC		65	09-Oct-25	16-Jan-26	187
PRO-23-1200	Prepare and submit Direct Digital Control (DDC) for HVAC System product data	50	09-Oct-25	24-Dec-25	187
PRO-23-2410	Prepare and submit Direct Digital Control (DDC) for HVAC System Shop Drawings	50	09-Oct-25	24-Dec-25	187
PRO-23-1220	Review and approve Direct Digital Control (DDC) for HVAC System Product Data	15	26-Dec-25	16-Jan-26	187
PRO-23-2415	Review and approve Direct Digital Control (DDC) for HVAC System Shop Drawings	15	26-Dec-25	16-Jan-26	187
230923.12 - CONTROL DAMPERS FOR HVAC		65	09-Oct-25	16-Jan-26	324
PRO-23-1670	Prepare and submit Control Dampers for HVAC System Product Data	50	09-Oct-25	24-Dec-25	324
PRO-23-2430	Prepare and submit Control Dampers for HVAC System Shop Drawings	50	09-Oct-25	24-Dec-25	324
PRO-23-1665	Review and approve Control Dampers for HVAC System Product Data	15	26-Dec-25	16-Jan-26	324
PRO-23-2435	Review and approve Control Dampers for HVAC System Shop Drawings	15	26-Dec-25	16-Jan-26	324
230923.16 - GAS INSTRUMENTS FOR HVAC		0			0
230923.18 - LEAK-DETECTION INSTRUMENTS FOR HVAC		65	09-Oct-25	16-Jan-26	227
PRO-23-1790	Prepare and submit Leak Detection Instruments for HVAC product data	50	09-Oct-25	24-Dec-25	227
PRO-23-2510	Prepare and submit Leak Detection Instruments for HVAC Shop Drawings	50	09-Oct-25	24-Dec-25	227
PRO-23-1785	Review and approve Leak Detection Instruments for HVAC product data	15	26-Dec-25	16-Jan-26	227
PRO-23-2515	Review and approve Leak Detection Instruments for HVAC Shop Drawings	15	26-Dec-25	16-Jan-26	227
230923.19 - MOISTURE INSTRUMENTS FOR HVAC		65	09-Oct-25	16-Jan-26	173
PRO-23-1850	Prepare and submit Moisture Instruments for hvac product data	50	09-Oct-25	24-Dec-25	173
PRO-23-2520	Prepare and submit Moisture Instruments for hvac Shop Drawings	50	09-Oct-25	24-Dec-25	173
PRO-23-1845	Review and approve Moisture Instruments for hvac product data	15	26-Dec-25	16-Jan-26	173
PRO-23-2525	Review and approve Moisture Instruments for hvac Shop Drawings	15	26-Dec-25	16-Jan-26	173
230923.22 - POSITION INSTRUMENTS FOR HVAC		65	09-Oct-25	16-Jan-26	173
PRO-23-1820	Prepare and submit Position Instruments for hvac product data	50	09-Oct-25	24-Dec-25	173
PRO-23-1815	Review and approve Position Instruments for hvac product data	15	26-Dec-25	16-Jan-26	173
230923.23 - PRESSURE INSTRUMENTS FOR HVAC		85	09-Oct-25	18-Feb-26	153
PRO-23-1910	Prepare and submit Pressure Instruments for hvac product data	70	09-Oct-25	26-Jan-26	153
PRO-23-1905	Review and approve Pressure Instruments for hvac product data	15	27-Jan-26	18-Feb-26	153
230923.24 - TEMPERATURE INSTRUMENTS FOR HVAC		85	09-Oct-25	18-Feb-26	153
PRO-23-1880	Prepare and submit Temperature Instruments for hvac product data	70	09-Oct-25	26-Jan-26	153
PRO-23-1875	Review and approve Temperature Instruments for hvac product data	15	27-Jan-26	18-Feb-26	153
230993.11 - SEQUENCE OF OPERATIONS DIRECT DIGITAL CONTROL (DDC) SYSTEM FOR HVAC		85	09-Oct-25	18-Feb-26	329
PRO-23-1940	Prepare and submit Sequence of Operation for Direct Digital Control (DDC) for HVAC System procedures	70	09-Oct-25	26-Jan-26	329
PRO-23-1935	Review and approve Sequence of Operation for Direct Digital Control (DDC) for HVAC System procedures	15	27-Jan-26	18-Feb-26	329
232300 - REFRIGERANT PIPING		95	09-Oct-25	04-Mar-26	197
PRO-23-2030	Prepare and submit Refrigerant piping product data	70	09-Oct-25	26-Jan-26	197
PRO-23-2040	Prepare and submit Refrigerant piping shop drawings	70	09-Oct-25	26-Jan-26	197
PRO-23-2570	Prepare and submit Leed Requirement Refrigerant piping	70	09-Oct-25	26-Jan-26	197

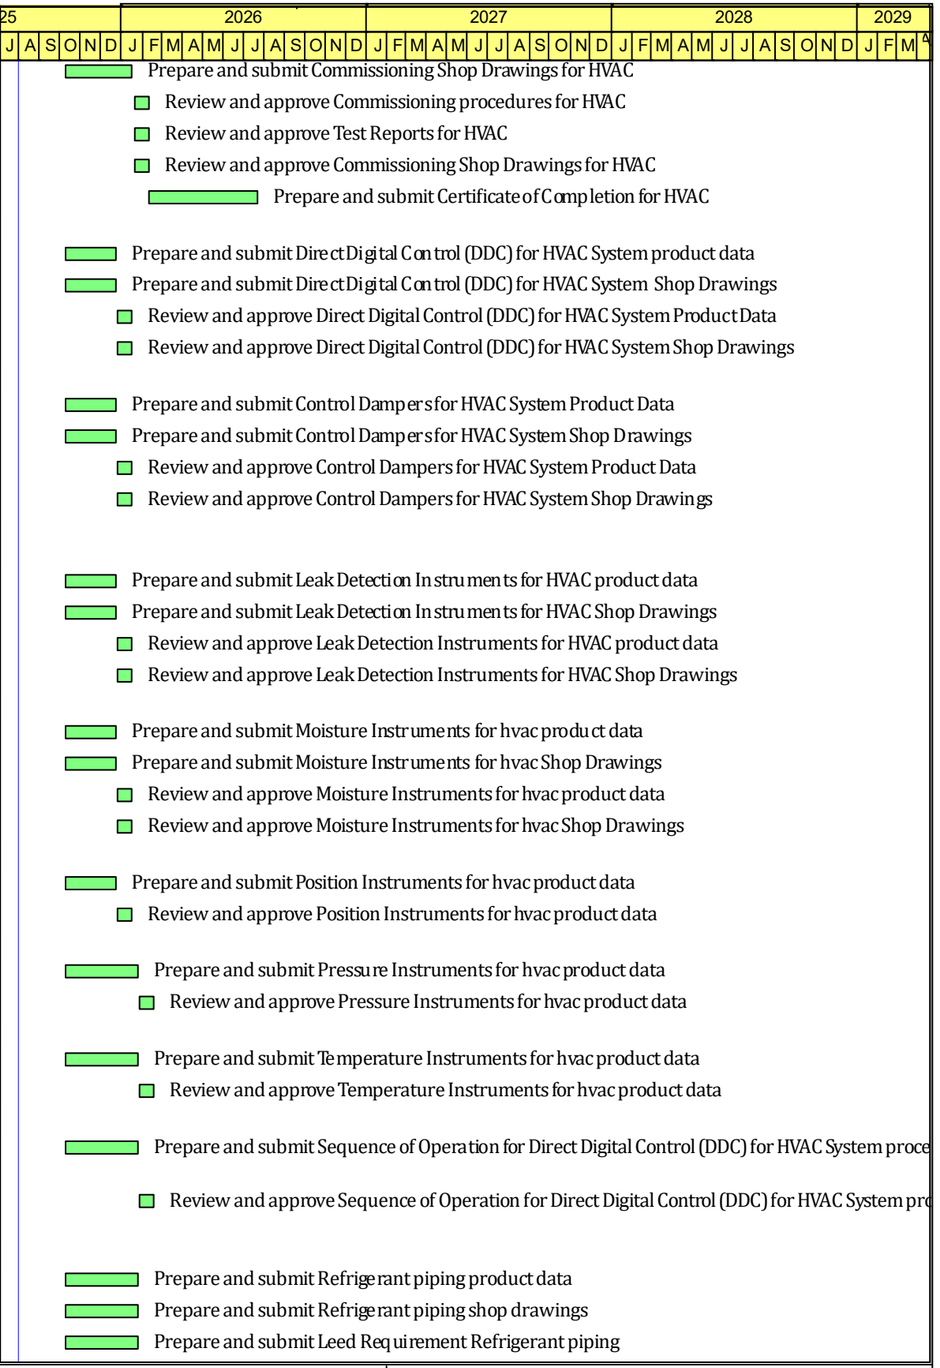

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PRO-23-2025	Review and approve Refrigerant piping product data	15	27-Jan-26	18-Feb-26	197
PRO-23-2035	Review and approve Refrigerant piping shop drawings	15	27-Jan-26	18-Feb-26	197
PRO-23-2575	Review and approve Leed Requirement Refrigerant piping	15	27-Jan-26	18-Feb-26	197
PRO-23-1570	Fabrication and delivery of Refrigerant piping	10	19-Feb-26	04-Mar-26	197
233113 - METAL DUCTS		170	09-Oct-25	24-Jun-26	161
PRO-23-1300	Prepare and submit hvac ductwork product data	70	09-Oct-25	26-Jan-26	123
PRO-23-2580	Prepare and submit Leed Requirement HVAC ductwork	70	09-Oct-25	26-Jan-26	123
PRO-23-1320	Review and approve hvac ductwork product data	15	27-Jan-26	18-Feb-26	123
PRO-23-2585	Review and approve Leed Requirement HVAC ductwork	15	27-Jan-26	18-Feb-26	123
233113 - METAL DUCTS NEW ADDITION SHOP DRAWINGS/DUCTWORK		110	12-Jan-26	24-Jun-26	132
PRO-23-1310	Prepare and submit hvac ductwork shop drawings New Addition Cellar	50	12-Jan-26	26-Mar-26	83
PRO-23-2915	Prepare and submit hvac ductwork shop drawings New Addition 1st Floor	20	03-Feb-26	04-Mar-26	132
PRO-23-2935	Prepare and submit hvac ductwork shop drawings New Addition 2nd Floor	20	26-Feb-26	26-Mar-26	132
PRO-23-2925	Review and approve hvac ductwork shop drawings 1st Floor	15	05-Mar-26	26-Mar-26	132
PRO-23-2955	Prepare and submit hvac ductwork shop drawings New Addition 3rd Floor	20	20-Mar-26	17-Apr-26	132
PRO-23-1330	Review and approve hvac ductwork shop drawings Cellar	15	27-Mar-26	17-Apr-26	83
PR0-23-1660	Fabrication and delivery of hvac ductwork New Addition 1st Floor	30	27-Mar-26	08-May-26	132
PRO-23-2945	Review and approve hvac ductwork shop drawings 2nd Floor	15	27-Mar-26	17-Apr-26	132
PRO-23-2975	Prepare and submit hvac ductwork shop drawings New Addition Roof	20	13-Apr-26	08-May-26	127
PR0-23-1480	Fabrication and delivery of hvac ductwork New Addition Cellar	30	20-Apr-26	02-Jun-26	83
PR0-23-1670	Fabrication and delivery of hvac ductwork New Addition 2nd Floor	30	20-Apr-26	02-Jun-26	132
PRO-23-2965	Review and approve hvac ductwork shop drawings 3rd Floor	15	20-Apr-26	08-May-26	132
PR0-23-1680	Fabrication and delivery of hvac ductwork New Addition 3rd Floor	30	11-May-26	24-Jun-26	132
PRO-23-2985	Review and approve hvac ductwork shop drawings Roof	15	11-May-26	02-Jun-26	127
PR0-23-1690	Fabrication and delivery of hvac ductwork New Addition Roof	10	03-Jun-26	17-Jun-26	127
233113 - METAL DUCTS EXISTING LIBRARY SHOP DRAWINGS/DUCTWORK		105	12-Jan-26	17-Jun-26	166
PRO-23-3005	Prepare and submit hvac ductwork shop drawings Cellar Existing Library	50	12-Jan-26	26-Mar-26	113
PRO-23-3025	Prepare and submit hvac ductwork shop drawings 1st Floor Existing Library	20	03-Feb-26	04-Mar-26	172
PRO-23-3045	Prepare and submit hvac ductwork shop drawings 2nd Floor Existing Library	20	26-Feb-26	26-Mar-26	157
PRO-23-3015	Review and approve hvac ductwork shop drawings 1st Floor Existing Library	15	05-Mar-26	26-Mar-26	172
PRO-23-3085	Prepare and submit hvac ductwork shop drawings Roof Existing Library	20	20-Mar-26	17-Apr-26	142
PRO-23-2995	Review and approve hvac ductwork shop drawings Cellar Existing Library	15	27-Mar-26	17-Apr-26	113
PR0-23-1710	Fabrication and delivery of hvac ductwork 1st Floor Existing Library	30	27-Mar-26	08-May-26	176
PRO-23-3035	Review and approve hvac ductwork shop drawings 2nd Floor Existing Library	15	27-Mar-26	17-Apr-26	157
PR0-23-1700	Fabrication and delivery of hvac ductwork Cellar Existing Library	30	20-Apr-26	02-Jun-26	113
PR0-23-1720	Fabrication and delivery of hvac ductwork 2nd Floor Existing Library	30	20-Apr-26	02-Jun-26	176
PRO-23-3075	Review and approve hvac ductwork shop drawings Roof Existing Library	15	20-Apr-26	08-May-26	142
PR0-23-1740	Fabrication and delivery of hvac ductwork Roof Existing Library	10	03-Jun-26	17-Jun-26	127
233300 - AIR DUCT ACCESSORIES		115	09-Oct-25	02-Apr-26	123
PRO-23-2070	Prepare and submit Air Duct Accessories Product Data	70	09-Oct-25	26-Jan-26	123
PRO-23-2610	Prepare and submit Air Duct Accessories Shop Drawings	70	09-Oct-25	26-Jan-26	123
PRO-23-2620	Prepare and submit Leed Requirement Air Duct Accessories	70	09-Oct-25	26-Jan-26	123

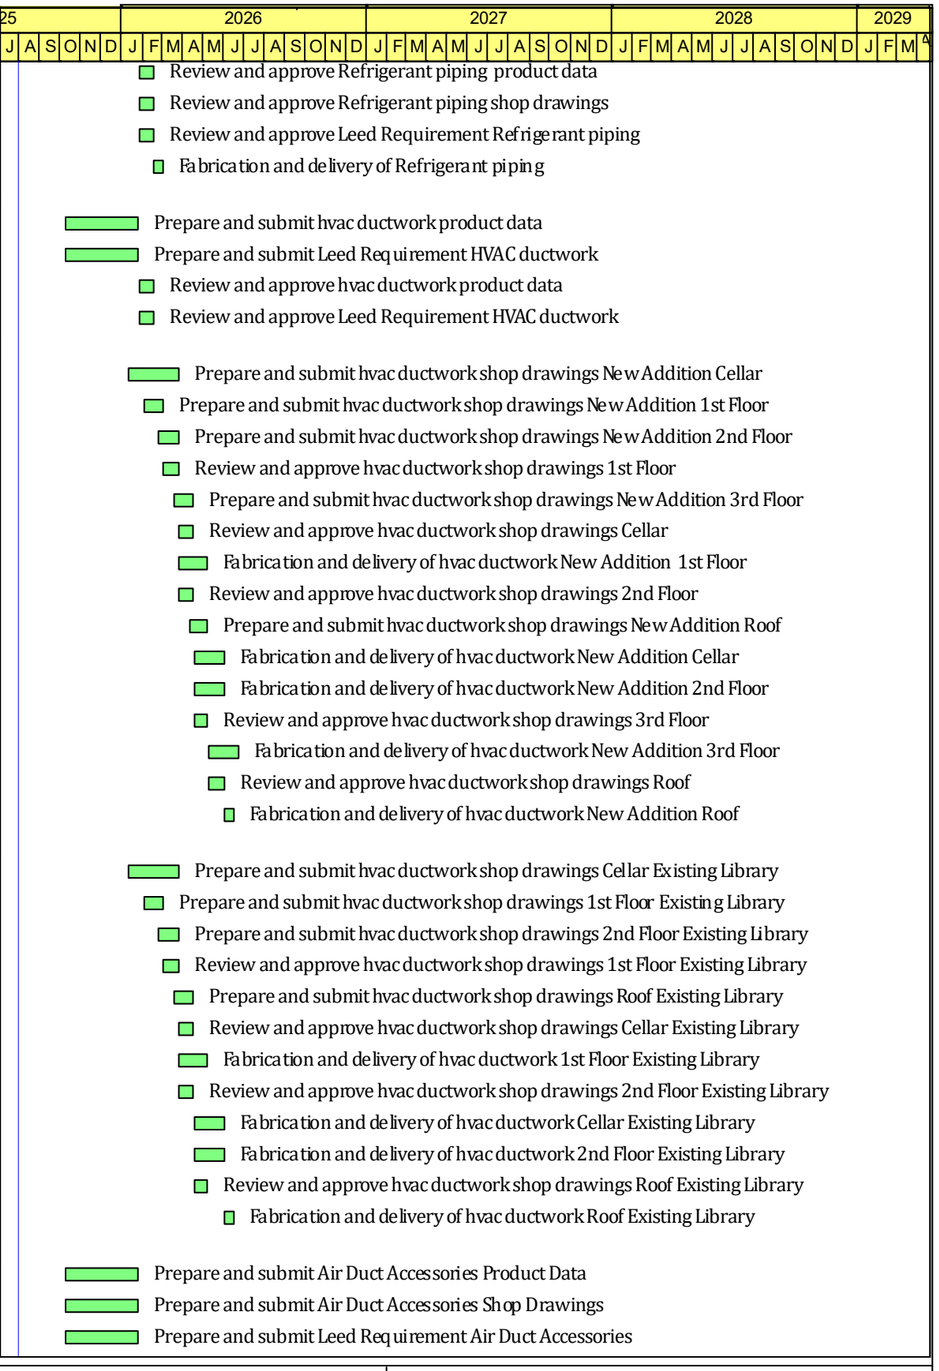

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PRO-23-2065	Review and approve Air Duct Accessories Product Data	15	27-Jan-26	18-Feb-26	123
PRO-23-2615	Review and approve Air Duct Accessories Shop Drawings	15	27-Jan-26	18-Feb-26	123
PRO-23-2625	Review and approve Leed Requirement Air Duct Accessories	15	27-Jan-26	18-Feb-26	123
PR0-23-1585	Fabrication and delivery of Air Duct Accessories	30	19-Feb-26	02-Apr-26	123
233416 - CENTRIFUGUAL HVAC FANS		115	09-Oct-25	02-Apr-26	303
PRO-23-2090	Prepare and submit Centrifugal HVAC Fans Product Data	70	09-Oct-25	26-Jan-26	84
PRO-23-2650	Prepare and submit Centrifugal HVAC Fans Shop Drawings	70	09-Oct-25	26-Jan-26	84
PRO-23-2660	Prepare and submit Leed Requirement Centrifugal HVAC Fans	70	09-Oct-25	26-Jan-26	84
PRO-23-2085	Review and approve Centrifugal HVAC Fans Product Data	15	27-Jan-26	18-Feb-26	84
PRO-23-2655	Review and approve Centrifugal HVAC Fans Shop Drawings	15	27-Jan-26	18-Feb-26	84
PRO-23-2665	Review and approve Leed Requirement Centrifugal HVAC Fans	15	27-Jan-26	18-Feb-26	84
PR0-23-1595	Fabrication and delivery of Centrifugal HVAC Fans	30	19-Feb-26	02-Apr-26	303
233713.13 - DIFFUSERS		115	09-Oct-25	02-Apr-26	292
PRO-23-1370	Prepare and submit diffusers product data	90	09-Oct-25	25-Feb-26	292
PRO-23-2690	Prepare and submit diffusers Samples	90	09-Oct-25	25-Feb-26	292
PRO-23-1380	Review and approve diffusers product data	15	26-Feb-26	19-Mar-26	292
PRO-23-2695	Review and approve diffusers Samples	15	26-Feb-26	19-Mar-26	292
PR0-23-1500	Fabrication and delivery of diffusers	10	20-Mar-26	02-Apr-26	292
233713.23 - REGISTERS & GRILLES		115	09-Oct-25	02-Apr-26	292
PRO-23-1430	Prepare and submit registers & grilles product data	90	09-Oct-25	25-Feb-26	292
PRO-23-2700	Prepare and submit registers & grilles Samples	90	09-Oct-25	25-Feb-26	292
PRO-23-2710	Prepare and submit registers & grilles Shop Drawings	90	09-Oct-25	25-Feb-26	292
PRO-23-1425	Review and approve registers & grilles product data	15	26-Feb-26	19-Mar-26	292
PRO-23-2705	Review and approve registers & grilles Samples	15	26-Feb-26	19-Mar-26	292
PRO-23-2715	Review and approve registers & grilles Shop Drawings	15	26-Feb-26	19-Mar-26	292
PR0-23-1515	Fabrication and delivery of registers & grilles	10	20-Mar-26	02-Apr-26	292
237433- DEDICATED OUTDOOR AIRUNITS		85	09-Oct-25	18-Feb-26	84
PRO-23-2140	Prepare and submit Dedicated Air Units product data	70	09-Oct-25	26-Jan-26	84
PRO-23-2780	Prepare and submit Dedicated Air Units Shop Drawings	70	09-Oct-25	26-Jan-26	84
PRO-23-2790	Prepare and submit Leed Requirement Dedicated Air Units	70	09-Oct-25	26-Jan-26	84
PRO-23-2135	Review and approve Dedicated Air Units product data	15	27-Jan-26	18-Feb-26	84
PRO-23-2785	Review and approve Dedicated Air Units Shop Drawings	15	27-Jan-26	18-Feb-26	84
PRO-23-2795	Review and approve Leed Requirement Dedicated Air Units	15	27-Jan-26	18-Feb-26	84
238129 - VARIABLE REFRIGERANT FLOW HVAC SYSTEMS		125	09-Oct-25	17-Apr-26	167
PRO-23-2150	Prepare and submit Variable Refrigerant Flow HVAC System product data	70	09-Oct-25	26-Jan-26	167
PRO-23-2800	Prepare and submit Variable Refrigerant Flow HVAC System Shop Drawings	70	09-Oct-25	26-Jan-26	167
PRO-23-2810	Prepare and submit Variable Refrigerant Flow HVAC System samples	70	09-Oct-25	26-Jan-26	167
PRO-23-2820	Prepare and submit Leed Requirement Variable Refrigerant Flow HVAC System	70	09-Oct-25	26-Jan-26	84
PRO-23-2145	Review and approve Variable Refrigerant Flow HVAC System product data	15	27-Jan-26	18-Feb-26	167
PRO-23-2805	Review and approve Variable Refrigerant Flow HVAC System Shop Drawings	15	27-Jan-26	18-Feb-26	167
PRO-23-2815	Review and approve Variable Refrigerant Flow HVAC System Samples	15	27-Jan-26	18-Feb-26	167
PRO-23-2825	Review and approve Leed Requirement Variable Refrigerant Flow HVAC System	15	27-Jan-26	18-Feb-26	84

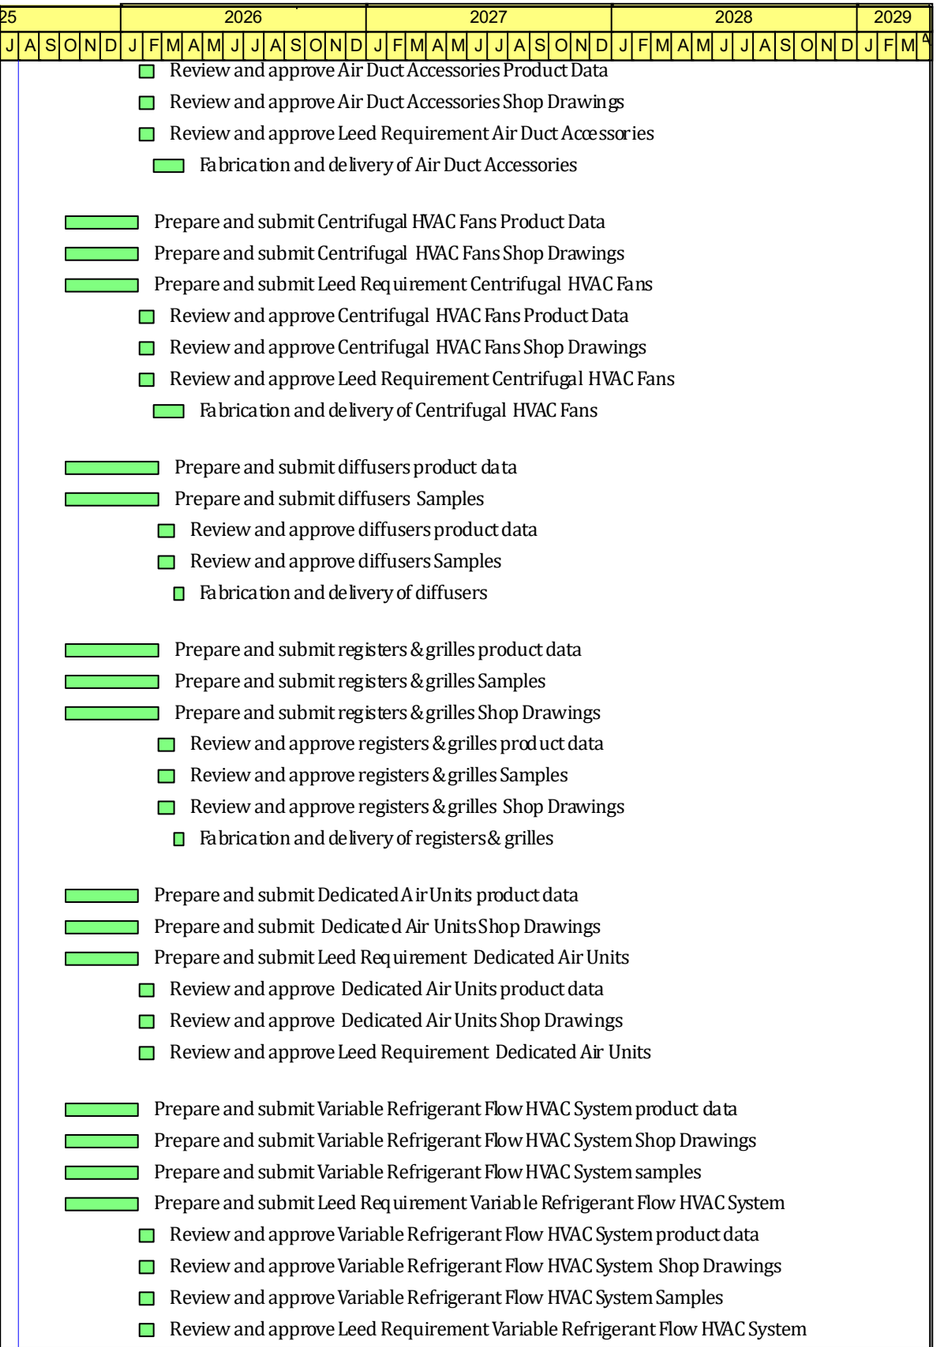

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PR0-23-1625	Fabrication and delivery of Variable Refrigerant Flow HVAC System	40	19-Feb-26	17-Apr-26	167
238216.14 - ELECTRIC-RESISTANCE AIR COIL UNITS		125	09-Oct-25	17-Apr-26	182
PR0-23-2190	Prepare and submit Electric-Resistance Air Coils product data	70	09-Oct-25	26-Jan-26	84
PR0-23-2185	Review and approve Electric-Resistance Air Coils Product Data data	15	27-Jan-26	18-Feb-26	84
PR0-23-1645	Fabrication and delivery of Electric-Resistance Air Coils	40	19-Feb-26	17-Apr-26	182
239239.16 - PROPELLER UNIT HEATERS		115	09-Oct-25	02-Apr-26	192
PR0-23-1080	Prepare and submit Propeller Unit Heaters product data	90	09-Oct-25	25-Feb-26	192
PR0-23-2890	Prepare and submit Propeller Unit Heaters shop drawings	50	09-Oct-25	24-Dec-25	232
PR0-23-2900	Prepare and submit Leed Requirement Propeller Unit Heaters	50	09-Oct-25	24-Dec-25	232
PR0-23-2895	Review and approve Propeller Unit Heaters shop drawings	15	26-Dec-25	16-Jan-26	232
PR0-23-2905	Review and approve Leed Requirement Propeller Unit Heaters	15	26-Dec-25	16-Jan-26	232
PR0-23-1100	Review and approve Propeller Unit Heaters product data	15	26-Feb-26	19-Mar-26	192
PR0-23-1440	Fabrication and delivery of Propeller Unit Heaters	10	20-Mar-26	02-Apr-26	192
DIVISION 26 - ELECTRICAL		140	09-Oct-25	08-May-26	352
260519 - LOW VOLTAGE ELECTRICAL POWER CONDUCTORS AND CABLES		85	09-Oct-25	18-Feb-26	288
PR0-26-1020	Prepare and submit raceways, wires,cables, switches & wiring devices Product Data	60	09-Oct-25	09-Jan-26	288
PR0-26-1685	Prepare and submit raceways, wires,cables, switches & wiring devices shop drawings	60	09-Oct-25	09-Jan-26	288
PR0-26-1695	Prepare and submit Leed Requirement raceways, wires, cables, switches & wiring devices	60	09-Oct-25	09-Jan-26	288
PR0-26-1040	Review and approve raceways, wires, cables, switches & wiring devices Product Data	15	12-Jan-26	02-Feb-26	288
PR0-26-1690	Review and approve raceways, wires, cables, switches & wiring devices shop drawings	15	12-Jan-26	02-Feb-26	288
PR0-26-1700	Review and approve Leed Requirement raceways, wires, cables, switches & wiring devices	15	12-Jan-26	02-Feb-26	288
PR0-26-1490	Fabrication and delivery of raceways, wires, cables, switches & wiring devices	10	03-Feb-26	18-Feb-26	288
260526- GROUNDING AND BONDING FOR ELECTRICAL SYSTEMS		100	09-Oct-25	12-Mar-26	273
PR0-26-1070	Prepare and submit Grounding &Bonding for Electrical System product data	60	09-Oct-25	09-Jan-26	273
PR0-26-1705	Prepare and submit Grounding &Bonding for Electrical System shop drawings	60	09-Oct-25	09-Jan-26	273
PR0-26-1715	Prepare and submit Leed Requirement Grounding & Bonding for Electrical System	60	09-Oct-25	09-Jan-26	273
PR0-26-1080	Review and approve Grounding & Bonding for Electrical System product data	15	12-Jan-26	02-Feb-26	273
PR0-26-1710	Review and approve Grounding & Bonding for Electrical System shop drawings	15	12-Jan-26	02-Feb-26	273
PR0-26-1720	Review and approve Leed Requirement Grounding &Bonding for Electrical System	15	12-Jan-26	02-Feb-26	273
PR0-26-1500	Fabrication and delivery Grounding & Bonding for Electrical System	25	03-Feb-26	12-Mar-26	273
260526 - HANGERS& SUPPORTS FOR ELECTRICAL SYSTEMS		80	09-Oct-25	10-Feb-26	98
PR0-26-1100	Prepare and submit Hangers & Supports for Electrical System product data	60	09-Oct-25	09-Jan-26	98
PR0-26-1725	Prepare and submit Hangers & Supports for Electrical System shop drawings	60	09-Oct-25	09-Jan-26	98
PR0-26-1120	Review and approve Hangers & Supports for Electrical System product data	15	12-Jan-26	02-Feb-26	98
PR0-26-1730	Review and approve Hangers & Supports for Electrical System shop drawings	15	12-Jan-26	02-Feb-26	98
PR0-26-1735	Fabricate & Deliver Hangers & Supports for Electrical System product data	5	03-Feb-26	10-Feb-26	98
260533.13 CONDUITS FOR ELECTRICAL SYSTEMS		80	09-Oct-25	10-Feb-26	98
PR0-26-1130	Prepare and submit raceways, conduits shop drawings	60	09-Oct-25	09-Jan-26	98
PR0-26-1140	Prepare and submit raceways, conduits product data	60	09-Oct-25	09-Jan-26	98
PR0-26-1150	Review and approve raceways, conduits shop drawings	15	12-Jan-26	02-Feb-26	98
PR0-26-1160	Review and approve raceways, conduits product data	15	12-Jan-26	02-Feb-26	98
PR0-26-1740	Fabricate & Deliver raceways, conduits	5	03-Feb-26	10-Feb-26	98

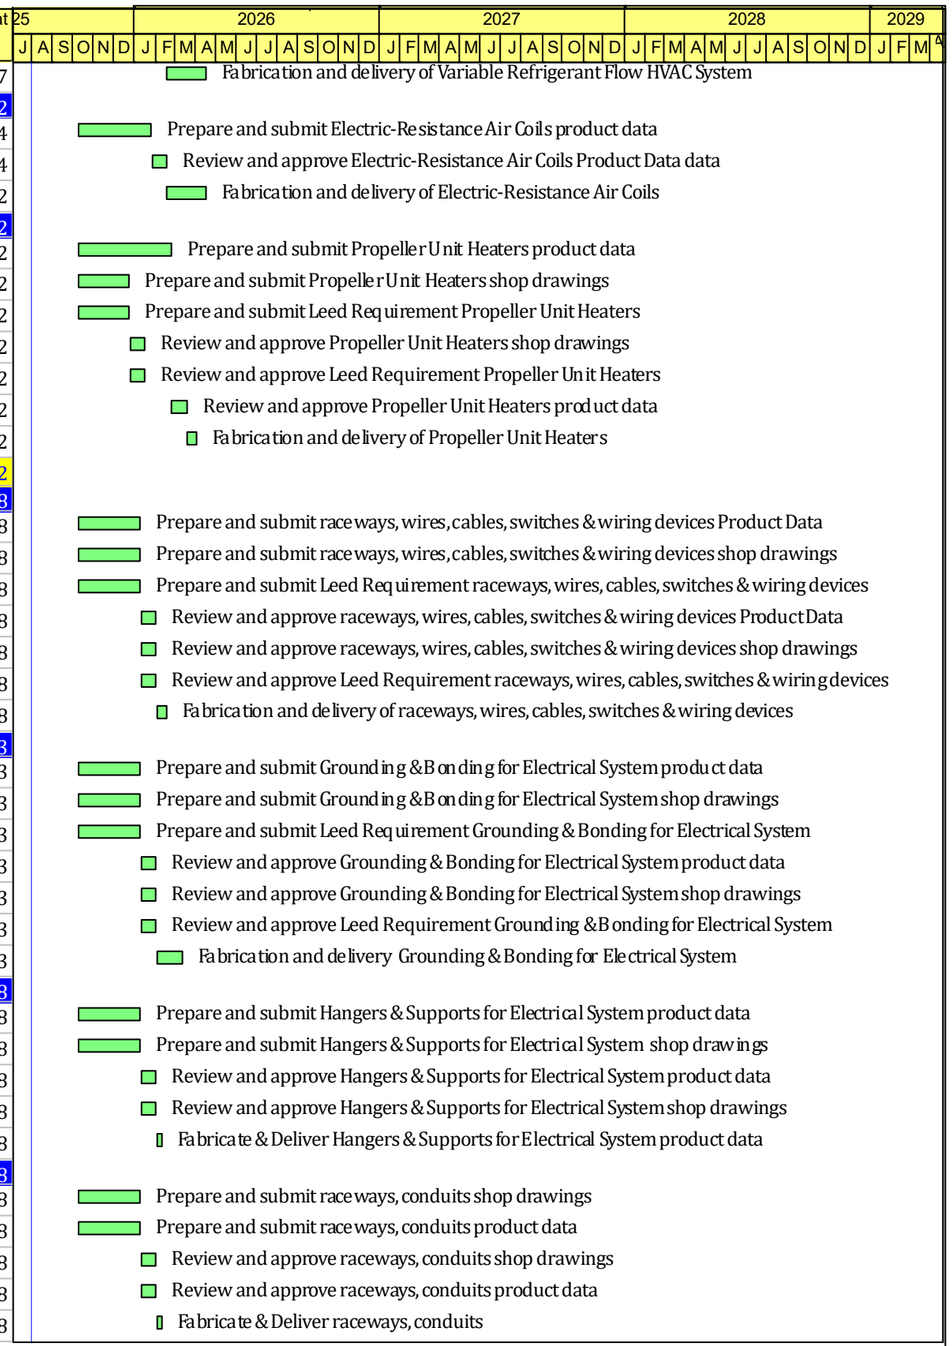

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
260533.16 BOXES AND COVERS FOR ELECTRICAL SYSTEMS		80	09-Oct-25	10-Feb-26	98
PRO-26-1180	Prepare and submit Boxes & Covers for Electrical System product data	60	09-Oct-25	09-Jan-26	98
PRO-26-1750	Prepare and submit Boxes & Covers for Electrical System Shop Drawings	60	09-Oct-25	09-Jan-26	98
PRO-26-1760	Prepare and submit Boxes & Covers for Electrical System Samples	60	09-Oct-25	09-Jan-26	98
PRO-26-1200	Review and approve Boxes & Covers for Electrical System product data	15	12-Jan-26	02-Feb-26	98
PRO-26-1755	Review and approve Boxes & Covers for Electrical System Shop Drawings	15	12-Jan-26	02-Feb-26	98
PRO-26-1765	Review and approve Boxes & Covers for Electrical System Samples	15	12-Jan-26	02-Feb-26	98
PRO-26-1745	Fabricate & Deliver Boxes & Covers for Electrical System	5	03-Feb-26	10-Feb-26	98
260544 - SLEEVES AND SLEEVE SEALS FOR ELECTRICAL SYSTEMS		95	09-Oct-25	04-Mar-26	83
PRO-26-1340	Prepare and submit Sleeves & Sleeve Seals for Electrical System product data	60	09-Oct-25	09-Jan-26	83
PRO-26-1770	Prepare and submit Leed Requirement Sleeves & Sleeve Seals for Electrical System	60	09-Oct-25	09-Jan-26	83
PRO-26-1360	Review and approve Sleeves & Sleeve Seals for Electrical System product data	15	12-Jan-26	02-Feb-26	83
PRO-26-1775	Review and approve Leed Requirement Sleeves & Sleeve Seals for Electrical System	15	12-Jan-26	02-Feb-26	83
PR0-26-1570	Fabrication and delivery of Sleeves & Sleeve Seals for Electrical System	20	03-Feb-26	04-Mar-26	83
260553 IDENTIFICATION FOR ELECTRICAL SYSTEMS		105	09-Oct-25	19-Mar-26	288
PRO-26-1420	Prepare and submit Identification Tags for Electrical System product data	60	09-Oct-25	09-Jan-26	288
PRO-26-1790	Prepare and submit Identification Tags for Electrical System Samples	60	09-Oct-25	09-Jan-26	288
PRO-26-1800	Prepare and submit Identification Tags for Electrical System ID Schedule	60	09-Oct-25	09-Jan-26	288
PRO-26-1440	Review and approve Identification Tags for Electrical System product data	15	12-Jan-26	02-Feb-26	288
PRO-26-1795	Review and approve Identification Tags for Electrical System Samples	15	12-Jan-26	02-Feb-26	288
PRO-26-1805	Review and approve Identification Tags for Electrical System ID Schedule	15	12-Jan-26	02-Feb-26	288
PRO-26-1785	Fabrication and delivery Identification Tags for Electrical System	30	03-Feb-26	19-Mar-26	288
260573.13 - SHORT CIRCUIT STUDIES		75	09-Oct-25	02-Feb-26	318
PRO-26-1450	Prepare and submit Short Circuit Study Report	60	09-Oct-25	09-Jan-26	318
PRO-26-1470	Review and approve Short Circuit Study Report	15	12-Jan-26	02-Feb-26	318
260573.16 - COORDINATION STUDIES		75	09-Oct-25	02-Feb-26	318
PRO-26-1475	Prepare and submit Coordination Study Report	60	09-Oct-25	09-Jan-26	318
PRO-26-1480	Review and approve Coordination Study Report	15	12-Jan-26	02-Feb-26	318
260800 - COMMISSIONING OF ELECTRICAL		95	09-Oct-25	04-Mar-26	397
PRO-26-1495	Prepare and submit Commissioning Procedures for Electrical Work	60	09-Oct-25	09-Jan-26	343
PRO-26-1500	Review and approve Commissioning Procedures for Electrical Work	15	12-Jan-26	02-Feb-26	343
PRO-26-1810	Prepare and submit Certificates of Completion for Electrical Work	20	03-Feb-26	04-Mar-26	397
260923 LIGHTING CONTROL DEVICES		95	09-Oct-25	04-Mar-26	291
PRO-26-1515	Prepare and submit Lighting Control Devices product data	60	09-Oct-25	09-Jan-26	291
PRO-26-1835	Prepare and submit Lighting Control Devices Shop Drawings	60	09-Oct-25	09-Jan-26	291
PRO-26-1520	Review and approve Lighting Control Devices product data	15	12-Jan-26	02-Feb-26	291
PRO-26-1840	Review and approve Lighting Control Devices Shop Drawings	15	12-Jan-26	02-Feb-26	291
PR0-26-1600	Fabrication and delivery of Lighting Control Devices	20	03-Feb-26	04-Mar-26	291
262413 SWITCHBOARDS		85	09-Oct-25	18-Feb-26	253
PRO-26-1525	Prepare and submit Switchboards product data	50	09-Oct-25	24-Dec-25	253
PRO-26-1845	Prepare and submit Switchboards Shop Drawings	50	09-Oct-25	24-Dec-25	253
PRO-26-1530	Review and approve Switchboards product data	15	26-Dec-25	16-Jan-26	253
PRO-26-1850	Review and approve Switchboards Shop Drawings	15	26-Dec-25	16-Jan-26	253

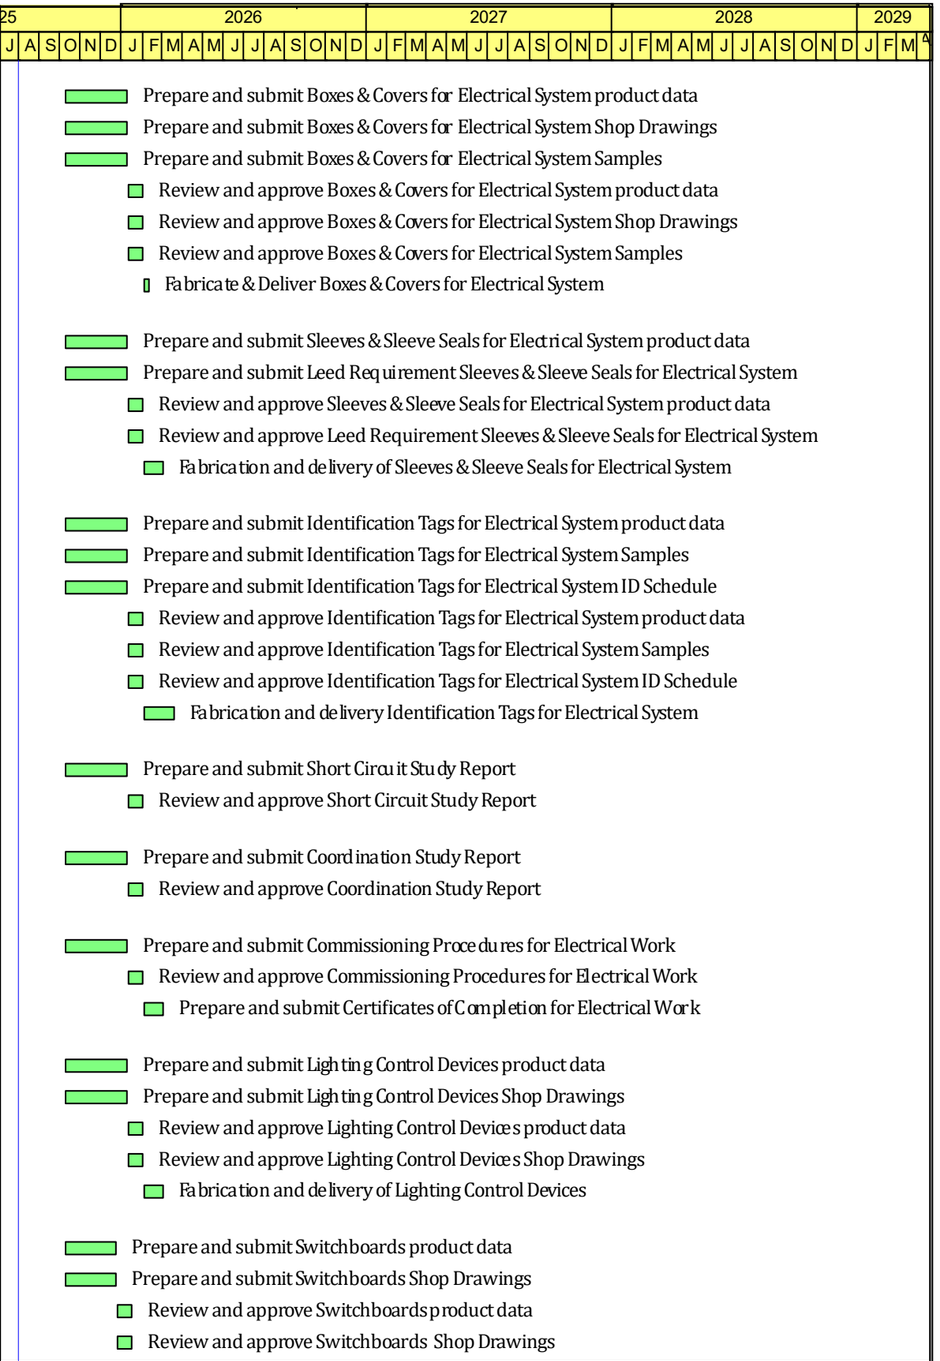

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PR0-26-1605	Fabrication and delivery of Switchboards	20	20-Jan-26	18-Feb-26	253
252416 PANELBOARDS		65	09-Oct-25	16-Jan-26	141
PR0-26-1535	Prepare and submit Panelboards product data	50	09-Oct-25	24-Dec-25	141
PR0-26-1855	Prepare and submit Panelboards Schedule	50	09-Oct-25	24-Dec-25	141
PR0-26-1865	Prepare and submit Panelboards Shop Drawings	50	09-Oct-25	24-Dec-25	141
PR0-26-1540	Review and approve Panelboards product data	15	26-Dec-25	16-Jan-26	141
PR0-26-1860	Review and approve Panelboards Schedule	15	26-Dec-25	16-Jan-26	141
PR0-26-1870	Review and approve Panelboards Shop Drawings	15	26-Dec-25	16-Jan-26	141
262713 ELECTRICITY METERING		85	09-Oct-25	18-Feb-26	303
PR0-26-1545	Prepare and submit Electricity Metering product data	50	09-Oct-25	24-Dec-25	303
PR0-26-1875	Prepare and submit Electricity Metering Shop Drawings	50	09-Oct-25	24-Dec-25	303
PR0-26-1550	Review and approve Electricity Metering product data	15	26-Dec-25	16-Jan-26	303
PR0-26-1880	Review and approve Electricity Metering Shop Drawings	15	26-Dec-25	16-Jan-26	303
PR0-26-1615	Fabrication and delivery of Electricity Metering	20	20-Jan-26	18-Feb-26	303
262726 WIRING DEVICES		95	09-Oct-25	04-Mar-26	291
PR0-26-1555	Prepare and submit Wiring Devices product data	60	09-Oct-25	09-Jan-26	291
PR0-26-1885	Prepare and submit Wiring Devices Samples	60	09-Oct-25	09-Jan-26	291
PR0-26-1895	Prepare and submit Wiring Devices Shop Drawings	60	09-Oct-25	09-Jan-26	291
PR0-26-1560	Review and approve Wiring Devices product data	15	12-Jan-26	02-Feb-26	291
PR0-26-1890	Review and approve Wiring Devices Samples	15	12-Jan-26	02-Feb-26	291
PR0-26-1900	Review and approve Wiring Devices Shop Drawings	15	12-Jan-26	02-Feb-26	291
PR0-26-1620	Fabrication and delivery of Wiring Devices	20	03-Feb-26	04-Mar-26	291
262813 - FUSES		95	09-Oct-25	04-Mar-26	243
PR0-26-1615	Prepare and submit Fuses product data	60	09-Oct-25	09-Jan-26	243
PR0-26-1620	Review and approve Fuses product data	15	12-Jan-26	02-Feb-26	243
PR0-26-1650	Fabrication and delivery of Fuses	20	03-Feb-26	04-Mar-26	243
262816 - ENCLOSED SWITCHES AND CIRSUIT BREAKERS		95	09-Oct-25	04-Mar-26	243
PR0-26-1605	Prepare and submit Enclosed Switches and Circuit Breakers product data	60	09-Oct-25	09-Jan-26	243
PR0-26-1610	Review and approve Enclosed Switches and Circuit Breakers product data	15	12-Jan-26	02-Feb-26	243
PR0-26-1645	Fabrication and delivery of Enclosed Switches and Circuit Breakers	20	03-Feb-26	04-Mar-26	243
262913.03 MANUAL AND MAGNETIC MOTOR CONTROLLERS		85	09-Oct-25	18-Feb-26	319
PR0-26-1595	Prepare and submit Manual & Magnetic Motor Controllers product data	50	09-Oct-25	24-Dec-25	319
PR0-26-1935	Prepare and submit Manual & Magnetic Motor Controllersv	50	09-Oct-25	24-Dec-25	319
PR0-26-1600	Review and approve Manual & Magnetic Motor Controllers product data	15	26-Dec-25	16-Jan-26	319
PR0-26-1940	Review and approve Manual & Magnetic Motor Controllers Shop Drawings	15	26-Dec-25	16-Jan-26	319
PR0-26-1640	Fabrication and delivery of Manual & Magnetic Motor Controllers	20	20-Jan-26	18-Feb-26	319
262913.06 - SOFT START MOTOR CONTROLLERS		85	09-Oct-25	18-Feb-26	319
PR0-26-2050	Prepare and submit Soft Start Motor Controllers product data	50	09-Oct-25	24-Dec-25	307
PR0-26-2070	Prepare and submit Soft Start Motor Controllers Shop Drawings	50	09-Oct-25	24-Dec-25	307
PR0-26-2040	Review and approve Soft Start Motor Controllers product data	15	26-Dec-25	16-Jan-26	307
PR0-26-2060	Review and approve Soft Start Motor Controllers Shop Drawings	15	26-Dec-25	16-Jan-26	307
PR0-26-1690	Fabrication and delivery of Soft Start Motor Controllers	20	20-Jan-26	18-Feb-26	319
265119 - LED INTERIOR LIGHTING		140	09-Oct-25	08-May-26	136

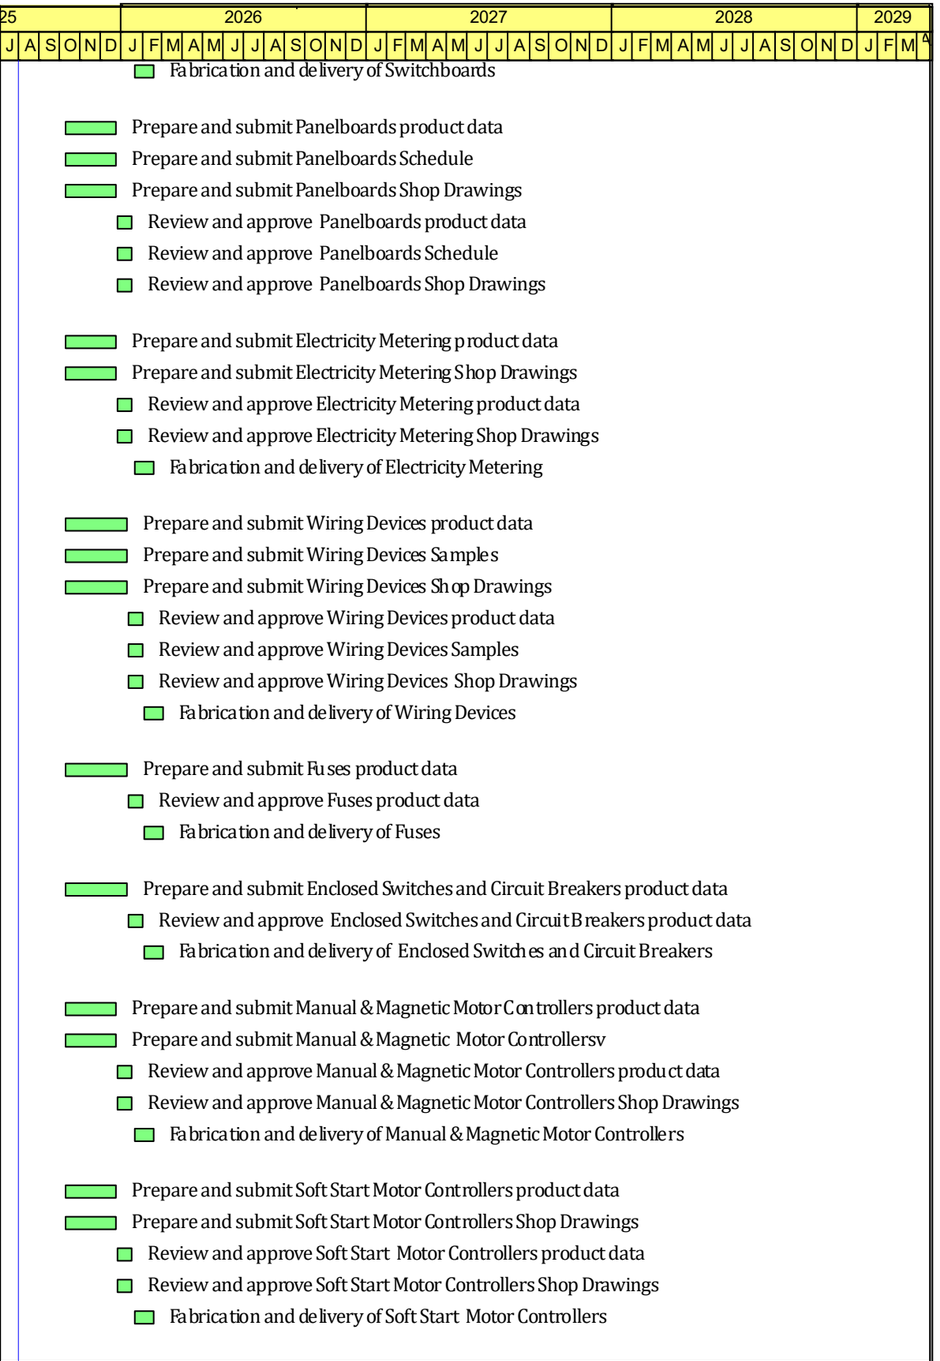

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PRO-26-1660	Prepare and submit LED Interior Lighting Shop Drawings	60	09-Oct-25	09-Jan-26	136
PRO-26-1975	Prepare and submit LED Interior Lighting product schedule	60	09-Oct-25	09-Jan-26	171
PRO-26-1985	Prepare and submit LED Interior Lighting product data	60	09-Oct-25	09-Jan-26	171
PRO-26-1980	Review and approve LED Interior Lighting product schedule	15	12-Jan-26	02-Feb-26	171
PRO-26-1990	Review and approve LED Interior Lighting Product Data	15	12-Jan-26	02-Feb-26	171
PRO-26-2000	Review and approve LED Interior Lighting Shop Drawings	50	12-Jan-26	26-Mar-26	136
PRO-26-1655	Prepare and submit LED Interior Lighting Mockup	15	27-Mar-26	17-Apr-26	136
PRO-26-1995	Review and approve LED Interior Lighting Mockup	15	20-Apr-26	08-May-26	136
265619 - LED EXTERIOR LIGHTING		95	09-Oct-25	04-Mar-26	317
PRO-26-1675	Prepare and submit LED Exterior Lighting product data	60	09-Oct-25	09-Jan-26	317
PRO-26-2005	Prepare and submit LED Exterior Lighting Shop Drawings	60	09-Oct-25	09-Jan-26	317
PRO-26-1680	Review and approve LED Exterior Lighting product data	15	12-Jan-26	02-Feb-26	317
PRO-26-2010	Review and approve LED Exterior Lighting Shop Drawings	15	12-Jan-26	02-Feb-26	317
PR0-26-1680	Fabrication and delivery of LED Exterior Lighting	20	03-Feb-26	04-Mar-26	317
DIVISION 27 - COMMUNICATIONS		85	09-Oct-25	18-Feb-26	333
270800 COMMISSIONING OF COMMUNICATION		65	09-Oct-25	16-Jan-26	353
PRO-27-1245	Prepare and submit Commissioning of Communication Procedure	50	09-Oct-25	24-Dec-25	353
PRO-27-1250	Review and approve Commissioning of Communication Procedure	15	26-Dec-25	16-Jan-26	353
271116 COMMUNICATION EQUIPMENT COMMUNICATION ROOMS		85	09-Oct-25	18-Feb-26	326
PRO-27-1215	Prepare and submit Communication Equipment Cabinets, Racks product data	50	09-Oct-25	24-Dec-25	326
PRO-27-1345	Prepare and submit Communication Equipment Cabinets, Racks Shop Drawings	50	09-Oct-25	24-Dec-25	326
PRO-27-1220	Review and approve Communication Equipment Cabinets, Racks product data	15	26-Dec-25	16-Jan-26	326
PRO-27-1350	Review and approve Communication Equipment Cabinets, Racks Shop Drawings	15	26-Dec-25	16-Jan-26	326
PR0-27-1250	Fabrication and delivery of Communication Equipment Cabinets, Racks	20	20-Jan-26	18-Feb-26	326
271513 COMMUNICATION HORIZONTAL CABLING FOR COMMUNICATION SYSTEMS		85	09-Oct-25	18-Feb-26	326
PRO-27-1255	Prepare and submit Communication Copper Horizontal Cabling product data	50	09-Oct-25	24-Dec-25	326
PRO-27-1395	Prepare and submit Communication Copper Horizontal Cabling Shop Drawings	50	09-Oct-25	24-Dec-25	326
PRO-27-1405	Prepare and submit Communication Copper Horizontal Cabling Samples	50	09-Oct-25	24-Dec-25	326
PRO-27-1260	Review and Communication Copper Horizontal Cabling product data	15	26-Dec-25	16-Jan-26	326
PRO-27-1400	Review and Communication Copper Horizontal Cabling Shop Drawings	15	26-Dec-25	16-Jan-26	326
PRO-27-1410	Review and Communication Copper Horizontal Cabling Samples	15	26-Dec-25	16-Jan-26	326
PR0-27-1270	Fabrication and delivery of Communication Copper Horizontal Cabling	20	20-Jan-26	18-Feb-26	326
271123 COMMUNICATION CONNECTION CORDS, DEVICE AND ADAPTERS		85	09-Oct-25	18-Feb-26	326
PRO-27-1235	Prepare and submit Communication Connector Cord, devices & Adapters product data	50	09-Oct-25	24-Dec-25	326
PRO-27-1375	Prepare and submit Communication Connector Cord, devices & Adapters Shop Drawings	50	09-Oct-25	24-Dec-25	326
PRO-27-1240	Review and approve Communication Connector Cord, devices &Adapters product data	15	26-Dec-25	16-Jan-26	326
PRO-27-1380	Review and approve Communication Connector Cord, devices &Adapters Shop Drawings	15	26-Dec-25	16-Jan-26	326
PR0-27-1260	Fabrication and delivery of Communication Connector Cord, devices & Adapters	20	20-Jan-26	18-Feb-26	326
274116 INTEGRATED AUDIOVISUAL SYSTEMS FOR COMMUNICATION SYSTEMS		85	09-Oct-25	18-Feb-26	319
PRO-27-1285	Prepare and submit Integrated Audiovisual System product data	50	09-Oct-25	24-Dec-25	319
PRO-27-1290	Review and approve Integrated Audiovisual System product data	15	26-Dec-25	16-Jan-26	319
PR0-27-1285	Fabrication and delivery of Integrated Audiovisual System	20	20-Jan-26	18-Feb-26	319

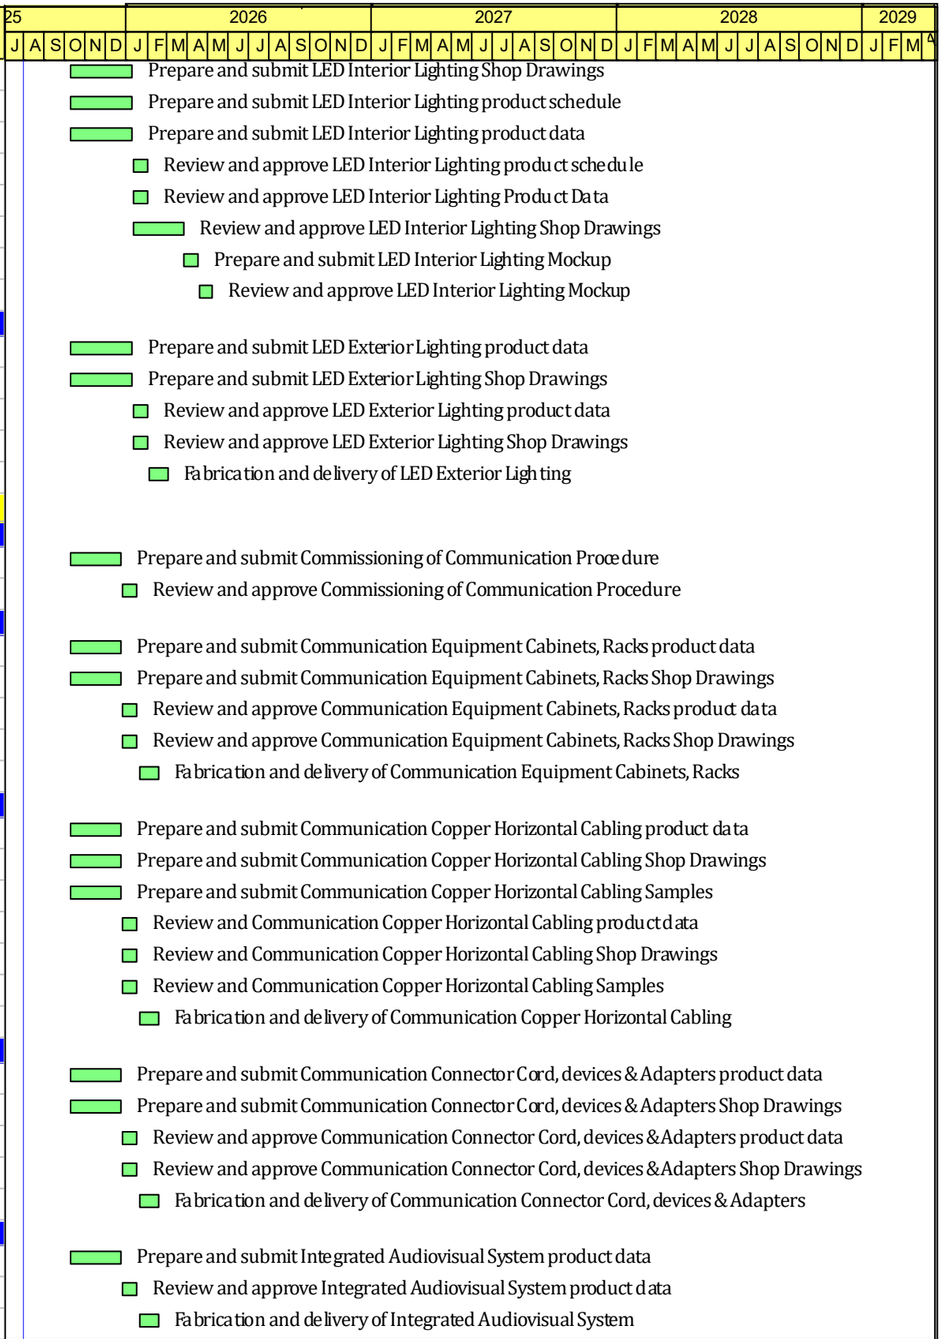

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
DIVISION 28 - ELECTRONIC SAFETY AND SECURITY		95	09-Oct-25	04-Mar-26	310
281510 - ACCESS CONTROL		95	09-Oct-25	04-Mar-26	310
PRO-28-1210	Prepare and submit Access Control product data	70	09-Oct-25	26-Jan-26	310
PRO-28-1215	Review and approve Access Control product data	15	27-Jan-26	18-Feb-26	310
PRO-28-1220	Fabrication and delivery of Access Control	10	19-Feb-26	04-Mar-26	310
282000 - VIDEO SURVEILLANCE		95	09-Oct-25	04-Mar-26	309
PRO-28-1240	Prepare and submit Video Surveillance product data	70	09-Oct-25	26-Jan-26	309
PRO-28-1295	Prepare and submit Video Surveillance Shop Drawings	70	09-Oct-25	26-Jan-26	309
PRO-28-1245	Review and approve Video Surveillance product data	15	27-Jan-26	18-Feb-26	309
PRO-28-1300	Review and approve Video Surveillance Shop Drawings	15	27-Jan-26	18-Feb-26	309
PRO-28-1250	Fabrication and delivery of Video Surveillance	10	19-Feb-26	04-Mar-26	309
283100 - INTRUSION DETECTION		95	09-Oct-25	04-Mar-26	310
PRO-28-1255	Prepare and submit Intrusion Detection product data	70	09-Oct-25	26-Jan-26	310
PRO-28-1260	Review and approve Intrusion Detection product data	15	27-Jan-26	18-Feb-26	310
PRO-28-1265	Fabrication and delivery of Intrusion Detection	10	19-Feb-26	04-Mar-26	310
284621.11 - ADDRESSABLE FIRE ALARM SYSTEM		85	09-Oct-25	18-Feb-26	314
PRO-28-1130	Prepare and submit Addressable fire alarm system shop drawings	70	09-Oct-25	26-Jan-26	274
PRO-28-1140	Prepare and submit Addressable fire alarm system product data	70	09-Oct-25	26-Jan-26	274
PRO-28-1305	Prepare and submit Addressable fire alarm system Permit	70	09-Oct-25	26-Jan-26	314
PRO-28-1150	Review and approve Addressable fire alarm system shop drawings	15	27-Jan-26	18-Feb-26	274
PRO-28-1160	Review and approve Addressable fire alarm system product data	15	27-Jan-26	18-Feb-26	274
PRO-28-1310	Obtain Addressable fire alarm system permit	15	27-Jan-26	18-Feb-26	314
DIVISION 31 - EARTHWORK		145	01-Aug-25	12-Mar-26	32
312000 - UNDERPINNING		61	01-Aug-25	30-Oct-25	86
PRO-31-1000	Prepare and submit Underpinning Test Reports	40	01-Aug-25	30-Sep-25	86
PRO-31-1175	Prepare and submit Underpinning Shop Drawings	10	01-Aug-25	15-Aug-25	116
PRO-31-1180	Review and approve Underpinning Shop Drawings	15	18-Aug-25	08-Sep-25	116
PRO-31-1010	Review and approve Underpinning Test Reports	15	01-Oct-25	22-Oct-25	86
PRO-31-1170	Delivery Material for Underpinning	6	23-Oct-25	30-Oct-25	86
315000 - EXCAVATION SUPPORT AND PROTECTION		85	30-Oct-25	12-Mar-26	17
PRO-31-1140	Prepare and submit earthwork/support of excavation Shop Drawings	60	30-Oct-25	02-Feb-26	17
PRO-31-1225	Prepare and submit earthwork/support of excavation Engineering	40	30-Oct-25	02-Jan-26	37
PRO-31-1235	Prepare and submit earthwork/support of excavation Shop Drawings	40	30-Oct-25	02-Jan-26	37
PRO-31-1150	Review and approve earthwork/support of excavation Shop Drawings	15	03-Feb-26	25-Feb-26	17
PRO-31-1230	Review and approve earthwork/support of excavation Engineering	15	03-Feb-26	25-Feb-26	17
PRO-31-1240	Review and approve earthwork/support of excavation Shop Drawings	15	03-Feb-26	25-Feb-26	17
PRO-31-1160	Fabrication and delivery of SOE	10	26-Feb-26	12-Mar-26	17
316316 AUGER CAST GROUT PILES		65	30-Oct-25	10-Feb-26	52
PRO-31-1265	Prepare and submit Auger Cast Grout Piles Shop Drawings	40	30-Oct-25	02-Jan-26	52
PRO-31-1270	Prepare and submit Auger Cast Grout Piles Design Mix	40	30-Oct-25	02-Jan-26	52
PRO-31-1275	Prepare and submit Auger Cast Grout Piles ID Plan	40	30-Oct-25	02-Jan-26	52
PRO-31-1280	Review and approve Auger Cast Grout Piles Shop Drawings	15	05-Jan-26	26-Jan-26	52
PRO-31-1285	Review and approve Auger Cast Grout Piles Design Mix	15	05-Jan-26	26-Jan-26	52

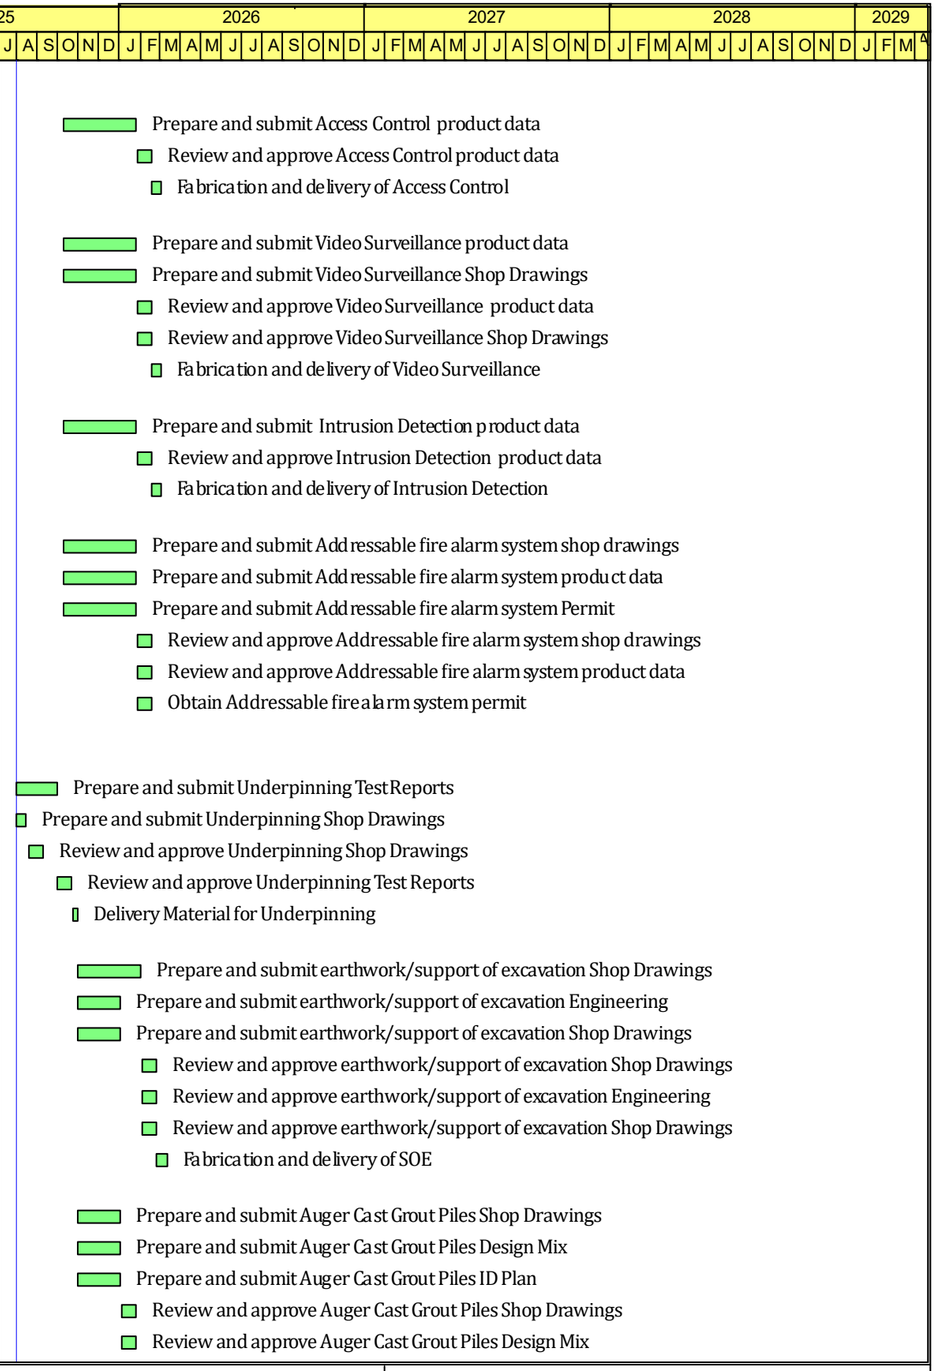

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PRO-31-1290	Review and approve Auger Cast Grout Piles ID Plan	15	05-Jan-26	26-Jan-26	52
PRO-31-1295	Fabrication and delivery of Auger Cast Grout Piles	10	27-Jan-26	10-Feb-26	52
DIVISION 32 - EXTERIOR IMPROVEMENTS		249	01-Aug-25	12-Aug-26	224
320110 - TEMPORARY TREE & PLANT PROTECTION		76	01-Aug-25	24-Nov-25	10
PRO-32-1080	Prepare and submit Temporary Tree & Plant Protection product data	60	01-Aug-25	29-Oct-25	10
PRO-32-1090	Review and approve Temporary Tree & Plant Protection product data	15	30-Oct-25	21-Nov-25	10
PRO-32-1140	Fabrication and delivery of Temporary Tree & Plant Protection materials	1	24-Nov-25	24-Nov-25	10
321213 - CONCRETE PAVING		80	10-Apr-26	05-Aug-26	168
PRO-32-1000	Prepare and submit concrete paving product data	60	10-Apr-26	07-Jul-26	168
PRO-32-1155	Prepare and submit concrete paving Design Mix	60	10-Apr-26	07-Jul-26	168
PRO-32-1010	Review and approve concrete paving product data	15	08-Jul-26	29-Jul-26	168
PRO-32-1160	Review and approve concrete paving Design Mix	15	08-Jul-26	29-Jul-26	168
PRO-32-1100	Fabrication and delivery of concrete paving	5	30-Jul-26	05-Aug-26	168
321400 - UNIT PAVERS		85	10-Apr-26	12-Aug-26	213
PRO-32-1040	Prepare and submit Unit Pavers product data	60	10-Apr-26	07-Jul-26	213
PRO-32-1145	Prepare and submit Unit Pavers Mockup	5	10-Apr-26	16-Apr-26	268
PRO-32-1150	Review and approve Unit Pavers Mockup	15	17-Apr-26	07-May-26	268
PRO-32-1050	Review and approve Unit Pavers product data	15	08-Jul-26	29-Jul-26	213
PRO-32-1120	Fabrication and delivery of Unit Pavers	10	30-Jul-26	12-Aug-26	213
321726 TACTILE WARNING SURFACING		25	10-Apr-26	15-May-26	208
PRO-32-1020	Prepare and submit Tactile Warning Surfacing product data	5	10-Apr-26	16-Apr-26	208
PRO-32-1030	Review and approve Tactile Warning Surfacing product data	15	17-Apr-26	07-May-26	208
PRO-32-1110	Fabrication and delivery of Tactile Warning Surfacing	5	08-May-26	15-May-26	208
323300 SITE FURNISHINGS		80	10-Apr-26	05-Aug-26	229
PRO-32-1180	Prepare and submit Site Furnishing product data	60	10-Apr-26	07-Jul-26	229
PRO-32-1190	Review and approve Site Furnishing product data	15	08-Jul-26	29-Jul-26	229
PRO-32-1170	Fabrication and delivery of Site Furnishing	5	30-Jul-26	05-Aug-26	229
328400 PLANTING IRRIGATION		80	10-Apr-26	05-Aug-26	222
PRO-32-1210	Prepare and submit Planting Irrigation product data	60	10-Apr-26	07-Jul-26	222
PRO-32-1220	Review and approve Planting Irrigation product data	15	08-Jul-26	29-Jul-26	222
PRO-32-1200	Fabrication and delivery of Planting Irrigation	5	30-Jul-26	05-Aug-26	222
329113 SOIL PREPARATION		85	10-Apr-26	12-Aug-26	163
PRO-32-1060	Prepare and submit Soil Preparation product data	60	10-Apr-26	07-Jul-26	163
PRO-32-1070	Review and approve Soil Preparation product data	15	08-Jul-26	29-Jul-26	163
PRO-32-1130	Fabrication and delivery of Soil Preparation materials	10	30-Jul-26	12-Aug-26	163
329300 - PLANTING		30	10-Apr-26	22-May-26	218
PRO-32-1240	Prepare and submit landscaping product data	5	10-Apr-26	16-Apr-26	218
PRO-32-1250	Review and approve landscaping product data	15	17-Apr-26	07-May-26	218
PRO-32-1230	Fabrication and delivery of landscaping materials	10	08-May-26	22-May-26	218
DIVISION 33 - SITE UTILITIES		55	30-Oct-25	26-Jan-26	257
331415 SITE WATER DISTRIBTION PIPING		55	30-Oct-25	26-Jan-26	257
PRO-33-1020	Prepare and submit Site Water Distribution Pipe product data	30	30-Oct-25	17-Dec-25	257
PRO-33-1040	Prepare and submit Site Water Distribution Pipe shop drawings	30	30-Oct-25	17-Dec-25	257

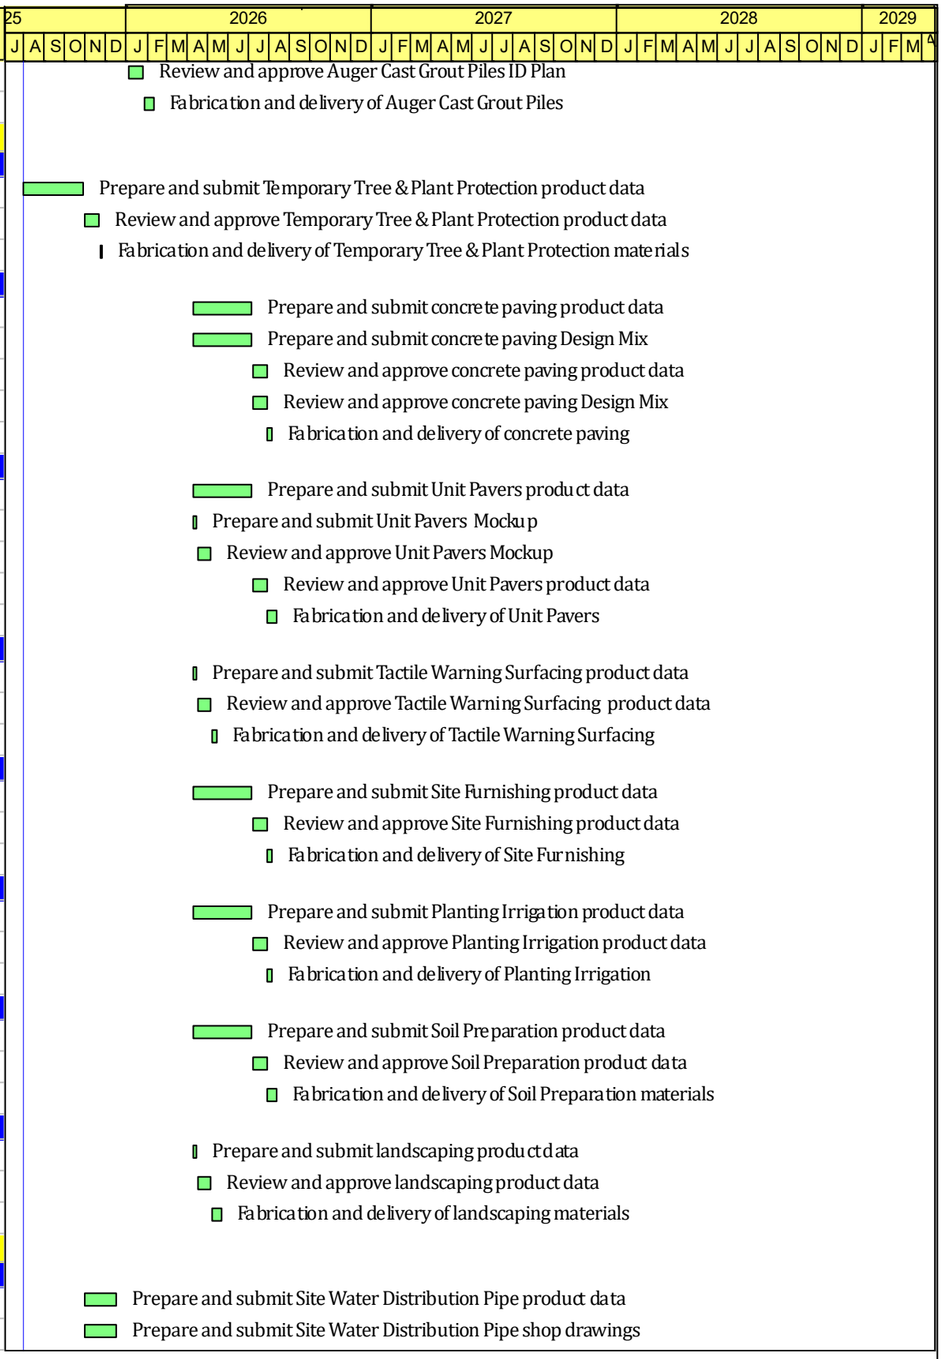

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PRO-33-1030	Review and approve Site Water Distribution Pipe product data	15	18-Dec-25	09-Jan-26	257
PRO-33-1050	Review and approve Site Water Distribution Pipe shop drawings	15	18-Dec-25	09-Jan-26	257
PRO-33-1000	Fabrication and delivery of Site Water Distribution Pipe materials	10	12-Jan-26	26-Jan-26	257
LONG LEAD ITEMS		206	18-Dec-25	22-Oct-26	169
PR0-23-1430	Fabrication and delivery of hvac vfd	60	18-Dec-25	19-Mar-26	207
PR0-08-1000	Fabrication and delivery of Wood Window Restoration	60	09-Jan-26	09-Apr-26	179
PRO-05-1000	Fabrication and delivery of steel structural framing	60	15-Jan-26	15-Apr-26	84
PR0-23-1460	Fabrication and delivery of instrumentation & control for hvac	60	20-Jan-26	17-Apr-26	187
PR0-26-1520	Fabrication and delivery of panel board & transformers	132	20-Jan-26	03-Aug-26	141
PR0-08-1060	Fabrication and delivery of aluminum entrance and storefront	100	03-Feb-26	01-Jul-26	123
PR0-26-1510	Fabrication and delivery of distribution switchboards	132	03-Feb-26	18-Aug-26	131
PR0-08-1770	Fabrication and delivery of Aluminium Entrances	60	03-Feb-26	01-May-26	260
PRO-04-1090	Fabricate and deliver Stone Masonry	90	06-Feb-26	19-Jun-26	106
PR0-28-1010	Fabrication and delivery of fire alarm system	40	19-Feb-26	17-Apr-26	274
PR0-23-1620	Fabrication and delivery of Dedicated Air Units	120	19-Feb-26	14-Aug-26	84
PR0-21-1080	Fabrication and delivery of Fire Pump	60	26-Feb-26	26-May-26	196
PR0-08-1070	Fabrication and delivery of Curtain Wall Glazing	100	09-Mar-26	03-Aug-26	106
PRO-05-1020	Fabrication and delivery of miscellaneous metals	60	16-Mar-26	11-Jun-26	92
PRO-05-1030	Fabrication and delivery of Metal Pan stairs metal framing material	40	16-Mar-26	11-May-26	236
PRO-05-1430	Fabrication and delivery of Stair Railings	40	16-Mar-26	11-May-26	242
PR0-08-1100	Fabrication and delivery of door hardware	40	27-Mar-26	26-May-26	214
PR0-14-1040	Fabrication and delivery of Hyrdraulic Elevator equipment	140	27-Mar-26	21-Oct-26	115
PR0-08-1760	Fabrication and delivery of Hollow Metal Doors	60	27-Mar-26	24-Jun-26	194
PR0-08-1790	Fabrication and delivery of Access Doors	60	27-Mar-26	24-Jun-26	68
PR0-11-1020	Fabrication and delivery of Metal Shelving	40	29-Apr-26	26-Jun-26	248
PR0-26-1590	Fabrication and delivery of architectural lighting fixtures	110	11-May-26	21-Oct-26	136
PR0-08-1110	Fabrication and delivery of glass and glazing	100	19-May-26	14-Oct-26	157
PRO-05-1425	Fabrication and delivery of Architectural Woodwork	60	14-Jul-26	09-Oct-26	175
PR0-08-1780	Fabrication and delivery of Aluminium Windows	60	27-Jul-26	22-Oct-26	57
PRE-CONSTRUCTION		515	01-Aug-25	22-Jul-27	0
PERMITTING AND LICENSING AGREEMENTS		104	01-Aug-25	08-Jan-26	268
PER-1010	Procure fence permit	40	01-Aug-25	30-Sep-25	35
PER-1020	Procure dot permit	70	01-Aug-25	13-Nov-25	3
SITE-1000	Con Edison Point of Entry	40	01-Aug-25	30-Sep-25	332
PER-1065	DEP Permit	40	01-Aug-25	30-Sep-25	332
PER-1040	Procure Scaffolding permit	20	01-Aug-25	29-Aug-25	288
PER-1045	Procure Sidewalk Shed Bridge permit	20	16-Sep-25	15-Oct-25	20
PER-1030	Obtain Demolition permit	5	03-Dec-25	09-Dec-25	4
PER-1000	Apply DOB for Excavaton permit	10	10-Dec-25	24-Dec-25	44
PER-1055	Apply DOB for building permit	10	24-Dec-25	08-Jan-26	179
MOBILIZATION		515	01-Aug-25	22-Jul-27	0



Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
MOB-1000	General Conditions (Meetings, CPM Updates, Supplies,Dumpster's,Storage Etc)	721	01-Aug-25	22-Jul-27	0
MOB-1005	Setup MPT	2	14-Nov-25	17-Nov-25	3
MOB-1040	Install Sidewalk Bridge Shed	15	14-Nov-25	09-Dec-25	0
MOB-1010	Prepare site for field office setup	5	18-Nov-25	25-Nov-25	3
MOB-1015	Install Construction (temporary) Fencing at Property Lines and Curbs	5	18-Nov-25	25-Nov-25	3
MOB-1045	Field Office Setup	10	18-Nov-25	04-Dec-25	3
MOB-1020	Install Soil Erosion & Sediment Control Measures	3	18-Nov-25	21-Nov-25	14
MOB-1025	Pre-Construction Photo Documentation	5	18-Nov-25	25-Nov-25	12
MOB-1035	Provide Utility Markouts	5	18-Nov-25	25-Nov-25	4
MOB-1030	Install Temporary Tree & Plant Protection	3	25-Nov-25	01-Dec-25	10
MOB-1050	Install project sign	5	26-Nov-25	04-Dec-25	3
MOB-1055	Furnish temporary toilets	3	10-Dec-25	12-Dec-25	1
MOB-1060	Install Vibration Monitoring Equipment	4	10-Dec-25	16-Dec-25	0
MOB-1065	Take Soil borings for Waste Characterization	1	24-Dec-25	24-Dec-25	37
MOB-1075	Receive results for Soil Disposal	10	26-Dec-25	09-Jan-26	37
MOB-1070	Surveying	254	02-Feb-26	18-Feb-27	19
ENABLING UTILITIES		20	26-Nov-25	29-Dec-25	186
UTIL-1000	Installation of temporary electrical service	20	26-Nov-25	29-Dec-25	186
UTIL-1010	Disconnect Electric to Existing Building	3	26-Nov-25	02-Dec-25	4
UTIL-1015	Disconnect Gas to Existing Building	3	26-Nov-25	02-Dec-25	4
UTIL-1020	Disconnect Water Service and Sewer to Existing Building	3	26-Nov-25	02-Dec-25	4
CONSTRUCTION		513	01-Aug-25	20-Jul-27	2
SITE DEMOLITION		5	02-Dec-25	08-Dec-25	10
CLEA-1000	Perform Site Clearing	5	02-Dec-25	08-Dec-25	10
ACM ABATEMENT		77	01-Aug-25	25-Nov-25	7
ASB-1000	MPCC to Procure Abatement Contractor	47	01-Aug-25	10-Oct-25	7
ASB-1005	ACM Ten day Notification Filings CCDs	10	13-Oct-25	24-Oct-25	7
ASB-1010	ACM Abatement of Existing Building	20	27-Oct-25	25-Nov-25	7
BUILDING DEMOLITION		50	17-Dec-25	03-Mar-26	0
BUILDING DEMOLITION FOR NEW ADDITION		50	17-Dec-25	03-Mar-26	0
DEMO-1010	Demo Existing South Elevation of Existing Roof Equipment & Slab	5	17-Dec-25	23-Dec-25	0
DEMO-1011	Demo Existing East Elevation of Existing Building	5	17-Dec-25	23-Dec-25	0
DEMO-1014	Demo Existing Interior Partions of Existing Building	15	17-Dec-25	08-Jan-26	5
DEMO-1015	Demo Existing MEP's of Existing Building	15	17-Dec-25	08-Jan-26	5
DEMO-1012	Demo Existing South Elevation of Existing Building	10	24-Dec-25	08-Jan-26	0
DEMO-1013	Demo Existing West Elevation of Existing Building	5	09-Jan-26	15-Jan-26	0
DEMO-1125	Demo Existing South Elevation of Existing Slabs	10	16-Jan-26	30-Jan-26	0
DEMO-1025	Demo Existing South Elevation of Existing Building Building Foundation	20	02-Feb-26	03-Mar-26	0
BUILDING DEMOLITION OF EXISTING BUILDING		45	24-Dec-25	03-Mar-26	0
DEMO-1100	Demolition of Existing Building Elevator	15	24-Dec-25	15-Jan-26	0
DEMO-1115	Demolition of Existing Building Interior Paritions	15	16-Jan-26	09-Feb-26	0
DEMO-1110	Demolition of Existing Building Circulation Stair	15	16-Jan-26	09-Feb-26	0

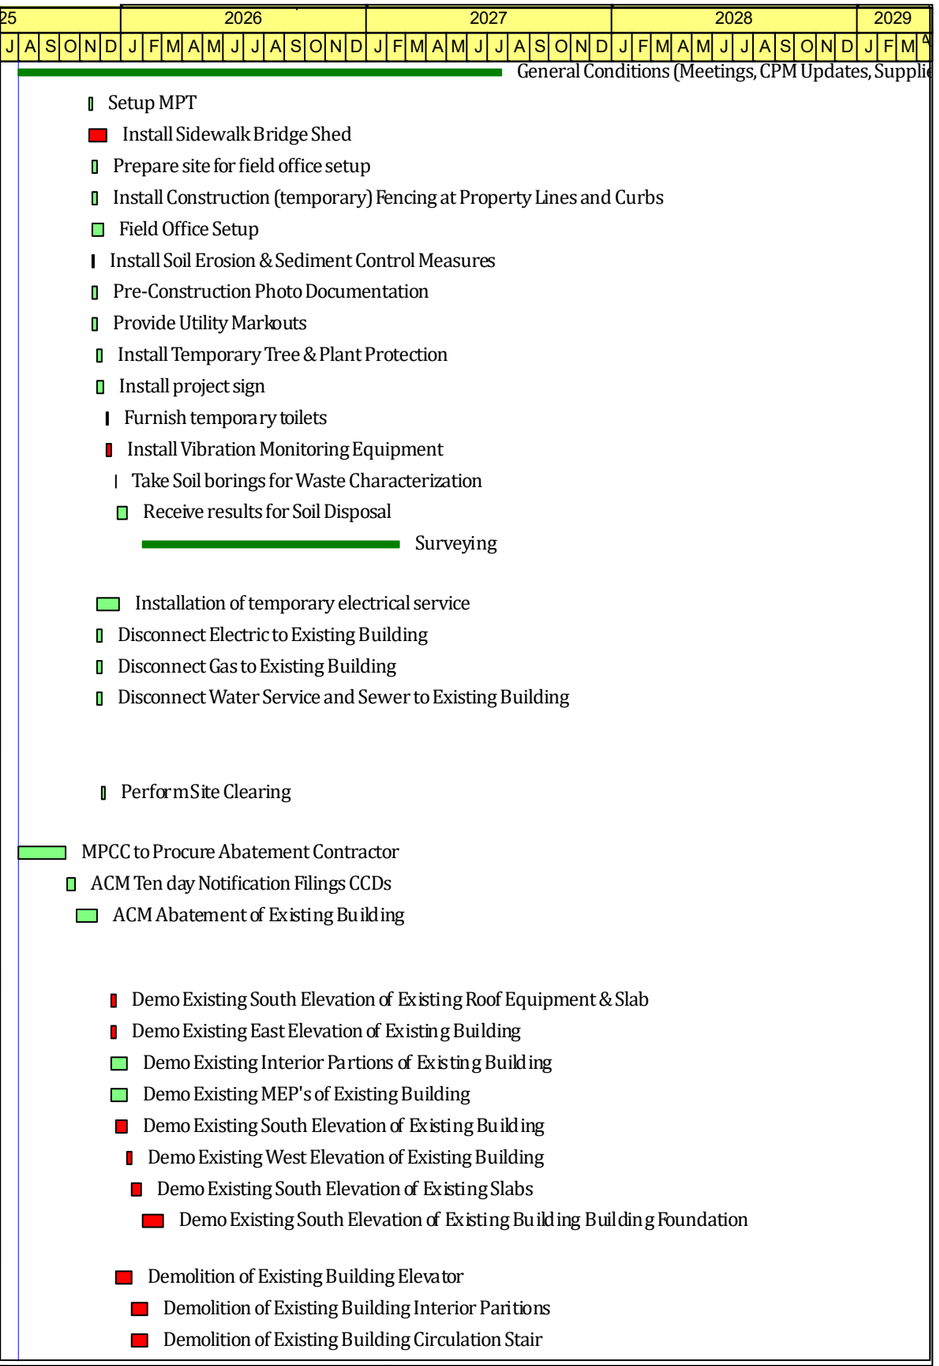

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
DEMO-1120	Demolition of Existing Building Atrium Area	15	10-Feb-26	03-Mar-26	0
NEW ADDITION CONSTRUCTION		345	04-Mar-26	29-Jun-27	17
EXCAVATION		8	04-Mar-26	16-Mar-26	0
ADD-1010	Dispose of Excavated Material	5	04-Mar-26	10-Mar-26	3
ADD-1015	Excavate Cellar Area	8	04-Mar-26	16-Mar-26	0
UNDERPINNING		15	17-Mar-26	06-Apr-26	0
ADD-1020	Install underpinning of Existing Building Cellar Area	15	17-Mar-26	06-Apr-26	0
SUPPORT OF EXCAVATION		15	08-Apr-26	28-Apr-26	0
ADD-1025	Install Support of Excavation for new Addition	15	08-Apr-26	28-Apr-26	0
AUGER GROUT PILES		15	29-Apr-26	20-May-26	0
ADD-1000	Install Augered Cast Grout Piles	15	29-Apr-26	20-May-26	0
UNDERGROUND PLUMBING		15	07-Jul-26	28-Jul-26	0
PLUMBING		15	07-Jul-26	28-Jul-26	0
ADD-1060	Install Underground plumbing of Building	15	07-Jul-26	28-Jul-26	0
ADD-1260	Install Underground Electrical Conduit from electrical room to custodian Room of Building	15	07-Jul-26	28-Jul-26	0
ADD-1335	Hold Point Inspection to backfill	15	07-Jul-26	28-Jul-26	0
FOUNDATIONS		141	21-May-26	03-Dec-26	129
FOOTINGS		16	21-May-26	11-Jun-26	0
ADD-1005	Form/ Rebar/Pour Concrete Footings for New Building Addition	10	21-May-26	04-Jun-26	0
ADD-1035	Cure Concrete Footings for New Building Addition	7	05-Jun-26	11-Jun-26	0
WALLS		22	05-Jun-26	06-Jul-26	0
ADD-1030	Form/ Rebar/Pour Concrete Foundation Walls for New Building Addition	16	05-Jun-26	29-Jun-26	0
ADD-1055	Cure Concrete Foundation Walls for New Building Addition	7	30-Jun-26	06-Jul-26	0
ELEVATOR PIT		130	05-Jun-26	03-Dec-26	129
ADD-1040	Form/ Rebar/Pour Concrete Walls Elevator Pit & Sump Pit	5	05-Jun-26	12-Jun-26	11
ADD-1045	Cure Concrete Walls Elevator Pit & Sump Pit	7	13-Jun-26	19-Jun-26	17
ADD-1050	Install crystalline waterproofing material Elevator Pit & Sump Pit	5	25-Nov-26	03-Dec-26	120
BACKFILL CELLAR		5	15-Jul-26	21-Jul-26	0
ADD-1065	Backfill area to allow pouring of slab on grade	5	15-Jul-26	21-Jul-26	0
SLAB		20	22-Jul-26	18-Aug-26	0
ADD-1070	Install Waterproofing under slab	5	22-Jul-26	28-Jul-26	0
ADD-1075	Form/ Rebar/Pour Cellar Slab on Grade	10	29-Jul-26	11-Aug-26	0
ADD-1080	Cure Cellar Slab on Grade	7	12-Aug-26	18-Aug-26	0
NEW ADDITION SUPERSTRUCTURE		59	19-Aug-26	09-Nov-26	135
STRUCTURAL STEEL COLUMNS & HORIZONTAL BEAMS & SLABS		59	19-Aug-26	09-Nov-26	29
STRUCTURAL STEEL COLUMNS CELLAR		5	19-Aug-26	25-Aug-26	0
ADD-1085	Install Structural Steel Columns Cellar Floor	5	19-Aug-26	25-Aug-26	0
GROUND LEVEL TO 2ND FLOOR		19	26-Aug-26	21-Sep-26	0
ADD-1090	Install Structural Steel Columns & Crossbeams 1st Floor Up to 2nd Floor Deck	5	26-Aug-26	01-Sep-26	0
ADD-1100	Install Metal Pan & Studs 1st Floor Concrete Slab	4	02-Sep-26	08-Sep-26	0
ADD-1105	Install Floor Drains, 1st floor	2	09-Sep-26	11-Sep-26	0
ADD-1110	Pour 1st Floor Concrete Slab	1	14-Sep-26	14-Sep-26	0
ADD-1120	Cure 1st floor Slab	7	15-Sep-26	21-Sep-26	0
2ND FLOOR		30	02-Sep-26	13-Oct-26	0

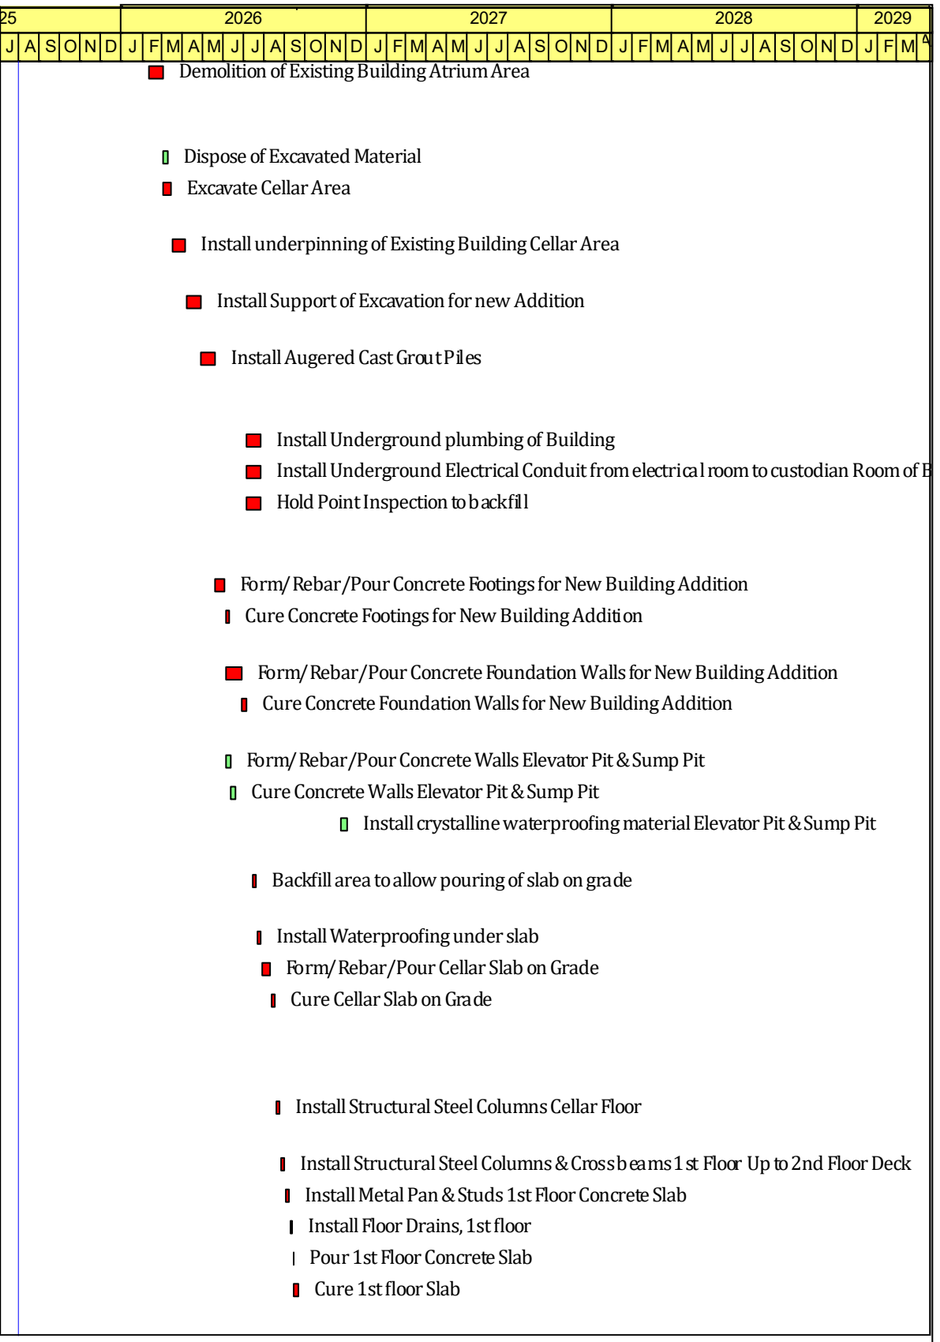

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
ADD-1095	Install Structural Steel Columns & Crossbeams 2nd floor	5	02-Sep-26	09-Sep-26	10
ADD-1130	Install Protection Barrier for 2nd Floor Slab Construction	3	22-Sep-26	24-Sep-26	0
ADD-1140	Install Metal Pan & Studs Second Floor Concrete Slab	4	25-Sep-26	30-Sep-26	0
ADD-1145	Install Floor Drains, 2nd floor	2	02-Oct-26	05-Oct-26	0
ADD-1150	Pour Second Floor Concrete Slab	1	06-Oct-26	06-Oct-26	0
ADD-1155	Cure 2nd Slab	7	07-Oct-26	13-Oct-26	0
3RD FLOOR TO ROOF		37	11-Sep-26	02-Nov-26	0
ADD-1115	Install Structural Steel Columns & Crossbeams 3rd floor up to Roof	5	11-Sep-26	17-Sep-26	20
ADD-1160	Install Protection Barrier for 3rd Floor Slab Construction	3	14-Oct-26	16-Oct-26	0
ADD-1170	Install Metal Pan & Studs Third Floor Concrete Slab	5	19-Oct-26	23-Oct-26	0
ADD-1180	Install Floor Drains, 3rd floor	2	22-Oct-26	23-Oct-26	0
ADD-1185	Pour 3rd Floor Concrete Slab	1	26-Oct-26	26-Oct-26	0
ADD-1200	Cure 3rd Slab	7	27-Oct-26	02-Nov-26	0
ROOF DECK		11	26-Oct-26	09-Nov-26	29
ADD-1175	Install Metal Pan & Studs Concrete Roof Slab	3	26-Oct-26	28-Oct-26	2
ADD-1190	Install Roof Drains	2	27-Oct-26	28-Oct-26	2
ADD-1195	Install Rooftop Dunnage Steel	3	29-Oct-26	02-Nov-26	31
ADD-1205	Pour Roof Concrete Deck	1	29-Oct-26	29-Oct-26	2
ADD-1210	Cure Roof Slab	7	03-Nov-26	09-Nov-26	0
STAIR "A"		5	18-Sep-26	24-Sep-26	150
ADD-1125	Installation of Stair "A" Stringers amd tread pans	5	18-Sep-26	24-Sep-26	150
STAIR "B"		5	25-Sep-26	02-Oct-26	150
ADD-1255	Installation of Stairs "B" Stringers amd tread pans	5	25-Sep-26	02-Oct-26	150
NEW ADDITION EXTERIOR ENCLOSURE		55	10-Nov-26	02-Feb-27	0
EXTERIOR SCAFFOLDING		10	10-Nov-26	24-Nov-26	0
ADD-1220	Installation of Exterior Scaffolding	10	10-Nov-26	24-Nov-26	0
WEST ELEVATION		45	25-Nov-26	02-Feb-27	0
ADD-1235	Installation of West Exterior Facade	15	25-Nov-26	17-Dec-26	0
ADD-1270	Installation of West Elevation Curtainwall framing	15	18-Dec-26	11-Jan-27	0
ADD-1300	Restoration of West Elevation Existing Wood Windows	10	18-Dec-26	04-Jan-27	20
ADD-1280	Installation of West Elevation Curtainwall Glazing	15	12-Jan-27	02-Feb-27	0
SOUTH ELEVATION		20	18-Dec-26	19-Jan-27	10
ADD-1240	Installation of South Exterior Facade	10	18-Dec-26	04-Jan-27	0
ADD-1290	Installation of South Elevation Windows	10	05-Jan-27	19-Jan-27	10
EAST ELEVATION		20	05-Jan-27	02-Feb-27	0
ADD-1245	Installation of East Exterior Facade	10	05-Jan-27	19-Jan-27	0
ADD-1310	Restoration of East Elevation Existing Wood Windows	10	20-Jan-27	02-Feb-27	0
NORTH ELEVATION		20	21-Dec-26	20-Jan-27	9
ADD-1320	Restoration of North Elevation Existing Wood Windows	20	21-Dec-26	20-Jan-27	9
ADD-1330	Restoration of North Elevation Storefront	20	21-Dec-26	20-Jan-27	9
NEW ADDITION INTERIOR WORK		201	22-Sep-26	29-Jun-27	17
CELLAR FLOOR NEW ADDITION		141	22-Sep-26	21-Apr-27	62
CEL-1000	Install Overhead Plumbing Pipe, Cellar Floor	15	22-Sep-26	13-Oct-26	9

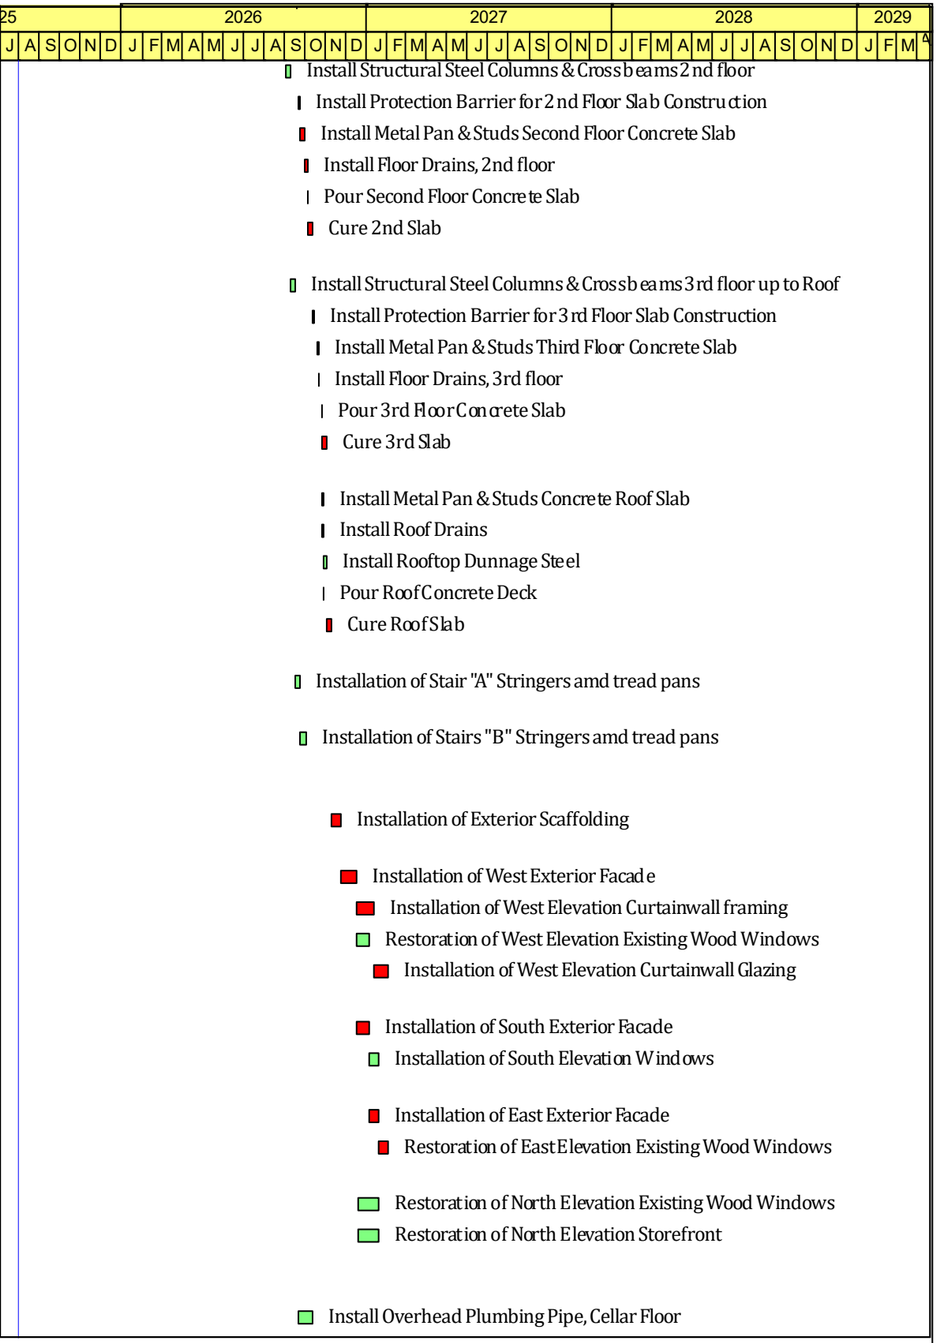

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
CEL-1010	Install Overhead Sprinkler Pipe, Cellar Floor	15	22-Sep-26	13-Oct-26	9
CEL-1005	Install Overhead Electrical, Cellar Floor	15	22-Sep-26	13-Oct-26	9
CEL-1260	Install Overhead Mechanical Ductwork & Split AC Units Cellar Floor	15	22-Sep-26	13-Oct-26	9
CEL-1015	Install Walls Framing Cellar Floor	15	14-Oct-26	03-Nov-26	9
CEL-1020	Install Plumbing Piping in Walls Cellar Floor	10	14-Oct-26	27-Oct-26	63
CEL-1025	Install Sprinkler Piping thru Walls, Cellar Floor	10	14-Oct-26	27-Oct-26	68
CEL-1030	Install Electrical Rough-in in Walls Cellar Floor	10	14-Oct-26	27-Oct-26	68
CEL-1270	Install Mechanical Ductwork in Walls Cellar Floor	10	14-Oct-26	27-Oct-26	68
CEL-1275	Install Overhead Mechanical Piping Cellar Floor	15	14-Oct-26	03-Nov-26	48
CEL-1290	Installl Control Dampers in Ductwork Cellar Floor	10	14-Oct-26	27-Oct-26	145
CEL-1045	Leak test & insulate Plumbing piping walls Cellar Floor	5	28-Oct-26	03-Nov-26	63
CEL-1300	Pull & Terminate Wires for Control Dampers Cellar Floor	10	28-Oct-26	10-Nov-26	145
CEL-1055	Install Mechanical Unit Heaters System Cellar Floor	15	04-Nov-26	25-Nov-26	48
CEL-1285	Install Mechanical Piping in Walls Cellar Floor	15	04-Nov-26	25-Nov-26	48
CEL-1296	Hold Point to start Gypsum Board wall and ceilings Cellar Floor	1	30-Nov-26	30-Nov-26	48
CEL-1295	Install Gypsum Board wall and ceilings Cellar Floor	10	03-Feb-27	18-Feb-27	5
CEL-1315	Perform Tape & Spackle Cellar Floor	5	19-Feb-27	25-Feb-27	47
CEL-1925	Install CCTVs Cellar	7	26-Feb-27	08-Mar-27	71
CEL-1690	Install Audiovisual Equipment Cellar	7	26-Feb-27	08-Mar-27	71
CEL-1655	Pull Communication cable,Install Telecom Outlets Cellar Floor	7	13-Apr-27	21-Apr-27	48
CEL-1680	Pull Security cable,Install Security Outlets Cellar Floor	7	13-Apr-27	21-Apr-27	48
CEL-1685	Pull Audiovisual cable,Install Audiovisual Outlets Cellar Floor	7	13-Apr-27	21-Apr-27	48
ELECTRICAL ROOM 009		116	22-Sep-26	16-Mar-27	53
CEL-1001	Form/Rebar/Pour Concrete Pads in Electrical Service Room	5	22-Sep-26	28-Sep-26	104
CEL-2445	Install Fire Pump Electrical Switch in Electrical Service Room	2	29-Sep-26	30-Sep-26	107
CEL-2450	Install Battery Inverter for emergency Lighting in Electrical Service Room	2	29-Sep-26	30-Sep-26	107
CEL-1160	Install Electrical Switchboards in Electrical Service Room	5	30-Nov-26	04-Dec-26	64
CEL-2165	Install Electrical Main Distribution Panelboard (MDP) in Electrical Service Room	5	30-Nov-26	04-Dec-26	64
CEL-2175	Install Electrical Distribution Switch (PBS) in Electrical Service Room	5	30-Nov-26	04-Dec-26	64
CEL-2440	Install Electrical Service End Box in Electrical Service Room	5	30-Nov-26	04-Dec-26	94
CEL-1190	Install Conduit in Electrical Service Room	20	07-Dec-26	05-Jan-27	64
CEL-1006	Pull Load Side Cable in Electrical Service Room towards Custodian Room Risers	15	07-Dec-26	28-Dec-26	99
CEL-1245	Pull & Terminate Electrical Cable in Electrical Service Room	15	06-Jan-27	27-Jan-27	74
CEL-1265	Install Con Edison Electric Meter & Terminate Cable in Electrical Service Room	5	02-Mar-27	08-Mar-27	53
CEL-1495	Inspection & Energize Electrical Service	5	09-Mar-27	16-Mar-27	53
PLUMBING ROOM 005		31	04-Nov-26	21-Dec-26	119
005-1000	Install new RPZ & Water Rig	5	04-Nov-26	10-Nov-26	72
005-1010	Install Sprinkler & Jockey Equipment	2	04-Nov-26	05-Nov-26	87
005-1110	Install Sewage Ejector Pump & Panel	2	04-Nov-26	05-Nov-26	128
005-1120	Install DEP Transfer Pump & Panel	2	04-Nov-26	05-Nov-26	128
005-1020	Install Sprinkler & Jockey Piping	19	06-Nov-26	07-Dec-26	87

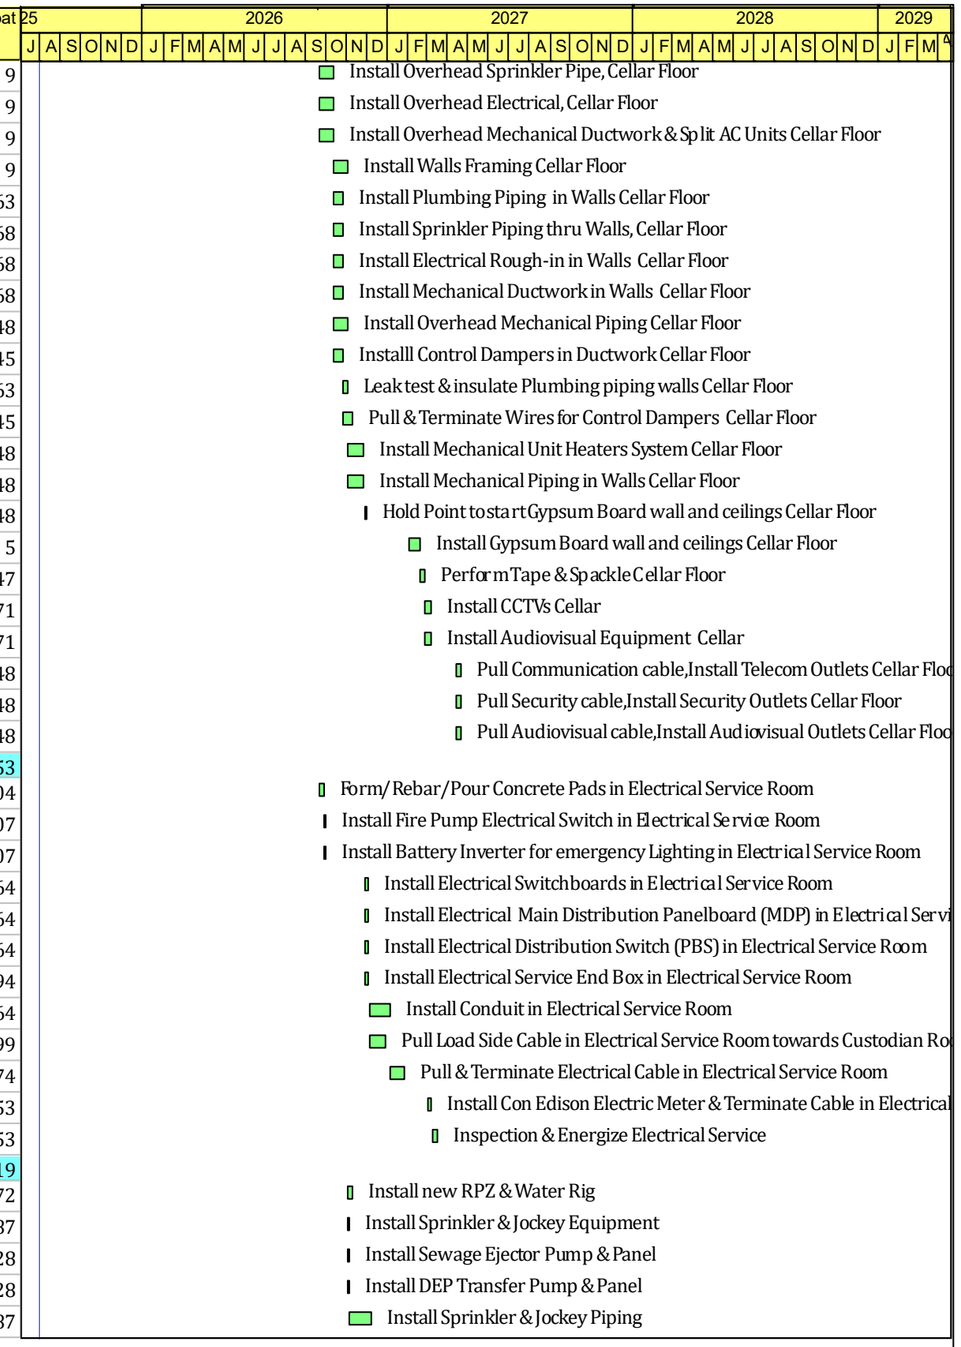

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
005-1130	Install Sanitary Discharge Piping	10	06-Nov-26	20-Nov-26	128
005-1140	Install DEP Transfer Pump Piping	10	06-Nov-26	20-Nov-26	128
005-1030	Install Domestic Water Piping from RPZ to Feed tank	10	12-Nov-26	25-Nov-26	72
005-1150	Pull Electrical Cable	5	23-Nov-26	01-Dec-26	128
005-1160	Terminate Sewage Ejector Pump & Panel	5	23-Nov-26	01-Dec-26	128
005-1170	Leak Test Water Pipe & Insulate	1	23-Nov-26	23-Nov-26	129
005-1180	Pull Electrical Cable for DEP Transfer Pump	5	23-Nov-26	01-Dec-26	128
005-1190	Terminate DEP Transfer Pump & Panel	5	23-Nov-26	01-Dec-26	128
005-1200	Leak Test Water Pipe & Insulate	1	23-Nov-26	23-Nov-26	129
005-1210	Connect Interior Sanitary Pipe	3	24-Nov-26	30-Nov-26	129
005-1220	Connect Interior Sanitary Pipe	3	24-Nov-26	30-Nov-26	129
005-1040	Install New Make-up Water Tank	2	30-Nov-26	01-Dec-26	72
005-1050	Install Heat Trace onWater Pipe & Insulate	1	30-Nov-26	30-Nov-26	73
005-1060	Leak Test Water Pipe & Insulate	1	02-Dec-26	02-Dec-26	72
005-1230	Preliminary Sewage Ejector Pump & Panel	5	02-Dec-26	08-Dec-26	128
005-1240	Preliminary DEP Transfer Pump	5	02-Dec-26	08-Dec-26	128
005-1070	Connect Water Service Pipe	3	03-Dec-26	07-Dec-26	72
005-1080	Pull & Terminate Electrical Cable	5	08-Dec-26	14-Dec-26	119
005-1090	Connect Sprinkler & Jockey Service Pipe	5	08-Dec-26	14-Dec-26	87
005-1100	Preliminary Test Sprinkler & Jockey Pump	5	15-Dec-26	21-Dec-26	119
STAIR "A" 006		16	25-Sep-26	19-Oct-26	155
006-1060	Install Concrete Fill Stair "A"	1	25-Sep-26	25-Sep-26	150
006-1065	Install Guard Rails & Tube Railings Stair "A"	5	28-Sep-26	05-Oct-26	150
006-1070	Install Electrical Stair Conduit Stair "A"	5	06-Oct-26	12-Oct-26	150
006-1075	Install Lighting Fixtures & Pull & Terminate Wire Stair "A"	5	13-Oct-26	19-Oct-26	155
LEARNING LAB 007		27	19-Feb-27	30-Mar-27	77
007-1000	Install Black Iron Grid Learning Room	5	19-Feb-27	25-Feb-27	16
007-1005	Install Lighting Fixtures & Control Devices Learning Room	5	26-Feb-27	04-Mar-27	53
007-1010	Prime Paint Ceiling Learning Room	5	05-Mar-27	12-Mar-27	53
007-1015	Pull & Terminate Lighting Cable Learning Room	5	05-Mar-27	12-Mar-27	56
007-1025	Final Paint Learning Room	1	15-Mar-27	15-Mar-27	53
007-1030	Install Terrazzo Flooring Learning Room	2	16-Mar-27	17-Mar-27	53
007-1055	Test Lighting Learning Room	1	17-Mar-27	17-Mar-27	86
007-1035	Install Acoustical Ceilings Learning Room	5	18-Mar-27	24-Mar-27	56
007-1020	Install Fire Alarm Devices and System Learning Room	6	18-Mar-27	25-Mar-27	53
007-1040	Install Sprinkler Heads Learning Room	3	25-Mar-27	29-Mar-27	75
007-1045	Install mechanical diffusers Learning Room	2	25-Mar-27	26-Mar-27	56
007-1050	Install Signage Learning Room	1	30-Mar-27	30-Mar-27	75
MECHANICAL SHAFT		60	14-Oct-26	12-Jan-27	107
CEL-1725	Install Backbone Communication Conduit Riser in Walls Cellar Floor	20	14-Oct-26	10-Nov-26	107
CEL-1730	Install Backbone Security Conduit Riser in Walls Cellar Floor	20	12-Nov-26	11-Dec-26	107
CEL-1035	Install Backbone Audiovisual Conduit Riser in Walls Cellar Floor	20	14-Dec-26	12-Jan-27	107

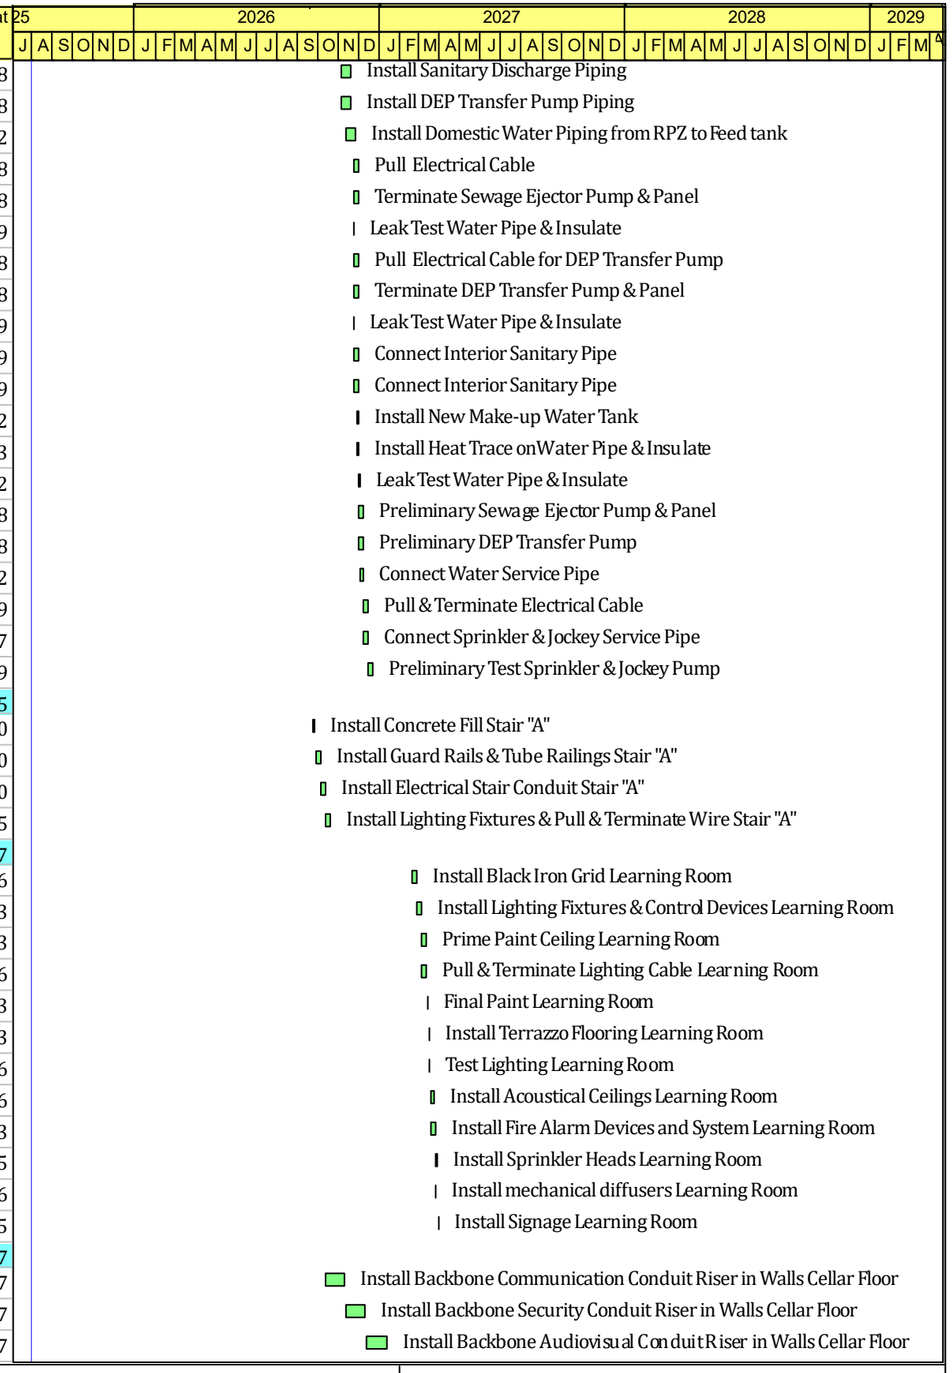

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
STAIR "B" 008		16	05-Oct-26	26-Oct-26	150
008-1000	Install Concrete Fill Stair "B"	1	05-Oct-26	05-Oct-26	150
008-1005	Install Guard Rails & Tube Railings Stair "B"	5	06-Oct-26	12-Oct-26	150
008-1010	Install Electrical Stair Conduit Stair "B"	5	13-Oct-26	19-Oct-26	150
008-1015	Install Lighting Fixtures & Pull & Terminate Wire Stair "B"	5	20-Oct-26	26-Oct-26	150
WATER CLOSET "C" 012		7	19-Feb-27	01-Mar-27	95
012-1000	Install ceramic Tile Toilet Water Closet "C"	2	19-Feb-27	22-Feb-27	80
012-1005	Install Plumbing Fixtures & connect trim Water Closet "C"	3	23-Feb-27	25-Feb-27	80
012-1015	Paint Water Closet "C"	2	23-Feb-27	24-Feb-27	84
012-1010	Install Accessories/Trim Water Closet "C"	2	26-Feb-27	01-Mar-27	95
012-1020	Install Lighting Fixture Water Closet "C"	1	26-Feb-27	26-Feb-27	83
012-1025	Install Lighting Cable, & Devices Water Closet "C"	1	01-Mar-27	01-Mar-27	83
WATER CLOSET "B" 011		8	23-Feb-27	04-Mar-27	92
011-1000	Install ceramic Tile Toilet Water Closet "B"	2	23-Feb-27	24-Feb-27	81
011-1015	Paint Water Closet "B"	2	25-Feb-27	26-Feb-27	82
011-1005	Install Plumbing Fixtures & connect trim Water Closet "B"	3	26-Feb-27	02-Mar-27	80
011-1010	Install Accessories/Trim Water Closet "B"	2	03-Mar-27	04-Mar-27	92
011-1020	Install Lighting Fixture Water Closet "B"	1	03-Mar-27	03-Mar-27	80
011-1025	Install Lighting Cable, & Devices Water Closet "B"	1	04-Mar-27	04-Mar-27	80
IT/DATA ROOM 013		21	15-Mar-27	13-Apr-27	63
013-1000	Install Electrical IT Equipment Room	5	15-Mar-27	19-Mar-27	48
013-1005	Install Security Electrical IT Equipment Room	5	15-Mar-27	19-Mar-27	48
013-1010	Install Audiovisual Electrical IT Equipment Room	5	15-Mar-27	19-Mar-27	48
013-1015	Install Conduit in IT Equipment Room	5	22-Mar-27	26-Mar-27	48
013-1020	Install Security Conduit in IT Equipment Room	5	22-Mar-27	26-Mar-27	48
013-1025	Install Audiovisual Conduit in IT Equipment Room	5	22-Mar-27	26-Mar-27	48
013-1030	Pull & Terminate Electrical Cable in IT Equipment Room	10	29-Mar-27	12-Apr-27	48
013-1035	Pull & Terminate Security Cable in IT Equipment Room	10	29-Mar-27	12-Apr-27	48
013-1055	Inspection & Energize Security Equipment Service	1	29-Mar-27	29-Mar-27	64
013-1040	Pull & Terminate Audiovisual Cable in IT Equipment Room	10	29-Mar-27	12-Apr-27	48
013-1045	Inspection & Energize Audiovisual Equipment Service	1	29-Mar-27	29-Mar-27	73
013-1050	Inspection & Energize IT Equipment Service	1	13-Apr-27	13-Apr-27	63
CUSTODIAN ROOM 014		27	26-Feb-27	06-Apr-27	72
014-1000	Install Black Iron Grid Custodian Room	5	26-Feb-27	04-Mar-27	16
014-1005	Install Lighting Fixtures & Control Devices Custodian Room	5	05-Mar-27	12-Mar-27	51
014-1010	Prime Paint Ceiling Custodian Room	5	15-Mar-27	19-Mar-27	51
014-1015	Pull & Terminate Lighting Cable Custodian Room	5	15-Mar-27	19-Mar-27	51
014-1020	Install Fire Alarm Devices and System Custodian Room	6	22-Mar-27	29-Mar-27	51
014-1025	Final Paint Custodian Room	1	22-Mar-27	22-Mar-27	51
014-1055	Test Lighting Custodian Room	1	22-Mar-27	22-Mar-27	83
014-1030	Install Terrazzo Flooring Custodian Room	2	23-Mar-27	24-Mar-27	51
014-1035	Install Acoustical Ceilings Custodian Room	5	25-Mar-27	31-Mar-27	51

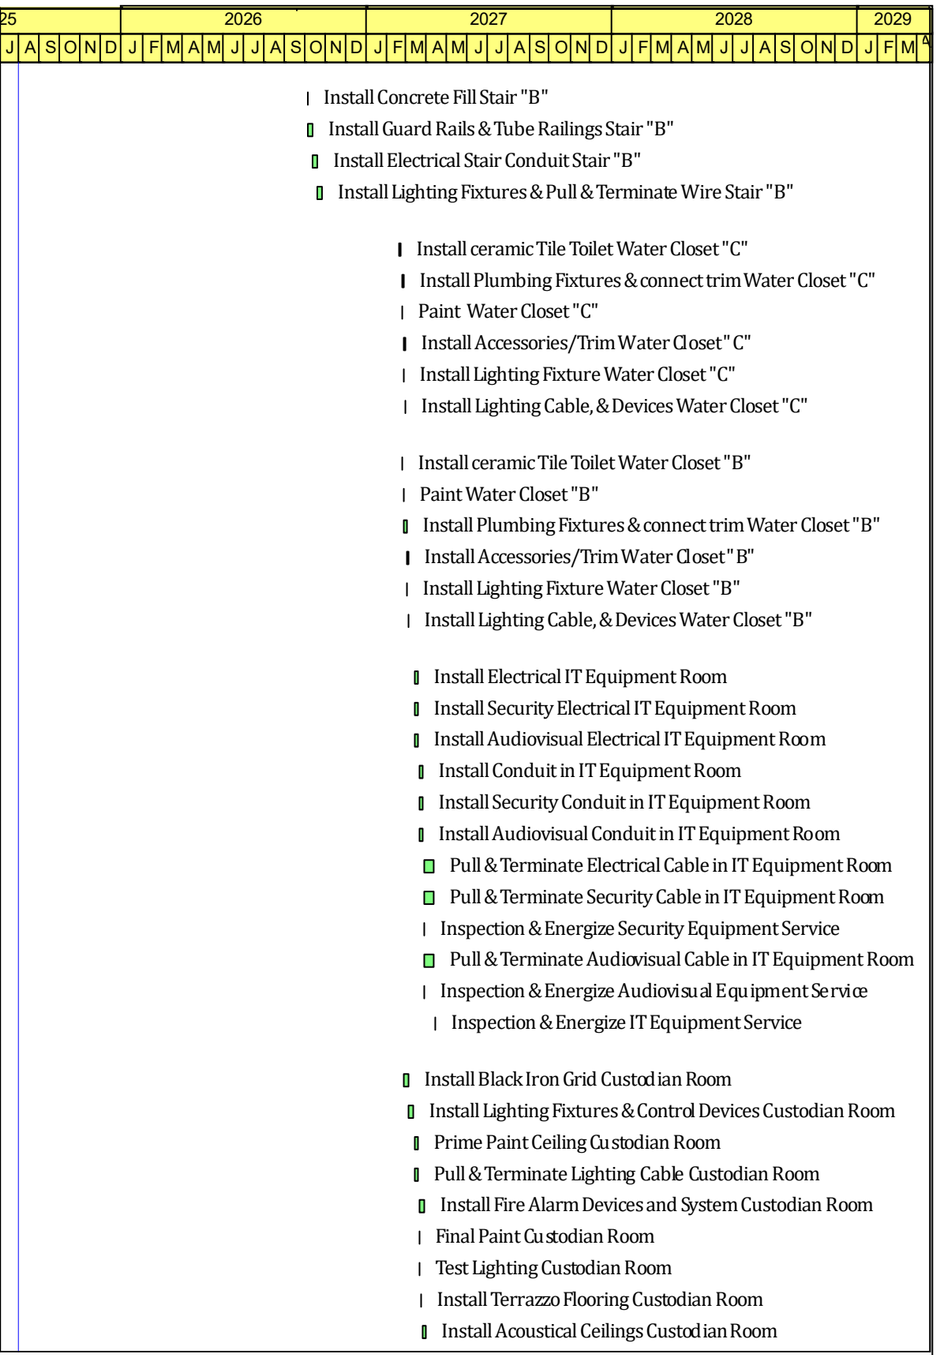

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
014-1040	Install Sprinkler Heads Custodian Room	3	01-Apr-27	05-Apr-27	70
014-1045	Install mechanical diffusers Custodian Room	2	01-Apr-27	02-Apr-27	51
014-1050	Install Signage Custodian Room	1	06-Apr-27	06-Apr-27	70
1ST FLOOR NEW ADDITION		149	28-Sep-26	07-May-27	50
1st-1180	Install Overhead Plumbing Pipe 1st Floor	15	14-Oct-26	03-Nov-26	35
1st-1190	Install Overhead Sprinkler Pipe 1st Floor	15	14-Oct-26	03-Nov-26	35
1st-1200	Install Overhead Electrical 1st Floor	15	14-Oct-26	03-Nov-26	35
1st-1210	Install Overhead Mechanical Ductwork& Split AC Units 1st Floor	15	14-Oct-26	03-Nov-26	28
1st-1220	Install Walls Framing 1st Floor	15	04-Nov-26	25-Nov-26	35
1st-1230	Install Plumbing Piping in Walls 1st Floor	10	04-Nov-26	18-Nov-26	59
1st-1240	Install Sprinkler Piping thru Walls 1st Floor	10	04-Nov-26	18-Nov-26	64
1st-1250	Install Electrical Rough-in in Walls 1st Floor	10	04-Nov-26	18-Nov-26	64
1st-1260	Install Mechanical Ductwork in Walls 1st Floor	10	04-Nov-26	18-Nov-26	64
1st-1270	Install Overhead Mechanical Piping 1st Floor	15	04-Nov-26	25-Nov-26	44
1st-1330	Installl Control Dampers in Ductwork 1st Floor	10	04-Nov-26	18-Nov-26	130
1st-1290	Leak test & insulate Plumbing piping walls 1st Floor	5	19-Nov-26	25-Nov-26	59
1st-1350	Pull & Terminate Wires for Control Dampers 1st Floor	10	19-Nov-26	04-Dec-26	130
1st-1310	Install Mechanical Unit Heaters System 1st Floor	15	30-Nov-26	18-Dec-26	44
1st-1320	Install Mechanical Piping in Walls 1st Floor	15	30-Nov-26	18-Dec-26	44
1st-1480	Pull Communication cable,Install Telecom Outlets 1st Floor	7	07-Dec-26	15-Dec-26	132
1st-1360	Install Gypsum Board wall and ceilings 1st Floor	10	19-Feb-27	04-Mar-27	5
INSP-1050	Hold Point Inspecton to Install Gypsum Board wall and ceilings 1st Floor	1	19-Feb-27	19-Feb-27	20
1st-1380	Perform Tape & Spackle 1st Floor	5	05-Mar-27	12-Mar-27	11
1st-1440	Install Sprinkler Heads 1st Floor	7	15-Mar-27	23-Mar-27	59
1st-1570	Install CCTVs 1st Floor	7	15-Mar-27	23-Mar-27	61
1st-1510	Install Audiovisual Equipment 1st Floor	7	15-Mar-27	23-Mar-27	61
1st-1490	Pull Security cable,Install Security Outlets 1st Floor	7	24-Mar-27	01-Apr-27	61
1st-1500	Pull Audiovisual cable,Install Audiovisual Outlets 1st Floor	7	24-Mar-27	01-Apr-27	61
COMMUNITY ROOM 105		44	05-Mar-27	07-May-27	50
105-1020	Install Induction Loop Community Room	10	05-Mar-27	19-Mar-27	34
105-1000	Install Black Iron Grid Community Room	3	15-Mar-27	17-Mar-27	11
105-1010	Prime Paint Ceiling Community Room	5	18-Mar-27	24-Mar-27	31
105-1005	Install Lighting Fixtures & Control Devices Community Room	5	18-Mar-27	24-Mar-27	46
105-1030	Install Terrazzo Flooring Community Room	10	25-Mar-27	08-Apr-27	31
105-1015	Pull & Terminate Lighting Cable Community Room	5	25-Mar-27	31-Mar-27	46
105-1055	Install Fire Alarm Devices and System Community Room	3	01-Apr-27	05-Apr-27	46
105-1025	Test Lighting in Community Room	1	01-Apr-27	01-Apr-27	75
105-1035	Install Acoustical Ceilings Community Room	5	09-Apr-27	15-Apr-27	41
105-1040	Final Paint Community Room	1	09-Apr-27	09-Apr-27	55
105-1045	Install Acoustical Wall Panel Ceilings Community Room	15	09-Apr-27	29-Apr-27	31
105-1050	Install Built in Storage Closet Community Room	10	12-Apr-27	23-Apr-27	55

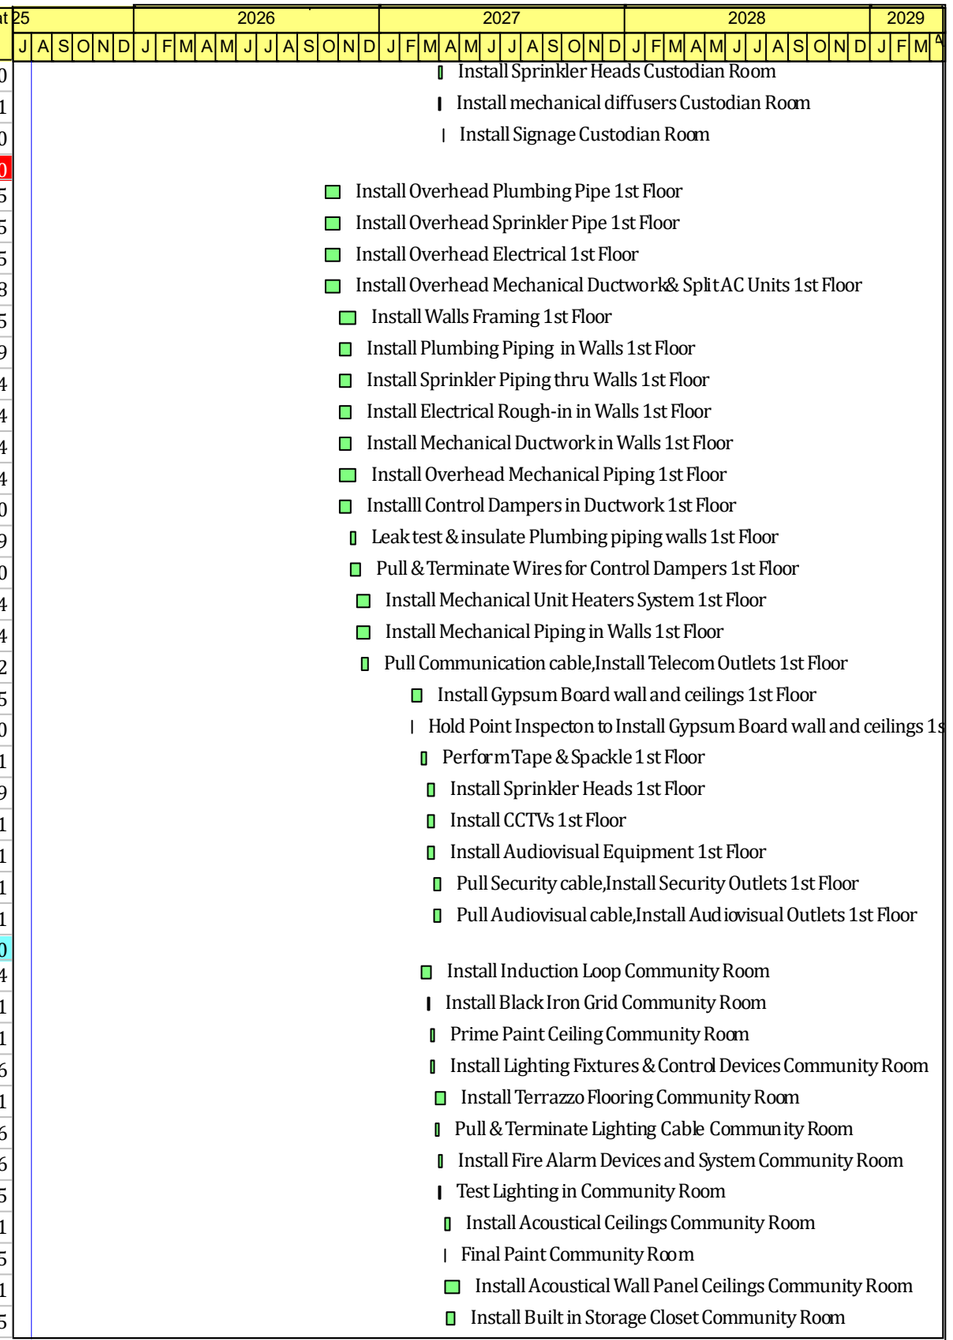

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
105-1060	Install Sprinkler Heads Community Room	3	30-Apr-27	04-May-27	48
105-1065	Install mechanical diffusers Community Room	2	30-Apr-27	03-May-27	31
105-1070	Install Signage Community Room	3	05-May-27	07-May-27	48
STAIR "A" 106		20	28-Sep-26	26-Oct-26	155
106-1000	Install Concrete Fill Stair "A"	1	28-Sep-26	28-Sep-26	159
106-1005	Install Guard Rails & Tube Railings Stair "A"	5	06-Oct-26	12-Oct-26	155
106-1010	Install Electrical Stair Conduit Stair "A"	5	13-Oct-26	19-Oct-26	155
106-1015	Install Lighting Fixtures & Pull & Terminate Wire Stair "A"	5	20-Oct-26	26-Oct-26	155
STEAM 107		25	18-Mar-27	22-Apr-27	61
107-1000	Install Black Iron Grid Steam Area	3	18-Mar-27	22-Mar-27	11
107-1005	Install Lighting Fixtures & Control Devices Steam Area	5	23-Mar-27	29-Mar-27	40
107-1010	Prime Paint Ceiling Steam Area	5	30-Mar-27	05-Apr-27	40
107-1015	Pull & Terminate Lighting Cable Steam Area	5	30-Mar-27	05-Apr-27	40
107-1020	Install Fire Alarm Devices and System Steam Area	6	06-Apr-27	14-Apr-27	40
107-1025	Final Paint Steam Area	1	06-Apr-27	06-Apr-27	40
107-1055	Test Lighting in Steam Area	1	06-Apr-27	06-Apr-27	72
107-1030	Install Terrazzo Flooring Steam Area	2	08-Apr-27	09-Apr-27	40
107-1035	Install Acoustical Ceilings Steam Area	5	12-Apr-27	16-Apr-27	40
107-1040	Install Sprinkler Heads Steam Area	3	19-Apr-27	21-Apr-27	59
107-1045	Install mechanical diffusers Steam Area	2	19-Apr-27	20-Apr-27	40
107-1050	Install Signage Steam Area	1	22-Apr-27	22-Apr-27	59
WATER CLOSET "B" 111		7	15-Mar-27	23-Mar-27	80
111-1000	Install ceramic Tile Toilet in Water Closet "B"	2	15-Mar-27	16-Mar-27	52
111-1005	Install Plumbing Fixtures & connect trim in Water Closet "B"	3	17-Mar-27	19-Mar-27	52
111-1015	Paint Water Closet "B"	2	17-Mar-27	18-Mar-27	53
111-1010	Install Accessories/Trim in Water Closet "B"	2	22-Mar-27	23-Mar-27	80
111-1020	Install Lighting Fixture in Water Closet "B"	1	22-Mar-27	22-Mar-27	52
111-1025	Install Lighting Cable, & Devices in Water Closet "B"	1	23-Mar-27	23-Mar-27	52
WATER CLOSET "C" 112		8	15-Mar-27	24-Mar-27	79
112-1000	Install ceramic Tile Toilet in Water Closet "C"	2	15-Mar-27	16-Mar-27	53
112-1005	Install Plumbing Fixtures & connect trim in Water Closet "C"	3	17-Mar-27	19-Mar-27	53
112-1015	Paint Water Closet "C"	2	17-Mar-27	18-Mar-27	54
112-1010	Install Accessories/Trim in Water Closet "C"	2	22-Mar-27	23-Mar-27	80
112-1020	Install Lighting Fixture in Water Closet "C"	1	22-Mar-27	22-Mar-27	53
112-1025	Install Lighting Cable, & Devices in Water Closet "C"	1	24-Mar-27	24-Mar-27	52
STAIR "B" 108		118	06-Oct-26	31-Mar-27	52
108-1000	Install Concrete Fill Stair "B"	1	06-Oct-26	06-Oct-26	154
108-1005	Install Guard Rails & Tube Railings Stair "B"	5	13-Oct-26	19-Oct-26	150
108-1010	Install Electrical Stair Conduit Stair "B"	5	20-Oct-26	26-Oct-26	150
108-1015	Install Lighting Fixtures & Pull & Terminate Wire Stair "B"	5	25-Mar-27	31-Mar-27	52
MATERIALS AND HANDLING ROOM 114		24	23-Mar-27	26-Apr-27	59
114-1000	Install Black Iron Grid Material and Handling Room	2	23-Mar-27	24-Mar-27	11

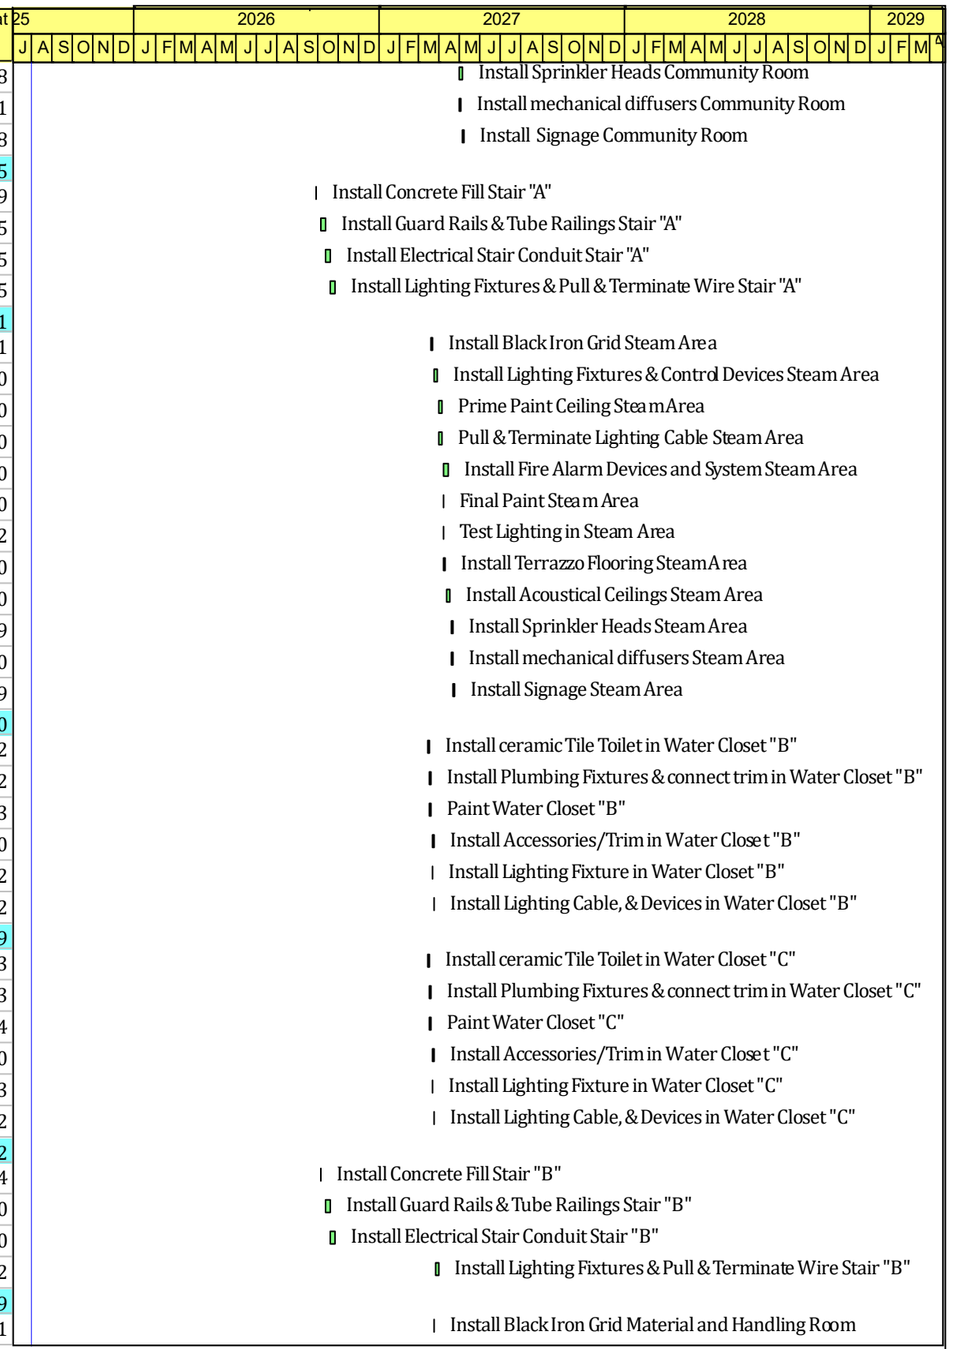

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
114-1005	Install Lighting Fixtures & Control Devices Material and Handling Room	5	25-Mar-27	31-Mar-27	38
114-1010	Prime Paint Ceiling Material and Handling Room	5	01-Apr-27	08-Apr-27	38
114-1015	Pull & Terminate Lighting Cable Material and Handling Room	5	01-Apr-27	08-Apr-27	38
114-1020	Install Fire Alarm Devices and System Material and Handling Room	6	09-Apr-27	16-Apr-27	38
114-1025	Final Paint Material and Handling Room	1	09-Apr-27	09-Apr-27	38
114-1055	Test Lighting in Material and Handling Room	1	09-Apr-27	09-Apr-27	70
114-1030	Install Terrazzo Flooring Material and Handling Room	2	12-Apr-27	13-Apr-27	38
114-1035	Install Acoustical Ceilings Material and Handling Room	5	14-Apr-27	20-Apr-27	38
114-1040	Install Sprinkler Heads Material and Handling Room	3	21-Apr-27	23-Apr-27	57
114-1045	Install mechanical diffusers Material and Handling Room	2	21-Apr-27	22-Apr-27	38
114-1050	Install Signage Material and Handling Room	1	26-Apr-27	26-Apr-27	57
LIBRARIAN OFFICE 115		26	25-Mar-27	30-Apr-27	55
115-1000	Install Black Iron Grid Librarian's Office	2	25-Mar-27	26-Mar-27	11
115-1005	Install Lighting Fixtures & Control Devices Librarian's Office	5	29-Mar-27	02-Apr-27	36
115-1010	Prime Paint Ceiling Librarian's Office	5	05-Apr-27	12-Apr-27	36
115-1015	Pull & Terminate Lighting Cable Librarian's Office	5	05-Apr-27	12-Apr-27	36
115-1020	Install Fire Alarm Devices and System Librarian's Office	6	13-Apr-27	20-Apr-27	36
115-1025	Final Paint Librarian's Office	1	13-Apr-27	13-Apr-27	36
115-1055	Test Lighting in Librarian's Office	1	13-Apr-27	13-Apr-27	68
115-1030	Install Terrazzo Flooring Librarian's Office	2	14-Apr-27	15-Apr-27	36
115-1035	Install Acoustical Ceilings Librarian's Office	5	16-Apr-27	22-Apr-27	36
115-1040	Install Sprinkler Heads Librarian's Office	3	23-Apr-27	27-Apr-27	53
115-1045	Install mechanical diffusers Librarian's Office	2	23-Apr-27	26-Apr-27	36
115-1050	Install Signage Librarian's Office	3	28-Apr-27	30-Apr-27	53
WATER CLOSET "A" 113		7	17-Mar-27	25-Mar-27	78
113-1000	Install ceramic Tile Toilet in Water Closet "A"	2	17-Mar-27	18-Mar-27	78
113-1005	Install Plumbing Fixtures & connect trim in Water Closet "A"	3	19-Mar-27	23-Mar-27	78
113-1015	Paint Water Closet "A"	2	19-Mar-27	22-Mar-27	79
113-1010	Install Accessories/Trim in Water Closet "A"	2	24-Mar-27	25-Mar-27	78
113-1020	Install Lighting Fixture in Water Closet "A"	1	24-Mar-27	24-Mar-27	78
113-1025	Install Lighting Cable, & Devices in Water Closet "A"	1	25-Mar-27	25-Mar-27	78
2ND FLOOR NEW ADDITION		159	29-Sep-26	26-May-27	39
2nd-1180	Install Overhead Plumbing Pipe 2nd Floor	15	04-Nov-26	25-Nov-26	35
2nd-1190	Install Overhead Sprinkler Pipe 2nd Floor	15	04-Nov-26	25-Nov-26	35
2nd-1200	Install Overhead Electrical 2nd Floor	15	04-Nov-26	25-Nov-26	35
2nd-1210	Install Overhead Mechanical Ductwork& Split AC Units 2nd Floor	15	04-Nov-26	25-Nov-26	28
2nd-1220	Install Walls Framing 2nd Floor	15	30-Nov-26	18-Dec-26	35
2nd-1230	Install Plumbing Piping in Walls 2nd Floor	10	30-Nov-26	11-Dec-26	54
2nd-1240	Install Sprinkler Piping thru Walls 2nd Floor	10	30-Nov-26	11-Dec-26	59
2nd-1250	Install Electrical Rough-in in Walls 2nd Floor	10	30-Nov-26	11-Dec-26	59
2nd-1260	Install Mechanical Ductwork in Walls 2nd Floor	10	30-Nov-26	11-Dec-26	59
2nd-1270	Install Overhead Mechanical Piping 2nd Floor	15	30-Nov-26	18-Dec-26	39

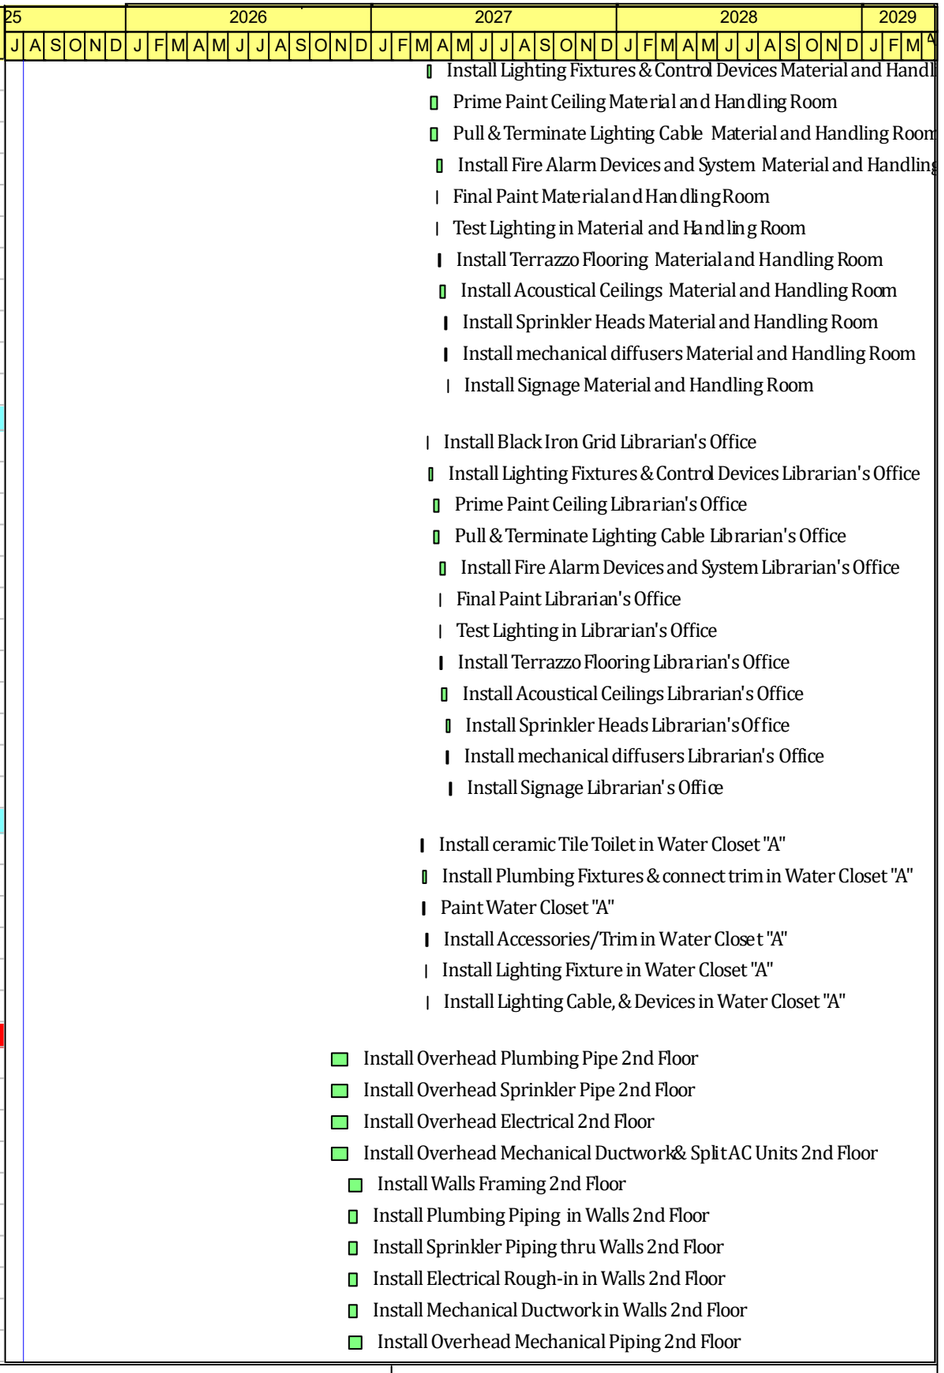

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
2nd-1330	Installl Control Dampers in Ductwork 2nd Floor	10	30-Nov-26	11-Dec-26	115
2nd-1480	Pull Communication cable,Install Telecom Outlets 2nd Floor	7	14-Dec-26	22-Dec-26	127
2nd-1290	Leak test & insulate Plumbing piping walls 2nd Floor	5	14-Dec-26	18-Dec-26	54
2nd-1570	Install CCTVs 2nd Floor	7	14-Dec-26	22-Dec-26	120
2nd-1350	Pull & Terminate Wires for Control Dampers 2nd Floor	10	14-Dec-26	28-Dec-26	115
2nd-1310	Install Mechanical Unit Heaters System 2nd Floor	15	21-Dec-26	12-Jan-27	39
2nd-1320	Install Mechanical Piping in Walls 2nd Floor	15	21-Dec-26	12-Jan-27	39
2nd-1490	Pull Security cable,Install Security Outlets 2nd Floor	7	23-Dec-26	04-Jan-27	120
INSP-1045	Hold Point Inspection to Install Gypsum Board wall and ceilings 2nd Floor	1	05-Mar-27	05-Mar-27	5
2nd-1360	Install Gypsum Board wall and ceilings 2nd Floor	10	08-Mar-27	22-Mar-27	5
2nd-1380	Perform Tape & Spackle 2nd Floor	5	23-Mar-27	29-Mar-27	10
2nd-1510	Install Audiovisual Equipment 2nd Floor	7	30-Mar-27	08-Apr-27	50
2nd-1500	Pull Audiovisual cable,Install Audiovisual Outlets 2nd Floor	7	09-Apr-27	19-Apr-27	50
CHILDREN ZONE 205		34	30-Mar-27	18-May-27	44
205-1000	Install Black Iron Grid Children Zone Room 205	3	30-Mar-27	01-Apr-27	10
205-1005	Install Lighting Fixtures & Control Devices Children Zone Room 205	5	02-Apr-27	09-Apr-27	25
205-1010	Prime Paint Ceiling Children Zone Room 205	5	12-Apr-27	16-Apr-27	25
205-1015	Pull & Terminate Lighting Cable Children Zone Room 205	5	12-Apr-27	16-Apr-27	35
205-1020	Install Terrazzo Flooring Children Zone Room 205	10	19-Apr-27	30-Apr-27	25
205-1055	Install Fire Alarm Devices and System Children Zone Room 205	3	19-Apr-27	21-Apr-27	35
205-1040	Test Lighting Adult Children Zone Room 205	1	19-Apr-27	19-Apr-27	64
205-1025	Install Acoustical Ceilings Children Zone Room 205	5	03-May-27	07-May-27	25
205-1030	Final Paint Children Zone Room 205	1	03-May-27	03-May-27	42
205-1035	Install Book Shelf Unit Children Zone Room 205	10	04-May-27	18-May-27	42
205-1045	Install Sprinkler Heads Children Zone Room 205	3	10-May-27	13-May-27	42
205-1050	Install mechanical diffusers Children Zone Room 205	2	10-May-27	11-May-27	25
205-1060	Install Fire Extinguishers and Signage Children Zone Room 205	3	14-May-27	18-May-27	42
STAIR "A" 206		24	29-Sep-26	02-Nov-26	155
206-1000	Install Concrete Fill Stair "A"	1	29-Sep-26	29-Sep-26	163
206-1005	Install Guard Rails & Tube Railings Stair "A"	5	13-Oct-26	19-Oct-26	155
206-1010	Install Electrical Stair Conduit Stair "A"	5	20-Oct-26	26-Oct-26	155
206-1015	Install Lighting Fixtures & Pull & Terminate Wire Stair "A"	5	27-Oct-26	02-Nov-26	155
CHILDREN ZONE 207		34	02-Apr-27	21-May-27	41
207-1000	Install Black Iron Grid Children Zone Room 207	3	02-Apr-27	06-Apr-27	10
207-1005	Install Lighting Fixtures & Control Devices Children Zone Room 207	5	08-Apr-27	14-Apr-27	22
207-1010	Prime Paint Ceiling Children Zone Room 207	5	15-Apr-27	21-Apr-27	22
207-1015	Pull & Terminate Lighting Cable Children Zone Room 207	5	15-Apr-27	21-Apr-27	32
207-1020	Install Terrazzo Flooring Children Zone Room 207	10	22-Apr-27	05-May-27	22
207-1055	Install Fire Alarm Devices and System Children Zone Room 207	3	22-Apr-27	26-Apr-27	32
207-1040	Test Lighting Adult Children Zone Room 207	1	22-Apr-27	22-Apr-27	61
207-1025	Install Acoustical Ceilings Children Zone Room 207	5	06-May-27	13-May-27	22
207-1030	Final Paint Children Zone Room 207	1	06-May-27	06-May-27	39

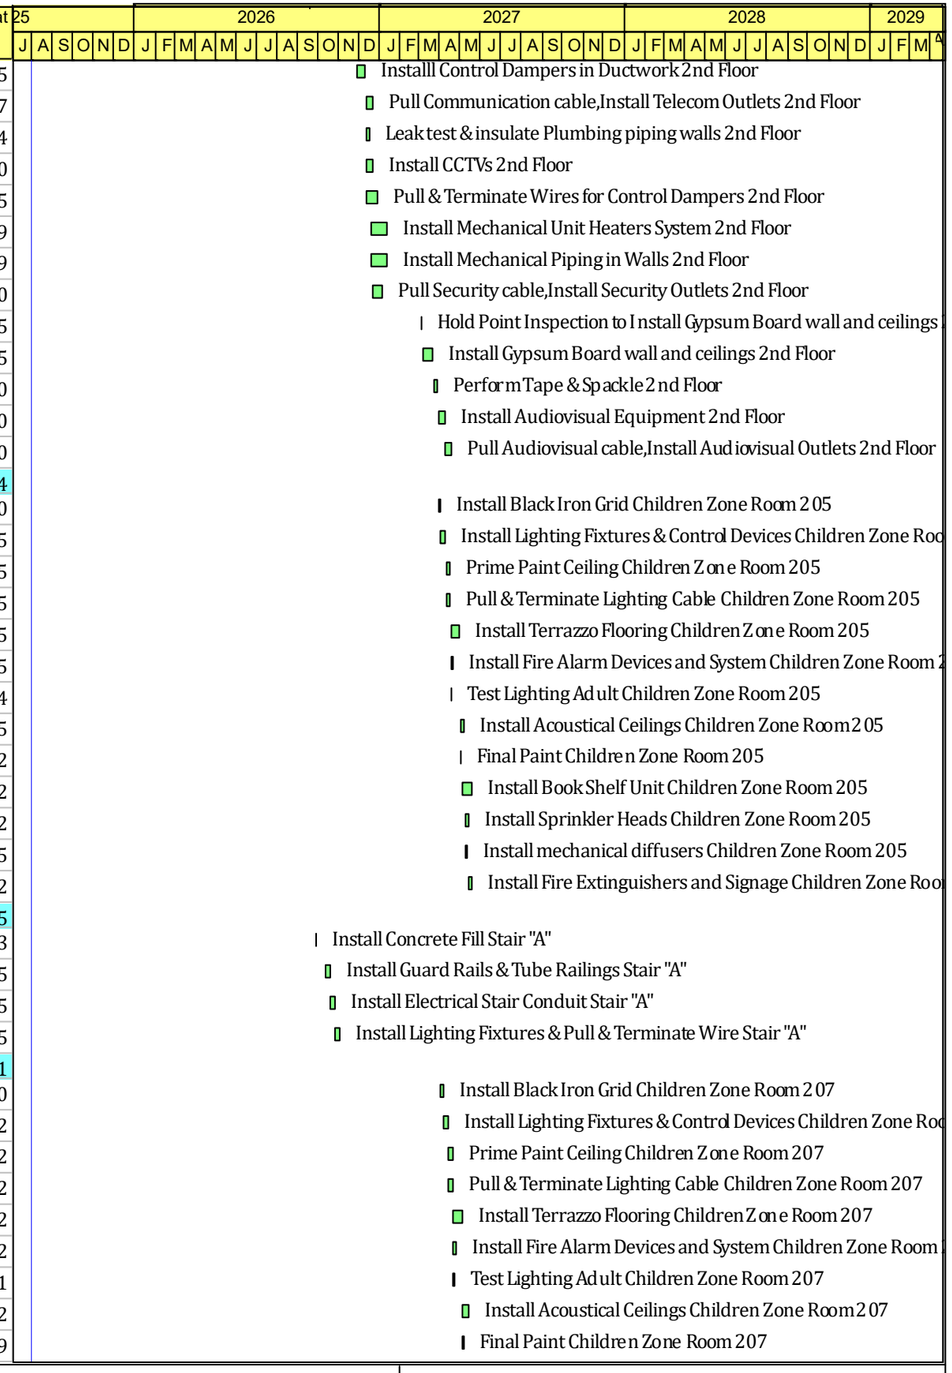

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
207-1035	Install Book Shelf Unit Children Zone Room 207	10	07-May-27	21-May-27	39
207-1045	Install Sprinkler Heads Children Zone Room 207	3	14-May-27	18-May-27	39
207-1050	Install mechanical diffusers Children Zone Room 207	2	14-May-27	17-May-27	22
207-1060	Install Fire Extinguishers and Signage Children Zone Room 207	3	19-May-27	21-May-27	39
WATER CLOSET "B"		7	30-Mar-27	08-Apr-27	70
2nd-1000	Install ceramic Tile Toilet in Water Closet "B"	2	30-Mar-27	31-Mar-27	51
2nd-1010	Install Plumbing Fixtures & connect trim in Water Closet "B"	3	01-Apr-27	05-Apr-27	69
2nd-1030	Paint Water Closet "B"	2	01-Apr-27	02-Apr-27	71
2nd-1020	Install Accessories/Trim in Water Closet "B"	2	06-Apr-27	08-Apr-27	69
2nd-1040	Install Lighting Fixture in Water Closet "B"	1	06-Apr-27	06-Apr-27	70
2nd-1050	Install Lighting Cable, & Devices in Water Closet "B"	1	08-Apr-27	08-Apr-27	70
WATER CLOSET "C"		7	01-Apr-27	12-Apr-27	69
2nd-1060	Install ceramic Tile Toilet in Water Closet "C"	2	01-Apr-27	02-Apr-27	51
2nd-1070	Install Plumbing Fixtures & connect trim in Water Closet "C"	3	05-Apr-27	08-Apr-27	67
2nd-1090	Paint Water Closet "C"	2	05-Apr-27	06-Apr-27	70
2nd-1080	Install Accessories/Trim in Water Closet "C"	2	09-Apr-27	12-Apr-27	67
2nd-1100	Install Lighting Fixture in Water Closet "C"	1	09-Apr-27	09-Apr-27	69
2nd-1110	Install Lighting Cable, & Devices in Water Closet "C"	1	12-Apr-27	12-Apr-27	69
STAIR "B" 208		122	07-Oct-26	08-Apr-27	52
208-1000	Install Concrete Fill Stair "B"	1	07-Oct-26	07-Oct-26	158
208-1005	Install Guard Rails & Tube Railings Stair "B"	5	20-Oct-26	26-Oct-26	150
208-1010	Install Electrical Stair Conduit Stair "B"	5	27-Oct-26	02-Nov-26	150
208-1015	Install Lighting Fixtures & Pull & Terminate Wire Stair "B"	5	01-Apr-27	08-Apr-27	52
CLASSROOM 209		33	08-Apr-27	26-May-27	39
209-1000	Install Black Iron Grid Classroom 209	2	08-Apr-27	09-Apr-27	10
209-1005	Install Lighting Fixtures & Control DevicesClassroom 209	5	12-Apr-27	16-Apr-27	20
209-1010	Prime Paint Ceiling Classroom 209	5	19-Apr-27	23-Apr-27	20
209-1015	Pull & Terminate Lighting Cable Classroom 209	5	19-Apr-27	23-Apr-27	30
209-1025	Install Terrazzo Flooring Classroom 209	10	26-Apr-27	07-May-27	20
209-1055	Install Fire Alarm Devices and System Classroom 209	3	26-Apr-27	28-Apr-27	30
209-1040	Test Lighting Classroom 209	1	26-Apr-27	26-Apr-27	59
209-1030	Install Acoustical Ceilings Classroom 209	5	10-May-27	17-May-27	20
209-1020	Install Door & Hardware Classroom 209	5	10-May-27	17-May-27	43
209-1035	Final Paint Classroom 209	1	10-May-27	10-May-27	45
209-1045	Install Sprinkler Heads Classroom 209	3	18-May-27	20-May-27	37
209-1050	Install mechanical diffusers Classroom 209	2	18-May-27	19-May-27	20
209-1060	Install Signage Classroom 209	3	21-May-27	26-May-27	37
STAFF WATER CLOSET "A"		29	05-Apr-27	17-May-27	45
2nd-1120	Install ceramic Tile Toilet in Water Closet "A"	2	05-Apr-27	06-Apr-27	65
2nd-1130	Install Plumbing Fixtures & connect trim in Water Closet "A"	3	08-Apr-27	12-Apr-27	65
2nd-1140	Install Accessories/Trim in Water Closet "A"	2	13-Apr-27	14-Apr-27	65
2nd-1150	Paint Water Closet "A"	2	11-May-27	13-May-27	45

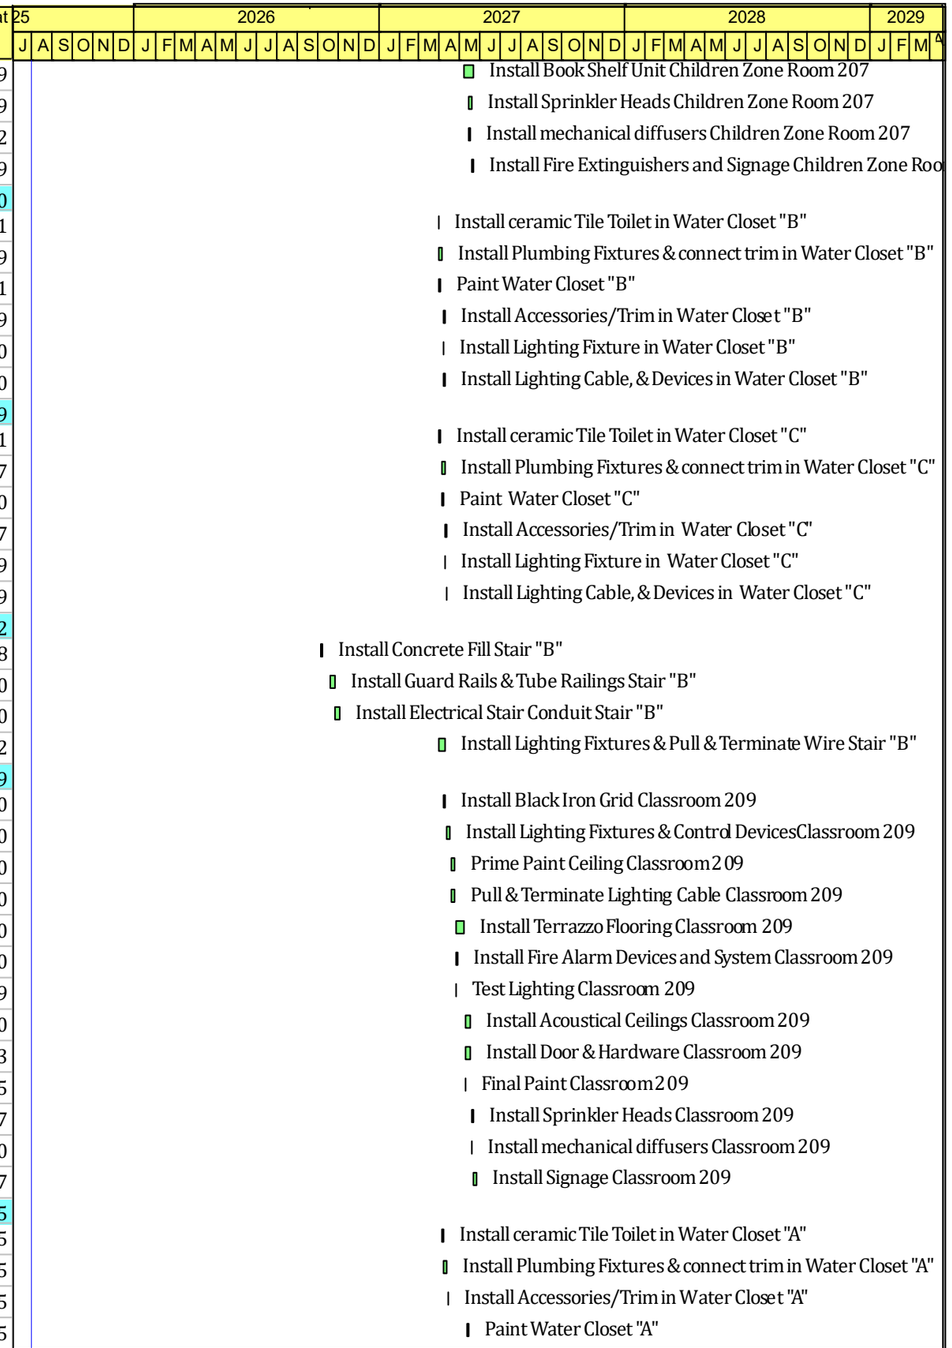

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
2nd-1160	Install Lighting Fixture in Water Closet "A"	1	14-May-27	14-May-27	45
2nd-1170	Install Lighting Cable, & Devices in Water Closet "A"	1	17-May-27	17-May-27	45
3RD FLOOR NEW ADDITION		195	30-Sep-26	29-Jun-27	17
3rd-1180	Install Overhead Plumbing Pipe 3rd Floor	15	30-Nov-26	18-Dec-26	35
3rd-1190	Install Overhead Sprinkler Pipe 3rd Floor	15	30-Nov-26	18-Dec-26	35
3rd-1200	Install Overhead Electrical 3rd Floor	15	30-Nov-26	18-Dec-26	35
3rd-1210	Install Overhead Mechanical Ductwork & Split AC Units 3rd Floor	15	30-Nov-26	18-Dec-26	28
3rd-1220	Install Walls Framing 3rd Floor	15	21-Dec-26	12-Jan-27	35
3rd-1230	Install Plumbing Piping in Walls 3rd Floor	10	21-Dec-26	05-Jan-27	50
3rd-1240	Install Sprinkler Piping thru Walls 3rd Floor	10	21-Dec-26	05-Jan-27	55
3rd-1250	Install Electrical Rough-in in Walls 3rd Floor	10	21-Dec-26	05-Jan-27	55
3rd-1260	Install Mechanical Ductwork in Walls 3rd Floor	10	21-Dec-26	05-Jan-27	55
3rd-1270	Install Overhead Mechanical Piping 3rd Floor	15	21-Dec-26	12-Jan-27	28
3rd-1330	Installl Control Dampers in Ductwork 3rd Floor	10	21-Dec-26	05-Jan-27	100
3rd-1480	Pull Communication cable,Install Telecom Outlets 3rd Floor	7	06-Jan-27	14-Jan-27	112
3rd-1290	Leak test & insulate Plumbing piping walls 3rd Floor	5	06-Jan-27	12-Jan-27	50
3rd-1350	Pull & Terminate Wires for Control Dampers 3rd Floor	10	06-Jan-27	20-Jan-27	100
3rd-1310	Install Mechanical Unit Heaters System 3rd Floor	5	13-Jan-27	20-Jan-27	45
3rd-1320	Install Mechanical Piping in Walls 3rd Floor	15	13-Jan-27	03-Feb-27	35
INSP-1000	Phase 1 Inspection Completion of Wall Framing Addition	2	13-Jan-27	14-Jan-27	61
INSP-1090	Phase 3 Inspection Start of Finishes Addition	2	05-Mar-27	08-Mar-27	87
INSP-1020	Hold Point Inspection to Install Gypsum Board wall and ceilings 3rd Floor	1	23-Mar-27	23-Mar-27	5
3rd-1360	Install Gypsum Board wall and ceilings 3rd Floor	10	24-Mar-27	06-Apr-27	5
INSP-1060	Phase 2 Inspection Completion of Gypsum Wall Board Addition	2	08-Apr-27	09-Apr-27	5
3rd-1380	Perform Tape & Spackle 3rd Floor	5	12-Apr-27	16-Apr-27	5
INSP-1110	Phase 4 Inspection Completion of Finishes Addition	2	02-Jun-27	03-Jun-27	31
READING TERRANCE 305		14	10-Jun-27	29-Jun-27	15
305-1000	Install Concrete Pavers ReadingTerrace	4	10-Jun-27	15-Jun-27	14
305-1005	Install Landscape Planters & Irrigation ReadingTerrace	4	16-Jun-27	21-Jun-27	14
305-1010	Install Landscaping ReadingTerrace	4	22-Jun-27	25-Jun-27	14
305-1015	Install Furnishing ReadingTerrace	2	28-Jun-27	29-Jun-27	14
STAIR "A" 306		28	30-Sep-26	09-Nov-26	155
306-1000	Install Concrete Fill Stair "A"	1	30-Sep-26	30-Sep-26	167
306-1005	Install Guard Rails & Tube Railings Stair "A"	5	20-Oct-26	26-Oct-26	155
306-1010	Install Electrical Stair Conduit Stair "A"	5	27-Oct-26	02-Nov-26	155
306-1015	Install Lighting Fixtures & Pull & Terminate Wire Stair "A"	5	03-Nov-26	09-Nov-26	155
MULTIPURPOSE ROOM 302		39	19-Apr-27	14-Jun-27	26
302-1000	Install Black Iron Grid Multipurpose Room	3	19-Apr-27	21-Apr-27	5
302-1010	Prime Paint Ceiling Multipurpose Room	5	22-Apr-27	28-Apr-27	17
302-1005	Install Lighting Fixtures & Control Devices Multipurpose Room	5	22-Apr-27	28-Apr-27	7
302-1015	Pull & Terminate Lighting Cable Multipurpose Room	5	29-Apr-27	05-May-27	22
302-1020	Install Induction Loop Multipurpose Room	10	29-Apr-27	13-May-27	7



Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
302-1045	Install Fire Alarm Devices and System Multipurpose Room	3	06-May-27	10-May-27	22
302-1025	Test Lighting in Multipurpose Room	1	06-May-27	06-May-27	37
302-1030	Install Terrazzo Flooring Multipurpose Room	10	14-May-27	28-May-27	7
302-1035	Install Acoustical Ceilings Multipurpose Room	5	31-May-27	04-Jun-27	7
302-1040	Final Paint Multipurpose Room	1	31-May-27	31-May-27	32
302-1050	Install Sprinkler Heads Multipurpose Room	3	07-Jun-27	09-Jun-27	26
302-1055	Install mechanical diffusers Multipurpose Room	2	07-Jun-27	08-Jun-27	7
302-1060	Install Signage Multipurpose Room	3	10-Jun-27	14-Jun-27	26
WATER CLOSET "B"		33	19-Apr-27	04-Jun-27	32
310-1000	Install ceramic Tile Toilet in Water Closet "B"	2	19-Apr-27	20-Apr-27	42
310-1005	Install Plumbing Fixtures & connect trim in Water Closet "B"	3	21-Apr-27	23-Apr-27	56
310-1010	Install Accessories/Trim in Water Closet "B"	2	26-Apr-27	27-Apr-27	56
310-1015	Paint Water Closet "B"	2	01-Jun-27	02-Jun-27	32
310-1020	Install Lighting Fixture in Water Closet "B"	1	03-Jun-27	03-Jun-27	32
310-1025	Install Lighting Cable, & Devices in Water Closet "B"	1	04-Jun-27	04-Jun-27	32
WATER CLOSET "C"		7	21-Apr-27	29-Apr-27	54
311-1000	Install ceramic Tile Toilet in Water Closet "C"	2	21-Apr-27	22-Apr-27	42
311-1005	Install Plumbing Fixtures & connect trim in Water Closet "C"	3	23-Apr-27	27-Apr-27	42
311-1015	Paint Water Closet "C"	2	23-Apr-27	26-Apr-27	43
311-1010	Install Accessories/Trim in Water Closet "C"	2	28-Apr-27	29-Apr-27	54
311-1020	Install Lighting Fixture in Water Closet "C"	1	28-Apr-27	28-Apr-27	42
311-1025	Install Lighting Cable, & Devices in Water Closet "C"	1	29-Apr-27	29-Apr-27	42
STAIR "B" 308		126	08-Oct-26	15-Apr-27	52
308-1000	Install Concrete Fill Stair "B"	1	08-Oct-26	08-Oct-26	162
308-1005	Install Guard Rails & Tube Railings Stair "B"	5	27-Oct-26	02-Nov-26	150
308-1010	Install Electrical Stair Conduit Stair "B"	5	03-Nov-26	09-Nov-26	150
308-1015	Install Lighting Fixtures & Pull & Terminate Wire Stair "B"	5	09-Apr-27	15-Apr-27	52
STAFF ROOM 301		34	22-Apr-27	10-Jun-27	28
301-1000	Install Black Iron Grid Staff Room 301	3	22-Apr-27	26-Apr-27	5
301-1005	Install Lighting Fixtures & Control Devices Staff Room 301	5	27-Apr-27	03-May-27	9
301-1010	Prime Paint Ceiling Staff Room 301	5	04-May-27	10-May-27	9
301-1015	Pull & Terminate Lighting Cable Staff Room 301	5	04-May-27	10-May-27	19
301-1025	Install Terrazzo Flooring Staff Room 301	10	11-May-27	26-May-27	9
301-1055	Install Fire Alarm Devices and System Staff Room 301	3	11-May-27	14-May-27	19
301-1040	Test Lighting Staff Room 301	1	11-May-27	11-May-27	34
301-1030	Install Acoustical Ceilings Staff Room 301	5	27-May-27	02-Jun-27	9
301-1020	Install Door & Hardware Staff Room 301	5	27-May-27	02-Jun-27	14
301-1035	Final Paint Staff Room 301	1	27-May-27	27-May-27	33
301-1045	Install Sprinkler Heads Staff Room 301	3	03-Jun-27	07-Jun-27	28
301-1050	Install mechanical diffusers Staff Room 301	2	03-Jun-27	04-Jun-27	9
301-1060	Install Signage Staff Room 301	3	08-Jun-27	10-Jun-27	28
STAFF SUPPORT ROOM 300		36	27-Apr-27	18-Jun-27	23

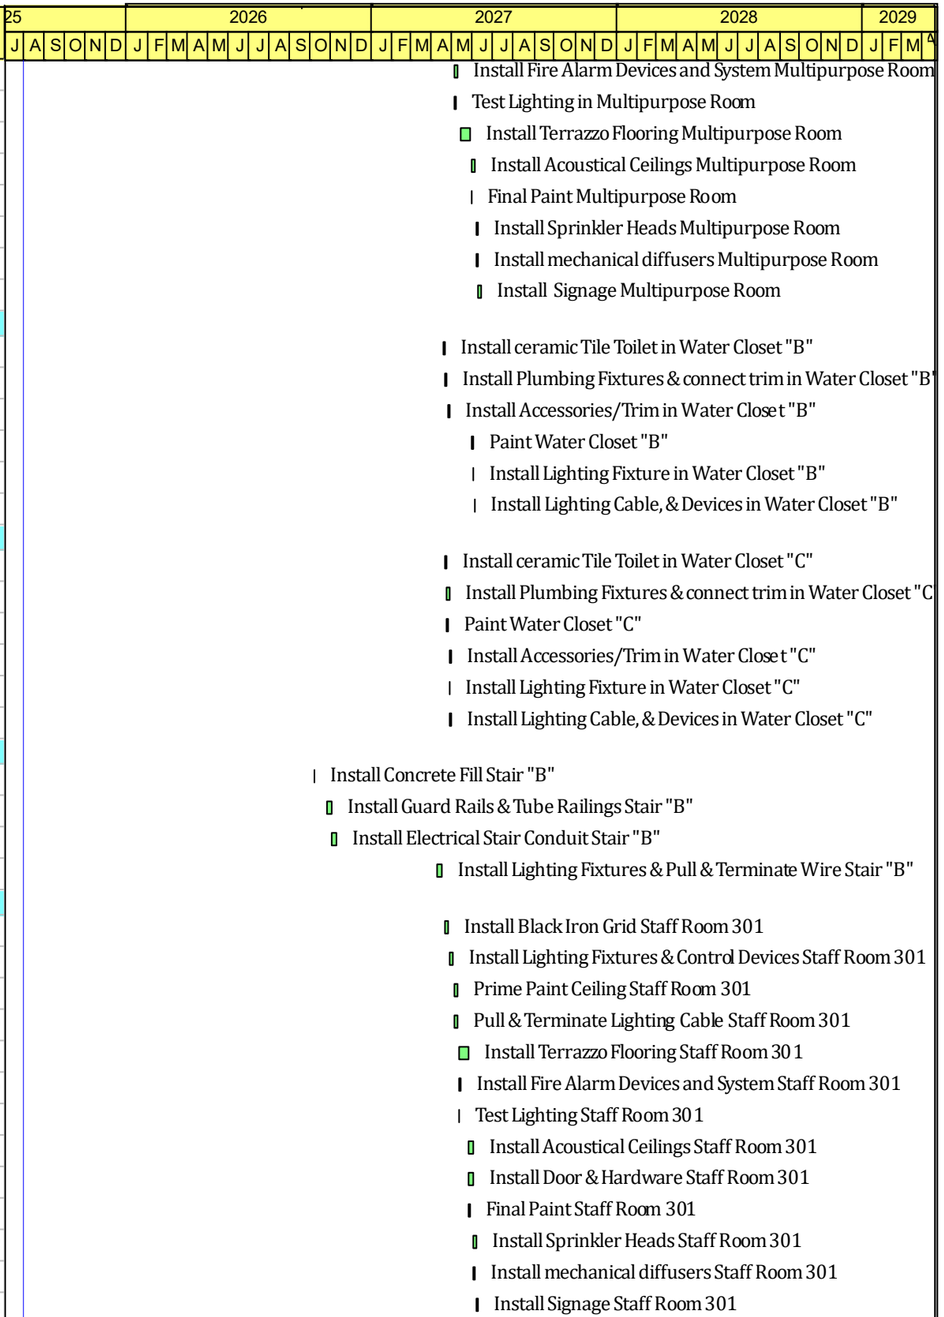

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
300-1000	Install Black Iron Grid Staff Support Room 300	5	27-Apr-27	03-May-27	5
300-1005	Install Lighting Fixtures & Control Devices Staff Support Room 300	5	04-May-27	10-May-27	5
300-1055	Install Fire Alarm Devices and System Staff Support Room 300	3	11-May-27	14-May-27	19
300-1010	Prime Paint Ceiling Staff Support Room 300	5	11-May-27	18-May-27	5
300-1015	Pull & Terminate Lighting Cable Staff Support Room 300	5	11-May-27	18-May-27	43
300-1025	Install Terrazzo Flooring Staff Support Room 300	10	19-May-27	02-Jun-27	5
300-1040	Test Lighting Staff Support Room 300	1	19-May-27	19-May-27	43
300-1030	Install Acoustical Ceilings Staff Support Room 300	5	03-Jun-27	09-Jun-27	5
300-1020	Install Door & Hardware Staff Support Room 300	5	03-Jun-27	09-Jun-27	14
300-1045	Install Sprinkler Heads Staff Support Room 300	3	10-Jun-27	14-Jun-27	23
300-1050	Install mechanical diffusers Staff Support Room 300	1	10-Jun-27	10-Jun-27	5
300-1035	Final Paint Staff Support Room 300	1	10-Jun-27	10-Jun-27	24
300-1060	Install Signage Staff Support Room 300	3	15-Jun-27	18-Jun-27	23
WATER CLOSET "A"		37	23-Apr-27	17-Jun-27	24
309-1000	Install ceramic Tile Toilet in Water Closet "A"	2	23-Apr-27	26-Apr-27	52
309-1005	Install Plumbing Fixtures & connect trim in Water Closet "A"	3	27-Apr-27	29-Apr-27	52
309-1010	Install Accessories/Trim in Water Closet "A"	2	30-Apr-27	03-May-27	52
309-1015	Paint Water Closet "A"	2	11-Jun-27	14-Jun-27	24
309-1020	Install Lighting Fixture in Water Closet "A"	1	15-Jun-27	15-Jun-27	24
309-1025	Install Lighting Cable, & Devices in Water Closet "A"	1	17-Jun-27	17-Jun-27	24
NEW ADDITION ROOFING		92	03-Nov-26	23-Mar-27	80
ROOFING		10	20-Jan-27	02-Feb-27	0
ADD-1250	Installation of Roofing	10	20-Jan-27	02-Feb-27	0
ROOFING MEPs		92	03-Nov-26	23-Mar-27	53
EXT-1030	Rig Rooftop Units	3	03-Nov-26	05-Nov-26	31
EXT-1045	Install Rooftop Units Mechanical Connections	20	06-Nov-26	08-Dec-26	31
EXT-1065	Install Rooftop Units Electrical Connections	20	09-Dec-26	07-Jan-27	31
EXT-1035	Install Lightning protection system	15	03-Feb-27	25-Feb-27	59
EXT-1145	Test Rooftop Units	5	17-Mar-27	23-Mar-27	53
ROOFING ACCESSORIES		6	03-Feb-27	10-Feb-27	106
EXT-1105	Install Gutters and Rain Guards	5	03-Feb-27	09-Feb-27	107
EXT-1110	Install Roof Railings	5	03-Feb-27	09-Feb-27	49
EXT-1165	Install Roof top Smoke Release Control Relay	3	03-Feb-27	05-Feb-27	88
EXT-1175	Install Roof top Smoke Horns &Strobes	3	08-Feb-27	10-Feb-27	88
NEW ADDITION LIBRARY ELEVATOR		167	10-Nov-26	20-Jul-27	2
ELEV-1010	Install CMU Elevator Shaft	10	10-Nov-26	24-Nov-26	92
ELEV-1015	Install Elevator Rails	5	25-Nov-26	03-Dec-26	92
ELEV-1020	Install Elevator Platforms	10	04-Dec-26	17-Dec-26	92
ELEV-1025	Install Elevator Cab	10	18-Dec-26	04-Jan-27	92
ELEV-1030	Install Sump Pump & Panel	2	18-Dec-26	21-Dec-26	110
ELEV-1035	Install Discharge Piping Sump Pump	10	22-Dec-26	06-Jan-27	110
ELEV-1045	Pull Electrical Cable Sump Pump & Panel	5	07-Jan-27	13-Jan-27	110

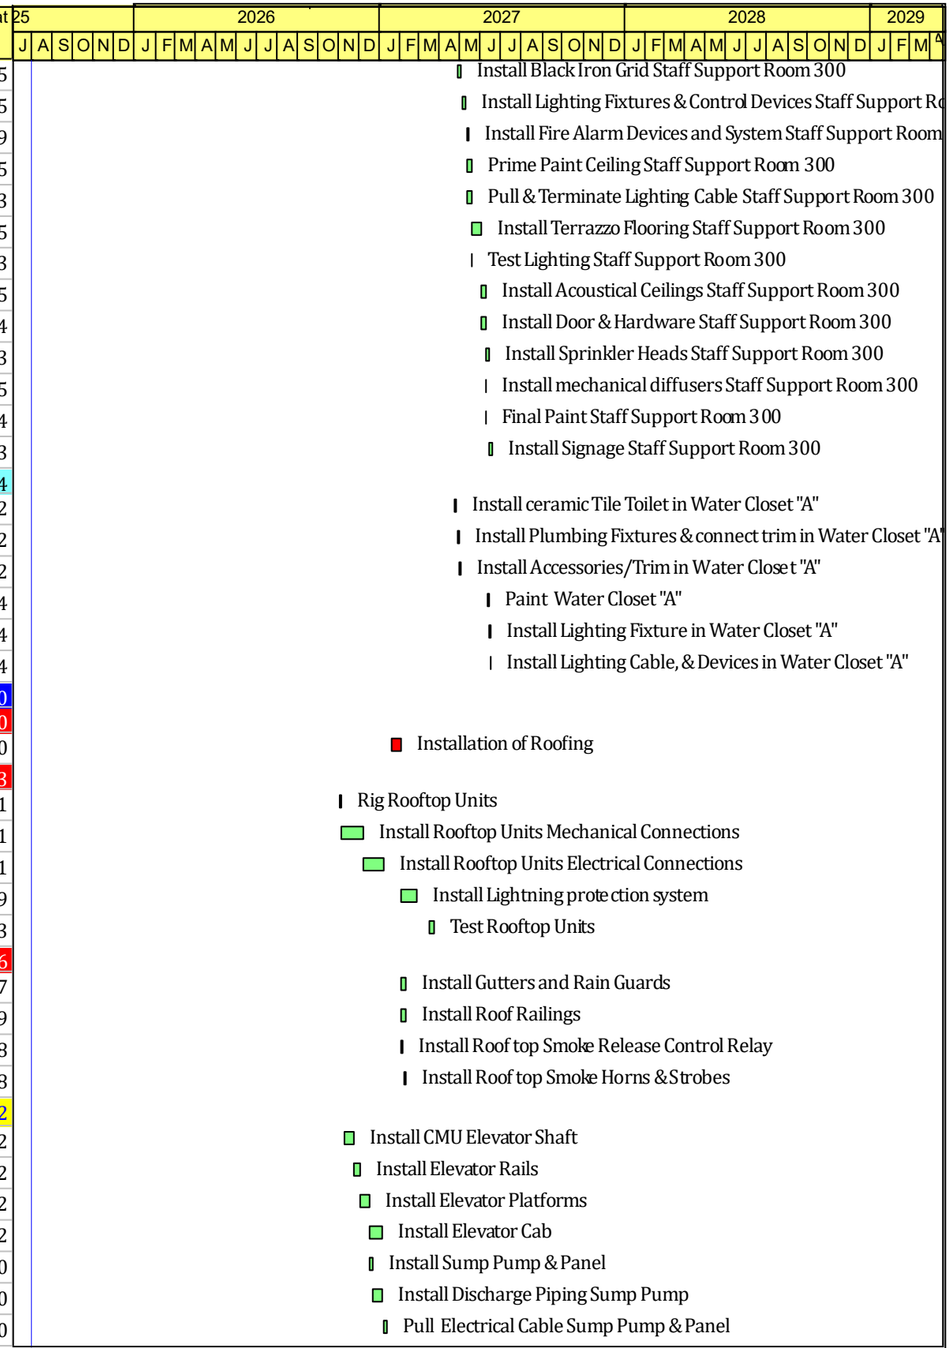

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
ELEV-1050	Terminate Cable Sump Pump & Panel	5	07-Jan-27	13-Jan-27	110
ELEV-1055	Leak Test Water Pipe & Insulate	1	07-Jan-27	07-Jan-27	114
ELEV-1060	Preliminary Test Sump Pump & Panel	5	14-Jan-27	21-Jan-27	110
ELEV-1040	Install Elevator Cab wiring & Terminations	15	21-May-27	11-Jun-27	0
ELEV-1085	Install Elevator Cab Fire Alarm Call back System	5	14-Jun-27	21-Jun-27	0
ELEV-1065	Install Elevator Cab Finishes & door Trim	10	22-Jun-27	05-Jul-27	0
ELEV-1070	Troubleshoot & Preliminary Testing of Elevator	5	06-Jul-27	12-Jul-27	0
ELEV-1075	Final Testing & sign-off of Elevator	5	13-Jul-27	20-Jul-27	2
ELEV-1095	Test Fire Alarm System for Elevator	5	13-Jul-27	20-Jul-27	0
EXISTING LIBRARY CONSTRUCTION		165	14-Oct-26	18-Jun-27	21
EXISTING LIBRARY CELLAR FLOOR		151	14-Oct-26	28-May-27	35
CEL-2240	Install Overhead Plumbing Pipe Existing Library Cellar Floor	15	14-Oct-26	03-Nov-26	24
CEL-2245	Install Overhead Sprinkler Pipe Existing Library Cellar Floor	15	14-Oct-26	03-Nov-26	24
CEL-2250	Install Overhead Electrical Existing Library Cellar Floor	15	14-Oct-26	03-Nov-26	24
CEL-2255	Install Overhead Mechanical Ductwork & Split AC Units Existing Library Cellar Floor	15	14-Oct-26	03-Nov-26	24
CEL-2260	Install Walls Framing Existing Library Cellar Floor	15	04-Nov-26	25-Nov-26	9
CEL-2265	Install Plumbing Piping in Walls Existing Library Cellar Floor	10	04-Nov-26	18-Nov-26	43
CEL-2270	Install Sprinkler Piping thru Walls Existing Library Cellar Floor	10	04-Nov-26	18-Nov-26	48
CEL-2275	Install Electrical Rough-in in Walls Existing Library Cellar Floor	10	04-Nov-26	18-Nov-26	48
CEL-2280	Install Mechanical Ductwork in Walls Existing Library Cellar Floor	10	04-Nov-26	18-Nov-26	48
CEL-2285	Install Overhead Mechanical Piping Existing Library Cellar Floor	15	04-Nov-26	25-Nov-26	28
CEL-2315	Installl Control Dampers in Ductwork Existing Library Cellar Floor	20	04-Nov-26	04-Dec-26	120
CEL-2295	Leak test & insulate Plumbing piping walls Existing Library Cellar Floor	5	19-Nov-26	25-Nov-26	43
CEL-2305	Install Mechanical Unit Heaters System Existing Library Cellar Floor	15	30-Nov-26	18-Dec-26	28
CEL-2310	Install Mechanical Piping in Walls Existing Library Cellar Floor	15	30-Nov-26	18-Dec-26	28
CEL-2325	Pull & Terminate Wires for Control Dampers Existing Library Cellar Floor	10	07-Dec-26	18-Dec-26	120
INSP-1025	Hold Point Inspection to Install Gypsum Board wall and ceilings Existing Library Cellar Floor	1	21-Dec-26	21-Dec-26	28
CEL-2330	Install Gypsum Board wall and ceilings Existing Library Cellar Floor	15	03-Feb-27	25-Feb-27	0
CEL-2340	Perform Tape & Spackle Existing Library Cellar Floor	10	26-Feb-27	12-Mar-27	0
CEL-2410	Prime Paint Existing Library Cellar Floor	5	15-Mar-27	19-Mar-27	45
CEL-2435	Install CCTVs Existing Library Cellar Floor	7	22-Mar-27	30-Mar-27	56
CEL-2405	Install Audiovisual Equipment Existing Library Cellar Floor	7	22-Mar-27	30-Mar-27	56
CEL-2425	Pull Communication cable,Install Telecom Outlets Existing Library Cellar Floor	7	31-Mar-27	09-Apr-27	56
CEL-2400	Pull Audiovisual cable,Install Audiovisual Outlets Existing Library Cellar Floor	7	31-Mar-27	09-Apr-27	56
CLASSROOM 002		30	15-Mar-27	26-Apr-27	57
002-1000	Install Black Iron Grid Classroom 002	3	15-Mar-27	17-Mar-27	0
002-1005	Install Lighting Fixtures & Control DevicesClassroom 002	5	18-Mar-27	24-Mar-27	2
002-1010	Prime Paint Ceiling Classroom002	5	25-Mar-27	31-Mar-27	2
002-1015	Pull & Terminate Lighting Cable Classroom 002	5	25-Mar-27	31-Mar-27	37
002-1025	Install Terrazzo Flooring Classroom 002	6	01-Apr-27	09-Apr-27	2
002-1055	Install Fire Alarm Devices and System Classroom 002	3	01-Apr-27	05-Apr-27	37

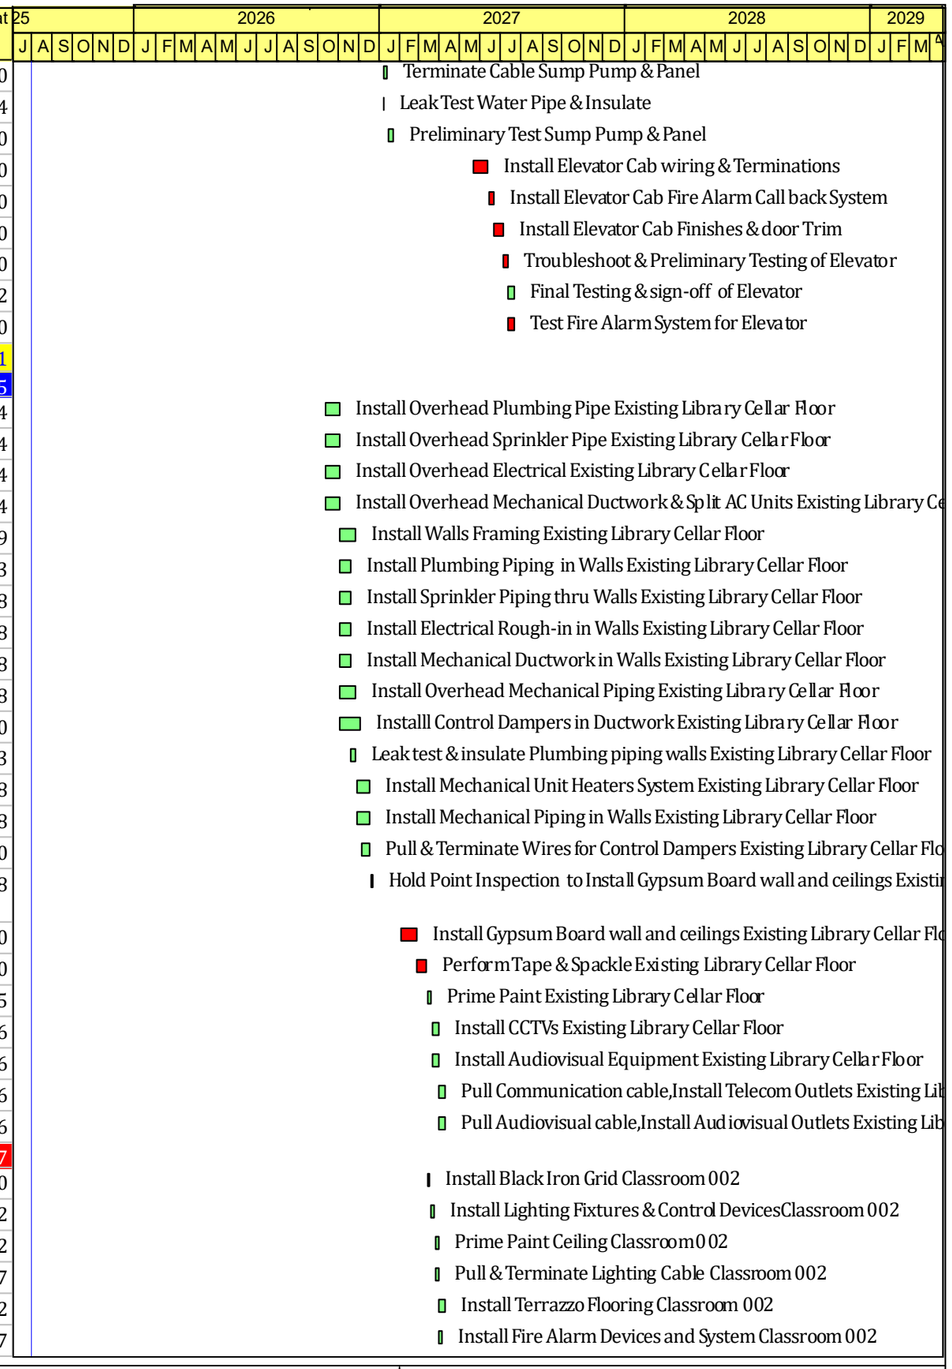

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
002-1040	Test Lighting Classroom 002	1	01-Apr-27	01-Apr-27	61
002-1030	Install Acoustical Ceilings Classroom 002	5	12-Apr-27	16-Apr-27	40
002-1020	Install Door & Hardware Classroom 002	5	12-Apr-27	16-Apr-27	2
002-1045	Install Sprinkler Heads Classroom 002	3	19-Apr-27	21-Apr-27	57
002-1050	Install mechanical diffusers Classroom 002	2	19-Apr-27	20-Apr-27	40
002-1035	Final Paint Classroom 002	1	19-Apr-27	19-Apr-27	12
002-1060	Install Signage Classroom 002	3	22-Apr-27	26-Apr-27	57
FLEXIBLE CLASSROOM 001		34	18-Mar-27	05-May-27	50
001-1000	Install Black Iron Grid Flexible Classroom 001	3	18-Mar-27	22-Mar-27	0
001-1005	Install Lighting Fixtures & Control Devices Flexible Classroom 001	5	23-Mar-27	29-Mar-27	0
001-1010	Prime Paint Ceiling Flexible Classroom 001	5	30-Mar-27	05-Apr-27	0
001-1015	Pull & Terminate Lighting Cable Flexible Classroom 001	5	30-Mar-27	05-Apr-27	37
001-1025	Install Terrazzo Flooring Flexible Classroom 001	10	06-Apr-27	20-Apr-27	0
001-1055	Install Fire Alarm Devices and System Flexible Classroom 001	3	06-Apr-27	09-Apr-27	37
001-1040	Test Lighting Flexible Classroom 001	1	06-Apr-27	06-Apr-27	58
001-1030	Install Acoustical Ceilings Flexible Classroom 001	5	21-Apr-27	27-Apr-27	33
001-1020	Install Door & Hardware Flexible Classroom 001	4	21-Apr-27	26-Apr-27	0
001-1035	Final Paint Flexible Classroom 001	1	21-Apr-27	21-Apr-27	11
001-1045	Install Sprinkler Heads Flexible Classroom 001	3	28-Apr-27	30-Apr-27	50
001-1050	Install mechanical diffusers Flexible Classroom 001	2	28-Apr-27	29-Apr-27	33
001-1060	Install Signage Flexible Classroom 001	3	03-May-27	05-May-27	50
STAFF ROOM 010		33	23-Mar-27	07-May-27	48
010-1000	Install Black Iron Grid Staff Room 010	2	23-Mar-27	24-Mar-27	2
010-1005	Install Lighting Fixtures & Control Devices Staff Room 010	5	25-Mar-27	31-Mar-27	2
010-1010	Prime Paint Ceiling Staff Room 010	5	01-Apr-27	08-Apr-27	2
010-1015	Pull & Terminate Lighting Cable Staff Room 010	5	01-Apr-27	08-Apr-27	38
010-1025	Install Terrazzo Flooring Staff Room 010	10	09-Apr-27	22-Apr-27	2
010-1040	Test Lighting Staff Room 010	1	09-Apr-27	09-Apr-27	56
010-1055	Install Fire Alarm Devices and System Staff Room 010	3	12-Apr-27	14-Apr-27	37
010-1030	Install Acoustical Ceilings Staff Room 010	5	23-Apr-27	29-Apr-27	31
010-1020	Install Door & Hardware Staff Room 010	4	27-Apr-27	30-Apr-27	0
010-1045	Install Sprinkler Heads Staff Room 010	3	30-Apr-27	04-May-27	48
010-1050	Install mechanical diffusers Staff Room 010	2	30-Apr-27	03-May-27	31
010-1035	Final Paint Staff Room 010	1	03-May-27	03-May-27	4
010-1060	Install Signage Staff Room 010	3	05-May-27	07-May-27	48
STAFF ROOM 003		33	25-Mar-27	11-May-27	46
003-1000	Install Black Iron Grid Staff Room 003	2	25-Mar-27	26-Mar-27	4
003-1005	Install Lighting Fixtures & Control Devices Staff Room 003	5	29-Mar-27	02-Apr-27	4
003-1010	Prime Paint Ceiling Staff Room 003	5	05-Apr-27	12-Apr-27	4
003-1015	Pull & Terminate Lighting Cable Staff Room 003	5	05-Apr-27	12-Apr-27	39
003-1025	Install Terrazzo Flooring Staff Room 003	10	13-Apr-27	26-Apr-27	4
003-1040	Test Lighting Staff Room 003	1	13-Apr-27	13-Apr-27	54

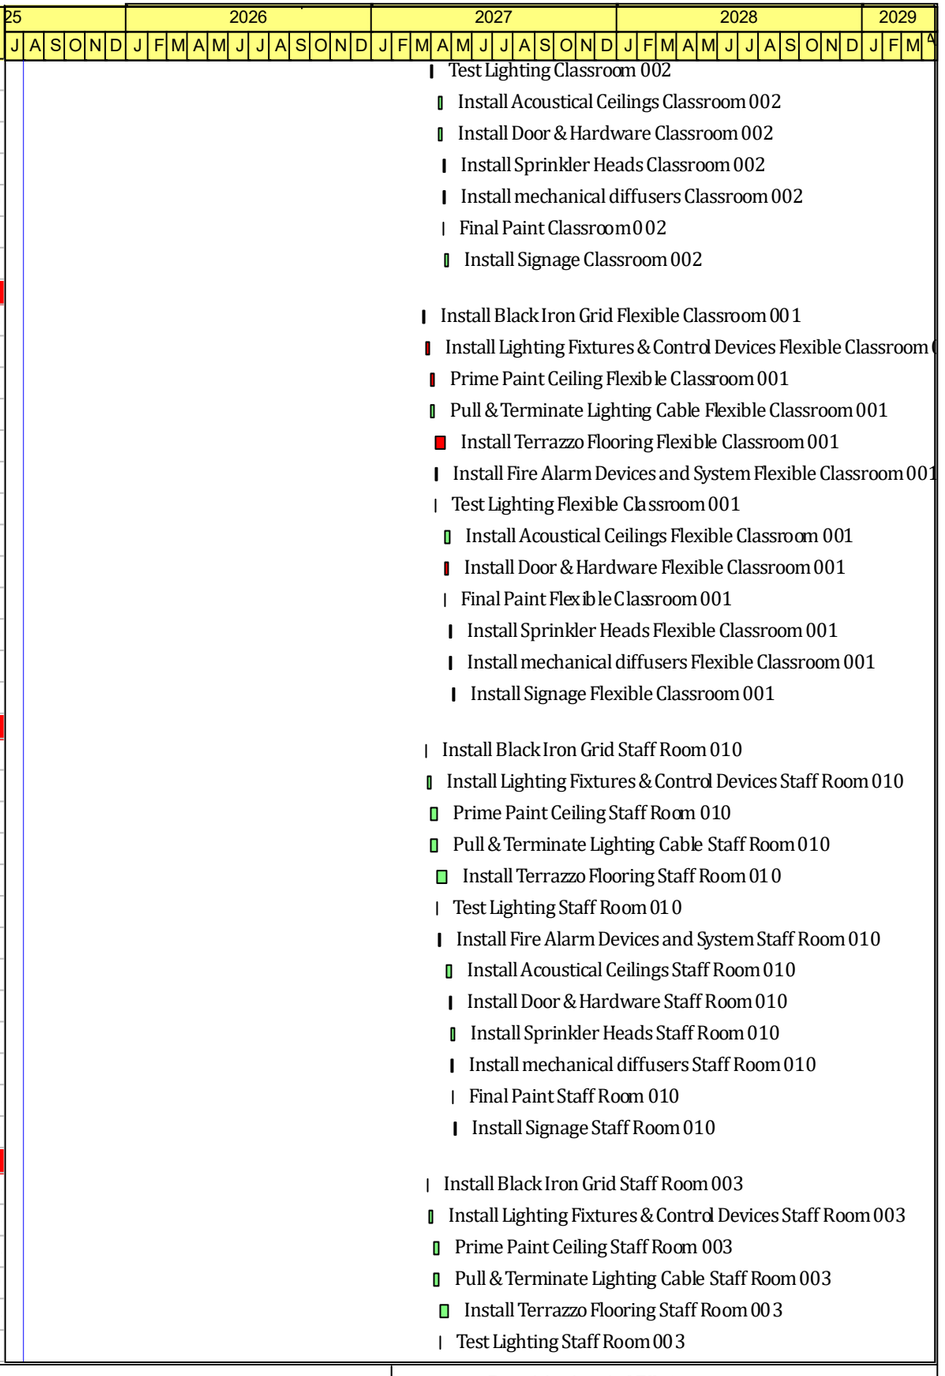

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
003-1055	Install Fire Alarm Devices and System Staff Room 003	3	15-Apr-27	19-Apr-27	37
003-1030	Install Acoustical Ceilings Staff Room 003	5	27-Apr-27	03-May-27	29
003-1020	Install Door & Hardware Staff Room 003	5	03-May-27	07-May-27	0
003-1045	Install Sprinkler Heads Staff Room 003	3	04-May-27	06-May-27	46
003-1050	Install mechanical diffusers Staff Room 003	2	04-May-27	05-May-27	29
003-1060	Install Signage Staff Room 003	3	07-May-27	11-May-27	46
003-1035	Final Paint Staff Room 003	1	10-May-27	10-May-27	0
ELEVATOR MACHINE ROOM 105		97	05-Jan-27	28-May-27	32
015-1040	Install Exhaust Fan in Elevator Control Room	3	05-Jan-27	07-Jan-27	120
015-1005	Pull & Terminate Cable for Exhaust Fan in Elevator Control Room	3	08-Jan-27	12-Jan-27	120
015-1010	Install Elevator Conduit & Wire Between Elevator Control Room & Elevator	10	15-Mar-27	26-Mar-27	37
015-1000	Test Exhaust Fan in Elevator Control Room	3	17-Mar-27	19-Mar-27	79
015-1035	Paint Elevator Control Room	2	11-May-27	13-May-27	0
015-1030	Install Elevator Controls Elevator Control Room	10	14-May-27	28-May-27	0
015-1025	Install Lighting Fixture in Elevator Control Room	1	14-May-27	14-May-27	39
015-1020	Install Lighting Cable, & Devices in Elevator Control Room	1	17-May-27	17-May-27	39
015-1015	Test Lighting in Elevator Control Room	1	18-May-27	18-May-27	39
WATER CLOSET "D" 106		7	26-Feb-27	08-Mar-27	90
016-1025	Install ceramic Tile Toilet in Water Closet "D"	2	26-Feb-27	01-Mar-27	78
016-1020	Install Plumbing Fixtures & connect trim in Water Closet "D"	3	02-Mar-27	04-Mar-27	78
016-1010	Paint Water Closet "D"	2	02-Mar-27	03-Mar-27	79
016-1015	Install Accessories/Trim in Water Closet "D"	2	05-Mar-27	08-Mar-27	90
016-1005	Install Lighting Fixture in Water Closet "D"	1	05-Mar-27	05-Mar-27	78
016-1000	Install Lighting Cable, & Devices in Water Closet "D"	1	08-Mar-27	08-Mar-27	78
EXISTING LIBRARY 1ST FLOOR		150	04-Nov-26	18-Jun-27	21
1st-1585	Install Overhead Plumbing Pipe Existing Library 1st Floor	15	04-Nov-26	25-Nov-26	72
1st-1590	Install Overhead Sprinkler Pipe Existing Library 1st Floor	15	04-Nov-26	25-Nov-26	72
1st-1595	Install Overhead Electrical Existing Library 1st Floor	15	04-Nov-26	25-Nov-26	72
1st-1600	Install Overhead Mechanical Ductwork & Split Ac Units Existing Library 1st Floor	15	04-Nov-26	25-Nov-26	57
1st-1605	Install Walls Framing Existing Library 1st Floor	15	30-Nov-26	18-Dec-26	9
1st-1620	Install Electrical Rough-in in Walls Existing Library 1st Floor	10	30-Nov-26	11-Dec-26	72
1st-1630	Install Overhead Mechanical Piping Existing Library 1st Floor	15	30-Nov-26	18-Dec-26	67
1st-1660	Installl Control Dampers in Ductwork Existing Library 1st Floor	10	30-Nov-26	11-Dec-26	115
1st-1670	Pull & Terminate Wires for Control Dampers Existing Library 1st Floor	10	14-Dec-26	28-Dec-26	115
INSP-1030	Hold Point Inspection to Install Gypsum Board wall and ceilings Existing Library 1st Floor	1	21-Dec-26	21-Dec-26	67
1st-1675	Install Gypsum Board wall and ceilings Existing Library 1st Floor	10	03-Feb-27	18-Feb-27	39
1st-1685	Perform Tape & Spackle Existing Library 1st Floor	5	19-Feb-27	25-Feb-27	64
1st-1735	Pull Communication cable,Install Telecom Outlets Existing Library 1st Floor	7	26-Feb-27	08-Mar-27	78
1st-1780	Install CCTVs Existing Library 1st Floor	7	26-Feb-27	08-Mar-27	64
1st-1750	Install Audiovisual Equipment Existing Library 1st Floor	7	26-Feb-27	08-Mar-27	64
1st-1740	Pull Security cable,Install Security Outlets Existing Library 1st Floor	7	09-Mar-27	18-Mar-27	71
1st-1725	Pull Audiovisual cable,Install Audiovisual Outlets Existing Library 1st Floor	7	09-Mar-27	18-Mar-27	71

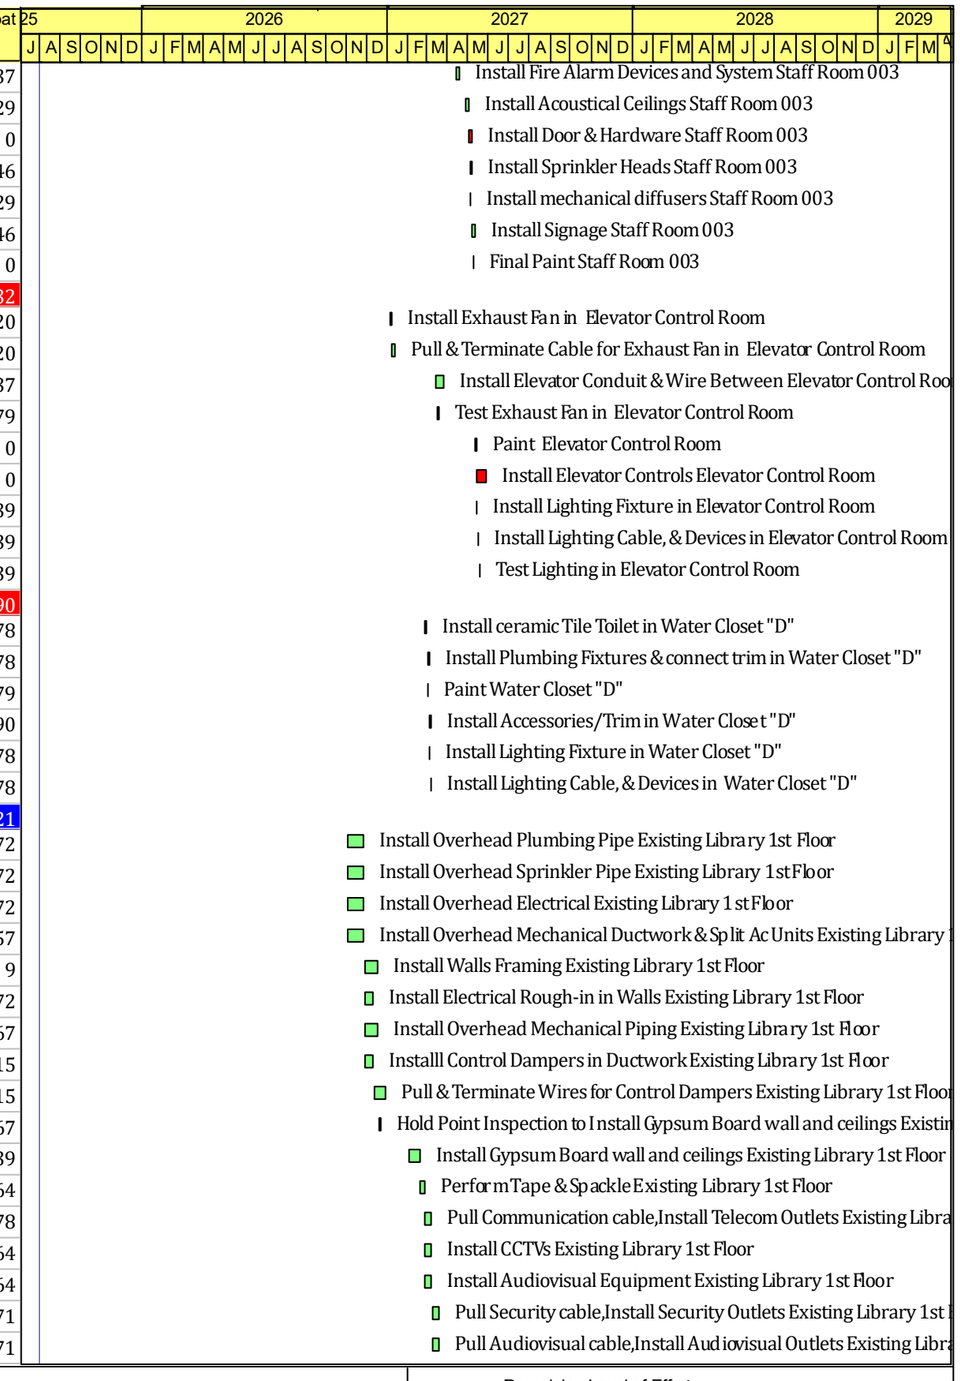

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
READING ROOM 102		42	29-Mar-27	28-May-27	35
102-1000	Install Black Iron Grid Reading Room 102	2	29-Mar-27	30-Mar-27	14
102-1005	Install Lighting Fixtures & Control Devices Reading Room 102	5	31-Mar-27	06-Apr-27	14
102-1010	Prime Paint Ceiling Reading Room 102	5	08-Apr-27	14-Apr-27	27
102-1015	Pull & Terminate Lighting Cable Reading Room 102	5	08-Apr-27	14-Apr-27	37
102-1020	Install Terrazzo Flooring Reading Room 102	10	15-Apr-27	28-Apr-27	27
102-1055	Install Fire Alarm Devices and System Reading Room 102	3	15-Apr-27	19-Apr-27	37
102-1040	Test Lighting Reading Room 102	1	15-Apr-27	15-Apr-27	52
102-1025	Install Acoustical Ceilings Reading Room 102	5	29-Apr-27	05-May-27	27
102-1030	Final Paint Reading Room 102	1	29-Apr-27	29-Apr-27	44
102-1065	Install White Oak Wood Veneer Reading Room 102	10	29-Apr-27	13-May-27	35
102-1045	Install Sprinkler Heads Reading Room 102	3	06-May-27	10-May-27	44
102-1050	Install mechanical diffusers Reading Room 102	2	06-May-27	07-May-27	27
102-1060	Install Fire Extinguishers and Signage Reading Room 102	3	11-May-27	14-May-27	44
102-1035	Install Millwork & Shelving Units Reading Room 102	10	14-May-27	28-May-27	35
VESTIBULE 100		44	08-Apr-27	10-Jun-27	26
100-1005	Install Lighting Fixtures & Control Devices Vestibule 100	5	08-Apr-27	14-Apr-27	14
100-1010	Prime Paint Ceiling Vestibule 100	5	15-Apr-27	21-Apr-27	14
100-1015	Pull & Terminate Lighting Cable Vestibule 100	5	15-Apr-27	21-Apr-27	47
100-1020	Install Terrazzo Flooring Vestibule 100	10	22-Apr-27	05-May-27	14
100-1055	Install Fire Alarm Devices and System Vestibule 100	3	22-Apr-27	26-Apr-27	32
100-1040	Test Lighting Vestibule 100	1	22-Apr-27	22-Apr-27	47
100-1075	Install White Oak Wood Veneer Vestibule 100	10	22-Apr-27	05-May-27	47
100-1030	Final Paint Vestibule 100	1	06-May-27	06-May-27	14
100-1035	Install Interior Door Vestibule 100	10	07-May-27	21-May-27	14
100-1045	Install Sprinkler Heads Vestibule 100	3	25-May-27	27-May-27	33
100-1050	Install mechanical diffusers Vestibule 100	2	25-May-27	26-May-27	16
100-1065	Install Security Access Vestibule 100	8	25-May-27	03-Jun-27	14
100-1060	Install Signage Vestibule 100	3	28-May-27	01-Jun-27	33
100-1070	Pull & Terminate Security Cable Vestibule 100	5	04-Jun-27	10-Jun-27	14
WELCOME AND SERVICE 101		54	31-Mar-27	18-Jun-27	21
101-1000	Install Black Iron Grid Welcome and Service Area 101	4	31-Mar-27	05-Apr-27	16
101-1005	Install Lighting Fixtures & Control Devices Welcome and Service Area 101	5	06-Apr-27	13-Apr-27	21
101-1010	Prime Paint Ceiling Welcome and Service Area 101	5	14-Apr-27	20-Apr-27	21
101-1015	Pull & Terminate Lighting Cable Welcome and Service Area 101	5	14-Apr-27	20-Apr-27	33
101-1020	Install Terrazzo Flooring Welcome and Service Area 101	5	21-Apr-27	27-Apr-27	21
101-1055	Install Fire Alarm Devices and System Welcome and Service Area 101	3	21-Apr-27	23-Apr-27	33
101-1040	Test Lighting Welcome and Service Area 101	1	21-Apr-27	21-Apr-27	48
101-1025	Install Acoustical Ceilings Welcome and Service Area 101	5	28-Apr-27	04-May-27	23
101-1030	Final Paint Welcome and Service Area 101	1	28-Apr-27	28-Apr-27	35
101-1065	Install White Oak Wood Veneer Welcome and Service Area 101	15	28-Apr-27	19-May-27	21
101-1045	Install Sprinkler Heads Welcome and Service Area 101	3	05-May-27	07-May-27	23

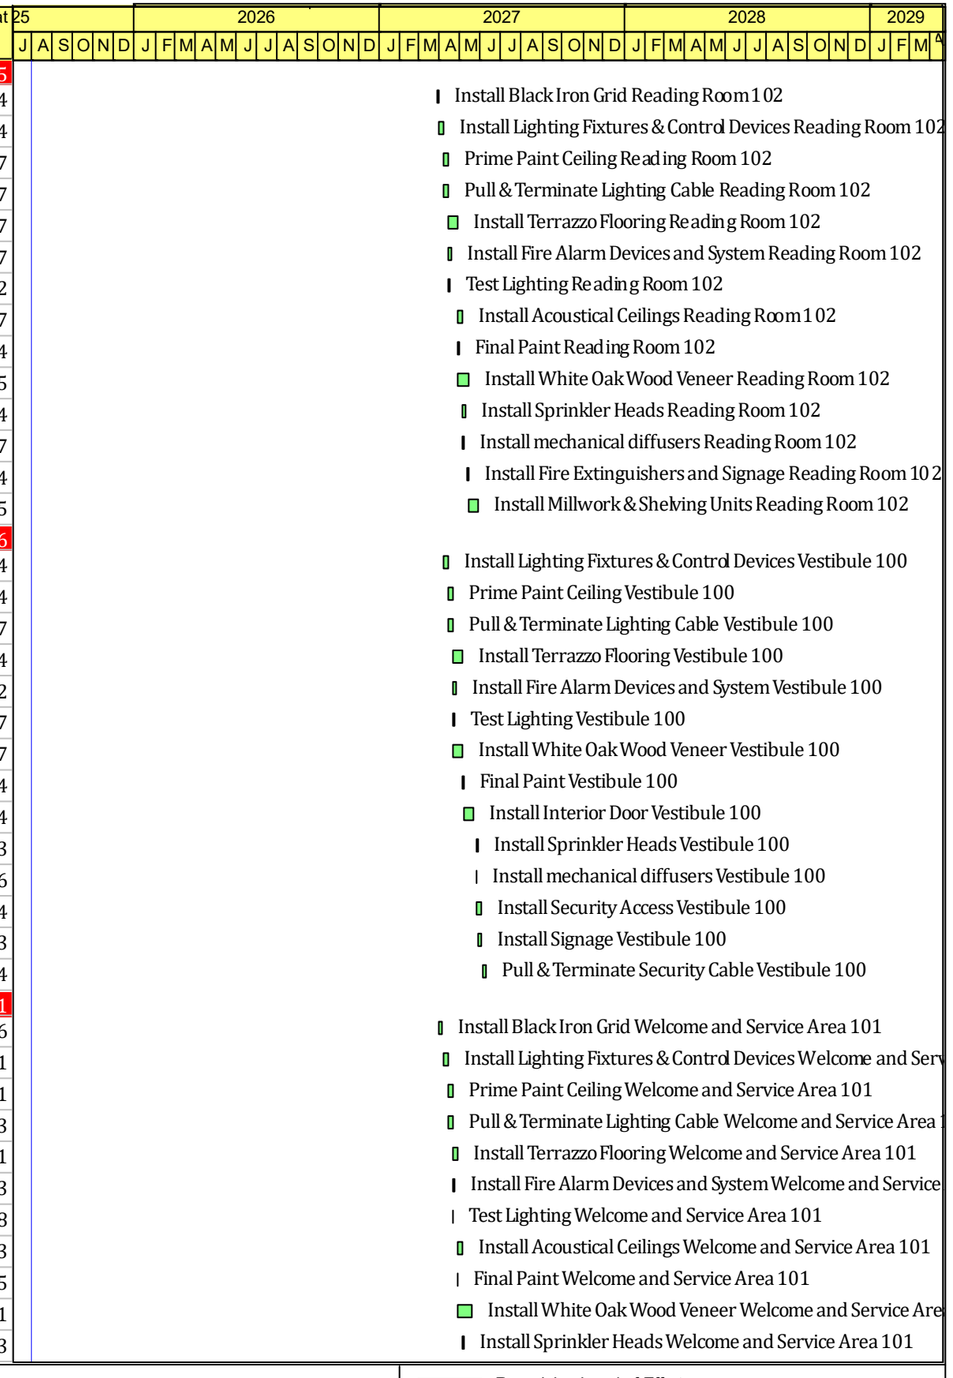

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
101-1050	Install mechanical diffusers Welcome and Service Area 101	2	05-May-27	06-May-27	28
101-1035	Install Reception Desk & Self Check-out Kiosk Unit Welcome and Service Area 101	5	20-May-27	27-May-27	21
101-1060	Fit-out Reception Desk & Self Check-out Kiosk Unit Welcome and Service Area 101	15	28-May-27	18-Jun-27	21
READING ROOM 103		35	06-Apr-27	27-May-27	36
103-1000	Install Black Iron Grid Reading Room 103	2	06-Apr-27	08-Apr-27	16
103-1005	Install Lighting Fixtures & Control Devices Reading Room 103	5	09-Apr-27	15-Apr-27	21
103-1010	Prime Paint Ceiling Reading Room 103	5	16-Apr-27	22-Apr-27	21
103-1015	Pull & Terminate Lighting Cable Reading Room 103	5	16-Apr-27	22-Apr-27	31
103-1020	Install Terrazzo Flooring Reading Room 103	10	23-Apr-27	06-May-27	21
103-1055	Install Fire Alarm Devices and System Reading Room 103	3	23-Apr-27	27-Apr-27	31
103-1040	Test Lighting Reading Room 103	1	23-Apr-27	23-Apr-27	46
103-1025	Install Acoustical Ceilings Reading Room 103	5	07-May-27	14-May-27	21
103-1030	Final Paint Reading Room 103	1	07-May-27	07-May-27	38
103-1065	Install White Oak Wood Veneer Reading Room 103	3	07-May-27	11-May-27	36
103-1035	Install Millwork & Shelving Units Reading Room 103	10	13-May-27	27-May-27	36
103-1045	Install Sprinkler Heads Reading Room 103	3	17-May-27	19-May-27	38
103-1050	Install mechanical diffusers Reading Room 103	2	17-May-27	18-May-27	21
103-1060	Install Signage Reading Room 103	3	20-May-27	25-May-27	38
MEETING ROOM 109		26	09-Apr-27	17-May-27	43
109-1000	Install Black Iron Grid Meeting Room 109	2	09-Apr-27	12-Apr-27	16
109-1025	Install Acoustical Ceilings Meeting Room 109	5	13-Apr-27	19-Apr-27	39
109-1005	Install Lighting Fixtures & Control Devices Meeting Room 109	5	13-Apr-27	19-Apr-27	29
109-1045	Install Sprinkler Heads Meeting Room 109	3	20-Apr-27	22-Apr-27	56
109-1050	Install mechanical diffusers Meeting Room 109	2	20-Apr-27	21-Apr-27	39
109-1010	Prime Paint Ceiling Meeting Room 109	5	20-Apr-27	26-Apr-27	43
109-1015	Pull & Terminate Lighting Cable Meeting Room 109	5	20-Apr-27	26-Apr-27	29
109-1055	Install Fire Alarm Devices and System Meeting Room 109	3	27-Apr-27	29-Apr-27	29
109-1030	Install Interior Glazing Meeting Room 109	1	27-Apr-27	27-Apr-27	43
109-1040	Test Lighting Meeting Room 109	1	27-Apr-27	27-Apr-27	44
109-1035	Install White Oak Base Trim Meeting Room 109	10	28-Apr-27	11-May-27	43
109-1060	Install Signage Meeting Room 109	3	13-May-27	17-May-27	43
EXISTING LIBRARY 2ND FLOOR		125	30-Nov-26	03-Jun-27	31
2nd-1585	Install Overhead Storm Plumbing Pipe, Existing 2nd Floor	15	30-Nov-26	18-Dec-26	72
2nd-1590	Install Overhead Sprinkler Pipe Existing 2nd Floor	15	30-Nov-26	18-Dec-26	72
2nd-1595	Install Overhead Electrical Existing 2nd Floor	15	30-Nov-26	18-Dec-26	72
2nd-1600	Install Overhead Mechanical Ductwork& Split AC Units Existing 2nd Floor	15	30-Nov-26	18-Dec-26	57
2nd-1660	Installl Control Dampers in Ductwork Existing 2nd Floor	10	30-Nov-26	11-Dec-26	115
2nd-1670	Pull & Terminate Wires for Control Dampers Existing 2nd Floor	10	14-Dec-26	28-Dec-26	115
2nd-1605	Install Walls Framing Existing 2nd Floor	15	21-Dec-26	12-Jan-27	57
2nd-1620	Install Electrical Rough-in in Walls Existing 2nd Floor	10	21-Dec-26	05-Jan-27	62
2nd-1630	Install Overhead Mechanical Piping Existing 2nd Floor	15	21-Dec-26	12-Jan-27	57
INSP-1040	Hold Point Inspection to Install Gypsum Board wall and ceilings Existing 2nd Floor	1	13-Jan-27	13-Jan-27	57

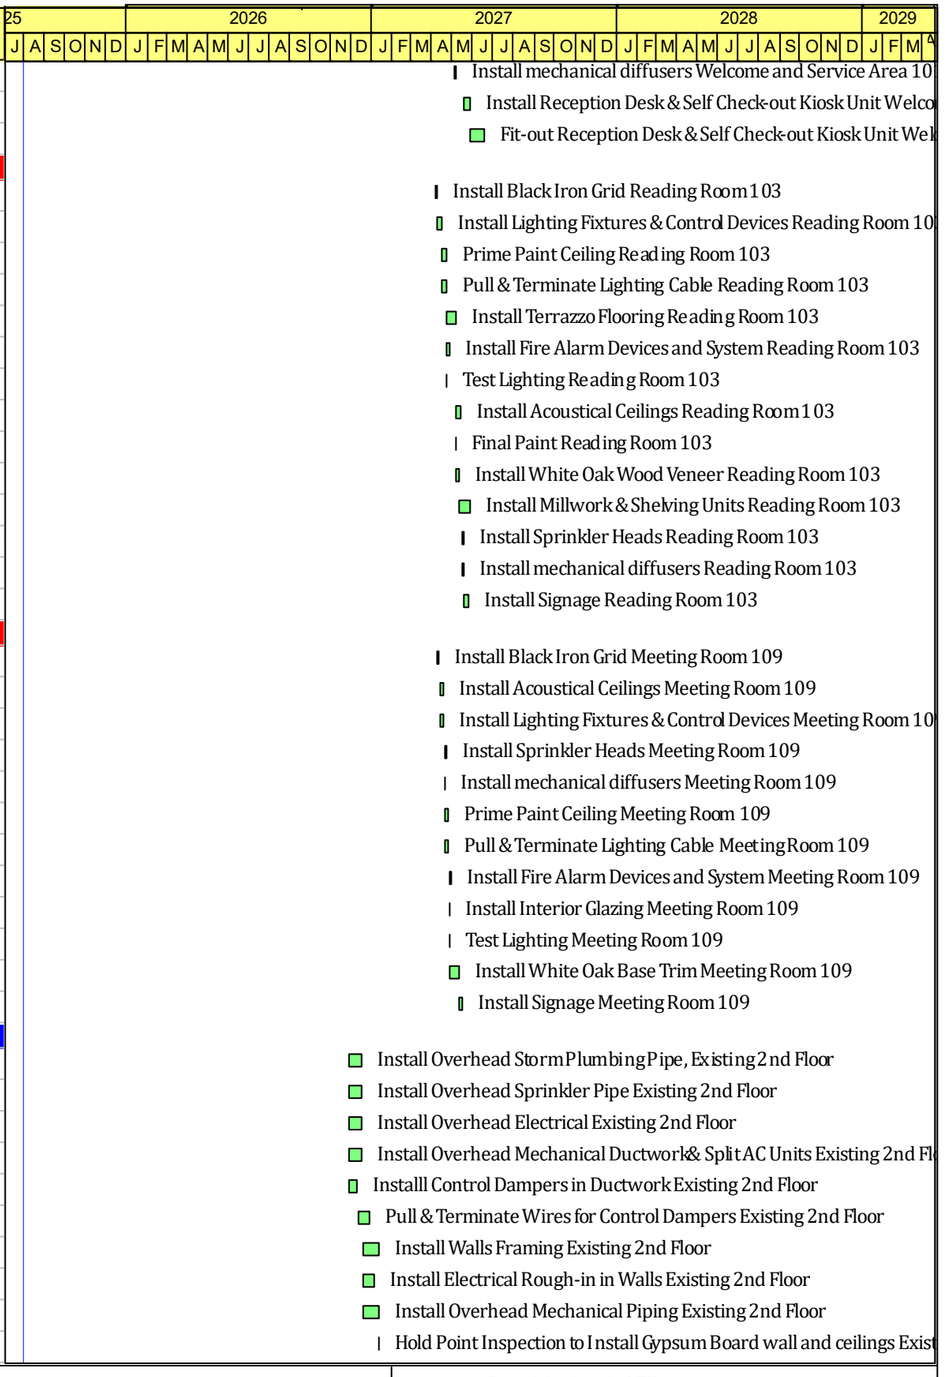

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
INSP-1010	Phase 1 Inspection Completion of Wall Framing Existing	2	13-Jan-27	14-Jan-27	68
2nd-1675	Install Gypsum Board wall and ceilings Existing 2nd Floor	10	03-Feb-27	18-Feb-27	44
INSP-1070	Phase 2 Inspection Completion of Gypsum Wall Board Existing	2	26-Feb-27	01-Mar-27	39
2nd-1685	Perform Tape & Spackle Existing 2nd Floor	5	02-Mar-27	08-Mar-27	39
2nd-1780	Install CCTVs Existing 2nd Floor	7	09-Mar-27	18-Mar-27	64
INSP-1080	Phase 3 Inspection Start of Finishes in Existing	2	15-Mar-27	16-Mar-27	59
2nd-1750	Install Audiovisual Equipment Existing 2nd Floor	7	17-Mar-27	25-Mar-27	59
2nd-1735	Pull Communication cable,Install Telecom Outlets Existing 2nd Floor	7	19-Mar-27	29-Mar-27	64
2nd-1725	Pull Audiovisual cable,Install Audiovisual Outlets Existing 2nd Floor	7	26-Mar-27	05-Apr-27	59
INSP-1100	Phase 4 Inspection Completion of Finishes in Existing	2	02-Jun-27	03-Jun-27	31
ADULT ZONE 202		31	13-Apr-27	27-May-27	36
202-1000	Install Black Iron Grid Adult Zone Room 202	2	13-Apr-27	14-Apr-27	16
202-1005	Install Lighting Fixtures & Control Devices Adult Zone Room 202	5	15-Apr-27	21-Apr-27	22
202-1010	Prime Paint Ceiling Adult Zone Room 202	5	22-Apr-27	28-Apr-27	22
202-1015	Pull & Terminate Lighting Cable Adult Zone Room 202	5	22-Apr-27	28-Apr-27	27
202-1020	Install Terrazzo Flooring Adult Zone Room 202	5	29-Apr-27	05-May-27	22
202-1055	Install Fire Alarm Devices and System Adult Zone Room 202	3	29-Apr-27	03-May-27	27
202-1040	Test Lighting Adult Zone Room 202	1	29-Apr-27	29-Apr-27	42
202-1025	Install Acoustical Ceilings Adult Zone Room 202	5	06-May-27	13-May-27	22
202-1030	Final Paint Adult Zone Room 202	1	06-May-27	06-May-27	36
202-1035	Install Book Shelf Unit Adult Zone Room 202	10	07-May-27	21-May-27	36
202-1045	Install Sprinkler Heads Adult Zone Room 202	3	14-May-27	18-May-27	39
202-1050	Install mechanical diffusers Adult Zone Room 202	2	14-May-27	17-May-27	22
202-1060	Install Fire Extinguishers and Signage Adult Zone Room 202	3	25-May-27	27-May-27	36
TEEN ZONE 201		20	15-Apr-27	13-May-27	45
201-1000	Install Black Iron Grid Teen Zone Room 201	4	15-Apr-27	20-Apr-27	16
201-1025	Install Metal Ceilings Teen Zone Room 201	5	21-Apr-27	27-Apr-27	33
201-1005	Install Lighting Fixtures & Control Devices Teen Zone Room 201	5	21-Apr-27	27-Apr-27	38
201-1045	Pull Communication cable,Install Telecom Outlets Teen Zone Room 201	7	23-Apr-27	03-May-27	24
201-1035	Install Sprinkler Heads Teen Zone Room 201	3	28-Apr-27	30-Apr-27	50
201-1050	Install mechanical diffusers Teen Zone Room 201	2	28-Apr-27	29-Apr-27	33
201-1020	Install Terrazzo Flooring Teen Zone Room 201	5	28-Apr-27	04-May-27	45
201-1010	Prime Paint Ceiling Teen Zone Room 201	5	28-Apr-27	04-May-27	45
201-1015	Pull & Terminate Lighting Cable Teen Zone Room 201	5	28-Apr-27	04-May-27	38
201-1065	Install Fire Extinguishers and Signage Teen Zone Room 201	3	03-May-27	05-May-27	50
201-1055	Install Fire Alarm Devices and System Teen Zone Room 201	3	04-May-27	06-May-27	24
201-1030	Final Paint Teen Zone Room 201	1	05-May-27	05-May-27	45
201-1060	Test Lighting Teen Zone Room 201	1	05-May-27	05-May-27	38
201-1040	Install Bench & Display Shelf Unit Teen Zone Room 201	5	06-May-27	13-May-27	45
ADULT ZONE 203		28	21-Apr-27	01-Jun-27	31
203-1000	Install Black Iron Grid Adult Zone Room 203	2	21-Apr-27	22-Apr-27	16
203-1005	Install Lighting Fixtures & Control Devices Adult Zone Room 203	5	23-Apr-27	29-Apr-27	16



Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
203-1010	Prime Paint Ceiling Adult Zone Room 203	5	30-Apr-27	06-May-27	16
203-1015	Pull & Terminate Lighting Cable Adult Zone Room 203	5	30-Apr-27	06-May-27	21
203-1020	Install Terrazzo Flooring Adult Zone Room 203	5	07-May-27	14-May-27	16
203-1055	Install Fire Alarm Devices and System Adult Zone Room 203	3	07-May-27	11-May-27	21
203-1040	Test Lighting Adult Zone Room 203	1	07-May-27	07-May-27	36
203-1025	Install Acoustical Ceiling Adult Zone Room 203	5	17-May-27	21-May-27	16
203-1030	Final Paint Adult Zone Room 203	1	17-May-27	17-May-27	33
203-1035	Install Book Shelf Unit Adult Zone Room 203	5	18-May-27	25-May-27	33
203-1045	Install Sprinkler Heads Adult Zone Room 203	3	25-May-27	27-May-27	31
203-1050	Install mechanical diffusers Adult Zone Room 203	2	25-May-27	26-May-27	16
203-1060	Install Fire Extinguishers and Signage Adult Zone Room 203	3	28-May-27	01-Jun-27	31
EXISTING LIBRARY ROOFING		92	03-Nov-26	23-Mar-27	53
ROOFING MEPs		92	03-Nov-26	23-Mar-27	53
EXT-1185	Rig Rooftop Units Existing Library	3	03-Nov-26	05-Nov-26	31
EXT-1195	Install Rooftop Units Mechanical Connections Existing Library	20	06-Nov-26	08-Dec-26	31
EXT-1205	Install Rooftop Units Electrical Connections Existing Library	20	09-Dec-26	07-Jan-27	31
EXT-1215	Install Lightning protection system Existing Library	15	03-Feb-27	25-Feb-27	59
EXT-1225	Test Rooftop Units Existing Library	5	17-Mar-27	23-Mar-27	53
SITEWORK		45	20-Jan-27	26-Mar-27	72
SITE-1050	Excavate, Drill penetration thru wall & Install Combined Sewer (Sanitary)	5	20-Jan-27	26-Jan-27	19
SITE-1060	Excavate, Drill penetration thru wall & Install water & Fire Service	5	20-Jan-27	26-Jan-27	19
SITE-1030	Excavate, Drill penetration thru wall & Install Electric Service From Street by Con Edison	2	20-Jan-27	21-Jan-27	19
SITE-1040	Excavate, Drill penetration thru wall & Install Data Service Cable Company	5	20-Jan-27	26-Jan-27	19
SITE-1130	Schedule Con Edison to Provide Upgraded Electric Service	20	22-Jan-27	22-Feb-27	53
SITE-1070	Install Site Grading and Site Concrete	15	27-Jan-27	18-Feb-27	19
SITE-1090	Install Site Lighting	15	27-Jan-27	18-Feb-27	29
SITE-1080	Install Site Paving	5	19-Feb-27	25-Feb-27	39
SITE-1220	Install Handicap Pedestrain Concrete Ramp	5	19-Feb-27	25-Feb-27	19
SITE-1140	Con Edison Upgrade Permanent ElectricService	5	23-Feb-27	01-Mar-27	53
SITE-1190	Install Bike Racks	5	26-Feb-27	04-Mar-27	87
SITE-1200	Install Exterior Benches	5	26-Feb-27	04-Mar-27	87
SITE-1230	Install Handralis Pedestrain Concrete Ramp	5	26-Feb-27	04-Mar-27	19
SITE-1100	Install Site Fences and Gates	15	05-Mar-27	26-Mar-27	19
SITE-1120	Install Landscaping	5	22-Mar-27	26-Mar-27	19
TESTING & COMMISSIONING		96	10-Feb-27	02-Jul-27	5
CLOS-1150	Building Envelope Testing	6	10-Feb-27	19-Feb-27	49
CLOS-1130	Commissioning Kick-off Meeting	6	24-Mar-27	31-Mar-27	53
CLOS-1010	Commissioning Fire Water Pump	5	01-Apr-27	08-Apr-27	53
CLOS-1005	Electrical Commissioning	6	13-May-27	20-May-27	34
CLOS-1035	Preliminary Fire Alarm Testing to Request TCO	5	17-May-27	21-May-27	19
CLOS-1025	HVAC Balancing	5	11-Jun-27	18-Jun-27	5
CLOS-1020	Low Voltage System Commissioning	6	11-Jun-27	21-Jun-27	14

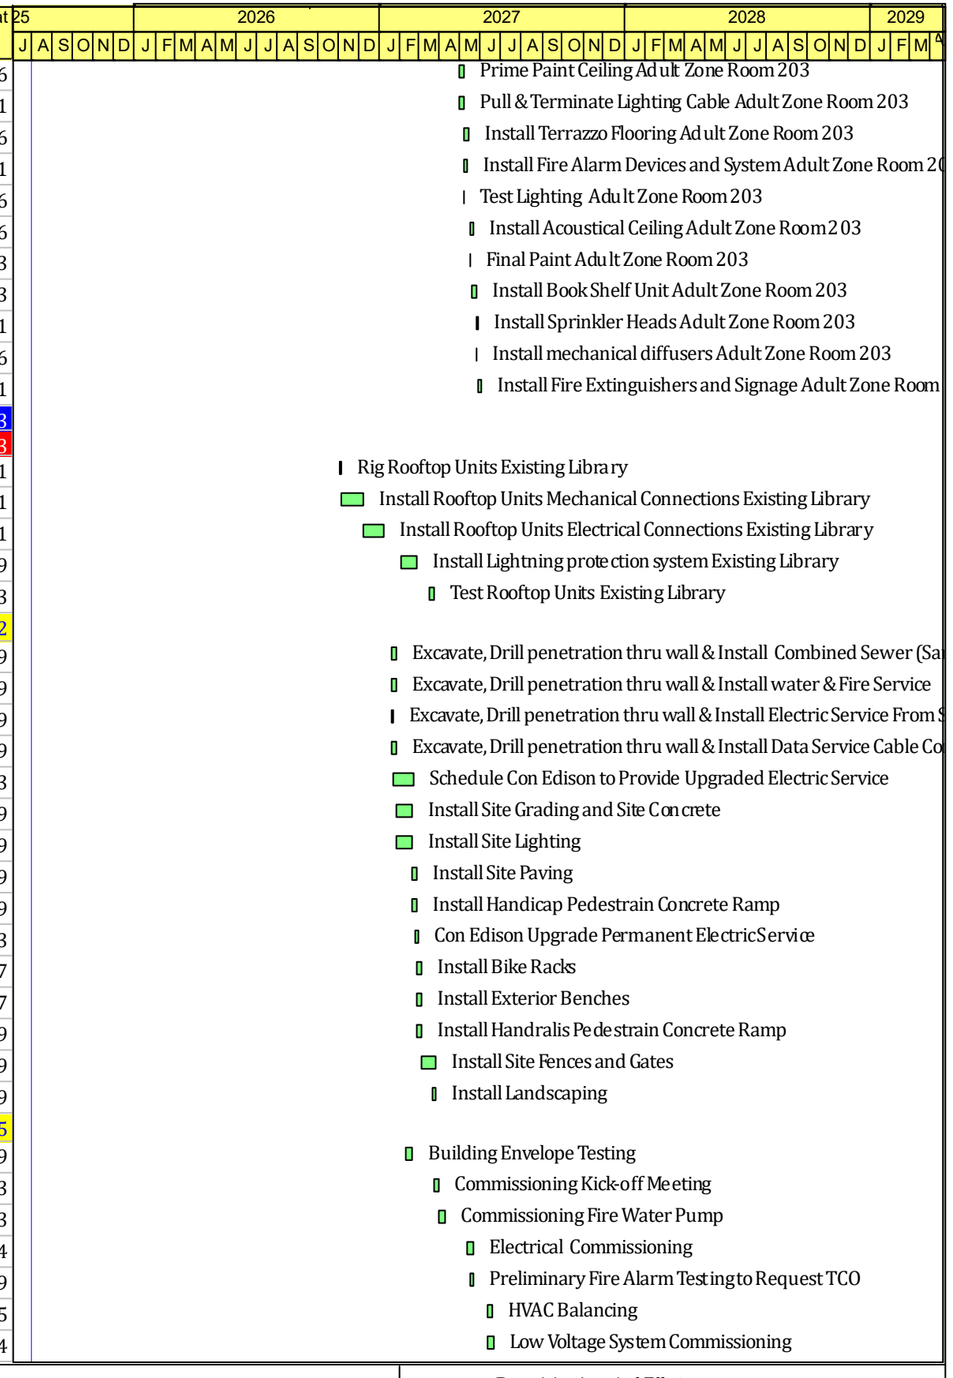

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
CLOS-1030	HVAC Commissioning	10	21-Jun-27	02-Jul-27	5
CLOSEOUT		251	04-Nov-26	20-Oct-27	0
INSPECTIONS & SIGN-OFFS		41	21-May-27	22-Jul-27	0
CLOS-1100	EC A433 Sign-off Milestone	0		21-May-27	23
CLOS-1045	Request Substantial completion	1	25-May-27	25-May-27	32
CLOS-1080	EC Submit B45 to FDNY	1	25-May-27	25-May-27	19
CLOS-1090	Request FDNY Pre-Inspection	3	26-May-27	28-May-27	19
CLOS-1040	FDNY Inspection for TCO	10	31-May-27	11-Jun-27	19
CLOS-1050	TCO Walk-through for Substantial Completion	1	14-Jun-27	14-Jun-27	20
CLOS-1140	DOB Inspection for Substantial Completion	2	05-Jul-27	06-Jul-27	5
CLOS-1120	Issue Temporary Certificate Occupyancy	1	07-Jul-27	07-Jul-27	5
CLOS-1055	Punch list to satisfy Substantial Completion being Granted	2	21-Jul-27	22-Jul-27	0
CLOSEOUT DOCUMENTATION		148	29-Mar-27	20-Oct-27	0
CLOSEOUT DOCUMENTATION FOR SUBSTANTIAL		74	29-Mar-27	14-Jul-27	5
CLOS-1060	Provide Post-construction Close-out Documentation Warranties	60	29-Mar-27	24-Jun-27	19
CLOS-1065	Provide Post-construction Close-out Documentation O & M Manuals	60	29-Mar-27	24-Jun-27	19
CLOS-1070	Post-construction Close-out Perform Training	5	08-Jul-27	14-Jul-27	5
CLOSEOUT DOCUMENTATION FOR FINAL		90	23-Jul-27	20-Oct-27	0
CLOS-1160	Final Inspection and review of Closeout Documentation for Final Completion	45	23-Jul-27	05-Sep-27	0
CLOS-1170	Incorporate any Changes & Submit Final Closeout Documentation for Final Completion	45	06-Sep-27	20-Oct-27	0
019500 - ASBUILTS		145	04-Nov-26	10-Jun-27	28
BIM MODEL - CELLAR LEVEL		101	04-Nov-26	06-Apr-27	72
BIM-1085	Prepare HVAC As-built Model - Cellar level	20	04-Nov-26	04-Dec-26	73
BIM-1075	Prepare Plumbing As-built Model - Cellar level	20	08-Dec-26	06-Jan-27	72
BIM-1095	Prepare fire protection As-built Model - Cellar level	20	07-Jan-27	04-Feb-27	72
BIM-1115	Prepare electrical As-built Model - Cellar level	20	05-Feb-27	08-Mar-27	72
BIM-1105	Prepare electronic safety and security work Asbuilt Model - Cellar level	20	09-Mar-27	06-Apr-27	72
BIM MODEL - FIRST LEVEL		100	30-Nov-26	27-Apr-27	58
BIM-1050	Prepare HVAC As-built Model - 1st level	20	30-Nov-26	28-Dec-26	58
BIM-1055	Prepare Plumbing As-built Model - 1st level	20	29-Dec-26	27-Jan-27	58
BIM-1025	Prepare fire protection As-built Model - 1st level	20	28-Jan-27	26-Feb-27	58
BIM-1045	Prepare electrical As-built Model - 1st level	20	01-Mar-27	29-Mar-27	58
BIM-1065	Prepare electronic safety and security work Asbuilt Model - 1st level	20	30-Mar-27	27-Apr-27	58
BIM MODEL - SECOND LEVEL		100	21-Dec-26	19-May-27	43
BIM-1035	Prepare HVAC As-built Model - 2nd level	20	21-Dec-26	20-Jan-27	43
BIM-1040	Prepare Plumbing As-built Model - 2nd level	20	21-Jan-27	19-Feb-27	43
BIM-1015	Prepare fire protection As-built Model- 2nd level	20	22-Feb-27	22-Mar-27	43
BIM-1000	Prepare electrical As-built Model - 2nd level	20	23-Mar-27	20-Apr-27	43
BIM-1060	Prepare electronic safety and security work As-built Model - 2nd level	20	21-Apr-27	19-May-27	43
BIM MODEL - THIRD LEVEL		100	13-Jan-27	10-Jun-27	28
BIM-1135	Prepare HVAC As-built Model - 3rd level	20	13-Jan-27	10-Feb-27	28
BIM-1125	Prepare Plumbing As-built Model - 3rd level	20	12-Feb-27	15-Mar-27	28



Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
BIM-1145	Prepare fire protection As-built Model- 3rd level	20	16-Mar-27	13-Apr-27	28
BIM-1155	Prepare electrical As-built Model - 3rd level	20	14-Apr-27	11-May-27	28
BIM-1165	Prepare electronic safety and security work As-built Model - 3rd level	20	13-May-27	10-Jun-27	28
BIM MODEL - ROOF LEVEL		100	08-Jan-27	07-Jun-27	31
BIM-1030	Prepare HVAC As-built Model - roof level	20	08-Jan-27	05-Feb-27	31
BIM-1010	Prepare Plumbing As-built Model - roof level	20	08-Feb-27	09-Mar-27	31
BIM-1020	Prepare fire protection As-built Model Roof level	20	10-Mar-27	08-Apr-27	31
BIM-1005	Prepare electrical As-built Model - roof level	20	09-Apr-27	06-May-27	31
BIM-1175	Prepare electronic safety and security work As-built Model - roof level	20	07-May-27	07-Jun-27	31

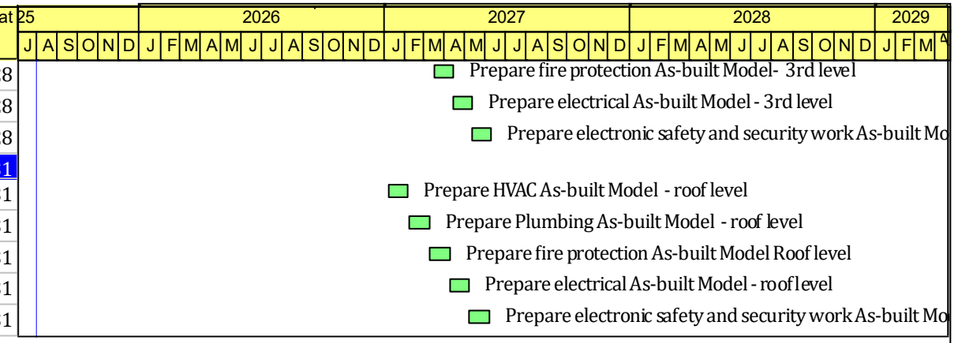

Eastern Parkway Library-Renovation and Expansion - Rev.1
Activity Details

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
