

IS 082K New Building

Design No. 093937

Baseline schedule Rev 00

TECHNICO Construction.

TECHNICO CONSTRUCTION PROJECS ENGINEERING CONSULTING SERVICES

TABLE OF CONTENTS

1. *PROJECT DESCRIPTION* 2
2. SCHEDULE METHODOLOGY 2
3. PROJECT DATA 2
4. ACTIVITIES ID STRUCTURE 2
5. WORK BREAKDOWN STRUCTURE 3
6. PROJECT STATISTICS AND INFORMATION 3
7. MILESTONES 4
8. STRATEGY OF WORK 4
9. LONGEST PATH 4
10. ONE MONTH LOOK-AHEAD 4
11. APPENDICES 5

1. *Project Description*

The work under this contract includes the construction of a new 4-story intermediate school with a partial cellar located on Block 5741, Lot 5 in Brooklyn. The school will accommodate 461 students and includes a program of requirements (POR) featuring 15 classrooms for grades 6-8, a speech room, a reading resource room, two CSD classrooms, and various specialized instruction spaces such as art, music, library, exercise room, and science lab/demonstration rooms. Additional facilities include student dining with a commercial kitchen, a gymatorium with a P.E. office and storage, male and female locker rooms, administration and guidance suites, a custodian office, school safety areas, storage, and other support spaces. All filing documents comply with the 2022 NYC Building Code, NYCSCA design standards, and other applicable regulatory requirements.

2. Schedule Methodology

This Schedule serves as the Project Baseline Schedule Rev 00. Primavera P6 was utilized as scheduling software. Schedule was utilized by developing the Critical Path Method (CPM). Durations were based on contractor best practice productivity from previous projects by week starting on Monday and grouping by trades and levels shown below in paragraph 6 WBS. All other schedule settings required in the Specifications is used while implementing the baseline.

3. Project Data

Contract NTP	December 2nd,2024
Project Duration (From NTP till TCO)	730 CDs
Contractual TCO	December 1st,2026
Contractual Substantial Completion	March 1st,2027
Contractual Final Completion	June 29th,2027

4. Activities ID Structure

Each activity has a unique ID and description based on letters and numbering criteria. The table below modifies the IDs applied to theactivities:

Reference	Prefix	-	Suffix	Increment value
ID	AAA	Separator	0000	10

A=Alphabets
0=Number

4.1 Prefix

The below table is showing the three letters structure for the ID Prefix. Those letters were based on the scope, WBS, or activity type.

ID	Prefix
MIL	Key dates & milestones
SUB	Submittals
APP	Approvals
PER	Permits
PRO	Procurements
CON	Construction

COR	Coordination
CLO	Close out

4.2 Suffix

It consists of four-digit numbers starting with value of 1000.

4.3 Increment value`

It works as a counter for project activities with increment value of 10.

5. Work Breakdown Structure

The Project WBS was broken down into the presented levels below:

Preconstruction:

This level contains Project Key dates and Milestones, including the NTP and project completion dates.

Procurement:

This level consists of different contractor's Submittals followed by Review/Approvals, as well as the fabrication, procurement and delivery of all item included in the project.

Construction:

This level consists of all the construction work under the scope of this project.

Close-Out:

This level consists of the close out activities including final inspection, punch list, final clean-up & demobilization.

Please refer to Appendix 1.

6. Project Statistics and Information

6.1 Schedule Summary and Log

Scheduling	Yes
Levelling	No
Ignore relationships to and from other projects	No
Make open-ended activities critical	No
cUse Expected Finish Dates	Yes
Schedule automatically when a change affects dates	No
Level resources during scheduling	No
Recalculate assignment costs after scheduling	No
When scheduling progressed activities use	Retained Logic
Calculate start-to-start lag from	Early Start
Define critical activities as Total Float	Longest Path
Compute Total Float As	Finish Float
Calculate float based on finish date of	Each project
Calendar for scheduling Relationship Lag	Predecessor Activity Calendar

6.2 Schedule Statistics

Activities	797
Not Started	797
In Progress	0
Completed	0
Relationships	1385

6.3 Open Ends Activities

Activity ID	Activity Description	Open end Type
MIL-1000	NTP	No Predecessor
MIL-1050	Final Completion	No Successor

6.4 List of Main Constraints

Activity ID	Activity Name	Constraint Date

MIL-1060	IDF and MDF Rooms Ready	03-Sep-26*
MIL-1070	IPDVS System Installed	02-Nov-26*
MIL-1030	TCO	01-Dec-26*
MIL-1040	Substantial Completion	01-Mar-27*
MIL-1050	Final Completion	29-Jun-27*

6.5 Calendars

IS82 - 5 Working Days Calendar	Default 5 Working Days* calendar with weekends and legal holidays.
IS82 - 7 Days Calendar	7 Days calendar is assigned to approvals and curing activities

*Working Hours: 8hrs/day

7. Milestones

Activity ID	Activity Name	Start	Finish
MIL-1000	NTP	2-Dec-24	-
MIL-1010	Project Duration (From NTP till TCO) = 730 CDs	2-Dec-24	1-Dec-26
MIL-1020	Building Tight	-	5-Mar-26
MIL-1060	IDF and MDF Rooms Ready	-	03-Sep-26*
MIL-1070	IPDVS System Installed	-	02-Nov-26*
MIL-1030	TCO	-	01-Dec-26*
MIL-1040	Substantial Completion	-	01-Mar-27*
MIL-1050	Final Completion	-	29-Jun-27*

8. Strategy of Work

The project includes 2 phases:

- Phase 1 shall be completed within 730 calendar days from NTP and it starts with obtaining the required permits followed by the foundation work then structural work. Material hoist will be installed during the construction. After the structural work is completed the roofing and elevations will start concurrently and also the building rough-ins will start, the sequence of rough-ins will be HVAC then Electrical followed by plumbing then fire protection rough-ins.
  After the Architectural work is completed the pre-TCO inspection will take place then punch list followed by obtaining the TCO.

- Phase 2 shall be completed within 210 calendar days after phase 1 and it contains pre-substantial completion punch list and then substantial completion followed by final inspections and final completion.

9. Longest path

The longest path commences with site access restrictions, followed by mobilization and foundation work. Subsequently, structural slabs and columns are constructed, leading to roofing work to establish a building tight environment. Once the mock-up classroom is approved, architectural finishes are performed, leading to project closeouts. Please refer to Appendix # 4.

10. One Month Look-ahead

One-month look-ahead performance includes preconstruction submittals and obtaining permits.

Please refer to Appendix # 6.

11. Appendices

APPENDIX 1 – WBS Layout

APPENDIX 2 – Full Schedule Grouped by WBS

APPENDIX 3 – Full Schedule Grouped by Trades

APPENDIX 4 – Longest Path Layout

APPENDIX 5 – One Month Look-ahead

APPENDIX 6 – Activity Report

APPENDIX 7 – Total Float Report

APPENDIX 8 – Schedule Log

APPENDIX 1 –
WBS Layout

Activity ID	Activity Name

IS 082K New Building Design No. 093937 - Baseline Schedule Rev 00

Pre-construction

Milestones

Major Milestones

Utilities Coordination

Temporary Electrical Power

Permits

Procurement

Submittals & Approvals

Division 01 - General Requirements

- Spec Section S01300 - Submittals
- Spec Section S01311 - Progress Schedule
- Spec Section S01400 - Quality Control
- Spec Section S01426 - Sample Classroom
- Spec Section S01500 - Temporary Facilities and Controls
- Spec Section S01524 - Construction Waste Management
- Spec Section S01535 - Safety Program
- Spec Section S01550 - Indoor Air Quality (IAQ) Requirements
- Spec Section S01720 - Record Documents

Division 02 - Site Work

- Spec Section 02010 - Environmental Site Assessment Reports
- Spec Section 02070 - Selective Removals & Demoloition
- Spec Section 02100 - Site Preparation
- Spec Section 02200 - Earthwork
- Spec Section 02220 - Gas Vapor Barrier (Fluid Applied)
- Spec Section 02221 - Sub-Slab Depressurization System
- Spec Section 02250 - Foundation & Other Change Adjustements
- Spec Section 02511 - Asphaltic Concrete Paving
- Spec Section 02513 - Sidewalk and Street Paving
- Spec Section 02722 - PC Basins, Detention Basins, and Manholes
- Spec Section 02723 - Storm Drainage Systems
- Spec Section 02831 - Chain Link Fences & Gates
- Spec Section 02870 - Site & Street Furnishings
- Spec Section 02900 - Landscaping

Division 03 - Concrete

- Spec Section 03100 - Concrete Formwork
- Spec Section 03200 - Concrete Reinforcement
- Spec Section 03300 - Cast in Place Concrete
- Spec Section 03542 - Cement Based Self Leveling Underlayment

Division 04 - Masonry

- Spec Section 04200 - Unit Masonry

Division 05 - Metals

- Spec Section 05120 - Structural Steel
- Spec Section 05170 - Support System for Suspended Ceilings
- Spec Section 05300 - Metal Deck
- Spec Section 05500 - Metal Fabrications

Division 06 - Wood & Plastics

- Spec Section 06200 - Finish Carpentry
- Spec Section 06410 - Custom Casework

Division 07 - Thermal & Moisture Protection

- Spec Section 07147 - Crystalline Waterproofing
- Spec Section 07211 - Perimeter Foundation Insulation
- Spec Section 07600 - Flashing and Sheet Metal
- Spec Section 07720 - Roof Accessories

Division 08 - Doors & Windows

Activity ID	Activity Name
	Spec Section 08110 - Steel Doors and Frames
	Spec Section 08210 - Wood Doors
	Spec Section 08525 - High Performance Aluminum Projected Windows
	Spec Section 08662 - Security Screens & Barriers
	Spec Section 08710 - Finish Hardware
	Division 09 - Finishes
	Spec Section 09260 - Gypsum Board Assemblies
	Spec Section 09310 - Ceramic Tiles
	Spec Section 09510 - Acoustical Ceilings
	Spec Section 09590 - Wood Flooring
	Spec Section 09650 - Resilient Flooring
	Spec Section 09900 - Painting
	Division 10 - Specialties
	Spec Section 10100 - Visual Display Boards
	Spec Section 10400 - Identification Devices
	Spec Section 10522 - Fire Extinguishers & Cabinets
	Spec Section 10720 - Window Guards
	Spec Section 10810 - Toilet & Bath Accessories
	Division 11 - Equipment
	Spec Section 11061 - Platform Curtains & Auditorium Window Curtains
	Spec Section 11400 - Food Service Equipment
	Spec Section 11450 - Domestic Type Equipment
	Spec Section 11480 - Gymnasium Equipment
	Division 12 - Furnishings
	Spec Section 12302 - Manufactured Wood Casework
	Division 14 - Conveying Systems
	Spec Section 14212 - Gearless Traction Passenger Elevators
	Spec Section 14420 - Hydraulic Vertical Wheelchair Lifts
	Division 15 - Mechanical
	Division 15A - Fire Protection
	Spec Section 15333 - Fire Pumps - Sprinkler Booster Pumps
	Division 15B - Plumbing & Drainage
	Spec Section 15410 - Plumbing Piping
	Spec Section 15411 - Hangers and Supports
	Spec Section 15415 - Drainage
	Spec Section 15417 - Cold Water Supply
	Spec Section 15418 - Hot Water Supply
	Spec Section 15440 - Plumbing Fixtures
	Spec Section 15453 - Pumping Apparatus & Tanks
	Division 15C - Heating & Ventilation & Air Conditioning
	Spec Section 15510 - HVAC Piping
	Spec Section 15783 - Split Heat Pump System
	Spec Section 15836 - Unit Heaters Cabinet Heaters
	Spec Section 15891 - Metal Ductwork
	Spec Section 15590 - Emergency Generator System Accessories
	Spec Section 15836 - Unit Heaters/Cabinet Heaters
	Spec Section 15940 - Air Outlets & Inlets
	Spec Section 15970 - Temperature Control System
	Division 16 - Electrical
	Spec Section 16010 - Gen Provisions for Elec Work
	Spec Section 16120 - Wiring Systems
	Spec Section 16502 - Interior Lighting Fixtures
	Spec Section 16520 - Illuminated Exit Sign
	Spec Section 16720 - Fire Detection Alarm System with COC
	Spec Section 16785 - Internet Protocol Digital Video Surveillance System using Digital Cameras
	Spec Section 16425 - Switch Boards & Panel Boards

Activity ID	Activity Name
	Spec Section 16475 - Overcurrent Protective Devices
	Fabrication & Delivery
	Construction
	Site Preparation
	Cellar Floor
	SSDS - Cellar Floor
	Structure - Cellar Floor
	Mechanical- Cellar Floor
	HVAC Rough-ins-1st Floor
	Mechanical Equipment-1st Floor
	Plumbing-Cellar Floor
	Fire Protection-Cellar Floor
	Electrical-Cellar Floor
	Architecture-Cellar Floor
	Interior Walls-1st Floor
	Ceiling-1st Floor
	Finishes-1st Floor
	First Floor
	SSDS - 1st Floor
	Structure-1st Floor
	Mechanical- 1st Floor
	HVAC Rough-ins-1st Floor
	Mechanical Equipment-1st Floor
	Plumbing-1st Floor
	Fire Protection-1st Floor
	Electrical-1st Floor
	Architecture-1st Floor
	Interior Walls-1st Floor
	Ceiling-1st Floor
	Finishes-1st Floor
	Second Floor
	Structure-2nd Floor
	Mechanical-2nd Floor
	HVAC Rough-ins-2nd Floor
	Mechanical Equipment-2nd Floor
	Plumbing-2nd Floor
	Electrical-2nd Floor
	Fire Protection-2nd Floor
	Architecture-2nd Floor
	Interior Walls-2nd Floor
	Ceiling-2nd Floor
	Finishes-2nd Floor
	Third Floor
	Material Hoist
	Structure -3rd Floor
	Mechanical -3rd Floor
	HVAC Rough-ins -3rd Floor
	Mechanical Equipment -3rd Floor
	Plumbing -3rd Floor
	Electrical -3rd Floor
	Fire Protection -3rd Floor
	Architecture -3rd Floor
	Interior Walls -3rd Floor
	Ceiling -3rd Floor
	Finishes -3rd Floor

WBS Layout

Activity ID	Activity Name

- Fourth Floor
  - Structure -4th Floor
  - Mechanical-4th Floor
    - HVAC Rough-ins-4th Floor
    - Mechanical Equipment-4th Floor
  - Plumbing-4th Floor
  - Electrical-4th Floor
  - Fire Protection-4th Floor
  - Architecture-4th Floor
    - Interior Walls-4th Floor
    - Ceiling-4th Floor
    - Finishes-4th Floor
- Lower Roof
  - Structure -Lower Floor
  - Mechanical -Lower Floor
    - HVAC Rough-ins -Lower Floor
    - Mechanical Equipment -Lower Floor
  - Plumbing -Lower Floor
  - Electrical -Lower Floor
  - Fire Protection -Lower Floor
  - Architecture -Lower Floor
    - Interior Walls -Lower Floor
    - Ceiling -Lower Floor
    - Finishes -Lower Floor
- Upper Roof
  - Structure -Roof Floor
  - Mechanical-Roof Floor
- Bulkhead
  - Structure-Bulkhead
- Elevations
  - West Elevation
  - South Elevation
  - East Elevation
  - North Elevation
- Roofing
  - Lower Roof
  - Upper Roof
- Special Rooms
  - Electrical Service Room -Cellar Floor
  - Fuel TankRoom-Cellar Floor
  - Water Meter Room - Cellar
  - Elevator Machine Room -Lower Roof
  - MDF Room 2nd Floor
  - Gymnatorium - 4th Floor
  - R01 - HVAC/ELEC. Penthouse - Lower Roof
  - Food Service Room - 1st
  - IDF Room - 4th Floor
- Mockup Room
- Site Work
  - 14th Avenue Street
  - 63RD Street
  - Building Perimeter


Close-out

- Testing & Commissioning
- Demobilization

APPENDIX 2
– Full Schedule
Grouped by WBS

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
IS 082K New Building Design No. 093937 - Baseline Schedule Rev 00		644	02-Dec-24	29-Jun-27
Pre-construction		644	02-Dec-24	29-Jun-27
Milestones		644	02-Dec-24	29-Jun-27
Major Milestones		644	02-Dec-24	29-Jun-27
PER-1120	No Site Access	180	02-Dec-24	30-May-25
MIL-1000	NTP	0	02-Dec-24	
MIL-1010	Project Duration (From NTP till TCO) = 730 CDs	730	02-Dec-24	01-Dec-26
CON-1000	Mobilization	5	02-Jun-25	06-Jun-25
MIL-1020	Building Tight	0		05-Mar-26
MIL-1060	IDF and MDF Rooms Ready	0		03-Sep-2(
MIL-1070	IPDVS System Installed	0		02-Nov-2(
MIL-1030	TCO	0		01-Dec-2(
MIL-1040	Substantial Completion	0		01-Mar-27*
MIL-1050	Final Completion	0		29-Jun-27*
Utilities Coordination		274	01-Apr-25	04-May-26
Temporary Electrical Power		274	01-Apr-25	04-May-26
COR-1000	Coordination With CON-ED For Temporary Electrical Power	10	01-Apr-25	14-Apr-25
COR-1010	Scheduling With CON-ED For Temporary Electrical Power	7	15-Apr-25	23-Apr-25
COR-1020	Procurement From CON-ED For Temporary Electrical Power	20	24-Apr-25	13-May-25
COR-1030	CON-ED Work For Temporary Electrical Power	10	14-May-25	28-May-25
COR-1040	Available Temporary Electrical Power For Testing MEP Equipment	0		28-May-25
COR-1050	Coordination With CON-ED For Trasnformers Work	10	21-Nov-25	05-Dec-25
COR-1060	CON-ED to Provide (1) 27KV Feeder To Transformer Vault	30	06-Dec-25	04-Jan-26
COR-1070	CON-ED to Furnish & Deliver (1) New 'V11-6 Transformer Vault	120	05-Jan-26	04-May-26
Permits		43	01-Apr-25	30-May-25
PER-1000	Obtain Construction Fences Permit	3	01-Apr-25	03-Apr-25
PER-1010	Obtain CCD1	3	01-Apr-25	03-Apr-25
PER-1020	Obtain Sidewalk Shed Permits	3	01-Apr-25	03-Apr-25
PER-1030	Meeting With SCA to Review The Permit Requirements	14	01-Apr-25	18-Apr-25
PER-1040	Prepare & Submit Permit Waiver Requests to SCA Chief Project Officer	5	01-Apr-25	07-Apr-25
PER-1050	Prepare & Submit FDNY Fuel Permit	10	01-Apr-25	14-Apr-25
PER-1060	Obtain Builders Pavement Permit	10	01-Apr-25	14-Apr-25
PER-1070	Obtain Excavation Permit	15	01-Apr-25	21-Apr-25
PER-1080	Obtain Permit to Enter (PTE)	10	01-Apr-25	14-Apr-25
PER-1090	Review & Approve FDNY Fuel Permit	21	15-Apr-25	05-May-25
PER-1100	DOB Permit & Insurance	21	01-May-25	30-May-25
PER-1110	SCA Work Notification	7	21-May-25	30-May-25
Procurement		497	02-Dec-24	25-Nov-26
Submittals & Approvals		497	02-Dec-24	25-Nov-26
Division 01 - General Requirements		497	02-Dec-24	25-Nov-26
Spec Section S01300 - Submittals		101	02-Dec-24	25-Apr-25
SUB-1640	Prepare & Submit Underground Coordination Drawings	50	02-Dec-24	12-Feb-25
SUB-1650	Prepare & Submit 1st Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25
SUB-1660	Prepare & Submit 2nd Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25
SUB-1670	Prepare & Submit 3rd Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25
SUB-1680	Prepare & Submit 4th Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25
SUB-1690	Prepare & Submit 5th Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25
APP-1200	Review & Approve Underground Coordination Drawings	21	13-Feb-25	05-Mar-25

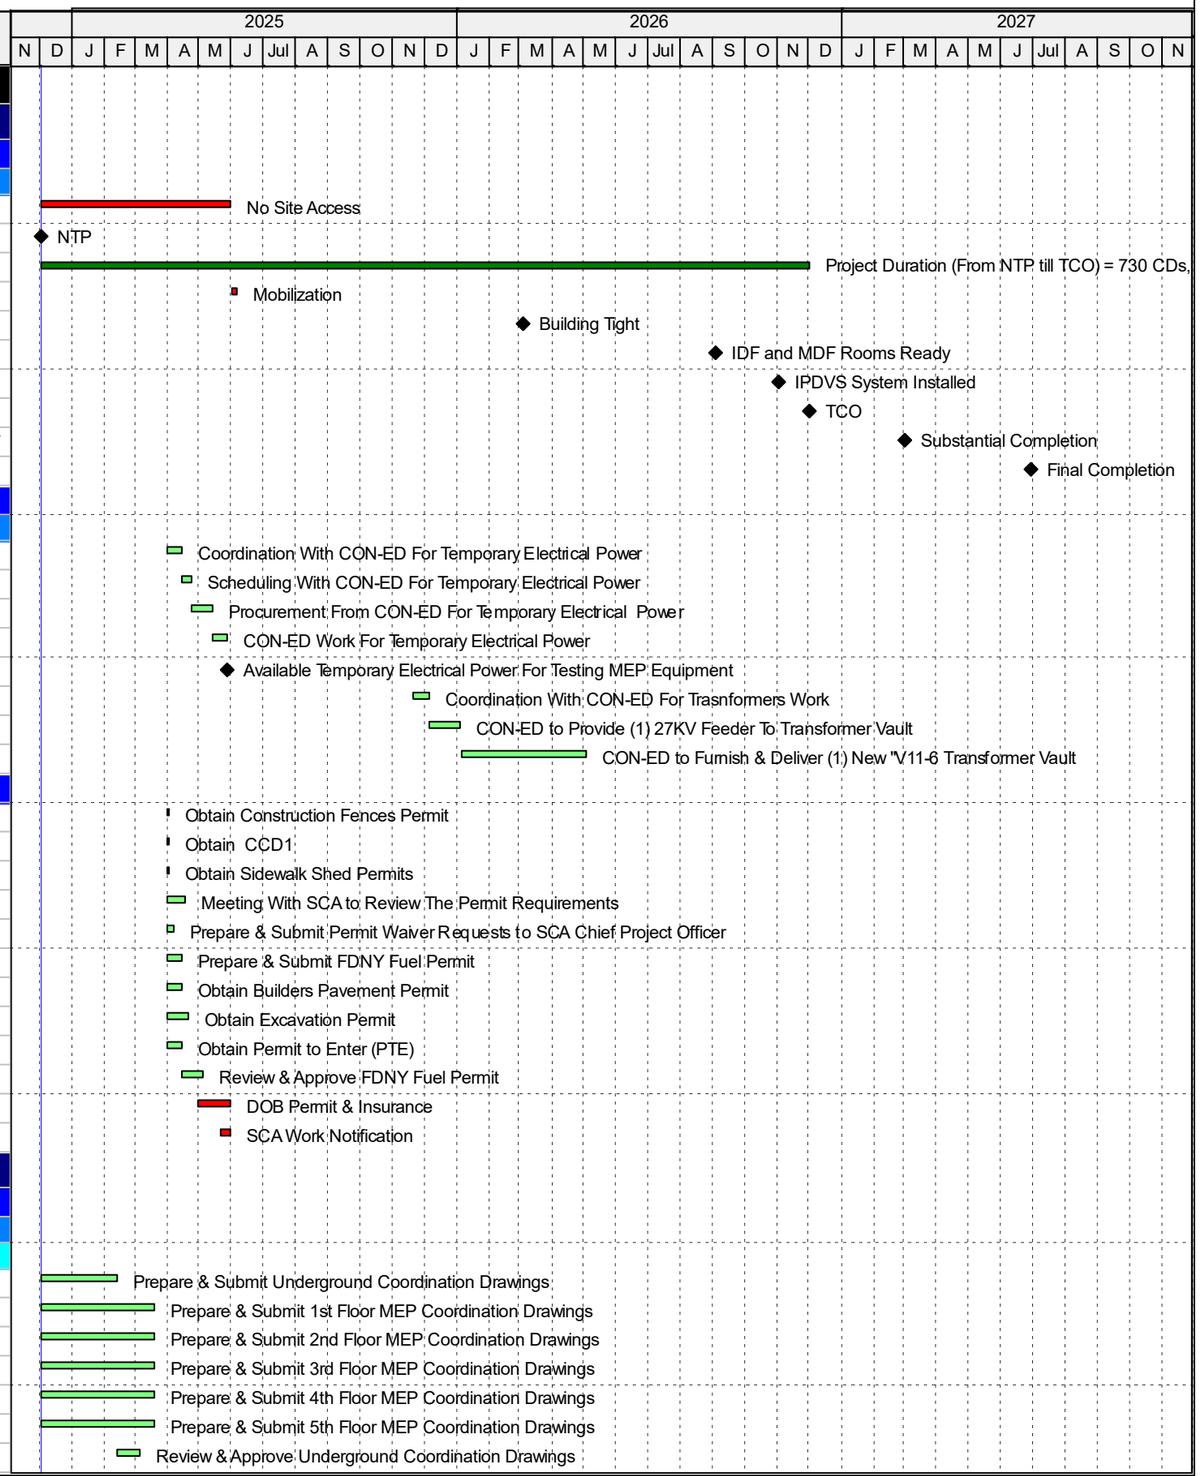

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

IS 082K New Building Design No. 093937 - Baseline Schedule Rev 00


TECHNICO CONSTRUCTION PROJECTS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1930	Prepare & Submit Final Underground Coordination Drawings	37	06-Mar-25	25-Apr-25
APP-1280	Review & Approve 1st Floor Coordination Drawings	21	21-Mar-25	10-Apr-25
APP-1290	Review & Approve 2nd Floor Coordination Drawings	21	21-Mar-25	10-Apr-25
APP-1300	Review & Approve 3rd Floor Coordination Drawings	21	21-Mar-25	10-Apr-25
APP-1310	Review & Approve 4th Floor Coordination Drawings	21	21-Mar-25	10-Apr-25
APP-1320	Review & Approve 5th Floor Coordination Drawings	21	21-Mar-25	10-Apr-25
Spec Section S01311 - Progress Schedule		66	02-Dec-24	07-Mar-25
SUB-1510	Prepare & Submit Baseline Schedule	52	02-Dec-24	14-Feb-25
APP-1210	Review & Approve Baseline Schedule	21	15-Feb-25	07-Mar-25
Spec Section S01400 - Quality Control		44	02-Dec-24	04-Feb-25
SUB-1470	Prepare & Submit QCP	30	02-Dec-24	14-Jan-25
APP-1100	Review & Approve QCP	21	15-Jan-25	04-Feb-25
Spec Section S01426 - Sample Classroom		96	02-Dec-24	18-Apr-25
SUB-1320	Prepare & Submit Sample Classroom Materials	81	02-Dec-24	28-Mar-25
APP-1540	Review & Approve Sample Classroom Materials	21	29-Mar-25	18-Apr-25
Spec Section S01500 - Temporary Facilities and Controls		96	02-Dec-24	18-Apr-25
SUB-1310	Prepare & Submit Heating Plan	81	02-Dec-24	28-Mar-25
APP-1530	Review & Approve Heating Plan	21	29-Mar-25	18-Apr-25
Spec Section S01524 - Construction Waste Management		96	02-Dec-24	18-Apr-25
SUB-1300	Prepare & Submit CWM Plan	81	02-Dec-24	28-Mar-25
APP-1520	Review & Approve CWM Plan	21	29-Mar-25	18-Apr-25
Spec Section S01535 - Safety Program		17	02-Dec-24	24-Dec-24
SUB-1290	Prepare & Submit Site Safety Plan	2	02-Dec-24	03-Dec-24
APP-1000	Review & Approve Site Safety Plan	21	04-Dec-24	24-Dec-24
Spec Section S01550 - Indoor Air Quality (IAQ) Requirements		96	02-Dec-24	18-Apr-25
SUB-1280	Prepare & Submit Construction Indoor Air Quality Management Plan	81	02-Dec-24	28-Mar-25
APP-1510	Review & Approve Construction Indoor Air Quality Management Plan	21	29-Mar-25	18-Apr-25
Spec Section S01720 - Record Documents		95	13-Jul-26	25-Nov-26
SUB-1960	Prepare & Submit Record Documents	81	13-Jul-26	04-Nov-26
APP-1930	Review & Approve Record Documents	21	05-Nov-26	25-Nov-26
Division 02 - Site Work		96	02-Dec-24	18-Apr-25
Spec Section 02010 - Environmental Site Assessment Reports		96	02-Dec-24	18-Apr-25
SUB-1700	Prepare & Submit Environmental Site Assessment Reports	81	02-Dec-24	28-Mar-25
APP-1720	Review & Approve Environmental Site Assessment Reports	21	29-Mar-25	18-Apr-25
Spec Section 02070 - Selective Removals & Demoloition		96	02-Dec-24	18-Apr-25
SUB-1710	Prepare & Submit Selective Removals & Demoloition	81	02-Dec-24	28-Mar-25
APP-1730	Review & Approve Selective Removals & Demoloition	21	29-Mar-25	18-Apr-25
Spec Section 02100 - Site Preparation		23	02-Dec-24	03-Jan-25
SUB-1270	Prepare & Submit Existing Conditions Survey	10	02-Dec-24	13-Dec-24
APP-1030	Review & Approve Existing Conditions Survey	21	14-Dec-24	03-Jan-25
Spec Section 02200 - Earthwork		21	02-Dec-24	31-Dec-24
SUB-1460	Prepare & Submit Erosion Control and Sedimentation Plan	7	02-Dec-24	10-Dec-24
APP-1020	Review & Approve Erosion Control and Sedimentation Plan	21	11-Dec-24	31-Dec-24
Spec Section 02220 - Gas Vapor Barrier (Fluid Applied)		96	02-Dec-24	18-Apr-25
SUB-1260	Prepare & Submit Gas Vapor Barrier Submittal & Inspection Schedule	81	02-Dec-24	28-Mar-25
SUB-1950	Review & Approve Gas Vapor Barrier Submittal & Inspection Schedule	21	29-Mar-25	18-Apr-25
Spec Section 02221 - Sub-Slab Depressurization System		54	02-Dec-24	19-Feb-25
SUB-1250	Prepare & Submit SSDS Geotextile	40	02-Dec-24	29-Jan-25
APP-1170	Review & Approve SSDS Geotextile	21	30-Jan-25	19-Feb-25
Spec Section 02250 - Foundation & Other Change Adjustements		19	02-Dec-24	27-Dec-24

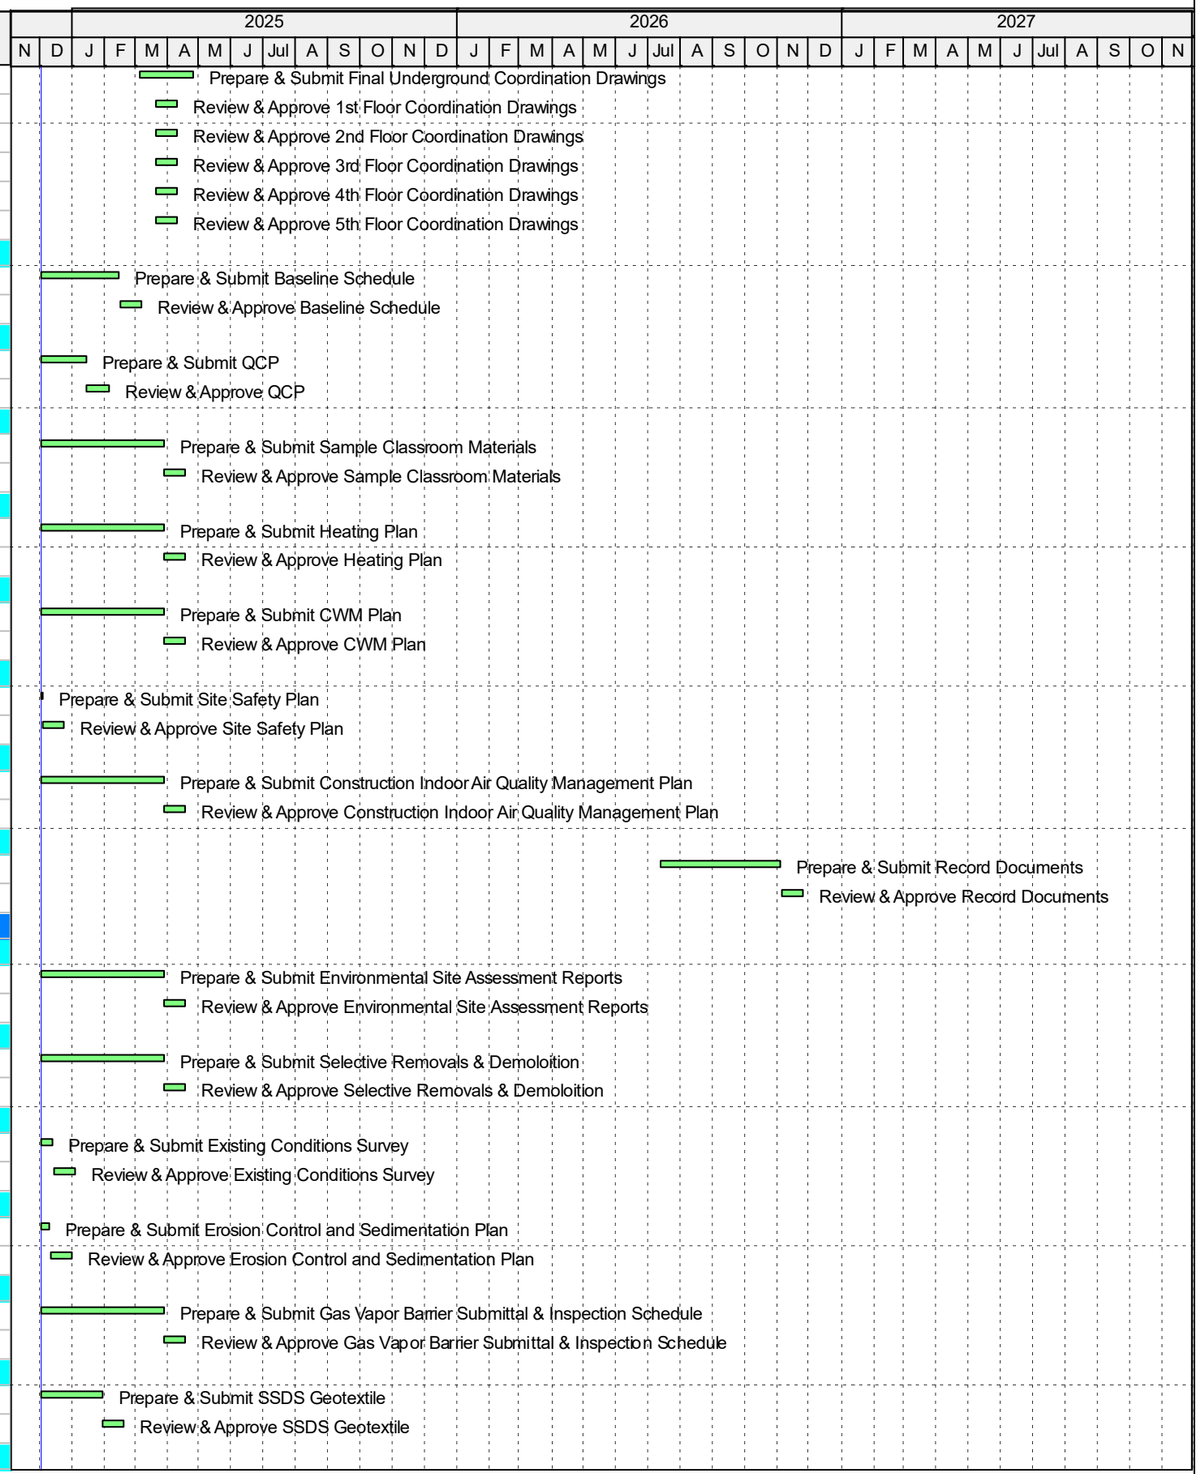

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone


TECHNICO CONSTRUCTION PROJECS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	


Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1720	Prepare & Submit Foundation Shop Drawings	5	02-Dec-24	06-Dec-24
APP-1010	Review & Approve Foundation Shop Drawings	21	07-Dec-24	27-Dec-24
Spec Section 02511 - Asphaltic Concrete Paving		96	02-Dec-24	18-Apr-25
SUB-1240	Prepare & Submit Asphaltic Concrete Paving	81	02-Dec-24	28-Mar-25
APP-1490	Review & Approve Asphaltic Concrete Paving	21	29-Mar-25	18-Apr-25
Spec Section 02513 - Sidewalk and Street Paving		96	02-Dec-24	18-Apr-25
SUB-1230	Prepare & Submit Steel Curb Facing Shop Drawing	81	02-Dec-24	28-Mar-25
APP-1480	Review & Approve Steel Curb Facing Shop Drawing	21	29-Mar-25	18-Apr-25
Spec Section 02722 - PC Basins, Detention Basins, and Manholes		96	02-Dec-24	18-Apr-25
SUB-1220	Prepare & Submit Catch Basin Shop Drawings	81	02-Dec-24	28-Mar-25
APP-1470	Review & Approve Catch Basin Shop Drawings	21	29-Mar-25	18-Apr-25
Spec Section 02723 - Storm Drainage Systems		52	02-Dec-24	14-Feb-25
SUB-1210	Prepare & Submit Ductile Iron Pipes	37	02-Dec-24	24-Jan-25
APP-1120	Review & Approve Ductile Iron Pipes	21	25-Jan-25	14-Feb-25
Spec Section 02831 - Chain Link Fences & Gates		96	02-Dec-24	18-Apr-25
SUB-1730	Prepare & Submit Chain Link Fences & Gates Drawings	81	02-Dec-24	28-Mar-25
APP-1740	Review & Approve Chain Link Fences & Gates Drawings	21	29-Mar-25	18-Apr-25
Spec Section 02870 - Site & Street Furnishings		28	02-Dec-24	10-Jan-25
SUB-1200	Prepare & Submit Site Furnishings Shop Drawings	15	02-Dec-24	20-Dec-24
APP-1040	Review & Approve Site Furnishings Shop Drawings	21	21-Dec-24	10-Jan-25
Spec Section 02900 - Landscaping		96	02-Dec-24	18-Apr-25
SUB-1190	Prepare & Submit Planting Schedule	81	02-Dec-24	28-Mar-25
APP-1460	Review & Approve Planting Schedule	21	29-Mar-25	18-Apr-25
Division 03 - Concrete		96	02-Dec-24	18-Apr-25
Spec Section 03100 - Concrete Formwork		96	02-Dec-24	18-Apr-25
SUB-1180	Prepare & Submit Formwork Shop Drawings	81	02-Dec-24	28-Mar-25
APP-1450	Review & Approve Formwork Shop Drawings	21	29-Mar-25	18-Apr-25
Spec Section 03200 - Concrete Reinforcement		44	02-Dec-24	04-Feb-25
SUB-1170	Prepare & Submit Concrete Reinforcement	30	02-Dec-24	14-Jan-25
APP-1070	Review & Approve Concrete Reinforcement	21	15-Jan-25	04-Feb-25
Spec Section 03300 - Cast in Place Concrete		44	02-Dec-24	04-Feb-25
SUB-1350	Prepare & Submit Concrete Shop Drawings	30	02-Dec-24	14-Jan-25
SUB-1480	Prepare & Submit Concrete Mix Design	30	02-Dec-24	14-Jan-25
APP-1080	Review & Approve Concrete Shop Drawings	21	15-Jan-25	04-Feb-25
APP-1110	Review & Approve Concrete Mix Design	21	15-Jan-25	04-Feb-25
Spec Section 03542 - Cement Based Self Leveling Underlayment		96	02-Dec-24	18-Apr-25
SUB-1160	Prepare & Submit Certification of Material	81	02-Dec-24	28-Mar-25
APP-1440	Review & Approve Certification of Material	21	29-Mar-25	18-Apr-25
Division 04 - Masonry		96	02-Dec-24	18-Apr-25
Spec Section 04200 - Unit Masonry		96	02-Dec-24	18-Apr-25
SUB-1740	Prepare & Submit Unit Masonry Product Data	81	02-Dec-24	28-Mar-25
APP-1750	Review & Approve Unit Masonry Product Data	21	29-Mar-25	18-Apr-25
Division 05 - Metals		96	02-Dec-24	18-Apr-25
Spec Section 05120 - Structural Steel		96	02-Dec-24	18-Apr-25
SUB-1750	Prepare & Submit Structure Steel Drawings	81	02-Dec-24	28-Mar-25
APP-1760	Review & Approve Structure Steel Drawings	21	29-Mar-25	18-Apr-25
Spec Section 05170 - Support System for Suspended Ceilings		96	02-Dec-24	18-Apr-25
SUB-1150	Prepare & Submit Suspension Assembly Shop Drawings	81	02-Dec-24	28-Mar-25
APP-1430	Review & Approve Suspension Assembly Shop Drawings	21	29-Mar-25	18-Apr-25
Spec Section 05300 - Metal Deck		96	02-Dec-24	18-Apr-25

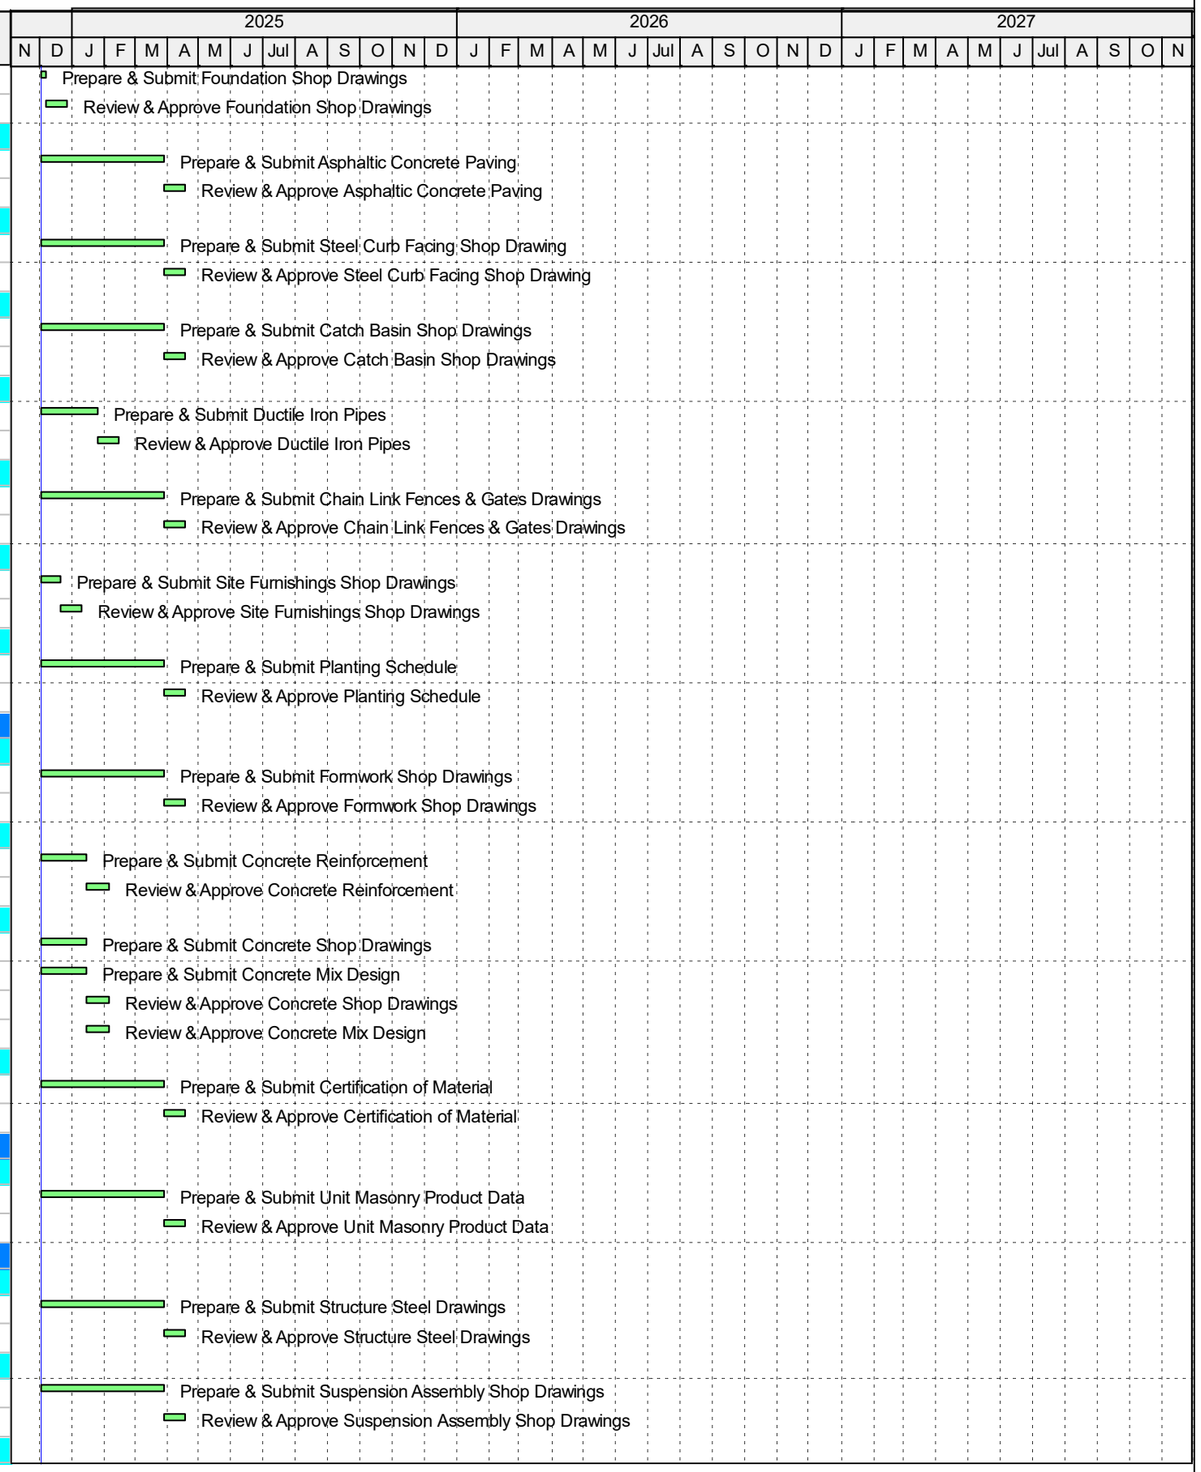

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1760	Prepare & Submit Metal Deck Product Data	81	02-Dec-24	28-Mar-25
APP-1770	Review & Approve Metal Deck Product Data	21	29-Mar-25	18-Apr-25
Spec Section 05500 - Metal Fabrications		96	02-Dec-24	18-Apr-25
SUB-1600	Prepare & Submit Roof Dunnage	81	02-Dec-24	28-Mar-25
APP-1700	Review & Approve Roof Dunnage	21	29-Mar-25	18-Apr-25
Division 06 - Wood & Plastics		96	02-Dec-24	18-Apr-25
Spec Section 06200 - Finish Carpentry		96	02-Dec-24	18-Apr-25
SUB-1430	Prepare & Submit Furniture	81	02-Dec-24	28-Mar-25
APP-1610	Review & Approve Furniture	21	29-Mar-25	18-Apr-25
Spec Section 06410 - Custom Casework		96	02-Dec-24	18-Apr-25
SUB-1410	Prepare & Submit Millwork	81	02-Dec-24	28-Mar-25
APP-1600	Review & Approve Millwork	21	29-Mar-25	18-Apr-25
Division 07 - Thermal & Moisture Protection		96	02-Dec-24	18-Apr-25
Spec Section 07147 - Crystalline Waterproofing		96	02-Dec-24	18-Apr-25
SUB-1140	Prepare & Submit Crystalline Waterproofing Product Data	81	02-Dec-24	28-Mar-25
APP-1420	Review & Approve Crystalline Waterproofing Product Data	21	29-Mar-25	18-Apr-25
Spec Section 07211 - Perimeter Foundation Insulation		96	02-Dec-24	18-Apr-25
SUB-1130	Prepare & Submit Perimeter Foundation Insulation Product Data	81	02-Dec-24	28-Mar-25
APP-1410	Review & Approve Perimeter Foundation Insulation Product Data	21	29-Mar-25	18-Apr-25
Spec Section 07600 - Flashing and Sheet Metal		96	02-Dec-24	18-Apr-25
SUB-1120	Prepare & Submit Flashing & Sheet Metal Shop Drawing	81	02-Dec-24	28-Mar-25
APP-1400	Review & Approve Flashing & Sheet Metal Shop Drawing	21	29-Mar-25	18-Apr-25
Spec Section 07720 - Roof Accessories		96	02-Dec-24	18-Apr-25
SUB-1110	Prepare & Submit Roof Drains & Clean Outs	81	02-Dec-24	28-Mar-25
APP-1390	Review & Approve Roof Drains & Clean Outs	21	29-Mar-25	18-Apr-25
Division 08 - Doors & Windows		96	02-Dec-24	18-Apr-25
Spec Section 08110 - Steel Doors and Frames		96	02-Dec-24	18-Apr-25
SUB-1100	Prepare & Submit Door & Frame Corners Samples	81	02-Dec-24	28-Mar-25
APP-1380	Review & Approve Door & Frame Corners Samples	21	29-Mar-25	18-Apr-25
Spec Section 08210 - Wood Doors		96	02-Dec-24	18-Apr-25
SUB-1520	Prepare & Submit Wood Doors	81	02-Dec-24	28-Mar-25
APP-1640	Review & Approve Wood Doors	21	29-Mar-25	18-Apr-25
Spec Section 08525 - High Performance Aluminum Projected Windows		88	02-Dec-24	08-Apr-25
SUB-1570	Prepare & Submit Windows	73	02-Dec-24	18-Mar-25
APP-1260	Review & Approve Windows	21	19-Mar-25	08-Apr-25
Spec Section 08662 - Security Screens & Barriers		96	02-Dec-24	18-Apr-25
SUB-1770	Prepare & Submit Security Screens & Barriers	81	02-Dec-24	28-Mar-25
APP-1780	Review & Approve Security Screens & Barriers	21	29-Mar-25	18-Apr-25
Spec Section 08710 - Finish Hardware		96	02-Dec-24	18-Apr-25
SUB-1080	Prepare & Submit Door Hardware Submittal	81	02-Dec-24	28-Mar-25
SUB-1940	Review & Approve Door Hardware Submittal	21	29-Mar-25	18-Apr-25
Division 09 - Finishes		96	02-Dec-24	18-Apr-25
Spec Section 09260 - Gypsum Board Assemblies		96	02-Dec-24	18-Apr-25
SUB-1370	Prepare & Submit Gypsum Board	81	02-Dec-24	28-Mar-25
APP-1570	Review & Approve Gypsum Board	21	29-Mar-25	18-Apr-25
Spec Section 09310 - Ceramic Tiles		96	02-Dec-24	18-Apr-25
SUB-1070	Prepare & Submit Ceramic Tiles Product Data	81	02-Dec-24	28-Mar-25
APP-1350	Review & Approve Ceramic Tiles Product Data	21	29-Mar-25	18-Apr-25
Spec Section 09510 - Acoustical Ceilings		75	02-Dec-24	20-Mar-25
SUB-1390	Prepare & Submit Acosutical Ceiling Tiles	60	02-Dec-24	27-Feb-25

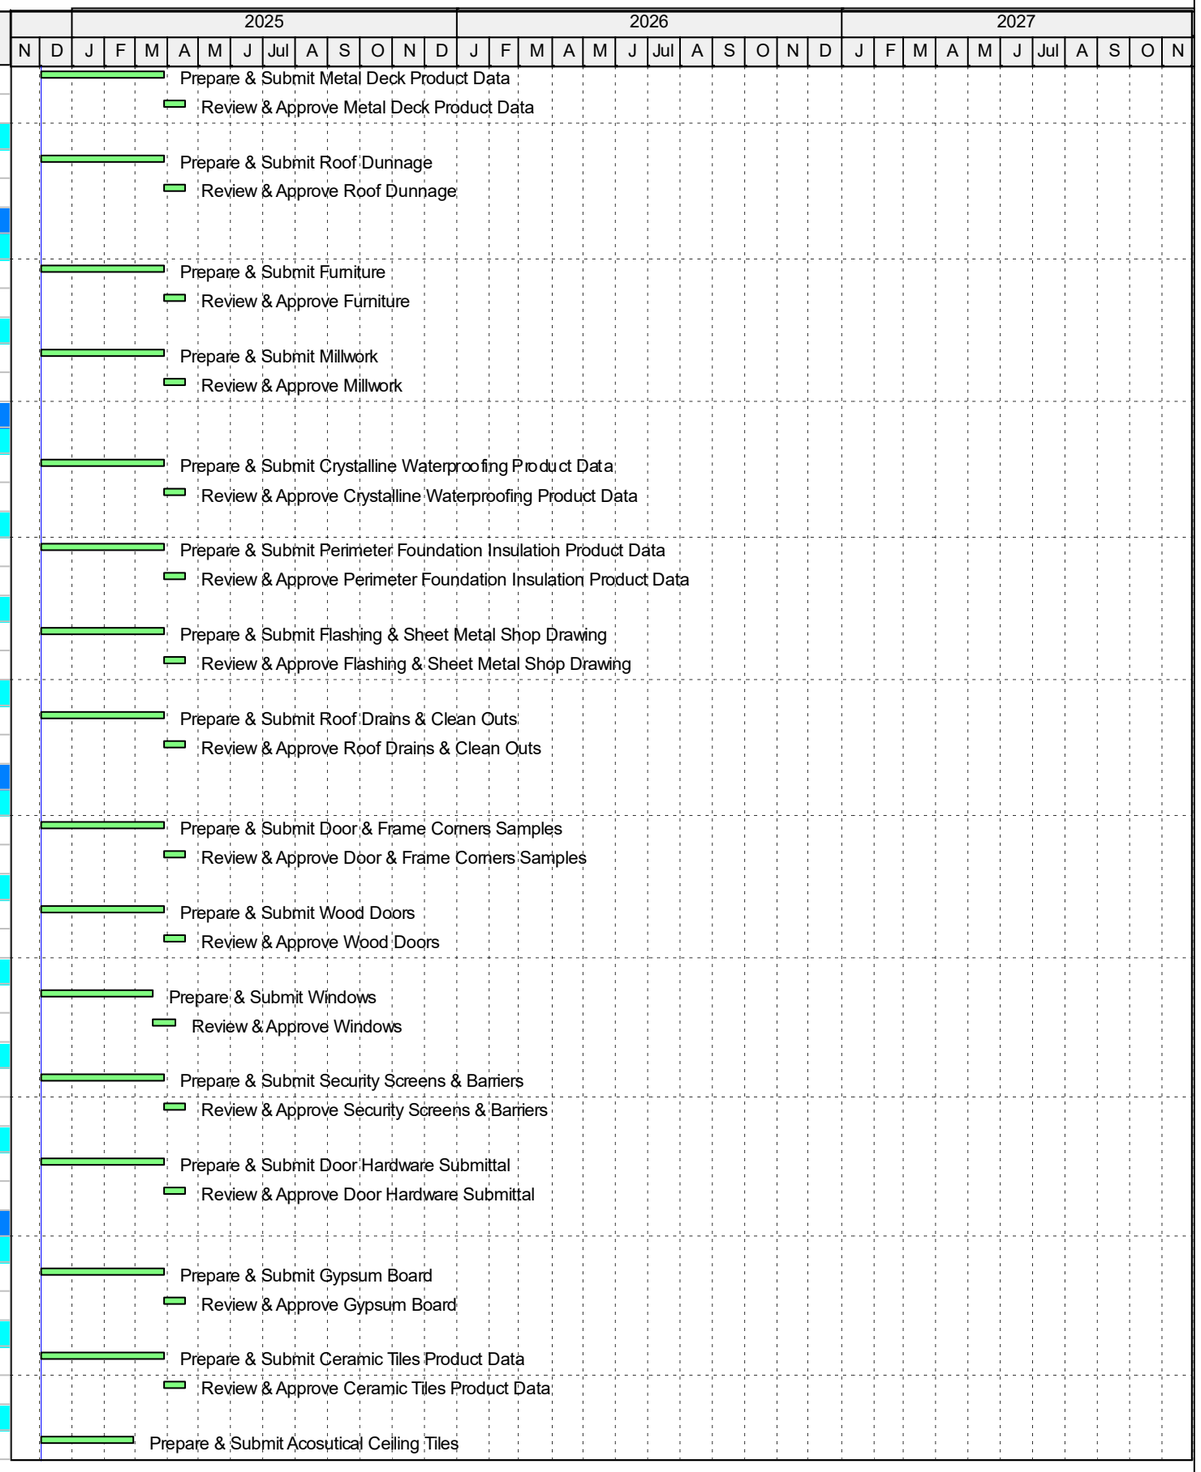

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

TECHNICO CONSTRUCTION PROJECS

Prepared By: A.A			
Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1230	Review & Approve Acosutical Ceiling Tiles	21	28-Feb-25	20-Mar-25
Spec Section 09590 - Wood Flooring		96	02-Dec-24	18-Apr-25
SUB-1780	Prepare & Submit Wood Flooring	81	02-Dec-24	28-Mar-25
APP-1790	Review & Approve Wood Flooring	21	29-Mar-25	18-Apr-25
Spec Section 09650 - Resilient Flooring		96	02-Dec-24	18-Apr-25
SUB-1380	Prepare & Submit Floorings	81	02-Dec-24	28-Mar-25
APP-1580	Review & Approve Floorings	21	29-Mar-25	18-Apr-25
Spec Section 09900 - Painting		96	02-Dec-24	18-Apr-25
SUB-1090	Prepare & Submit Painting	81	02-Dec-24	28-Mar-25
APP-1370	Review & Approve Painting	21	29-Mar-25	18-Apr-25
Division 10 - Specialties		96	02-Dec-24	18-Apr-25
Spec Section 10100 - Visual Display Boards		96	02-Dec-24	18-Apr-25
SUB-1790	Prepare & Submit Visual Display Boards	81	02-Dec-24	28-Mar-25
APP-1800	Review & Approve Visual Display Boards	21	29-Mar-25	18-Apr-25
Spec Section 10400 - Identification Devices		96	02-Dec-24	18-Apr-25
SUB-1060	Prepare & Submit Interior Signage Shop Drawings	81	02-Dec-24	28-Mar-25
APP-1340	Review & Approve Interior Signage Shop Drawings	21	29-Mar-25	18-Apr-25
Spec Section 10522 - Fire Extinguishers & Cabinets		96	02-Dec-24	18-Apr-25
SUB-1800	Prepare & Submit Fire Extinguishers & Cabinets	81	02-Dec-24	28-Mar-25
APP-1810	Review & Approve Fire Extinguishers & Cabinets	21	29-Mar-25	18-Apr-25
Spec Section 10720 - Window Guards		88	02-Dec-24	08-Apr-25
SUB-1810	Prepare & Submit Stationary Metal Wall Louvers	73	02-Dec-24	18-Mar-25
APP-1270	Review & Approve Stationary Metal Wall Louvers	21	19-Mar-25	08-Apr-25
Spec Section 10810 - Toilet & Bath Accessories		96	02-Dec-24	18-Apr-25
SUB-1400	Prepare & Submit Toilet Accessories	81	02-Dec-24	28-Mar-25
APP-1590	Review & Approve Toilet Accessories	21	29-Mar-25	18-Apr-25
Division 11 - Equipment		96	02-Dec-24	18-Apr-25
Spec Section 11061 - Platform Curtains & Auditorium Window Curtains		96	02-Dec-24	18-Apr-25
SUB-1820	Prepare & Submit Platform Curtains & Auditorium Window Curtains	81	02-Dec-24	28-Mar-25
APP-1820	Review & Approve Platform Curtains & Auditorium Window Curtains	21	29-Mar-25	18-Apr-25
Spec Section 11400 - Food Service Equipment		96	02-Dec-24	18-Apr-25
SUB-1550	Prepare & Submit Kitchen Equipment	81	02-Dec-24	28-Mar-25
APP-1670	Review & Approve Kitchen Equipment	21	29-Mar-25	18-Apr-25
Spec Section 11450 - Domestic Type Equipment		96	02-Dec-24	18-Apr-25
SUB-1830	Prepare & Submit Domestic Equipment	81	02-Dec-24	28-Mar-25
APP-1830	Review & Approve Domestic Equipment	21	29-Mar-25	18-Apr-25
Spec Section 11480 - Gymnasium Equipment		96	02-Dec-24	18-Apr-25
SUB-1630	Prepare & Submit Gymnasium Equipment	81	02-Dec-24	28-Mar-25
APP-1710	Review & Approve Gymnasium Equipment	21	29-Mar-25	18-Apr-25
Division 12 - Furnishings		96	02-Dec-24	18-Apr-25
Spec Section 12302 - Manufactured Wood Casework		96	02-Dec-24	18-Apr-25
SUB-1840	Prepare & Submit Manufactured Wood Casework	81	02-Dec-24	28-Mar-25
APP-1840	Review & Approve Manufactured Wood Casework	21	29-Mar-25	18-Apr-25
Division 14 - Conveying Systems		96	02-Dec-24	18-Apr-25
Spec Section 14212 - Gearless Traction Passenger Elevators		64	02-Dec-24	05-Mar-25
SUB-1360	Prepare & Submit Elevator Machine	50	02-Dec-24	12-Feb-25
APP-1180	Review & Approve Elevator Machine	21	13-Feb-25	05-Mar-25
Spec Section 14420 - Hydraulic Vertical Wheelchair Lifts		96	02-Dec-24	18-Apr-25
SUB-1850	Prepare & Submit Hydraulic Vertical Wheelchair Lifts	81	02-Dec-24	28-Mar-25
APP-1850	Review & Approve Hydraulic Vertical Wheelchair Lifts	21	29-Mar-25	18-Apr-25

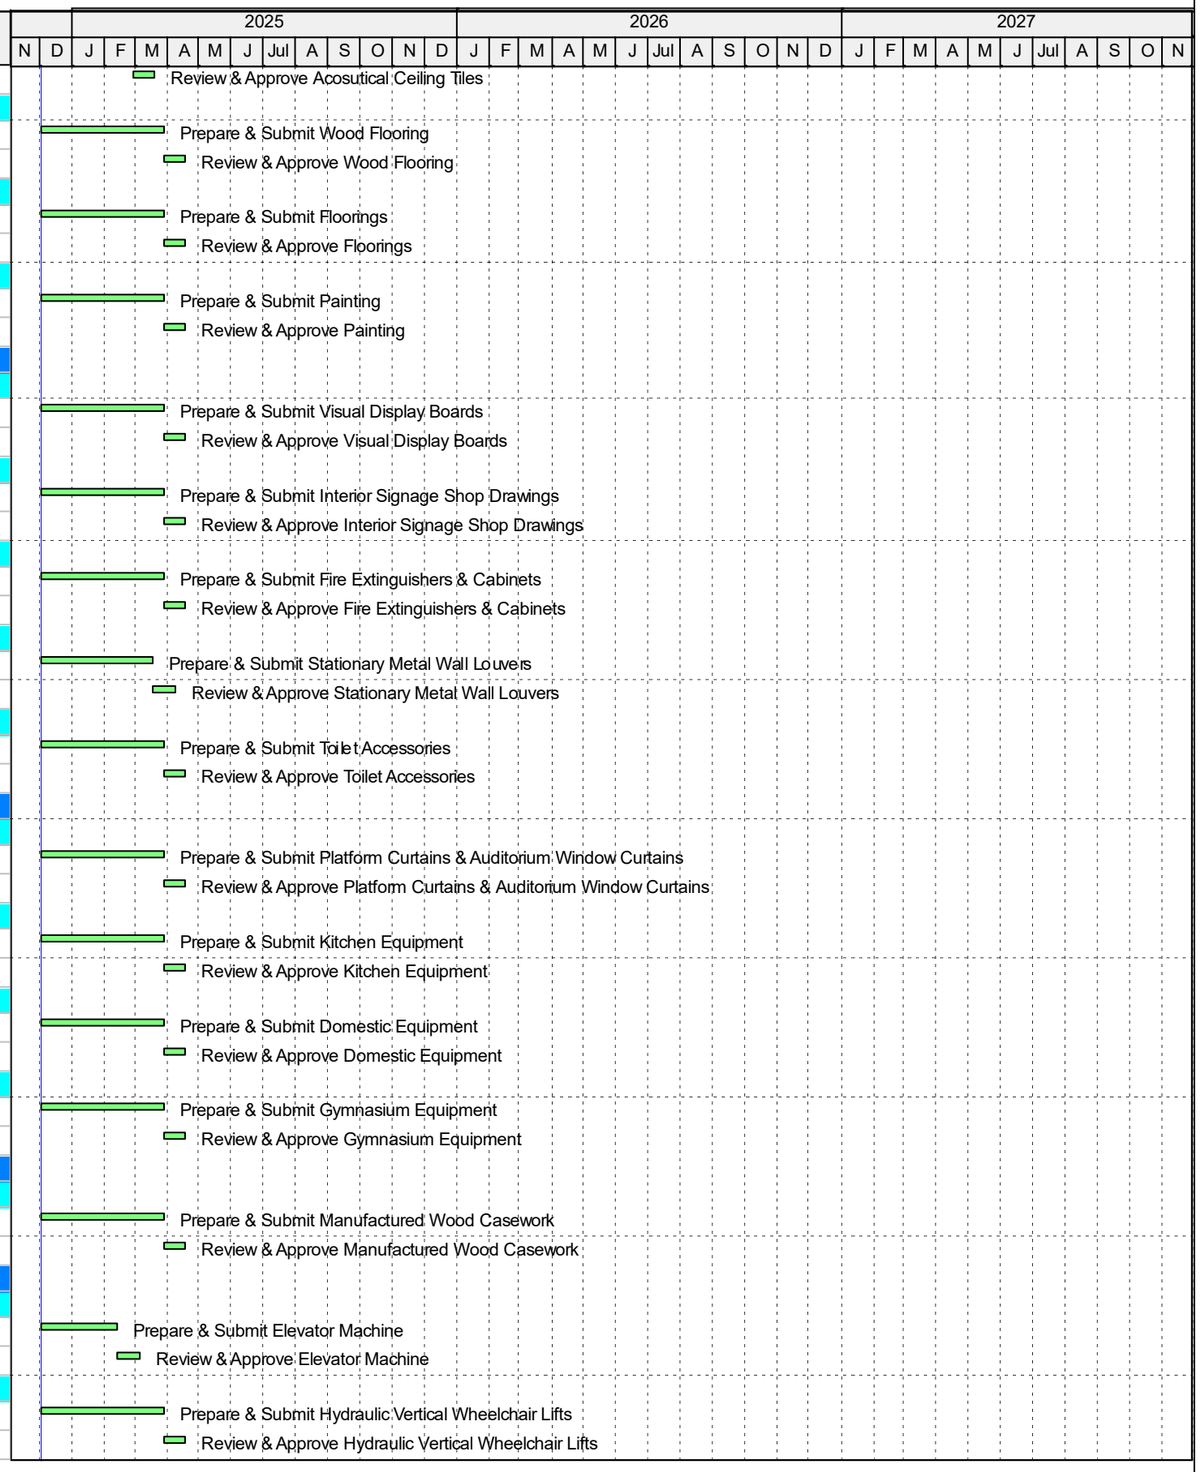

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

TECHNICO CONSTRUCTION PROJECS

Prepared By: A.A			
Date	Revision	Checked	Approved
16-Dec-24	00	AR	


Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
Division 15 - Mechanical		96	02-Dec-24	18-Apr-25
Division 15A - Fire Protection		96	02-Dec-24	18-Apr-25
Spec Section 15333 - Fire Pumps - Sprinkler Booster Pumps		96	02-Dec-24	18-Apr-25
SUB-1050	Prepare & Submit Fire & Jockey Pumps	81	02-Dec-24	28-Mar-25
SUB-1530	Prepare & Submit Fire Protection Shop Drawings	81	02-Dec-24	28-Mar-25
APP-1330	Review & Approve Fire & Jockey Pumps	21	29-Mar-25	18-Apr-25
APP-1650	Review & Approve Fire Protection Shop Drawings	21	29-Mar-25	18-Apr-25
Division 15B - Plumbing & Drainage		96	02-Dec-24	18-Apr-25
Spec Section 15410 - Plumbing Piping		96	02-Dec-24	18-Apr-25
SUB-1340	Prepare & Submit Plumbing Shop Drawings	81	02-Dec-24	28-Mar-25
APP-1560	Review & Approve Plumbing Shop Drawings	21	29-Mar-25	18-Apr-25
Spec Section 15411 - Hangers and Supports		54	02-Dec-24	19-Feb-25
SUB-1040	Prepare & Submit Hangers & Supports	40	02-Dec-24	29-Jan-25
APP-1160	Review & Approve Hangers & Supports	21	30-Jan-25	19-Feb-25
Spec Section 15415 - Drainage		54	02-Dec-24	19-Feb-25
SUB-1030	Prepare & Submit Floor Drains	40	02-Dec-24	29-Jan-25
APP-1150	Review & Approve Floor Drains	21	30-Jan-25	19-Feb-25
Spec Section 15417 - Cold Water Supply		54	02-Dec-24	19-Feb-25
SUB-1020	Prepare & Submit Pressure Gages	40	02-Dec-24	29-Jan-25
APP-1140	Review & Approve Pressure Gages	21	30-Jan-25	19-Feb-25
Spec Section 15418 - Hot Water Supply		54	02-Dec-24	19-Feb-25
SUB-1010	Prepare & Submit Thermometers	40	02-Dec-24	29-Jan-25
APP-1130	Review & Approve Thermometers	21	30-Jan-25	19-Feb-25
Spec Section 15440 - Plumbing Fixtures		96	02-Dec-24	18-Apr-25
SUB-1500	Prepare & Submit Plumbing Fixtures	81	02-Dec-24	28-Mar-25
APP-1630	Review & Approve Plumbing Fixtures	21	29-Mar-25	18-Apr-25
Spec Section 15453 - Pumping Apparatus & Tanks		96	02-Dec-24	18-Apr-25
SUB-1880	Prepare & Submit Pumping Apparatus & Tanks	81	02-Dec-24	28-Mar-25
APP-1880	Review & Approve Pumping Apparatus & Tanks	21	29-Mar-25	18-Apr-25
Division 15C - Heating & Ventilation & Air Conditioning		96	02-Dec-24	18-Apr-25
Spec Section 15510 - HVAC Piping		75	02-Dec-24	20-Mar-25
SUB-1450	Prepare & Submit Mechanical Piping	60	02-Dec-24	27-Feb-25
APP-1240	Review & Approve Mechanical Piping	21	28-Feb-25	20-Mar-25
Spec Section 15783 - Split Heat Pump System		75	02-Dec-24	20-Mar-25
SUB-1000	Prepare & Submit Split Heat Pump System - SUB	60	02-Dec-24	27-Feb-25
APP-1220	Review & Approve Split Heat Pump System - SUB	21	28-Feb-25	20-Mar-25
Spec Section 15836 - Unit Heaters Cabinet Heaters		75	02-Dec-24	20-Mar-25
SUB-1620	Prepare & Submit Unit Cabinet Heaters	60	02-Dec-24	27-Feb-25
APP-1250	Review & Approve Unit Cabinet Heaters	21	28-Feb-25	20-Mar-25
Spec Section 15891 - Metal Ductwork		96	02-Dec-24	18-Apr-25
SUB-1440	Prepare & Submit Mechanical Ducts	81	02-Dec-24	28-Mar-25
APP-1620	Review & Approve Mechanical Ducts	21	29-Mar-25	18-Apr-25
Spec Section 15590 - Emergency Generator System Accessories		96	02-Dec-24	18-Apr-25
SUB-1890	Prepare & Submit Emergency Generator System Accessories	81	02-Dec-24	28-Mar-25
APP-1890	Review & Approve Emergency Generator System Accessories	21	29-Mar-25	18-Apr-25
Spec Section 15836 - Unit Heaters/Cabinet Heaters		96	02-Dec-24	18-Apr-25
SUB-1900	Prepare & Submit Unit Heaters/Cabinet Heaters Equipment	81	02-Dec-24	28-Mar-25
APP-1900	Review & Approve Unit Heaters/Cabinet Heaters Equipment	21	29-Mar-25	18-Apr-25
Spec Section 15940 - Air Outlets & Inlets		96	02-Dec-24	18-Apr-25
SUB-1920	Prepare & Submit Air Outlets & Inlets	81	02-Dec-24	28-Mar-25

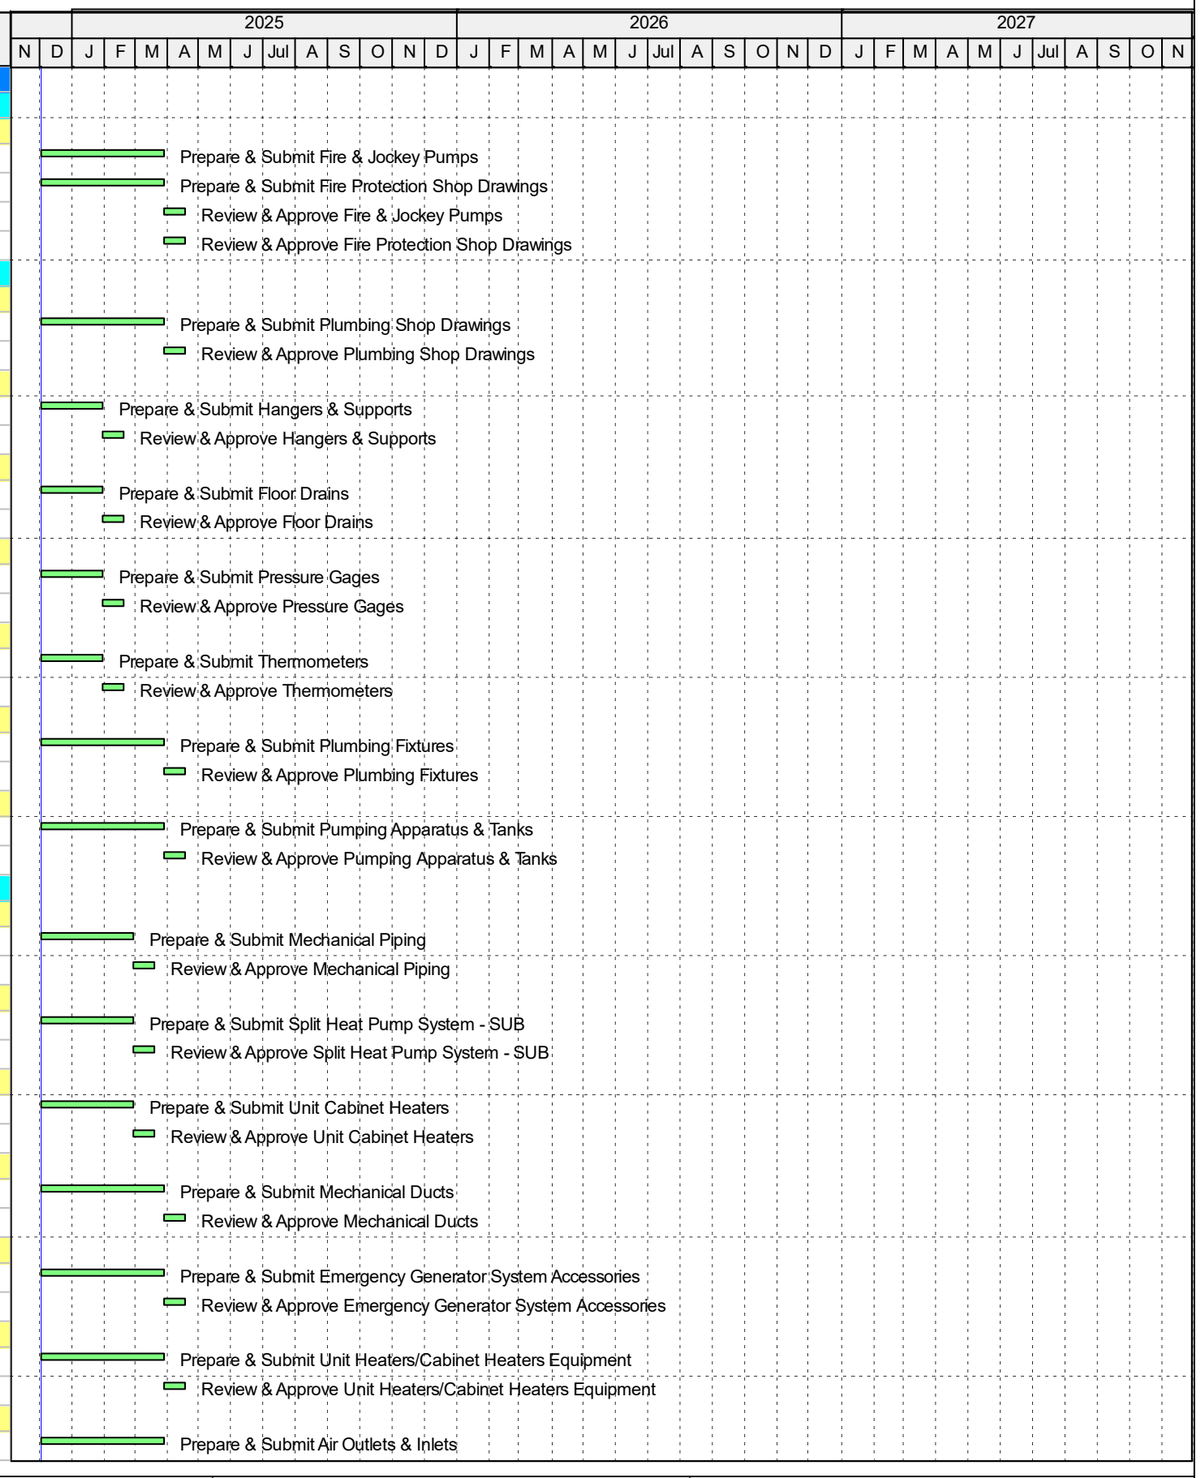

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1920	Review & Approve Air Outlets & Inlets	21	29-Mar-25	18-Apr-25
Spec Section 15970 - Temperature Control System		96	02-Dec-24	18-Apr-25
SUB-1910	Prepare & Submit Temperature Control System	81	02-Dec-24	28-Mar-25
APP-1910	Review & Approve Temperature Control System	21	29-Mar-25	18-Apr-25
Division 16 - Electrical		96	02-Dec-24	18-Apr-25
Spec Section 16010 - Gen Provisions for Elec Work		96	02-Dec-24	18-Apr-25
SUB-1330	Prepare & Submit Electrical Shop Drawings	81	02-Dec-24	28-Mar-25
SUB-1490	Prepare & Submit Electrical Equipment, Conduits, and Cables	20	02-Dec-24	30-Dec-24
SUB-1610	Prepare & Submit Switch Gears Product Data	20	02-Dec-24	30-Dec-24
APP-1050	Review & Approve Electrical Equipment, Conduits, and Cables	21	31-Dec-24	20-Jan-25
APP-1060	Review & Approve Switch Gears Product Data	21	31-Dec-24	20-Jan-25
APP-1550	Review & Approve Electrical Shop Drawings	21	29-Mar-25	18-Apr-25
Spec Section 16120 - Wiring Systems		96	02-Dec-24	18-Apr-25
SUB-1580	Prepare & Submit Telecommunication System Drawings	81	02-Dec-24	28-Mar-25
APP-1690	Review & Approve Telecommunication System Drawings	21	29-Mar-25	18-Apr-25
Spec Section 16502 - Interior Lighting Fixtures		44	02-Dec-24	04-Feb-25
SUB-1420	Prepare & Submit Lighting Fixtures	30	02-Dec-24	14-Jan-25
APP-1090	Review & Approve Lighting Fixtures	21	15-Jan-25	04-Feb-25
Spec Section 16520 - Illuminated Exit Sign		96	02-Dec-24	18-Apr-25
SUB-1560	Prepare & Submit Signs	81	02-Dec-24	28-Mar-25
APP-1680	Review & Approve Signs	21	29-Mar-25	18-Apr-25
Spec Section 16720 - Fire Detection Alarm System with COC		96	02-Dec-24	18-Apr-25
SUB-1540	Prepare & Submit Fire Detectors & Alarms	81	02-Dec-24	28-Mar-25
APP-1660	Review & Approve Fire Detectors & Alarms	21	29-Mar-25	18-Apr-25
Spec Section 16785 - Internet Protocol Digital Video Surveillance System using Digital Cameras		64	02-Dec-24	05-Mar-25
SUB-1590	Prepare & Submit Internet Protocol Digital Video Surveillance System using Digital Cameras	50	02-Dec-24	12-Feb-25
APP-1190	Review & Approve Internet Protocol Digital Video Surveillance System using Digital Cameras	21	13-Feb-25	05-Mar-25
Spec Section 16425 - Switch Boards & Panel Boards		96	02-Dec-24	18-Apr-25
SUB-1860	Prepare & Submit Switch & Panel Boards	81	02-Dec-24	28-Mar-25
APP-1860	Review & Approve Switch & Panel Boards	21	29-Mar-25	18-Apr-25
Spec Section 16475 - Overcurrent Protective Devices		96	02-Dec-24	18-Apr-25
SUB-1870	Prepare & Submit Overcurrent Protective Devices Data	81	02-Dec-24	28-Mar-25
APP-1870	Review & Approve Overcurrent Protective Devices Data	21	29-Mar-25	18-Apr-25
Fabrication & Delivery		358	01-Jan-25	24-Dec-25
PRO-1120	Procure & Deliver Erosion Control and Sedimentation Devices	25	01-Jan-25	25-Jan-25
PRO-1140	Procure & Deliver Lighting Fixtures	60	05-Feb-25	05-Apr-25
PRO-1200	Procure & Deliver Elevator Machine	150	06-Mar-25	02-Aug-25
PRO-1330	Procure & Deliver Cameras	60	06-Mar-25	04-May-25
PRO-1170	Procure & Deliver Acosutical Ceiling Tiles	120	21-Mar-25	18-Jul-25
PRO-1020	Procure & Deliver Mechanical Piping	70	21-Mar-25	29-May-25
PRO-1220	Procure & Deliver Windows	154	09-Apr-25	09-Sep-25
PRO-1420	Procure & Deliver Painting	70	19-Apr-25	27-Jun-25
PRO-1410	Procure & Deliver Door Frames	70	19-Apr-25	27-Jun-25
PRO-1150	Procure & Deliver Gypsum Board	150	19-Apr-25	15-Sep-25
PRO-1160	Procure & Deliver Floorings	80	19-Apr-25	07-Jul-25
PRO-1190	Procure & Deliver Toilet Accessories	100	19-Apr-25	27-Jul-25
PRO-1000	Procure & Deliver Kitchen Equipment	180	19-Apr-25	15-Oct-25
PRO-1010	Procure & Deliver Furnitures	130	19-Apr-25	26-Aug-25
PRO-1030	Procure & Deliver Mechanical Ducts	70	19-Apr-25	27-Jun-25

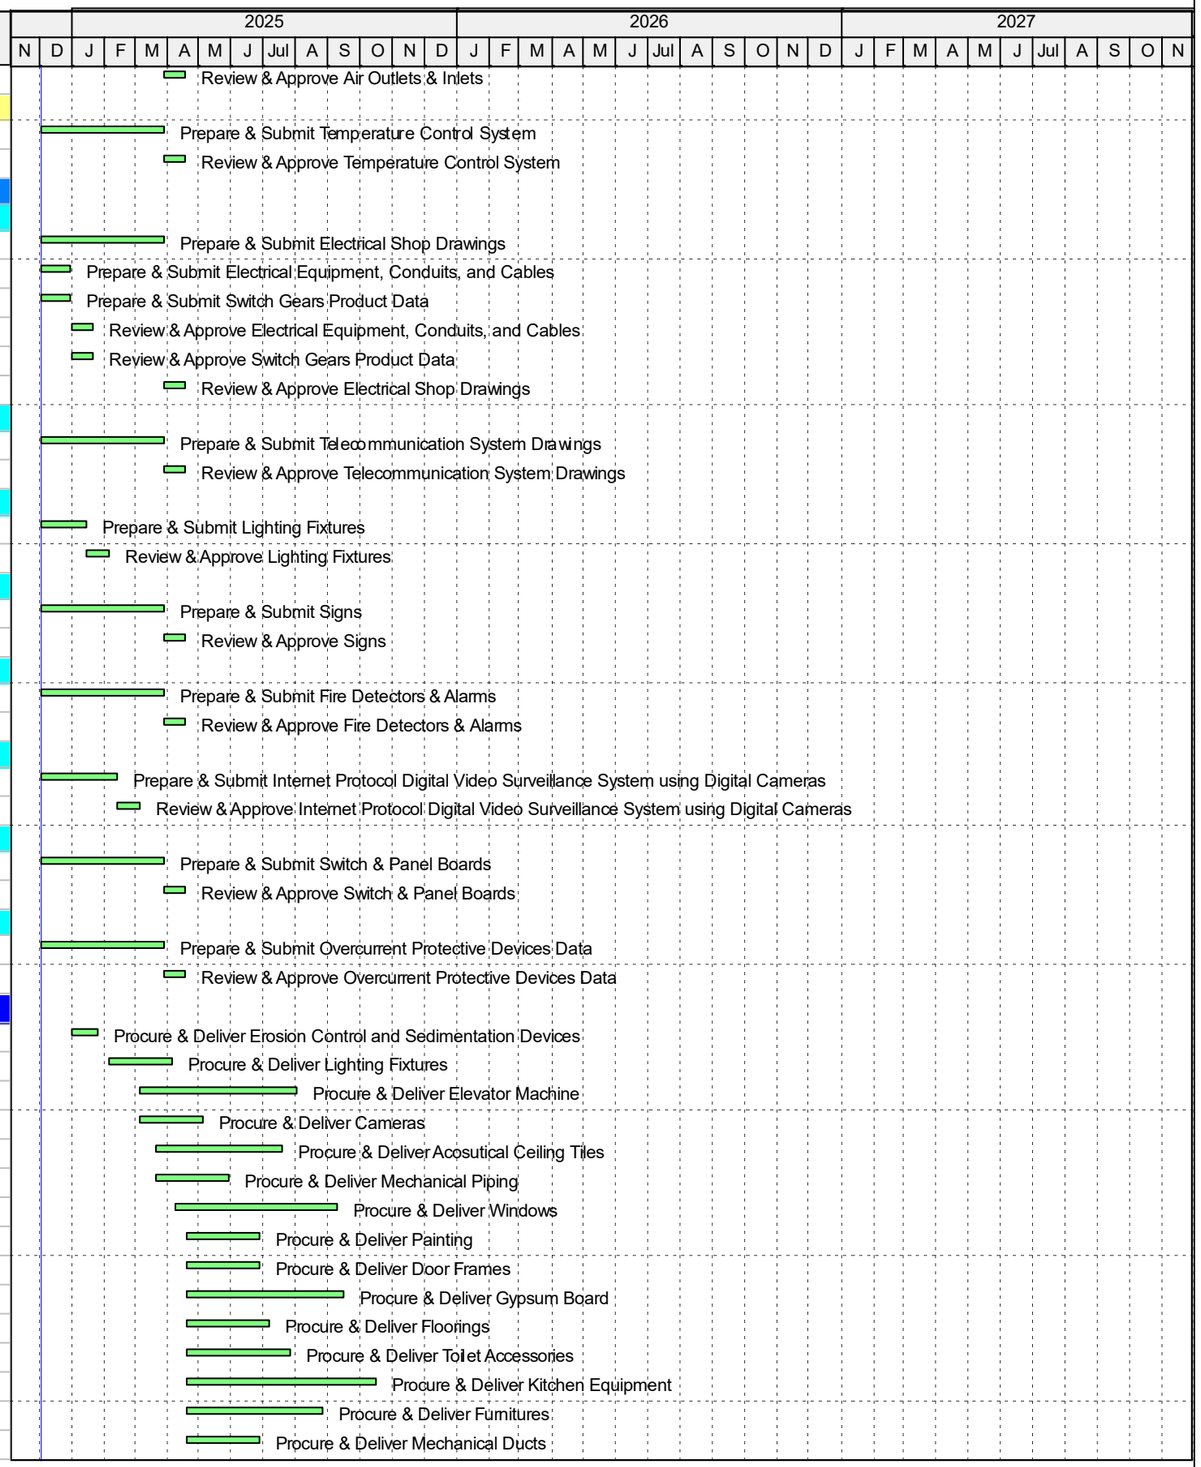

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

IS 082K New Building Design No. 093937 - Baseline Schedule Rev 00


TECHNICO CONSTRUCTION PROJECTS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
PRO-1050	Procure & Deliver Electrical Equipment	130	19-Apr-25	26-Aug-25
PRO-1060	Procure & Deliver Plumbing Fixtures	100	19-Apr-25	27-Jul-25
PRO-1070	Procure & Deliver Doors	50	19-Apr-25	07-Jun-25
PRO-1110	Procure & Deliver Fire Detectors & Alarms	60	19-Apr-25	17-Jun-25
PRO-1210	Procure & Deliver Signs	70	19-Apr-25	27-Jun-25
PRO-1250	Procure & Deliver Plumbing Pipes	60	19-Apr-25	17-Jun-25
PRO-1260	Procure & Deliver Electrical Wires & Conduits	130	19-Apr-25	26-Aug-25
PRO-1270	Procure & Deliver Mechanical Pumps	70	19-Apr-25	27-Jun-25
PRO-1280	Procure & Deliver Fire Protection Pumps	70	19-Apr-25	27-Jun-25
PRO-1290	Procure & Deliver Plumbing Pumps	250	19-Apr-25	24-Dec-25
PRO-1310	Procure & Deliver Telecommunication System	60	19-Apr-25	17-Jun-25
PRO-1380	Procure & Deliver Roof Dunnage	100	19-Apr-25	27-Jul-25
PRO-1470	Procure & Deliver Cabinet Heaters	126	19-Apr-25	22-Aug-25
PRO-1530	Procure & Deliver Hydraulic Vertical Wheelchair Lift	90	19-Apr-25	17-Jul-25
PRO-1560	Procure & Deliver Gymnasium Equipment	180	19-Apr-25	15-Oct-25
PRO-1580	Procure & Deliver Metal Deck	120	19-Apr-25	16-Aug-25
PRO-1590	Procure & Deliver Steel Columns	120	19-Apr-25	16-Aug-25
PRO-1600	Procure & Deliver Steel Framing	60	19-Apr-25	17-Jun-25
PRO-1630	Procure & Deliver Wood Flooring	120	19-Apr-25	16-Aug-25
Construction		348	09-Jun-25	28-Oct-26
Site Preparation		81	09-Jun-25	02-Oct-25
CON-1010	Install Site Fence	2	09-Jun-25	10-Jun-25
CON-1020	Install Construction Entrance - Stage 1	1	09-Jun-25	09-Jun-25
CON-1030	Install Erosion Control Devices - Stage 1	2	11-Jun-25	12-Jun-25
CON-1040	Remove Existing Asphalt Pavement and Subbase	2	13-Jun-25	16-Jun-25
CON-1050	Install Remove Existing Concrete Pavement and Subbase	2	13-Jun-25	16-Jun-25
CON-1060	Prepare Temporary Staging & Storage Area - Stage 1	3	17-Jun-25	20-Jun-25
CON-1250	Install Construction Entrance - Stage 2	1	30-Sep-25	30-Sep-25
CON-1260	Install Erosion Control Devices - Stage 2	2	01-Oct-25	02-Oct-25
CON-1270	Prepare Temporary Staging & Storage Area - Stage 2	2	01-Oct-25	02-Oct-25
Cellar Floor		276	23-Jun-25	29-Jul-26
SSDS - Cellar Floor		10	28-Jul-25	08-Aug-25
CON-1110	Install Non-Woven Geotextile Layer - Below Cellar	2	28-Jul-25	29-Jul-25
CON-1130	Install Gas Permeable Aggregate Layer- Below Cellar	2	30-Jul-25	31-Jul-25
CON-1140	Install 6" C.I Pipe - Below Cellar	2	30-Jul-25	31-Jul-25
CON-1150	Install VI-20 Geomembrane Gas Permeable Aggregate Layer - Below Cellar	2	01-Aug-25	04-Aug-25
CON-1160	Install 60 Dry Mils of Liquid Boot - Below Cellar	2	05-Aug-25	06-Aug-25
CON-1170	Install Liquid Boot Ultrashield G-1000 - Below Cellar	2	07-Aug-25	08-Aug-25
Structure - Cellar Floor		62	23-Jun-25	18-Sep-25
CON-1070	Survey and Verify All Underground Utilities	3	23-Jun-25	25-Jun-25
CON-1080	Excavation	7	26-Jun-25	07-Jul-25
CON-1090	F/R/P Cellar Wall Footings	6	08-Jul-25	15-Jul-25
CON-1100	F/R/P Cellar Retaining Wall	8	16-Jul-25	25-Jul-25
CON-1120	Insulate Cellar Retaining Wal	5	28-Jul-25	01-Aug-25
CON-1180	F/R/P Slab on Grade - Cellar	4	11-Aug-25	14-Aug-25
CON-1190	F/R/P First Floor Slab - Cellar Side	5	15-Aug-25	21-Aug-25
CON-1220	Curing For The First Floor Slab	28	22-Aug-25	18-Sep-25
CON-1230	F/R/P Columns & Shear Walls From First Level To Second Level - Cellar Area	4	22-Aug-25	27-Aug-25

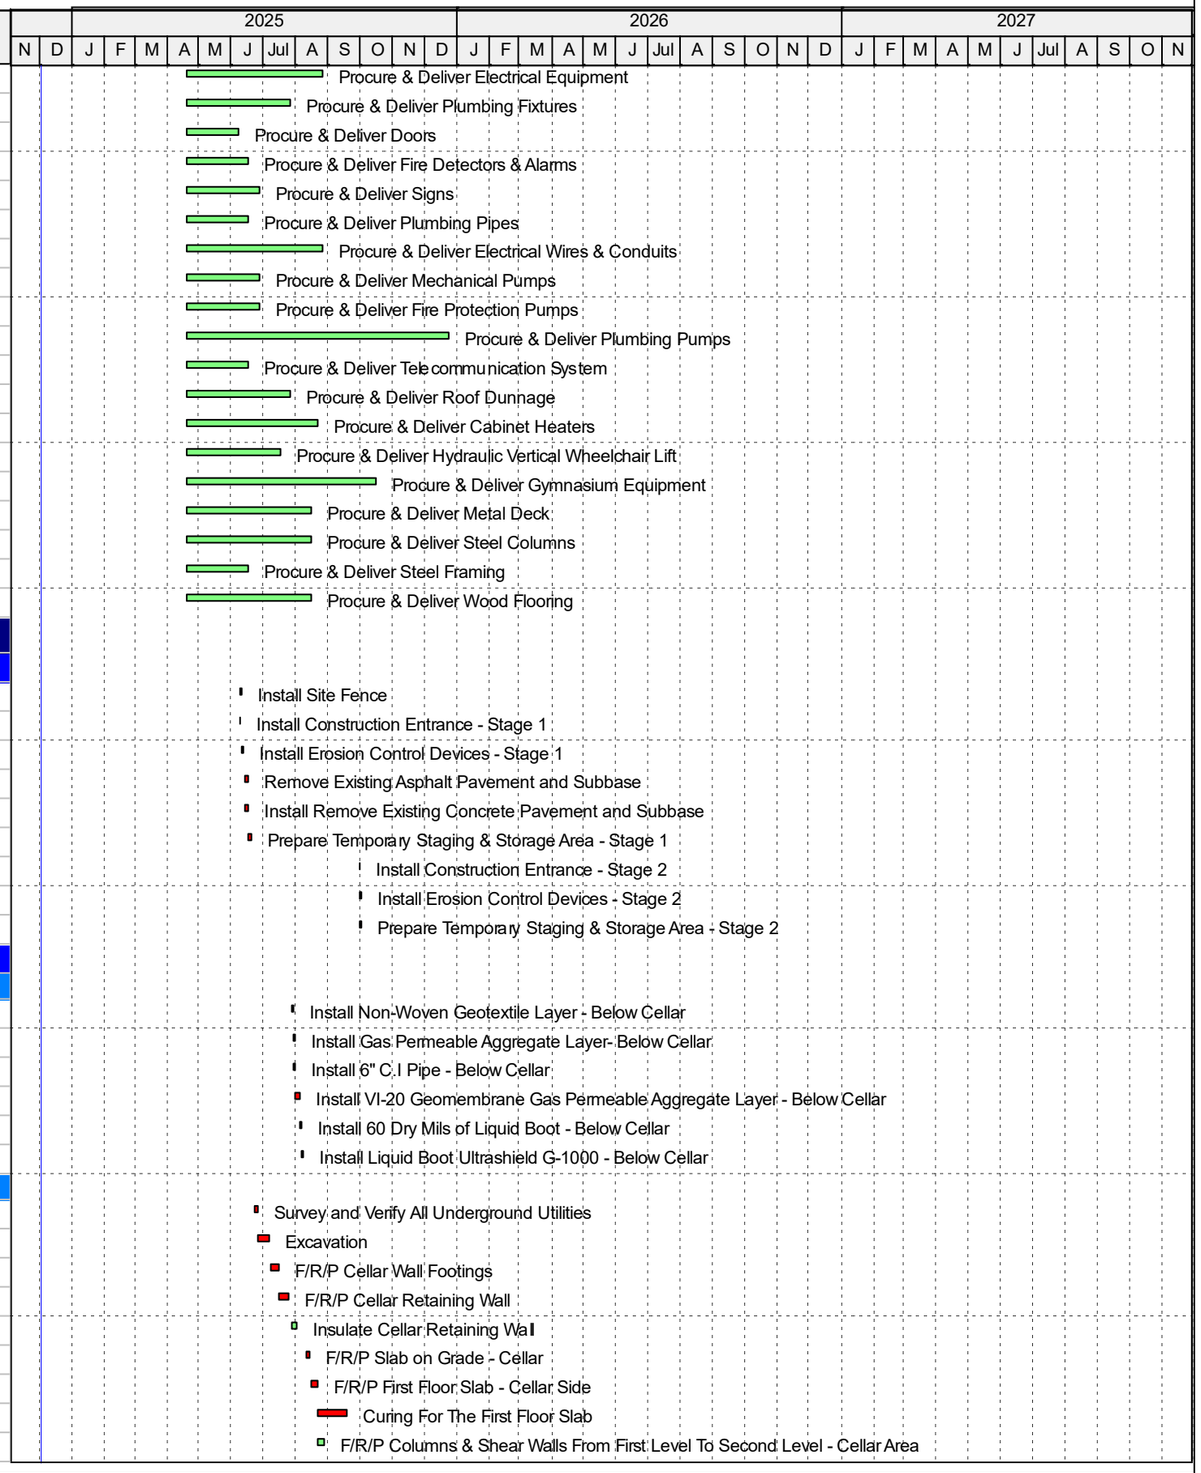

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone


TECHNICO CONSTRUCTION PROJECS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
Mechanical- Cellar Floor		93	09-Jan-26	21-May-26
HVAC Rough-ins-1st Floor		9	09-Jan-26	22-Jan-26
CON-1720	Rough-in Duct Risers - Cellar Floor	3	09-Jan-26	13-Jan-26
CON-1850	Rough-in Duct Work -VAV Devices & Diffusers - Cellar Floor	5	15-Jan-26	22-Jan-26
Mechanical Equipment-1st Floor		84	23-Jan-26	21-May-26
CON-2110	Install AC-C17.1 - Cellar	3	23-Jan-26	27-Jan-26
CON-2120	Install AC-C17.2 - Cellar	3	23-Jan-26	27-Jan-26
CON-2140	Install Electric Unit Heater - Cellar Floor	2	23-Jan-26	26-Jan-26
CON-5010	Install Electric Cabinet Heaters - Cellar Floor	3	19-May-26	21-May-26
Plumbing-Cellar Floor		196	15-Aug-25	28-May-26
CON-1200	Install Floor Drains - Cellar Floor	2	15-Aug-25	18-Aug-25
CON-1790	Rough-in Refrigerant Piping - Cellar Floor	5	14-Jan-26	21-Jan-26
CON-1810	Rough-in Electrical Risers (Power & Low Voltage) - Cellar Floor	3	14-Jan-26	16-Jan-26
CON-1820	Rough-in SSDS Risers - Cellar Floor	3	14-Jan-26	16-Jan-26
CON-1920	Rough-in Plumbing Risers - Cellar Floor	3	20-Jan-26	22-Jan-26
CON-2710	Rough-in Plumbing Pipes- Cellar Floor	5	06-Feb-26	12-Feb-26
CON-5040	Install Plumbing Fixtures - Cellar Floor	7	19-May-26	28-May-26
Fire Protection-Cellar Floor		5	13-Feb-26	20-Feb-26
CON-2990	Rough-in Sprinkler Piping - Cellar Floor	5	13-Feb-26	20-Feb-26
CON-3120	Install Sprinkler Heads - Cellar Floor	2	19-Feb-26	20-Feb-26
Electrical-Cellar Floor		130	23-Jan-26	29-Jul-26
CON-2160	Rough-in Power Conduits & Wires - Cellar Floor	5	23-Jan-26	29-Jan-26
CON-2410	Rough-in Low Voltage Conduits & Wires - Cellar Floor	5	30-Jan-26	05-Feb-26
CON-2720	Install Electrical Panels - Cellar Floor	5	06-Feb-26	12-Feb-26
CON-4870	Install Lighting Fixtures - Cellar Floor	7	08-May-26	18-May-26
CON-5030	Install Data & Video Intercome Systems -Cellar Floor	7	19-May-26	28-May-26
CON-5170	Install Voice Systems Components -Cellar Floor	7	29-May-26	08-Jun-26
CON-5370	Install Public Address and Clock Systems Components -Cellar Floor	7	09-Jun-26	17-Jun-26
CON-5580	Install Auxiliary Signal System Components - Cellar Floor	7	18-Jun-26	29-Jun-26
CON-5740	Install Intrusion Alarm System Components- Cellar Floor	7	30-Jun-26	09-Jul-26
CON-5880	Install IPDVS System Components - Cellar Floor	7	10-Jul-26	20-Jul-26
CON-6010	Install Fire Alarm Devices- Cellar Floor	7	21-Jul-26	29-Jul-26
Architecture-Cellar Floor		107	09-Jan-26	11-Jun-26
Interior Walls-1st Floor		69	09-Jan-26	17-Apr-26
CON-1690	Layout - Cellar Floor	2	09-Jan-26	12-Jan-26
CON-1760	Install Top & Bottom Tracks - Cellar Floor	2	13-Jan-26	14-Jan-26
CON-1770	Install CMU - Cellar Floor	3	13-Jan-26	15-Jan-26
CON-2100	Install Steel Studs - Cellar Floor	4	23-Jan-26	28-Jan-26
CON-4420	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - Cellar Floor	7	09-Apr-26	17-Apr-26
Ceiling-1st Floor		47	23-Feb-26	28-Apr-26
CON-3210	Install Ceiling Hangers - Cellar Floor	5	23-Feb-26	27-Feb-26
CON-4590	Install Acoustical Ceiling Tiles- Cellar Floor	7	20-Apr-26	28-Apr-26
CON-4600	Install Gypsum Board Ceiling- Cellar Floor	7	20-Apr-26	28-Apr-26
Finishes-1st Floor		38	20-Apr-26	11-Jun-26
CON-4610	Install Doors- Cellar Floor	3	20-Apr-26	22-Apr-26
CON-4730	Install First Coat Painting - Cellar Floor	7	29-Apr-26	07-May-26
CON-4860	Install Flooring - Cellar Floor	7	08-May-26	18-May-26
CON-4890	Install Milling Work - Cellar Floor	7	08-May-26	18-May-26
CON-5070	Install Furniture - Cellar Floor	7	19-May-26	28-May-26

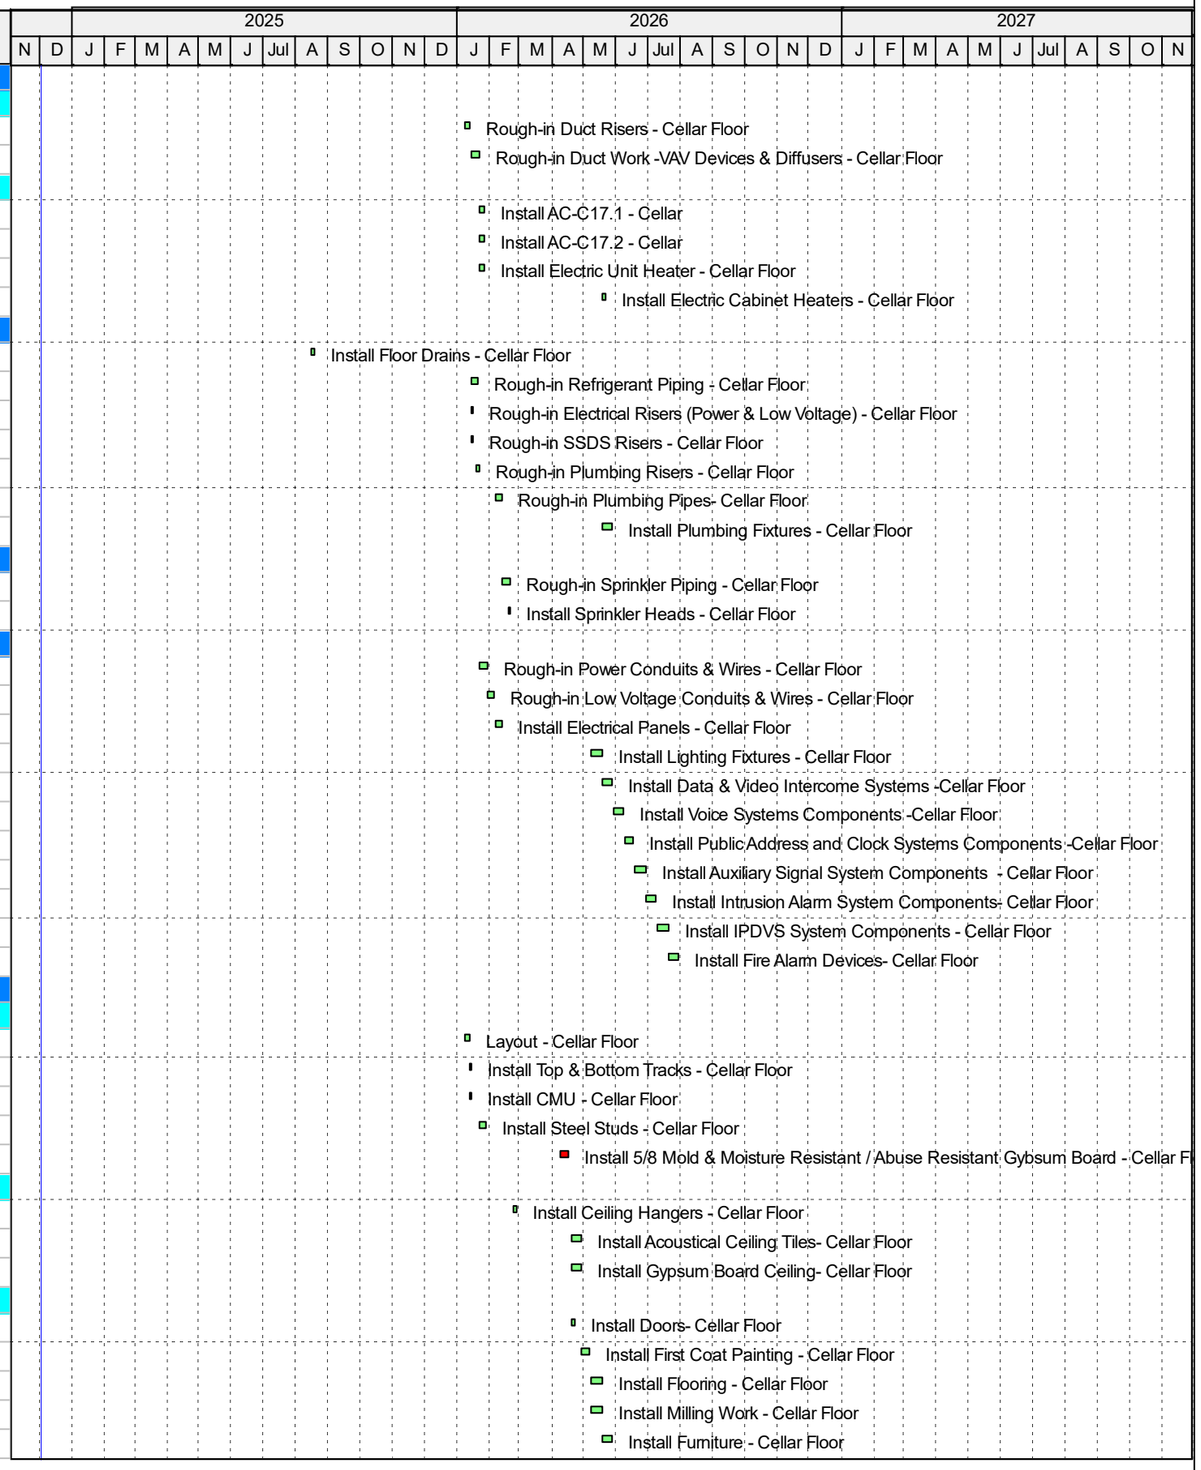

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

TECHNICO CONSTRUCTION PROJECS

Prepared By: A.A			
Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-5200	Install Final Coat Painting - Cellar Floor	7	29-May-26	08-Jun-26
CON-5430	Install Signage- Cellar Floor	3	09-Jun-26	11-Jun-26
First Floor		298	20-Aug-25	28-Oct-26
SSDS - 1st Floor		14	27-Oct-25	14-Nov-25
CON-1320	Install Non-Woven Geotextile Layer - Below 1st Floor SOG	3	27-Oct-25	29-Oct-25
CON-1330	Install Gas Permeable Aggregate Layer - Below 1st Floor SOG	3	30-Oct-25	03-Nov-25
CON-1340	Install 6" C.I Pipe - Below 1st Floor SOG	2	30-Oct-25	31-Oct-25
CON-1350	Install VI-20 Geomembrane Gas Permeable Aggregate Layer - Below 1st Floor SOG	3	04-Nov-25	06-Nov-25
CON-1360	Install 60 Dry Mils of Liquid Boot - Below 1st Floor SOG	3	07-Nov-25	12-Nov-25
CON-1370	Install Liquid Boot Ultrashield G-1000 - Below 1st Floor SOG	2	13-Nov-25	14-Nov-25
Structure-1st Floor		43	19-Sep-25	20-Nov-25
CON-1240	Backfilling	7	19-Sep-25	29-Sep-25
CON-1280	F/R/P First Floor Foundation	7	03-Oct-25	14-Oct-25
CON-1290	F/R/P Columns From First Level To Second Level - First Level Area	5	07-Oct-25	14-Oct-25
CON-1300	Insulate First Floor Foundations	3	15-Oct-25	17-Oct-25
CON-1310	Backfilling	5	20-Oct-25	24-Oct-25
CON-1380	F/R/P First Floor SOG	4	17-Nov-25	20-Nov-25
Mechanical- 1st Floor		207	20-Aug-25	17-Jun-26
HVAC Rough-ins-1st Floor		198	20-Aug-25	04-Jun-26
CON-1210	Install MEP Hangers - 1st Floor - Cellar Side	2	20-Aug-25	21-Aug-25
CON-2460	Rough-in Duct Risers - 1st Floor	3	02-Feb-26	04-Feb-26
CON-5120	Rough-in Duct Work -VAV Devices & Diffusers - 1st Floor	5	29-May-26	04-Jun-26
Mechanical Equipment-1st Floor		26	12-May-26	17-Jun-26
CON-4930	Install Electric Wall Convectors - 1st Floor	3	12-May-26	14-May-26
CON-5250	Install Heat Pump Unit (HP-108 B) - 1st Floor	4	05-Jun-26	10-Jun-26
CON-5260	Install Electrical Heat Air Curtain - 1st Floor	2	05-Jun-26	08-Jun-26
CON-5280	Install Electric Unit Heater - 1st Floor	2	05-Jun-26	08-Jun-26
CON-5490	Install Electric Cabinet Heaters - 1st Roof	3	15-Jun-26	17-Jun-26
Plumbing-1st Floor		166	19-Nov-25	20-Jul-26
CON-1390	Install Floor Drains - 1st Floor	2	19-Nov-25	20-Nov-25
CON-2640	Rough-in SSDS Risers - 1st Floor	3	05-Feb-26	09-Feb-26
CON-2780	Rough-in Plumbing Risers - 1st Floor	3	10-Feb-26	12-Feb-26
CON-5130	Rough-in Refrigerant Piping - 1st Floor	5	29-May-26	04-Jun-26
CON-5640	Rough-in Plumbing Pipes - 1st Floor	5	22-Jun-26	26-Jun-26
CON-5890	Install Plumbing Fixtures - 1st Floor	7	10-Jul-26	20-Jul-26
Fire Protection-1st Floor		5	29-Jun-26	06-Jul-26
CON-5680	Rough-in Sprinkler Piping - 1st Floor	5	29-Jun-26	06-Jul-26
CON-5780	Install Sprinkler Heads - 1st Floor	2	02-Jul-26	06-Jul-26
Electrical-1st Floor		184	05-Feb-26	28-Oct-26
CON-2600	Rough-in Electrical Risers (Power & Low Voltage) - 1st Floor	3	05-Feb-26	09-Feb-26
CON-4000	Install Electrical Panels - 1st Floor	5	16-Mar-26	20-Mar-26
CON-5290	Rough-in Power Conduits & Wires - 1st Floor	5	05-Jun-26	11-Jun-26
CON-5470	Rough-in Low Voltage Conduits & Wires - 1st Floor	5	12-Jun-26	18-Jun-26
CON-6100	Install Lighting Fixtures - 1st Floor	7	03-Aug-26	11-Aug-26
CON-6160	Install Data & Video Intercome Systems - 1st Floor	7	12-Aug-26	20-Aug-26
CON-6220	Install Voice Systems Components - 1st Floor	7	21-Aug-26	31-Aug-26
CON-6260	Install Public Address and Clock Systems Components - 1st Floor	7	01-Sep-26	10-Sep-26
CON-6280	Install Auxiliary Signal System Components - 1st Floor	7	11-Sep-26	21-Sep-26
CON-6290	Install Intrusion Alarm System Components - 1st Floor	7	22-Sep-26	30-Sep-26

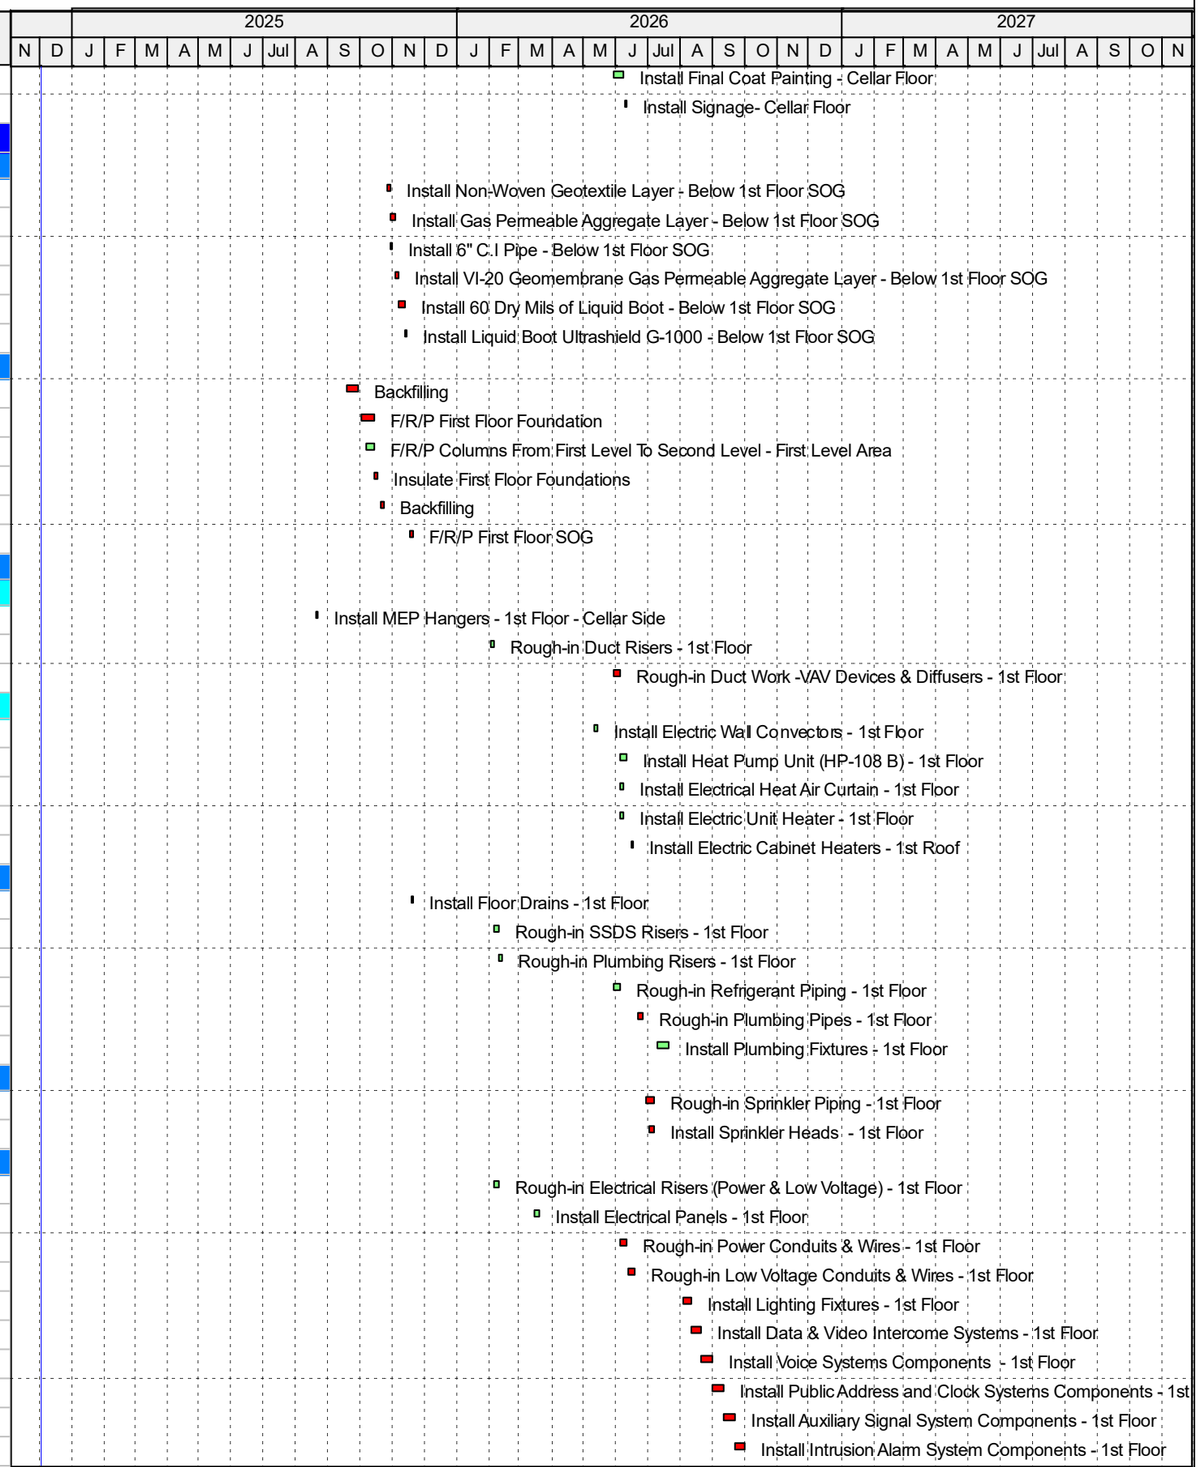

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

TECHNICO CONSTRUCTION PROJECTS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-6300	Install IPDVS System Components - 1st Floor	12	01-Oct-26	19-Oct-26
CON-6310	Install Fire Alarm Devices - 1st Floor	7	20-Oct-26	28-Oct-26
Architecture-1st Floor		63	05-Jun-26	03-Sep-26
Interior Walls-1st Floor		15	05-Jun-26	26-Jun-26
CON-5240	Layout - 1st Floor	2	05-Jun-26	08-Jun-26
CON-5300	Install Top & Bottom Tracks - 1st Floor	2	09-Jun-26	10-Jun-26
CON-5310	Install CMU - 1st Floor	3	09-Jun-26	11-Jun-26
CON-5450	Install Steel Studs - 1st Floor	4	11-Jun-26	16-Jun-26
CON-5500	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 1st Floor	7	17-Jun-26	26-Jun-26
Ceiling-1st Floor		12	07-Jul-26	22-Jul-26
CON-5810	Install Ceiling Hangers - 1st Floor	5	07-Jul-26	13-Jul-26
CON-5920	Install Gypsum Board Ceiling - 1st Floor	7	14-Jul-26	22-Jul-26
CON-5930	Install Acoustical Ceiling Tiles - 1st Floor	7	14-Jul-26	22-Jul-26
CON-5940	Install Wood Slat Ceiling - 1st Floor	7	14-Jul-26	22-Jul-26
CON-5950	MCP-Wood Slat Ceiling Panel - 1st Floor	7	14-Jul-26	22-Jul-26
Finishes-1st Floor		48	29-Jun-26	03-Sep-26
CON-4910	Install Doors- 1st Floor	3	29-Jun-26	01-Jul-26
CON-6030	Install First Coat Painting - 1st Floor	7	23-Jul-26	31-Jul-26
CON-6090	Install Flooring - 1st Floor	7	03-Aug-26	11-Aug-26
CON-6110	Install Milling Work - 1st Floor	7	03-Aug-26	11-Aug-26
CON-6170	Install Furniture - 1st Floor	7	12-Aug-26	20-Aug-26
CON-6230	Install Final Coat Painting - 1st Floor	7	21-Aug-26	31-Aug-26
CON-6270	Install Signage - 1st Floor	3	01-Sep-26	03-Sep-26
Second Floor		178	21-Nov-25	07-Aug-26
Structure-2nd Floor		8	21-Nov-25	03-Dec-25
CON-1400	F/R/P Concrete Slab - 2nd Floor	5	21-Nov-25	28-Nov-25
CON-1430	F/R/P Columns & Shear Walls From Second Floor To Third Floor	3	01-Dec-25	03-Dec-25
Mechanical-2nd Floor		125	26-Nov-25	27-May-26
HVAC Rough-ins-2nd Floor		43	26-Nov-25	29-Jan-26
CON-1410	Install MEP Hangers - 2nd Floor	2	26-Nov-25	28-Nov-25
CON-1800	Rough-in Duct Risers - 2nd Floor	3	14-Jan-26	16-Jan-26
CON-2130	Rough-in Duct Work -VAV Devices & Diffusers - 2nd Floor	5	23-Jan-26	29-Jan-26
Mechanical Equipment-2nd Floor		82	30-Jan-26	27-May-26
CON-2380	Install AC-204 - 2nd Floor	3	30-Jan-26	03-Feb-26
CON-4720	Install Electric Wall Convectors - 2nd Floor	3	29-Apr-26	01-May-26
CON-5080	Install Electric Cabinet Heaters - 2nd Floor	3	22-May-26	27-May-26
Plumbing-2nd Floor		133	26-Nov-25	08-Jun-26
CON-1420	Install Floor Drains - 2nd Floor	2	26-Nov-25	28-Nov-25
CON-1930	Rough-in SSDS Risers - 2nd Floor	3	20-Jan-26	22-Jan-26
CON-2040	Rough-in Refrigerant Piping - 2nd Floor	5	22-Jan-26	28-Jan-26
CON-2180	Rough-in Plumbing Risers - 2nd Floor	3	23-Jan-26	27-Jan-26
CON-2970	Rough-in Plumbing Pipes - 2nd Floor	5	13-Feb-26	20-Feb-26
CON-5180	Install Plumbing Fixtures - 2nd Floor	7	29-May-26	08-Jun-26
Electrical-2nd Floor		140	20-Jan-26	07-Aug-26
CON-1910	Rough-in Electrical Risers (Power & Low Voltage) - 2nd Floor	3	20-Jan-26	22-Jan-26
CON-2400	Rough-in Power Conduits & Wires - 2nd Floor	5	30-Jan-26	05-Feb-26
CON-2700	Rough-in Low Voltage Conduits & Wires - 2nd Floor	5	06-Feb-26	12-Feb-26
CON-2980	Install Electrical Panels - 2nd Floor	5	13-Feb-26	20-Feb-26
CON-5020	Install Lighting Fixtures - 2nd Floor	7	19-May-26	28-May-26



Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone


TECHNICO CONSTRUCTION PROJECTS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-5160	Install Data & Video Intercome Systems - 2nd Floor	7	29-May-26	08-Jun-26
CON-5360	Install Voice Systems Components - 2nd Floor	7	09-Jun-26	17-Jun-26
CON-5570	Install Public Address and Clock Systems Components - 2nd Floor	7	18-Jun-26	29-Jun-26
CON-5730	Install Auxiliary Signal System Components - 2nd Floor	7	30-Jun-26	09-Jul-26
CON-5870	Install Intrusion Alarm System Components - 2nd Floor	7	10-Jul-26	20-Jul-26
CON-6000	Install IPDVS System Components - 2nd Floor	7	21-Jul-26	29-Jul-26
CON-6080	Install Fire Alarm Devices - 2nd Floor	7	30-Jul-26	07-Aug-26
Fire Protection-2nd Floor		5	23-Feb-26	27-Feb-26
CON-3270	Rough-in Sprinkler Piping - 2nd Floor	5	23-Feb-26	27-Feb-26
CON-3330	Install Sprinkler Heads - 2nd Floor	2	26-Feb-26	27-Feb-26
Architecture-2nd Floor		109	13-Jan-26	17-Jun-26
Interior Walls-2nd Floor		74	13-Jan-26	28-Apr-26
CON-1750	Layout - 2nd Floor	2	13-Jan-26	14-Jan-26
CON-1840	Install Top & Bottom Tracks - 2nd Floor	2	15-Jan-26	16-Jan-26
CON-1870	Install CMU - 2nd Floor	3	16-Jan-26	21-Jan-26
CON-2360	Install Steel Studs - 2nd Floor	4	30-Jan-26	04-Feb-26
CON-4580	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gypsum Board - 2nd Floor	7	20-Apr-26	28-Apr-26
Ceiling-2nd Floor		49	02-Mar-26	07-May-26
CON-3380	Install Ceiling Hangers - 2nd Floor	5	02-Mar-26	06-Mar-26
CON-4700	Install Acoustical Ceiling Tiles - 2nd Floor	7	29-Apr-26	07-May-26
CON-4710	Install Gypsum Board Ceiling - 2nd Floor	7	29-Apr-26	07-May-26
Finishes-2nd Floor		39	23-Apr-26	17-Jun-26
CON-4640	Install Doors- 2nd Floor	3	23-Apr-26	27-Apr-26
CON-4880	Install First Coat Painting - 2nd Floor	7	08-May-26	18-May-26
CON-5000	Install Flooring - 2nd Floor	7	19-May-26	28-May-26
CON-5060	Install Milling Work - 2nd Floor	7	19-May-26	28-May-26
CON-5220	Install Furniture - 2nd Floor	7	29-May-26	08-Jun-26
CON-5400	Install Final Coat Painting - 2nd Floor	7	09-Jun-26	17-Jun-26
CON-5480	Install Signage - 2nd Floor	3	12-Jun-26	16-Jun-26
Third Floor		177	04-Dec-25	18-Aug-26
Material Hoist		108	11-Dec-25	15-May-26
CON-1480	Install Elevator Hoist Pad	3	11-Dec-25	15-Dec-25
CON-1500	Erect Material Hoist	2	16-Dec-25	17-Dec-25
CON-1530	Drop Test & Sign-Off	2	18-Dec-25	19-Dec-25
CON-4660	Dismantle Hoist	5	27-Apr-26	01-May-26
CON-4780	Demolish Hoist Pad	5	04-May-26	08-May-26
CON-4900	Hoist In-Fill	5	11-May-26	15-May-26
Structure -3rd Floor		8	04-Dec-25	15-Dec-25
CON-1440	F/R/P Concrete Slab - 3rd Floor	5	04-Dec-25	10-Dec-25
CON-1460	F/R/P Columns & Shear Walls From Third Floor To Fourth Floor	3	11-Dec-25	15-Dec-25
Mechanical -3rd Floor		120	09-Dec-25	01-Jun-26
HVAC Rough-ins -3rd Floor		40	09-Dec-25	05-Feb-26
CON-1450	Install MEP Hangers - 3rd Floor	2	09-Dec-25	10-Dec-25
CON-1900	Rough-in Duct Risers - 3rd Floor	3	20-Jan-26	22-Jan-26
CON-2390	Rough-in Duct Work -VAV Devices & Diffusers - 3rd Floor	5	30-Jan-26	05-Feb-26
Mechanical Equipment -3rd Floor		20	04-May-26	01-Jun-26
CON-4770	Install Electric Wall Convectors - 3rd Floor	3	04-May-26	06-May-26
CON-5090	Install Electric Cabinet Heaters - 3rd Floor	3	28-May-26	01-Jun-26
Plumbing -3rd Floor		130	11-Dec-25	17-Jun-26

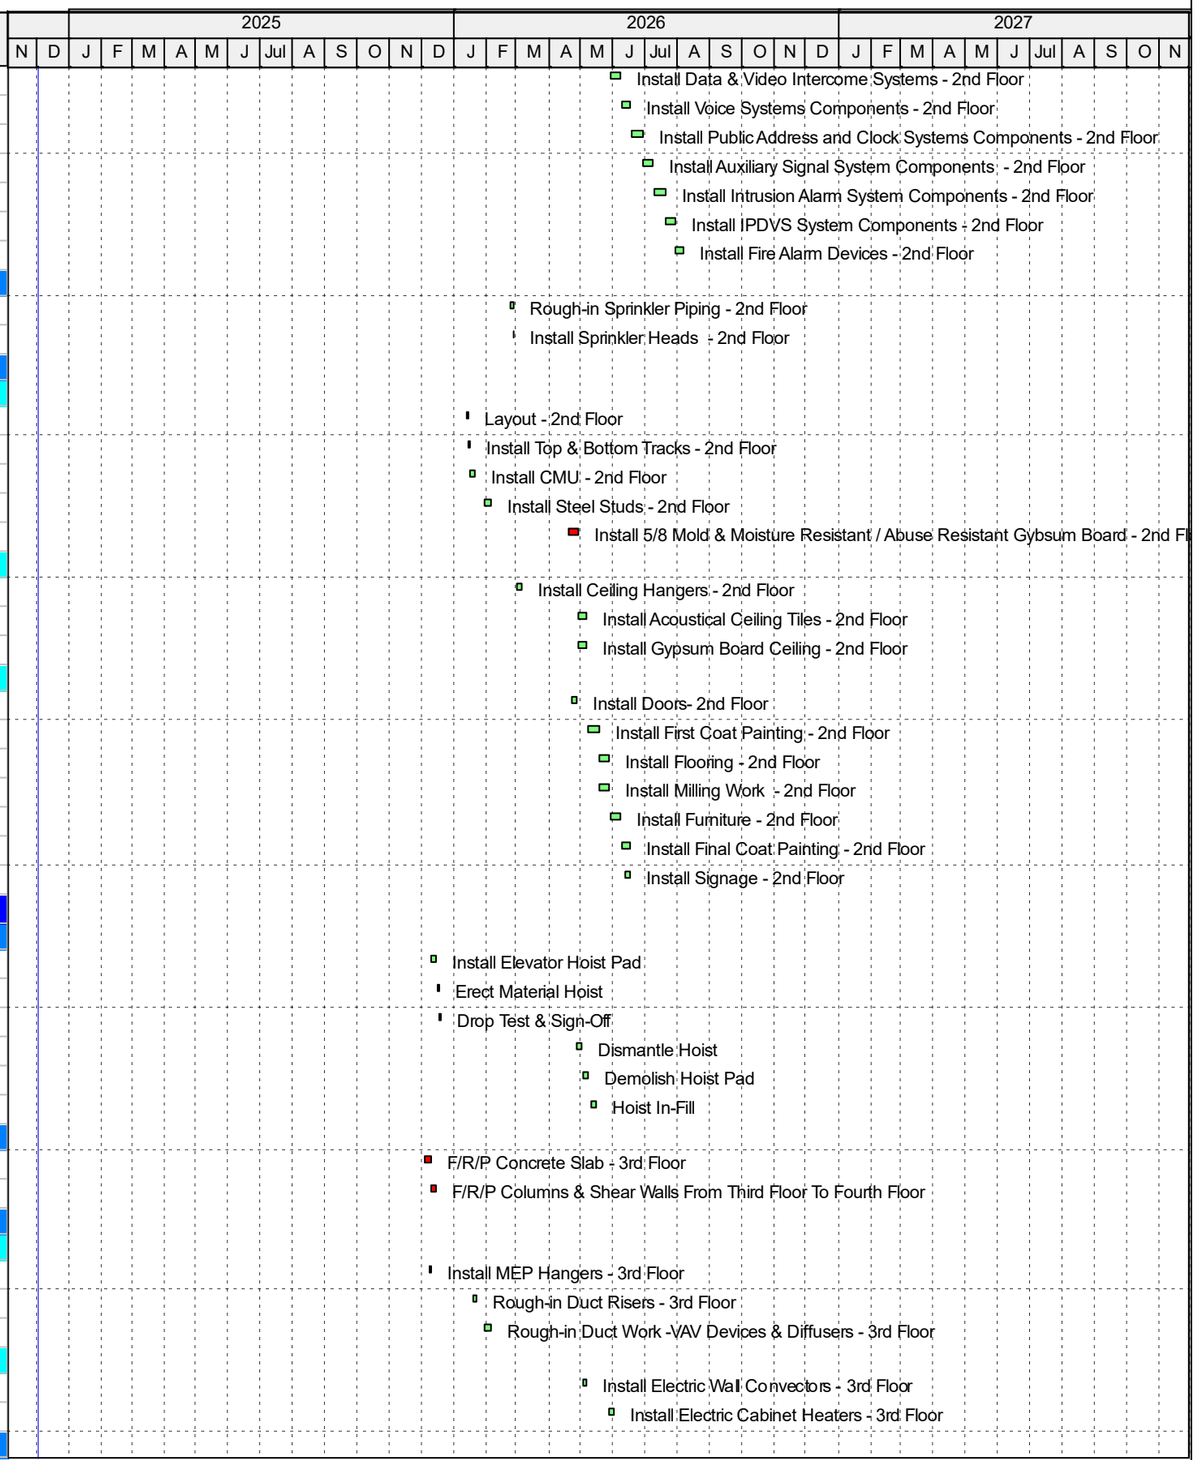

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

TECHNICO CONSTRUCTION PROJECTS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	


Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1470	Install Floor Drains - 3rd Floor	2	11-Dec-25	12-Dec-25
CON-2190	Rough-in SSDS Risers - 3rd Floor	3	23-Jan-26	27-Jan-26
CON-2280	Rough-in Plumbing Risers - 3rd Floor	3	28-Jan-26	30-Jan-26
CON-2330	Rough-in Refrigerant Piping - 3rd Floor	5	29-Jan-26	04-Feb-26
CON-3250	Rough-in Plumbing Pipes - 3rd Floor	5	23-Feb-26	27-Feb-26
CON-5380	Install Plumbing Fixtures - 3rd Floor	7	09-Jun-26	17-Jun-26
Electrical -3rd Floor		144	23-Jan-26	18-Aug-26
CON-2170	Rough-in Electrical Risers (Power & Low Voltage) - 3rd Floor	3	23-Jan-26	27-Jan-26
CON-2690	Rough-in Power Conduits & Wires - 3rd Floor	5	06-Feb-26	12-Feb-26
CON-2950	Rough-in Low Voltage Conduits & Wires - 3rd Floor	5	13-Feb-26	20-Feb-26
CON-3260	Install Electrical Panels - 3rd Floor	5	23-Feb-26	27-Feb-26
CON-5140	Install Lighting Fixtures - 3rd Floor	7	29-May-26	08-Jun-26
CON-5350	Install Data & Video Intercome Systems - 3rd Floor	7	09-Jun-26	17-Jun-26
CON-5560	Install Voice Systems Components - 3rd Floor	7	18-Jun-26	29-Jun-26
CON-5720	Install Public Address and Clock Systems Components - 3rd Floor	7	30-Jun-26	09-Jul-26
CON-5860	Install Auxiliary Signal System Components - 3rd Floor	7	10-Jul-26	20-Jul-26
CON-5990	Install Intrusion Alarm System Components - 3rd Floor	7	21-Jul-26	29-Jul-26
CON-6070	Install IPDVS System Components - 3rd Floor	7	30-Jul-26	07-Aug-26
CON-6150	Install Fire Alarm Devices - 3rd Floor	7	10-Aug-26	18-Aug-26
Fire Protection -3rd Floor		5	02-Mar-26	06-Mar-26
CON-3430	Rough-in Sprinkler Piping - 3rd Floor	5	02-Mar-26	06-Mar-26
CON-3510	Install Sprinkler Heads - 3rd Floor	2	05-Mar-26	06-Mar-26
Architecture -3rd Floor		114	15-Jan-26	29-Jun-26
Interior Walls -3rd Floor		79	15-Jan-26	07-May-26
CON-1830	Layout - 3rd Floor	2	15-Jan-26	16-Jan-26
CON-1890	Install Top & Bottom Tracks - 3rd Floor	2	20-Jan-26	21-Jan-26
CON-2030	Install CMU - 3rd Floor	3	22-Jan-26	26-Jan-26
CON-2670	Install Steel Studs - 3rd Floor	4	06-Feb-26	11-Feb-26
CON-4690	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 3rd Floor	7	29-Apr-26	07-May-26
Ceiling -3rd Floor		51	09-Mar-26	18-May-26
CON-3680	Install Ceiling Hangers - 3rd Floor	5	09-Mar-26	13-Mar-26
CON-4840	Install Gypsum Board Ceiling - 3rd Floor	7	08-May-26	18-May-26
CON-4850	Install Acoustical Ceiling Tiles - 3rd Floor	7	08-May-26	18-May-26
Finishes -3rd Floor		43	28-Apr-26	29-Jun-26
CON-4680	Install Doors- 3rd Floor	3	28-Apr-26	30-Apr-26
CON-5050	Install First Coat Painting - 3rd Floor	7	19-May-26	28-May-26
CON-5110	Install Flooring - 3rd Floor	7	29-May-26	08-Jun-26
CON-5210	Install Milling Work - 3rd Floor	7	29-May-26	08-Jun-26
CON-5420	Install Furniture - 3rd Floor	7	09-Jun-26	17-Jun-26
CON-5510	Install Signage - 3rd Floor	3	17-Jun-26	22-Jun-26
CON-5600	Install Final Coat Painting - 3rd Floor	7	18-Jun-26	29-Jun-26
Fourth Floor		176	16-Dec-25	27-Aug-26
Structure -4th Floor		6	16-Dec-25	23-Dec-25
CON-1490	F/R/P Concrete Slab - 4th Floor	4	16-Dec-25	19-Dec-25
CON-1550	F/R/P Concrete Columns From Fourth Slab to Lower Roof Slab- 4th Floor	2	22-Dec-25	23-Dec-25
Mechanical-4th Floor		116	18-Dec-25	04-Jun-26
HVAC Rough-ins-4th Floor		38	18-Dec-25	12-Feb-26
CON-1510	Install MEP Hangers - 4th Floor	2	18-Dec-25	19-Dec-25
CON-2150	Rough-in Duct Risers - 4th Floor	3	23-Jan-26	27-Jan-26



Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2680	Rough-in Duct Work -VAV Devices & Diffusers - 4th Floor	5	06-Feb-26	12-Feb-26
Mechanical Equipment-4th Floor		78	13-Feb-26	04-Jun-26
CON-2910	Install AC-412 - 4th Floor	3	13-Feb-26	18-Feb-26
CON-4810	Install Electric Wal l Convectors - 4th Floor	3	07-May-26	11-May-26
CON-5230	Install Electric Cabinet Heaters - 4th Floor	3	02-Jun-26	04-Jun-26
Plumbing-4th Floor		132	18-Dec-25	29-Jun-26
CON-1520	Install Floor Drains - 4th Floor	2	18-Dec-25	19-Dec-25
CON-2290	Rough-in SSDS Risers - 4th Floor	3	28-Jan-26	30-Jan-26
CON-2480	Rough-in Plumbing Risers - 4th Floor	3	02-Feb-26	04-Feb-26
CON-2590	Rough-in Refrigerant Piping - 4th Floor	5	05-Feb-26	11-Feb-26
CON-3410	Rough-in Plumbing Pipes - 4th Floor	5	02-Mar-26	06-Mar-26
CON-5590	Install Plumbing Fixtures - 4th Floor	7	18-Jun-26	29-Jun-26
Electrical-4th Floor		148	28-Jan-26	27-Aug-26
CON-2270	Rough-in Electrical Risers (Power & Low Voltage) - 4th Floor	3	28-Jan-26	30-Jan-26
CON-2940	Rough-in Power Conduits & Wires - 4th Floor	5	13-Feb-26	20-Feb-26
CON-3240	Rough-in Low Voltage Conduits & Wires - 4th Floor	5	23-Feb-26	27-Feb-26
CON-3420	Install Electrical Panels - 4th Floor	5	02-Mar-26	06-Mar-26
CON-5330	Install Lighting Fixtures - 4th Floor	7	09-Jun-26	17-Jun-26
CON-5550	Install Data & Video Intercome Systems - 4th Floor	7	18-Jun-26	29-Jun-26
CON-5710	Install Voice Systems Components - 4th Floor	7	30-Jun-26	09-Jul-26
CON-5850	Install Public Address and Clock Systems Components - 4th Floor	7	10-Jul-26	20-Jul-26
CON-5980	Install Auxiliary Signal System Components - 4th Floor	7	21-Jul-26	29-Jul-26
CON-6060	Install Intrusion Alarm System Components - 4th Floor	7	30-Jul-26	07-Aug-26
CON-6140	Install IPDVS System Components - 4th Floor	7	10-Aug-26	18-Aug-26
CON-6210	Install Fire Alarm Devices - 4th Floor	7	19-Aug-26	27-Aug-26
Fire Protection-4th Floor		5	09-Mar-26	13-Mar-26
CON-3720	Rough-in Sprinkler Piping - 4th Floor	5	09-Mar-26	13-Mar-26
CON-3900	Install Sprinkler Heads - 4th Floor	2	12-Mar-26	13-Mar-26
Architecture-4th Floor		119	20-Jan-26	09-Jul-26
Interior Walls-4th Floor		84	20-Jan-26	18-May-26
CON-1880	Layout - 4th Floor	2	20-Jan-26	21-Jan-26
CON-2020	Install Top & Bottom Tracks - 4th Floor	2	22-Jan-26	23-Jan-26
CON-2230	Install CMU - 4th Floor	3	27-Jan-26	29-Jan-26
CON-2900	Install Steel Studs - 4th Floor	4	13-Feb-26	19-Feb-26
CON-4830	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 4th Floor	7	08-May-26	18-May-26
Ceiling-4th Floor		53	16-Mar-26	28-May-26
CON-3970	Install Ceiling Hangers - 4th Floor	5	16-Mar-26	20-Mar-26
CON-4970	Install Acoustical Ceiling Tiles - 4th Floor	7	19-May-26	28-May-26
CON-4980	Install Gypsum Board Ceiling- 4th Floor	7	19-May-26	28-May-26
CON-4990	Install TECTUM WOOD Fiber Composition Ceiling Tiles- 4th Floor	7	19-May-26	28-May-26
Finishes-4th Floor		47	01-May-26	09-Jul-26
CON-4750	Install Doors- 4th Floor	3	01-May-26	05-May-26
CON-5190	Install First Coat Painting - 4th Floor	7	29-May-26	08-Jun-26
CON-5320	Install Flooring - 4th Floor	7	09-Jun-26	17-Jun-26
CON-5410	Install Milling Work - 4th Floor	7	09-Jun-26	17-Jun-26
CON-5620	Install Furniture - 4th Floor	7	18-Jun-26	29-Jun-26
CON-5650	Install Signage - 4th Floor	3	23-Jun-26	25-Jun-26
CON-5760	Install Final Coat Painting - 4th Floor	7	30-Jun-26	09-Jul-26
Lower Roof		177	24-Dec-25	08-Sep-26

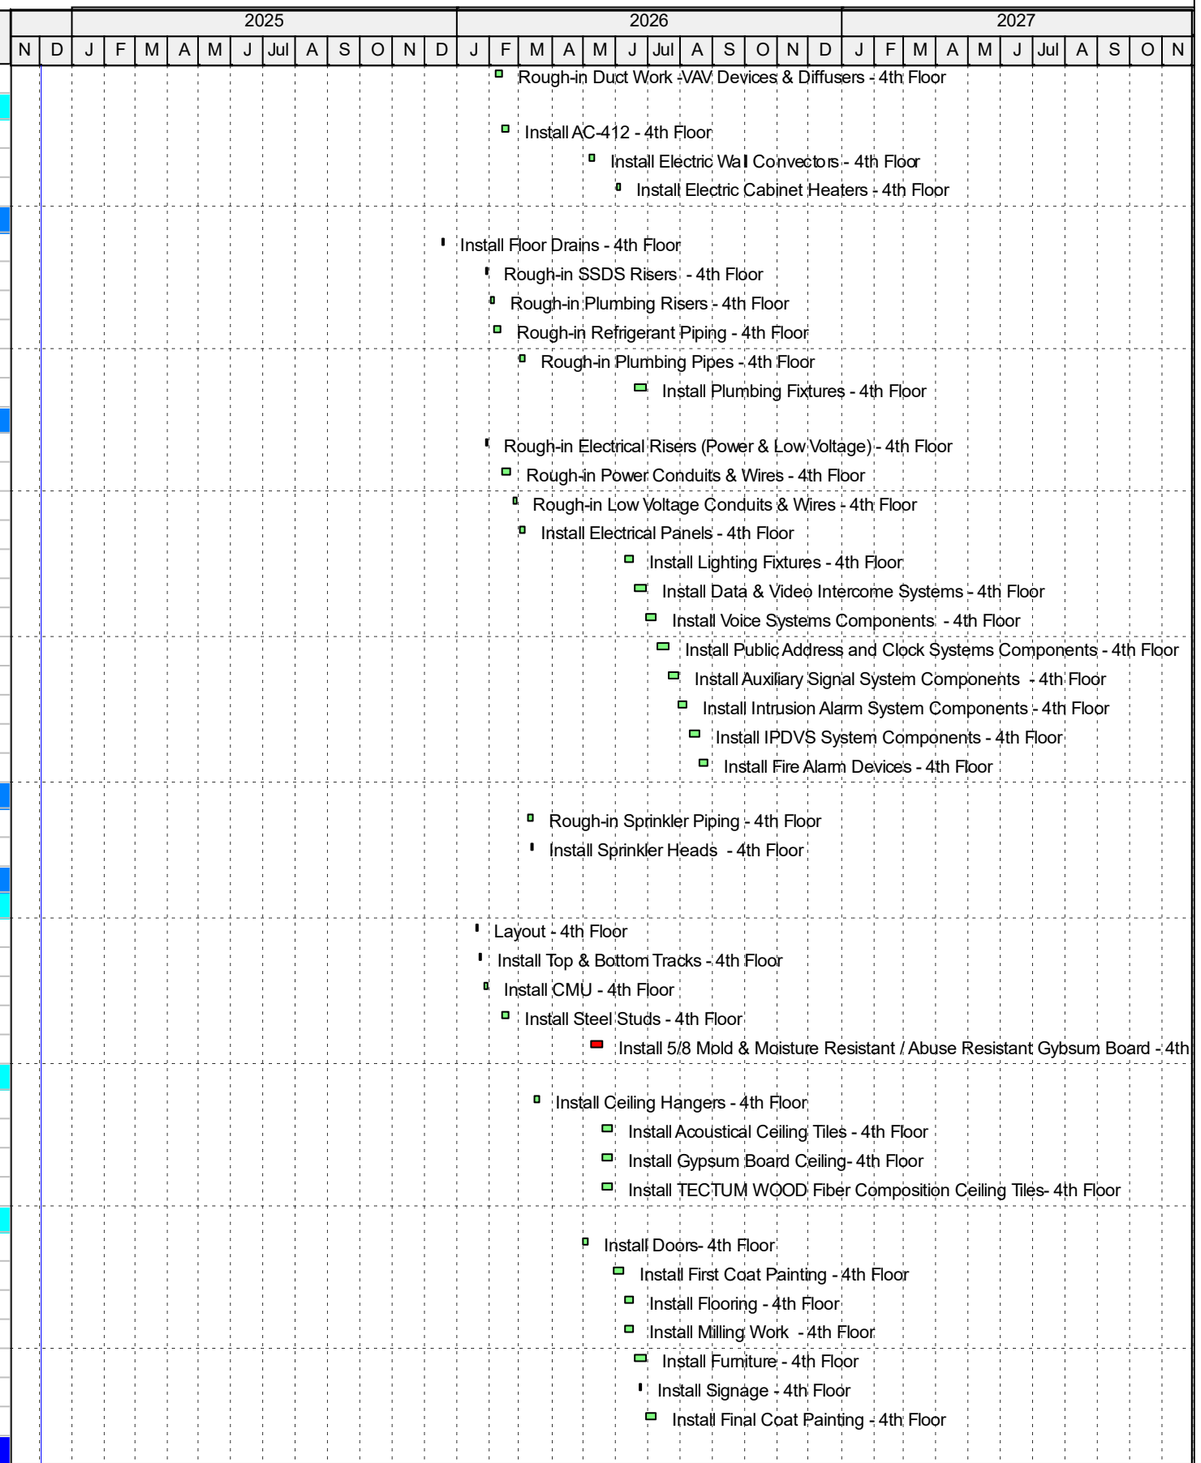

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

IS 082K New Building Design No. 093937 - Baseline Schedule Rev 00

TECHNICO CONSTRUCTION PROJECS

Prepared By: A.A			
Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
Structure -Lower Floor		8	24-Dec-25	06-Jan-26
CON-1560	F/R/P Concrete Slab- Lower Roof	4	24-Dec-25	30-Dec-25
CON-1590	Install Penthouse Posts and Roof Framing	3	31-Dec-25	05-Jan-26
CON-1600	Install Dunnage Framing - Lower Roof	4	31-Dec-25	06-Jan-26
CON-1610	F/R/P Parapets - Lower Roof	3	31-Dec-25	05-Jan-26
Mechanical -Lower Floor		113	29-Dec-25	09-Jun-26
HVAC Rough-ins -Lower Floor		37	29-Dec-25	20-Feb-26
CON-1570	Install MEP Hangers - Lower Roof	2	29-Dec-25	30-Dec-25
CON-2260	Rough-in Duct Risers - Lower Roof	3	28-Jan-26	30-Jan-26
CON-2920	Rough-in Duct Work -VAV Devices & Diffusers - Lower Roof	5	13-Feb-26	20-Feb-26
Mechanical Equipment -Lower Floor		107	07-Jan-26	09-Jun-26
CON-1640	Install RTU-2 - Lower Roof	6	07-Jan-26	14-Jan-26
CON-1650	Install Fans - Lower Roof	4	07-Jan-26	12-Jan-26
CON-3220	Install Electric Unit Heater - Lower Roof	2	23-Feb-26	24-Feb-26
CON-5270	Install Electric Cabinet Heaters - Lower Roof	3	05-Jun-26	09-Jun-26
Plumbing -Lower Floor		133	29-Dec-25	09-Jul-26
CON-1580	Install Floor Drains - Lower Roof	2	29-Dec-25	30-Dec-25
CON-2490	Rough-in SSDS Risers - Lower Roof	3	02-Feb-26	04-Feb-26
CON-2630	Rough-in Plumbing Risers - Lower Roof	3	05-Feb-26	09-Feb-26
CON-2870	Rough-in Refrigerant Piping - Lower Roof	5	12-Feb-26	19-Feb-26
CON-3700	Rough-in Plumbing Pipes - Lower Roof	5	09-Mar-26	13-Mar-26
CON-5750	Install Plumbing Fixtures - Lower Roof	7	30-Jun-26	09-Jul-26
Electrical -Lower Floor		169	07-Jan-26	08-Sep-26
CON-1660	Install Emergency Generator - Lower Roof	10	07-Jan-26	21-Jan-26
CON-2470	Rough-in Electrical Risers (Power & Low Voltage) - Lower Roof	3	02-Feb-26	04-Feb-26
CON-3230	Rough-in Power Conduits & Wires - Lower Roof	5	23-Feb-26	27-Feb-26
CON-3390	Rough-in Low Voltage Conduits & Wires - Lower Roof	5	02-Mar-26	06-Mar-26
CON-3710	Install Electrical Panels - Lower Roof	5	09-Mar-26	13-Mar-26
CON-5530	Install Lighting Fixtures - Lower Roof	7	18-Jun-26	29-Jun-26
CON-5700	Install Data & Video Intercome Systems - Lower Roof	7	30-Jun-26	09-Jul-26
CON-5840	Install Voice Systems Components - Lower Roof	7	10-Jul-26	20-Jul-26
CON-5970	Install Public Address and Clock Systems Components - Lower Roof	7	21-Jul-26	29-Jul-26
CON-6050	Install Auxiliary Signal System Components - Lower Roof	7	30-Jul-26	07-Aug-26
CON-6130	Install Intrusion Alarm System Components - Lower Roof	7	10-Aug-26	18-Aug-26
CON-6200	Install IPDVS System Components - Lower Roof	7	19-Aug-26	27-Aug-26
CON-6240	Install Fire Alarm Devices - Lower Roof	7	28-Aug-26	08-Sep-26
Fire Protection -Lower Floor		5	16-Mar-26	20-Mar-26
CON-4010	Rough-in Sprinkler Piping - Lower Roof	5	16-Mar-26	20-Mar-26
CON-4120	Install Sprinkler Heads - Lower Roof	2	19-Mar-26	20-Mar-26
Architecture -Lower Floor		124	22-Jan-26	20-Jul-26
Interior Walls -Lower Floor		89	22-Jan-26	28-May-26
CON-2010	Layout - Lower Roof	2	22-Jan-26	23-Jan-26
CON-2200	Install Top & Bottom Tracks - Lower Roof	2	26-Jan-26	27-Jan-26
CON-2370	Install CMU - Lower Roof	3	30-Jan-26	03-Feb-26
CON-3200	Install Steel Studs - Lower Roof	4	23-Feb-26	26-Feb-26
CON-4960	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gypsum Board - Lower Roof	7	19-May-26	28-May-26
Ceiling -Lower Floor		55	23-Mar-26	08-Jun-26
CON-4200	Install Ceiling Hangers - Lower Roof	5	23-Mar-26	27-Mar-26
CON-5100	Install Gypsum Board Ceiling - Lower Roof	7	29-May-26	08-Jun-26



Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

IS 082K New Building Design No. 093937 - Baseline Schedule Rev 00

TECHNICO CONSTRUCTION PROJECS

Prepared By: A.A			
Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
Finishes -Lower Floor		51	06-May-26	20-Jul-26
CON-4800	Install Doors- Lower Roof	3	06-May-26	08-May-26
CON-5390	Install First Coat Painting - Lower Roof	7	09-Jun-26	17-Jun-26
CON-5520	Install Flooring - Lower Roof	7	18-Jun-26	29-Jun-26
CON-5610	Install Milling Work - Lower Roof	7	18-Jun-26	29-Jun-26
CON-5660	Install Signage - Lower Roof	3	26-Jun-26	30-Jun-26
CON-5770	Install Furniture - Lower Roof	7	30-Jun-26	09-Jul-26
CON-5900	Install Final Coat Painting - Lower Roof	7	10-Jul-26	20-Jul-26
Upper Roof		122	22-Dec-25	16-Jun-26
Structure -Roof Floor		19	22-Dec-25	20-Jan-26
CON-1540	Install Mainroof Posts and Framing	7	22-Dec-25	31-Dec-25
CON-1620	F/R/P Concrete Deck Slab - Upper Roof	5	02-Jan-26	08-Jan-26
CON-1710	Install Dunnage Framing - Upper Roof	7	09-Jan-26	20-Jan-26
CON-1730	F/R/P Parapets - Upper Roof	3	09-Jan-26	13-Jan-26
Mechanical-Roof Floor		112	07-Jan-26	16-Jun-26
CON-1670	Install MEP Hangers - Upper Roof	2	07-Jan-26	08-Jan-26
CON-1680	Install Floor Drains - Upper Roof	2	07-Jan-26	08-Jan-26
CON-1970	Install RTU-1 - Upper Roof	6	21-Jan-26	28-Jan-26
CON-1980	Install RTU-3 - Upper Roof	6	21-Jan-26	28-Jan-26
CON-1990	Install RTU-4 - Upper Roof	6	21-Jan-26	28-Jan-26
CON-2000	Install Fans - Upper Roof	4	21-Jan-26	26-Jan-26
CON-5440	Install Electric Cabinet Heaters - Upper Roof	3	10-Jun-26	12-Jun-26
CON-5460	Install Heat Pump Unit (HP-R02) - Roof	4	11-Jun-26	16-Jun-26
Bulkhead		4	09-Jan-26	14-Jan-26
Structure-Bulkhead		4	09-Jan-26	14-Jan-26
CON-1700	F/R/P Columns and Slab of The Bulkheads	4	09-Jan-26	14-Jan-26
Elevations		43	14-Jan-26	17-Mar-26
West Elevation		25	29-Jan-26	05-Mar-26
CON-2320	Install Scaffolding - West Elevation	2	29-Jan-26	30-Jan-26
CON-2440	Scaffolding Inspection & Sign-Off - West Elevation	2	02-Feb-26	03-Feb-26
CON-2580	Install 5/8 Sheathing - West Elevation	3	04-Feb-26	06-Feb-26
CON-2750	Install 6" Semi-Rigid Mineral Wool System - West Elevation	3	09-Feb-26	11-Feb-26
CON-2840	Install Metal Clip System - West Elevation	2	12-Feb-26	13-Feb-26
CON-2850	Install Brick Veneer - West Elevation	2	12-Feb-26	13-Feb-26
CON-2860	Install Window Frames & Windows / Storefronts - West Elevation	3	12-Feb-26	17-Feb-26
CON-3000	Install Graffiti Resistant Coating At Brick - West Elevation	2	17-Feb-26	18-Feb-26
CON-3030	Install Terra Cotta Panel Rainscreen - West Elevation	6	18-Feb-26	25-Feb-26
CON-3320	Paint Exterior Elevation @ Window Sections - West Elevation	2	26-Feb-26	27-Feb-26
CON-3360	Scaffolding Removal Inspection & Sign-Off - West Elevation	2	02-Mar-26	03-Mar-26
CON-3460	Dismantle Scaffolding - West Elevation	2	04-Mar-26	05-Mar-26
South Elevation		37	23-Jan-26	17-Mar-26
CON-2080	Install Scaffolding - South Elevation	4	23-Jan-26	28-Jan-26
CON-2310	Scaffolding Inspection & Sign-Off -South Elevation	2	29-Jan-26	30-Jan-26
CON-2430	Install 5/8 Sheathing -South Elevation	4	02-Feb-26	05-Feb-26
CON-2660	Install 6" Semi-Rigid Mineral Wool System -South Elevation	4	06-Feb-26	11-Feb-26
CON-2810	Install Metal Clip System -South Elevation	2	12-Feb-26	13-Feb-26
CON-2820	Install Brick Veneer -South Elevation	3	12-Feb-26	17-Feb-26
CON-2830	Install Window Frames & Windows / Storefronts -South Elevation	5	12-Feb-26	19-Feb-26
CON-3020	Install Graffiti Resistant Coating At Brick -South Elevation	2	18-Feb-26	19-Feb-26



Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3140	Install Terra Cotta Panel Rainscreen -South Elevation	10	20-Feb-26	05-Mar-26
CON-3150	Install Wall Speakers -South Elevation	2	20-Feb-26	23-Feb-26
CON-3600	Paint Exterior Elevation @ Window Sections -South Elevation	3	06-Mar-26	10-Mar-26
CON-3790	Scaffolding Removal Inspection & Sign-Off -South Elevation	2	11-Mar-26	12-Mar-26
CON-3940	Dismantle Scaffolding -South Elevation	3	13-Mar-26	17-Mar-26
East Elevation		25	21-Jan-26	25-Feb-26
CON-1950	Install Scaffolding - East Elevation	2	21-Jan-26	22-Jan-26
CON-2070	Scaffolding Inspection & Sign-Off - East Elevation	2	23-Jan-26	26-Jan-26
CON-2210	Install 5/8 Sheathing - East Elevation	3	27-Jan-26	29-Jan-26
CON-2350	Install 6" Semi-Rigid Mineral Wool System - East Elevation	3	30-Jan-26	03-Feb-26
CON-2550	Install Metal Clip System - East Elevation	2	04-Feb-26	05-Feb-26
CON-2560	Install Brick Veneer - East Elevation	2	04-Feb-26	05-Feb-26
CON-2570	Install Window Frames & Windows / Storefronts - East Elevation	3	04-Feb-26	06-Feb-26
CON-2650	Install Graffiti Resistant Coating At Brick - East Elevation	2	06-Feb-26	09-Feb-26
CON-2740	Install Terra Cotta Panel Rainscreen - East Elevation	6	09-Feb-26	17-Feb-26
CON-3010	Paint Exterior Elevation @ Window Sections - East Elevation	2	18-Feb-26	19-Feb-26
CON-3130	Scaffolding Removal Inspection & Sign-Off - East Elevation	2	20-Feb-26	23-Feb-26
CON-3280	Dismantle Scaffolding - East Elevation	2	24-Feb-26	25-Feb-26
North Elevation		37	14-Jan-26	09-Mar-26
CON-1780	Install Scaffolding - North Elevation	4	14-Jan-26	20-Jan-26
CON-1940	Scaffolding Inspection & Sign-Off -North Elevation	2	21-Jan-26	22-Jan-26
CON-2060	Install 5/8 Sheathing -North Elevation	4	23-Jan-26	28-Jan-26
CON-2300	Install 6" Semi-Rigid Mineral Wool System -North Elevation	4	29-Jan-26	03-Feb-26
CON-2520	Install Metal Clip System -North Elevation	2	04-Feb-26	05-Feb-26
CON-2530	Install Brick Veneer -North Elevation	3	04-Feb-26	06-Feb-26
CON-2540	Install Window Frames & Windows / Storefronts -North Elevation	5	04-Feb-26	10-Feb-26
CON-2730	Install Graffiti Resistant Coating At Brick -North Elevation	2	09-Feb-26	10-Feb-26
CON-2790	Install Terra Cotta Panel Rainscreen -North Elevation	10	11-Feb-26	25-Feb-26
CON-2800	Install Exterior Wall Lights -North Elevation	2	11-Feb-26	12-Feb-26
CON-3310	Paint Exterior Elevation @ Window Sections -North Elevation	3	26-Feb-26	02-Mar-26
CON-3440	Scaffolding Removal Inspection & Sign-Off -North Elevation	2	03-Mar-26	04-Mar-26
CON-3500	Dismantle Scaffolding -North Elevation	3	05-Mar-26	09-Mar-26
Roofing		64	07-Jan-26	08-Apr-26
Lower Roof		48	07-Jan-26	17-Mar-26
CON-1630	Pour Concrete Topping Slab	3	07-Jan-26	09-Jan-26
CON-1740	Install Hot Fluid-Applied Rubberized Asphalt Fabric-Reinforced Roofing Membrane	4	12-Jan-26	15-Jan-26
CON-1860	Install Fabric Reinforcing Sheet	4	16-Jan-26	22-Jan-26
CON-2090	Install Protection Sheet and Roof Barrier	3	23-Jan-26	27-Jan-26
CON-2250	Install 1/2" Drainage Panel	3	28-Jan-26	30-Jan-26
CON-2450	Install 8" Roof Insulation (R-40 Min) Multi-Layered and Staggered	5	02-Feb-26	06-Feb-26
CON-2760	Install Filter Fabric	3	09-Feb-26	11-Feb-26
CON-2880	Lower Roofing Testing	5	12-Feb-26	19-Feb-26
CON-3160	Install Air Layer	2	20-Feb-26	23-Feb-26
CON-3170	Install Paver Pedestal System	5	20-Feb-26	26-Feb-26
CON-3290	Install Mineral Water Retention Layer	4	24-Feb-26	27-Feb-26
CON-3340	Install Concrete Pavers	7	27-Feb-26	09-Mar-26
CON-3370	Install 18" Wide Filter Fabric Strip	2	02-Mar-26	03-Mar-26
CON-3470	Install Extensive Growing Media	5	04-Mar-26	10-Mar-26



Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3800	Install Sedum Mat	5	11-Mar-26	17-Mar-26
Upper Roof		55	21-Jan-26	08-Apr-26
CON-1960	Pour Concrete Topping Slab	4	21-Jan-26	26-Jan-26
CON-2220	Install Hot Fluid-Applied Rubberized Asphalt Fabric-Reinforced Roofing Membrane	5	27-Jan-26	02-Feb-26
CON-2510	Install Fabric Reinforcing Sheet	4	03-Feb-26	06-Feb-26
CON-2770	Install Protection Sheet and Roof Barrier	4	09-Feb-26	12-Feb-26
CON-2890	Install 1/2" Drainage Panel	4	13-Feb-26	19-Feb-26
CON-3180	Install 8" Roof Insulation (R-40 Min) Multi-Layered and Staggered	5	20-Feb-26	26-Feb-26
CON-3350	Install Filter Fabric	3	27-Feb-26	03-Mar-26
CON-3490	Upper Roofing Testing	2	04-Mar-26	05-Mar-26
CON-3610	Install Air Layer	3	06-Mar-26	10-Mar-26
CON-3620	Install Paver Pedestal System	6	06-Mar-26	13-Mar-26
CON-3810	Install Mineral Water Retention Layer	5	11-Mar-26	17-Mar-26
CON-3960	Install Concrete Pavers	8	16-Mar-26	25-Mar-26
CON-4060	Install 18" Wide Filter Fabric Strip	3	18-Mar-26	20-Mar-26
CON-4190	Install Extensive Growing Media	6	23-Mar-26	30-Mar-26
CON-4320	Install Sedum Mat	7	31-Mar-26	08-Apr-26
Special Rooms		146	30-Jan-26	27-Aug-26
Electrical Service Room -Cellar Floor		38	30-Jan-26	25-Mar-26
CON-2420	Install Service End Box	4	30-Jan-26	04-Feb-26
CON-2610	Install Switch Boards (SWBD-1, SWBD-2, SWBD-3)	10	05-Feb-26	19-Feb-26
CON-2620	Install Fire Alarm Fused Disconnect Switch	3	05-Feb-26	09-Feb-26
CON-3190	Install Main Service Switch Board (MSS#1 & MSS#2)	8	20-Feb-26	03-Mar-26
CON-3480	Install TAP Section	3	04-Mar-26	06-Mar-26
CON-3690	Install Dry-Type Transformer	6	09-Mar-26	16-Mar-26
CON-4020	Install 2 Current Transformers (C/T)	4	17-Mar-26	20-Mar-26
CON-4210	Install Power and Lighting Panels	3	23-Mar-26	25-Mar-26
Fuel TankRoom-Cellar Floor		25	13-Feb-26	20-Mar-26
CON-2930	F/R/P Concrete Pads - Fuel Tank Room	3	13-Feb-26	18-Feb-26
CON-3040	Install Fuel Oil Transfer Pump (FP-1) - Fuel Tank Room	4	19-Feb-26	24-Feb-26
CON-3300	Install Fuel Oil Filtration System (FFS-1) - Fuel Tank Room	4	25-Feb-26	02-Mar-26
CON-3450	Install 275 GAL NYC Fuel Tank With 200% Secondary Containment	6	03-Mar-26	10-Mar-26
CON-3820	Install Fuel Oil Pipings	3	11-Mar-26	13-Mar-26
CON-3980	Install 55 GAL Spill Tank with Sensor Alarm	3	16-Mar-26	18-Mar-26
CON-4100	Install Oil Leak Detector CAC	2	19-Mar-26	20-Mar-26
Water Meter Room -Cellar		8	13-Feb-26	25-Feb-26
CON-2960	Install Main Ground Bus	3	13-Feb-26	18-Feb-26
CON-3050	Install Domestic Water Booster Pump (DWBP-1)	5	19-Feb-26	25-Feb-26
CON-3060	Install Sprinkler Booster Panel	3	19-Feb-26	23-Feb-26
CON-3070	Install Jockey Pump	3	19-Feb-26	23-Feb-26
CON-3080	Install Water Filter Devices	3	19-Feb-26	23-Feb-26
CON-3090	Install Domestic Cold Water Booster Pump (DWBP-1)	4	19-Feb-26	24-Feb-26
CON-3100	Install Duplex Sewage Ejector Pump (SE-1)	4	19-Feb-26	24-Feb-26
CON-3110	Install Sprinkler Booster Pumps	4	19-Feb-26	24-Feb-26
Elevator Machine Room -Lower Roof		26	02-Mar-26	06-Apr-26
CON-3400	Install EMR Panel	4	02-Mar-26	05-Mar-26
CON-3640	Install Elevator Machines	10	06-Mar-26	19-Mar-26
CON-4150	Install Elevator Controls	6	20-Mar-26	27-Mar-26



Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

TECHNICO CONSTRUCTION PROJECTS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-4280	Install Elevator Cabinets	6	30-Mar-26	06-Apr-26
MDF Room 2nd Floor		42	29-May-26	29-Jul-26
CON-5150	Install Voice Cabinet	7	29-May-26	08-Jun-26
CON-5340	Install Data Equipment Rack	7	09-Jun-26	17-Jun-26
CON-5540	Install Data Cabinet Patch Panel Rack	7	18-Jun-26	29-Jun-26
CON-5690	Install Vertical Wire Manager	7	30-Jun-26	09-Jul-26
CON-5910	Install MDF Telephone System Backboard	7	10-Jul-26	20-Jul-26
CON-6020	Install Telecom Panel	7	21-Jul-26	29-Jul-26
Gymnatorium - 4th Floor		25	18-Jun-26	24-Jul-26
CON-5630	Install Gym Flooring	10	18-Jun-26	02-Jul-26
CON-5800	Install Gym Equipment	15	06-Jul-26	24-Jul-26
R01 - HVAC/ELEC. Penthouse - Lower Roof		35	06-Mar-26	23-Apr-26
CON-3630	Install Power Panels	4	06-Mar-26	11-Mar-26
CON-3890	Install Bacnet Data Enclosure	6	12-Mar-26	19-Mar-26
CON-4140	Install Switch Boards (SWBD-4, SWBD-5)	4	20-Mar-26	25-Mar-26
CON-4250	Install Secondary Transformer Disconnect Switch (MSWB-C)	5	26-Mar-26	01-Apr-26
CON-4350	Install Domestic Hot Water Heat Pump (HWHP-1 & HWHP-2)	4	02-Apr-26	07-Apr-26
CON-4410	Install Storage Tank (ST-1)	6	08-Apr-26	15-Apr-26
CON-4560	Install Thermal Expansion Tank (ET-1)	6	16-Apr-26	23-Apr-26
Food Service Room - 1st		15	29-Jun-26	20-Jul-26
CON-5670	Install Hot Water Circulator Pump (CP-1) / (CP-2)	4	29-Jun-26	02-Jul-26
CON-5790	Install Grease Interceptor (GI-1) / (GI-2)	4	06-Jul-26	09-Jul-26
CON-5830	Install Kitchen Equipment	7	10-Jul-26	20-Jul-26
IDF Room - 4th Floor		35	10-Jul-26	27-Aug-26
CON-5820	Install Bacnet Data Enclosure	7	10-Jul-26	20-Jul-26
CON-5960	Install PA Rack	7	21-Jul-26	29-Jul-26
CON-6040	Install Voice Rack	7	30-Jul-26	07-Aug-26
CON-6120	Install Data Rack	7	10-Aug-26	18-Aug-26
CON-6190	Install Voice Cabinet	7	19-Aug-26	27-Aug-26
Mockup Room		24	06-Mar-26	08-Apr-26
CON-3650	Install Walls GWB-Mockup Room	3	06-Mar-26	10-Mar-26
CON-3850	Install Door Frames-Mockup Room	2	11-Mar-26	12-Mar-26
CON-3950	Install Gypsum Board Ceiling -Mockup Room	3	13-Mar-26	17-Mar-26
CON-4070	Install Doors & Hardware-Mockup Room	2	18-Mar-26	19-Mar-26
CON-4160	Paint First coat -Mockup Room	3	20-Mar-26	24-Mar-26
CON-4230	Flooring Finishes-Mockup Room	3	25-Mar-26	27-Mar-26
CON-4290	Paint Second coat-Mockup Room	3	30-Mar-26	01-Apr-26
CON-4360	Install Furniture & Signs -Mockup Room	3	02-Apr-26	06-Apr-26
CON-4390	Mockup Room Inspection & Punchlist	2	07-Apr-26	08-Apr-26
Site Work		69	06-Mar-26	11-Jun-26
14th Avenue Street		20	18-Mar-26	14-Apr-26
CON-4050	Install Traffic Control Devices - 14th Avenue	1	18-Mar-26	18-Mar-26
CON-4090	Mill & Remove Existing Asphalt Pavement - 14th Avenue	2	19-Mar-26	20-Mar-26
CON-4180	Excavation For The Full Depth Asphalt Pavement Replacement - 14th Avenue	2	23-Mar-26	24-Mar-26
CON-4220	Install 6-IN Gravel - 14th Avenue	2	25-Mar-26	26-Mar-26
CON-4260	Sawcut & Apply Tack Coat - Before Concrete Base Course - 14th Avenue	2	27-Mar-26	30-Mar-26
CON-4270	Install 6-IN Concrete Base Course - 14th Avenue	2	27-Mar-26	30-Mar-26
CON-4300	Sawcut & Apply Tack Coat - Before Leveling Course - 14th Avenue	2	31-Mar-26	01-Apr-26
CON-4310	Install Leveling Course - 14th Avenue	2	31-Mar-26	01-Apr-26



Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

TECHNICO CONSTRUCTION PROJECTS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-4340	Install 1.5-Inch Asphalt Binder Course - 14th Avenue	2	02-Apr-26	03-Apr-26
CON-4370	Install 1.5-Inch Thick Asphalt Surface Course - 14th Avenue	2	06-Apr-26	07-Apr-26
CON-4400	Install Pavement Markings - 14th Avenue	2	08-Apr-26	09-Apr-26
CON-4430	Remove and Replace Existing Pedestrian Ramps -14th Avenue	2	10-Apr-26	13-Apr-26
CON-4470	Remove Traffic Control Devices - 14th Avenue	1	14-Apr-26	14-Apr-26
63RD Street		24	08-May-26	11-Jun-26
CON-4480	Install Traffic Control Devices - 63rd Street	1	08-May-26	08-May-26
CON-4500	Mill & Remove Existing Asphalt Pavement - 63rd Street	2	11-May-26	12-May-26
CON-4570	Excavation For The Full Depth Asphalt Pavement Replacement - 63rd Street	2	13-May-26	14-May-26
CON-4630	Install 6-IN Gravel - 63rd Street	2	15-May-26	18-May-26
CON-4650	Sawcut & Apply Tack Coat - Before Concrete Base Course - 63rd Street	2	19-May-26	20-May-26
CON-4670	Install 6-IN Concrete Base Course - 63rd Street	2	21-May-26	22-May-26
CON-4740	Sawcut & Apply Tack Coat - Before Leveling Course - 63rd Street	2	26-May-26	27-May-26
CON-4760	Install Leveling Course - 63rd Street	2	28-May-26	29-May-26
CON-4790	Install 1.5-Inch Asphalt Binder Course - 63rd Street	2	01-Jun-26	02-Jun-26
CON-4820	Install 1.5-Inch Thick Asphalt Surface Course - 63rd Street	2	03-Jun-26	04-Jun-26
CON-4920	Install Pavement Markings - 63rd Street	2	05-Jun-26	08-Jun-26
CON-4940	Remove and Replace Existing Pedestrian Ramps -63rd Street	2	09-Jun-26	10-Jun-26
CON-4950	Remove Traffic Control Devices - 63rd Street	1	11-Jun-26	11-Jun-26
Building Perimeter		62	06-Mar-26	02-Jun-26
CON-3520	Install Storm Inlet 1	1	06-Mar-26	06-Mar-26
CON-3530	Install Storm Inlet 2	1	06-Mar-26	06-Mar-26
CON-3540	Install 60 LF of 8-IN DIP [Storm Inlet 1 to Storm Inlet 2]	1	06-Mar-26	06-Mar-26
CON-3550	Install Domestic Water Service Piping	3	06-Mar-26	10-Mar-26
CON-3560	Install Sewer Piping	3	06-Mar-26	10-Mar-26
CON-3570	Install Sanitary Piping	3	06-Mar-26	10-Mar-26
CON-3590	Install Telecom Service Point of Entry	3	06-Mar-26	10-Mar-26
CON-3660	Install 33 LF of 8-IN DIP [Storm Inlet 2 to Catch Basin 2]	1	09-Mar-26	09-Mar-26
CON-3670	Install Catch Basin 2	1	09-Mar-26	09-Mar-26
CON-3730	Install Grit Champer-1	2	10-Mar-26	11-Mar-26
CON-3740	Install 106 LF of 12-IN DIP [Catch Basin 2 to Grit Champer-1]	2	10-Mar-26	11-Mar-26
CON-3750	Connect Water Piping To The Existing Water Line	2	11-Mar-26	12-Mar-26
CON-3760	Connect Sewer Piping To The Existing Sewer Line	2	11-Mar-26	12-Mar-26
CON-3770	Connect Sanitary Piping To The Existing Sanitary Line	2	11-Mar-26	12-Mar-26
CON-3780	Verizon To Provide Connection	5	11-Mar-26	17-Mar-26
CON-3860	Install Storm Manhole-2	1	12-Mar-26	12-Mar-26
CON-3870	Install 9-LF of 12-IN DIP [Grit Champer-1 to Storm Manhole-2]	1	12-Mar-26	12-Mar-26
CON-3880	Install 3-LF of 12-IN DIP [Grit Champer-1 to Stormwater Retention System]	1	12-Mar-26	12-Mar-26
CON-3910	Install 10-IN DIP Roof Leader	1	13-Mar-26	13-Mar-26
CON-3920	Install Stormwater Retention System	3	13-Mar-26	17-Mar-26
CON-3930	Install Catch Basin 2	1	13-Mar-26	13-Mar-26
CON-4030	Install 3-LF of 12-IN DIP [Stormwater Retention System to Overflow Storm Manhole-1]	1	18-Mar-26	18-Mar-26
CON-4040	Install Overflow Storm Manhole-1	1	18-Mar-26	18-Mar-26
CON-4080	Install 43.8 LF of 6-IN DIP [Overflow Storm Manhole-1 to Existing 30-IN x 45IN Combined Sewer]	2	19-Mar-26	20-Mar-26
CON-4130	Connect Sewer System To The Existing Sewer Line	1	20-Mar-26	20-Mar-26
CON-4170	Prepare & Compact Subgrade Layer	3	23-Mar-26	25-Mar-26
CON-4240	Install 6-IN Thick Crushed Stone	5	26-Mar-26	01-Apr-26
CON-4330	F/R/P Concrete Pavement	6	02-Apr-26	09-Apr-26



Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-4440	Install Acrylic Court Surfacing	4	10-Apr-26	15-Apr-26
CON-4450	Install Concrete Pavers	4	10-Apr-26	15-Apr-26
CON-4510	Install Tree Pit	3	16-Apr-26	20-Apr-26
CON-4550	Install Site Gates	3	16-Apr-26	20-Apr-26
CON-4520	Install Elevated Movable Planter	3	21-Apr-26	23-Apr-26
CON-6330	Install Magnetic Induction Loop Wires at Cafeteria	5	21-Apr-26	27-Apr-26
CON-4530	Install Flag Pole	3	24-Apr-26	28-Apr-26
CON-6340	Install Cafeteria Flooring	10	28-Apr-26	11-May-26
CON-4540	Install Backless Site Bench	3	29-Apr-26	01-May-26
CON-3580	Install The Transformer Vault	3	05-May-26	07-May-26
CON-3830	Install 6 Sets of 4#500MCM IN 4" RGS Conduits & 3 Spare 4" RGS Conduits Encased In Concret	3	08-May-26	12-May-26
CON-3840	Install Aluminum Lighting Conductor	3	08-May-26	12-May-26
CON-6350	Install Cafeteria Assembly	15	12-May-26	02-Jun-26
CON-3990	CON-ED to Insulate 6 Sets of 4#500MCM IN 4" RGS Conduits	3	13-May-26	15-May-26
CON-4110	CON-ED to Connect The 6 Sets of 4#500MCM to The Customer End Box	2	18-May-26	19-May-26
Close-out		360	22-Jan-26	29-Jun-27
Testing & Commissioning		197	22-Jan-26	02-Nov-26
CON-2050	Emergency Generator Electric Load Test	3	22-Jan-26	24-Jan-26
CON-2240	Obtain Emergency Generator Permit	5	26-Jan-26	30-Jan-26
CON-2340	HVAC System Testing and Commissioning	5	29-Jan-26	02-Feb-26
CON-2500	Emergency Generator Final Sign-off	0		30-Jan-26
CON-4380	Elevators Testing and Commissioning	5	07-Apr-26	11-Apr-26
CON-4460	Elevator DOB Inspection	5	12-Apr-26	16-Apr-26
CON-4490	Elevator Equipment Use Permit	5	17-Apr-26	21-Apr-26
CON-4620	Elevator Final Sign-off	5	22-Apr-26	26-Apr-26
CON-6180	Electrical Testing and Commissioning	5	12-Aug-26	16-Aug-26
CON-6250	MDF & IDF Rooms Testing and Inspection (Before 3-Sep-26)	7	28-Aug-26	03-Sep-26
CON-6320	IPDV System Testing and Inspection (Before 2-Nov-26)	10	20-Oct-26	02-Nov-26
Demobilization		163	03-Nov-26	29-Jun-27
CLO-1000	Pre-Final Clean-Out	2	03-Nov-26	04-Nov-26
CLO-1010	Pre-TCO Inspection	4	05-Nov-26	08-Nov-26
CLO-1020	Pre-TCO Punchlist	15	09-Nov-26	01-Dec-26
CLO-1030	Pre-Final Clean-Out	2	02-Dec-26	03-Dec-26
CLO-1040	Pre-Substantial Completion Inspection	10	04-Dec-26	13-Dec-26
CLO-1050	Pre-Substantial Punchlist	52	14-Dec-26	01-Mar-27
CLO-1060	Pre-Final Clean-Out	2	02-Mar-27	03-Mar-27
CLO-1070	Pre-Final Completion Inspection	10	04-Mar-27	13-Mar-27
CLO-1080	Pre-Final Punchlist	75	15-Mar-27	29-Jun-27



Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

IS 082K New Building Design No. 093937 - Baseline Schedule Rev 00

TECHNICO CONSTRUCTION PROJECTS


Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	

APPENDIX 3
– Full Schedule
Grouped by Trades

Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
Key Dates		644	02-Dec-24	29-Jun-27
MIL-1000	NTP	0	02-Dec-24	
MIL-1010	Project Duration (From NTP till TCO) = 730 CDs	730	02-Dec-24	01-Dec-26
MIL-1020	Building Tight	0		05-Mar-26
MIL-1060	IDF and MDF Rooms Ready	0		03-Sep-26
MIL-1070	IPDVS System Installed	0		02-Nov-26
MIL-1030	TCO	0		01-Dec-26
MIL-1040	Substantial Completion	0		01-Mar-27*
MIL-1050	Final Completion	0		29-Jun-27*
Procurement		497	02-Dec-24	25-Nov-26
Submittals & Approvals		497	02-Dec-24	25-Nov-26
Division 01 - General Requirements		497	02-Dec-24	25-Nov-26
Spec Section S01300 - Submittals		101	02-Dec-24	25-Apr-25
SUB-1640	Prepare & Submit Underground Coordination Drawings	50	02-Dec-24	12-Feb-25
SUB-1650	Prepare & Submit 1st Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25
SUB-1660	Prepare & Submit 2nd Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25
SUB-1670	Prepare & Submit 3rd Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25
SUB-1680	Prepare & Submit 4th Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25
SUB-1690	Prepare & Submit 5th Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25
APP-1200	Review & Approve Underground Coordination Drawings	21	13-Feb-25	05-Mar-25
SUB-1930	Prepare & Submit Final Underground Coordination Drawings	37	06-Mar-25	25-Apr-25
APP-1280	Review & Approve 1st Floor Coordination Drawings	21	21-Mar-25	10-Apr-25
APP-1290	Review & Approve 2nd Floor Coordination Drawings	21	21-Mar-25	10-Apr-25
APP-1300	Review & Approve 3rd Floor Coordination Drawings	21	21-Mar-25	10-Apr-25
APP-1310	Review & Approve 4th Floor Coordination Drawings	21	21-Mar-25	10-Apr-25
APP-1320	Review & Approve 5th Floor Coordination Drawings	21	21-Mar-25	10-Apr-25
Spec Section S01311 - Progress Schedule		66	02-Dec-24	07-Mar-25
SUB-1510	Prepare & Submit Baseline Schedule	52	02-Dec-24	14-Feb-25
APP-1210	Review & Approve Baseline Schedule	21	15-Feb-25	07-Mar-25
Spec Section S01400 - Quality Control		44	02-Dec-24	04-Feb-25
SUB-1470	Prepare & Submit QCP	30	02-Dec-24	14-Jan-25
APP-1100	Review & Approve QCP	21	15-Jan-25	04-Feb-25
Spec Section S01426 - Sample Classroom		96	02-Dec-24	18-Apr-25
SUB-1320	Prepare & Submit Sample Classroom Materials	81	02-Dec-24	28-Mar-25
APP-1540	Review & Approve Sample Classroom Materials	21	29-Mar-25	18-Apr-25
Spec Section S01500 - Temporary Facilities and Controls		96	02-Dec-24	18-Apr-25
SUB-1310	Prepare & Submit Heating Plan	81	02-Dec-24	28-Mar-25
APP-1530	Review & Approve Heating Plan	21	29-Mar-25	18-Apr-25
Spec Section S01524 - Construction Waste Management		96	02-Dec-24	18-Apr-25
SUB-1300	Prepare & Submit CWM Plan	81	02-Dec-24	28-Mar-25
APP-1520	Review & Approve CWM Plan	21	29-Mar-25	18-Apr-25
Spec Section S01535 - Safety Program		17	02-Dec-24	24-Dec-24
SUB-1290	Prepare & Submit Site Safety Plan	2	02-Dec-24	03-Dec-24
APP-1000	Review & Approve Site Safety Plan	21	04-Dec-24	24-Dec-24
Spec Section S01550 - Indoor Air Quality (IAQ) Requirements		96	02-Dec-24	18-Apr-25
SUB-1280	Prepare & Submit Construction Indoor Air Quality Management Plan	81	02-Dec-24	28-Mar-25
APP-1510	Review & Approve Construction Indoor Air Quality Management Plan	21	29-Mar-25	18-Apr-25
Spec Section S01720 - Record Documents		95	13-Jul-26	25-Nov-26
SUB-1960	Prepare & Submit Record Documents	81	13-Jul-26	04-Nov-26
APP-1930	Review & Approve Record Documents	21	05-Nov-26	25-Nov-26
Division 02 - Site Work		96	02-Dec-24	18-Apr-25

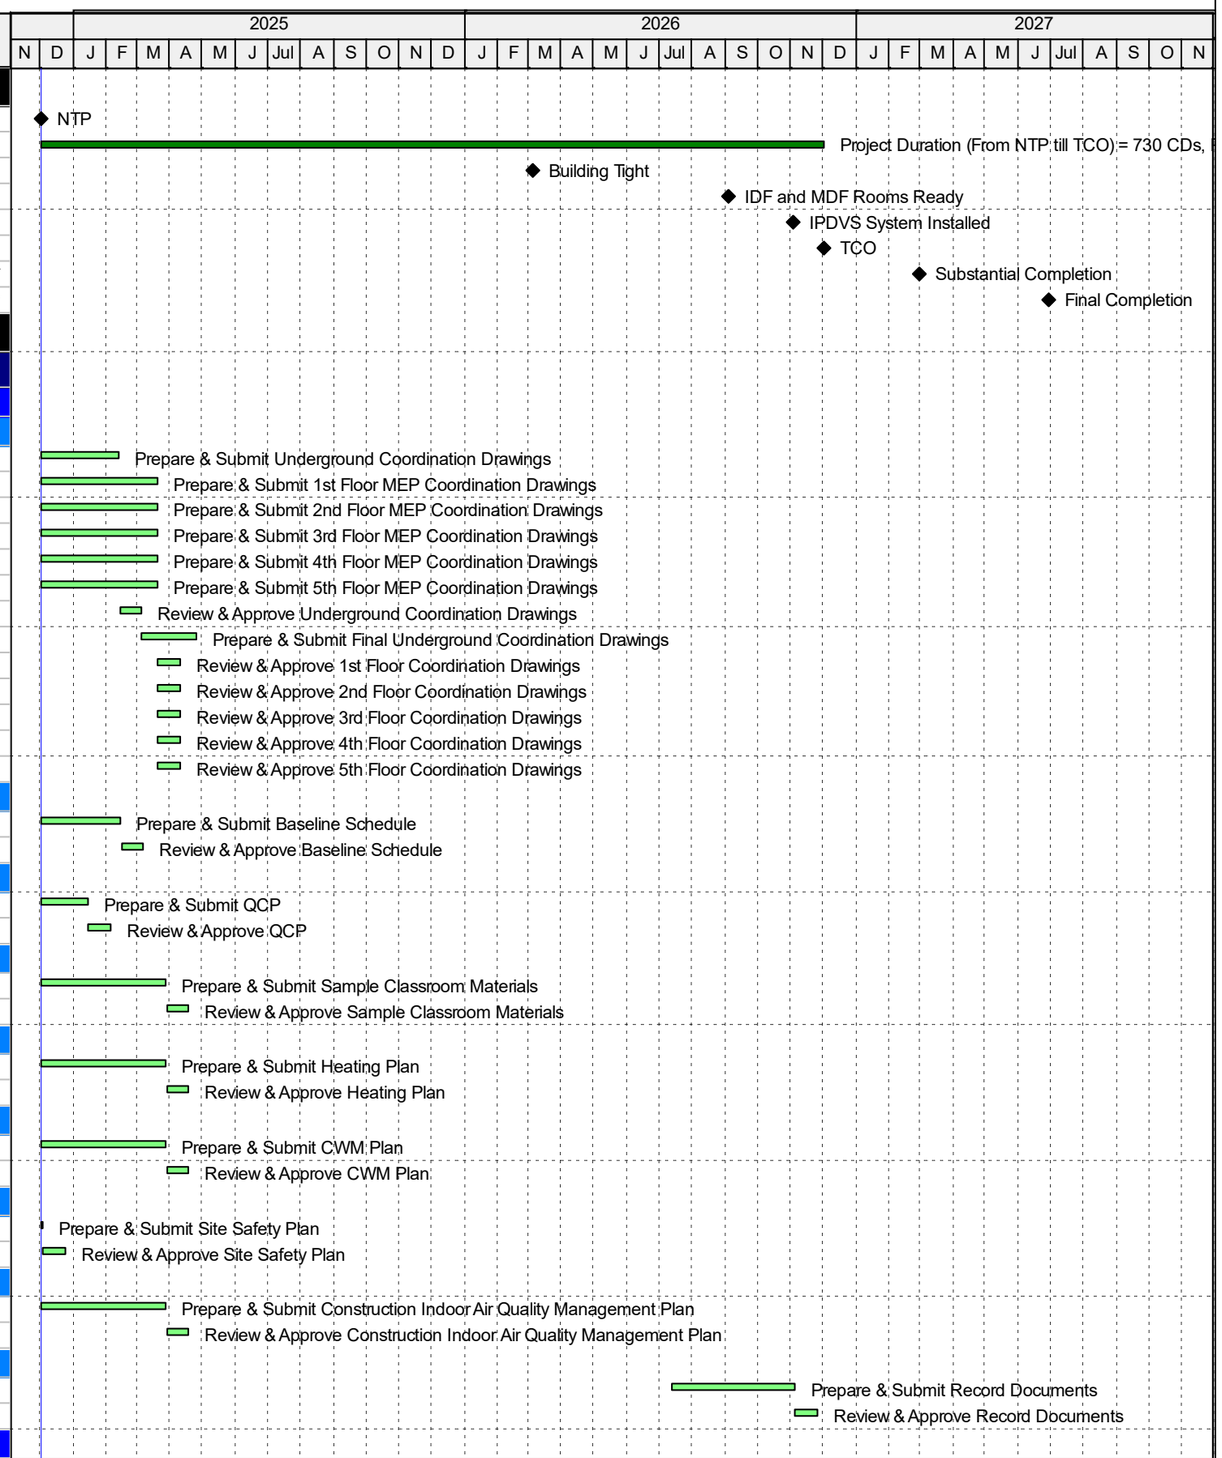

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

IS 082K New Building Design No. 093937 - Baseline Schedule Rev 00


TECHNICO CONSTRUCTION PROJECTS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
Spec Section 02010 - Environmental Site Assessment Reports		96	02-Dec-24	18-Apr-25
SUB-1700	Prepare & Submit Environmental Site Assessment Reports	81	02-Dec-24	28-Mar-25
APP-1720	Review & Approve Environmental Site Assessment Reports	21	29-Mar-25	18-Apr-25
Spec Section 02070 - Selective Removals & Demoloition		96	02-Dec-24	18-Apr-25
SUB-1710	Prepare & Submit Selective Removals & Demoloition	81	02-Dec-24	28-Mar-25
APP-1730	Review & Approve Selective Removals & Demoloition	21	29-Mar-25	18-Apr-25
Spec Section 02100 - Site Preparation		23	02-Dec-24	03-Jan-25
SUB-1270	Prepare & Submit Existing Conditions Survey	10	02-Dec-24	13-Dec-24
APP-1030	Review & Approve Existing Conditions Survey	21	14-Dec-24	03-Jan-25
Spec Section 02200 - Earthwork		21	02-Dec-24	31-Dec-24
SUB-1460	Prepare & Submit Erosion Control and Sedimentation Plan	7	02-Dec-24	10-Dec-24
APP-1020	Review & Approve Erosion Control and Sedimentation Plan	21	11-Dec-24	31-Dec-24
Spec Section 02220 - Gas Vapor Barrier (Fluid Applied)		96	02-Dec-24	18-Apr-25
SUB-1260	Prepare & Submit Gas Vapor Barrier Submittal & Inspection Schedule	81	02-Dec-24	28-Mar-25
SUB-1950	Review & Approve Gas Vapor Barrier Submittal & Inspection Schedule	21	29-Mar-25	18-Apr-25
Spec Section 02221 - Sub-Slab Depressurization System		54	02-Dec-24	19-Feb-25
SUB-1250	Prepare & Submit SSDS Geotextile	40	02-Dec-24	29-Jan-25
APP-1170	Review & Approve SSDS Geotextile	21	30-Jan-25	19-Feb-25
Spec Section 02250 - Foundation & Other Change Adjustements		19	02-Dec-24	27-Dec-24
SUB-1720	Prepare & Submit Foundation Shop Drawings	5	02-Dec-24	06-Dec-24
APP-1010	Review & Approve Foundation Shop Drawings	21	07-Dec-24	27-Dec-24
Spec Section 02511 - Asphaltic Concrete Paving		96	02-Dec-24	18-Apr-25
SUB-1240	Prepare & Submit Asphaltic Concrete Paving	81	02-Dec-24	28-Mar-25
APP-1490	Review & Approve Asphaltic Concrete Paving	21	29-Mar-25	18-Apr-25
Spec Section 02513 - Sidewalk and Street Paving		96	02-Dec-24	18-Apr-25
SUB-1230	Prepare & Submit Steel Curb Facing Shop Drawing	81	02-Dec-24	28-Mar-25
APP-1480	Review & Approve Steel Curb Facing Shop Drawing	21	29-Mar-25	18-Apr-25
Spec Section 02722 - PC Basins, Detention Basins, and Manholes		96	02-Dec-24	18-Apr-25
SUB-1220	Prepare & Submit Catch Basin Shop Drawings	81	02-Dec-24	28-Mar-25
APP-1470	Review & Approve Catch Basin Shop Drawings	21	29-Mar-25	18-Apr-25
Spec Section 02723 - Storm Drainage Systems		52	02-Dec-24	14-Feb-25
SUB-1210	Prepare & Submit Ductile Iron Pipes	37	02-Dec-24	24-Jan-25
APP-1120	Review & Approve Ductile Iron Pipes	21	25-Jan-25	14-Feb-25
Spec Section 02831 - Chain Link Fences & Gates		96	02-Dec-24	18-Apr-25
SUB-1730	Prepare & Submit Chain Link Fences & Gates Drawings	81	02-Dec-24	28-Mar-25
APP-1740	Review & Approve Chain Link Fences & Gates Drawings	21	29-Mar-25	18-Apr-25
Spec Section 02870 - Site & Street Furnishings		28	02-Dec-24	10-Jan-25
SUB-1200	Prepare & Submit Site Furnishings Shop Drawings	15	02-Dec-24	20-Dec-24
APP-1040	Review & Approve Site Furnishings Shop Drawings	21	21-Dec-24	10-Jan-25
Spec Section 02900 - Landscaping		96	02-Dec-24	18-Apr-25
SUB-1190	Prepare & Submit Planting Schedule	81	02-Dec-24	28-Mar-25
APP-1460	Review & Approve Planting Schedule	21	29-Mar-25	18-Apr-25
Division 03 - Concrete		96	02-Dec-24	18-Apr-25
Spec Section 03100 - Concrete Formwork		96	02-Dec-24	18-Apr-25
SUB-1180	Prepare & Submit Formwork Shop Drawings	81	02-Dec-24	28-Mar-25
APP-1450	Review & Approve Formwork Shop Drawings	21	29-Mar-25	18-Apr-25
Spec Section 03200 - Concrete Reinforcement		44	02-Dec-24	04-Feb-25
SUB-1170	Prepare & Submit Concrete Reinforcement	30	02-Dec-24	14-Jan-25
APP-1070	Review & Approve Concrete Reinforcement	21	15-Jan-25	04-Feb-25
Spec Section 03300 - Cast in Place Concrete		44	02-Dec-24	04-Feb-25
SUB-1350	Prepare & Submit Concrete Shop Drawings	30	02-Dec-24	14-Jan-25
SUB-1480	Prepare & Submit Concrete Mix Design	30	02-Dec-24	14-Jan-25

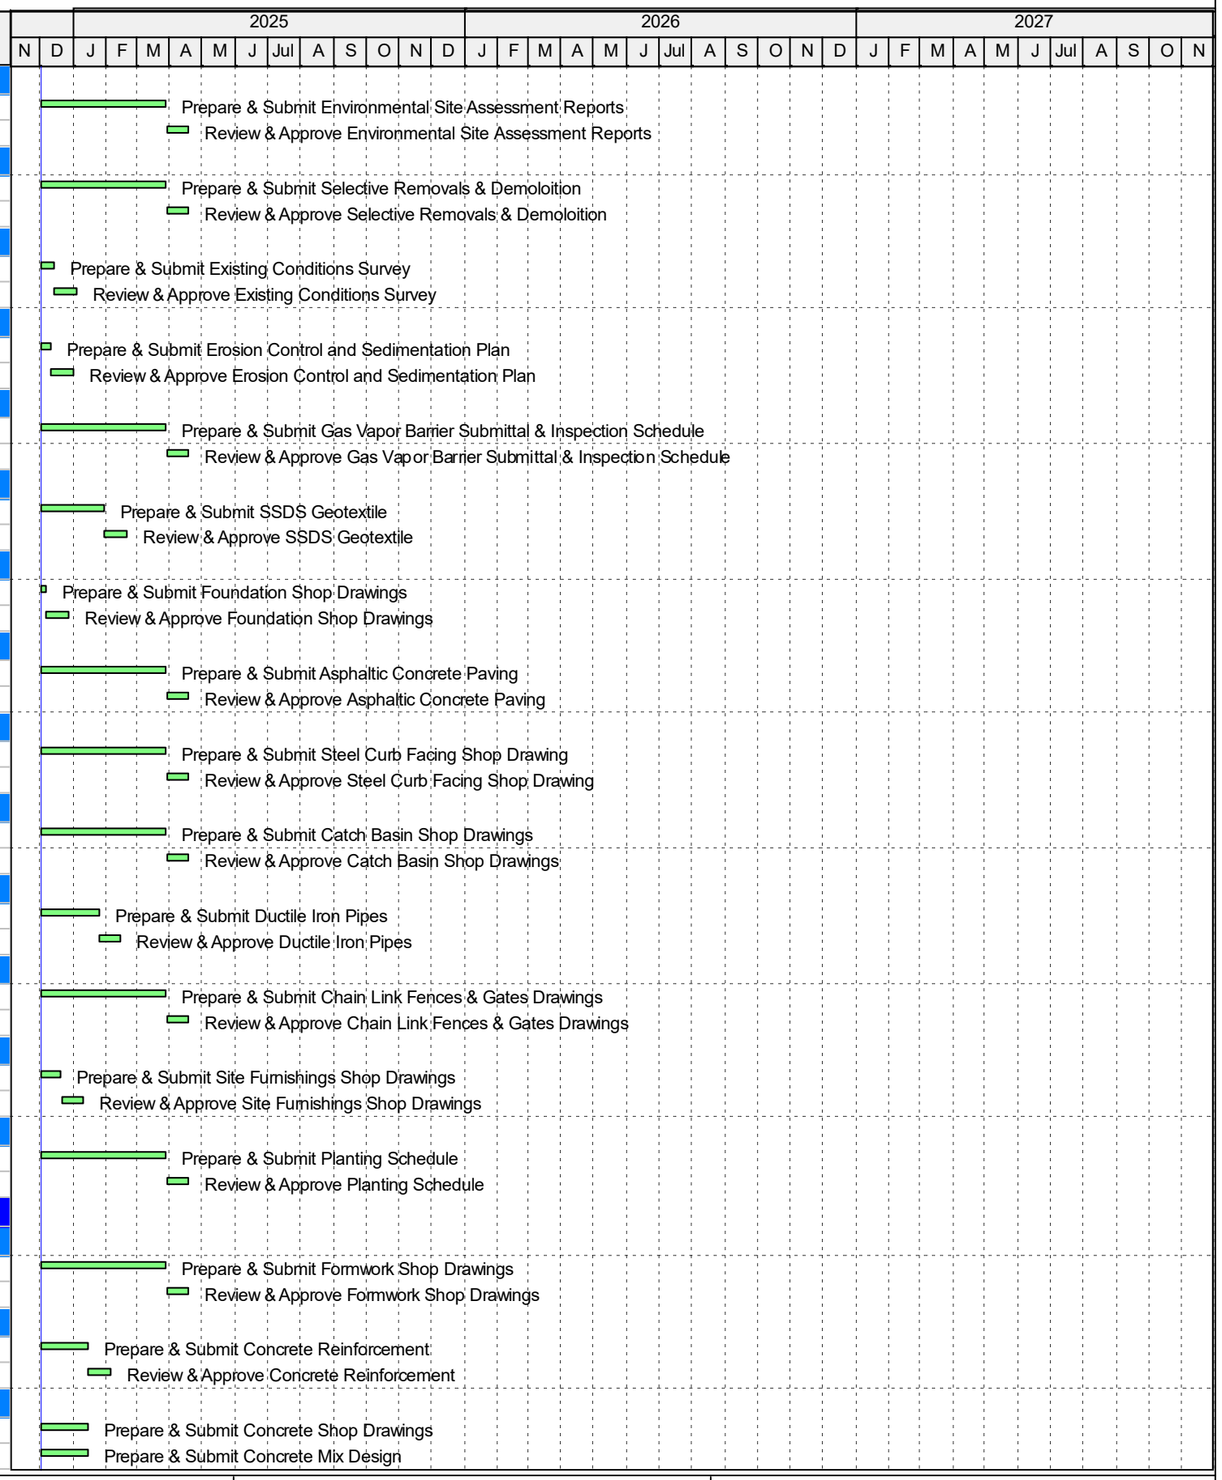

Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1080	Review & Approve Concrete Shop Drawings	21	15-Jan-25	04-Feb-25
APP-1110	Review & Approve Concrete Mix Design	21	15-Jan-25	04-Feb-25
Spec Section 03542 - Cement Based Self Leveling Underlayment		96	02-Dec-24	18-Apr-25
SUB-1160	Prepare & Submit Certification of Material	81	02-Dec-24	28-Mar-25
APP-1440	Review & Approve Certification of Material	21	29-Mar-25	18-Apr-25
Division 04 - Masonry		96	02-Dec-24	18-Apr-25
Spec Section 04200 - Unit Masonry		96	02-Dec-24	18-Apr-25
SUB-1740	Prepare & Submit Unit Masonry Product Data	81	02-Dec-24	28-Mar-25
APP-1750	Review & Approve Unit Masonry Product Data	21	29-Mar-25	18-Apr-25
Division 05 - Metals		96	02-Dec-24	18-Apr-25
Spec Section 05120 - Structural Steel		96	02-Dec-24	18-Apr-25
SUB-1750	Prepare & Submit Structure Steel Drawings	81	02-Dec-24	28-Mar-25
APP-1760	Review & Approve Structure Steel Drawings	21	29-Mar-25	18-Apr-25
Spec Section 05170 - Support System for Suspended Ceilings		96	02-Dec-24	18-Apr-25
SUB-1150	Prepare & Submit Suspension Assembly Shop Drawings	81	02-Dec-24	28-Mar-25
APP-1430	Review & Approve Suspension Assembly Shop Drawings	21	29-Mar-25	18-Apr-25
Spec Section 05300 - Metal Deck		96	02-Dec-24	18-Apr-25
SUB-1760	Prepare & Submit Metal Deck Product Data	81	02-Dec-24	28-Mar-25
APP-1770	Review & Approve Metal Deck Product Data	21	29-Mar-25	18-Apr-25
Spec Section 05500 - Metal Fabrications		96	02-Dec-24	18-Apr-25
SUB-1600	Prepare & Submit Roof Dunnage	81	02-Dec-24	28-Mar-25
APP-1700	Review & Approve Roof Dunnage	21	29-Mar-25	18-Apr-25
Division 06 - Wood & Plastics		96	02-Dec-24	18-Apr-25
Spec Section 06200 - Finish Carpentry		96	02-Dec-24	18-Apr-25
SUB-1430	Prepare & Submit Furniture	81	02-Dec-24	28-Mar-25
APP-1610	Review & Approve Furniture	21	29-Mar-25	18-Apr-25
Spec Section 06410 - Custom Casework		96	02-Dec-24	18-Apr-25
SUB-1410	Prepare & Submit Millwork	81	02-Dec-24	28-Mar-25
APP-1600	Review & Approve Millwork	21	29-Mar-25	18-Apr-25
Division 07 - Thermal & Moisture Protection		96	02-Dec-24	18-Apr-25
Spec Section 07147 - Crystalline Waterproofing		96	02-Dec-24	18-Apr-25
SUB-1140	Prepare & Submit Crystalline Waterproofing Product Data	81	02-Dec-24	28-Mar-25
APP-1420	Review & Approve Crystalline Waterproofing Product Data	21	29-Mar-25	18-Apr-25
Spec Section 07211 - Perimeter Foundation Insulation		96	02-Dec-24	18-Apr-25
SUB-1130	Prepare & Submit Perimeter Foundation Insulation Product Data	81	02-Dec-24	28-Mar-25
APP-1410	Review & Approve Perimeter Foundation Insulation Product Data	21	29-Mar-25	18-Apr-25
Spec Section 07600 - Flashing and Sheet Metal		96	02-Dec-24	18-Apr-25
SUB-1120	Prepare & Submit Flashing & Sheet Metal Shop Drawing	81	02-Dec-24	28-Mar-25
APP-1400	Review & Approve Flashing & Sheet Metal Shop Drawing	21	29-Mar-25	18-Apr-25
Spec Section 07720 - Roof Accessories		96	02-Dec-24	18-Apr-25
SUB-1110	Prepare & Submit Roof Drains & Clean Outs	81	02-Dec-24	28-Mar-25
APP-1390	Review & Approve Roof Drains & Clean Outs	21	29-Mar-25	18-Apr-25
Division 08 - Doors & Windows		96	02-Dec-24	18-Apr-25
Spec Section 08110 - Steel Doors and Frames		96	02-Dec-24	18-Apr-25
SUB-1100	Prepare & Submit Door & Frame Corners Samples	81	02-Dec-24	28-Mar-25
APP-1380	Review & Approve Door & Frame Corners Samples	21	29-Mar-25	18-Apr-25
Spec Section 08210 - Wood Doors		96	02-Dec-24	18-Apr-25
SUB-1520	Prepare & Submit Wood Doors	81	02-Dec-24	28-Mar-25
APP-1640	Review & Approve Wood Doors	21	29-Mar-25	18-Apr-25
Spec Section 08525 - High Performance Aluminum Projected Windows		88	02-Dec-24	08-Apr-25
SUB-1570	Prepare & Submit Windows	73	02-Dec-24	18-Mar-25



Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone


TECHNICO CONSTRUCTION PROJECTS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1260	Review & Approve Windows	21	19-Mar-25	08-Apr-25
Spec Section 08662 - Security Screens & Barriers		96	02-Dec-24	18-Apr-25
SUB-1770	Prepare & Submit Security Screens & Barriers	81	02-Dec-24	28-Mar-25
APP-1780	Review & Approve Security Screens & Barriers	21	29-Mar-25	18-Apr-25
Spec Section 08710 - Finish Hardware		96	02-Dec-24	18-Apr-25
SUB-1080	Prepare & Submit Door Hardware Submittal	81	02-Dec-24	28-Mar-25
SUB-1940	Review & Approve Door Hardware Submittal	21	29-Mar-25	18-Apr-25
Division 09 - Finishes		96	02-Dec-24	18-Apr-25
Spec Section 09260 - Gypsum Board Assemblies		96	02-Dec-24	18-Apr-25
SUB-1370	Prepare & Submit Gypsum Board	81	02-Dec-24	28-Mar-25
APP-1570	Review & Approve Gypsum Board	21	29-Mar-25	18-Apr-25
Spec Section 09310 - Ceramic Tiles		96	02-Dec-24	18-Apr-25
SUB-1070	Prepare & Submit Ceramic Tiles Product Data	81	02-Dec-24	28-Mar-25
APP-1350	Review & Approve Ceramic Tiles Product Data	21	29-Mar-25	18-Apr-25
Spec Section 09510 - Acoustical Ceilings		75	02-Dec-24	20-Mar-25
SUB-1390	Prepare & Submit Acosutical Ceiling Tiles	60	02-Dec-24	27-Feb-25
APP-1230	Review & Approve Acosutical Ceiling Tiles	21	28-Feb-25	20-Mar-25
Spec Section 09590 - Wood Flooring		96	02-Dec-24	18-Apr-25
SUB-1780	Prepare & Submit Wood Flooring	81	02-Dec-24	28-Mar-25
APP-1790	Review & Approve Wood Flooring	21	29-Mar-25	18-Apr-25
Spec Section 09650 - Resilient Flooring		96	02-Dec-24	18-Apr-25
SUB-1380	Prepare & Submit Floorings	81	02-Dec-24	28-Mar-25
APP-1580	Review & Approve Floorings	21	29-Mar-25	18-Apr-25
Spec Section 09900 - Painting		96	02-Dec-24	18-Apr-25
SUB-1090	Prepare & Submit Painting	81	02-Dec-24	28-Mar-25
APP-1370	Review & Approve Painting	21	29-Mar-25	18-Apr-25
Division 10 - Specialties		96	02-Dec-24	18-Apr-25
Spec Section 10100 - Visual Display Boards		96	02-Dec-24	18-Apr-25
SUB-1790	Prepare & Submit Visual Display Boards	81	02-Dec-24	28-Mar-25
APP-1800	Review & Approve Visual Display Boards	21	29-Mar-25	18-Apr-25
Spec Section 10400 - Identification Devices		96	02-Dec-24	18-Apr-25
SUB-1060	Prepare & Submit Interior Signage Shop Drawings	81	02-Dec-24	28-Mar-25
APP-1340	Review & Approve Interior Signage Shop Drawings	21	29-Mar-25	18-Apr-25
Spec Section 10522 - Fire Extinguishers & Cabinets		96	02-Dec-24	18-Apr-25
SUB-1800	Prepare & Submit Fire Extinguishers & Cabinets	81	02-Dec-24	28-Mar-25
APP-1810	Review & Approve Fire Extinguishers & Cabinets	21	29-Mar-25	18-Apr-25
Spec Section 10720 - Window Guards		88	02-Dec-24	08-Apr-25
SUB-1810	Prepare & Submit Stationary Metal Wall Louvers	73	02-Dec-24	18-Mar-25
APP-1270	Review & Approve Stationary Metal Wall Louvers	21	19-Mar-25	08-Apr-25
Spec Section 10810 - Toilet & Bath Accessories		96	02-Dec-24	18-Apr-25
SUB-1400	Prepare & Submit Toilet Accessories	81	02-Dec-24	28-Mar-25
APP-1590	Review & Approve Toilet Accessories	21	29-Mar-25	18-Apr-25
Division 11 - Equipment		96	02-Dec-24	18-Apr-25
Spec Section 11061 - Platform Curtains & Auditorium Window Curtains		96	02-Dec-24	18-Apr-25
SUB-1820	Prepare & Submit Platform Curtains & Auditorium Window Curtains	81	02-Dec-24	28-Mar-25
APP-1820	Review & Approve Platform Curtains & Auditorium Window Curtains	21	29-Mar-25	18-Apr-25
Spec Section 11400 - Food Service Equipment		96	02-Dec-24	18-Apr-25
SUB-1550	Prepare & Submit Kitchen Equipment	81	02-Dec-24	28-Mar-25
APP-1670	Review & Approve Kitchen Equipment	21	29-Mar-25	18-Apr-25
Spec Section 11450 - Domestic Type Equipment		96	02-Dec-24	18-Apr-25
SUB-1830	Prepare & Submit Domestic Equipment	81	02-Dec-24	28-Mar-25
APP-1830	Review & Approve Domestic Equipment	21	29-Mar-25	18-Apr-25

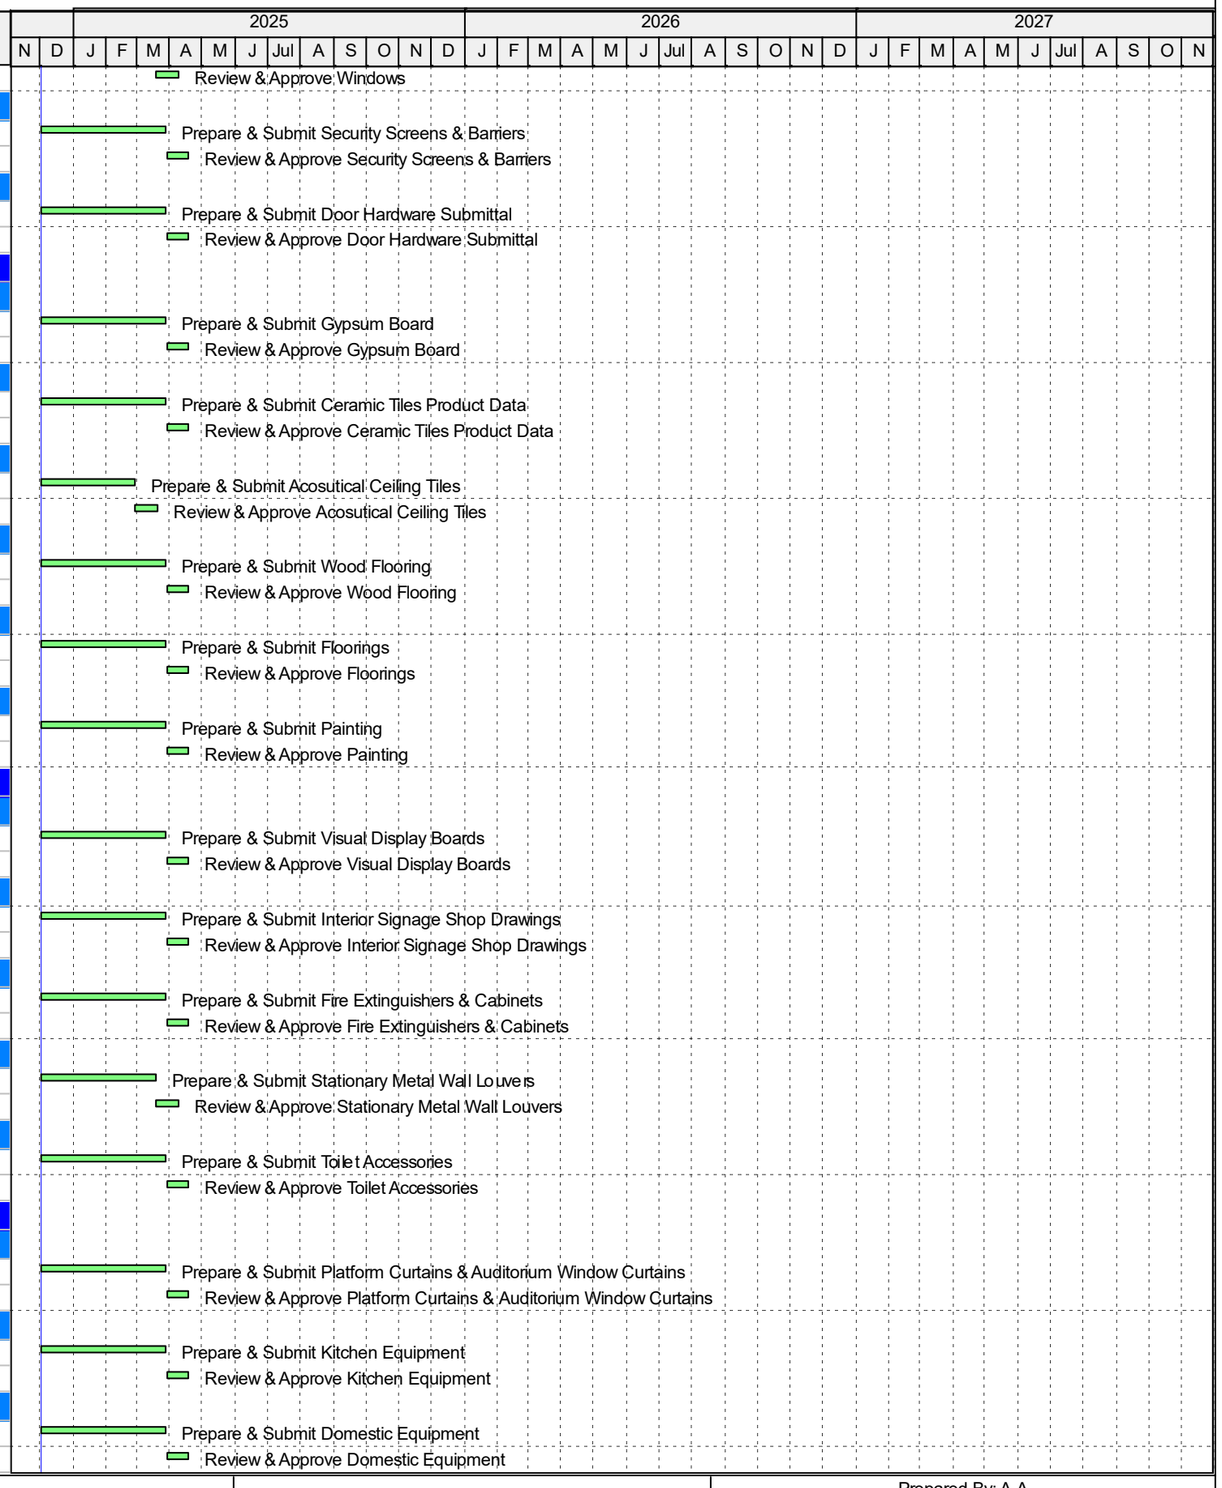

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone


TECHNICO CONSTRUCTION PROJECS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	


Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
Spec Section 11480 - Gymnasium Equipment		96	02-Dec-24	18-Apr-25
SUB-1630	Prepare & Submit Gymnasium Equipment	81	02-Dec-24	28-Mar-25
APP-1710	Review & Approve Gymnasium Equipment	21	29-Mar-25	18-Apr-25
Division 12 - Furnishings		96	02-Dec-24	18-Apr-25
Spec Section 12302 - Manufactured Wood Casework		96	02-Dec-24	18-Apr-25
SUB-1840	Prepare & Submit Manufactured Wood Casework	81	02-Dec-24	28-Mar-25
APP-1840	Review & Approve Manufactured Wood Casework	21	29-Mar-25	18-Apr-25
Division 14 - Conveying Systems		96	02-Dec-24	18-Apr-25
Spec Section 14212 - Gearless Traction Passenger Elevators		64	02-Dec-24	05-Mar-25
SUB-1360	Prepare & Submit Elevator Machine	50	02-Dec-24	12-Feb-25
APP-1180	Review & Approve Elevator Machine	21	13-Feb-25	05-Mar-25
Spec Section 14420 - Hydraulic Vertical Wheelchair Lifts		96	02-Dec-24	18-Apr-25
SUB-1850	Prepare & Submit Hydraulic Vertical Wheelchair Lifts	81	02-Dec-24	28-Mar-25
APP-1850	Review & Approve Hydraulic Vertical Wheelchair Lifts	21	29-Mar-25	18-Apr-25
Division 15 - Mechanical		96	02-Dec-24	18-Apr-25
Division 15A - Fire Protection		96	02-Dec-24	18-Apr-25
Spec Section 15333 - Fire Pumps - Sprinkler Booster Pumps		96	02-Dec-24	18-Apr-25
SUB-1050	Prepare & Submit Fire & Jockey Pumps	81	02-Dec-24	28-Mar-25
SUB-1530	Prepare & Submit Fire Protection Shop Drawings	81	02-Dec-24	28-Mar-25
APP-1330	Review & Approve Fire & Jockey Pumps	21	29-Mar-25	18-Apr-25
APP-1650	Review & Approve Fire Protection Shop Drawings	21	29-Mar-25	18-Apr-25
Division 15B - Plumbing & Drainage		96	02-Dec-24	18-Apr-25
Spec Section 15410 - Plumbing Piping		96	02-Dec-24	18-Apr-25
SUB-1340	Prepare & Submit Plumbing Shop Drawings	81	02-Dec-24	28-Mar-25
APP-1560	Review & Approve Plumbing Shop Drawings	21	29-Mar-25	18-Apr-25
Spec Section 15411 - Hangers and Supports		54	02-Dec-24	19-Feb-25
SUB-1040	Prepare & Submit Hangers & Supports	40	02-Dec-24	29-Jan-25
APP-1160	Review & Approve Hangers & Supports	21	30-Jan-25	19-Feb-25
Spec Section 15415 - Drainage		54	02-Dec-24	19-Feb-25
SUB-1030	Prepare & Submit Floor Drains	40	02-Dec-24	29-Jan-25
APP-1150	Review & Approve Floor Drains	21	30-Jan-25	19-Feb-25
Spec Section 15417 - Cold Water Supply		54	02-Dec-24	19-Feb-25
SUB-1020	Prepare & Submit Pressure Gages	40	02-Dec-24	29-Jan-25
APP-1140	Review & Approve Pressure Gages	21	30-Jan-25	19-Feb-25
Spec Section 15418 - Hot Water Supply		54	02-Dec-24	19-Feb-25
SUB-1010	Prepare & Submit Thermometers	40	02-Dec-24	29-Jan-25
APP-1130	Review & Approve Thermometers	21	30-Jan-25	19-Feb-25
Spec Section 15440 - Plumbing Fixtures		96	02-Dec-24	18-Apr-25
SUB-1500	Prepare & Submit Plumbing Fixtures	81	02-Dec-24	28-Mar-25
APP-1630	Review & Approve Plumbing Fixtures	21	29-Mar-25	18-Apr-25
Spec Section 15453 - Pumping Apparatus & Tanks		96	02-Dec-24	18-Apr-25
SUB-1880	Prepare & Submit Pumping Apparatus & Tanks	81	02-Dec-24	28-Mar-25
APP-1880	Review & Approve Pumping Apparatus & Tanks	21	29-Mar-25	18-Apr-25
Division 15C - Heating & Ventilation & Air Conditioning		96	02-Dec-24	18-Apr-25
Spec Section 15510 - HVAC Piping		75	02-Dec-24	20-Mar-25
SUB-1450	Prepare & Submit Mechanical Piping	60	02-Dec-24	27-Feb-25
APP-1240	Review & Approve Mechanical Piping	21	28-Feb-25	20-Mar-25
Spec Section 15783 - Split Heat Pump System		75	02-Dec-24	20-Mar-25
SUB-1000	Prepare & Submit Split Heat Pump System - SUB	60	02-Dec-24	27-Feb-25
APP-1220	Review & Approve Split Heat Pump System - SUB	21	28-Feb-25	20-Mar-25
Spec Section 15836 - Unit Heaters Cabinet Heaters		75	02-Dec-24	20-Mar-25

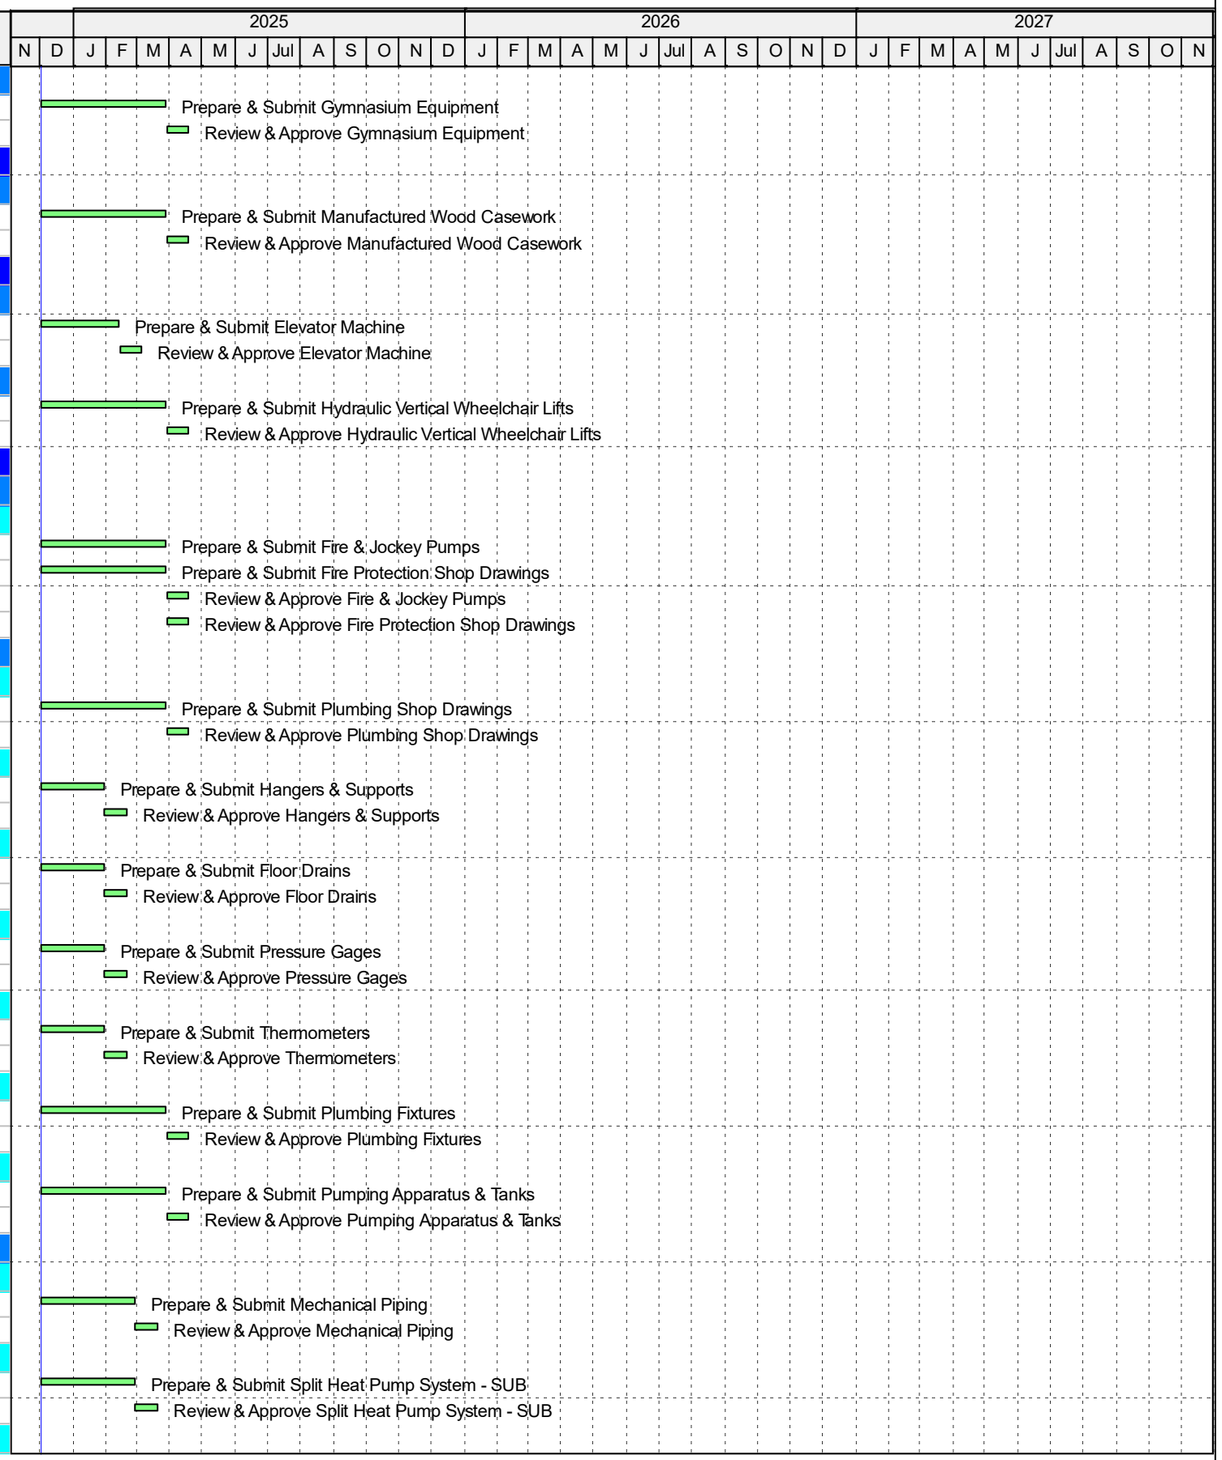


Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1620	Prepare & Submit Unit Cabinet Heaters	60	02-Dec-24	27-Feb-25
APP-1250	Review & Approve Unit Cabinet Heaters	21	28-Feb-25	20-Mar-25
Spec Section 15891 - Metal Ductwork		96	02-Dec-24	18-Apr-25
SUB-1440	Prepare & Submit Mechanical Ducts	81	02-Dec-24	28-Mar-25
APP-1620	Review & Approve Mechanical Ducts	21	29-Mar-25	18-Apr-25
Spec Section 15590 - Emergency Generator System Accessories		96	02-Dec-24	18-Apr-25
SUB-1890	Prepare & Submit Emergency Generator System Accessories	81	02-Dec-24	28-Mar-25
APP-1890	Review & Approve Emergency Generator System Accessories	21	29-Mar-25	18-Apr-25
Spec Section 15836 - Unit Heaters/Cabinet Heaters		96	02-Dec-24	18-Apr-25
SUB-1900	Prepare & Submit Unit Heaters/Cabinet Heaters Equipment	81	02-Dec-24	28-Mar-25
APP-1900	Review & Approve Unit Heaters/Cabinet Heaters Equipment	21	29-Mar-25	18-Apr-25
Spec Section 15970 - Temperature Control System		96	02-Dec-24	18-Apr-25
SUB-1920	Prepare & Submit Air Outlets & Inlets	81	02-Dec-24	28-Mar-25
APP-1920	Review & Approve Air Outlets & Inlets	21	29-Mar-25	18-Apr-25
Spec Section 15940 - Air Outlets & Inlets		96	02-Dec-24	18-Apr-25
SUB-1910	Prepare & Submit Temperature Control System	81	02-Dec-24	28-Mar-25
APP-1910	Review & Approve Temperature Control System	21	29-Mar-25	18-Apr-25
Division 16 - Electrical		96	02-Dec-24	18-Apr-25
Spec Section 16010 - Gen Provisions for Elec Work		96	02-Dec-24	18-Apr-25
SUB-1330	Prepare & Submit Electrical Shop Drawings	81	02-Dec-24	28-Mar-25
SUB-1490	Prepare & Submit Electrical Equipment, Conduits, and Cables	20	02-Dec-24	30-Dec-24
SUB-1610	Prepare & Submit Switch Gears Product Data	20	02-Dec-24	30-Dec-24
APP-1050	Review & Approve Electrical Equipment, Conduits, and Cables	21	31-Dec-24	20-Jan-25
APP-1060	Review & Approve Switch Gears Product Data	21	31-Dec-24	20-Jan-25
APP-1550	Review & Approve Electrical Shop Drawings	21	29-Mar-25	18-Apr-25
Spec Section 16120 - Wiring Systems		96	02-Dec-24	18-Apr-25
SUB-1580	Prepare & Submit Telecommunication System Drawings	81	02-Dec-24	28-Mar-25
APP-1690	Review & Approve Telecommunication System Drawings	21	29-Mar-25	18-Apr-25
Spec Section 16502 - Interior Lighting Fixtures		44	02-Dec-24	04-Feb-25
SUB-1420	Prepare & Submit Lighting Fixtures	30	02-Dec-24	14-Jan-25
APP-1090	Review & Approve Lighting Fixtures	21	15-Jan-25	04-Feb-25
Spec Section 16520 - Illuminated Exit Sign		96	02-Dec-24	18-Apr-25
SUB-1560	Prepare & Submit Signs	81	02-Dec-24	28-Mar-25
APP-1680	Review & Approve Signs	21	29-Mar-25	18-Apr-25
Spec Section 16720 - Fire Detection Alarm System with COC		96	02-Dec-24	18-Apr-25
SUB-1540	Prepare & Submit Fire Detectors & Alarms	81	02-Dec-24	28-Mar-25
APP-1660	Review & Approve Fire Detectors & Alarms	21	29-Mar-25	18-Apr-25
Spec Section 16785 - Internet Protocol Digital Video Surveillance System using Digital Cameras		64	02-Dec-24	05-Mar-25
SUB-1590	Prepare & Submit Internet Protocol Digital Video Surveillance System using Digital Cameras	50	02-Dec-24	12-Feb-25
APP-1190	Review & Approve Internet Protocol Digital Video Surveillance System using Digital Cameras	21	13-Feb-25	05-Mar-25
Spec Section 16425 - Switch Boards & Panel Boards		96	02-Dec-24	18-Apr-25
SUB-1860	Prepare & Submit Switch & Panel Boards	81	02-Dec-24	28-Mar-25
APP-1860	Review & Approve Switch & Panel Boards	21	29-Mar-25	18-Apr-25
Spec Section 16475 - Overcurrent Protective Devices		96	02-Dec-24	18-Apr-25
SUB-1870	Prepare & Submit Overcurrent Protective Devices Data	81	02-Dec-24	28-Mar-25
APP-1870	Review & Approve Overcurrent Protective Devices Data	21	29-Mar-25	18-Apr-25
Fabrication & Delivery		358	01-Jan-25	24-Dec-25
PRO-1120	Procure & Deliver Erosion Control and Sedimentation Devices	25	01-Jan-25	25-Jan-25
PRO-1140	Procure & Deliver Lighting Fixtures	60	05-Feb-25	05-Apr-25
PRO-1200	Procure & Deliver Elevator Machine	150	06-Mar-25	02-Aug-25
PRO-1330	Procure & Deliver Cameras	60	06-Mar-25	04-May-25
PRO-1170	Procure & Deliver Acosutical Ceiling Tiles	120	21-Mar-25	18-Jul-25

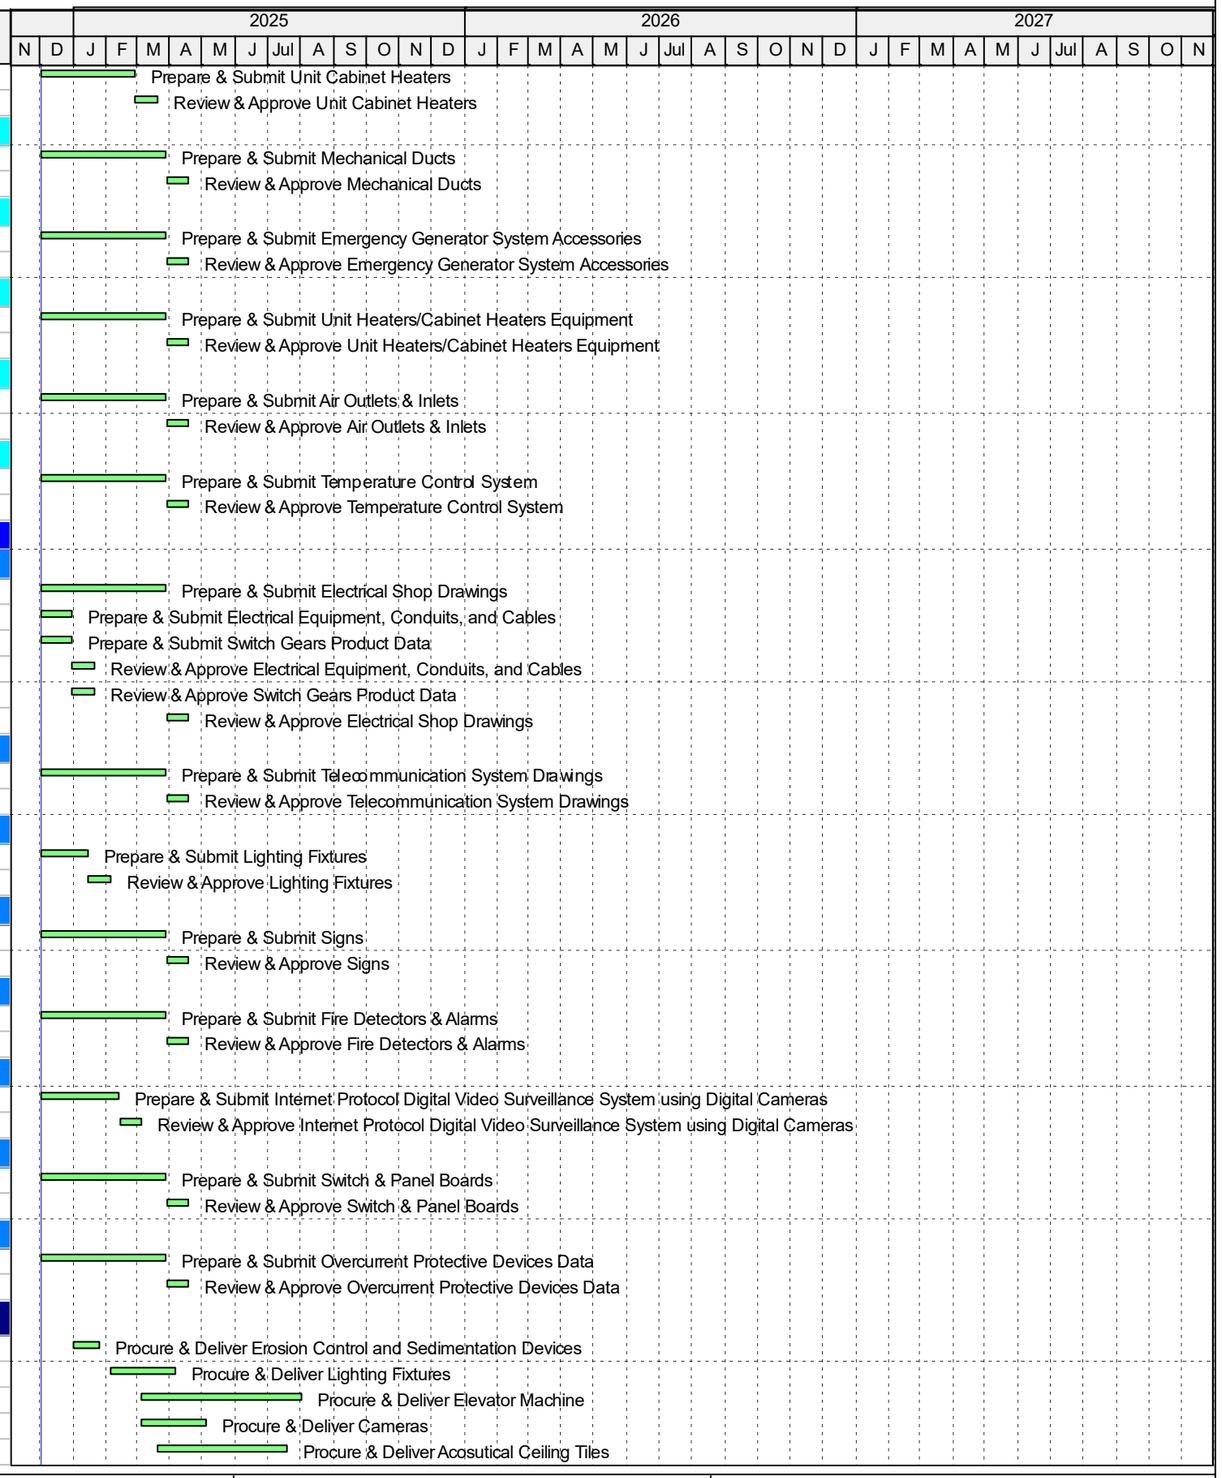


Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
PRO-1020	Procure & Deliver Mechanical Piping	70	21-Mar-25	29-May-25
PRO-1220	Procure & Deliver Windows	154	09-Apr-25	09-Sep-25
PRO-1420	Procure & Deliver Painting	70	19-Apr-25	27-Jun-25
PRO-1410	Procure & Deliver Door Frames	70	19-Apr-25	27-Jun-25
PRO-1150	Procure & Deliver Gypsum Board	150	19-Apr-25	15-Sep-25
PRO-1160	Procure & Deliver Floorings	80	19-Apr-25	07-Jul-25
PRO-1190	Procure & Deliver Toilet Accessories	100	19-Apr-25	27-Jul-25
PRO-1000	Procure & Deliver Kitchen Equipment	180	19-Apr-25	15-Oct-25
PRO-1010	Procure & Deliver Furnitures	130	19-Apr-25	26-Aug-25
PRO-1030	Procure & Deliver Mechanical Ducts	70	19-Apr-25	27-Jun-25
PRO-1050	Procure & Deliver Electrical Equipment	130	19-Apr-25	26-Aug-25
PRO-1060	Procure & Deliver Plumbing Fixtures	100	19-Apr-25	27-Jul-25
PRO-1070	Procure & Deliver Doors	50	19-Apr-25	07-Jun-25
PRO-1110	Procure & Deliver Fire Detectors & Alarms	60	19-Apr-25	17-Jun-25
PRO-1210	Procure & Deliver Signs	70	19-Apr-25	27-Jun-25
PRO-1250	Procure & Deliver Plumbing Pipes	60	19-Apr-25	17-Jun-25
PRO-1260	Procure & Deliver Electrical Wires & Conduits	130	19-Apr-25	26-Aug-25
PRO-1270	Procure & Deliver Mechanical Pumps	70	19-Apr-25	27-Jun-25
PRO-1280	Procure & Deliver Fire Protection Pumps	70	19-Apr-25	27-Jun-25
PRO-1290	Procure & Deliver Plumbing Pumps	250	19-Apr-25	24-Dec-25
PRO-1310	Procure & Deliver Telecommunication System	60	19-Apr-25	17-Jun-25
PRO-1380	Procure & Deliver Roof Dunnage	100	19-Apr-25	27-Jul-25
PRO-1470	Procure & Deliver Cabinet Heaters	126	19-Apr-25	22-Aug-25
PRO-1530	Procure & Deliver Hydraulic Vertical Wheelchair Lift	90	19-Apr-25	17-Jul-25
PRO-1560	Procure & Deliver Gymnasium Equipment	180	19-Apr-25	15-Oct-25
PRO-1580	Procure & Deliver Metal Deck	120	19-Apr-25	16-Aug-25
PRO-1590	Procure & Deliver Steel Columns	120	19-Apr-25	16-Aug-25
PRO-1600	Procure & Deliver Steel Framing	60	19-Apr-25	17-Jun-25
PRO-1630	Procure & Deliver Wood Flooring	120	19-Apr-25	16-Aug-25
Permits		43	01-Apr-25	30-May-25
PER-1000	Obtain Construction Fences Permit	3	01-Apr-25	03-Apr-25
PER-1010	Obtain CCD1	3	01-Apr-25	03-Apr-25
PER-1020	Obtain Sidewalk Shed Permits	3	01-Apr-25	03-Apr-25
PER-1030	Meeting With SCA to Review The Permit Requirements	14	01-Apr-25	18-Apr-25
PER-1040	Prepare & Submit Permit Waiver Requests to SCA Chief Project Officer	5	01-Apr-25	07-Apr-25
PER-1050	Prepare & Submit FDNY Fuel Permit	10	01-Apr-25	14-Apr-25
PER-1060	Obtain Builders Pavement Permit	10	01-Apr-25	14-Apr-25
PER-1070	Obtain Excavation Permit	15	01-Apr-25	21-Apr-25
PER-1080	Obtain Permit to Enter (PTE)	10	01-Apr-25	14-Apr-25
PER-1090	Review & Approve FDNY Fuel Permit	21	15-Apr-25	05-May-25
PER-1100	DOB Permit & Insurance	21	01-May-25	30-May-25
PER-1110	SCA Work Notification	7	21-May-25	30-May-25
Utilities Coordination		274	01-Apr-25	04-May-26
Temporary Electrical Power		274	01-Apr-25	04-May-26
COR-1000	Coordination With CON-ED For Temporary Electrical Power	10	01-Apr-25	14-Apr-25
COR-1010	Scheduling With CON-ED For Temporary Electrical Power	7	15-Apr-25	23-Apr-25
COR-1020	Procurement From CON-ED For Temporary Electrical Power	20	24-Apr-25	13-May-25
COR-1030	CON-ED Work For Temporary Electrical Power	10	14-May-25	28-May-25
COR-1040	Available Temporary Electrical Power For Testing MEP Equipment	0		28-May-25
COR-1050	Coordination With CON-ED For Trasnformers Work	10	21-Nov-25	05-Dec-25
COR-1060	CON-ED to Provide (1) 27KV Feeder To Transformer Vault	30	06-Dec-25	04-Jan-26
COR-1070	CON-ED to Furnish & Deliver (1) New "V11-6 Transformer Vault	120	05-Jan-26	04-May-26

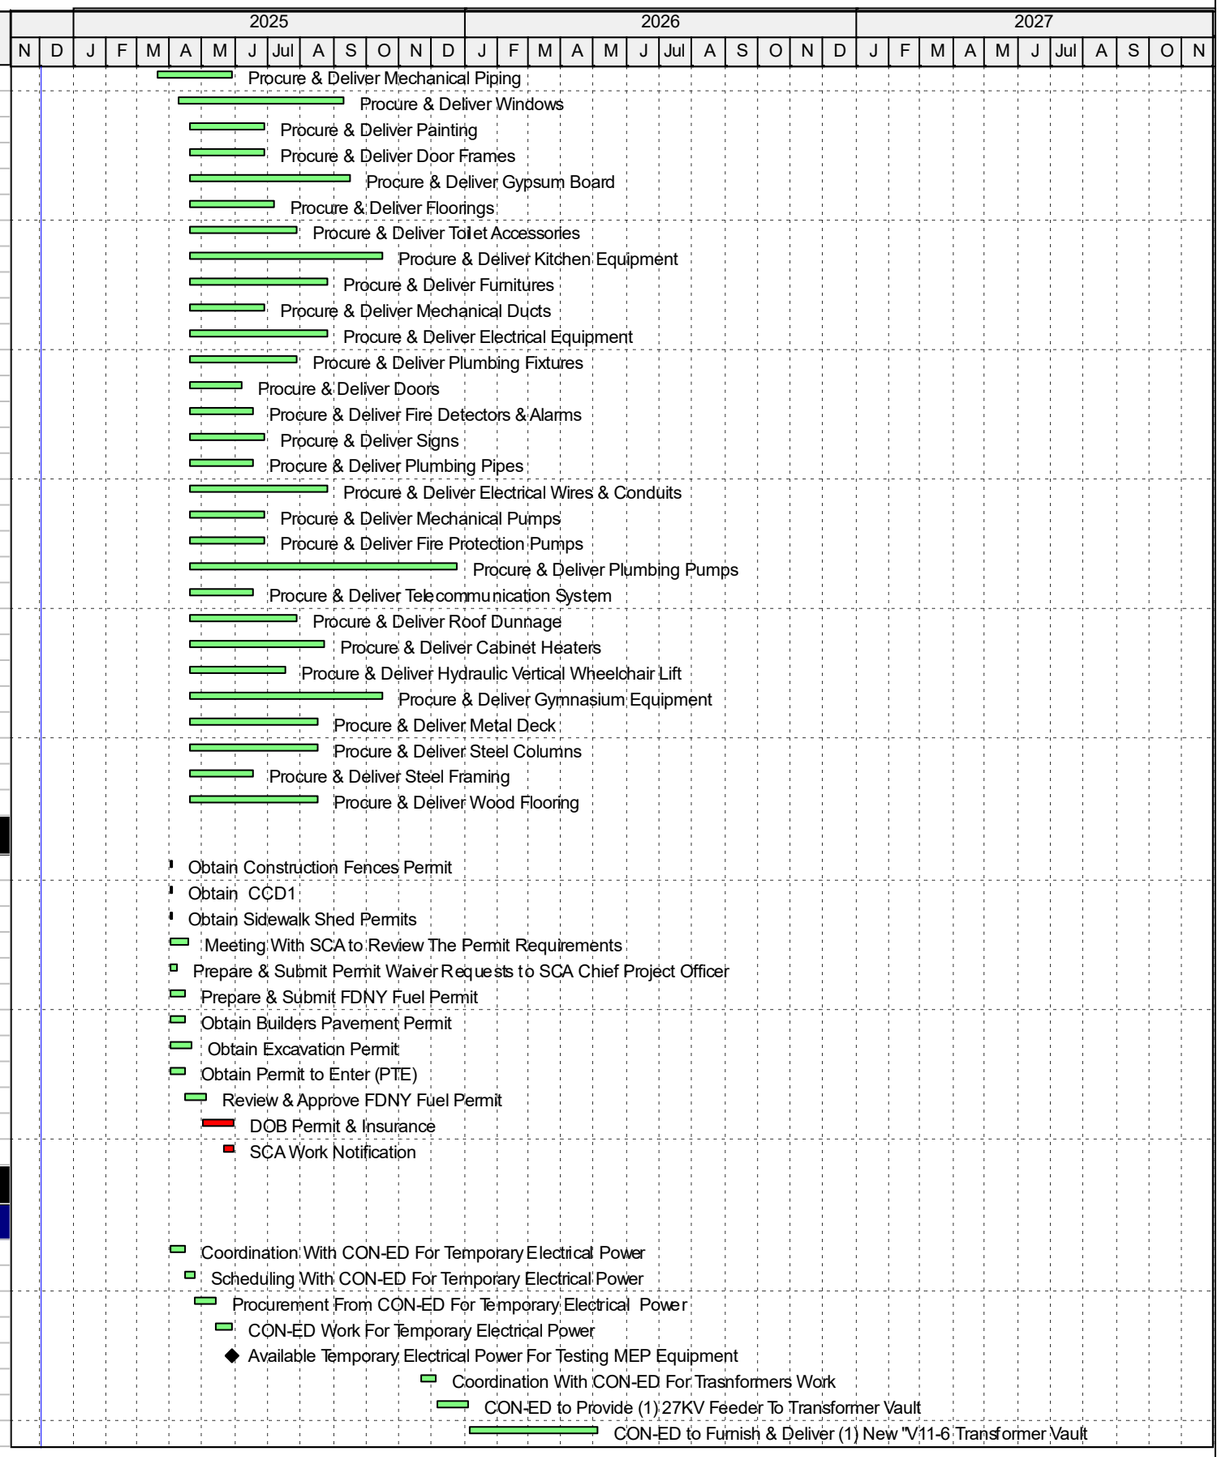

Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
Site Access Restrictions		180	02-Dec-24	30-May-25
PER-1120	No Site Access	180	02-Dec-24	30-May-25
Preliminary Work		86	02-Jun-25	02-Oct-25
CON-1000	Mobilization	5	02-Jun-25	06-Jun-25
CON-1010	Install Site Fence	2	09-Jun-25	10-Jun-25
CON-1020	Install Construction Entrance - Stage 1	1	09-Jun-25	09-Jun-25
CON-1030	Install Erosion Control Devices - Stage 1	2	11-Jun-25	12-Jun-25
CON-1040	Remove Existing Asphalt Pavement and Subbase	2	13-Jun-25	16-Jun-25
CON-1050	Install Remove Existing Concrete Pavement and Subbase	2	13-Jun-25	16-Jun-25
CON-1060	Prepare Temporary Staging & Storage Area - Stage 1	3	17-Jun-25	20-Jun-25
CON-1250	Install Construction Entrance - Stage 2	1	30-Sep-25	30-Sep-25
CON-1260	Install Erosion Control Devices - Stage 2	2	01-Oct-25	02-Oct-25
CON-1270	Prepare Temporary Staging & Storage Area - Stage 2	2	01-Oct-25	02-Oct-25
Foundation Work		105	23-Jun-25	20-Nov-25
CON-1070	Survey and Verify All Underground Utilities	3	23-Jun-25	25-Jun-25
CON-1080	Excavation	7	26-Jun-25	07-Jul-25
CON-1090	F/R/P Cellar Wall Footings	6	08-Jul-25	15-Jul-25
CON-1100	F/R/P Cellar Retaining Wall	8	16-Jul-25	25-Jul-25
CON-1120	Insulate Cellar Retaining Wall	5	28-Jul-25	01-Aug-25
CON-1180	F/R/P Slab on Grade - Cellar	4	11-Aug-25	14-Aug-25
CON-1190	F/R/P First Floor Slab - Cellar Side	5	15-Aug-25	21-Aug-25
CON-1200	Install Floor Drains - Cellar Floor	2	15-Aug-25	18-Aug-25
CON-1210	Install MEP Hangers - 1st Floor - Cellar Side	2	20-Aug-25	21-Aug-25
CON-1220	Curing For The First Floor Slab	28	22-Aug-25	18-Sep-25
CON-1230	F/R/P Columns & Shear Walls From First Level To Second Level - Cellar Area	4	22-Aug-25	27-Aug-25
CON-1240	Backfilling	7	19-Sep-25	29-Sep-25
CON-1280	F/R/P First Floor Foundation	7	03-Oct-25	14-Oct-25
CON-1290	F/R/P Columns From First Level To Second Level - First Level Area	5	07-Oct-25	14-Oct-25
CON-1300	Insulate First Floor Foundations	3	15-Oct-25	17-Oct-25
CON-1310	Backfilling	5	20-Oct-25	24-Oct-25
CON-1380	F/R/P First Floor SOG	4	17-Nov-25	20-Nov-25
SSDS System		77	28-Jul-25	14-Nov-25
Below Cellar		10	28-Jul-25	08-Aug-25
CON-1110	Install Non-Woven Geotextile Layer - Below Cellar	2	28-Jul-25	29-Jul-25
CON-1130	Install Gas Permeable Aggregate Layer- Below Cellar	2	30-Jul-25	31-Jul-25
CON-1140	Install 6" C.I Pipe - Below Cellar	2	30-Jul-25	31-Jul-25
CON-1150	Install VI-20 Geomembrane Gas Permeable Aggregate Layer - Below Cellar	2	01-Aug-25	04-Aug-25
CON-1160	Install 60 Dry Mils of Liquid Boot - Below Cellar	2	05-Aug-25	06-Aug-25
CON-1170	Install Liquid Boot Ultrashield G-1000 - Below Cellar	2	07-Aug-25	08-Aug-25
Below First Floor SOG		14	27-Oct-25	14-Nov-25
CON-1320	Install Non-Woven Geotextile Layer - Below 1st Floor SOG	3	27-Oct-25	29-Oct-25
CON-1330	Install Gas Permeable Aggregate Layer - Below 1st Floor SOG	3	30-Oct-25	03-Nov-25
CON-1340	Install 6" C.I Pipe - Below 1st Floor SOG	2	30-Oct-25	31-Oct-25
CON-1350	Install VI-20 Geomembrane Gas Permeable Aggregate Layer - Below 1st Floor SOG	3	04-Nov-25	06-Nov-25
CON-1360	Install 60 Dry Mils of Liquid Boot - Below 1st Floor SOG	3	07-Nov-25	12-Nov-25
CON-1370	Install Liquid Boot Ultrashield G-1000 - Below 1st Floor SOG	2	13-Nov-25	14-Nov-25
Floor Drains		34	19-Nov-25	08-Jan-26
CON-1390	Install Floor Drains - 1st Floor	2	19-Nov-25	20-Nov-25
CON-1420	Install Floor Drains - 2nd Floor	2	26-Nov-25	28-Nov-25
CON-1470	Install Floor Drains - 3rd Floor	2	11-Dec-25	12-Dec-25
CON-1520	Install Floor Drains - 4th Floor	2	18-Dec-25	19-Dec-25

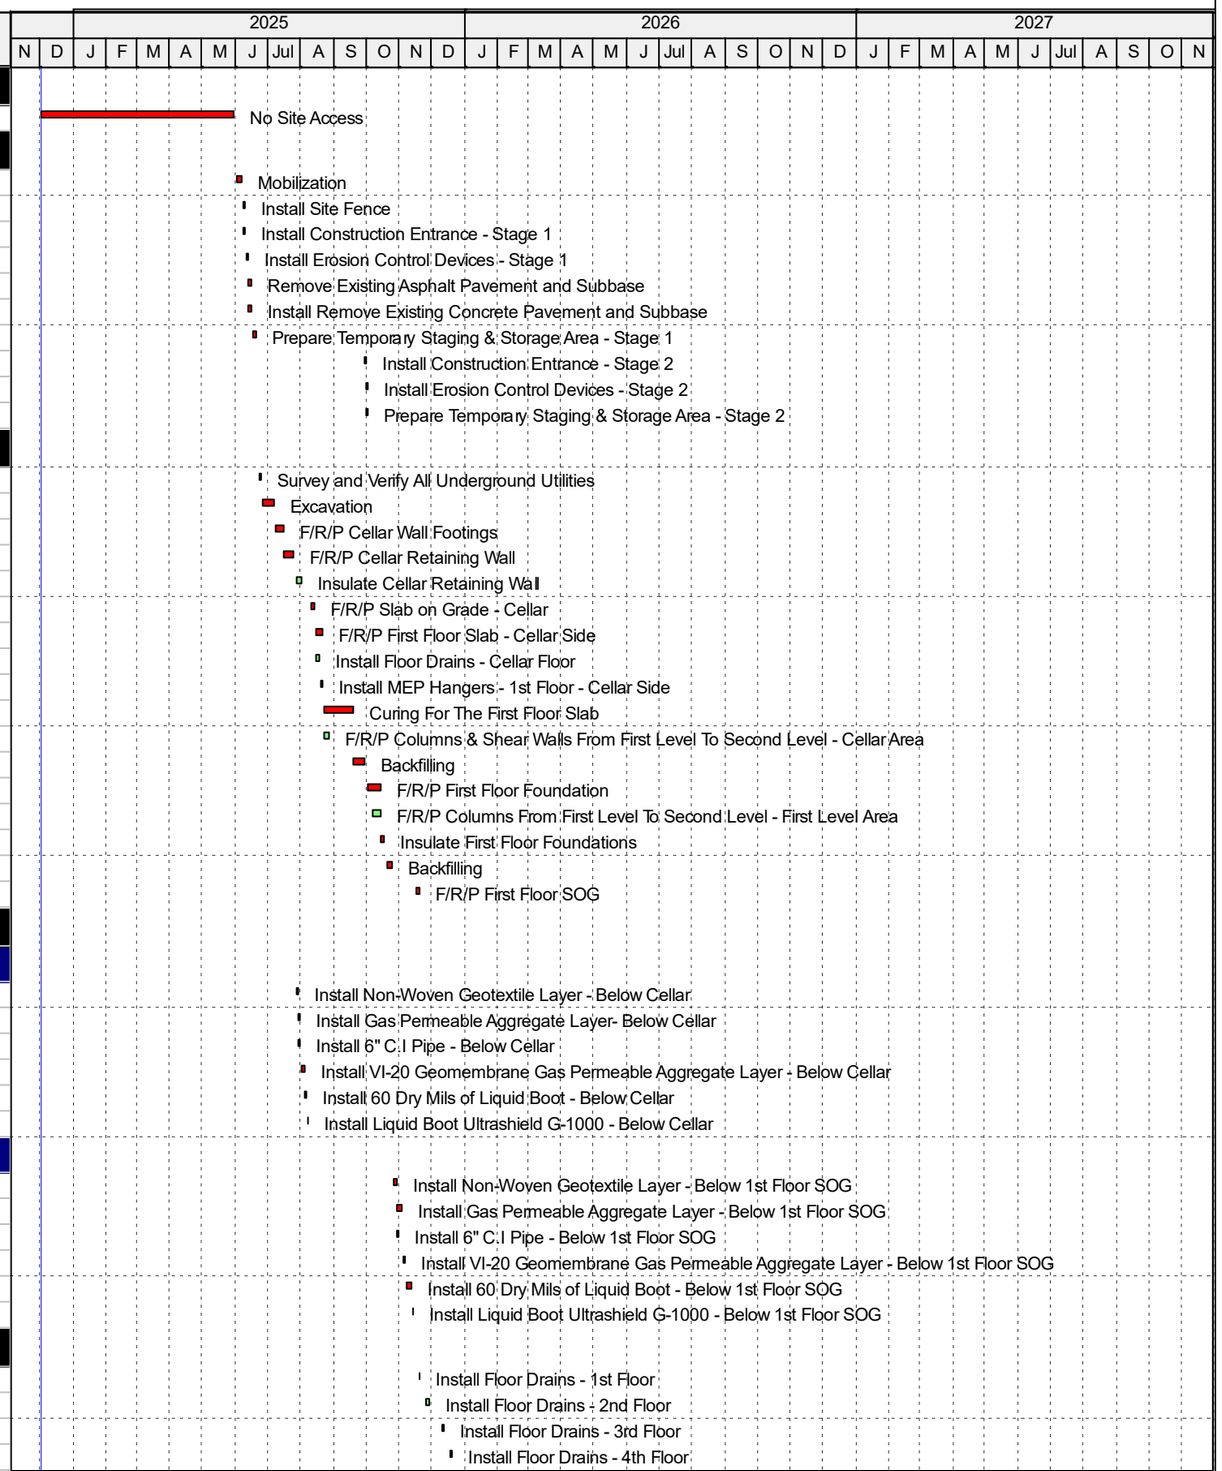

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

TECHNICO CONSTRUCTION PROJECTS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1580	Install Floor Drains - Lower Roof	2	29-Dec-25	30-Dec-25
CON-1680	Install Floor Drains - Upper Roof	2	07-Jan-26	08-Jan-26
Super Structure		36	21-Nov-25	14-Jan-26
CON-1400	F/R/P Concrete Slab - 2nd Floor	5	21-Nov-25	28-Nov-25
CON-1430	F/R/P Columns & Shear Walls From Second Floor To Third Floor	3	01-Dec-25	03-Dec-25
CON-1440	F/R/P Concrete Slab - 3rd Floor	5	04-Dec-25	10-Dec-25
CON-1460	F/R/P Columns & Shear Walls From Third Floor To Fourth Floor	3	11-Dec-25	15-Dec-25
CON-1490	F/R/P Concrete Slab - 4th Floor	4	16-Dec-25	19-Dec-25
CON-1540	Install Mainroof Posts and Framing	7	22-Dec-25	31-Dec-25
CON-1550	F/R/P Concrete Columns From Fourth Slab to Lower Roof Slab- 4th Floor	2	22-Dec-25	23-Dec-25
CON-1560	F/R/P Concrete Slab- Lower Roof	4	24-Dec-25	30-Dec-25
CON-1590	Install Penthouse Posts and Roof Framing	3	31-Dec-25	05-Jan-26
CON-1610	F/R/P Parapets - Lower Roof	3	31-Dec-25	05-Jan-26
CON-1620	F/R/P Concrete Deck Slab - Upper Roof	5	02-Jan-26	08-Jan-26
CON-1700	F/R/P Columns and Slab of The Bulkheads	4	09-Jan-26	14-Jan-26
CON-1730	F/R/P Parapets - Upper Roof	3	09-Jan-26	13-Jan-26
MEP Hangers		29	26-Nov-25	08-Jan-26
CON-1410	Install MEP Hangers - 2nd Floor	2	26-Nov-25	28-Nov-25
CON-1450	Install MEP Hangers - 3rd Floor	2	09-Dec-25	10-Dec-25
CON-1510	Install MEP Hangers - 4th Floor	2	18-Dec-25	19-Dec-25
CON-1570	Install MEP Hangers - Lower Roof	2	29-Dec-25	30-Dec-25
CON-1670	Install MEP Hangers - Upper Roof	2	07-Jan-26	08-Jan-26
Material Hoist		108	11-Dec-25	15-May-26
CON-1480	Install Elevator Hoist Pad	3	11-Dec-25	15-Dec-25
CON-1500	Erect Material Hoist	2	16-Dec-25	17-Dec-25
CON-1530	Drop Test & Sign-Off	2	18-Dec-25	19-Dec-25
CON-4660	Dismantle Hoist	5	27-Apr-26	01-May-26
CON-4780	Demolish Hoist Pad	5	04-May-26	08-May-26
CON-4900	Hoist In-Fill	5	11-May-26	15-May-26
Dunnage		13	31-Dec-25	20-Jan-26
CON-1600	Install Dunnage Framing - Lower Roof	4	31-Dec-25	06-Jan-26
CON-1710	Install Dunnage Framing - Upper Roof	7	09-Jan-26	20-Jan-26
Roofing		64	07-Jan-26	08-Apr-26
Lower Roof		48	07-Jan-26	17-Mar-26
Insulation		30	07-Jan-26	19-Feb-26
CON-1630	Pour Concrete Topping Slab	3	07-Jan-26	09-Jan-26
CON-1740	Install Hot Fluid-Applied Rubberized Asphalt Fabric-Reinforced Roofing Membrane	4	12-Jan-26	15-Jan-26
CON-1860	Install Fabric Reinforcing Sheet	4	16-Jan-26	22-Jan-26
CON-2090	Install Protection Sheet and Roof Barrier	3	23-Jan-26	27-Jan-26
CON-2250	Install 1/2" Drainage Panel	3	28-Jan-26	30-Jan-26
CON-2450	Install 8" Roof Insulation (R-40 Min) Multi-Layered and Staggered	5	02-Feb-26	06-Feb-26
CON-2760	Install Filter Fabric	3	09-Feb-26	11-Feb-26
CON-2880	Lower Roofing Testing	5	12-Feb-26	19-Feb-26
Sedum Green Roof		18	20-Feb-26	17-Mar-26
CON-3160	Install Air Layer	2	20-Feb-26	23-Feb-26
CON-3290	Install Mineral Water Retention Layer	4	24-Feb-26	27-Feb-26
CON-3370	Install 18" Wide Filter Fabric Strip	2	02-Mar-26	03-Mar-26
CON-3470	Install Extensive Growing Media	5	04-Mar-26	10-Mar-26
CON-3800	Install Sedum Mat	5	11-Mar-26	17-Mar-26
Concrete Pavers Roof		12	20-Feb-26	09-Mar-26
CON-3170	Install Paver Pedestal System	5	20-Feb-26	26-Feb-26



Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

TECHNICO CONSTRUCTION PROJECS

Prepared By: A.A			
Date	Revision	Checked	Approved
16-Dec-24	00	AR	


Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3340	Install Concrete Pavers	7	27-Feb-26	09-Mar-26
Upper Roof		55	21-Jan-26	08-Apr-26
Insulation		31	21-Jan-26	05-Mar-26
CON-1960	Pour Concrete Topping Slab	4	21-Jan-26	26-Jan-26
CON-2220	Install Hot Fluid-Applied Rubberized Asphalt Fabric-Reinforced Roofing Membrane	5	27-Jan-26	02-Feb-26
CON-2510	Install Fabric Reinforcing Sheet	4	03-Feb-26	06-Feb-26
CON-2770	Install Protection Sheet and Roof Barrier	4	09-Feb-26	12-Feb-26
CON-2890	Install 1/2" Drainage Panel	4	13-Feb-26	19-Feb-26
CON-3180	Install 8" Roof Insulation (R-40 Min) Multi-Layered and Staggered	5	20-Feb-26	26-Feb-26
CON-3350	Install Filter Fabric	3	27-Feb-26	03-Mar-26
CON-3490	Upper Roofing Testing	2	04-Mar-26	05-Mar-26
Sedum Green Roof		24	06-Mar-26	08-Apr-26
CON-3610	Install Air Layer	3	06-Mar-26	10-Mar-26
CON-3810	Install Mineral Water Retention Layer	5	11-Mar-26	17-Mar-26
CON-4060	Install 18" Wide Filter Fabric Strip	3	18-Mar-26	20-Mar-26
CON-4190	Install Extensive Growing Media	6	23-Mar-26	30-Mar-26
CON-4320	Install Sedum Mat	7	31-Mar-26	08-Apr-26
Concrete Pavers Roof		14	06-Mar-26	25-Mar-26
CON-3620	Install Paver Pedestal System	6	06-Mar-26	13-Mar-26
CON-3960	Install Concrete Pavers	8	16-Mar-26	25-Mar-26
Roof Top Units (RTUs)		15	07-Jan-26	28-Jan-26
CON-1640	Install RTU-2 - Lower Roof	6	07-Jan-26	14-Jan-26
CON-1650	Install Fans - Lower Roof	4	07-Jan-26	12-Jan-26
CON-1660	Install Emergency Generator - Lower Roof	10	07-Jan-26	21-Jan-26
CON-1970	Install RTU-1 - Upper Roof	6	21-Jan-26	28-Jan-26
CON-1980	Install RTU-3 - Upper Roof	6	21-Jan-26	28-Jan-26
CON-1990	Install RTU-4 - Upper Roof	6	21-Jan-26	28-Jan-26
CON-2000	Install Fans - Upper Roof	4	21-Jan-26	26-Jan-26
HVAC Rough-Ins		102	09-Jan-26	04-Jun-26
Duct Risers		18	09-Jan-26	04-Feb-26
CON-1720	Rough-in Duct Risers - Cellar Floor	3	09-Jan-26	13-Jan-26
CON-1800	Rough-in Duct Risers - 2nd Floor	3	14-Jan-26	16-Jan-26
CON-1900	Rough-in Duct Risers - 3rd Floor	3	20-Jan-26	22-Jan-26
CON-2150	Rough-in Duct Risers - 4th Floor	3	23-Jan-26	27-Jan-26
CON-2260	Rough-in Duct Risers - Lower Roof	3	28-Jan-26	30-Jan-26
CON-2460	Rough-in Duct Risers - 1st Floor	3	02-Feb-26	04-Feb-26
Duct Horizontals		98	15-Jan-26	04-Jun-26
CON-1850	Rough-in Duct Work -VAV Devices & Diffusers - Cellar Floor	5	15-Jan-26	22-Jan-26
CON-2130	Rough-in Duct Work -VAV Devices & Diffusers - 2nd Floor	5	23-Jan-26	29-Jan-26
CON-2390	Rough-in Duct Work -VAV Devices & Diffusers - 3rd Floor	5	30-Jan-26	05-Feb-26
CON-2680	Rough-in Duct Work -VAV Devices & Diffusers - 4th Floor	5	06-Feb-26	12-Feb-26
CON-2920	Rough-in Duct Work -VAV Devices & Diffusers - Lower Roof	5	13-Feb-26	20-Feb-26
CON-5120	Rough-in Duct Work -VAV Devices & Diffusers - 1st Floor	5	29-May-26	04-Jun-26
Refrigerant Piping		99	14-Jan-26	04-Jun-26
CON-1790	Rough-in Refrigerant Piping - Cellar Floor	5	14-Jan-26	21-Jan-26
CON-2040	Rough-in Refrigerant Piping - 2nd Floor	5	22-Jan-26	28-Jan-26
CON-2330	Rough-in Refrigerant Piping - 3rd Floor	5	29-Jan-26	04-Feb-26
CON-2590	Rough-in Refrigerant Piping - 4th Floor	5	05-Feb-26	11-Feb-26
CON-2870	Rough-in Refrigerant Piping - Lower Roof	5	12-Feb-26	19-Feb-26
CON-5130	Rough-in Refrigerant Piping - 1st Floor	5	29-May-26	04-Jun-26
Layout		104	09-Jan-26	08-Jun-26




Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1690	Layout - Cellar Floor	2	09-Jan-26	12-Jan-26
CON-1750	Layout - 2nd Floor	2	13-Jan-26	14-Jan-26
CON-1830	Layout - 3rd Floor	2	15-Jan-26	16-Jan-26
CON-1880	Layout - 4th Floor	2	20-Jan-26	21-Jan-26
CON-2010	Layout - Lower Roof	2	22-Jan-26	23-Jan-26
CON-5240	Layout - 1st Floor	2	05-Jun-26	08-Jun-26
Top & Bottom Track		104	13-Jan-26	10-Jun-26
CON-1760	Install Top & Bottom Tracks - Cellar Floor	2	13-Jan-26	14-Jan-26
CON-1840	Install Top & Bottom Tracks - 2nd Floor	2	15-Jan-26	16-Jan-26
CON-1890	Install Top & Bottom Tracks - 3rd Floor	2	20-Jan-26	21-Jan-26
CON-2020	Install Top & Bottom Tracks - 4th Floor	2	22-Jan-26	23-Jan-26
CON-2200	Install Top & Bottom Tracks - Lower Roof	2	26-Jan-26	27-Jan-26
CON-5300	Install Top & Bottom Tracks - 1st Floor	2	09-Jun-26	10-Jun-26
CMU		105	13-Jan-26	11-Jun-26
CON-1770	Install CMU - Cellar Floor	3	13-Jan-26	15-Jan-26
CON-1870	Install CMU - 2nd Floor	3	16-Jan-26	21-Jan-26
CON-2030	Install CMU - 3rd Floor	3	22-Jan-26	26-Jan-26
CON-2230	Install CMU - 4th Floor	3	27-Jan-26	29-Jan-26
CON-2370	Install CMU - Lower Roof	3	30-Jan-26	03-Feb-26
CON-5310	Install CMU - 1st Floor	3	09-Jun-26	11-Jun-26
Elevations		43	14-Jan-26	17-Mar-26
North Elevation (63rd Street)		37	14-Jan-26	09-Mar-26
CON-1780	Install Scaffolding - North Elevation	4	14-Jan-26	20-Jan-26
CON-1940	Scaffolding Inspection & Sign-Off -North Elevation	2	21-Jan-26	22-Jan-26
CON-2060	Install 5/8 Sheathing -North Elevation	4	23-Jan-26	28-Jan-26
CON-2300	Install 6" Semi-Rigid Mineral Wool System -North Elevation	4	29-Jan-26	03-Feb-26
CON-2520	Install Metal Clip System -North Elevation	2	04-Feb-26	05-Feb-26
CON-2530	Install Brick Veneer -North Elevation	3	04-Feb-26	06-Feb-26
CON-2540	Install Window Frames & Windows / Storefronts -North Elevation	5	04-Feb-26	10-Feb-26
CON-2730	Install Graffiti Resistant Coating At Brick -North Elevation	2	09-Feb-26	10-Feb-26
CON-2790	Install Terra Cotta Panel Rainscreen -North Elevation	10	11-Feb-26	25-Feb-26
CON-2800	Install Exterior Wall Lights -North Elevation	2	11-Feb-26	12-Feb-26
CON-3310	Paint Exterior Elevation @ Window Sections -North Elevation	3	26-Feb-26	02-Mar-26
CON-3440	Scaffolding Removal Inspection & Sign-Off -North Elevation	2	03-Mar-26	04-Mar-26
CON-3500	Dismantle Scaffolding -North Elevation	3	05-Mar-26	09-Mar-26
East Elevation		25	21-Jan-26	25-Feb-26
CON-1950	Install Scaffolding - East Elevation	2	21-Jan-26	22-Jan-26
CON-2070	Scaffolding Inspection & Sign-Off - East Elevation	2	23-Jan-26	26-Jan-26
CON-2210	Install 5/8 Sheathing - East Elevation	3	27-Jan-26	29-Jan-26
CON-2350	Install 6" Semi-Rigid Mineral Wool System - East Elevation	3	30-Jan-26	03-Feb-26
CON-2550	Install Metal Clip System - East Elevation	2	04-Feb-26	05-Feb-26
CON-2560	Install Brick Veneer - East Elevation	2	04-Feb-26	05-Feb-26
CON-2570	Install Window Frames & Windows / Storefronts - East Elevation	3	04-Feb-26	06-Feb-26
CON-2650	Install Graffiti Resistant Coating At Brick - East Elevation	2	06-Feb-26	09-Feb-26
CON-2740	Install Terra Cotta Panel Rainscreen - East Elevation	6	09-Feb-26	17-Feb-26
CON-3010	Paint Exterior Elevation @ Window Sections - East Elevation	2	18-Feb-26	19-Feb-26
CON-3130	Scaffolding Removal Inspection & Sign-Off - East Elevation	2	20-Feb-26	23-Feb-26
CON-3280	Dismantle Scaffolding - East Elevation	2	24-Feb-26	25-Feb-26
South Elevation		37	23-Jan-26	17-Mar-26
CON-2080	Install Scaffolding - South Elevation	4	23-Jan-26	28-Jan-26
CON-2310	Scaffolding Inspection & Sign-Off -South Elevation	2	29-Jan-26	30-Jan-26

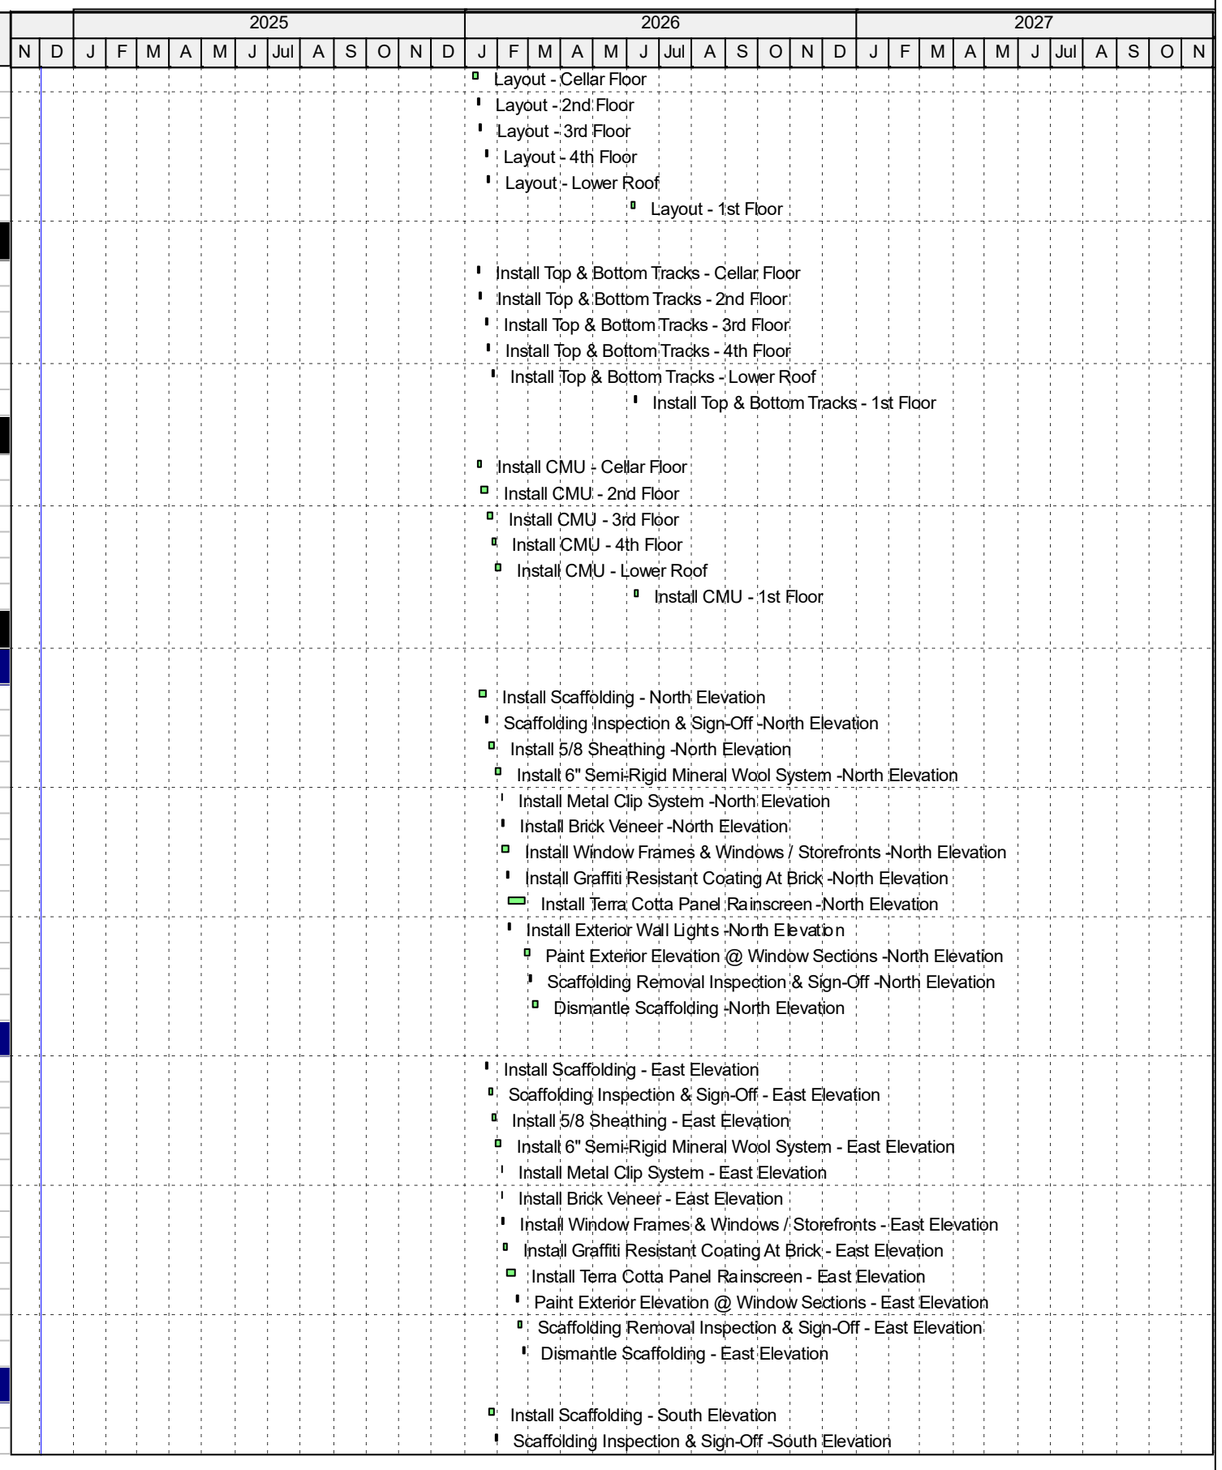


Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2430	Install 5/8 Sheathing -South Elevation	4	02-Feb-26	05-Feb-26
CON-2660	Install 6" Semi-Rigid Mineral Wool System -South Elevation	4	06-Feb-26	11-Feb-26
CON-2810	Install Metal Clip System -South Elevation	2	12-Feb-26	13-Feb-26
CON-2820	Install Brick Veneer -South Elevation	3	12-Feb-26	17-Feb-26
CON-2830	Install Window Frames & Windows / Storefronts -South Elevation	5	12-Feb-26	19-Feb-26
CON-3020	Install Graffiti Resistant Coating At Brick -South Elevation	2	18-Feb-26	19-Feb-26
CON-3140	Install Terra Cotta Panel Rainscreen -South Elevation	10	20-Feb-26	05-Mar-26
CON-3150	Install Wall Speakers -South Elevation	2	20-Feb-26	23-Feb-26
CON-3600	Paint Exterior Elevation @ Window Sections -South Elevation	3	06-Mar-26	10-Mar-26
CON-3790	Scaffolding Removal Inspection & Sign-Off -South Elevation	2	11-Mar-26	12-Mar-26
CON-3940	Dismantle Scaffolding -South Elevation	3	13-Mar-26	17-Mar-26
West Elevation		25	29-Jan-26	05-Mar-26
CON-2320	Install Scaffolding - West Elevation	2	29-Jan-26	30-Jan-26
CON-2440	Scaffolding Inspection & Sign-Off - West Elevation	2	02-Feb-26	03-Feb-26
CON-2580	Install 5/8 Sheathing - West Elevation	3	04-Feb-26	06-Feb-26
CON-2750	Install 6" Semi-Rigid Mineral Wool System - West Elevation	3	09-Feb-26	11-Feb-26
CON-2840	Install Metal Clip System - West Elevation	2	12-Feb-26	13-Feb-26
CON-2850	Install Brick Veneer - West Elevation	2	12-Feb-26	13-Feb-26
CON-2860	Install Window Frames & Windows / Storefronts - West Elevation	3	12-Feb-26	17-Feb-26
CON-3000	Install Graffiti Resistant Coating At Brick - West Elevation	2	17-Feb-26	18-Feb-26
CON-3030	Install Terra Cotta Panel Rainscreen - West Elevation	6	18-Feb-26	25-Feb-26
CON-3320	Paint Exterior Elevation @ Window Sections - West Elevation	2	26-Feb-26	27-Feb-26
CON-3360	Scaffolding Removal Inspection & Sign-Off - West Elevation	2	02-Mar-26	03-Mar-26
CON-3460	Dismantle Scaffolding - West Elevation	2	04-Mar-26	05-Mar-26
SSDS Risers		18	14-Jan-26	09-Feb-26
CON-1820	Rough-in SSDS Risers - Cellar Floor	3	14-Jan-26	16-Jan-26
CON-1930	Rough-in SSDS Risers - 2nd Floor	3	20-Jan-26	22-Jan-26
CON-2190	Rough-in SSDS Risers - 3rd Floor	3	23-Jan-26	27-Jan-26
CON-2290	Rough-in SSDS Risers - 4th Floor	3	28-Jan-26	30-Jan-26
CON-2490	Rough-in SSDS Risers - Lower Roof	3	02-Feb-26	04-Feb-26
CON-2640	Rough-in SSDS Risers - 1st Floor	3	05-Feb-26	09-Feb-26
Electrical Rough-Ins		109	14-Jan-26	18-Jun-26
Electrical Risers		18	14-Jan-26	09-Feb-26
CON-1810	Rough-in Electrical Risers (Power & Low Voltage) - Cellar Floor	3	14-Jan-26	16-Jan-26
CON-1910	Rough-in Electrical Risers (Power & Low Voltage) - 2nd Floor	3	20-Jan-26	22-Jan-26
CON-2170	Rough-in Electrical Risers (Power & Low Voltage) - 3rd Floor	3	23-Jan-26	27-Jan-26
CON-2270	Rough-in Electrical Risers (Power & Low Voltage) - 4th Floor	3	28-Jan-26	30-Jan-26
CON-2470	Rough-in Electrical Risers (Power & Low Voltage) - Lower Roof	3	02-Feb-26	04-Feb-26
CON-2600	Rough-in Electrical Risers (Power & Low Voltage) - 1st Floor	3	05-Feb-26	09-Feb-26
Power Rough-Ins		98	23-Jan-26	11-Jun-26
CON-2160	Rough-in Power Conduits & Wires - Cellar Floor	5	23-Jan-26	29-Jan-26
CON-2400	Rough-in Power Conduits & Wires - 2nd Floor	5	30-Jan-26	05-Feb-26
CON-2690	Rough-in Power Conduits & Wires - 3rd Floor	5	06-Feb-26	12-Feb-26
CON-2940	Rough-in Power Conduits & Wires - 4th Floor	5	13-Feb-26	20-Feb-26
CON-3230	Rough-in Power Conduits & Wires - Lower Roof	5	23-Feb-26	27-Feb-26
CON-5290	Rough-in Power Conduits & Wires - 1st Floor	5	05-Jun-26	11-Jun-26
Low Voltage Rough-Ins		98	30-Jan-26	18-Jun-26
CON-2410	Rough-in Low Voltage Conduits & Wires - Cellar Floor	5	30-Jan-26	05-Feb-26
CON-2700	Rough-in Low Voltage Conduits & Wires - 2nd Floor	5	06-Feb-26	12-Feb-26
CON-2950	Rough-in Low Voltage Conduits & Wires - 3rd Floor	5	13-Feb-26	20-Feb-26
CON-3240	Rough-in Low Voltage Conduits & Wires - 4th Floor	5	23-Feb-26	27-Feb-26

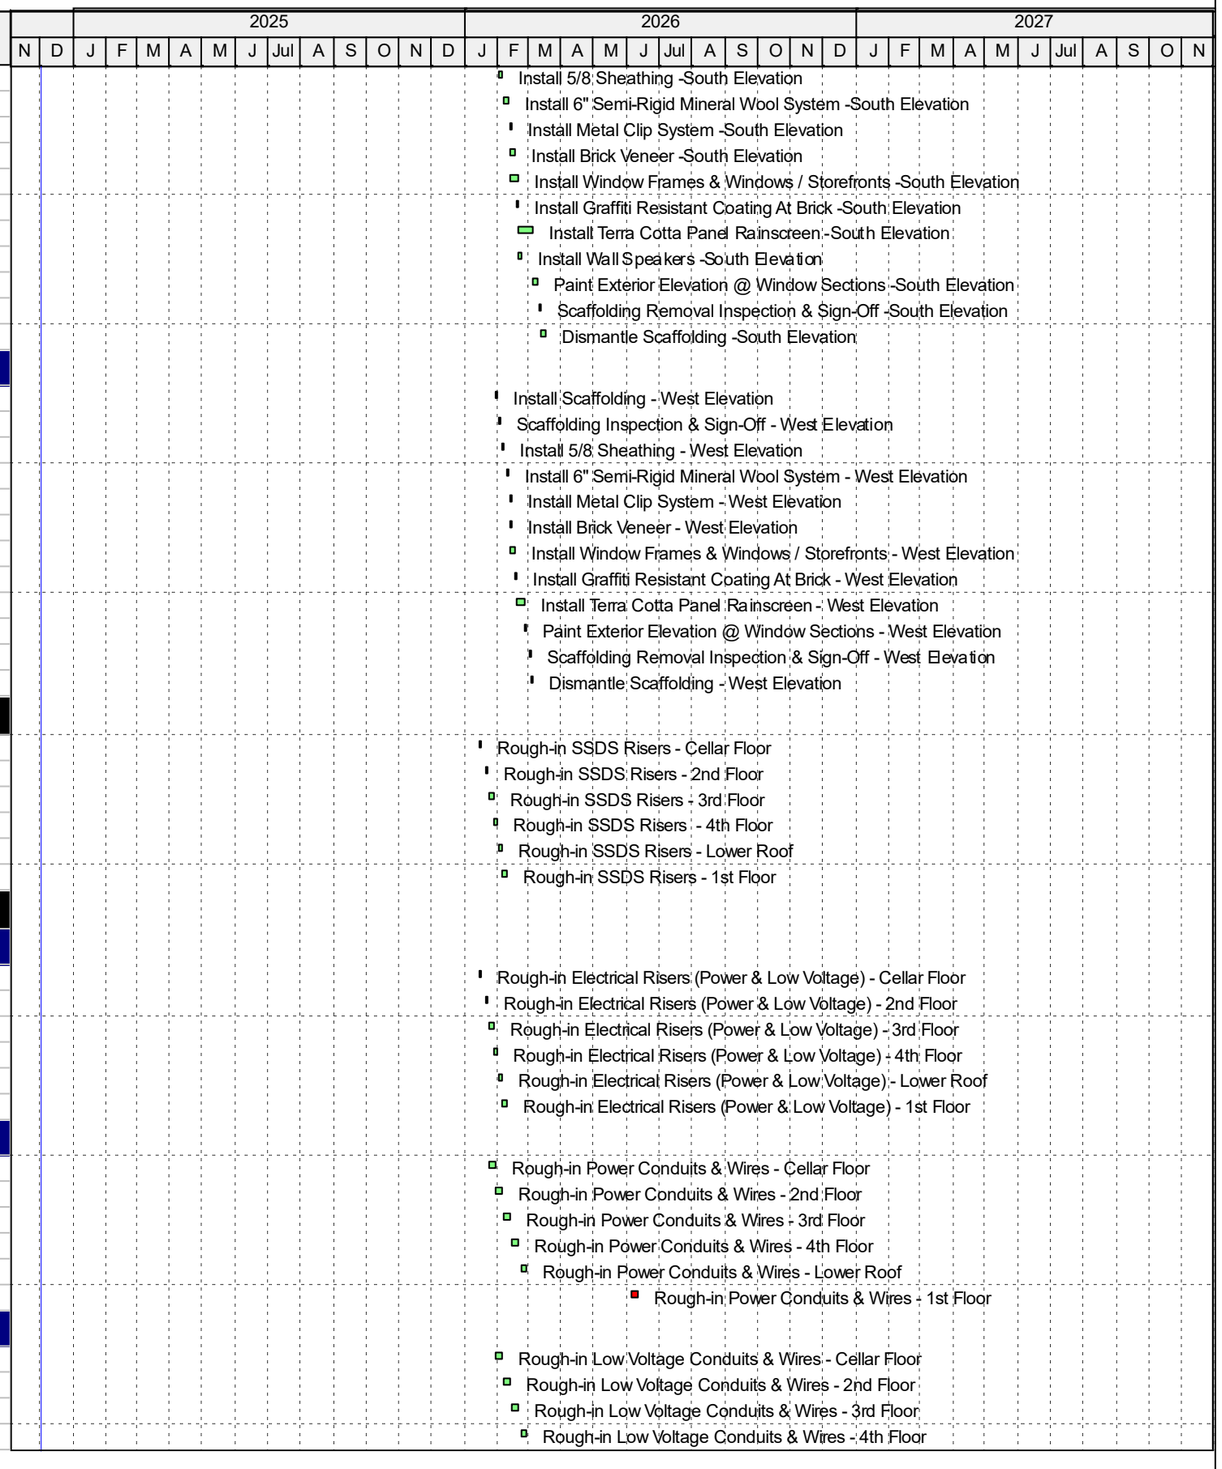

Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3390	Rough-in Low Voltage Conduits & Wires - Lower Roof	5	02-Mar-26	06-Mar-26
CON-5470	Rough-in Low Voltage Conduits & Wires - 1st Floor	5	12-Jun-26	18-Jun-26
Plumbing Rough-ins		111	20-Jan-26	26-Jun-26
Plumbing Risers		18	20-Jan-26	12-Feb-26
CON-1920	Rough-in Plumbing Risers - Cellar Floor	3	20-Jan-26	22-Jan-26
CON-2180	Rough-in Plumbing Risers - 2nd Floor	3	23-Jan-26	27-Jan-26
CON-2280	Rough-in Plumbing Risers - 3rd Floor	3	28-Jan-26	30-Jan-26
CON-2480	Rough-in Plumbing Risers - 4th Floor	3	02-Feb-26	04-Feb-26
CON-2630	Rough-in Plumbing Risers - Lower Roof	3	05-Feb-26	09-Feb-26
CON-2780	Rough-in Plumbing Risers - 1st Floor	3	10-Feb-26	12-Feb-26
Plumbing Horizontals		98	06-Feb-26	26-Jun-26
CON-2710	Rough-in Plumbing Pipes- Cellar Floor	5	06-Feb-26	12-Feb-26
CON-2970	Rough-in Plumbing Pipes - 2nd Floor	5	13-Feb-26	20-Feb-26
CON-3250	Rough-in Plumbing Pipes - 3rd Floor	5	23-Feb-26	27-Feb-26
CON-3410	Rough-in Plumbing Pipes - 4th Floor	5	02-Mar-26	06-Mar-26
CON-3700	Rough-in Plumbing Pipes - Lower Roof	5	09-Mar-26	13-Mar-26
CON-5640	Rough-in Plumbing Pipes - 1st Floor	5	22-Jun-26	26-Jun-26
Mechanical Equipment		101	23-Jan-26	16-Jun-26
CON-2110	Install AC-C17.1 - Cellar	3	23-Jan-26	27-Jan-26
CON-2120	Install AC-C17.2 - Cellar	3	23-Jan-26	27-Jan-26
CON-2140	Install Electric Unit Heater - Cellar Floor	2	23-Jan-26	26-Jan-26
CON-2380	Install AC-204 - 2nd Floor	3	30-Jan-26	03-Feb-26
CON-2910	Install AC-412 - 4th Floor	3	13-Feb-26	18-Feb-26
CON-3220	Install Electric Unit Heater - Lower Roof	2	23-Feb-26	24-Feb-26
CON-5250	Install Heat Pump Unit (HP-108 B) - 1st Floor	4	05-Jun-26	10-Jun-26
CON-5260	Install Electrical Heat Air Curtain - 1st Floor	2	05-Jun-26	08-Jun-26
CON-5280	Install Electric Unit Heater - 1st Floor	2	05-Jun-26	08-Jun-26
CON-5460	Install Heat Pump Unit (HP-R02) - Roof	4	11-Jun-26	16-Jun-26
Wall Framing		101	23-Jan-26	16-Jun-26
CON-2100	Install Steel Studs - Cellar Floor	4	23-Jan-26	28-Jan-26
CON-2360	Install Steel Studs - 2nd Floor	4	30-Jan-26	04-Feb-26
CON-2670	Install Steel Studs - 3rd Floor	4	06-Feb-26	11-Feb-26
CON-2900	Install Steel Studs - 4th Floor	4	13-Feb-26	19-Feb-26
CON-3200	Install Steel Studs - Lower Roof	4	23-Feb-26	26-Feb-26
CON-5450	Install Steel Studs - 1st Floor	4	11-Jun-26	16-Jun-26
Special Rooms		146	30-Jan-26	27-Aug-26
C17 - Electrical Room - Cellar		38	30-Jan-26	25-Mar-26
CON-2420	Install Service End Box	4	30-Jan-26	04-Feb-26
CON-2610	Install Switch Boards (SWBD-1, SWBD-2, SWBD-3)	10	05-Feb-26	19-Feb-26
CON-2620	Install Fire Alarm Fused Disconnect Switch	3	05-Feb-26	09-Feb-26
CON-3190	Install Main Service Switch Board (MSS#1 & MSS#2)	8	20-Feb-26	03-Mar-26
CON-3480	Install TAP Section	3	04-Mar-26	06-Mar-26
CON-3690	Install Dry-Type Transformer	6	09-Mar-26	16-Mar-26
CON-4020	Install 2 Current Transformers (C/T)	4	17-Mar-26	20-Mar-26
CON-4210	Install Power and Lighting Panels	3	23-Mar-26	25-Mar-26
C06 - Water Meter Room - Cellar		8	13-Feb-26	25-Feb-26
CON-2960	Install Main Ground Bus	3	13-Feb-26	18-Feb-26
CON-3050	Install Domestic Water Booster Pump (DWBP-1)	5	19-Feb-26	25-Feb-26
CON-3060	Install Sprinkler Booster Panel	3	19-Feb-26	23-Feb-26
CON-3070	Install Jockey Pump	3	19-Feb-26	23-Feb-26

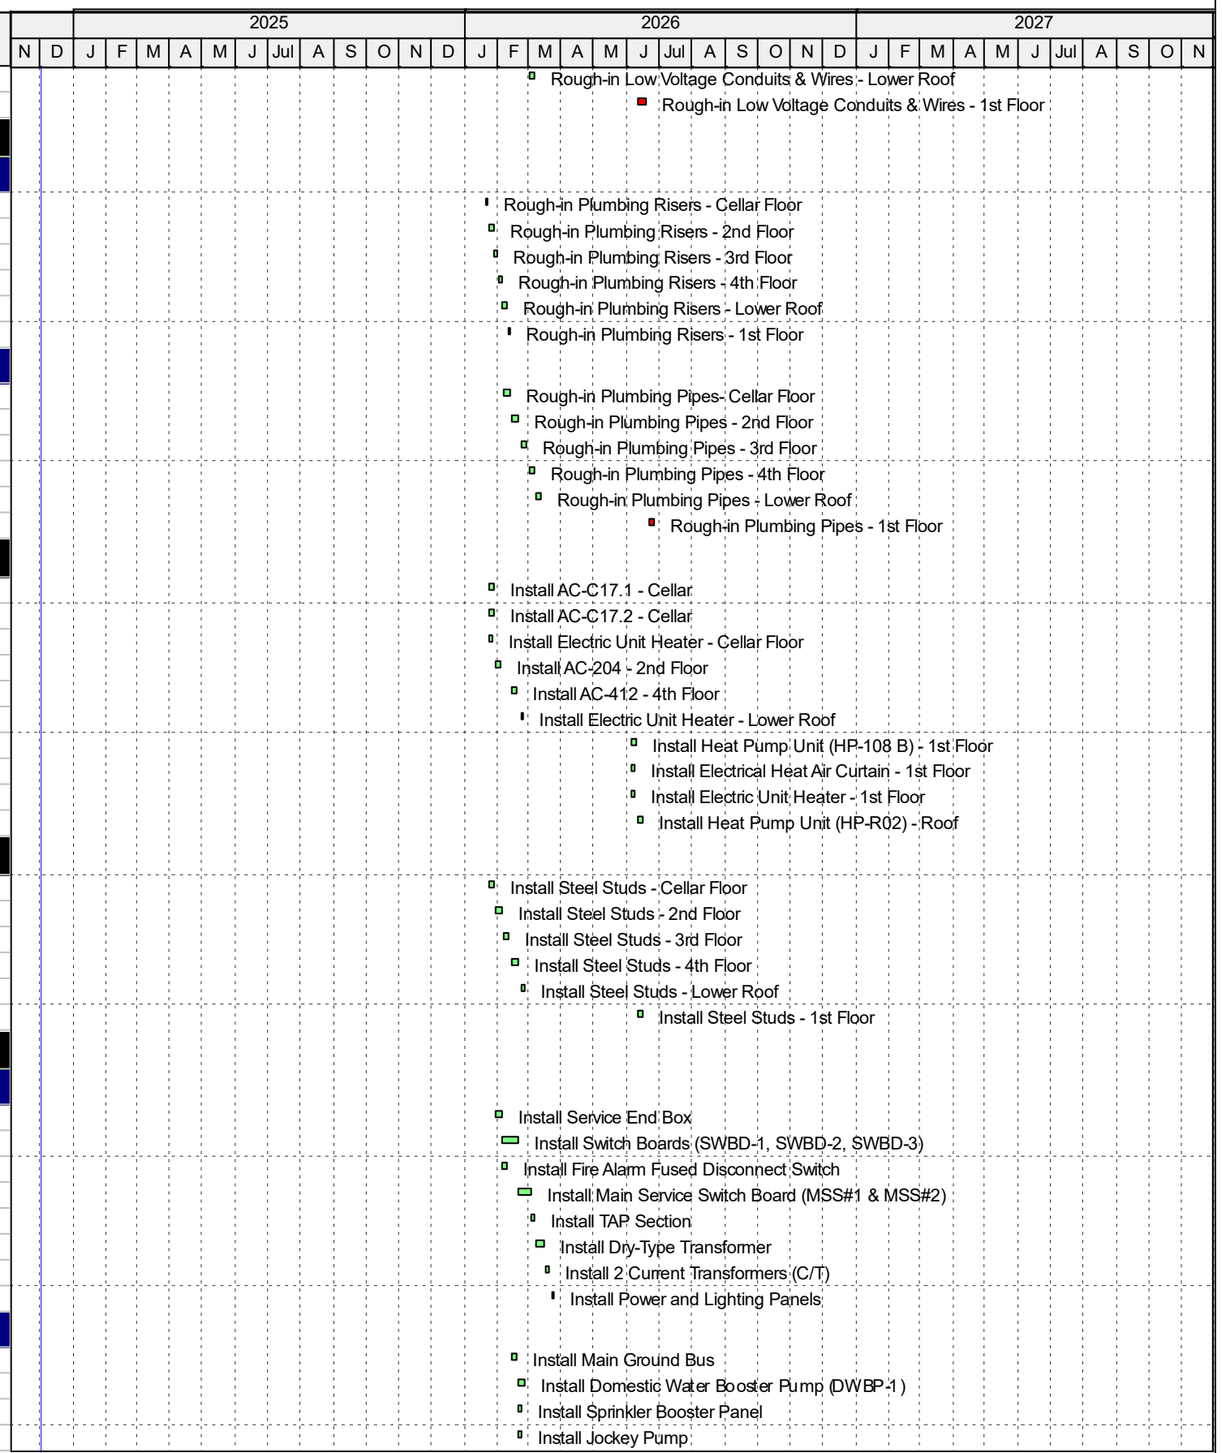

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

TECHNICO CONSTRUCTION PROJECTS

Prepared By: A.A			
Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3080	Install Water Filter Devices	3	19-Feb-26	23-Feb-26
CON-3090	Install Domestic Cold Water Booster Pump (DWBP-1)	4	19-Feb-26	24-Feb-26
CON-3100	Install Duplex Sewage Ejector Pump (SE-1)	4	19-Feb-26	24-Feb-26
CON-3110	Install Sprinkler Booster Pumps	4	19-Feb-26	24-Feb-26
C15 - Fuel Tank Room - Cellar		25	13-Feb-26	20-Mar-26
CON-2930	F/R/P Concrete Pads - Fuel Tank Room	3	13-Feb-26	18-Feb-26
CON-3040	Install Fuel Oil Transfer Pump (FP-1) - Fuel Tank Room	4	19-Feb-26	24-Feb-26
CON-3300	Install Fuel Oil Filtration System (FFS-1) - Fuel Tank Room	4	25-Feb-26	02-Mar-26
CON-3450	Install 275 GAL NYC Fuel Tank With 200% Secondary Containment	6	03-Mar-26	10-Mar-26
CON-3820	Install Fuel Oil Pipings	3	11-Mar-26	13-Mar-26
CON-3980	Install 55 GAL Spill Tank with Sensor Alarm	3	16-Mar-26	18-Mar-26
CON-4100	Install Oil Leak Detector CAC	2	19-Mar-26	20-Mar-26
Food Service Room - 1st Floor		15	29-Jun-26	20-Jul-26
CON-5670	Install Hot Water Circulator Pump (CP-1) / (CP-2)	4	29-Jun-26	02-Jul-26
CON-5790	Install Grease Interceptor (GI-1) / (GI-2)	4	06-Jul-26	09-Jul-26
CON-5830	Install Kitchen Equipment	7	10-Jul-26	20-Jul-26
204 - MDF Room - 2nd Floor		42	29-May-26	29-Jul-26
CON-5150	Install Voice Cabinet	7	29-May-26	08-Jun-26
CON-5340	Install Data Equipment Rack	7	09-Jun-26	17-Jun-26
CON-5540	Install Data Cabinet Patch Panel Rack	7	18-Jun-26	29-Jun-26
CON-5690	Install Vertical Wire Manager	7	30-Jun-26	09-Jul-26
CON-5910	Install MDF Telephone System Backboard	7	10-Jul-26	20-Jul-26
CON-6020	Install Telecom Panel	7	21-Jul-26	29-Jul-26
407B - Gymnatorium - 4th Floor		25	18-Jun-26	24-Jul-26
CON-5630	Install Gym Flooring	10	18-Jun-26	02-Jul-26
CON-5800	Install Gym Equipment	15	06-Jul-26	24-Jul-26
412 - IDF - 4th Floor		35	10-Jul-26	27-Aug-26
CON-5820	Install Bacnet Data Enclosure	7	10-Jul-26	20-Jul-26
CON-5960	Install PA Rack	7	21-Jul-26	29-Jul-26
CON-6040	Install Voice Rack	7	30-Jul-26	07-Aug-26
CON-6120	Install Data Rack	7	10-Aug-26	18-Aug-26
CON-6190	Install Voice Cabinet	7	19-Aug-26	27-Aug-26
R02 - Elevator Machine Room - Lower Roof		26	02-Mar-26	06-Apr-26
CON-3400	Install EMR Panel	4	02-Mar-26	05-Mar-26
CON-3640	Install Elevator Machines	10	06-Mar-26	19-Mar-26
CON-4150	Install Elevator Controls	6	20-Mar-26	27-Mar-26
CON-4280	Install Elevator Cabinets	6	30-Mar-26	06-Apr-26
R01 - HVAC/ELEC. Penthouse - Lower Roof		35	06-Mar-26	23-Apr-26
CON-3630	Install Power Panels	4	06-Mar-26	11-Mar-26
CON-3890	Install Bacnet Data Enclosure	6	12-Mar-26	19-Mar-26
CON-4140	Install Switch Boards (SWBD-4, SWBD-5)	4	20-Mar-26	25-Mar-26
CON-4250	Install Secondary Transformer Disconnect Switch (MSWB-C)	5	26-Mar-26	01-Apr-26
CON-4350	Install Domestic Hot Water Heat Pump (HWHP-1 & HWHP-2)	4	02-Apr-26	07-Apr-26
CON-4410	Install Storage Tank (ST-1)	6	08-Apr-26	15-Apr-26
CON-4560	Install Thermal Expansion Tank (ET-1)	6	16-Apr-26	23-Apr-26
Electrical Panels		30	06-Feb-26	20-Mar-26
CON-2720	Install Electrical Panels - Cellar Floor	5	06-Feb-26	12-Feb-26
CON-2980	Install Electrical Panels - 2nd Floor	5	13-Feb-26	20-Feb-26
CON-3260	Install Electrical Panels - 3rd Floor	5	23-Feb-26	27-Feb-26
CON-3420	Install Electrical Panels - 4th Floor	5	02-Mar-26	06-Mar-26
CON-3710	Install Electrical Panels - Lower Roof	5	09-Mar-26	13-Mar-26

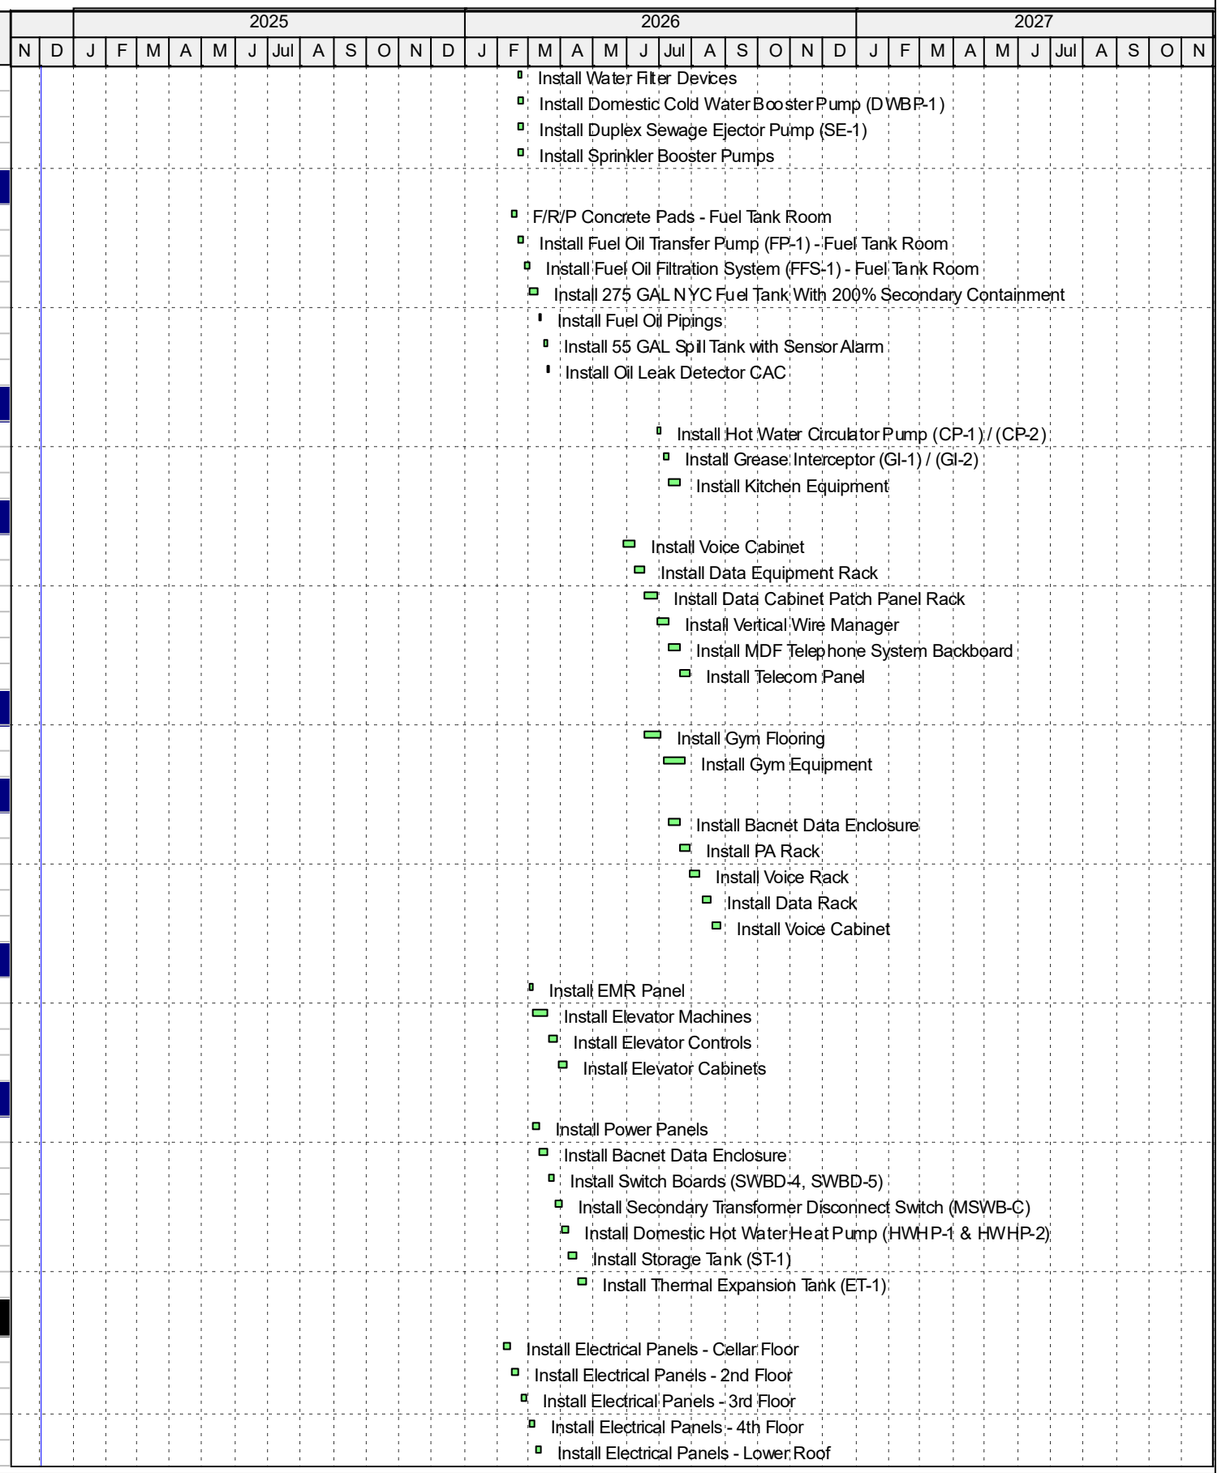

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

TECHNICO CONSTRUCTION PROJECTS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-4000	Install Electrical Panels - 1st Floor	5	16-Mar-26	20-Mar-26
Fire Protection		98	13-Feb-26	06-Jul-26
Sprinkler Piping		98	13-Feb-26	06-Jul-26
CON-2990	Rough-in Sprinkler Piping - Cellar Floor	5	13-Feb-26	20-Feb-26
CON-3270	Rough-in Sprinkler Piping - 2nd Floor	5	23-Feb-26	27-Feb-26
CON-3430	Rough-in Sprinkler Piping - 3rd Floor	5	02-Mar-26	06-Mar-26
CON-3720	Rough-in Sprinkler Piping - 4th Floor	5	09-Mar-26	13-Mar-26
CON-4010	Rough-in Sprinkler Piping - Lower Roof	5	16-Mar-26	20-Mar-26
CON-5680	Rough-in Sprinkler Piping - 1st Floor	5	29-Jun-26	06-Jul-26
Sprinkler Heads		95	19-Feb-26	06-Jul-26
CON-3120	Install Sprinkler Heads - Cellar Floor	2	19-Feb-26	20-Feb-26
CON-3330	Install Sprinkler Heads - 2nd Floor	2	26-Feb-26	27-Feb-26
CON-3510	Install Sprinkler Heads - 3rd Floor	2	05-Mar-26	06-Mar-26
CON-3900	Install Sprinkler Heads - 4th Floor	2	12-Mar-26	13-Mar-26
CON-4120	Install Sprinkler Heads - Lower Roof	2	19-Mar-26	20-Mar-26
CON-5780	Install Sprinkler Heads - 1st Floor	2	02-Jul-26	06-Jul-26
Ceiling Hangers		98	23-Feb-26	13-Jul-26
CON-3210	Install Ceiling Hangers - Cellar Floor	5	23-Feb-26	27-Feb-26
CON-3380	Install Ceiling Hangers - 2nd Floor	5	02-Mar-26	06-Mar-26
CON-3680	Install Ceiling Hangers - 3rd Floor	5	09-Mar-26	13-Mar-26
CON-3970	Install Ceiling Hangers - 4th Floor	5	16-Mar-26	20-Mar-26
CON-4200	Install Ceiling Hangers - Lower Roof	5	23-Mar-26	27-Mar-26
CON-5810	Install Ceiling Hangers - 1st Floor	5	07-Jul-26	13-Jul-26
Mockup Room		24	06-Mar-26	08-Apr-26
CON-3650	Install Walls GWB-Mockup Room	3	06-Mar-26	10-Mar-26
CON-3850	Install Door Frames-Mockup Room	2	11-Mar-26	12-Mar-26
CON-3950	Install Gypsum Board Ceiling -Mockup Room	3	13-Mar-26	17-Mar-26
CON-4070	Install Doors & Hardware-Mockup Room	2	18-Mar-26	19-Mar-26
CON-4160	Paint First coat -Mockup Room	3	20-Mar-26	24-Mar-26
CON-4230	Flooring Finishes-Mockup Room	3	25-Mar-26	27-Mar-26
CON-4290	Paint Second coat-Mockup Room	3	30-Mar-26	01-Apr-26
CON-4360	Install Furniture & Signs -Mockup Room	3	02-Apr-26	06-Apr-26
CON-4390	Mockup Room Inspection & Punchlist	2	07-Apr-26	08-Apr-26
Site Area		69	06-Mar-26	11-Jun-26
Underground Utilities		53	06-Mar-26	19-May-26
Stormwater Drainage System		11	06-Mar-26	20-Mar-26
CON-3520	Install Storm Inlet 1	1	06-Mar-26	06-Mar-26
CON-3530	Install Storm Inlet 2	1	06-Mar-26	06-Mar-26
CON-3540	Install 60 LF of 8-IN DIP [Storm Inlet 1 to Storm Inlet 2]	1	06-Mar-26	06-Mar-26
CON-3660	Install 33 LF of 8-IN DIP [Storm Inlet 2 to Catch Basin 2]	1	09-Mar-26	09-Mar-26
CON-3670	Install Catch Basin 2	1	09-Mar-26	09-Mar-26
CON-3730	Install Grit Champer-1	2	10-Mar-26	11-Mar-26
CON-3740	Install 106 LF of 12-IN DIP [Catch Basin 2 to Grit Champer-1]	2	10-Mar-26	11-Mar-26
CON-3860	Install Storm Manhole-2	1	12-Mar-26	12-Mar-26
CON-3870	Install 9-LF of 12-IN DIP [Grit Champer-1 to Storm Manhole-2]	1	12-Mar-26	12-Mar-26
CON-3880	Install 3-LF of 12-IN DIP [Grit Champer-1 to Stormwater Retention System]	1	12-Mar-26	12-Mar-26
CON-3910	Install 10-IN DIP Roof Leader	1	13-Mar-26	13-Mar-26
CON-3920	Install Stormwater Retention System	3	13-Mar-26	17-Mar-26
CON-3930	Install Catch Basin 2	1	13-Mar-26	13-Mar-26
CON-4030	Install 3-LF of 12-IN DIP [Stormwater Retention System to Overflow Storm Manhole-1]	1	18-Mar-26	18-Mar-26
CON-4040	Install Overflow Storm Manhole-1	1	18-Mar-26	18-Mar-26



Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-4080	Install 43.8 LF of 6-IN DIP [Overflow Storm Manhole-1 to Existing 30-IN x 45IN Combined Sewer]	2	19-Mar-26	20-Mar-26
CON-4130	Connect Sewer System To The Existing Sewer Line	1	20-Mar-26	20-Mar-26
Water Lines		5	06-Mar-26	12-Mar-26
CON-3550	Install Domestic Water Service Piping	3	06-Mar-26	10-Mar-26
CON-3750	Connect Water Piping To The Existing Water Line	2	11-Mar-26	12-Mar-26
Sewer Lines		5	06-Mar-26	12-Mar-26
CON-3560	Install Sewer Piping	3	06-Mar-26	10-Mar-26
CON-3760	Connect Sewer Piping To The Existing Sewer Line	2	11-Mar-26	12-Mar-26
Sanitary Lines		5	06-Mar-26	12-Mar-26
CON-3570	Install Sanitary Piping	3	06-Mar-26	10-Mar-26
CON-3770	Connect Sanitary Piping To The Existing Sanitary Line	2	11-Mar-26	12-Mar-26
Underground Electrical Utilities		11	05-May-26	19-May-26
CON-3580	Install The Transformer Vault	3	05-May-26	07-May-26
CON-3830	Install 6 Sets of 4#500MCM IN 4" RGS Conduits & 3 Spare 4" RGS Conduits Encased In Concrel	3	08-May-26	12-May-26
CON-3840	Install Aluminum Lighting Conductor	3	08-May-26	12-May-26
CON-3990	CON-ED to Insulate 6 Sets of 4#500MCM IN 4" RGS Conduits	3	13-May-26	15-May-26
CON-4110	CON-ED to Connect The 6 Sets of 4#500MCM to The Customer End Box	2	18-May-26	19-May-26
Telecom Service		8	06-Mar-26	17-Mar-26
CON-3590	Install Telecom Service Point of Entry	3	06-Mar-26	10-Mar-26
CON-3780	Verizon To Provide Connection	5	11-Mar-26	17-Mar-26
Builders Pavement		61	18-Mar-26	11-Jun-26
Building Perimeter		14	23-Mar-26	09-Apr-26
CON-4170	Prepare & Compact Subgrade Layer	3	23-Mar-26	25-Mar-26
CON-4240	Install 6-IN Thick Crushed Stone	5	26-Mar-26	01-Apr-26
CON-4330	F/R/P Concrete Pavement	6	02-Apr-26	09-Apr-26
14th Avenue		20	18-Mar-26	14-Apr-26
CON-4050	Install Traffic Control Devices - 14th Avenue	1	18-Mar-26	18-Mar-26
CON-4090	Mill & Remove Existing Asphalt Pavement - 14th Avenue	2	19-Mar-26	20-Mar-26
CON-4180	Excavation For The Full Depth Asphalt Pavement Replacement - 14th Avenue	2	23-Mar-26	24-Mar-26
CON-4220	Install 6-IN Gravel - 14th Avenue	2	25-Mar-26	26-Mar-26
CON-4260	Sawcut & Apply Tack Coat - Before Concrete Base Course - 14th Avenue	2	27-Mar-26	30-Mar-26
CON-4270	Install 6-IN Concrete Base Course - 14th Avenue	2	27-Mar-26	30-Mar-26
CON-4300	Sawcut & Apply Tack Coat - Before Leveling Course - 14th Avenue	2	31-Mar-26	01-Apr-26
CON-4310	Install Leveling Course - 14th Avenue	2	31-Mar-26	01-Apr-26
CON-4340	Install 1.5-Inch Asphalt Binder Course - 14th Avenue	2	02-Apr-26	03-Apr-26
CON-4370	Install 1.5-Inch Thick Asphalt Surface Course - 14th Avenue	2	06-Apr-26	07-Apr-26
CON-4400	Install Pavement Markings - 14th Avenue	2	08-Apr-26	09-Apr-26
CON-4430	Remove and Replace Existing Pedestrian Ramps -14th Avenue	2	10-Apr-26	13-Apr-26
CON-4470	Remove Traffic Control Devices - 14th Avenue	1	14-Apr-26	14-Apr-26
63rd Street		24	08-May-26	11-Jun-26
CON-4480	Install Traffic Control Devices - 63rd Street	1	08-May-26	08-May-26
CON-4500	Mill & Remove Existing Asphalt Pavement - 63rd Street	2	11-May-26	12-May-26
CON-4570	Excavation For The Full Depth Asphalt Pavement Replacement - 63rd Street	2	13-May-26	14-May-26
CON-4630	Install 6-IN Gravel - 63rd Street	2	15-May-26	18-May-26
CON-4650	Sawcut & Apply Tack Coat - Before Concrete Base Course - 63rd Street	2	19-May-26	20-May-26
CON-4670	Install 6-IN Concrete Base Course - 63rd Street	2	21-May-26	22-May-26
CON-4740	Sawcut & Apply Tack Coat - Before Leveling Course - 63rd Street	2	26-May-26	27-May-26
CON-4760	Install Leveling Course - 63rd Street	2	28-May-26	29-May-26
CON-4790	Install 1.5-Inch Asphalt Binder Course - 63rd Street	2	01-Jun-26	02-Jun-26
CON-4820	Install 1.5-Inch Thick Asphalt Surface Course - 63rd Street	2	03-Jun-26	04-Jun-26
CON-4920	Install Pavement Markings - 63rd Street	2	05-Jun-26	08-Jun-26
CON-4940	Remove and Replace Existing Pedestrian Ramps -63rd Street	2	09-Jun-26	10-Jun-26
CON-4950	Remove Traffic Control Devices - 63rd Street	1	11-Jun-26	11-Jun-26



Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

TECHNICO CONSTRUCTION PROJECS

Prepared By: A.A			
Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
Landscape Work		16	10-Apr-26	01-May-26
CON-4440	Install Acrylic Court Surfacing	4	10-Apr-26	15-Apr-26
CON-4450	Install Concrete Pavers	4	10-Apr-26	15-Apr-26
CON-4510	Install Tree Pit	3	16-Apr-26	20-Apr-26
CON-4550	Install Site Gates	3	16-Apr-26	20-Apr-26
CON-4520	Install Elevated Movable Planter	3	21-Apr-26	23-Apr-26
CON-4530	Install Flag Pole	3	24-Apr-26	28-Apr-26
CON-4540	Install Backless Site Bench	3	29-Apr-26	01-May-26
Cafeteria Work		30	21-Apr-26	02-Jun-26
CON-6330	Install Magnetic Induction Loop Wires at Cafeteria	5	21-Apr-26	27-Apr-26
CON-6340	Install Cafeteria Flooring	10	28-Apr-26	11-May-26
CON-6350	Install Cafeteria Assembly	15	12-May-26	02-Jun-26
Wall Gypsum Board		55	09-Apr-26	26-Jun-26
CON-4420	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - Cellar Floor	7	09-Apr-26	17-Apr-26
CON-4580	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 2nd Floor	7	20-Apr-26	28-Apr-26
CON-4690	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 3rd Floor	7	29-Apr-26	07-May-26
CON-4830	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 4th Floor	7	08-May-26	18-May-26
CON-4960	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - Lower Roof	7	19-May-26	28-May-26
CON-5500	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 1st Floor	7	17-Jun-26	26-Jun-26
Ceiling		65	20-Apr-26	22-Jul-26
CON-4590	Install Acoustical Ceiling Tiles- Cellar Floor	7	20-Apr-26	28-Apr-26
CON-4600	Install Gypsum Board Ceiling- Cellar Floor	7	20-Apr-26	28-Apr-26
CON-4700	Install Acoustical Ceiling Tiles - 2nd Floor	7	29-Apr-26	07-May-26
CON-4710	Install Gypsum Board Ceiling - 2nd Floor	7	29-Apr-26	07-May-26
CON-4840	Install Gypsum Board Ceiling - 3rd Floor	7	08-May-26	18-May-26
CON-4850	Install Acoustical Ceiling Tiles - 3rd Floor	7	08-May-26	18-May-26
CON-4970	Install Acoustical Ceiling Tiles - 4th Floor	7	19-May-26	28-May-26
CON-4980	Install Gypsum Board Ceiling- 4th Floor	7	19-May-26	28-May-26
CON-4990	Install TECTUM WOOD Fiber Composition Ceiling Tiles- 4th Floor	7	19-May-26	28-May-26
CON-5100	Install Gypsum Board Ceiling - Lower Roof	7	29-May-26	08-Jun-26
CON-5920	Install Gypsum Board Ceiling - 1st Floor	7	14-Jul-26	22-Jul-26
CON-5930	Install Acoustical Ceiling Tiles - 1st Floor	7	14-Jul-26	22-Jul-26
CON-5940	Install Wood Slat Ceiling - 1st Floor	7	14-Jul-26	22-Jul-26
CON-5950	MCP-Wood Slat Ceiling Panel - 1st Floor	7	14-Jul-26	22-Jul-26
Doors		51	20-Apr-26	01-Jul-26
CON-4610	Install Doors- Cellar Floor	3	20-Apr-26	22-Apr-26
CON-4640	Install Doors- 2nd Floor	3	23-Apr-26	27-Apr-26
CON-4680	Install Doors- 3rd Floor	3	28-Apr-26	30-Apr-26
CON-4750	Install Doors- 4th Floor	3	01-May-26	05-May-26
CON-4800	Install Doors- Lower Roof	3	06-May-26	08-May-26
CON-4910	Install Doors- 1st Floor	3	29-Jun-26	01-Jul-26
First Coat Painting		65	29-Apr-26	31-Jul-26
CON-4730	Install First Coat Painting - Cellar Floor	7	29-Apr-26	07-May-26
CON-4880	Install First Coat Painting - 2nd Floor	7	08-May-26	18-May-26
CON-5050	Install First Coat Painting - 3rd Floor	7	19-May-26	28-May-26
CON-5190	Install First Coat Painting - 4th Floor	7	29-May-26	08-Jun-26
CON-5390	Install First Coat Painting - Lower Roof	7	09-Jun-26	17-Jun-26
CON-6030	Install First Coat Painting - 1st Floor	7	23-Jul-26	31-Jul-26
Electric Wall Convector		12	29-Apr-26	14-May-26
CON-4720	Install Electric Wall Convectors - 2nd Floor	3	29-Apr-26	01-May-26
CON-4770	Install Electric Wall Convectors - 3rd Floor	3	04-May-26	06-May-26

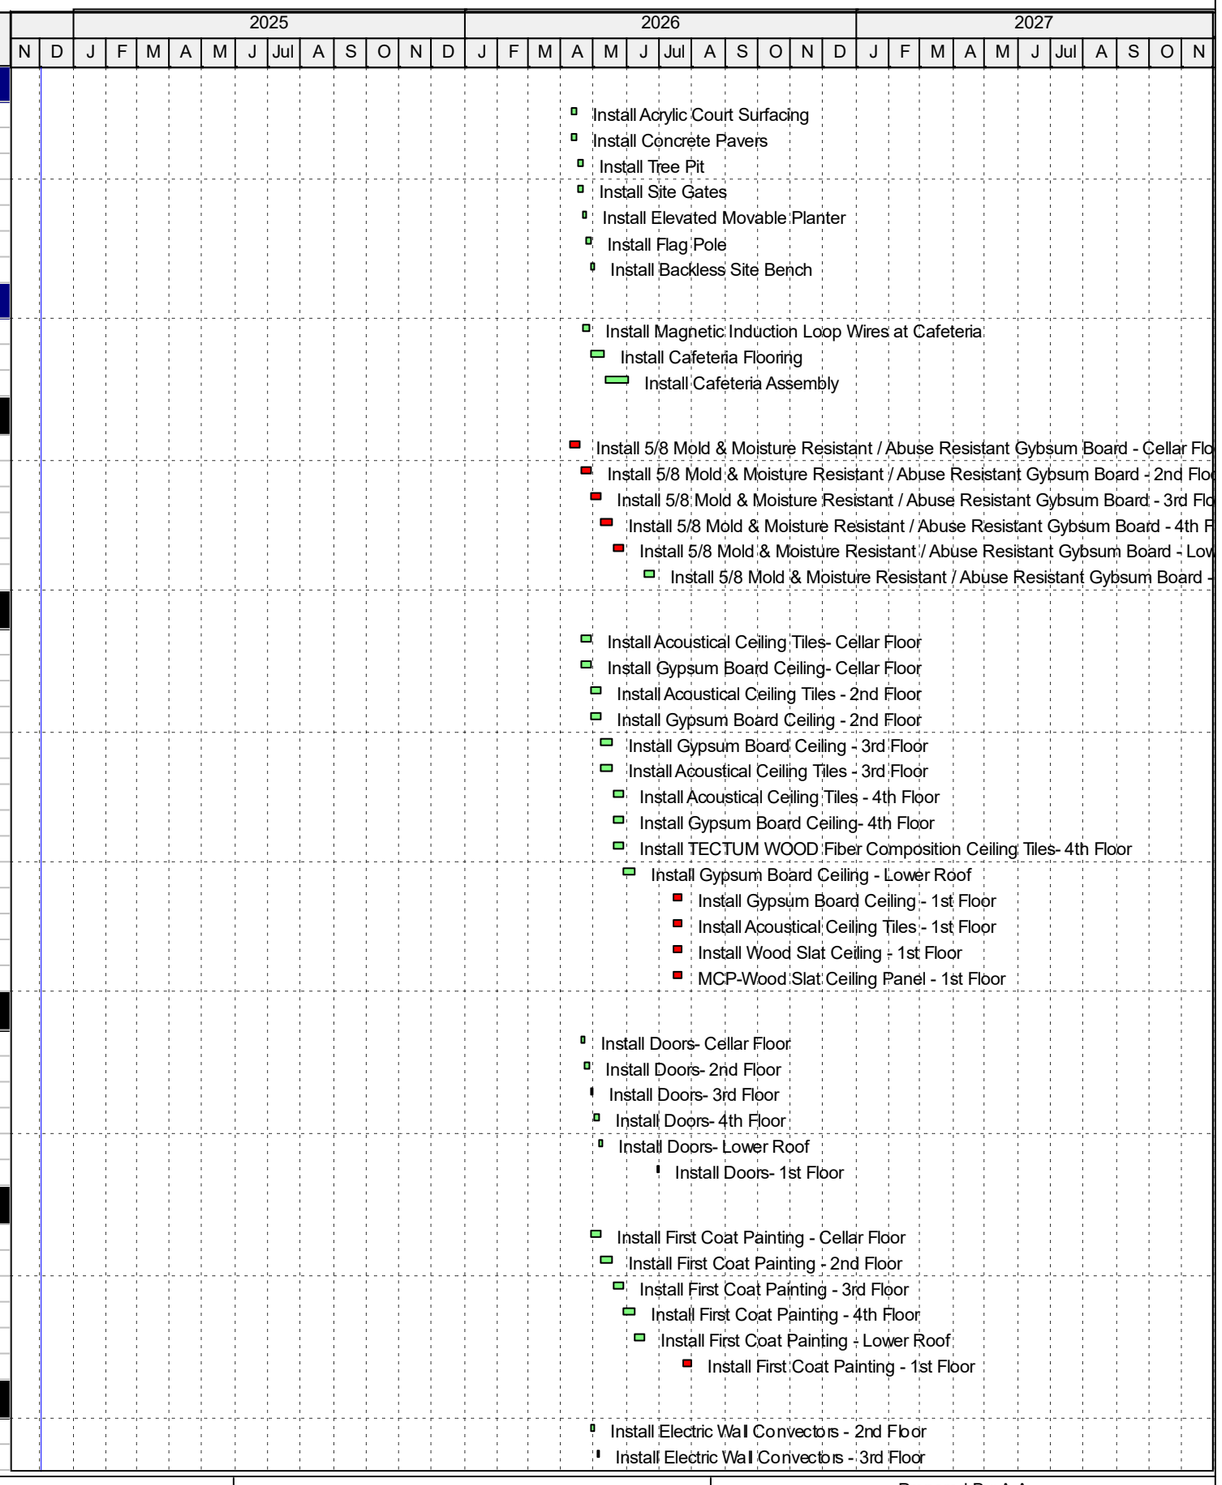

Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-4810	Install Electric Wall Convectors - 4th Floor	3	07-May-26	11-May-26
CON-4930	Install Electric Wall Convectors - 1st Floor	3	12-May-26	14-May-26
Lighting Fixtures		65	08-May-26	11-Aug-26
CON-4870	Install Lighting Fixtures - Cellar Floor	7	08-May-26	18-May-26
CON-5020	Install Lighting Fixtures - 2nd Floor	7	19-May-26	28-May-26
CON-5140	Install Lighting Fixtures - 3rd Floor	7	29-May-26	08-Jun-26
CON-5330	Install Lighting Fixtures - 4th Floor	7	09-Jun-26	17-Jun-26
CON-5530	Install Lighting Fixtures - Lower Roof	7	18-Jun-26	29-Jun-26
CON-6100	Install Lighting Fixtures - 1st Floor	7	03-Aug-26	11-Aug-26
Flooring		65	08-May-26	11-Aug-26
CON-4860	Install Flooring - Cellar Floor	7	08-May-26	18-May-26
CON-5000	Install Flooring - 2nd Floor	7	19-May-26	28-May-26
CON-5110	Install Flooring - 3rd Floor	7	29-May-26	08-Jun-26
CON-5320	Install Flooring - 4th Floor	7	09-Jun-26	17-Jun-26
CON-5520	Install Flooring - Lower Roof	7	18-Jun-26	29-Jun-26
CON-6090	Install Flooring - 1st Floor	7	03-Aug-26	11-Aug-26
Milling Work		65	08-May-26	11-Aug-26
CON-4890	Install Milling Work - Cellar Floor	7	08-May-26	18-May-26
CON-5060	Install Milling Work - 2nd Floor	7	19-May-26	28-May-26
CON-5210	Install Milling Work - 3rd Floor	7	29-May-26	08-Jun-26
CON-5410	Install Milling Work - 4th Floor	7	09-Jun-26	17-Jun-26
CON-5610	Install Milling Work - Lower Roof	7	18-Jun-26	29-Jun-26
CON-6110	Install Milling Work - 1st Floor	7	03-Aug-26	11-Aug-26
Electric Cabinet Heater		21	19-May-26	17-Jun-26
CON-5010	Install Electric Cabinet Heaters - Cellar Floor	3	19-May-26	21-May-26
CON-5080	Install Electric Cabinet Heaters - 2nd Floor	3	22-May-26	27-May-26
CON-5090	Install Electric Cabinet Heaters - 3rd Floor	3	28-May-26	01-Jun-26
CON-5230	Install Electric Cabinet Heaters - 4th Floor	3	02-Jun-26	04-Jun-26
CON-5270	Install Electric Cabinet Heaters - Lower Roof	3	05-Jun-26	09-Jun-26
CON-5440	Install Electric Cabinet Heaters - Upper Roof	3	10-Jun-26	12-Jun-26
CON-5490	Install Electric Cabinet Heaters - 1st Roof	3	15-Jun-26	17-Jun-26
Data System & Video Intercom System		65	19-May-26	20-Aug-26
CON-5030	Install Data & Video Intercome Systems -Cellar Floor	7	19-May-26	28-May-26
CON-5160	Install Data & Video Intercome Systems - 2nd Floor	7	29-May-26	08-Jun-26
CON-5350	Install Data & Video Intercome Systems - 3rd Floor	7	09-Jun-26	17-Jun-26
CON-5550	Install Data & Video Intercome Systems - 4th Floor	7	18-Jun-26	29-Jun-26
CON-5700	Install Data & Video Intercome Systems - Lower Roof	7	30-Jun-26	09-Jul-26
CON-6160	Install Data & Video Intercome Systems - 1st Floor	7	12-Aug-26	20-Aug-26
Plumbing Fixtures		42	19-May-26	20-Jul-26
CON-5040	Install Plumbing Fixtures - Cellar Floor	7	19-May-26	28-May-26
CON-5180	Install Plumbing Fixtures - 2nd Floor	7	29-May-26	08-Jun-26
CON-5380	Install Plumbing Fixtures - 3rd Floor	7	09-Jun-26	17-Jun-26
CON-5590	Install Plumbing Fixtures - 4th Floor	7	18-Jun-26	29-Jun-26
CON-5750	Install Plumbing Fixtures - Lower Roof	7	30-Jun-26	09-Jul-26
CON-5890	Install Plumbing Fixtures - 1st Floor	7	10-Jul-26	20-Jul-26
Furniture		65	19-May-26	20-Aug-26
CON-5070	Install Furniture - Cellar Floor	7	19-May-26	28-May-26
CON-5220	Install Furniture - 2nd Floor	7	29-May-26	08-Jun-26
CON-5420	Install Furniture - 3rd Floor	7	09-Jun-26	17-Jun-26
CON-5620	Install Furniture - 4th Floor	7	18-Jun-26	29-Jun-26



Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

TECHNICO CONSTRUCTION PROJECTS

Prepared By: A.A			
Date	Revision	Checked	Approved
16-Dec-24	00	AR	


Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-5770	Install Furniture - Lower Roof	7	30-Jun-26	09-Jul-26
CON-6170	Install Furniture - 1st Floor	7	12-Aug-26	20-Aug-26
Final Coat Painting		65	29-May-26	31-Aug-26
CON-5200	Install Final Coat Painting - Cellar Floor	7	29-May-26	08-Jun-26
CON-5400	Install Final Coat Painting - 2nd Floor	7	09-Jun-26	17-Jun-26
CON-5600	Install Final Coat Painting - 3rd Floor	7	18-Jun-26	29-Jun-26
CON-5760	Install Final Coat Painting - 4th Floor	7	30-Jun-26	09-Jul-26
CON-5900	Install Final Coat Painting - Lower Roof	7	10-Jul-26	20-Jul-26
CON-6230	Install Final Coat Painting - 1st Floor	7	21-Aug-26	31-Aug-26
Voice System		65	29-May-26	31-Aug-26
CON-5170	Install Voice Systems Components -Cellar Floor	7	29-May-26	08-Jun-26
CON-5360	Install Voice Systems Components - 2nd Floor	7	09-Jun-26	17-Jun-26
CON-5560	Install Voice Systems Components - 3rd Floor	7	18-Jun-26	29-Jun-26
CON-5710	Install Voice Systems Components - 4th Floor	7	30-Jun-26	09-Jul-26
CON-5840	Install Voice Systems Components - Lower Roof	7	10-Jul-26	20-Jul-26
CON-6220	Install Voice Systems Components - 1st Floor	7	21-Aug-26	31-Aug-26
Public Address and Clock System		65	09-Jun-26	10-Sep-26
CON-5370	Install Public Address and Clock Systems Components -Cellar Floor	7	09-Jun-26	17-Jun-26
CON-5570	Install Public Address and Clock Systems Components - 2nd Floor	7	18-Jun-26	29-Jun-26
CON-5720	Install Public Address and Clock Systems Components - 3rd Floor	7	30-Jun-26	09-Jul-26
CON-5850	Install Public Address and Clock Systems Components - 4th Floor	7	10-Jul-26	20-Jul-26
CON-5970	Install Public Address and Clock Systems Components - Lower Roof	7	21-Jul-26	29-Jul-26
CON-6260	Install Public Address and Clock Systems Components - 1st Floor	7	01-Sep-26	10-Sep-26
Signage		61	09-Jun-26	03-Sep-26
CON-5430	Install Signage- Cellar Floor	3	09-Jun-26	11-Jun-26
CON-5480	Install Signage - 2nd Floor	3	12-Jun-26	16-Jun-26
CON-5510	Install Signage - 3rd Floor	3	17-Jun-26	22-Jun-26
CON-5650	Install Signage - 4th Floor	3	23-Jun-26	25-Jun-26
CON-5660	Install Signage - Lower Roof	3	26-Jun-26	30-Jun-26
CON-6270	Install Signage - 1st Floor	3	01-Sep-26	03-Sep-26
Auxiliary Signal System		65	18-Jun-26	21-Sep-26
CON-5580	Install Auxiliary Signal System Components - Cellar Floor	7	18-Jun-26	29-Jun-26
CON-5730	Install Auxiliary Signal System Components - 2nd Floor	7	30-Jun-26	09-Jul-26
CON-5860	Install Auxiliary Signal System Components - 3rd Floor	7	10-Jul-26	20-Jul-26
CON-5980	Install Auxiliary Signal System Components - 4th Floor	7	21-Jul-26	29-Jul-26
CON-6050	Install Auxiliary Signal System Components - Lower Roof	7	30-Jul-26	07-Aug-26
CON-6280	Install Auxiliary Signal System Components - 1st Floor	7	11-Sep-26	21-Sep-26
Intrusion Alarm System		65	30-Jun-26	30-Sep-26
CON-5740	Install Intrusion Alarm System Components- Cellar Floor	7	30-Jun-26	09-Jul-26
CON-5870	Install Intrusion Alarm System Components - 2nd Floor	7	10-Jul-26	20-Jul-26
CON-5990	Install Intrusion Alarm System Components - 3rd Floor	7	21-Jul-26	29-Jul-26
CON-6060	Install Intrusion Alarm System Components - 4th Floor	7	30-Jul-26	07-Aug-26
CON-6130	Install Intrusion Alarm System Components - Lower Roof	7	10-Aug-26	18-Aug-26
CON-6290	Install Intrusion Alarm System Components - 1st Floor	7	22-Sep-26	30-Sep-26
IPDVS System		70	10-Jul-26	19-Oct-26
CON-5880	Install IPDVS System Components - Cellar Floor	7	10-Jul-26	20-Jul-26
CON-6000	Install IPDVS System Components - 2nd Floor	7	21-Jul-26	29-Jul-26
CON-6070	Install IPDVS System Components - 3rd Floor	7	30-Jul-26	07-Aug-26
CON-6140	Install IPDVS System Components - 4th Floor	7	10-Aug-26	18-Aug-26
CON-6200	Install IPDVS System Components - Lower Roof	7	19-Aug-26	27-Aug-26



Full Schedule Grouped by Trades Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-6300	Install IPDVS System Components - 1st Floor	12	01-Oct-26	19-Oct-26
Fire Alarm Devices		70	21-Jul-26	28-Oct-26
CON-6010	Install Fire Alarm Devices- Cellar Floor	7	21-Jul-26	29-Jul-26
CON-6080	Install Fire Alarm Devices - 2nd Floor	7	30-Jul-26	07-Aug-26
CON-6150	Install Fire Alarm Devices - 3rd Floor	7	10-Aug-26	18-Aug-26
CON-6210	Install Fire Alarm Devices - 4th Floor	7	19-Aug-26	27-Aug-26
CON-6240	Install Fire Alarm Devices - Lower Roof	7	28-Aug-26	08-Sep-26
CON-6310	Install Fire Alarm Devices - 1st Floor	7	20-Oct-26	28-Oct-26
Testing & Commissioning		197	22-Jan-26	02-Nov-26
CON-2050	Emergency Generator Electric Load Test	3	22-Jan-26	24-Jan-26
CON-2240	Obtain Emergency Generator Permit	5	26-Jan-26	30-Jan-26
CON-2340	HVAC System Testing and Commissioning	5	29-Jan-26	02-Feb-26
CON-2500	Emergency Generator Final Sign-off	0		30-Jan-26
CON-4380	Elevators Testing and Commissioning	5	07-Apr-26	11-Apr-26
CON-4460	Elevator DOB Inspection	5	12-Apr-26	16-Apr-26
CON-4490	Elevator Equipment Use Permit	5	17-Apr-26	21-Apr-26
CON-4620	Elevator Final Sign-off	5	22-Apr-26	26-Apr-26
CON-6180	Electrical Testing and Commissioning	5	12-Aug-26	16-Aug-26
CON-6250	MDF & IDF Rooms Testing and Inspection (Before 3-Sep-26)	7	28-Aug-26	03-Sep-26
CON-6320	IPDV System Testing and Inspection (Before 2-Nov-26)	10	20-Oct-26	02-Nov-26
TCO		19	03-Nov-26	01-Dec-26
CLO-1000	Pre-Final Clean-Out	2	03-Nov-26	04-Nov-26
CLO-1010	Pre-TCO Inspection	4	05-Nov-26	08-Nov-26
CLO-1020	Pre-TCO Punchlist	15	09-Nov-26	01-Dec-26
Substantial Completion		60	02-Dec-26	01-Mar-27
CLO-1030	Pre-Final Clean-Out	2	02-Dec-26	03-Dec-26
CLO-1040	Pre-Substantial Completion Inspection	10	04-Dec-26	13-Dec-26
CLO-1050	Pre-Substantial Punchlist	52	14-Dec-26	01-Mar-27
Final Completion		84	02-Mar-27	29-Jun-27
CLO-1060	Pre-Final Clean-Out	2	02-Mar-27	03-Mar-27
CLO-1070	Pre-Final Completion Inspection	10	04-Mar-27	13-Mar-27
CLO-1080	Pre-Final Punchlist	75	15-Mar-27	29-Jun-27

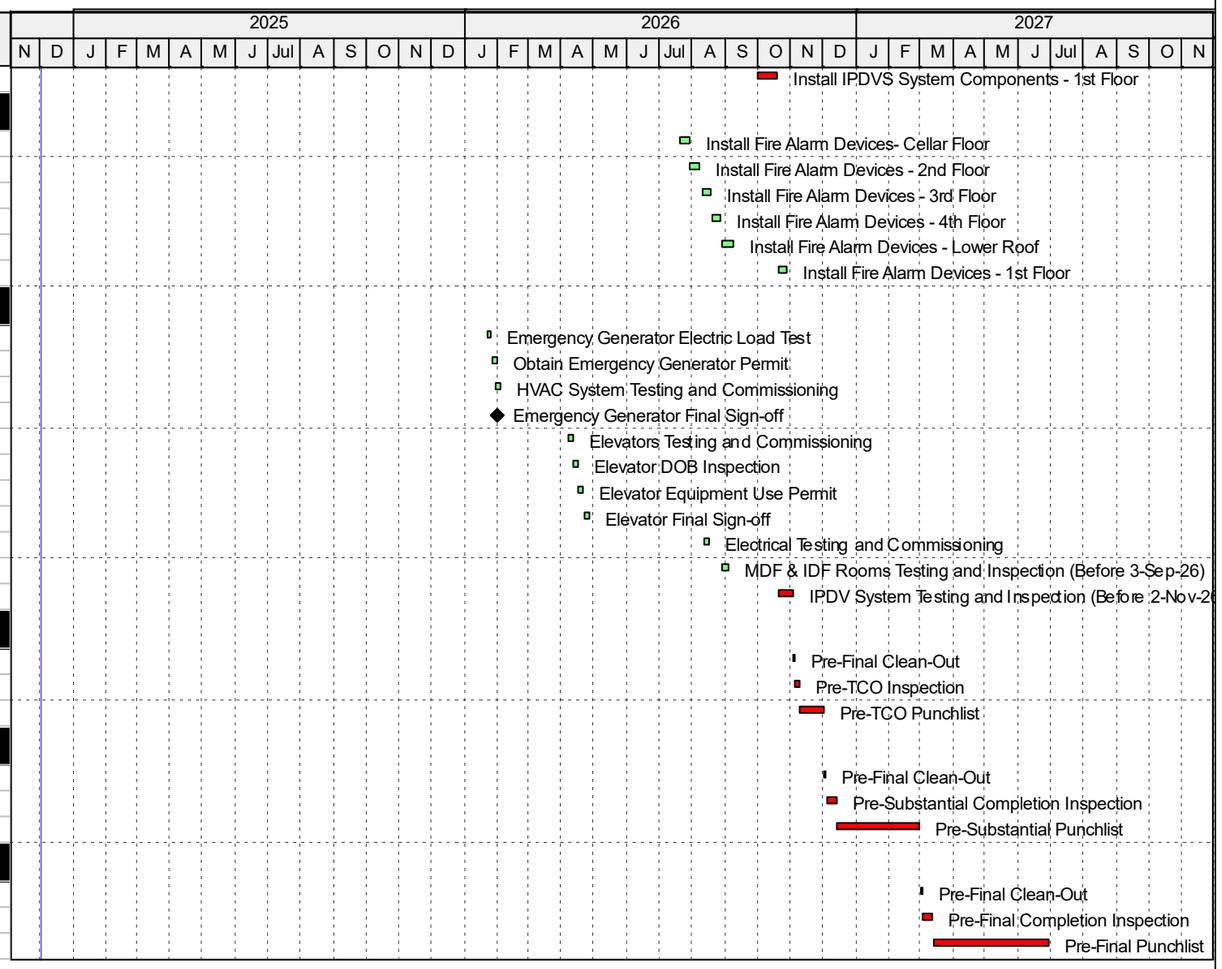

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

IS 082K New Building Design No. 093937 - Baseline Schedule Rev 00

TECHNICO CONSTRUCTION PROJECTS


Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	

APPENDIX 4 – Longest Path Layout

Longest Path Layout

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
Key Dates		644	02-Dec-24	29-Jun-27	0
MIL-1000	NTP	0	02-Dec-24		0
MIL-1010	Project Duration (From NTP till TCO) = 730 CDs	730	02-Dec-24	01-Dec-26	0
MIL-1020	Building Tight	0		05-Mar-26	0
MIL-1030	TCO	0		01-Dec-26	0
MIL-1040	Substantial Completion	0		01-Mar-27*	0
MIL-1050	Final Completion	0		29-Jun-27*	0
Permits		21	01-May-25	30-May-25	0
PER-1100	DOB Permit & Insurance	21	01-May-25	30-May-25	0
PER-1110	SCA Work Notification	7	21-May-25	30-May-25	0
Site Access Restrictions		180	02-Dec-24	30-May-25	0
PER-1120	No Site Access	180	02-Dec-24	30-May-25	0
Preliminary Work		86	02-Jun-25	02-Oct-25	0
CON-1000	Mobilization	5	02-Jun-25	06-Jun-25	0
CON-1010	Install Site Fence	2	09-Jun-25	10-Jun-25	0
CON-1030	Install Erosion Control Devices - Stage 1	2	11-Jun-25	12-Jun-25	0
CON-1040	Remove Existing Asphalt Pavement and Subbase	2	13-Jun-25	16-Jun-25	0
CON-1050	Install Remove Existing Concrete Pavement and Subbase	2	13-Jun-25	16-Jun-25	0
CON-1060	Prepare Temporary Staging & Storage Area - Stage 1	3	17-Jun-25	20-Jun-25	0
CON-1250	Install Construction Entrance - Stage 2	1	30-Sep-25	30-Sep-25	0
CON-1260	Install Erosion Control Devices - Stage 2	2	01-Oct-25	02-Oct-25	0
CON-1270	Prepare Temporary Staging & Storage Area - Stage 2	2	01-Oct-25	02-Oct-25	0
Foundation Work		105	23-Jun-25	20-Nov-25	0
CON-1070	Survey and Verify All Underground Utilities	3	23-Jun-25	25-Jun-25	0
CON-1080	Excavation	7	26-Jun-25	07-Jul-25	0
CON-1090	F/R/P Cellar Wall Footings	6	08-Jul-25	15-Jul-25	0
CON-1100	F/R/P Cellar Retaining Wall	8	16-Jul-25	25-Jul-25	0
CON-1180	F/R/P Slab on Grade - Cellar	4	11-Aug-25	14-Aug-25	0
CON-1190	F/R/P First Floor Slab - Cellar Side	5	15-Aug-25	21-Aug-25	0
CON-1210	Install MEP Hangers - 1st Floor - Cellar Side	2	20-Aug-25	21-Aug-25	0
CON-1220	Curing For The First Floor Slab	28	22-Aug-25	18-Sep-25	0
CON-1240	Backfilling	7	19-Sep-25	29-Sep-25	0
CON-1280	F/R/P First Floor Foundation	7	03-Oct-25	14-Oct-25	0
CON-1300	Insulate First Floor Foundations	3	15-Oct-25	17-Oct-25	0
CON-1310	Backfilling	5	20-Oct-25	24-Oct-25	0
CON-1380	F/R/P First Floor SOG	4	17-Nov-25	20-Nov-25	0
SSDS System		77	28-Jul-25	14-Nov-25	0
Below Cellar		10	28-Jul-25	08-Aug-25	0
CON-1110	Install Non-Woven Geotextile Layer - Below Cellar	2	28-Jul-25	29-Jul-25	0
CON-1130	Install Gas Permeable Aggregate Layer- Below Cellar	2	30-Jul-25	31-Jul-25	0
CON-1140	Install 6" C.I Pipe - Below Cellar	2	30-Jul-25	31-Jul-25	0
CON-1150	Install VI-20 Geomembrane Gas Permeable Aggregate Layer - Below Cellar	2	01-Aug-25	04-Aug-25	0
CON-1160	Install 60 Dry Mils of Liquid Boot - Below Cellar	2	05-Aug-25	06-Aug-25	0
CON-1170	Install Liquid Boot Ultrashield G-1000 - Below Cellar	2	07-Aug-25	08-Aug-25	0
Below First Floor SOG		14	27-Oct-25	14-Nov-25	0

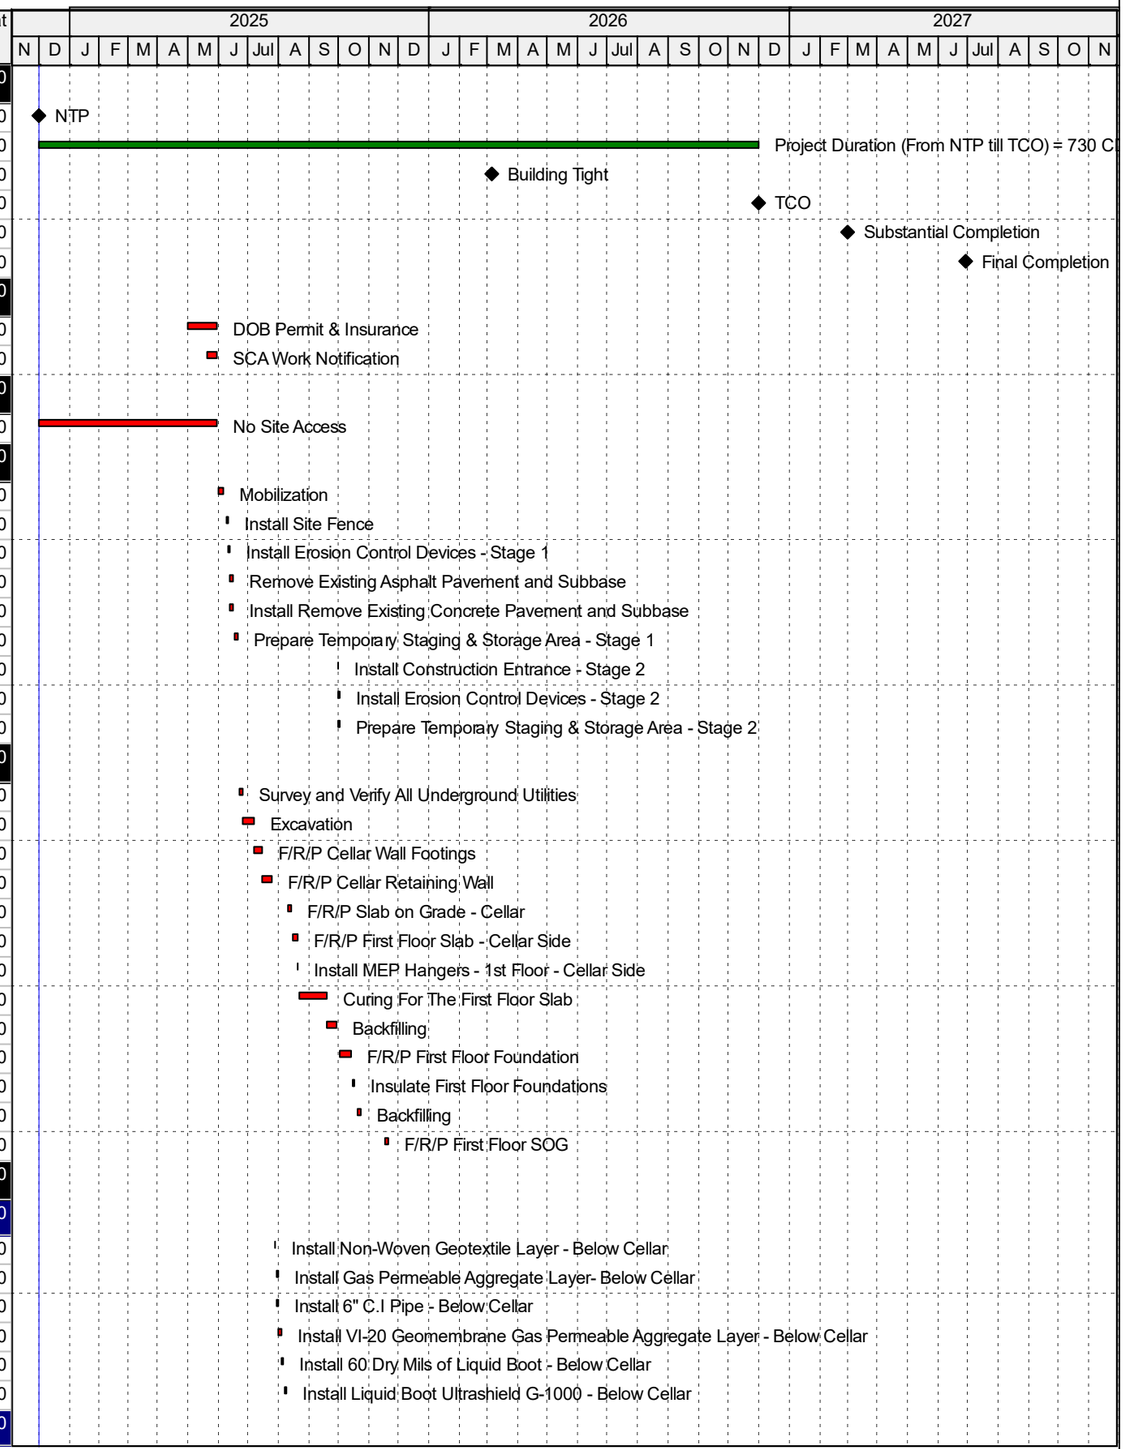

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

IS 082K New Building Design No. 093937 - Baseline Schedule Rev 00

TECHNICO CONSTRUCTION PROJECS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Longest Path Layout

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
CON-1320	Install Non-Woven Geotextile Layer - Below 1st Floor SOG	3	27-Oct-25	29-Oct-25	0
CON-1330	Install Gas Permeable Aggregate Layer - Below 1st Floor SOG	3	30-Oct-25	03-Nov-25	0
CON-1350	Install VI-20 Geomembrane Gas Permeable Aggregate Layer - Below 1st Floor SOG	3	04-Nov-25	06-Nov-25	0
CON-1360	Install 60 Dry Mils of Liquid Boot - Below 1st Floor SOG	3	07-Nov-25	12-Nov-25	0
CON-1370	Install Liquid Boot Ultrashield G-1000 - Below 1st Floor SOG	2	13-Nov-25	14-Nov-25	0
Super Structure		32	21-Nov-25	08-Jan-26	0
CON-1400	F/R/P Concrete Slab - 2nd Floor	5	21-Nov-25	28-Nov-25	0
CON-1430	F/R/P Columns & Shear Walls From Second Floor To Third Floor	3	01-Dec-25	03-Dec-25	0
CON-1440	F/R/P Concrete Slab - 3rd Floor	5	04-Dec-25	10-Dec-25	0
CON-1460	F/R/P Columns & Shear Walls From Third Floor To Fourth Floor	3	11-Dec-25	15-Dec-25	0
CON-1490	F/R/P Concrete Slab - 4th Floor	4	16-Dec-25	19-Dec-25	0
CON-1540	Install Mainroof Posts and Framing	7	22-Dec-25	31-Dec-25	0
CON-1620	F/R/P Concrete Deck Slab - Upper Roof	5	02-Jan-26	08-Jan-26	0
Dunnage		7	09-Jan-26	20-Jan-26	0
CON-1710	Install Dunnage Framing - Upper Roof	7	09-Jan-26	20-Jan-26	0
Roofing		31	21-Jan-26	05-Mar-26	0
Upper Roof		31	21-Jan-26	05-Mar-26	0
Insulation		31	21-Jan-26	05-Mar-26	0
CON-1960	Pour Concrete Topping Slab	4	21-Jan-26	26-Jan-26	0
CON-2220	Install Hot Fluid-Applied Rubberized Asphalt Fabric-Reinforced Roofing Membrane	5	27-Jan-26	02-Feb-26	0
CON-2510	Install Fabric Reinforcing Sheet	4	03-Feb-26	06-Feb-26	0
CON-2770	Install Protection Sheet and Roof Barrier	4	09-Feb-26	12-Feb-26	0
CON-2890	Install 1/2" Drainage Panel	4	13-Feb-26	19-Feb-26	0
CON-3180	Install 8" Roof Insulation (R-40 Min) Multi-Layered and Staggered	5	20-Feb-26	26-Feb-26	0
CON-3350	Install Filter Fabric	3	27-Feb-26	03-Mar-26	0
CON-3490	Upper Roofing Testing	2	04-Mar-26	05-Mar-26	0
HVAC Rough-Ins		5	29-May-26	04-Jun-26	0
Duct Horizontals		5	29-May-26	04-Jun-26	0
CON-5120	Rough-in Duct Work -VAV Devices & Diffusers - 1st Floor	5	29-May-26	04-Jun-26	0
Electrical Rough-Ins		10	05-Jun-26	18-Jun-26	0
Power Rough-Ins		5	05-Jun-26	11-Jun-26	0
CON-5290	Rough-in Power Conduits & Wires - 1st Floor	5	05-Jun-26	11-Jun-26	0
Low Voltage Rough-Ins		5	12-Jun-26	18-Jun-26	0
CON-5470	Rough-in Low Voltage Conduits & Wires - 1st Floor	5	12-Jun-26	18-Jun-26	0
Plumbing Rough-ins		5	22-Jun-26	26-Jun-26	0
Plumbing Horizontals		5	22-Jun-26	26-Jun-26	0
CON-5640	Rough-in Plumbing Pipes - 1st Floor	5	22-Jun-26	26-Jun-26	0
Fire Protection		5	29-Jun-26	06-Jul-26	0
Sprinkler Piping		5	29-Jun-26	06-Jul-26	0
CON-5680	Rough-in Sprinkler Piping - 1st Floor	5	29-Jun-26	06-Jul-26	0
Sprinkler Heads		2	02-Jul-26	06-Jul-26	0
CON-5780	Install Sprinkler Heads - 1st Floor	2	02-Jul-26	06-Jul-26	0
Ceiling Hangers		5	07-Jul-26	13-Jul-26	0
CON-5810	Install Ceiling Hangers - 1st Floor	5	07-Jul-26	13-Jul-26	0



Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone


TECHNICO CONSTRUCTION PROJECS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Longest Path Layout

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
Mockup Room		24	06-Mar-26	08-Apr-26	0
CON-3650	Install Walls GWB-Mockup Room	3	06-Mar-26	10-Mar-26	0
CON-3850	Install Door Frames-Mockup Room	2	11-Mar-26	12-Mar-26	0
CON-3950	Install Gypsum Board Ceiling -Mockup Room	3	13-Mar-26	17-Mar-26	0
CON-4070	Install Doors & Hardware-Mockup Room	2	18-Mar-26	19-Mar-26	0
CON-4160	Paint First coat -Mockup Room	3	20-Mar-26	24-Mar-26	0
CON-4230	Flooring Finishes-Mockup Room	3	25-Mar-26	27-Mar-26	0
CON-4290	Paint Second coat-Mockup Room	3	30-Mar-26	01-Apr-26	0
CON-4360	Install Furniture & Signs -Mockup Room	3	02-Apr-26	06-Apr-26	0
CON-4390	Mockup Room Inspection & Punchlist	2	07-Apr-26	08-Apr-26	0
Wall Gypsum Board		35	09-Apr-26	28-May-26	0
CON-4420	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - Cellar Floor	7	09-Apr-26	17-Apr-26	0
CON-4580	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 2nd Floor	7	20-Apr-26	28-Apr-26	0
CON-4690	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 3rd Floor	7	29-Apr-26	07-May-26	0
CON-4830	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 4th Floor	7	08-May-26	18-May-26	0
CON-4960	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - Lower Roof	7	19-May-26	28-May-26	0
Ceiling		7	14-Jul-26	22-Jul-26	0
CON-5920	Install Gypsum Board Ceiling - 1st Floor	7	14-Jul-26	22-Jul-26	0
CON-5930	Install Acoustical Ceiling Tiles - 1st Floor	7	14-Jul-26	22-Jul-26	0
CON-5940	Install Wood Slat Ceiling - 1st Floor	7	14-Jul-26	22-Jul-26	0
CON-5950	MCP-Wood Slat Ceiling Panel - 1st Floor	7	14-Jul-26	22-Jul-26	0
First Coat Painting		7	23-Jul-26	31-Jul-26	0
CON-6030	Install First Coat Painting - 1st Floor	7	23-Jul-26	31-Jul-26	0
Lighting Fixtures		7	03-Aug-26	11-Aug-26	0
CON-6100	Install Lighting Fixtures - 1st Floor	7	03-Aug-26	11-Aug-26	0
Data System & Video Intercom System		7	12-Aug-26	20-Aug-26	0
CON-6160	Install Data & Video Intercome Systems - 1st Floor	7	12-Aug-26	20-Aug-26	0
Voice System		7	21-Aug-26	31-Aug-26	0
CON-6220	Install Voice Systems Components - 1st Floor	7	21-Aug-26	31-Aug-26	0
Public Address and Clock System		7	01-Sep-26	10-Sep-26	0
CON-6260	Install Public Address and Clock Systems Components - 1st Floor	7	01-Sep-26	10-Sep-26	0
Auxiliary Signal System		7	11-Sep-26	21-Sep-26	0
CON-6280	Install Auxiliary Signal System Components - 1st Floor	7	11-Sep-26	21-Sep-26	0
Intrusion Alarm System		7	22-Sep-26	30-Sep-26	0
CON-6290	Install Intrusion Alarm System Components - 1st Floor	7	22-Sep-26	30-Sep-26	0
IPDVS System		12	01-Oct-26	19-Oct-26	0
CON-6300	Install IPDVS System Components - 1st Floor	12	01-Oct-26	19-Oct-26	0
Testing & Commissioning		10	20-Oct-26	02-Nov-26	0
CON-6320	IPDV System Testing and Inspection (Before 2-Nov-26)	10	20-Oct-26	02-Nov-26	0
TCO		19	03-Nov-26	01-Dec-26	0
CLO-1000	Pre-Final Clean-Out	2	03-Nov-26	04-Nov-26	0
CLO-1010	Pre-TCO Inspection	4	05-Nov-26	08-Nov-26	0
CLO-1020	Pre-TCO Punchlist	15	09-Nov-26	01-Dec-26	0

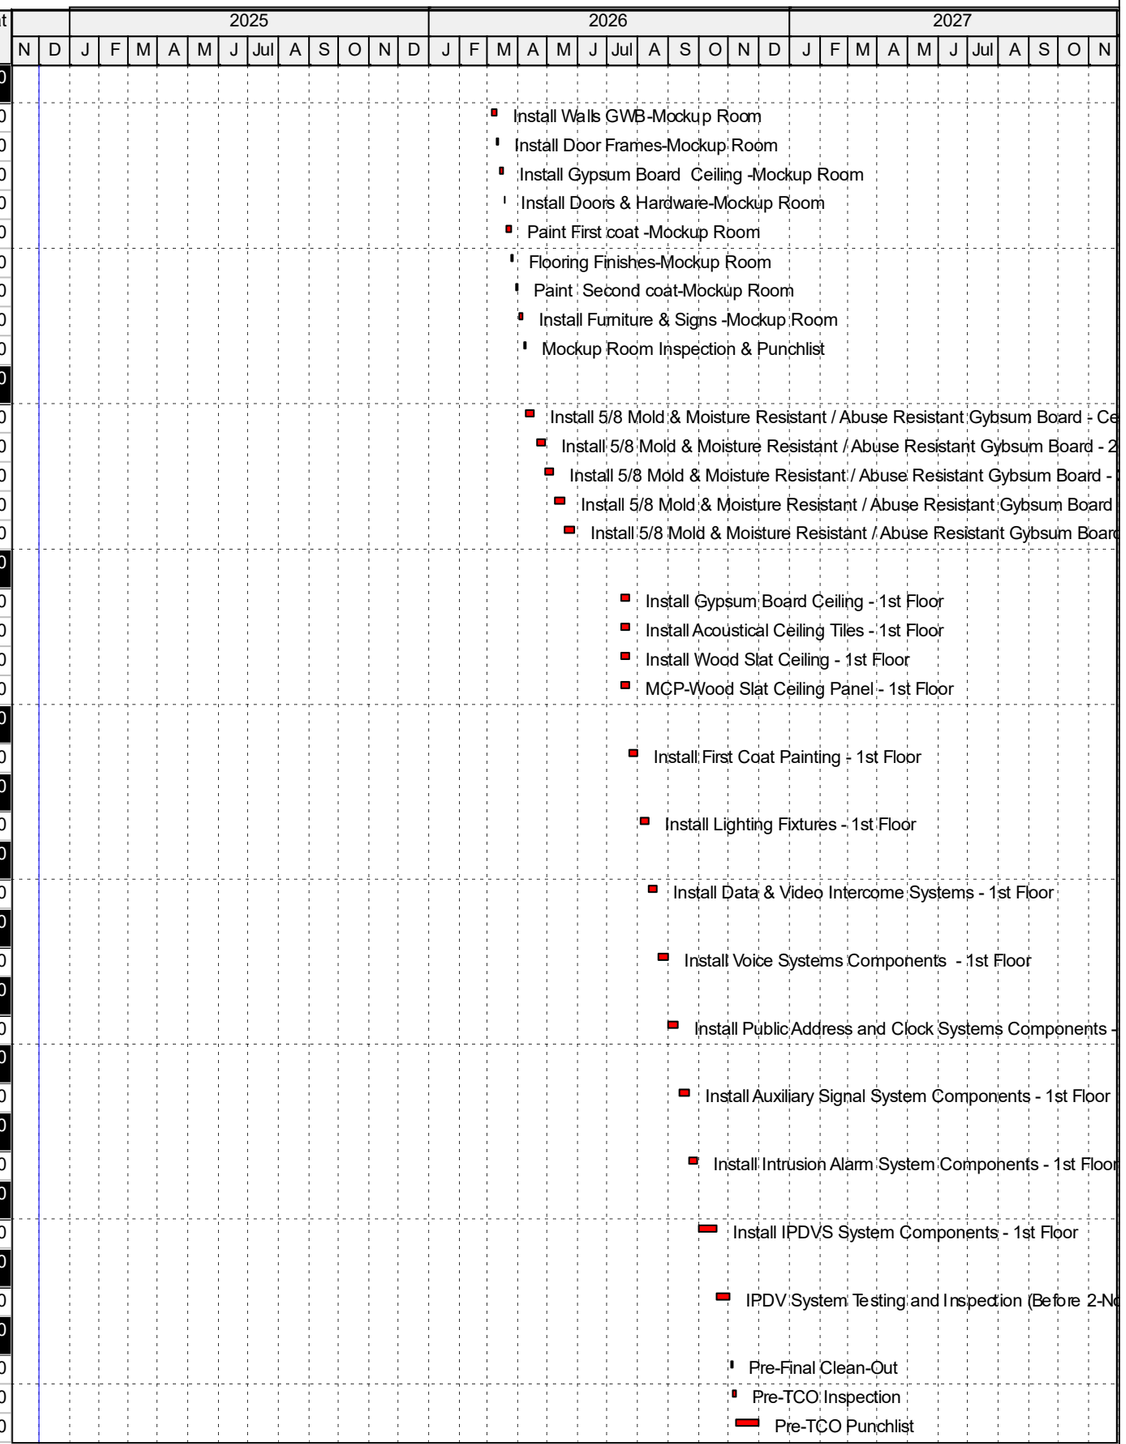

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

IS 082K New Building Design No. 093937 - Baseline Schedule Rev 00


TECHNICO CONSTRUCTION PROJECS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	

Longest Path Layout


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
Substantial Completion		60	02-Dec-26	01-Mar-27	0
CLO-1030	Pre-Final Clean-Out	2	02-Dec-26	03-Dec-26	0
CLO-1040	Pre-Substantial Completion Inspection	10	04-Dec-26	13-Dec-26	0
CLO-1050	Pre-Substantial Punchlist	52	14-Dec-26	01-Mar-27	0
Final Completion		84	02-Mar-27	29-Jun-27	0
CLO-1060	Pre-Final Clean-Out	2	02-Mar-27	03-Mar-27	1
CLO-1070	Pre-Final Completion Inspection	10	04-Mar-27	13-Mar-27	1
CLO-1080	Pre-Final Punchlist	75	15-Mar-27	29-Jun-27	0

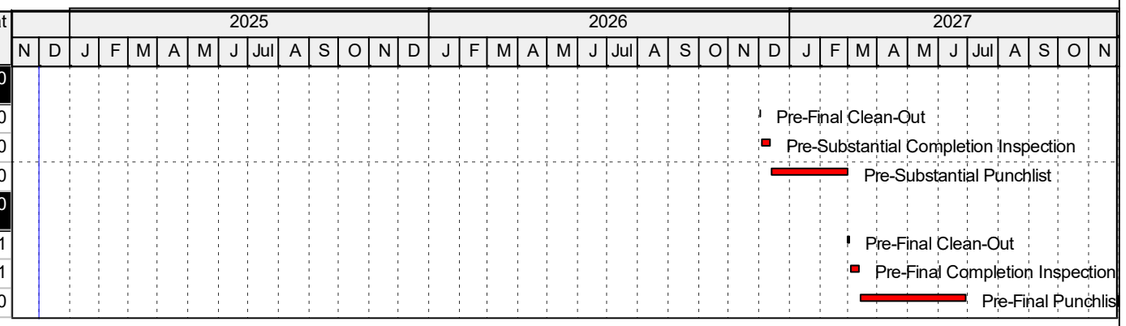

APPENDIX 5 – One Month Look-ahead

One Month Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
Key Dates		500	02-Dec-24	01-Dec-26	0
MIL-1000	NTP	0	02-Dec-24		0
MIL-1010	Project Duration (From NTP till TCO) = 730 CDs	730	02-Dec-24	01-Dec-26	0
Procurement		81	02-Dec-24	28-Mar-25	381
Submittals & Approvals		81	02-Dec-24	28-Mar-25	381
Division 01 - General Requirements		81	02-Dec-24	28-Mar-25	358
Spec Section S01300 - Submittals		75	02-Dec-24	20-Mar-25	179
SUB-1640	Prepare & Submit Underground Coordination Drawings	50	02-Dec-24	12-Feb-25	37
SUB-1650	Prepare & Submit 1st Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25	151
SUB-1660	Prepare & Submit 2nd Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25	155
SUB-1670	Prepare & Submit 3rd Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25	155
SUB-1680	Prepare & Submit 4th Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25	171
SUB-1690	Prepare & Submit 5th Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25	179
Spec Section S01311 - Progress Schedule		52	02-Dec-24	14-Feb-25	59
SUB-1510	Prepare & Submit Baseline Schedule	52	02-Dec-24	14-Feb-25	59
Spec Section S01400 - Quality Control		30	02-Dec-24	14-Jan-25	81
SUB-1470	Prepare & Submit QCP	30	02-Dec-24	14-Jan-25	81
Spec Section S01426 - Sample Classroom		81	02-Dec-24	28-Mar-25	219
SUB-1320	Prepare & Submit Sample Classroom Materials	81	02-Dec-24	28-Mar-25	219
Spec Section S01500 - Temporary Facilities and Controls		81	02-Dec-24	28-Mar-25	358
SUB-1310	Prepare & Submit Heating Plan	81	02-Dec-24	28-Mar-25	358
Spec Section S01524 - Construction Waste Management		81	02-Dec-24	28-Mar-25	30
SUB-1300	Prepare & Submit CWM Plan	81	02-Dec-24	28-Mar-25	30
Spec Section S01535 - Safety Program		17	02-Dec-24	24-Dec-24	67
SUB-1290	Prepare & Submit Site Safety Plan	2	02-Dec-24	03-Dec-24	67
APP-1000	Review & Approve Site Safety Plan	21	04-Dec-24	24-Dec-24	99
Spec Section S01550 - Indoor Air Quality (IAQ) Requirements		81	02-Dec-24	28-Mar-25	30
SUB-1280	Prepare & Submit Construction Indoor Air Quality Management Plan	81	02-Dec-24	28-Mar-25	30
Division 02 - Site Work		81	02-Dec-24	28-Mar-25	381
Spec Section 02010 - Environmental Site Assessment Reports		81	02-Dec-24	28-Mar-25	30
SUB-1700	Prepare & Submit Environmental Site Assessment Reports	81	02-Dec-24	28-Mar-25	30
Spec Section 02070 - Selective Removals & Demoloition		81	02-Dec-24	28-Mar-25	378
SUB-1710	Prepare & Submit Selective Removals & Demoloition	81	02-Dec-24	28-Mar-25	378
Spec Section 02100 - Site Preparation		23	02-Dec-24	03-Jan-25	116
SUB-1270	Prepare & Submit Existing Conditions Survey	10	02-Dec-24	13-Dec-24	115
APP-1030	Review & Approve Existing Conditions Survey	21	14-Dec-24	03-Jan-25	170
Spec Section 02200 - Earthwork		21	02-Dec-24	31-Dec-24	95
SUB-1460	Prepare & Submit Erosion Control and Sedimentation Plan	7	02-Dec-24	10-Dec-24	94
APP-1020	Review & Approve Erosion Control and Sedimentation Plan	21	11-Dec-24	31-Dec-24	136
Spec Section 02220 - Gas Vapor Barrier (Fluid Applied)		81	02-Dec-24	28-Mar-25	71
SUB-1260	Prepare & Submit Gas Vapor Barrier Submittal & Inspection Schedule	81	02-Dec-24	28-Mar-25	71
Spec Section 02221 - Sub-Slab Depressurization System		40	02-Dec-24	29-Jan-25	108
SUB-1250	Prepare & Submit SSDS Geotextile	40	02-Dec-24	29-Jan-25	108
Spec Section 02250 - Foundation & Other Change Adjustements		19	02-Dec-24	27-Dec-24	192
SUB-1720	Prepare & Submit Foundation Shop Drawings	5	02-Dec-24	06-Dec-24	191
APP-1010	Review & Approve Foundation Shop Drawings	21	07-Dec-24	27-Dec-24	279
Spec Section 02511 - Asphaltic Concrete Paving		81	02-Dec-24	28-Mar-25	353
SUB-1240	Prepare & Submit Asphaltic Concrete Paving	81	02-Dec-24	28-Mar-25	353
Spec Section 02513 - Sidewalk and Street Paving		81	02-Dec-24	28-Mar-25	359

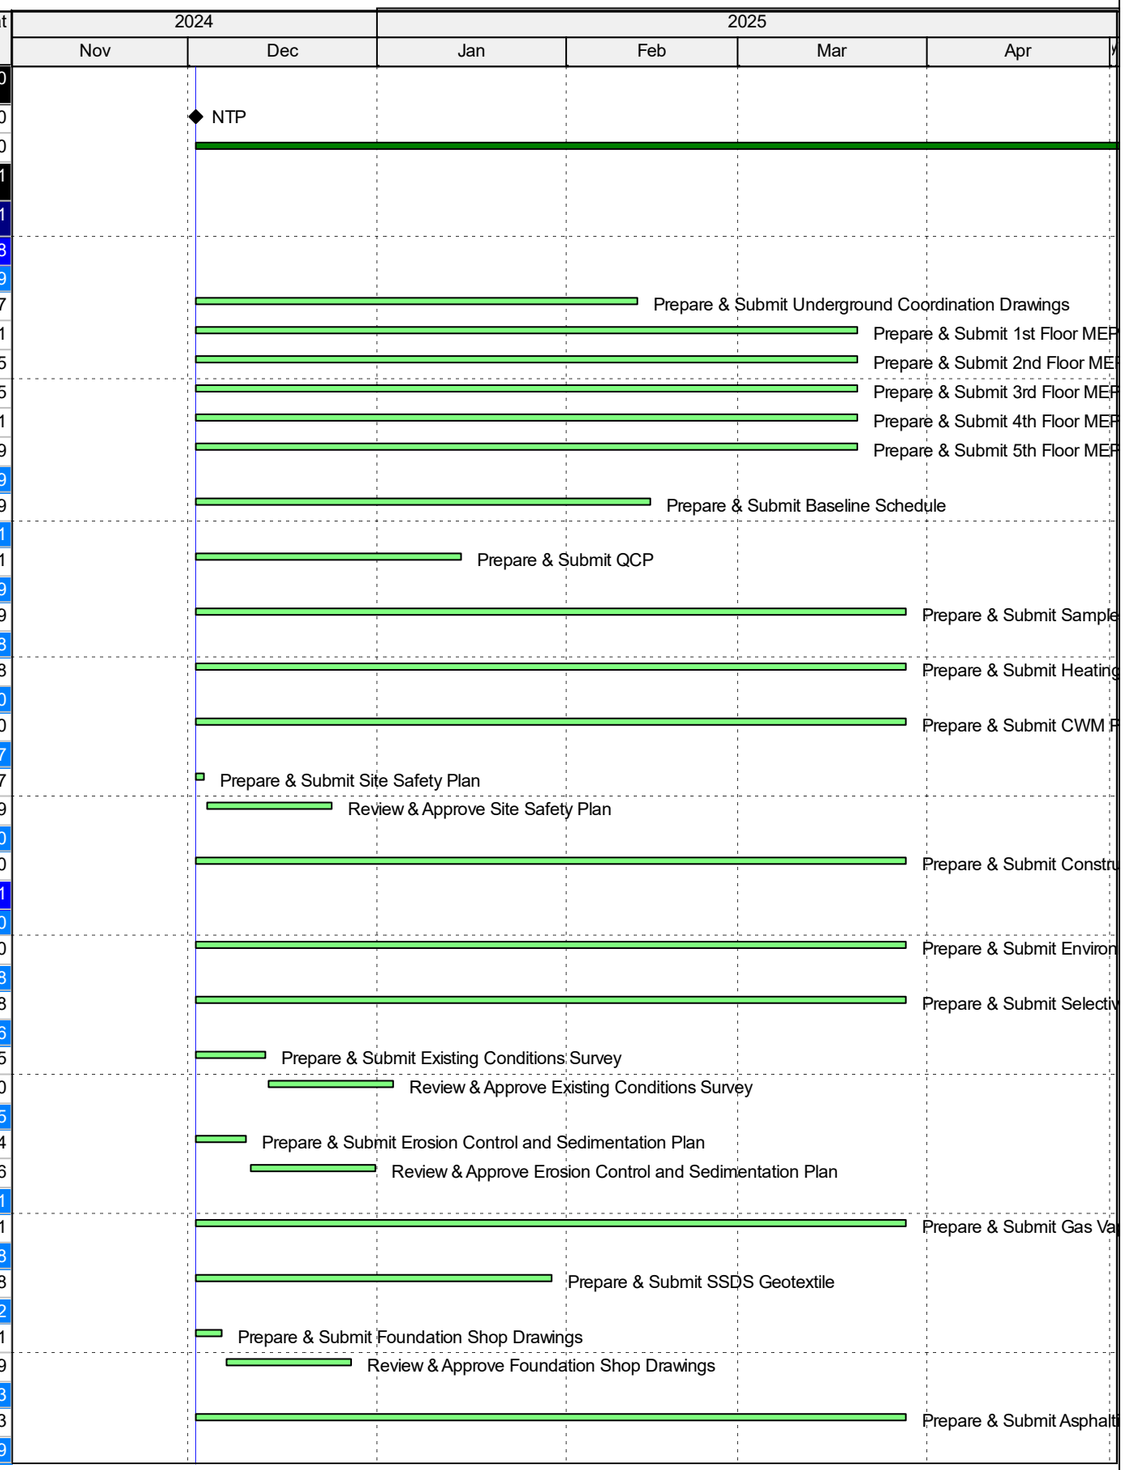

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

IS 082K New Building Design No. 093937 - Baseline Schedule Rev 00

TECHNICO CONSTRUCTION PROJECTS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	

One Month Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
SUB-1230	Prepare & Submit Steel Curb Facing Shop Drawing	81	02-Dec-24	28-Mar-25	359
Spec Section 02722 - PC Basins, Detention Basins, and Manholes		81	02-Dec-24	28-Mar-25	326
SUB-1220	Prepare & Submit Catch Basin Shop Drawings	81	02-Dec-24	28-Mar-25	326
Spec Section 02723 - Storm Drainage Systems		37	02-Dec-24	24-Jan-25	331
SUB-1210	Prepare & Submit Ductile Iron Pipes	37	02-Dec-24	24-Jan-25	331
Spec Section 02831 - Chain Link Fences & Gates		81	02-Dec-24	28-Mar-25	35
SUB-1730	Prepare & Submit Chain Link Fences & Gates Drawings	81	02-Dec-24	28-Mar-25	35
Spec Section 02870 - Site & Street Furnishings		28	02-Dec-24	10-Jan-25	102
SUB-1200	Prepare & Submit Site Furnishings Shop Drawings	15	02-Dec-24	20-Dec-24	101
APP-1040	Review & Approve Site Furnishings Shop Drawings	21	21-Dec-24	10-Jan-25	149
Spec Section 02900 - Landscaping		81	02-Dec-24	28-Mar-25	381
SUB-1190	Prepare & Submit Planting Schedule	81	02-Dec-24	28-Mar-25	381
Division 03 - Concrete		81	02-Dec-24	28-Mar-25	189
Spec Section 03100 - Concrete Formwork		81	02-Dec-24	28-Mar-25	189
SUB-1180	Prepare & Submit Formwork Shop Drawings	81	02-Dec-24	28-Mar-25	189
Spec Section 03200 - Concrete Reinforcement		30	02-Dec-24	14-Jan-25	106
SUB-1170	Prepare & Submit Concrete Reinforcement	30	02-Dec-24	14-Jan-25	106
Spec Section 03300 - Cast in Place Concrete		30	02-Dec-24	14-Jan-25	240
SUB-1350	Prepare & Submit Concrete Shop Drawings	30	02-Dec-24	14-Jan-25	240
SUB-1480	Prepare & Submit Concrete Mix Design	30	02-Dec-24	14-Jan-25	240
Spec Section 03542 - Cement Based Self Leveling Underlayment		81	02-Dec-24	28-Mar-25	55
SUB-1160	Prepare & Submit Certification of Material	81	02-Dec-24	28-Mar-25	55
Division 04 - Masonry		81	02-Dec-24	28-Mar-25	297
Spec Section 04200 - Unit Masonry		81	02-Dec-24	28-Mar-25	297
SUB-1740	Prepare & Submit Unit Masonry Product Data	81	02-Dec-24	28-Mar-25	297
Division 05 - Metals		81	02-Dec-24	28-Mar-25	192
Spec Section 05120 - Structural Steel		81	02-Dec-24	28-Mar-25	100
SUB-1750	Prepare & Submit Structure Steel Drawings	81	02-Dec-24	28-Mar-25	100
Spec Section 05170 - Support System for Suspended Ceilings		81	02-Dec-24	28-Mar-25	192
SUB-1150	Prepare & Submit Suspension Assembly Shop Drawings	81	02-Dec-24	28-Mar-25	192
Spec Section 05300 - Metal Deck		81	02-Dec-24	28-Mar-25	95
SUB-1760	Prepare & Submit Metal Deck Product Data	81	02-Dec-24	28-Mar-25	95
Spec Section 05500 - Metal Fabrications		81	02-Dec-24	28-Mar-25	111
SUB-1600	Prepare & Submit Roof Dunnage	81	02-Dec-24	28-Mar-25	111
Division 06 - Wood & Plastics		81	02-Dec-24	28-Mar-25	333
Spec Section 06200 - Finish Carpentry		81	02-Dec-24	28-Mar-25	150
SUB-1430	Prepare & Submit Furniture	81	02-Dec-24	28-Mar-25	150
Spec Section 06410 - Custom Casework		81	02-Dec-24	28-Mar-25	333
SUB-1410	Prepare & Submit Millwork	81	02-Dec-24	28-Mar-25	333
Division 07 - Thermal & Moisture Protection		81	02-Dec-24	28-Mar-25	310
Spec Section 07147 - Crystalline Waterproofing		81	02-Dec-24	28-Mar-25	192
SUB-1140	Prepare & Submit Crystalline Waterproofing Product Data	81	02-Dec-24	28-Mar-25	192
Spec Section 07211 - Perimeter Foundation Insulation		81	02-Dec-24	28-Mar-25	123
SUB-1130	Prepare & Submit Perimeter Foundation Insulation Product Data	81	02-Dec-24	28-Mar-25	123
Spec Section 07600 - Flashing and Sheet Metal		81	02-Dec-24	28-Mar-25	310
SUB-1120	Prepare & Submit Flashing & Sheet Metal Shop Drawing	81	02-Dec-24	28-Mar-25	310
Spec Section 07720 - Roof Accessories		81	02-Dec-24	28-Mar-25	169
SUB-1110	Prepare & Submit Roof Drains & Clean Outs	81	02-Dec-24	28-Mar-25	169
Division 08 - Doors & Windows		81	02-Dec-24	28-Mar-25	214
Spec Section 08110 - Steel Doors and Frames		81	02-Dec-24	28-Mar-25	175



Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

TECHNICO CONSTRUCTION PROJECTS

Prepared By: A.A			
Date	Revision	Checked	Approved
16-Dec-24	00	AR	

One Month Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
SUB-1100	Prepare & Submit Door & Frame Corners Samples	81	02-Dec-24	28-Mar-25	175
Spec Section 08210 - Wood Doors		81	02-Dec-24	28-Mar-25	188
SUB-1520	Prepare & Submit Wood Doors	81	02-Dec-24	28-Mar-25	188
Spec Section 08525 - High Performance Aluminum Projected Windows		73	02-Dec-24	18-Mar-25	118
SUB-1570	Prepare & Submit Windows	73	02-Dec-24	18-Mar-25	118
Spec Section 08662 - Security Screens & Barriers		81	02-Dec-24	28-Mar-25	214
SUB-1770	Prepare & Submit Security Screens & Barriers	81	02-Dec-24	28-Mar-25	214
Spec Section 08710 - Finish Hardware		81	02-Dec-24	28-Mar-25	175
SUB-1080	Prepare & Submit Door Hardware Submittal	81	02-Dec-24	28-Mar-25	175
Division 09 - Finishes		81	02-Dec-24	28-Mar-25	182
Spec Section 09260 - Gypsum Board Assemblies		81	02-Dec-24	28-Mar-25	122
SUB-1370	Prepare & Submit Gypsum Board	81	02-Dec-24	28-Mar-25	122
Spec Section 09310 - Ceramic Tiles		81	02-Dec-24	28-Mar-25	178
SUB-1070	Prepare & Submit Ceramic Tiles Product Data	81	02-Dec-24	28-Mar-25	178
Spec Section 09510 - Acoustical Ceilings		60	02-Dec-24	27-Feb-25	189
SUB-1390	Prepare & Submit Acosutical Ceiling Tiles	60	02-Dec-24	27-Feb-25	189
Spec Section 09590 - Wood Flooring		81	02-Dec-24	28-Mar-25	181
SUB-1780	Prepare & Submit Wood Flooring	81	02-Dec-24	28-Mar-25	181
Spec Section 09650 - Resilient Flooring		81	02-Dec-24	28-Mar-25	178
SUB-1380	Prepare & Submit Floorings	81	02-Dec-24	28-Mar-25	178
Spec Section 09900 - Painting		81	02-Dec-24	28-Mar-25	182
SUB-1090	Prepare & Submit Painting	81	02-Dec-24	28-Mar-25	182
Division 10 - Specialties		81	02-Dec-24	28-Mar-25	318
Spec Section 10100 - Visual Display Boards		81	02-Dec-24	28-Mar-25	308
SUB-1790	Prepare & Submit Visual Display Boards	81	02-Dec-24	28-Mar-25	308
Spec Section 10400 - Identification Devices		81	02-Dec-24	28-Mar-25	318
SUB-1060	Prepare & Submit Interior Signage Shop Drawings	81	02-Dec-24	28-Mar-25	318
Spec Section 10522 - Fire Extinguishers & Cabinets		81	02-Dec-24	28-Mar-25	298
SUB-1800	Prepare & Submit Fire Extinguishers & Cabinets	81	02-Dec-24	28-Mar-25	298
Spec Section 10720 - Window Guards		73	02-Dec-24	18-Mar-25	118
SUB-1810	Prepare & Submit Stationary Metal Wall Louvers	73	02-Dec-24	18-Mar-25	118
Spec Section 10810 - Toilet & Bath Accessories		81	02-Dec-24	28-Mar-25	274
SUB-1400	Prepare & Submit Toilet Accessories	81	02-Dec-24	28-Mar-25	274
Division 11 - Equipment		81	02-Dec-24	28-Mar-25	257
Spec Section 11061 - Platform Curtains & Auditorium Window Curtains		81	02-Dec-24	28-Mar-25	214
SUB-1820	Prepare & Submit Platform Curtains & Auditorium Window Curtains	81	02-Dec-24	28-Mar-25	214
Spec Section 11400 - Food Service Equipment		81	02-Dec-24	28-Mar-25	257
SUB-1550	Prepare & Submit Kitchen Equipment	81	02-Dec-24	28-Mar-25	257
Spec Section 11450 - Domestic Type Equipment		81	02-Dec-24	28-Mar-25	257
SUB-1830	Prepare & Submit Domestic Equipment	81	02-Dec-24	28-Mar-25	257
Spec Section 11480 - Gymnasium Equipment		81	02-Dec-24	28-Mar-25	247
SUB-1630	Prepare & Submit Gymnasium Equipment	81	02-Dec-24	28-Mar-25	247
Division 12 - Furnishings		81	02-Dec-24	28-Mar-25	150
Spec Section 12302 - Manufactured Wood Casework		81	02-Dec-24	28-Mar-25	150
SUB-1840	Prepare & Submit Manufactured Wood Casework	81	02-Dec-24	28-Mar-25	150
Division 14 - Conveying Systems		81	02-Dec-24	28-Mar-25	292
Spec Section 14212 - Gearless Traction Passenger Elevators		50	02-Dec-24	12-Feb-25	265
SUB-1360	Prepare & Submit Elevator Machine	50	02-Dec-24	12-Feb-25	265
Spec Section 14420 - Hydraulic Vertical Wheelchair Lifts		81	02-Dec-24	28-Mar-25	292
SUB-1850	Prepare & Submit Hydraulic Vertical Wheelchair Lifts	81	02-Dec-24	28-Mar-25	292

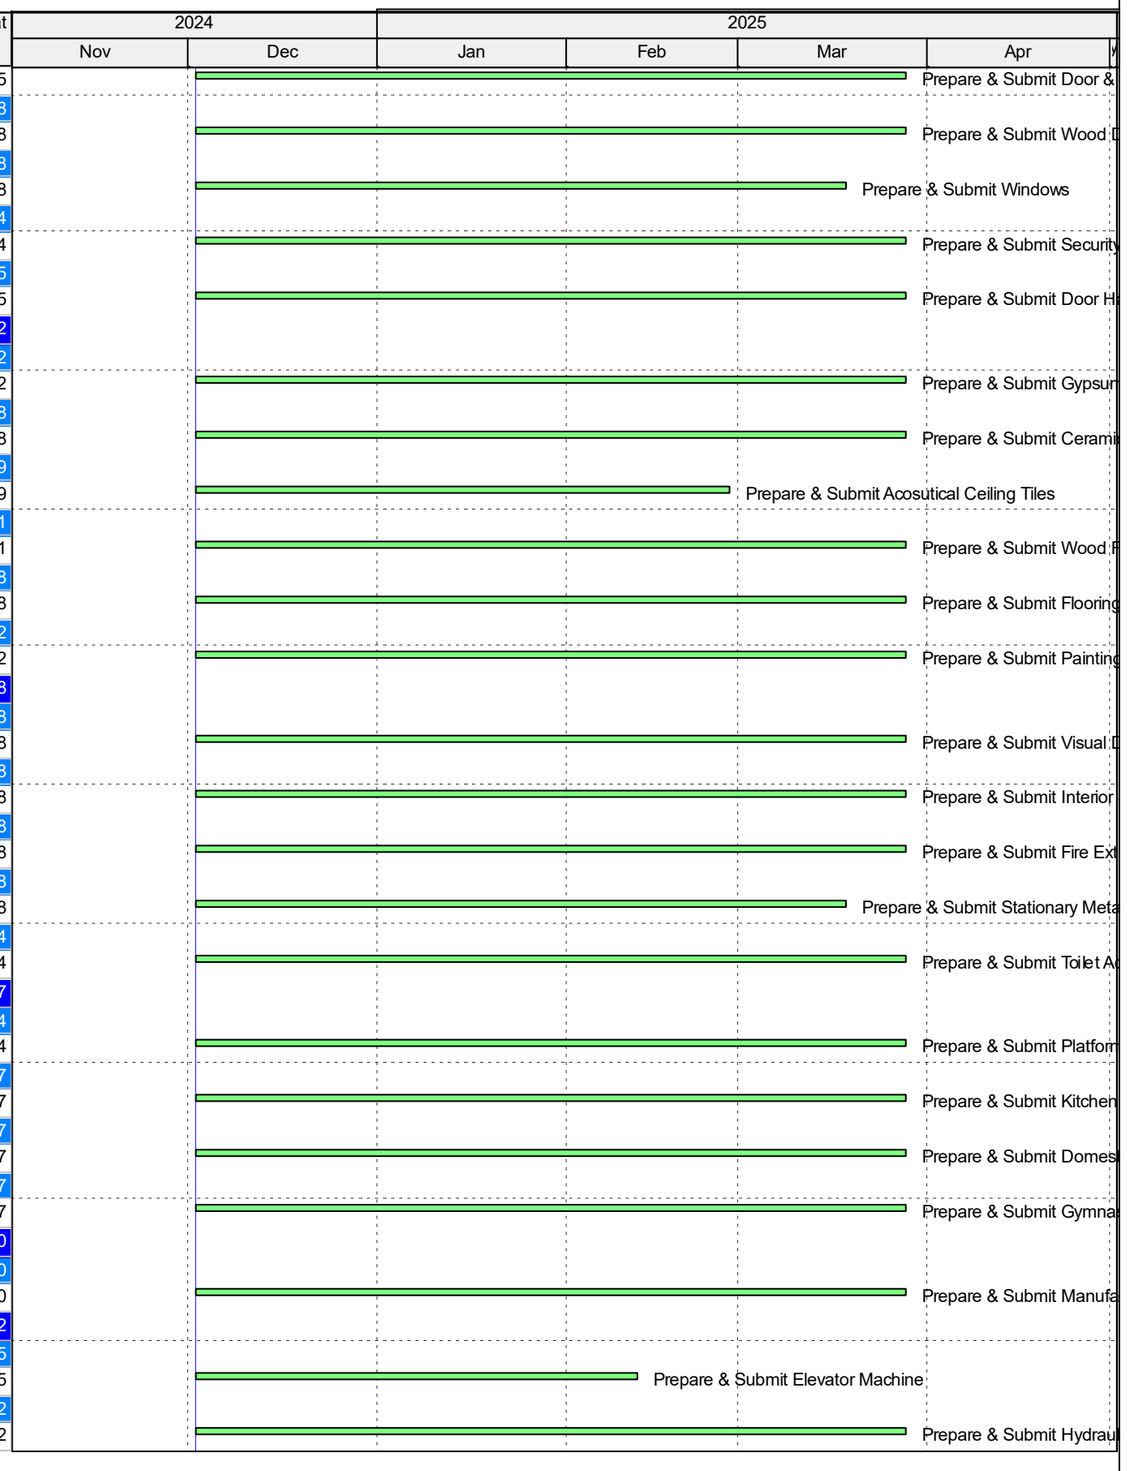

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

TECHNICO CONSTRUCTION PROJECS

Prepared By: A.A			
Date	Revision	Checked	Approved
16-Dec-24	00	AR	


One Month Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
Division 15 - Mechanical		81	02-Dec-24	28-Mar-25	364
Division 15A - Fire Protection		81	02-Dec-24	28-Mar-25	248
Spec Section 15333 - Fire Pumps - Sprinkler Booster Pumps		81	02-Dec-24	28-Mar-25	248
SUB-1050	Prepare & Submit Fire & Jockey Pumps	81	02-Dec-24	28-Mar-25	248
SUB-1530	Prepare & Submit Fire Protection Shop Drawings	81	02-Dec-24	28-Mar-25	248
Division 15B - Plumbing & Drainage		81	02-Dec-24	28-Mar-25	358
Spec Section 15410 - Plumbing Piping		81	02-Dec-24	28-Mar-25	205
SUB-1340	Prepare & Submit Plumbing Shop Drawings	81	02-Dec-24	28-Mar-25	205
Spec Section 15411 - Hangers and Supports		40	02-Dec-24	29-Jan-25	220
SUB-1040	Prepare & Submit Hangers & Supports	40	02-Dec-24	29-Jan-25	220
Spec Section 15415 - Drainage		40	02-Dec-24	29-Jan-25	213
SUB-1030	Prepare & Submit Floor Drains	40	02-Dec-24	29-Jan-25	213
Spec Section 15417 - Cold Water Supply		40	02-Dec-24	29-Jan-25	334
SUB-1020	Prepare & Submit Pressure Gages	40	02-Dec-24	29-Jan-25	334
Spec Section 15418 - Hot Water Supply		40	02-Dec-24	29-Jan-25	399
SUB-1010	Prepare & Submit Thermometers	40	02-Dec-24	29-Jan-25	399
Spec Section 15440 - Plumbing Fixtures		81	02-Dec-24	28-Mar-25	274
SUB-1500	Prepare & Submit Plumbing Fixtures	81	02-Dec-24	28-Mar-25	274
Spec Section 15453 - Pumping Apparatus & Tanks		81	02-Dec-24	28-Mar-25	241
SUB-1880	Prepare & Submit Pumping Apparatus & Tanks	81	02-Dec-24	28-Mar-25	241
Division 15C - Heating & Ventilation & Air Conditioning		81	02-Dec-24	28-Mar-25	364
Spec Section 15510 - HVAC Piping		60	02-Dec-24	27-Feb-25	308
SUB-1450	Prepare & Submit Mechanical Piping	60	02-Dec-24	27-Feb-25	308
Spec Section 15783 - Split Heat Pump System		60	02-Dec-24	27-Feb-25	385
SUB-1000	Prepare & Submit Split Heat Pump System - SUB	60	02-Dec-24	27-Feb-25	385
Spec Section 15836 - Unit Heaters Cabinet Heaters		60	02-Dec-24	27-Feb-25	292
SUB-1620	Prepare & Submit Unit Cabinet Heaters	60	02-Dec-24	27-Feb-25	292
Spec Section 15891 - Metal Ductwork		81	02-Dec-24	28-Mar-25	172
SUB-1440	Prepare & Submit Mechanical Ducts	81	02-Dec-24	28-Mar-25	172
Spec Section 15590 - Emergency Generator System Accessories		81	02-Dec-24	28-Mar-25	364
SUB-1890	Prepare & Submit Emergency Generator System Accessories	81	02-Dec-24	28-Mar-25	364
Spec Section 15836 - Unit Heaters/Cabinet Heaters		81	02-Dec-24	28-Mar-25	271
SUB-1900	Prepare & Submit Unit Heaters/Cabinet Heaters Equipment	81	02-Dec-24	28-Mar-25	271
Spec Section 15970 - Temperature Control System		81	02-Dec-24	28-Mar-25	325
SUB-1920	Prepare & Submit Air Outlets & Inlets	81	02-Dec-24	28-Mar-25	325
Spec Section 15940 - Air Outlets & Inlets		81	02-Dec-24	28-Mar-25	307
SUB-1910	Prepare & Submit Temperature Control System	81	02-Dec-24	28-Mar-25	307
Division 16 - Electrical		81	02-Dec-24	28-Mar-25	376
Spec Section 16010 - Gen Provisions for Elec Work		81	02-Dec-24	28-Mar-25	363
SUB-1330	Prepare & Submit Electrical Shop Drawings	81	02-Dec-24	28-Mar-25	136
SUB-1490	Prepare & Submit Electrical Equipment, Conduits, and Cables	20	02-Dec-24	30-Dec-24	197
SUB-1610	Prepare & Submit Switch Gears Product Data	20	02-Dec-24	30-Dec-24	410
APP-1050	Review & Approve Electrical Equipment, Conduits, and Cables	21	31-Dec-24	20-Jan-25	286
APP-1060	Review & Approve Switch Gears Product Data	21	31-Dec-24	20-Jan-25	597
Spec Section 16120 - Wiring Systems		81	02-Dec-24	28-Mar-25	287
SUB-1580	Prepare & Submit Telecommunication System Drawings	81	02-Dec-24	28-Mar-25	287
Spec Section 16502 - Interior Lighting Fixtures		30	02-Dec-24	14-Jan-25	295
SUB-1420	Prepare & Submit Lighting Fixtures	30	02-Dec-24	14-Jan-25	295
Spec Section 16520 - Illuminated Exit Sign		81	02-Dec-24	28-Mar-25	318
SUB-1560	Prepare & Submit Signs	81	02-Dec-24	28-Mar-25	318
Spec Section 16720 - Fire Detection Alarm System with COC		81	02-Dec-24	28-Mar-25	303



One Month Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
SUB-1540	Prepare & Submit Fire Detectors & Alarms	81	02-Dec-24	28-Mar-25	303
Spec Section 16785 - Internet Protocol Digital Video Surveillance System using Digital Cameras		50	02-Dec-24	12-Feb-25	320
SUB-1590	Prepare & Submit Internet Protocol Digital Video Surveillance System using Digital Cameras	50	02-Dec-24	12-Feb-25	320
Spec Section 16425 - Switch Boards & Panel Boards		81	02-Dec-24	28-Mar-25	349
SUB-1860	Prepare & Submit Switch & Panel Boards	81	02-Dec-24	28-Mar-25	349
Spec Section 16475 - Overcurrent Protective Devices		81	02-Dec-24	28-Mar-25	376
SUB-1870	Prepare & Submit Overcurrent Protective Devices Data	81	02-Dec-24	28-Mar-25	376
Fabrication & Delivery		25	01-Jan-25	25-Jan-25	136
PRO-1120	Procure & Deliver Erosion Control and Sedimentation Devices	25	01-Jan-25	25-Jan-25	136
Site Access Restrictions		180	02-Dec-24	30-May-25	0
PER-1120	No Site Access	180	02-Dec-24	30-May-25	0

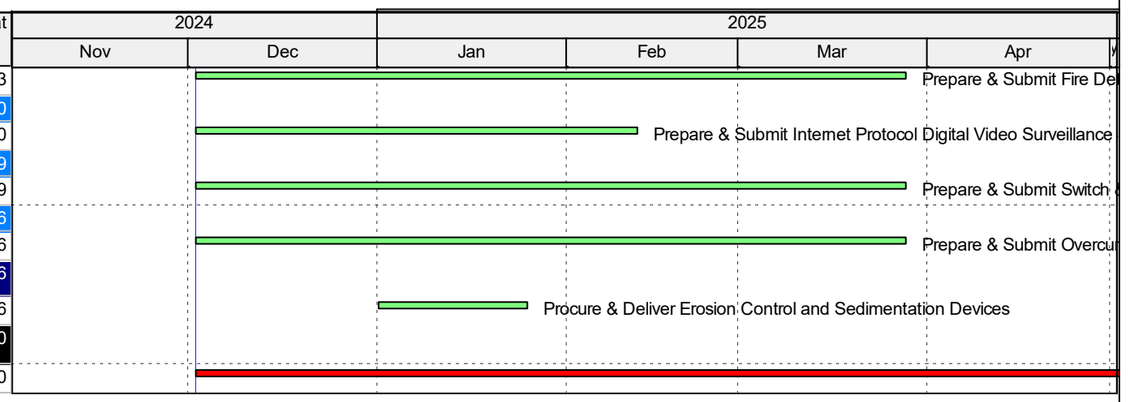

Start: 02-Dec-24
Finish: 29-Jun-27
Data Date: 02-Dec-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone

IS 082K New Building Design No. 093937 - Baseline Schedule Rev 00

TECHNICO CONSTRUCTION PROJECS

Prepared By: A.A

Date	Revision	Checked	Approved
16-Dec-24	00	AR	

APPENDIX 7
– Activity Report

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
APP-1000	Review & Approve Site Safety Plan	21	21	04-Dec-24	24-Dec-24	99			04-Dec-24	24-Dec-24	13-Mar-25	02-Apr-25	Not Started
APP-1010	Review & Approve Foundation Shop Drawings	21	21	07-Dec-24	27-Dec-24	279			07-Dec-24	27-Dec-24	12-Sep-25	02-Oct-25	Not Started
APP-1020	Review & Approve Erosion Control and Sedimentation Plan	21	21	11-Dec-24	31-Dec-24	136			11-Dec-24	31-Dec-24	26-Apr-25	16-May-25	Not Started
APP-1030	Review & Approve Existing Conditions Survey	21	21	14-Dec-24	03-Jan-25	170			14-Dec-24	03-Jan-25	02-Jun-25	22-Jun-25	Not Started
APP-1040	Review & Approve Site Furnishings Shop Drawings	21	21	21-Dec-24	10-Jan-25	149			21-Dec-24	10-Jan-25	19-May-25	08-Jun-25	Not Started
APP-1050	Review & Approve Electrical Equipment, Conduits, and Cables	21	21	31-Dec-24	20-Jan-25	286			31-Dec-24	20-Jan-25	13-Oct-25	02-Nov-25	Not Started
APP-1060	Review & Approve Switch Gears Product Data	21	21	31-Dec-24	20-Jan-25	597			31-Dec-24	20-Jan-25	20-Aug-26	09-Sep-26	Not Started
APP-1070	Review & Approve Concrete Reinforcement	21	21	15-Jan-25	04-Feb-25	153			15-Jan-25	04-Feb-25	17-Jun-25	07-Jul-25	Not Started
APP-1080	Review & Approve Concrete Shop Drawings	21	21	15-Jan-25	04-Feb-25	350			15-Jan-25	04-Feb-25	31-Dec-25	20-Jan-26	Not Started
APP-1090	Review & Approve Lighting Fixtures	21	21	15-Jan-25	04-Feb-25	431			15-Jan-25	04-Feb-25	22-Mar-26	11-Apr-26	Not Started
APP-1100	Review & Approve QCP	21	21	15-Jan-25	04-Feb-25	117			15-Jan-25	04-Feb-25	12-May-25	01-Jun-25	Not Started
APP-1110	Review & Approve Concrete Mix Design	21	21	15-Jan-25	04-Feb-25	350			15-Jan-25	04-Feb-25	31-Dec-25	20-Jan-26	Not Started
APP-1120	Review & Approve Ductile Iron Pipes	21	21	25-Jan-25	14-Feb-25	481			25-Jan-25	14-Feb-25	21-May-26	10-Jun-26	Not Started
APP-1130	Review & Approve Thermometers	21	21	30-Jan-25	19-Feb-25	580			30-Jan-25	19-Feb-25	02-Sep-26	22-Sep-26	Not Started
APP-1140	Review & Approve Pressure Gages	21	21	30-Jan-25	19-Feb-25	487			30-Jan-25	19-Feb-25	01-Jun-26	21-Jun-26	Not Started
APP-1150	Review & Approve Floor Drains	21	21	30-Jan-25	19-Feb-25	309			30-Jan-25	19-Feb-25	05-Dec-25	25-Dec-25	Not Started
APP-1160	Review & Approve Hangers & Supports	21	21	30-Jan-25	19-Feb-25	320			30-Jan-25	19-Feb-25	16-Dec-25	05-Jan-26	Not Started
APP-1170	Review & Approve SSDS Geotextile	21	21	30-Jan-25	19-Feb-25	158			30-Jan-25	19-Feb-25	07-Jul-25	27-Jul-25	Not Started
APP-1180	Review & Approve Elevator Machine	21	21	13-Feb-25	05-Mar-25	387			13-Feb-25	05-Mar-25	07-Mar-26	27-Mar-26	Not Started
APP-1190	Review & Approve Internet Protocol Digital Video Surveillance System using Digital Cameras	21	21	13-Feb-25	05-Mar-25	464			13-Feb-25	05-Mar-25	23-May-26	12-Jun-26	Not Started
APP-1200	Review & Approve Underground Coordination Drawings	21	21	13-Feb-25	05-Mar-25	54			13-Feb-25	05-Mar-25	08-Apr-25	28-Apr-25	Not Started
APP-1210	Review & Approve Baseline Schedule	21	21	15-Feb-25	07-Mar-25	86			15-Feb-25	07-Mar-25	12-May-25	01-Jun-25	Not Started
APP-1220	Review & Approve Split Heat Pump System - SUB	21	21	28-Feb-25	20-Mar-25	560			28-Feb-25	20-Mar-25	11-Sep-26	01-Oct-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
APP-1230	Review & Approve Acosutical Ceiling Tiles	21	21	28-Feb-25	20-Mar-25	275			28-Feb-25	20-Mar-25	30-Nov-25	20-Dec-25	Not Started
APP-1240	Review & Approve Mechanical Piping	21	21	28-Feb-25	20-Mar-25	447			28-Feb-25	20-Mar-25	21-May-26	10-Jun-26	Not Started
APP-1250	Review & Approve Unit Cabinet Heaters	21	21	28-Feb-25	20-Mar-25	425			28-Feb-25	20-Mar-25	29-Apr-26	19-May-26	Not Started
APP-1260	Review & Approve Windows	21	21	19-Mar-25	08-Apr-25	170			19-Mar-25	08-Apr-25	05-Sep-25	25-Sep-25	Not Started
APP-1270	Review & Approve Stationary Metal Wall Louvers	21	21	19-Mar-25	08-Apr-25	170			19-Mar-25	08-Apr-25	05-Sep-25	25-Sep-25	Not Started
APP-1280	Review & Approve 1st Floor Coordination Drawings	21	21	21-Mar-25	10-Apr-25	220			21-Mar-25	10-Apr-25	27-Oct-25	16-Nov-25	Not Started
APP-1290	Review & Approve 2nd Floor Coordination Drawings	21	21	21-Mar-25	10-Apr-25	224			21-Mar-25	10-Apr-25	31-Oct-25	20-Nov-25	Not Started
APP-1300	Review & Approve 3rd Floor Coordination Drawings	21	21	21-Mar-25	10-Apr-25	224			21-Mar-25	10-Apr-25	31-Oct-25	20-Nov-25	Not Started
APP-1310	Review & Approve 4th Floor Coordination Drawings	21	21	21-Mar-25	10-Apr-25	249			21-Mar-25	10-Apr-25	25-Nov-25	15-Dec-25	Not Started
APP-1320	Review & Approve 5th Floor Coordination Drawings	21	21	21-Mar-25	10-Apr-25	262			21-Mar-25	10-Apr-25	08-Dec-25	28-Dec-25	Not Started
APP-1330	Review & Approve Fire & Jockey Pumps	21	21	29-Mar-25	18-Apr-25	363			29-Mar-25	18-Apr-25	27-Mar-26	16-Apr-26	Not Started
APP-1340	Review & Approve Interior Signage Shop Drawings	21	21	29-Mar-25	18-Apr-25	466			29-Mar-25	18-Apr-25	08-Jul-26	28-Jul-26	Not Started
APP-1350	Review & Approve Ceramic Tiles Product Data	21	21	29-Mar-25	18-Apr-25	260			29-Mar-25	18-Apr-25	14-Dec-25	03-Jan-26	Not Started
APP-1370	Review & Approve Painting	21	21	29-Mar-25	18-Apr-25	265			29-Mar-25	18-Apr-25	19-Dec-25	08-Jan-26	Not Started
APP-1380	Review & Approve Door & Frame Corners Samples	21	21	29-Mar-25	18-Apr-25	256			29-Mar-25	18-Apr-25	10-Dec-25	30-Dec-25	Not Started
APP-1390	Review & Approve Roof Drains & Clean Outs	21	21	29-Mar-25	18-Apr-25	248			29-Mar-25	18-Apr-25	02-Dec-25	22-Dec-25	Not Started
APP-1400	Review & Approve Flashing & Sheet Metal Shop Drawing	21	21	29-Mar-25	18-Apr-25	453			29-Mar-25	18-Apr-25	25-Jun-26	15-Jul-26	Not Started
APP-1410	Review & Approve Perimeter Foundation Insulation Product Data	21	21	29-Mar-25	18-Apr-25	179			29-Mar-25	18-Apr-25	24-Sep-25	14-Oct-25	Not Started
APP-1420	Review & Approve Crystalline Waterproofing Product Data	21	21	29-Mar-25	18-Apr-25	283			29-Mar-25	18-Apr-25	06-Jan-26	26-Jan-26	Not Started
APP-1430	Review & Approve Suspension Assembly Shop Drawings	21	21	29-Mar-25	18-Apr-25	283			29-Mar-25	18-Apr-25	06-Jan-26	26-Jan-26	Not Started
APP-1440	Review & Approve Certification of Material	21	21	29-Mar-25	18-Apr-25	80			29-Mar-25	18-Apr-25	17-Jun-25	07-Jul-25	Not Started
APP-1450	Review & Approve Formwork Shop Drawings	21	21	29-Mar-25	18-Apr-25	277			29-Mar-25	18-Apr-25	31-Dec-25	20-Jan-26	Not Started
APP-1460	Review & Approve Planting Schedule	21	21	29-Mar-25	18-Apr-25	556			29-Mar-25	18-Apr-25	06-Oct-26	26-Oct-26	Not Started
APP-1470	Review & Approve Catch Basin Shop Drawings	21	21	29-Mar-25	18-Apr-25	478			29-Mar-25	18-Apr-25	20-Jul-26	09-Aug-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
APP-1480	Review & Approve Steel Curb Facing Shop Drawing	21	21	29-Mar-25	18-Apr-25	523			29-Mar-25	18-Apr-25	03-Sep-26	23-Sep-26	Not Started
APP-1490	Review & Approve Asphaltic Concrete Paving	21	21	29-Mar-25	18-Apr-25	515			29-Mar-25	18-Apr-25	26-Aug-26	15-Sep-26	Not Started
APP-1510	Review & Approve Construction Indoor Air Quality Management Plan	21	21	29-Mar-25	18-Apr-25	44			29-Mar-25	18-Apr-25	12-May-25	01-Jun-25	Not Started
APP-1520	Review & Approve CWM Plan	21	21	29-Mar-25	18-Apr-25	44			29-Mar-25	18-Apr-25	12-May-25	01-Jun-25	Not Started
APP-1530	Review & Approve Heating Plan	21	21	29-Mar-25	18-Apr-25	522			29-Mar-25	18-Apr-25	02-Sep-26	22-Sep-26	Not Started
APP-1540	Review & Approve Sample Classroom Materials	21	21	29-Mar-25	18-Apr-25	321			29-Mar-25	18-Apr-25	13-Feb-26	05-Mar-26	Not Started
APP-1550	Review & Approve Electrical Shop Drawings	21	21	29-Mar-25	18-Apr-25	198			29-Mar-25	18-Apr-25	13-Oct-25	02-Nov-25	Not Started
APP-1560	Review & Approve Plumbing Shop Drawings	21	21	29-Mar-25	18-Apr-25	301			29-Mar-25	18-Apr-25	24-Jan-26	13-Feb-26	Not Started
APP-1570	Review & Approve Gypsum Board	21	21	29-Mar-25	18-Apr-25	178			29-Mar-25	18-Apr-25	23-Sep-25	13-Oct-25	Not Started
APP-1580	Review & Approve Floorings	21	21	29-Mar-25	18-Apr-25	260			29-Mar-25	18-Apr-25	14-Dec-25	03-Jan-26	Not Started
APP-1590	Review & Approve Toilet Accessories	21	21	29-Mar-25	18-Apr-25	401			29-Mar-25	18-Apr-25	04-May-26	24-May-26	Not Started
APP-1600	Review & Approve Millwork	21	21	29-Mar-25	18-Apr-25	487			29-Mar-25	18-Apr-25	29-Jul-26	18-Aug-26	Not Started
APP-1610	Review & Approve Furniture	21	21	29-Mar-25	18-Apr-25	218			29-Mar-25	18-Apr-25	02-Nov-25	22-Nov-25	Not Started
APP-1620	Review & Approve Mechanical Ducts	21	21	29-Mar-25	18-Apr-25	251			29-Mar-25	18-Apr-25	05-Dec-25	25-Dec-25	Not Started
APP-1630	Review & Approve Plumbing Fixtures	21	21	29-Mar-25	18-Apr-25	401			29-Mar-25	18-Apr-25	04-May-26	24-May-26	Not Started
APP-1640	Review & Approve Wood Doors	21	21	29-Mar-25	18-Apr-25	276			29-Mar-25	18-Apr-25	30-Dec-25	19-Jan-26	Not Started
APP-1650	Review & Approve Fire Protection Shop Drawings	21	21	29-Mar-25	18-Apr-25	363			29-Mar-25	18-Apr-25	27-Mar-26	16-Apr-26	Not Started
APP-1660	Review & Approve Fire Detectors & Alarms	21	21	29-Mar-25	18-Apr-25	441			29-Mar-25	18-Apr-25	13-Jun-26	03-Jul-26	Not Started
APP-1670	Review & Approve Kitchen Equipment	21	21	29-Mar-25	18-Apr-25	376			29-Mar-25	18-Apr-25	09-Apr-26	29-Apr-26	Not Started
APP-1680	Review & Approve Signs	21	21	29-Mar-25	18-Apr-25	466			29-Mar-25	18-Apr-25	08-Jul-26	28-Jul-26	Not Started
APP-1690	Review & Approve Telecommunication System Drawings	21	21	29-Mar-25	18-Apr-25	418			29-Mar-25	18-Apr-25	21-May-26	10-Jun-26	Not Started
APP-1700	Review & Approve Roof Dunnage	21	21	29-Mar-25	18-Apr-25	161			29-Mar-25	18-Apr-25	06-Sep-25	26-Sep-25	Not Started
APP-1710	Review & Approve Gymnasium Equipment	21	21	29-Mar-25	18-Apr-25	362			29-Mar-25	18-Apr-25	26-Mar-26	15-Apr-26	Not Started
APP-1720	Review & Approve Environmental Site Assessment Reports	21	21	29-Mar-25	18-Apr-25	44			29-Mar-25	18-Apr-25	12-May-25	01-Jun-25	Not Started
APP-1730	Review & Approve Selective Removals & Demoloition	21	21	29-Mar-25	18-Apr-25	551			29-Mar-25	18-Apr-25	01-Oct-26	21-Oct-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
APP-1740	Review & Approve Chain Link Fences & Gates Drawings	21	21	29-Mar-25	18-Apr-25	51			29-Mar-25	18-Apr-25	19-May-25	08-Jun-25	Not Started
APP-1750	Review & Approve Unit Masonry Product Data	21	21	29-Mar-25	18-Apr-25	433			29-Mar-25	18-Apr-25	05-Jun-26	25-Jun-26	Not Started
APP-1760	Review & Approve Structure Steel Drawings	21	21	29-Mar-25	18-Apr-25	145			29-Mar-25	18-Apr-25	21-Aug-25	10-Sep-25	Not Started
APP-1770	Review & Approve Metal Deck Product Data	21	21	29-Mar-25	18-Apr-25	138			29-Mar-25	18-Apr-25	14-Aug-25	03-Sep-25	Not Started
APP-1780	Review & Approve Security Screens & Barriers	21	21	29-Mar-25	18-Apr-25	314			29-Mar-25	18-Apr-25	06-Feb-26	26-Feb-26	Not Started
APP-1790	Review & Approve Wood Flooring	21	21	29-Mar-25	18-Apr-25	264			29-Mar-25	18-Apr-25	18-Dec-25	07-Jan-26	Not Started
APP-1800	Review & Approve Visual Display Boards	21	21	29-Mar-25	18-Apr-25	451			29-Mar-25	18-Apr-25	23-Jun-26	13-Jul-26	Not Started
APP-1810	Review & Approve Fire Extinguishers & Cabinets	21	21	29-Mar-25	18-Apr-25	436			29-Mar-25	18-Apr-25	08-Jun-26	28-Jun-26	Not Started
APP-1820	Review & Approve Platform Curtains & Auditorium Window Curtains	21	21	29-Mar-25	18-Apr-25	314			29-Mar-25	18-Apr-25	06-Feb-26	26-Feb-26	Not Started
APP-1830	Review & Approve Domestic Equipment	21	21	29-Mar-25	18-Apr-25	376			29-Mar-25	18-Apr-25	09-Apr-26	29-Apr-26	Not Started
APP-1840	Review & Approve Manufactured Wood Casework	21	21	29-Mar-25	18-Apr-25	218			29-Mar-25	18-Apr-25	02-Nov-25	22-Nov-25	Not Started
APP-1850	Review & Approve Hydraulic Vertical Wheelchair Lifts	21	21	29-Mar-25	18-Apr-25	426			29-Mar-25	18-Apr-25	29-May-26	18-Jun-26	Not Started
APP-1860	Review & Approve Switch & Panel Boards	21	21	29-Mar-25	18-Apr-25	509			29-Mar-25	18-Apr-25	20-Aug-26	09-Sep-26	Not Started
APP-1870	Review & Approve Overcurrent Protective Devices Data	21	21	29-Mar-25	18-Apr-25	549			29-Mar-25	18-Apr-25	29-Sep-26	19-Oct-26	Not Started
APP-1880	Review & Approve Pumping Apparatus & Tanks	21	21	29-Mar-25	18-Apr-25	354			29-Mar-25	18-Apr-25	18-Mar-26	07-Apr-26	Not Started
APP-1890	Review & Approve Emergency Generator System Accessories	21	21	29-Mar-25	18-Apr-25	531			29-Mar-25	18-Apr-25	11-Sep-26	01-Oct-26	Not Started
APP-1900	Review & Approve Unit Heaters/Cabinet Heaters Equipment	21	21	29-Mar-25	18-Apr-25	396			29-Mar-25	18-Apr-25	29-Apr-26	19-May-26	Not Started
APP-1910	Review & Approve Temperature Control System	21	21	29-Mar-25	18-Apr-25	447			29-Mar-25	18-Apr-25	19-Jun-26	09-Jul-26	Not Started
APP-1920	Review & Approve Air Outlets & Inlets	21	21	29-Mar-25	18-Apr-25	475			29-Mar-25	18-Apr-25	17-Jul-26	06-Aug-26	Not Started
APP-1930	Review & Approve Record Documents	21	21	05-Nov-26	25-Nov-26	96			05-Nov-26	25-Nov-26	09-Feb-27	01-Mar-27	Not Started
CLO-1000	Pre-Final Clean-Out	2	2	03-Nov-26	04-Nov-26	0			03-Nov-26	04-Nov-26	03-Nov-26	04-Nov-26	Not Started
CLO-1010	Pre-TCO Inspection	4	4	05-Nov-26	08-Nov-26	0			05-Nov-26	08-Nov-26	05-Nov-26	08-Nov-26	Not Started
CLO-1020	Pre-TCO Punchlist	15	15	09-Nov-26	01-Dec-26	0			09-Nov-26	01-Dec-26	09-Nov-26	01-Dec-26	Not Started
CLO-1030	Pre-Final Clean-Out	2	2	02-Dec-26	03-Dec-26	0			02-Dec-26	03-Dec-26	02-Dec-26	03-Dec-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CLO-1040	Pre-Substantial Completion Inspection	10	10	04-Dec-26	13-Dec-26	0			04-Dec-26	13-Dec-26	04-Dec-26	13-Dec-26	Not Started
CLO-1050	Pre-Substantial Punchlist	52	52	14-Dec-26	01-Mar-27	0			14-Dec-26	01-Mar-27	14-Dec-26	01-Mar-27	Not Started
CLO-1060	Pre-Final Clean-Out	2	2	02-Mar-27	03-Mar-27	1			02-Mar-27	03-Mar-27	03-Mar-27	04-Mar-27	Not Started
CLO-1070	Pre-Final Completion Inspection	10	10	04-Mar-27	13-Mar-27	1			04-Mar-27	13-Mar-27	05-Mar-27	14-Mar-27	Not Started
CLO-1080	Pre-Final Punchlist	75	75	15-Mar-27	29-Jun-27	0			15-Mar-27	29-Jun-27	15-Mar-27	29-Jun-27	Not Started
CON-1000	Mobilization	5	5	02-Jun-25	06-Jun-25	0			02-Jun-25	06-Jun-25	02-Jun-25	06-Jun-25	Not Started
CON-1010	Install Site Fence	2	2	09-Jun-25	10-Jun-25	0			09-Jun-25	10-Jun-25	09-Jun-25	10-Jun-25	Not Started
CON-1020	Install Construction Entrance - Stage 1	1	1	09-Jun-25	09-Jun-25	1			09-Jun-25	09-Jun-25	10-Jun-25	10-Jun-25	Not Started
CON-1030	Install Erosion Control Devices - Stage 1	2	2	11-Jun-25	12-Jun-25	0			11-Jun-25	12-Jun-25	11-Jun-25	12-Jun-25	Not Started
CON-1040	Remove Existing Asphalt Pavement and Subbase	2	2	13-Jun-25	16-Jun-25	0			13-Jun-25	16-Jun-25	13-Jun-25	16-Jun-25	Not Started
CON-1050	Install Remove Existing Concrete Pavement and Subbase	2	2	13-Jun-25	16-Jun-25	0			13-Jun-25	16-Jun-25	13-Jun-25	16-Jun-25	Not Started
CON-1060	Prepare Temporary Staging & Storage Area - Stage 1	3	3	17-Jun-25	20-Jun-25	0			17-Jun-25	20-Jun-25	17-Jun-25	20-Jun-25	Not Started
CON-1070	Survey and Verify All Underground Utilities	3	3	23-Jun-25	25-Jun-25	0			23-Jun-25	25-Jun-25	23-Jun-25	25-Jun-25	Not Started
CON-1080	Excavation	7	7	26-Jun-25	07-Jul-25	0			26-Jun-25	07-Jul-25	26-Jun-25	07-Jul-25	Not Started
CON-1090	F/R/P Cellar Wall Footings	6	6	08-Jul-25	15-Jul-25	0			08-Jul-25	15-Jul-25	08-Jul-25	15-Jul-25	Not Started
CON-1100	F/R/P Cellar Retaining Wall	8	8	16-Jul-25	25-Jul-25	0			16-Jul-25	25-Jul-25	16-Jul-25	25-Jul-25	Not Started
CON-1110	Install Non-Woven Geotextile Layer - Below Cellar	2	2	28-Jul-25	29-Jul-25	0			28-Jul-25	29-Jul-25	28-Jul-25	29-Jul-25	Not Started
CON-1120	Insulate Cellar Retaining Wall	5	5	28-Jul-25	01-Aug-25	33			28-Jul-25	01-Aug-25	12-Sep-25	18-Sep-25	Not Started
CON-1130	Install Gas Permeable Aggregate Layer- Below Cellar	2	2	30-Jul-25	31-Jul-25	0			30-Jul-25	31-Jul-25	30-Jul-25	31-Jul-25	Not Started
CON-1140	Install 6" C.I Pipe - Below Cellar	2	2	30-Jul-25	31-Jul-25	0			30-Jul-25	31-Jul-25	30-Jul-25	31-Jul-25	Not Started
CON-1150	Install VI-20 Geomembrane Gas Permeable Aggregate Layer - Below Cellar	2	2	01-Aug-25	04-Aug-25	0			01-Aug-25	04-Aug-25	01-Aug-25	04-Aug-25	Not Started
CON-1160	Install 60 Dry Mils of Liquid Boot - Below Cellar	2	2	05-Aug-25	06-Aug-25	0			05-Aug-25	06-Aug-25	05-Aug-25	06-Aug-25	Not Started
CON-1170	Install Liquid Boot Ultrashield G-1000 - Below Cellar	2	2	07-Aug-25	08-Aug-25	0			07-Aug-25	08-Aug-25	07-Aug-25	08-Aug-25	Not Started
CON-1180	F/R/P Slab on Grade - Cellar	4	4	11-Aug-25	14-Aug-25	0			11-Aug-25	14-Aug-25	11-Aug-25	14-Aug-25	Not Started
CON-1190	F/R/P First Floor Slab - Cellar Side	5	5	15-Aug-25	21-Aug-25	0			15-Aug-25	21-Aug-25	15-Aug-25	21-Aug-25	Not Started
CON-1200	Install Floor Drains - Cellar Floor	2	2	15-Aug-25	18-Aug-25	88			15-Aug-25	18-Aug-25	23-Dec-25	24-Dec-25	Not Started
CON-1210	Install MEP Hangers - 1st Floor - Cellar Side	2	2	20-Aug-25	21-Aug-25	0			20-Aug-25	21-Aug-25	20-Aug-25	21-Aug-25	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-1220	Curing For The First Floor Slab	28	28	22-Aug-25	18-Sep-25	0			22-Aug-25	18-Sep-25	22-Aug-25	18-Sep-25	Not Started
CON-1230	F/R/P Columns & Shear Walls From First Level To Second Level - Cellar Area	4	4	22-Aug-25	27-Aug-25	15			22-Aug-25	27-Aug-25	15-Sep-25	18-Sep-25	Not Started
CON-1240	Backfilling	7	7	19-Sep-25	29-Sep-25	0			19-Sep-25	29-Sep-25	19-Sep-25	29-Sep-25	Not Started
CON-1250	Install Construction Entrance - Stage 2	1	1	30-Sep-25	30-Sep-25	0			30-Sep-25	30-Sep-25	30-Sep-25	30-Sep-25	Not Started
CON-1260	Install Erosion Control Devices - Stage 2	2	2	01-Oct-25	02-Oct-25	0			01-Oct-25	02-Oct-25	01-Oct-25	02-Oct-25	Not Started
CON-1270	Prepare Temporary Staging & Storage Area - Stage 2	2	2	01-Oct-25	02-Oct-25	0			01-Oct-25	02-Oct-25	01-Oct-25	02-Oct-25	Not Started
CON-1280	F/R/P First Floor Foundation	7	7	03-Oct-25	14-Oct-25	0			03-Oct-25	14-Oct-25	03-Oct-25	14-Oct-25	Not Started
CON-1290	F/R/P Columns From First Level To Second Level - First Level Area	5	5	07-Oct-25	14-Oct-25	26			07-Oct-25	14-Oct-25	14-Nov-25	20-Nov-25	Not Started
CON-1300	Insulate First Floor Foundations	3	3	15-Oct-25	17-Oct-25	0			15-Oct-25	17-Oct-25	15-Oct-25	17-Oct-25	Not Started
CON-1310	Backfilling	5	5	20-Oct-25	24-Oct-25	0			20-Oct-25	24-Oct-25	20-Oct-25	24-Oct-25	Not Started
CON-1320	Install Non-Woven Geotextile Layer - Below 1st Floor SOG	3	3	27-Oct-25	29-Oct-25	0			27-Oct-25	29-Oct-25	27-Oct-25	29-Oct-25	Not Started
CON-1330	Install Gas Permeable Aggregate Layer - Below 1st Floor SOG	3	3	30-Oct-25	03-Nov-25	0			30-Oct-25	03-Nov-25	30-Oct-25	03-Nov-25	Not Started
CON-1340	Install 6" C.I Pipe - Below 1st Floor SOG	2	2	30-Oct-25	31-Oct-25	1			30-Oct-25	31-Oct-25	31-Oct-25	03-Nov-25	Not Started
CON-1350	Install VI-20 Geomembrane Gas Permeable Aggregate Layer - Below 1st Floor SOG	3	3	04-Nov-25	06-Nov-25	0			04-Nov-25	06-Nov-25	04-Nov-25	06-Nov-25	Not Started
CON-1360	Install 60 Dry Mils of Liquid Boot - Below 1st Floor SOG	3	3	07-Nov-25	12-Nov-25	0			07-Nov-25	12-Nov-25	07-Nov-25	12-Nov-25	Not Started
CON-1370	Install Liquid Boot Ultrashield G-1000 - Below 1st Floor SOG	2	2	13-Nov-25	14-Nov-25	0			13-Nov-25	14-Nov-25	13-Nov-25	14-Nov-25	Not Started
CON-1380	F/R/P First Floor SOG	4	4	17-Nov-25	20-Nov-25	0			17-Nov-25	20-Nov-25	17-Nov-25	20-Nov-25	Not Started
CON-1390	Install Floor Drains - 1st Floor	2	2	19-Nov-25	20-Nov-25	25			19-Nov-25	20-Nov-25	26-Dec-25	29-Dec-25	Not Started
CON-1400	F/R/P Concrete Slab - 2nd Floor	5	5	21-Nov-25	28-Nov-25	0			21-Nov-25	28-Nov-25	21-Nov-25	28-Nov-25	Not Started
CON-1410	Install MEP Hangers - 2nd Floor	2	2	26-Nov-25	28-Nov-25	26			26-Nov-25	28-Nov-25	06-Jan-26	07-Jan-26	Not Started
CON-1420	Install Floor Drains - 2nd Floor	2	2	26-Nov-25	28-Nov-25	22			26-Nov-25	28-Nov-25	30-Dec-25	31-Dec-25	Not Started
CON-1430	F/R/P Columns & Shear Walls From Second Floor To Third Floor	3	3	01-Dec-25	03-Dec-25	0			01-Dec-25	03-Dec-25	01-Dec-25	03-Dec-25	Not Started
CON-1440	F/R/P Concrete Slab - 3rd Floor	5	5	04-Dec-25	10-Dec-25	0			04-Dec-25	10-Dec-25	04-Dec-25	10-Dec-25	Not Started
CON-1450	Install MEP Hangers - 3rd Floor	2	2	09-Dec-25	10-Dec-25	20			09-Dec-25	10-Dec-25	08-Jan-26	09-Jan-26	Not Started
CON-1460	F/R/P Columns & Shear Walls From Third Floor To Fourth Floor	3	3	11-Dec-25	15-Dec-25	0			11-Dec-25	15-Dec-25	11-Dec-25	15-Dec-25	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-1470	Install Floor Drains - 3rd Floor	2	2	11-Dec-25	12-Dec-25	14			11-Dec-25	12-Dec-25	02-Jan-26	05-Jan-26	Not Started
CON-1480	Install Elevator Hoist Pad	3	3	11-Dec-25	15-Dec-25	79			11-Dec-25	15-Dec-25	07-Apr-26	09-Apr-26	Not Started
CON-1490	F/R/P Concrete Slab - 4th Floor	4	4	16-Dec-25	19-Dec-25	0			16-Dec-25	19-Dec-25	16-Dec-25	19-Dec-25	Not Started
CON-1500	Erect Material Hoist	2	2	16-Dec-25	17-Dec-25	79			16-Dec-25	17-Dec-25	10-Apr-26	13-Apr-26	Not Started
CON-1510	Install MEP Hangers - 4th Floor	2	2	18-Dec-25	19-Dec-25	15			18-Dec-25	19-Dec-25	12-Jan-26	13-Jan-26	Not Started
CON-1520	Install Floor Drains - 4th Floor	2	2	18-Dec-25	19-Dec-25	11			18-Dec-25	19-Dec-25	06-Jan-26	07-Jan-26	Not Started
CON-1530	Drop Test & Sign-Off	2	2	18-Dec-25	19-Dec-25	79			18-Dec-25	19-Dec-25	14-Apr-26	15-Apr-26	Not Started
CON-1540	Install Mainroof Posts and Framing	7	7	22-Dec-25	31-Dec-25	0			22-Dec-25	31-Dec-25	22-Dec-25	31-Dec-25	Not Started
CON-1550	F/R/P Concrete Columns From Fourth Slab to Lower Roof Slab-4th Floor	2	2	22-Dec-25	23-Dec-25	2			22-Dec-25	23-Dec-25	24-Dec-25	26-Dec-25	Not Started
CON-1560	F/R/P Concrete Slab- Lower Roof	4	4	24-Dec-25	30-Dec-25	2			24-Dec-25	30-Dec-25	29-Dec-25	02-Jan-26	Not Started
CON-1570	Install MEP Hangers - Lower Roof	2	2	29-Dec-25	30-Dec-25	11			29-Dec-25	30-Dec-25	14-Jan-26	15-Jan-26	Not Started
CON-1580	Install Floor Drains - Lower Roof	2	2	29-Dec-25	30-Dec-25	7			29-Dec-25	30-Dec-25	08-Jan-26	09-Jan-26	Not Started
CON-1590	Install Penthouse Posts and Roof Framing	3	3	31-Dec-25	05-Jan-26	8			31-Dec-25	05-Jan-26	13-Jan-26	15-Jan-26	Not Started
CON-1600	Install Dunnage Framing - Lower Roof	4	4	31-Dec-25	06-Jan-26	2			31-Dec-25	06-Jan-26	05-Jan-26	08-Jan-26	Not Started
CON-1610	F/R/P Parapets - Lower Roof	3	3	31-Dec-25	05-Jan-26	11			31-Dec-25	05-Jan-26	16-Jan-26	21-Jan-26	Not Started
CON-1620	F/R/P Concrete Deck Slab - Upper Roof	5	5	02-Jan-26	08-Jan-26	0			02-Jan-26	08-Jan-26	02-Jan-26	08-Jan-26	Not Started
CON-1630	Pour Concrete Topping Slab	3	3	07-Jan-26	09-Jan-26	10			07-Jan-26	09-Jan-26	22-Jan-26	26-Jan-26	Not Started
CON-1640	Install RTU-2 - Lower Roof	6	6	07-Jan-26	14-Jan-26	192			07-Jan-26	14-Jan-26	13-Oct-26	20-Oct-26	Not Started
CON-1650	Install Fans - Lower Roof	4	4	07-Jan-26	12-Jan-26	196			07-Jan-26	12-Jan-26	19-Oct-26	22-Oct-26	Not Started
CON-1660	Install Emergency Generator - Lower Roof	10	10	07-Jan-26	21-Jan-26	186			07-Jan-26	21-Jan-26	02-Oct-26	16-Oct-26	Not Started
CON-1670	Install MEP Hangers - Upper Roof	2	2	07-Jan-26	08-Jan-26	7			07-Jan-26	08-Jan-26	16-Jan-26	20-Jan-26	Not Started
CON-1680	Install Floor Drains - Upper Roof	2	2	07-Jan-26	08-Jan-26	3			07-Jan-26	08-Jan-26	12-Jan-26	13-Jan-26	Not Started
CON-1690	Layout - Cellar Floor	2	2	09-Jan-26	12-Jan-26	34			09-Jan-26	12-Jan-26	02-Mar-26	03-Mar-26	Not Started
CON-1700	F/R/P Columns and Slab of The Bulkheads	4	4	09-Jan-26	14-Jan-26	3			09-Jan-26	14-Jan-26	14-Jan-26	20-Jan-26	Not Started
CON-1710	Install Dunnage Framing - Upper Roof	7	7	09-Jan-26	20-Jan-26	0			09-Jan-26	20-Jan-26	09-Jan-26	20-Jan-26	Not Started
CON-1720	Rough-in Duct Risers - Cellar Floor	3	3	09-Jan-26	13-Jan-26	35			09-Jan-26	13-Jan-26	03-Mar-26	05-Mar-26	Not Started
CON-1730	F/R/P Parapets - Upper Roof	3	3	09-Jan-26	13-Jan-26	10			09-Jan-26	13-Jan-26	26-Jan-26	28-Jan-26	Not Started
CON-1740	Install Hot Fluid-Applied Rubberized Asphalt	4	4	12-Jan-26	15-Jan-26	10			12-Jan-26	15-Jan-26	27-Jan-26	30-Jan-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
	Fabric-Reinforced Roofing Membrane												
CON-1750	Layout - 2nd Floor	2	2	13-Jan-26	14-Jan-26	54			13-Jan-26	14-Jan-26	01-Apr-26	02-Apr-26	Not Started
CON-1760	Install Top & Bottom Tracks - Cellar Floor	2	2	13-Jan-26	14-Jan-26	34			13-Jan-26	14-Jan-26	04-Mar-26	05-Mar-26	Not Started
CON-1770	Install CMU - Cellar Floor	3	3	13-Jan-26	15-Jan-26	114			13-Jan-26	15-Jan-26	26-Jun-26	30-Jun-26	Not Started
CON-1780	Install Scaffolding - North Elevation	4	4	14-Jan-26	20-Jan-26	10			14-Jan-26	20-Jan-26	29-Jan-26	03-Feb-26	Not Started
CON-1790	Rough-in Refrigerant Piping - Cellar Floor	5	5	14-Jan-26	21-Jan-26	151			14-Jan-26	21-Jan-26	20-Aug-26	26-Aug-26	Not Started
CON-1800	Rough-in Duct Risers - 2nd Floor	3	3	14-Jan-26	16-Jan-26	161			14-Jan-26	16-Jan-26	03-Sep-26	08-Sep-26	Not Started
CON-1810	Rough-in Electrical Risers (Power & Low Voltage) - Cellar Floor	3	3	14-Jan-26	16-Jan-26	88			14-Jan-26	16-Jan-26	20-May-26	22-May-26	Not Started
CON-1820	Rough-in SSDS Risers - Cellar Floor	3	3	14-Jan-26	16-Jan-26	88			14-Jan-26	16-Jan-26	20-May-26	22-May-26	Not Started
CON-1830	Layout - 3rd Floor	2	2	15-Jan-26	16-Jan-26	64			15-Jan-26	16-Jan-26	17-Apr-26	20-Apr-26	Not Started
CON-1840	Install Top & Bottom Tracks - 2nd Floor	2	2	15-Jan-26	16-Jan-26	54			15-Jan-26	16-Jan-26	03-Apr-26	06-Apr-26	Not Started
CON-1850	Rough-in Duct Work -VAV Devices & Diffusers - Cellar Floor	5	5	15-Jan-26	22-Jan-26	34			15-Jan-26	22-Jan-26	06-Mar-26	12-Mar-26	Not Started
CON-1860	Install Fabric Reinforcing Sheet	4	4	16-Jan-26	22-Jan-26	10			16-Jan-26	22-Jan-26	02-Feb-26	05-Feb-26	Not Started
CON-1870	Install CMU - 2nd Floor	3	3	16-Jan-26	21-Jan-26	114			16-Jan-26	21-Jan-26	01-Jul-26	06-Jul-26	Not Started
CON-1880	Layout - 4th Floor	2	2	20-Jan-26	21-Jan-26	69			20-Jan-26	21-Jan-26	28-Apr-26	29-Apr-26	Not Started
CON-1890	Install Top & Bottom Tracks - 3rd Floor	2	2	20-Jan-26	21-Jan-26	64			20-Jan-26	21-Jan-26	21-Apr-26	22-Apr-26	Not Started
CON-1900	Rough-in Duct Risers - 3rd Floor	3	3	20-Jan-26	22-Jan-26	161			20-Jan-26	22-Jan-26	09-Sep-26	11-Sep-26	Not Started
CON-1910	Rough-in Electrical Risers (Power & Low Voltage) - 2nd Floor	3	3	20-Jan-26	22-Jan-26	88			20-Jan-26	22-Jan-26	26-May-26	28-May-26	Not Started
CON-1920	Rough-in Plumbing Risers - Cellar Floor	3	3	20-Jan-26	22-Jan-26	88			20-Jan-26	22-Jan-26	26-May-26	28-May-26	Not Started
CON-1930	Rough-in SSDS Risers - 2nd Floor	3	3	20-Jan-26	22-Jan-26	88			20-Jan-26	22-Jan-26	26-May-26	28-May-26	Not Started
CON-1940	Scaffolding Inspection & Sign-Off -North Elevation	2	2	21-Jan-26	22-Jan-26	16			21-Jan-26	22-Jan-26	12-Feb-26	13-Feb-26	Not Started
CON-1950	Install Scaffolding - East Elevation	2	2	21-Jan-26	22-Jan-26	10			21-Jan-26	22-Jan-26	04-Feb-26	05-Feb-26	Not Started
CON-1960	Pour Concrete Topping Slab	4	4	21-Jan-26	26-Jan-26	0			21-Jan-26	26-Jan-26	21-Jan-26	26-Jan-26	Not Started
CON-1970	Install RTU-1 - Upper Roof	6	6	21-Jan-26	28-Jan-26	189			21-Jan-26	28-Jan-26	21-Oct-26	28-Oct-26	Not Started
CON-1980	Install RTU-3 - Upper Roof	6	6	21-Jan-26	28-Jan-26	189			21-Jan-26	28-Jan-26	21-Oct-26	28-Oct-26	Not Started
CON-1990	Install RTU-4 - Upper Roof	6	6	21-Jan-26	28-Jan-26	189			21-Jan-26	28-Jan-26	21-Oct-26	28-Oct-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-2000	Install Fans - Upper Roof	4	4	21-Jan-26	26-Jan-26	191			21-Jan-26	26-Jan-26	23-Oct-26	28-Oct-26	Not Started
CON-2010	Layout - Lower Roof	2	2	22-Jan-26	23-Jan-26	74			22-Jan-26	23-Jan-26	07-May-26	08-May-26	Not Started
CON-2020	Install Top & Bottom Tracks - 4th Floor	2	2	22-Jan-26	23-Jan-26	69			22-Jan-26	23-Jan-26	30-Apr-26	01-May-26	Not Started
CON-2030	Install CMU - 3rd Floor	3	3	22-Jan-26	26-Jan-26	114			22-Jan-26	26-Jan-26	07-Jul-26	09-Jul-26	Not Started
CON-2040	Rough-in Refrigerant Piping - 2nd Floor	5	5	22-Jan-26	28-Jan-26	151			22-Jan-26	28-Jan-26	27-Aug-26	02-Sep-26	Not Started
CON-2050	Emergency Generator Electric Load Test	3	3	22-Jan-26	24-Jan-26	270			22-Jan-26	24-Jan-26	19-Oct-26	21-Oct-26	Not Started
CON-2060	Install 5/8 Sheathing -North Elevation	4	4	23-Jan-26	28-Jan-26	16			23-Jan-26	28-Jan-26	17-Feb-26	20-Feb-26	Not Started
CON-2070	Scaffolding Inspection & Sign-Off - East Elevation	2	2	23-Jan-26	26-Jan-26	18			23-Jan-26	26-Jan-26	19-Feb-26	20-Feb-26	Not Started
CON-2080	Install Scaffolding - South Elevation	4	4	23-Jan-26	28-Jan-26	10			23-Jan-26	28-Jan-26	06-Feb-26	11-Feb-26	Not Started
CON-2090	Install Protection Sheet and Roof Barrier	3	3	23-Jan-26	27-Jan-26	10			23-Jan-26	27-Jan-26	06-Feb-26	10-Feb-26	Not Started
CON-2100	Install Steel Studs - Cellar Floor	4	4	23-Jan-26	28-Jan-26	49			23-Jan-26	28-Jan-26	03-Apr-26	08-Apr-26	Not Started
CON-2110	Install AC-C17.1 - Cellar	3	3	23-Jan-26	27-Jan-26	84			23-Jan-26	27-Jan-26	22-May-26	27-May-26	Not Started
CON-2120	Install AC-C17.2 - Cellar	3	3	23-Jan-26	27-Jan-26	84			23-Jan-26	27-Jan-26	22-May-26	27-May-26	Not Started
CON-2130	Rough-in Duct Work -VAV Devices & Diffusers - 2nd Floor	5	5	23-Jan-26	29-Jan-26	51			23-Jan-26	29-Jan-26	07-Apr-26	13-Apr-26	Not Started
CON-2140	Install Electric Unit Heater - Cellar Floor	2	2	23-Jan-26	26-Jan-26	171			23-Jan-26	26-Jan-26	28-Sep-26	29-Sep-26	Not Started
CON-2150	Rough-in Duct Risers - 4th Floor	3	3	23-Jan-26	27-Jan-26	161			23-Jan-26	27-Jan-26	14-Sep-26	16-Sep-26	Not Started
CON-2160	Rough-in Power Conduits & Wires - Cellar Floor	5	5	23-Jan-26	29-Jan-26	34			23-Jan-26	29-Jan-26	13-Mar-26	19-Mar-26	Not Started
CON-2170	Rough-in Electrical Risers (Power & Low Voltage) - 3rd Floor	3	3	23-Jan-26	27-Jan-26	88			23-Jan-26	27-Jan-26	29-May-26	02-Jun-26	Not Started
CON-2180	Rough-in Plumbing Risers - 2nd Floor	3	3	23-Jan-26	27-Jan-26	88			23-Jan-26	27-Jan-26	29-May-26	02-Jun-26	Not Started
CON-2190	Rough-in SSDS Risers - 3rd Floor	3	3	23-Jan-26	27-Jan-26	88			23-Jan-26	27-Jan-26	29-May-26	02-Jun-26	Not Started
CON-2200	Install Top & Bottom Tracks - Lower Roof	2	2	26-Jan-26	27-Jan-26	74			26-Jan-26	27-Jan-26	11-May-26	12-May-26	Not Started
CON-2210	Install 5/8 Sheathing - East Elevation	3	3	27-Jan-26	29-Jan-26	18			27-Jan-26	29-Jan-26	23-Feb-26	25-Feb-26	Not Started
CON-2220	Install Hot Fluid-Applied Rubberized Asphalt Fabric-Reinforced Roofing Membrane	5	5	27-Jan-26	02-Feb-26	0			27-Jan-26	02-Feb-26	27-Jan-26	02-Feb-26	Not Started
CON-2230	Install CMU - 4th Floor	3	3	27-Jan-26	29-Jan-26	114			27-Jan-26	29-Jan-26	10-Jul-26	14-Jul-26	Not Started
CON-2240	Obtain Emergency Generator Permit	5	5	26-Jan-26	30-Jan-26	187			26-Jan-26	30-Jan-26	22-Oct-26	28-Oct-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-2250	Install 1/2" Drainage Panel	3	3	28-Jan-26	30-Jan-26	10			28-Jan-26	30-Jan-26	11-Feb-26	13-Feb-26	Not Started
CON-2260	Rough-in Duct Risers - Lower Roof	3	3	28-Jan-26	30-Jan-26	161			28-Jan-26	30-Jan-26	17-Sep-26	21-Sep-26	Not Started
CON-2270	Rough-in Electrical Risers (Power & Low Voltage) - 4th Floor	3	3	28-Jan-26	30-Jan-26	88			28-Jan-26	30-Jan-26	03-Jun-26	05-Jun-26	Not Started
CON-2280	Rough-in Plumbing Risers - 3rd Floor	3	3	28-Jan-26	30-Jan-26	88			28-Jan-26	30-Jan-26	03-Jun-26	05-Jun-26	Not Started
CON-2290	Rough-in SSDS Risers - 4th Floor	3	3	28-Jan-26	30-Jan-26	88			28-Jan-26	30-Jan-26	03-Jun-26	05-Jun-26	Not Started
CON-2300	Install 6" Semi-Rigid Mineral Wool System -North Elevation	4	4	29-Jan-26	03-Feb-26	16			29-Jan-26	03-Feb-26	23-Feb-26	26-Feb-26	Not Started
CON-2310	Scaffolding Inspection & Sign-Off -South Elevation	2	2	29-Jan-26	30-Jan-26	10			29-Jan-26	30-Jan-26	12-Feb-26	13-Feb-26	Not Started
CON-2320	Install Scaffolding - West Elevation	2	2	29-Jan-26	30-Jan-26	12			29-Jan-26	30-Jan-26	17-Feb-26	18-Feb-26	Not Started
CON-2330	Rough-in Refrigerant Piping - 3rd Floor	5	5	29-Jan-26	04-Feb-26	151			29-Jan-26	04-Feb-26	03-Sep-26	10-Sep-26	Not Started
CON-2340	HVAC System Testing and Commissioning	5	5	29-Jan-26	02-Feb-26	273			29-Jan-26	02-Feb-26	29-Oct-26	02-Nov-26	Not Started
CON-2350	Install 6" Semi-Rigid Mineral Wool System - East Elevation	3	3	30-Jan-26	03-Feb-26	18			30-Jan-26	03-Feb-26	26-Feb-26	02-Mar-26	Not Started
CON-2360	Install Steel Studs - 2nd Floor	4	4	30-Jan-26	04-Feb-26	51			30-Jan-26	04-Feb-26	14-Apr-26	17-Apr-26	Not Started
CON-2370	Install CMU - Lower Roof	3	3	30-Jan-26	03-Feb-26	114			30-Jan-26	03-Feb-26	15-Jul-26	17-Jul-26	Not Started
CON-2380	Install AC-204 - 2nd Floor	3	3	30-Jan-26	03-Feb-26	82			30-Jan-26	03-Feb-26	28-May-26	01-Jun-26	Not Started
CON-2390	Rough-in Duct Work -VAV Devices & Diffusers - 3rd Floor	5	5	30-Jan-26	05-Feb-26	53			30-Jan-26	05-Feb-26	16-Apr-26	22-Apr-26	Not Started
CON-2400	Rough-in Power Conduits & Wires - 2nd Floor	5	5	30-Jan-26	05-Feb-26	68			30-Jan-26	05-Feb-26	07-May-26	13-May-26	Not Started
CON-2410	Rough-in Low Voltage Conduits & Wires - Cellar Floor	5	5	30-Jan-26	05-Feb-26	34			30-Jan-26	05-Feb-26	20-Mar-26	26-Mar-26	Not Started
CON-2420	Install Service End Box	4	4	30-Jan-26	04-Feb-26	150			30-Jan-26	04-Feb-26	03-Sep-26	09-Sep-26	Not Started
CON-2430	Install 5/8 Sheathing -South Elevation	4	4	02-Feb-26	05-Feb-26	10			02-Feb-26	05-Feb-26	17-Feb-26	20-Feb-26	Not Started
CON-2440	Scaffolding Inspection & Sign-Off - West Elevation	2	2	02-Feb-26	03-Feb-26	12			02-Feb-26	03-Feb-26	19-Feb-26	20-Feb-26	Not Started
CON-2450	Install 8" Roof Insulation (R-40 Min) Multi-Layered and Staggered	5	5	02-Feb-26	06-Feb-26	10			02-Feb-26	06-Feb-26	17-Feb-26	23-Feb-26	Not Started
CON-2460	Rough-in Duct Risers - 1st Floor	3	3	02-Feb-26	04-Feb-26	161			02-Feb-26	04-Feb-26	22-Sep-26	24-Sep-26	Not Started
CON-2470	Rough-in Electrical Risers (Power & Low Voltage) - Lower Roof	3	3	02-Feb-26	04-Feb-26	88			02-Feb-26	04-Feb-26	08-Jun-26	10-Jun-26	Not Started
CON-2480	Rough-in Plumbing Risers - 4th Floor	3	3	02-Feb-26	04-Feb-26	88			02-Feb-26	04-Feb-26	08-Jun-26	10-Jun-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-2490	Rough-in SSDS Risers - Lower Roof	3	3	02-Feb-26	04-Feb-26	88			02-Feb-26	04-Feb-26	08-Jun-26	10-Jun-26	Not Started
CON-2500	Emergency Generator Final Sign-off	0	0		30-Jan-26	271				30-Jan-26		28-Oct-26	Not Started
CON-2510	Install Fabric Reinforcing Sheet	4	4	03-Feb-26	06-Feb-26	0			03-Feb-26	06-Feb-26	03-Feb-26	06-Feb-26	Not Started
CON-2520	Install Metal Clip System -North Elevation	2	2	04-Feb-26	05-Feb-26	116			04-Feb-26	05-Feb-26	22-Jul-26	23-Jul-26	Not Started
CON-2530	Install Brick Veneer -North Elevation	3	3	04-Feb-26	06-Feb-26	121			04-Feb-26	06-Feb-26	29-Jul-26	31-Jul-26	Not Started
CON-2540	Install Window Frames & Windows / Storefronts -North Elevation	5	5	04-Feb-26	10-Feb-26	16			04-Feb-26	10-Feb-26	27-Feb-26	05-Mar-26	Not Started
CON-2550	Install Metal Clip System - East Elevation	2	2	04-Feb-26	05-Feb-26	112			04-Feb-26	05-Feb-26	16-Jul-26	17-Jul-26	Not Started
CON-2560	Install Brick Veneer - East Elevation	2	2	04-Feb-26	05-Feb-26	116			04-Feb-26	05-Feb-26	22-Jul-26	23-Jul-26	Not Started
CON-2570	Install Window Frames & Windows / Storefronts - East Elevation	3	3	04-Feb-26	06-Feb-26	18			04-Feb-26	06-Feb-26	03-Mar-26	05-Mar-26	Not Started
CON-2580	Install 5/8 Sheathing - West Elevation	3	3	04-Feb-26	06-Feb-26	12			04-Feb-26	06-Feb-26	23-Feb-26	25-Feb-26	Not Started
CON-2590	Rough-in Refrigerant Piping - 4th Floor	5	5	05-Feb-26	11-Feb-26	151			05-Feb-26	11-Feb-26	11-Sep-26	17-Sep-26	Not Started
CON-2600	Rough-in Electrical Risers (Power & Low Voltage) - 1st Floor	3	3	05-Feb-26	09-Feb-26	88			05-Feb-26	09-Feb-26	11-Jun-26	15-Jun-26	Not Started
CON-2610	Install Switch Boards (SWBD-1, SWBD-2, SWBD-3)	10	10	05-Feb-26	19-Feb-26	150			05-Feb-26	19-Feb-26	10-Sep-26	23-Sep-26	Not Started
CON-2620	Install Fire Alarm Fused Disconnect Switch	3	3	05-Feb-26	09-Feb-26	157			05-Feb-26	09-Feb-26	21-Sep-26	23-Sep-26	Not Started
CON-2630	Rough-in Plumbing Risers - Lower Roof	3	3	05-Feb-26	09-Feb-26	88			05-Feb-26	09-Feb-26	11-Jun-26	15-Jun-26	Not Started
CON-2640	Rough-in SSDS Risers - 1st Floor	3	3	05-Feb-26	09-Feb-26	88			05-Feb-26	09-Feb-26	11-Jun-26	15-Jun-26	Not Started
CON-2650	Install Graffiti Resistant Coating At Brick - East Elevation	2	2	06-Feb-26	09-Feb-26	116			06-Feb-26	09-Feb-26	24-Jul-26	27-Jul-26	Not Started
CON-2660	Install 6" Semi-Rigid Mineral Wool System -South Elevation	4	4	06-Feb-26	11-Feb-26	10			06-Feb-26	11-Feb-26	23-Feb-26	26-Feb-26	Not Started
CON-2670	Install Steel Studs - 3rd Floor	4	4	06-Feb-26	11-Feb-26	53			06-Feb-26	11-Feb-26	23-Apr-26	28-Apr-26	Not Started
CON-2680	Rough-in Duct Work -VAV Devices & Diffusers - 4th Floor	5	5	06-Feb-26	12-Feb-26	55			06-Feb-26	12-Feb-26	27-Apr-26	01-May-26	Not Started
CON-2690	Rough-in Power Conduits & Wires - 3rd Floor	5	5	06-Feb-26	12-Feb-26	68			06-Feb-26	12-Feb-26	14-May-26	20-May-26	Not Started
CON-2700	Rough-in Low Voltage Conduits & Wires - 2nd Floor	5	5	06-Feb-26	12-Feb-26	68			06-Feb-26	12-Feb-26	14-May-26	20-May-26	Not Started
CON-2710	Rough-in Plumbing Pipes- Cellar Floor	5	5	06-Feb-26	12-Feb-26	34			06-Feb-26	12-Feb-26	27-Mar-26	02-Apr-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-2720	Install Electrical Panels - Cellar Floor	5	5	06-Feb-26	12-Feb-26	53			06-Feb-26	12-Feb-26	23-Apr-26	29-Apr-26	Not Started
CON-2730	Install Graffiti Resistant Coating At Brick -North Elevation	2	2	09-Feb-26	10-Feb-26	121			09-Feb-26	10-Feb-26	03-Aug-26	04-Aug-26	Not Started
CON-2740	Install Terra Cotta Panel Rainscreen - East Elevation	6	6	09-Feb-26	17-Feb-26	111			09-Feb-26	17-Feb-26	20-Jul-26	27-Jul-26	Not Started
CON-2750	Install 6" Semi-Rigid Mineral Wool System - West Elevation	3	3	09-Feb-26	11-Feb-26	12			09-Feb-26	11-Feb-26	26-Feb-26	02-Mar-26	Not Started
CON-2760	Install Filter Fabric	3	3	09-Feb-26	11-Feb-26	10			09-Feb-26	11-Feb-26	24-Feb-26	26-Feb-26	Not Started
CON-2770	Install Protection Sheet and Roof Barrier	4	4	09-Feb-26	12-Feb-26	0			09-Feb-26	12-Feb-26	09-Feb-26	12-Feb-26	Not Started
CON-2780	Rough-in Plumbing Risers - 1st Floor	3	3	10-Feb-26	12-Feb-26	88			10-Feb-26	12-Feb-26	16-Jun-26	18-Jun-26	Not Started
CON-2790	Install Terra Cotta Panel Rainscreen -North Elevation	10	10	11-Feb-26	25-Feb-26	113			11-Feb-26	25-Feb-26	24-Jul-26	06-Aug-26	Not Started
CON-2800	Install Exterior Wall Lights -North Elevation	2	2	11-Feb-26	12-Feb-26	121			11-Feb-26	12-Feb-26	05-Aug-26	06-Aug-26	Not Started
CON-2810	Install Metal Clip System -South Elevation	2	2	12-Feb-26	13-Feb-26	113			12-Feb-26	13-Feb-26	27-Jul-26	28-Jul-26	Not Started
CON-2820	Install Brick Veneer -South Elevation	3	3	12-Feb-26	17-Feb-26	118			12-Feb-26	17-Feb-26	03-Aug-26	05-Aug-26	Not Started
CON-2830	Install Window Frames & Windows / Storefronts -South Elevation	5	5	12-Feb-26	19-Feb-26	10			12-Feb-26	19-Feb-26	27-Feb-26	05-Mar-26	Not Started
CON-2840	Install Metal Clip System - West Elevation	2	2	12-Feb-26	13-Feb-26	108			12-Feb-26	13-Feb-26	20-Jul-26	21-Jul-26	Not Started
CON-2850	Install Brick Veneer - West Elevation	2	2	12-Feb-26	13-Feb-26	112			12-Feb-26	13-Feb-26	24-Jul-26	27-Jul-26	Not Started
CON-2860	Install Window Frames & Windows / Storefronts - West Elevation	3	3	12-Feb-26	17-Feb-26	12			12-Feb-26	17-Feb-26	03-Mar-26	05-Mar-26	Not Started
CON-2870	Rough-in Refrigerant Piping - Lower Roof	5	5	12-Feb-26	19-Feb-26	151			12-Feb-26	19-Feb-26	18-Sep-26	24-Sep-26	Not Started
CON-2880	Lower Roofing Testing	5	5	12-Feb-26	19-Feb-26	10			12-Feb-26	19-Feb-26	27-Feb-26	05-Mar-26	Not Started
CON-2890	Install 1/2" Drainage Panel	4	4	13-Feb-26	19-Feb-26	0			13-Feb-26	19-Feb-26	13-Feb-26	19-Feb-26	Not Started
CON-2900	Install Steel Studs - 4th Floor	4	4	13-Feb-26	19-Feb-26	55			13-Feb-26	19-Feb-26	04-May-26	07-May-26	Not Started
CON-2910	Install AC-412 - 4th Floor	3	3	13-Feb-26	18-Feb-26	86			13-Feb-26	18-Feb-26	17-Jun-26	22-Jun-26	Not Started
CON-2920	Rough-in Duct Work -VAV Devices & Diffusers - Lower Roof	5	5	13-Feb-26	20-Feb-26	57			13-Feb-26	20-Feb-26	06-May-26	12-May-26	Not Started
CON-2930	F/R/P Concrete Pads - Fuel Tank Room	3	3	13-Feb-26	18-Feb-26	34			13-Feb-26	18-Feb-26	03-Apr-26	07-Apr-26	Not Started
CON-2940	Rough-in Power Conduits & Wires - 4th Floor	5	5	13-Feb-26	20-Feb-26	68			13-Feb-26	20-Feb-26	21-May-26	28-May-26	Not Started
CON-2950	Rough-in Low Voltage Conduits & Wires - 3rd Floor	5	5	13-Feb-26	20-Feb-26	68			13-Feb-26	20-Feb-26	21-May-26	28-May-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-2960	Install Main Ground Bus	3	3	13-Feb-26	18-Feb-26	89			13-Feb-26	18-Feb-26	23-Jun-26	25-Jun-26	Not Started
CON-2970	Rough-in Plumbing Pipes - 2nd Floor	5	5	13-Feb-26	20-Feb-26	68			13-Feb-26	20-Feb-26	21-May-26	28-May-26	Not Started
CON-2980	Install Electrical Panels - 2nd Floor	5	5	13-Feb-26	20-Feb-26	53			13-Feb-26	20-Feb-26	30-Apr-26	06-May-26	Not Started
CON-2990	Rough-in Sprinkler Piping - Cellar Floor	5	5	13-Feb-26	20-Feb-26	35			13-Feb-26	20-Feb-26	06-Apr-26	10-Apr-26	Not Started
CON-3000	Install Graffiti Resistant Coating At Brick - West Elevation	2	2	17-Feb-26	18-Feb-26	112			17-Feb-26	18-Feb-26	28-Jul-26	29-Jul-26	Not Started
CON-3010	Paint Exterior Elevation @ Window Sections - East Elevation	2	2	18-Feb-26	19-Feb-26	111			18-Feb-26	19-Feb-26	28-Jul-26	29-Jul-26	Not Started
CON-3020	Install Graffiti Resistant Coating At Brick -South Elevation	2	2	18-Feb-26	19-Feb-26	118			18-Feb-26	19-Feb-26	06-Aug-26	07-Aug-26	Not Started
CON-3030	Install Terra Cotta Panel Rainscreen - West Elevation	6	6	18-Feb-26	25-Feb-26	107			18-Feb-26	25-Feb-26	22-Jul-26	29-Jul-26	Not Started
CON-3040	Install Fuel Oil Transfer Pump (FP-1) - Fuel Tank Room	4	4	19-Feb-26	24-Feb-26	34			19-Feb-26	24-Feb-26	08-Apr-26	13-Apr-26	Not Started
CON-3050	Install Domestic Water Booster Pump (DWBP-1)	5	5	19-Feb-26	25-Feb-26	170			19-Feb-26	25-Feb-26	22-Oct-26	28-Oct-26	Not Started
CON-3060	Install Sprinkler Booster Panel	3	3	19-Feb-26	23-Feb-26	90			19-Feb-26	23-Feb-26	29-Jun-26	01-Jul-26	Not Started
CON-3070	Install Jockey Pump	3	3	19-Feb-26	23-Feb-26	90			19-Feb-26	23-Feb-26	29-Jun-26	01-Jul-26	Not Started
CON-3080	Install Water Filter Devices	3	3	19-Feb-26	23-Feb-26	178			19-Feb-26	23-Feb-26	03-Nov-26	05-Nov-26	Not Started
CON-3090	Install Domestic Cold Water Booster Pump (DWBP-1)	4	4	19-Feb-26	24-Feb-26	171			19-Feb-26	24-Feb-26	23-Oct-26	28-Oct-26	Not Started
CON-3100	Install Duplex Sewage Ejector Pump (SE-1)	4	4	19-Feb-26	24-Feb-26	171			19-Feb-26	24-Feb-26	23-Oct-26	28-Oct-26	Not Started
CON-3110	Install Sprinkler Booster Pumps	4	4	19-Feb-26	24-Feb-26	89			19-Feb-26	24-Feb-26	26-Jun-26	01-Jul-26	Not Started
CON-3120	Install Sprinkler Heads - Cellar Floor	2	2	19-Feb-26	20-Feb-26	83			19-Feb-26	20-Feb-26	17-Jun-26	18-Jun-26	Not Started
CON-3130	Scaffolding Removal Inspection & Sign-Off - East Elevation	2	2	20-Feb-26	23-Feb-26	111			20-Feb-26	23-Feb-26	30-Jul-26	31-Jul-26	Not Started
CON-3140	Install Terra Cotta Panel Rainscreen -South Elevation	10	10	20-Feb-26	05-Mar-26	110			20-Feb-26	05-Mar-26	29-Jul-26	11-Aug-26	Not Started
CON-3150	Install Wall Speakers -South Elevation	2	2	20-Feb-26	23-Feb-26	118			20-Feb-26	23-Feb-26	10-Aug-26	11-Aug-26	Not Started
CON-3160	Install Air Layer	2	2	20-Feb-26	23-Feb-26	154			20-Feb-26	23-Feb-26	30-Sep-26	01-Oct-26	Not Started
CON-3170	Install Paver Pedestal System	5	5	20-Feb-26	26-Feb-26	149			20-Feb-26	26-Feb-26	23-Sep-26	29-Sep-26	Not Started
CON-3180	Install 8" Roof Insulation (R-40 Min) Multi-Layered and Staggered	5	5	20-Feb-26	26-Feb-26	0			20-Feb-26	26-Feb-26	20-Feb-26	26-Feb-26	Not Started
CON-3190	Install Main Service Switch Board (MSS#1 & MSS#2)	8	8	20-Feb-26	03-Mar-26	150			20-Feb-26	03-Mar-26	24-Sep-26	05-Oct-26	Not Started
CON-3200	Install Steel Studs - Lower Roof	4	4	23-Feb-26	26-Feb-26	57			23-Feb-26	26-Feb-26	13-May-26	18-May-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-3210	Install Ceiling Hangers - Cellar Floor	5	5	23-Feb-26	27-Feb-26	35			23-Feb-26	27-Feb-26	13-Apr-26	17-Apr-26	Not Started
CON-3220	Install Electric Unit Heater - Lower Roof	2	2	23-Feb-26	24-Feb-26	153			23-Feb-26	24-Feb-26	30-Sep-26	01-Oct-26	Not Started
CON-3230	Rough-in Power Conduits & Wires - Lower Roof	5	5	23-Feb-26	27-Feb-26	68			23-Feb-26	27-Feb-26	29-May-26	04-Jun-26	Not Started
CON-3240	Rough-in Low Voltage Conduits & Wires - 4th Floor	5	5	23-Feb-26	27-Feb-26	68			23-Feb-26	27-Feb-26	29-May-26	04-Jun-26	Not Started
CON-3250	Rough-in Plumbing Pipes - 3rd Floor	5	5	23-Feb-26	27-Feb-26	68			23-Feb-26	27-Feb-26	29-May-26	04-Jun-26	Not Started
CON-3260	Install Electrical Panels - 3rd Floor	5	5	23-Feb-26	27-Feb-26	53			23-Feb-26	27-Feb-26	07-May-26	13-May-26	Not Started
CON-3270	Rough-in Sprinkler Piping - 2nd Floor	5	5	23-Feb-26	27-Feb-26	63			23-Feb-26	27-Feb-26	21-May-26	28-May-26	Not Started
CON-3280	Dismantle Scaffolding - East Elevation	2	2	24-Feb-26	25-Feb-26	111			24-Feb-26	25-Feb-26	03-Aug-26	04-Aug-26	Not Started
CON-3290	Install Mineral Water Retention Layer	4	4	24-Feb-26	27-Feb-26	154			24-Feb-26	27-Feb-26	02-Oct-26	07-Oct-26	Not Started
CON-3300	Install Fuel Oil Filtration System (FFS-1) - Fuel Tank Room	4	4	25-Feb-26	02-Mar-26	34			25-Feb-26	02-Mar-26	14-Apr-26	17-Apr-26	Not Started
CON-3310	Paint Exterior Elevation @ Window Sections -North Elevation	3	3	26-Feb-26	02-Mar-26	113			26-Feb-26	02-Mar-26	07-Aug-26	11-Aug-26	Not Started
CON-3320	Paint Exterior Elevation @ Window Sections - West Elevation	2	2	26-Feb-26	27-Feb-26	107			26-Feb-26	27-Feb-26	30-Jul-26	31-Jul-26	Not Started
CON-3330	Install Sprinkler Heads - 2nd Floor	2	2	26-Feb-26	27-Feb-26	80			26-Feb-26	27-Feb-26	22-Jun-26	23-Jun-26	Not Started
CON-3340	Install Concrete Pavers	7	7	27-Feb-26	09-Mar-26	149			27-Feb-26	09-Mar-26	30-Sep-26	08-Oct-26	Not Started
CON-3350	Install Filter Fabric	3	3	27-Feb-26	03-Mar-26	0			27-Feb-26	03-Mar-26	27-Feb-26	03-Mar-26	Not Started
CON-3360	Scaffolding Removal Inspection & Sign-Off - West Elevation	2	2	02-Mar-26	03-Mar-26	107			02-Mar-26	03-Mar-26	03-Aug-26	04-Aug-26	Not Started
CON-3370	Install 18" Wide Filter Fabric Strip	2	2	02-Mar-26	03-Mar-26	154			02-Mar-26	03-Mar-26	08-Oct-26	09-Oct-26	Not Started
CON-3380	Install Ceiling Hangers - 2nd Floor	5	5	02-Mar-26	06-Mar-26	60			02-Mar-26	06-Mar-26	26-May-26	01-Jun-26	Not Started
CON-3390	Rough-in Low Voltage Conduits & Wires - Lower Roof	5	5	02-Mar-26	06-Mar-26	68			02-Mar-26	06-Mar-26	05-Jun-26	11-Jun-26	Not Started
CON-3400	Install EMR Panel	4	4	02-Mar-26	05-Mar-26	119			02-Mar-26	05-Mar-26	19-Aug-26	24-Aug-26	Not Started
CON-3410	Rough-in Plumbing Pipes - 4th Floor	5	5	02-Mar-26	06-Mar-26	68			02-Mar-26	06-Mar-26	05-Jun-26	11-Jun-26	Not Started
CON-3420	Install Electrical Panels - 4th Floor	5	5	02-Mar-26	06-Mar-26	53			02-Mar-26	06-Mar-26	14-May-26	20-May-26	Not Started
CON-3430	Rough-in Sprinkler Piping - 3rd Floor	5	5	02-Mar-26	06-Mar-26	68			02-Mar-26	06-Mar-26	05-Jun-26	11-Jun-26	Not Started
CON-3440	Scaffolding Removal Inspection & Sign-Off -North Elevation	2	2	03-Mar-26	04-Mar-26	113			03-Mar-26	04-Mar-26	12-Aug-26	13-Aug-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-3450	Install 275 GAL NYC Fuel Tank With 200% Secondary Containment	6	6	03-Mar-26	10-Mar-26	34			03-Mar-26	10-Mar-26	20-Apr-26	27-Apr-26	Not Started
CON-3460	Dismantle Scaffolding - West Elevation	2	2	04-Mar-26	05-Mar-26	107			04-Mar-26	05-Mar-26	05-Aug-26	06-Aug-26	Not Started
CON-3470	Install Extensive Growing Media	5	5	04-Mar-26	10-Mar-26	154			04-Mar-26	10-Mar-26	13-Oct-26	19-Oct-26	Not Started
CON-3480	Install TAP Section	3	3	04-Mar-26	06-Mar-26	150			04-Mar-26	06-Mar-26	06-Oct-26	08-Oct-26	Not Started
CON-3490	Upper Roofing Testing	2	2	04-Mar-26	05-Mar-26	0			04-Mar-26	05-Mar-26	04-Mar-26	05-Mar-26	Not Started
CON-3500	Dismantle Scaffolding -North Elevation	3	3	05-Mar-26	09-Mar-26	113			05-Mar-26	09-Mar-26	14-Aug-26	18-Aug-26	Not Started
CON-3510	Install Sprinkler Heads - 3rd Floor	2	2	05-Mar-26	06-Mar-26	77			05-Mar-26	06-Mar-26	24-Jun-26	25-Jun-26	Not Started
CON-3520	Install Storm Inlet 1	1	1	06-Mar-26	06-Mar-26	107			06-Mar-26	06-Mar-26	07-Aug-26	07-Aug-26	Not Started
CON-3530	Install Storm Inlet 2	1	1	06-Mar-26	06-Mar-26	107			06-Mar-26	06-Mar-26	07-Aug-26	07-Aug-26	Not Started
CON-3540	Install 60 LF of 8-IN DIP [Storm Inlet 1 to Storm Inlet 2]	1	1	06-Mar-26	06-Mar-26	107			06-Mar-26	06-Mar-26	07-Aug-26	07-Aug-26	Not Started
CON-3550	Install Domestic Water Service Piping	3	3	06-Mar-26	10-Mar-26	118			06-Mar-26	10-Mar-26	24-Aug-26	26-Aug-26	Not Started
CON-3560	Install Sewer Piping	3	3	06-Mar-26	10-Mar-26	118			06-Mar-26	10-Mar-26	24-Aug-26	26-Aug-26	Not Started
CON-3570	Install Sanitary Piping	3	3	06-Mar-26	10-Mar-26	138			06-Mar-26	10-Mar-26	22-Sep-26	24-Sep-26	Not Started
CON-3580	Install The Transformer Vault	3	3	05-May-26	07-May-26	98			05-May-26	07-May-26	24-Sep-26	28-Sep-26	Not Started
CON-3590	Install Telecom Service Point of Entry	3	3	06-Mar-26	10-Mar-26	115			06-Mar-26	10-Mar-26	19-Aug-26	21-Aug-26	Not Started
CON-3600	Paint Exterior Elevation @ Window Sections -South Elevation	3	3	06-Mar-26	10-Mar-26	110			06-Mar-26	10-Mar-26	12-Aug-26	14-Aug-26	Not Started
CON-3610	Install Air Layer	3	3	06-Mar-26	10-Mar-26	145			06-Mar-26	10-Mar-26	01-Oct-26	05-Oct-26	Not Started
CON-3620	Install Paver Pedestal System	6	6	06-Mar-26	13-Mar-26	155			06-Mar-26	13-Mar-26	16-Oct-26	23-Oct-26	Not Started
CON-3630	Install Power Panels	4	4	06-Mar-26	11-Mar-26	151			06-Mar-26	11-Mar-26	09-Oct-26	15-Oct-26	Not Started
CON-3640	Install Elevator Machines	10	10	06-Mar-26	19-Mar-26	119			06-Mar-26	19-Mar-26	25-Aug-26	08-Sep-26	Not Started
CON-3650	Install Walls GWB-Mockup Room	3	3	06-Mar-26	10-Mar-26	0			06-Mar-26	10-Mar-26	06-Mar-26	10-Mar-26	Not Started
CON-3660	Install 33 LF of 8-IN DIP [Storm Inlet 2 to Catch Basin 2]	1	1	09-Mar-26	09-Mar-26	107			09-Mar-26	09-Mar-26	10-Aug-26	10-Aug-26	Not Started
CON-3670	Install Catch Basin 2	1	1	09-Mar-26	09-Mar-26	107			09-Mar-26	09-Mar-26	10-Aug-26	10-Aug-26	Not Started
CON-3680	Install Ceiling Hangers - 3rd Floor	5	5	09-Mar-26	13-Mar-26	62			09-Mar-26	13-Mar-26	04-Jun-26	10-Jun-26	Not Started
CON-3690	Install Dry-Type Transformer	6	6	09-Mar-26	16-Mar-26	150			09-Mar-26	16-Mar-26	09-Oct-26	19-Oct-26	Not Started
CON-3700	Rough-in Plumbing Pipes - Lower Roof	5	5	09-Mar-26	13-Mar-26	68			09-Mar-26	13-Mar-26	12-Jun-26	18-Jun-26	Not Started
CON-3710	Install Electrical Panels - Lower Roof	5	5	09-Mar-26	13-Mar-26	53			09-Mar-26	13-Mar-26	21-May-26	28-May-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-3720	Rough-in Sprinkler Piping - 4th Floor	5	5	09-Mar-26	13-Mar-26	68			09-Mar-26	13-Mar-26	12-Jun-26	18-Jun-26	Not Started
CON-3730	Install Grit Champer-1	2	2	10-Mar-26	11-Mar-26	107			10-Mar-26	11-Mar-26	11-Aug-26	12-Aug-26	Not Started
CON-3740	Install 106 LF of 12-IN DIP [Catch Basin 2 to Grit Champer-1]	2	2	10-Mar-26	11-Mar-26	107			10-Mar-26	11-Mar-26	11-Aug-26	12-Aug-26	Not Started
CON-3750	Connect Water Piping To The Existing Water Line	2	2	11-Mar-26	12-Mar-26	118			11-Mar-26	12-Mar-26	27-Aug-26	28-Aug-26	Not Started
CON-3760	Connect Sewer Piping To The Existing Sewer Line	2	2	11-Mar-26	12-Mar-26	118			11-Mar-26	12-Mar-26	27-Aug-26	28-Aug-26	Not Started
CON-3770	Connect Sanitary Piping To The Existing Sanitary Line	2	2	11-Mar-26	12-Mar-26	138			11-Mar-26	12-Mar-26	25-Sep-26	28-Sep-26	Not Started
CON-3780	Verizon To Provide Connection	5	5	11-Mar-26	17-Mar-26	115			11-Mar-26	17-Mar-26	24-Aug-26	28-Aug-26	Not Started
CON-3790	Scaffolding Removal Inspection & Sign-Off -South Elevation	2	2	11-Mar-26	12-Mar-26	110			11-Mar-26	12-Mar-26	17-Aug-26	18-Aug-26	Not Started
CON-3800	Install Sedum Mat	5	5	11-Mar-26	17-Mar-26	154			11-Mar-26	17-Mar-26	20-Oct-26	26-Oct-26	Not Started
CON-3810	Install Mineral Water Retention Layer	5	5	11-Mar-26	17-Mar-26	145			11-Mar-26	17-Mar-26	06-Oct-26	13-Oct-26	Not Started
CON-3820	Install Fuel Oil Pipings	3	3	11-Mar-26	13-Mar-26	34			11-Mar-26	13-Mar-26	28-Apr-26	30-Apr-26	Not Started
CON-3830	Install 6 Sets of 4#500MCM IN 4" RGS Conduits & 3 Spare 4" RGS Conduits Encased In Concrete	3	3	08-May-26	12-May-26	111			08-May-26	12-May-26	19-Oct-26	21-Oct-26	Not Started
CON-3840	Install Aluminum Lighting Conductor	3	3	08-May-26	12-May-26	111			08-May-26	12-May-26	19-Oct-26	21-Oct-26	Not Started
CON-3850	Install Door Frames-Mockup Room	2	2	11-Mar-26	12-Mar-26	0			11-Mar-26	12-Mar-26	11-Mar-26	12-Mar-26	Not Started
CON-3860	Install Storm Manhole-2	1	1	12-Mar-26	12-Mar-26	109			12-Mar-26	12-Mar-26	17-Aug-26	17-Aug-26	Not Started
CON-3870	Install 9-LF of 12-IN DIP [Grit Champer-1 to Storm Manhole-2]	1	1	12-Mar-26	12-Mar-26	109			12-Mar-26	12-Mar-26	17-Aug-26	17-Aug-26	Not Started
CON-3880	Install 3-LF of 12-IN DIP [Grit Champer-1 to Stormwater Retention System]	1	1	12-Mar-26	12-Mar-26	107			12-Mar-26	12-Mar-26	13-Aug-26	13-Aug-26	Not Started
CON-3890	Install Bacnet Data Enclosure	6	6	12-Mar-26	19-Mar-26	151			12-Mar-26	19-Mar-26	16-Oct-26	23-Oct-26	Not Started
CON-3900	Install Sprinkler Heads - 4th Floor	2	2	12-Mar-26	13-Mar-26	74			12-Mar-26	13-Mar-26	26-Jun-26	29-Jun-26	Not Started
CON-3910	Install 10-IN DIP Roof Leader	1	1	13-Mar-26	13-Mar-26	109			13-Mar-26	13-Mar-26	18-Aug-26	18-Aug-26	Not Started
CON-3920	Install Stormwater Retention System	3	3	13-Mar-26	17-Mar-26	107			13-Mar-26	17-Mar-26	14-Aug-26	18-Aug-26	Not Started
CON-3930	Install Catch Basin 2	1	1	13-Mar-26	13-Mar-26	109			13-Mar-26	13-Mar-26	18-Aug-26	18-Aug-26	Not Started
CON-3940	Dismantle Scaffolding -South Elevation	3	3	13-Mar-26	17-Mar-26	110			13-Mar-26	17-Mar-26	19-Aug-26	21-Aug-26	Not Started
CON-3950	Install Gypsum Board Ceiling -Mockup Room	3	3	13-Mar-26	17-Mar-26	0			13-Mar-26	17-Mar-26	13-Mar-26	17-Mar-26	Not Started
CON-3960	Install Concrete Pavers	8	8	16-Mar-26	25-Mar-26	155			16-Mar-26	25-Mar-26	26-Oct-26	04-Nov-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-3970	Install Ceiling Hangers - 4th Floor	5	5	16-Mar-26	20-Mar-26	64			16-Mar-26	20-Mar-26	15-Jun-26	22-Jun-26	Not Started
CON-3980	Install 55 GAL Spill Tank with Sensor Alarm	3	3	16-Mar-26	18-Mar-26	34			16-Mar-26	18-Mar-26	01-May-26	05-May-26	Not Started
CON-3990	CON-ED to Insulate 6 Sets of 4#500MCM IN 4" RGS Conduits	3	3	13-May-26	15-May-26	111			13-May-26	15-May-26	22-Oct-26	26-Oct-26	Not Started
CON-4000	Install Electrical Panels - 1st Floor	5	5	16-Mar-26	20-Mar-26	53			16-Mar-26	20-Mar-26	29-May-26	04-Jun-26	Not Started
CON-4010	Rough-in Sprinkler Piping - Lower Roof	5	5	16-Mar-26	20-Mar-26	68			16-Mar-26	20-Mar-26	22-Jun-26	26-Jun-26	Not Started
CON-4020	Install 2 Current Transformers (C/T)	4	4	17-Mar-26	20-Mar-26	150			17-Mar-26	20-Mar-26	20-Oct-26	23-Oct-26	Not Started
CON-4030	Install 3-LF of 12-IN DIP [Stormwater Retention System to Overflow Storm Manhole-1]	1	1	18-Mar-26	18-Mar-26	107			18-Mar-26	18-Mar-26	19-Aug-26	19-Aug-26	Not Started
CON-4040	Install Overflow Storm Manhole-1	1	1	18-Mar-26	18-Mar-26	107			18-Mar-26	18-Mar-26	19-Aug-26	19-Aug-26	Not Started
CON-4050	Install Traffic Control Devices - 14th Avenue	1	1	18-Mar-26	18-Mar-26	115			18-Mar-26	18-Mar-26	31-Aug-26	31-Aug-26	Not Started
CON-4060	Install 18" Wide Filter Fabric Strip	3	3	18-Mar-26	20-Mar-26	145			18-Mar-26	20-Mar-26	14-Oct-26	16-Oct-26	Not Started
CON-4070	Install Doors & Hardware-Mockup Room	2	2	18-Mar-26	19-Mar-26	0			18-Mar-26	19-Mar-26	18-Mar-26	19-Mar-26	Not Started
CON-4080	Install 43.8 LF of 6-IN DIP [Overflow Storm Manhole-1 to Existing 30-IN x 45IN Combined Sewer]	2	2	19-Mar-26	20-Mar-26	107			19-Mar-26	20-Mar-26	20-Aug-26	21-Aug-26	Not Started
CON-4090	Mill & Remove Existing Asphalt Pavement - 14th Avenue	2	2	19-Mar-26	20-Mar-26	115			19-Mar-26	20-Mar-26	01-Sep-26	02-Sep-26	Not Started
CON-4100	Install Oil Leak Detector CAC	2	2	19-Mar-26	20-Mar-26	34			19-Mar-26	20-Mar-26	06-May-26	07-May-26	Not Started
CON-4110	CON-ED to Connect The 6 Sets of 4#500MCM to The Customer End Box	2	2	18-May-26	19-May-26	111			18-May-26	19-May-26	27-Oct-26	28-Oct-26	Not Started
CON-4120	Install Sprinkler Heads - Lower Roof	2	2	19-Mar-26	20-Mar-26	71			19-Mar-26	20-Mar-26	30-Jun-26	01-Jul-26	Not Started
CON-4130	Connect Sewer System To The Existing Sewer Line	1	1	20-Mar-26	20-Mar-26	107			20-Mar-26	20-Mar-26	21-Aug-26	21-Aug-26	Not Started
CON-4140	Install Switch Boards (SWBD-4, SWBD-5)	4	4	20-Mar-26	25-Mar-26	151			20-Mar-26	25-Mar-26	26-Oct-26	29-Oct-26	Not Started
CON-4150	Install Elevator Controls	6	6	20-Mar-26	27-Mar-26	119			20-Mar-26	27-Mar-26	09-Sep-26	16-Sep-26	Not Started
CON-4160	Paint First coat -Mockup Room	3	3	20-Mar-26	24-Mar-26	0			20-Mar-26	24-Mar-26	20-Mar-26	24-Mar-26	Not Started
CON-4170	Prepare & Compact Subgrade Layer	3	3	23-Mar-26	25-Mar-26	107			23-Mar-26	25-Mar-26	24-Aug-26	26-Aug-26	Not Started
CON-4180	Excavation For The Full Depth Asphalt Pavement Replacement - 14th Avenue	2	2	23-Mar-26	24-Mar-26	115			23-Mar-26	24-Mar-26	03-Sep-26	04-Sep-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-4190	Install Extensive Growing Media	6	6	23-Mar-26	30-Mar-26	145			23-Mar-26	30-Mar-26	19-Oct-26	26-Oct-26	Not Started
CON-4200	Install Ceiling Hangers - Lower Roof	5	5	23-Mar-26	27-Mar-26	66			23-Mar-26	27-Mar-26	25-Jun-26	01-Jul-26	Not Started
CON-4210	Install Power and Lighting Panels	3	3	23-Mar-26	25-Mar-26	150			23-Mar-26	25-Mar-26	26-Oct-26	28-Oct-26	Not Started
CON-4220	Install 6-IN Gravel - 14th Avenue	2	2	25-Mar-26	26-Mar-26	115			25-Mar-26	26-Mar-26	08-Sep-26	09-Sep-26	Not Started
CON-4230	Flooring Finishes-Mockup Room	3	3	25-Mar-26	27-Mar-26	0			25-Mar-26	27-Mar-26	25-Mar-26	27-Mar-26	Not Started
CON-4240	Install 6-IN Thick Crushed Stone	5	5	26-Mar-26	01-Apr-26	107			26-Mar-26	01-Apr-26	27-Aug-26	02-Sep-26	Not Started
CON-4250	Install Secondary Transformer Disconnect Switch (MSWB-C)	5	5	26-Mar-26	01-Apr-26	151			26-Mar-26	01-Apr-26	30-Oct-26	05-Nov-26	Not Started
CON-4260	Sawcut & Apply Tack Coat - Before Concrete Base Course - 14th Avenue	2	2	27-Mar-26	30-Mar-26	115			27-Mar-26	30-Mar-26	10-Sep-26	11-Sep-26	Not Started
CON-4270	Install 6-IN Concrete Base Course - 14th Avenue	2	2	27-Mar-26	30-Mar-26	115			27-Mar-26	30-Mar-26	10-Sep-26	11-Sep-26	Not Started
CON-4280	Install Elevator Cabinets	6	6	30-Mar-26	06-Apr-26	119			30-Mar-26	06-Apr-26	17-Sep-26	24-Sep-26	Not Started
CON-4290	Paint Second coat-Mockup Room	3	3	30-Mar-26	01-Apr-26	0			30-Mar-26	01-Apr-26	30-Mar-26	01-Apr-26	Not Started
CON-4300	Sawcut & Apply Tack Coat - Before Leveling Course - 14th Avenue	2	2	31-Mar-26	01-Apr-26	115			31-Mar-26	01-Apr-26	14-Sep-26	15-Sep-26	Not Started
CON-4310	Install Leveling Course - 14th Avenue	2	2	31-Mar-26	01-Apr-26	115			31-Mar-26	01-Apr-26	14-Sep-26	15-Sep-26	Not Started
CON-4320	Install Sedum Mat	7	7	31-Mar-26	08-Apr-26	145			31-Mar-26	08-Apr-26	27-Oct-26	04-Nov-26	Not Started
CON-4330	F/R/P Concrete Pavement	6	6	02-Apr-26	09-Apr-26	107			02-Apr-26	09-Apr-26	03-Sep-26	11-Sep-26	Not Started
CON-4340	Install 1.5-Inch Asphalt Binder Course - 14th Avenue	2	2	02-Apr-26	03-Apr-26	115			02-Apr-26	03-Apr-26	16-Sep-26	17-Sep-26	Not Started
CON-4350	Install Domestic Hot Water Heat Pump (HWHP-1 & HWHP-2)	4	4	02-Apr-26	07-Apr-26	151			02-Apr-26	07-Apr-26	06-Nov-26	12-Nov-26	Not Started
CON-4360	Install Furniture & Signs -Mockup Room	3	3	02-Apr-26	06-Apr-26	0			02-Apr-26	06-Apr-26	02-Apr-26	06-Apr-26	Not Started
CON-4370	Install 1.5-Inch Thick Asphalt Surface Course - 14th Avenue	2	2	06-Apr-26	07-Apr-26	115			06-Apr-26	07-Apr-26	18-Sep-26	21-Sep-26	Not Started
CON-4380	Elevators Testing and Commissioning	5	5	07-Apr-26	11-Apr-26	171			07-Apr-26	11-Apr-26	25-Sep-26	29-Sep-26	Not Started
CON-4390	Mockup Room Inspection & Punchlist	2	2	07-Apr-26	08-Apr-26	0			07-Apr-26	08-Apr-26	07-Apr-26	08-Apr-26	Not Started
CON-4400	Install Pavement Markings - 14th Avenue	2	2	08-Apr-26	09-Apr-26	115			08-Apr-26	09-Apr-26	22-Sep-26	23-Sep-26	Not Started
CON-4410	Install Storage Tank (ST-1)	6	6	08-Apr-26	15-Apr-26	151			08-Apr-26	15-Apr-26	13-Nov-26	20-Nov-26	Not Started
CON-4420	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - Cellar Floor	7	7	09-Apr-26	17-Apr-26	0			09-Apr-26	17-Apr-26	09-Apr-26	17-Apr-26	Not Started
CON-4430	Remove and Replace Existing Pedestrian Ramps -14th Avenue	2	2	10-Apr-26	13-Apr-26	115			10-Apr-26	13-Apr-26	24-Sep-26	25-Sep-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-4440	Install Acrylic Court Surfacing	4	4	10-Apr-26	15-Apr-26	128			10-Apr-26	15-Apr-26	14-Oct-26	19-Oct-26	Not Started
CON-4450	Install Concrete Pavers	4	4	10-Apr-26	15-Apr-26	107			10-Apr-26	15-Apr-26	14-Sep-26	17-Sep-26	Not Started
CON-4460	Elevator DOB Inspection	5	5	12-Apr-26	16-Apr-26	171			12-Apr-26	16-Apr-26	30-Sep-26	04-Oct-26	Not Started
CON-4470	Remove Traffic Control Devices - 14th Avenue	1	1	14-Apr-26	14-Apr-26	115			14-Apr-26	14-Apr-26	28-Sep-26	28-Sep-26	Not Started
CON-4480	Install Traffic Control Devices - 63rd Street	1	1	08-May-26	08-May-26	98			08-May-26	08-May-26	29-Sep-26	29-Sep-26	Not Started
CON-4490	Elevator Equipment Use Permit	5	5	17-Apr-26	21-Apr-26	171			17-Apr-26	21-Apr-26	05-Oct-26	09-Oct-26	Not Started
CON-4500	Mill & Remove Existing Asphalt Pavement - 63rd Street	2	2	11-May-26	12-May-26	98			11-May-26	12-May-26	30-Sep-26	01-Oct-26	Not Started
CON-4510	Install Tree Pit	3	3	16-Apr-26	20-Apr-26	128			16-Apr-26	20-Apr-26	20-Oct-26	22-Oct-26	Not Started
CON-4520	Install Elevated Movable Planter	3	3	21-Apr-26	23-Apr-26	128			21-Apr-26	23-Apr-26	23-Oct-26	27-Oct-26	Not Started
CON-4530	Install Flag Pole	3	3	24-Apr-26	28-Apr-26	128			24-Apr-26	28-Apr-26	28-Oct-26	30-Oct-26	Not Started
CON-4540	Install Backless Site Bench	3	3	29-Apr-26	01-May-26	128			29-Apr-26	01-May-26	02-Nov-26	04-Nov-26	Not Started
CON-4550	Install Site Gates	3	3	16-Apr-26	20-Apr-26	107			16-Apr-26	20-Apr-26	18-Sep-26	22-Sep-26	Not Started
CON-4560	Install Thermal Expansion Tank (ET-1)	6	6	16-Apr-26	23-Apr-26	151			16-Apr-26	23-Apr-26	23-Nov-26	01-Dec-26	Not Started
CON-4570	Excavation For The Full Depth Asphalt Pavement Replacement - 63rd Street	2	2	13-May-26	14-May-26	98			13-May-26	14-May-26	02-Oct-26	05-Oct-26	Not Started
CON-4580	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 2nd Floor	7	7	20-Apr-26	28-Apr-26	0			20-Apr-26	28-Apr-26	20-Apr-26	28-Apr-26	Not Started
CON-4590	Install Acoustical Ceiling Tiles- Cellar Floor	7	7	20-Apr-26	28-Apr-26	0			20-Apr-26	28-Apr-26	20-Apr-26	28-Apr-26	Not Started
CON-4600	Install Gypsum Board Ceiling- Cellar Floor	7	7	20-Apr-26	28-Apr-26	0			20-Apr-26	28-Apr-26	20-Apr-26	28-Apr-26	Not Started
CON-4610	Install Doors- Cellar Floor	3	3	20-Apr-26	22-Apr-26	11			20-Apr-26	22-Apr-26	05-May-26	07-May-26	Not Started
CON-4620	Elevator Final Sign-off	5	5	22-Apr-26	26-Apr-26	171			22-Apr-26	26-Apr-26	10-Oct-26	14-Oct-26	Not Started
CON-4630	Install 6-IN Gravel - 63rd Street	2	2	15-May-26	18-May-26	98			15-May-26	18-May-26	06-Oct-26	07-Oct-26	Not Started
CON-4640	Install Doors- 2nd Floor	3	3	23-Apr-26	27-Apr-26	15			23-Apr-26	27-Apr-26	14-May-26	18-May-26	Not Started
CON-4650	Sawcut & Apply Tack Coat - Before Concrete Base Course - 63rd Street	2	2	19-May-26	20-May-26	98			19-May-26	20-May-26	08-Oct-26	09-Oct-26	Not Started
CON-4660	Dismantle Hoist	5	5	27-Apr-26	01-May-26	118			27-Apr-26	01-May-26	15-Oct-26	21-Oct-26	Not Started
CON-4670	Install 6-IN Concrete Base Course - 63rd Street	2	2	21-May-26	22-May-26	98			21-May-26	22-May-26	13-Oct-26	14-Oct-26	Not Started
CON-4680	Install Doors- 3rd Floor	3	3	28-Apr-26	30-Apr-26	82			28-Apr-26	30-Apr-26	25-Aug-26	27-Aug-26	Not Started
CON-4690	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 3rd Floor	7	7	29-Apr-26	07-May-26	0			29-Apr-26	07-May-26	29-Apr-26	07-May-26	Not Started
CON-4700	Install Acoustical Ceiling Tiles -	7	7	29-Apr-26	07-May-26	23			29-Apr-26	07-May-26	02-Jun-26	10-Jun-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
	2nd Floor												
CON-4710	Install Gypsum Board Ceiling - 2nd Floor	7	7	29-Apr-26	07-May-26	23			29-Apr-26	07-May-26	02-Jun-26	10-Jun-26	Not Started
CON-4720	Install Electric Wall Convectors - 2nd Floor	3	3	29-Apr-26	01-May-26	53			29-Apr-26	01-May-26	16-Jul-26	20-Jul-26	Not Started
CON-4730	Install First Coat Painting - Cellar Floor	7	7	29-Apr-26	07-May-26	0			29-Apr-26	07-May-26	29-Apr-26	07-May-26	Not Started
CON-4740	Sawcut & Apply Tack Coat - Before Leveling Course - 63rd Street	2	2	26-May-26	27-May-26	98			26-May-26	27-May-26	15-Oct-26	16-Oct-26	Not Started
CON-4750	Install Doors- 4th Floor	3	3	01-May-26	05-May-26	86			01-May-26	05-May-26	03-Sep-26	08-Sep-26	Not Started
CON-4760	Install Leveling Course - 63rd Street	2	2	28-May-26	29-May-26	98			28-May-26	29-May-26	19-Oct-26	20-Oct-26	Not Started
CON-4770	Install Electric Wall Convectors - 3rd Floor	3	3	04-May-26	06-May-26	53			04-May-26	06-May-26	21-Jul-26	23-Jul-26	Not Started
CON-4780	Demolish Hoist Pad	5	5	04-May-26	08-May-26	118			04-May-26	08-May-26	22-Oct-26	28-Oct-26	Not Started
CON-4790	Install 1.5-Inch Asphalt Binder Course - 63rd Street	2	2	01-Jun-26	02-Jun-26	98			01-Jun-26	02-Jun-26	21-Oct-26	22-Oct-26	Not Started
CON-4800	Install Doors- Lower Roof	3	3	06-May-26	08-May-26	90			06-May-26	08-May-26	15-Sep-26	17-Sep-26	Not Started
CON-4810	Install Electric Wall Convectors - 4th Floor	3	3	07-May-26	11-May-26	53			07-May-26	11-May-26	24-Jul-26	28-Jul-26	Not Started
CON-4820	Install 1.5-Inch Thick Asphalt Surface Course - 63rd Street	2	2	03-Jun-26	04-Jun-26	98			03-Jun-26	04-Jun-26	23-Oct-26	26-Oct-26	Not Started
CON-4830	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 4th Floor	7	7	08-May-26	18-May-26	0			08-May-26	18-May-26	08-May-26	18-May-26	Not Started
CON-4840	Install Gypsum Board Ceiling - 3rd Floor	7	7	08-May-26	18-May-26	23			08-May-26	18-May-26	11-Jun-26	22-Jun-26	Not Started
CON-4850	Install Acoustical Ceiling Tiles - 3rd Floor	7	7	08-May-26	18-May-26	23			08-May-26	18-May-26	11-Jun-26	22-Jun-26	Not Started
CON-4860	Install Flooring - Cellar Floor	7	7	08-May-26	18-May-26	0			08-May-26	18-May-26	08-May-26	18-May-26	Not Started
CON-4870	Install Lighting Fixtures - Cellar Floor	7	7	08-May-26	18-May-26	23			08-May-26	18-May-26	11-Jun-26	22-Jun-26	Not Started
CON-4880	Install First Coat Painting - 2nd Floor	7	7	08-May-26	18-May-26	23			08-May-26	18-May-26	11-Jun-26	22-Jun-26	Not Started
CON-4890	Install Milling Work - Cellar Floor	7	7	08-May-26	18-May-26	70			08-May-26	18-May-26	19-Aug-26	27-Aug-26	Not Started
CON-4900	Hoist In-Fill	5	5	11-May-26	15-May-26	118			11-May-26	15-May-26	29-Oct-26	04-Nov-26	Not Started
CON-4910	Install Doors- 1st Floor	3	3	29-Jun-26	01-Jul-26	61			29-Jun-26	01-Jul-26	24-Sep-26	28-Sep-26	Not Started
CON-4920	Install Pavement Markings - 63rd Street	2	2	05-Jun-26	08-Jun-26	98			05-Jun-26	08-Jun-26	27-Oct-26	28-Oct-26	Not Started
CON-4930	Install Electric Wall Convectors - 1st Floor	3	3	12-May-26	14-May-26	53			12-May-26	14-May-26	29-Jul-26	31-Jul-26	Not Started
CON-4940	Remove and Replace Existing Pedestrian Ramps -63rd Street	2	2	09-Jun-26	10-Jun-26	98			09-Jun-26	10-Jun-26	29-Oct-26	30-Oct-26	Not Started
CON-4950	Remove Traffic Control Devices - 63rd Street	1	1	11-Jun-26	11-Jun-26	98			11-Jun-26	11-Jun-26	02-Nov-26	02-Nov-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-4960	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - Lower Roof	7	7	19-May-26	28-May-26	0			19-May-26	28-May-26	19-May-26	28-May-26	Not Started
CON-4970	Install Acoustical Ceiling Tiles - 4th Floor	7	7	19-May-26	28-May-26	23			19-May-26	28-May-26	23-Jun-26	01-Jul-26	Not Started
CON-4980	Install Gypsum Board Ceiling- 4th Floor	7	7	19-May-26	28-May-26	23			19-May-26	28-May-26	23-Jun-26	01-Jul-26	Not Started
CON-4990	Install TECTUM WOOD Fiber Composition Ceiling Tiles- 4th Floor	7	7	19-May-26	28-May-26	23			19-May-26	28-May-26	23-Jun-26	01-Jul-26	Not Started
CON-5000	Install Flooring - 2nd Floor	7	7	19-May-26	28-May-26	0			19-May-26	28-May-26	19-May-26	28-May-26	Not Started
CON-5010	Install Electric Cabinet Heaters - Cellar Floor	3	3	19-May-26	21-May-26	87			19-May-26	21-May-26	23-Sep-26	25-Sep-26	Not Started
CON-5020	Install Lighting Fixtures - 2nd Floor	7	7	19-May-26	28-May-26	23			19-May-26	28-May-26	23-Jun-26	01-Jul-26	Not Started
CON-5030	Install Data & Video Intercome Systems -Cellar Floor	7	7	19-May-26	28-May-26	23			19-May-26	28-May-26	23-Jun-26	01-Jul-26	Not Started
CON-5040	Install Plumbing Fixtures - Cellar Floor	7	7	19-May-26	28-May-26	73			19-May-26	28-May-26	02-Sep-26	11-Sep-26	Not Started
CON-5050	Install First Coat Painting - 3rd Floor	7	7	19-May-26	28-May-26	23			19-May-26	28-May-26	23-Jun-26	01-Jul-26	Not Started
CON-5060	Install Milling Work - 2nd Floor	7	7	19-May-26	28-May-26	70			19-May-26	28-May-26	28-Aug-26	08-Sep-26	Not Started
CON-5070	Install Furniture - Cellar Floor	7	7	19-May-26	28-May-26	63			19-May-26	28-May-26	19-Aug-26	27-Aug-26	Not Started
CON-5080	Install Electric Cabinet Heaters - 2nd Floor	3	3	22-May-26	27-May-26	87			22-May-26	27-May-26	28-Sep-26	30-Sep-26	Not Started
CON-5090	Install Electric Cabinet Heaters - 3rd Floor	3	3	28-May-26	01-Jun-26	87			28-May-26	01-Jun-26	01-Oct-26	05-Oct-26	Not Started
CON-5100	Install Gypsum Board Ceiling - Lower Roof	7	7	29-May-26	08-Jun-26	23			29-May-26	08-Jun-26	02-Jul-26	13-Jul-26	Not Started
CON-5110	Install Flooring - 3rd Floor	7	7	29-May-26	08-Jun-26	63			29-May-26	08-Jun-26	28-Aug-26	08-Sep-26	Not Started
CON-5120	Rough-in Duct Work -VAV Devices & Diffusers - 1st Floor	5	5	29-May-26	04-Jun-26	0			29-May-26	04-Jun-26	29-May-26	04-Jun-26	Not Started
CON-5130	Rough-in Refrigerant Piping - 1st Floor	5	5	29-May-26	04-Jun-26	82			29-May-26	04-Jun-26	25-Sep-26	01-Oct-26	Not Started
CON-5140	Install Lighting Fixtures - 3rd Floor	7	7	29-May-26	08-Jun-26	23			29-May-26	08-Jun-26	02-Jul-26	13-Jul-26	Not Started
CON-5150	Install Voice Cabinet	7	7	29-May-26	08-Jun-26	0			29-May-26	08-Jun-26	29-May-26	08-Jun-26	Not Started
CON-5160	Install Data & Video Intercome Systems - 2nd Floor	7	7	29-May-26	08-Jun-26	23			29-May-26	08-Jun-26	02-Jul-26	13-Jul-26	Not Started
CON-5170	Install Voice Systems Components -Cellar Floor	7	7	29-May-26	08-Jun-26	23			29-May-26	08-Jun-26	02-Jul-26	13-Jul-26	Not Started
CON-5180	Install Plumbing Fixtures - 2nd Floor	7	7	29-May-26	08-Jun-26	73			29-May-26	08-Jun-26	14-Sep-26	22-Sep-26	Not Started
CON-5190	Install First Coat Painting - 4th Floor	7	7	29-May-26	08-Jun-26	23			29-May-26	08-Jun-26	02-Jul-26	13-Jul-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-5200	Install Final Coat Painting - Cellar Floor	7	7	29-May-26	08-Jun-26	63			29-May-26	08-Jun-26	28-Aug-26	08-Sep-26	Not Started
CON-5210	Install Milling Work - 3rd Floor	7	7	29-May-26	08-Jun-26	70			29-May-26	08-Jun-26	09-Sep-26	17-Sep-26	Not Started
CON-5220	Install Furniture - 2nd Floor	7	7	29-May-26	08-Jun-26	63			29-May-26	08-Jun-26	28-Aug-26	08-Sep-26	Not Started
CON-5230	Install Electric Cabinet Heaters - 4th Floor	3	3	02-Jun-26	04-Jun-26	87			02-Jun-26	04-Jun-26	06-Oct-26	08-Oct-26	Not Started
CON-5240	Layout - 1st Floor	2	2	05-Jun-26	08-Jun-26	10			05-Jun-26	08-Jun-26	22-Jun-26	23-Jun-26	Not Started
CON-5250	Install Heat Pump Unit (HP-108 B) - 1st Floor	4	4	05-Jun-26	10-Jun-26	82			05-Jun-26	10-Jun-26	02-Oct-26	07-Oct-26	Not Started
CON-5260	Install Electrical Heat Air Curtain - 1st Floor	2	2	05-Jun-26	08-Jun-26	84			05-Jun-26	08-Jun-26	06-Oct-26	07-Oct-26	Not Started
CON-5270	Install Electric Cabinet Heaters - Lower Roof	3	3	05-Jun-26	09-Jun-26	87			05-Jun-26	09-Jun-26	09-Oct-26	14-Oct-26	Not Started
CON-5280	Install Electric Unit Heater - 1st Floor	2	2	05-Jun-26	08-Jun-26	84			05-Jun-26	08-Jun-26	06-Oct-26	07-Oct-26	Not Started
CON-5290	Rough-in Power Conduits & Wires - 1st Floor	5	5	05-Jun-26	11-Jun-26	0			05-Jun-26	11-Jun-26	05-Jun-26	11-Jun-26	Not Started
CON-5300	Install Top & Bottom Tracks - 1st Floor	2	2	09-Jun-26	10-Jun-26	10			09-Jun-26	10-Jun-26	24-Jun-26	25-Jun-26	Not Started
CON-5310	Install CMU - 1st Floor	3	3	09-Jun-26	11-Jun-26	27			09-Jun-26	11-Jun-26	20-Jul-26	22-Jul-26	Not Started
CON-5320	Install Flooring - 4th Floor	7	7	09-Jun-26	17-Jun-26	63			09-Jun-26	17-Jun-26	09-Sep-26	17-Sep-26	Not Started
CON-5330	Install Lighting Fixtures - 4th Floor	7	7	09-Jun-26	17-Jun-26	23			09-Jun-26	17-Jun-26	14-Jul-26	22-Jul-26	Not Started
CON-5340	Install Data Equipment Rack	7	7	09-Jun-26	17-Jun-26	0			09-Jun-26	17-Jun-26	09-Jun-26	17-Jun-26	Not Started
CON-5350	Install Data & Video Intercome Systems - 3rd Floor	7	7	09-Jun-26	17-Jun-26	23			09-Jun-26	17-Jun-26	14-Jul-26	22-Jul-26	Not Started
CON-5360	Install Voice Systems Components - 2nd Floor	7	7	09-Jun-26	17-Jun-26	23			09-Jun-26	17-Jun-26	14-Jul-26	22-Jul-26	Not Started
CON-5370	Install Public Address and Clock Systems Components -Cellar Floor	7	7	09-Jun-26	17-Jun-26	23			09-Jun-26	17-Jun-26	14-Jul-26	22-Jul-26	Not Started
CON-5380	Install Plumbing Fixtures - 3rd Floor	7	7	09-Jun-26	17-Jun-26	73			09-Jun-26	17-Jun-26	23-Sep-26	01-Oct-26	Not Started
CON-5390	Install First Coat Painting - Lower Roof	7	7	09-Jun-26	17-Jun-26	23			09-Jun-26	17-Jun-26	14-Jul-26	22-Jul-26	Not Started
CON-5400	Install Final Coat Painting - 2nd Floor	7	7	09-Jun-26	17-Jun-26	63			09-Jun-26	17-Jun-26	09-Sep-26	17-Sep-26	Not Started
CON-5410	Install Milling Work - 4th Floor	7	7	09-Jun-26	17-Jun-26	70			09-Jun-26	17-Jun-26	18-Sep-26	28-Sep-26	Not Started
CON-5420	Install Furniture - 3rd Floor	7	7	09-Jun-26	17-Jun-26	63			09-Jun-26	17-Jun-26	09-Sep-26	17-Sep-26	Not Started
CON-5430	Install Signage- Cellar Floor	3	3	09-Jun-26	11-Jun-26	83			09-Jun-26	11-Jun-26	07-Oct-26	09-Oct-26	Not Started
CON-5440	Install Electric Cabinet Heaters - Upper Roof	3	3	10-Jun-26	12-Jun-26	87			10-Jun-26	12-Jun-26	15-Oct-26	19-Oct-26	Not Started
CON-5450	Install Steel Studs - 1st Floor	4	4	11-Jun-26	16-Jun-26	10			11-Jun-26	16-Jun-26	26-Jun-26	01-Jul-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-5460	Install Heat Pump Unit (HP-R02) - Roof	4	4	11-Jun-26	16-Jun-26	82			11-Jun-26	16-Jun-26	08-Oct-26	14-Oct-26	Not Started
CON-5470	Rough-in Low Voltage Conduits & Wires - 1st Floor	5	5	12-Jun-26	18-Jun-26	0			12-Jun-26	18-Jun-26	12-Jun-26	18-Jun-26	Not Started
CON-5480	Install Signage - 2nd Floor	3	3	12-Jun-26	16-Jun-26	83			12-Jun-26	16-Jun-26	13-Oct-26	15-Oct-26	Not Started
CON-5490	Install Electric Cabinet Heaters - 1st Roof	3	3	15-Jun-26	17-Jun-26	87			15-Jun-26	17-Jun-26	20-Oct-26	22-Oct-26	Not Started
CON-5500	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 1st Floor	7	7	17-Jun-26	26-Jun-26	10			17-Jun-26	26-Jun-26	02-Jul-26	13-Jul-26	Not Started
CON-5510	Install Signage - 3rd Floor	3	3	17-Jun-26	22-Jun-26	83			17-Jun-26	22-Jun-26	16-Oct-26	20-Oct-26	Not Started
CON-5520	Install Flooring - Lower Roof	7	7	18-Jun-26	29-Jun-26	63			18-Jun-26	29-Jun-26	18-Sep-26	28-Sep-26	Not Started
CON-5530	Install Lighting Fixtures - Lower Roof	7	7	18-Jun-26	29-Jun-26	23			18-Jun-26	29-Jun-26	23-Jul-26	31-Jul-26	Not Started
CON-5540	Install Data Cabinet Patch Panel Rack	7	7	18-Jun-26	29-Jun-26	0			18-Jun-26	29-Jun-26	18-Jun-26	29-Jun-26	Not Started
CON-5550	Install Data & Video Intercome Systems - 4th Floor	7	7	18-Jun-26	29-Jun-26	23			18-Jun-26	29-Jun-26	23-Jul-26	31-Jul-26	Not Started
CON-5560	Install Voice Systems Components - 3rd Floor	7	7	18-Jun-26	29-Jun-26	23			18-Jun-26	29-Jun-26	23-Jul-26	31-Jul-26	Not Started
CON-5570	Install Public Address and Clock Systems Components - 2nd Floor	7	7	18-Jun-26	29-Jun-26	23			18-Jun-26	29-Jun-26	23-Jul-26	31-Jul-26	Not Started
CON-5580	Install Auxiliary Signal System Components - Cellar Floor	7	7	18-Jun-26	29-Jun-26	23			18-Jun-26	29-Jun-26	23-Jul-26	31-Jul-26	Not Started
CON-5590	Install Plumbing Fixtures - 4th Floor	7	7	18-Jun-26	29-Jun-26	73			18-Jun-26	29-Jun-26	02-Oct-26	13-Oct-26	Not Started
CON-5600	Install Final Coat Painting - 3rd Floor	7	7	18-Jun-26	29-Jun-26	63			18-Jun-26	29-Jun-26	18-Sep-26	28-Sep-26	Not Started
CON-5610	Install Milling Work - Lower Roof	7	7	18-Jun-26	29-Jun-26	70			18-Jun-26	29-Jun-26	29-Sep-26	07-Oct-26	Not Started
CON-5620	Install Furniture - 4th Floor	7	7	18-Jun-26	29-Jun-26	63			18-Jun-26	29-Jun-26	18-Sep-26	28-Sep-26	Not Started
CON-5630	Install Gym Flooring	10	10	18-Jun-26	02-Jul-26	69			18-Jun-26	02-Jul-26	28-Sep-26	09-Oct-26	Not Started
CON-5640	Rough-in Plumbing Pipes - 1st Floor	5	5	22-Jun-26	26-Jun-26	0			22-Jun-26	26-Jun-26	22-Jun-26	26-Jun-26	Not Started
CON-5650	Install Signage - 4th Floor	3	3	23-Jun-26	25-Jun-26	83			23-Jun-26	25-Jun-26	21-Oct-26	23-Oct-26	Not Started
CON-5660	Install Signage - Lower Roof	3	3	26-Jun-26	30-Jun-26	83			26-Jun-26	30-Jun-26	26-Oct-26	28-Oct-26	Not Started
CON-5670	Install Hot Water Circulator Pump (CP-1) / (CP-2)	4	4	29-Jun-26	02-Jul-26	75			29-Jun-26	02-Jul-26	15-Oct-26	20-Oct-26	Not Started
CON-5680	Rough-in Sprinkler Piping - 1st Floor	5	5	29-Jun-26	06-Jul-26	0			29-Jun-26	06-Jul-26	29-Jun-26	06-Jul-26	Not Started
CON-5690	Install Vertical Wire Manager	7	7	30-Jun-26	09-Jul-26	0			30-Jun-26	09-Jul-26	30-Jun-26	09-Jul-26	Not Started
CON-5700	Install Data & Video Intercome Systems - Lower Roof	7	7	30-Jun-26	09-Jul-26	23			30-Jun-26	09-Jul-26	03-Aug-26	11-Aug-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-5710	Install Voice Systems Components - 4th Floor	7	7	30-Jun-26	09-Jul-26	23			30-Jun-26	09-Jul-26	03-Aug-26	11-Aug-26	Not Started
CON-5720	Install Public Address and Clock Systems Components - 3rd Floor	7	7	30-Jun-26	09-Jul-26	23			30-Jun-26	09-Jul-26	03-Aug-26	11-Aug-26	Not Started
CON-5730	Install Auxiliary Signal System Components - 2nd Floor	7	7	30-Jun-26	09-Jul-26	23			30-Jun-26	09-Jul-26	03-Aug-26	11-Aug-26	Not Started
CON-5740	Install Intrusion Alarm System Components- Cellar Floor	7	7	30-Jun-26	09-Jul-26	23			30-Jun-26	09-Jul-26	03-Aug-26	11-Aug-26	Not Started
CON-5750	Install Plumbing Fixtures - Lower Roof	7	7	30-Jun-26	09-Jul-26	73			30-Jun-26	09-Jul-26	14-Oct-26	22-Oct-26	Not Started
CON-5760	Install Final Coat Painting - 4th Floor	7	7	30-Jun-26	09-Jul-26	63			30-Jun-26	09-Jul-26	29-Sep-26	07-Oct-26	Not Started
CON-5770	Install Furniture - Lower Roof	7	7	30-Jun-26	09-Jul-26	63			30-Jun-26	09-Jul-26	29-Sep-26	07-Oct-26	Not Started
CON-5780	Install Sprinkler Heads - 1st Floor	2	2	02-Jul-26	06-Jul-26	0			02-Jul-26	06-Jul-26	02-Jul-26	06-Jul-26	Not Started
CON-5790	Install Grease Interceptor (GI-1) / (GI-2)	4	4	06-Jul-26	09-Jul-26	75			06-Jul-26	09-Jul-26	21-Oct-26	26-Oct-26	Not Started
CON-5800	Install Gym Equipment	15	15	06-Jul-26	24-Jul-26	69			06-Jul-26	24-Jul-26	13-Oct-26	02-Nov-26	Not Started
CON-5810	Install Ceiling Hangers - 1st Floor	5	5	07-Jul-26	13-Jul-26	0			07-Jul-26	13-Jul-26	07-Jul-26	13-Jul-26	Not Started
CON-5820	Install Bacnet Data Enclosure	7	7	10-Jul-26	20-Jul-26	0			10-Jul-26	20-Jul-26	10-Jul-26	20-Jul-26	Not Started
CON-5830	Install Kitchen Equipment	7	7	10-Jul-26	20-Jul-26	75			10-Jul-26	20-Jul-26	27-Oct-26	04-Nov-26	Not Started
CON-5840	Install Voice Systems Components - Lower Roof	7	7	10-Jul-26	20-Jul-26	23			10-Jul-26	20-Jul-26	12-Aug-26	20-Aug-26	Not Started
CON-5850	Install Public Address and Clock Systems Components - 4th Floor	7	7	10-Jul-26	20-Jul-26	23			10-Jul-26	20-Jul-26	12-Aug-26	20-Aug-26	Not Started
CON-5860	Install Auxiliary Signal System Components - 3rd Floor	7	7	10-Jul-26	20-Jul-26	23			10-Jul-26	20-Jul-26	12-Aug-26	20-Aug-26	Not Started
CON-5870	Install Intrusion Alarm System Components - 2nd Floor	7	7	10-Jul-26	20-Jul-26	23			10-Jul-26	20-Jul-26	12-Aug-26	20-Aug-26	Not Started
CON-5880	Install IPDVS System Components - Cellar Floor	7	7	10-Jul-26	20-Jul-26	23			10-Jul-26	20-Jul-26	12-Aug-26	20-Aug-26	Not Started
CON-5890	Install Plumbing Fixtures - 1st Floor	7	7	10-Jul-26	20-Jul-26	73			10-Jul-26	20-Jul-26	23-Oct-26	02-Nov-26	Not Started
CON-5900	Install Final Coat Painting - Lower Roof	7	7	10-Jul-26	20-Jul-26	63			10-Jul-26	20-Jul-26	08-Oct-26	19-Oct-26	Not Started
CON-5910	Install MDF Telephone System Backboard	7	7	10-Jul-26	20-Jul-26	21			10-Jul-26	20-Jul-26	10-Aug-26	18-Aug-26	Not Started
CON-5920	Install Gypsum Board Ceiling - 1st Floor	7	7	14-Jul-26	22-Jul-26	0			14-Jul-26	22-Jul-26	14-Jul-26	22-Jul-26	Not Started
CON-5930	Install Acoustical Ceiling Tiles - 1st Floor	7	7	14-Jul-26	22-Jul-26	0			14-Jul-26	22-Jul-26	14-Jul-26	22-Jul-26	Not Started
CON-5940	Install Wood Slat Ceiling - 1st Floor	7	7	14-Jul-26	22-Jul-26	0			14-Jul-26	22-Jul-26	14-Jul-26	22-Jul-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-5950	MCP-Wood Slat Ceiling Panel - 1st Floor	7	7	14-Jul-26	22-Jul-26	0			14-Jul-26	22-Jul-26	14-Jul-26	22-Jul-26	Not Started
CON-5960	Install PA Rack	7	7	21-Jul-26	29-Jul-26	0			21-Jul-26	29-Jul-26	21-Jul-26	29-Jul-26	Not Started
CON-5970	Install Public Address and Clock Systems Components - Lower Roof	7	7	21-Jul-26	29-Jul-26	23			21-Jul-26	29-Jul-26	21-Aug-26	31-Aug-26	Not Started
CON-5980	Install Auxiliary Signal System Components - 4th Floor	7	7	21-Jul-26	29-Jul-26	23			21-Jul-26	29-Jul-26	21-Aug-26	31-Aug-26	Not Started
CON-5990	Install Intrusion Alarm System Components - 3rd Floor	7	7	21-Jul-26	29-Jul-26	23			21-Jul-26	29-Jul-26	21-Aug-26	31-Aug-26	Not Started
CON-6000	Install IPDVS System Components - 2nd Floor	7	7	21-Jul-26	29-Jul-26	23			21-Jul-26	29-Jul-26	21-Aug-26	31-Aug-26	Not Started
CON-6010	Install Fire Alarm Devices- Cellar Floor	7	7	21-Jul-26	29-Jul-26	31			21-Jul-26	29-Jul-26	02-Sep-26	11-Sep-26	Not Started
CON-6020	Install Telecom Panel	7	7	21-Jul-26	29-Jul-26	21			21-Jul-26	29-Jul-26	19-Aug-26	27-Aug-26	Not Started
CON-6030	Install First Coat Painting - 1st Floor	7	7	23-Jul-26	31-Jul-26	0			23-Jul-26	31-Jul-26	23-Jul-26	31-Jul-26	Not Started
CON-6040	Install Voice Rack	7	7	30-Jul-26	07-Aug-26	0			30-Jul-26	07-Aug-26	30-Jul-26	07-Aug-26	Not Started
CON-6050	Install Auxiliary Signal System Components - Lower Roof	7	7	30-Jul-26	07-Aug-26	23			30-Jul-26	07-Aug-26	01-Sep-26	10-Sep-26	Not Started
CON-6060	Install Intrusion Alarm System Components - 4th Floor	7	7	30-Jul-26	07-Aug-26	23			30-Jul-26	07-Aug-26	01-Sep-26	10-Sep-26	Not Started
CON-6070	Install IPDVS System Components - 3rd Floor	7	7	30-Jul-26	07-Aug-26	23			30-Jul-26	07-Aug-26	01-Sep-26	10-Sep-26	Not Started
CON-6080	Install Fire Alarm Devices - 2nd Floor	7	7	30-Jul-26	07-Aug-26	31			30-Jul-26	07-Aug-26	14-Sep-26	22-Sep-26	Not Started
CON-6090	Install Flooring - 1st Floor	7	7	03-Aug-26	11-Aug-26	40			03-Aug-26	11-Aug-26	29-Sep-26	07-Oct-26	Not Started
CON-6100	Install Lighting Fixtures - 1st Floor	7	7	03-Aug-26	11-Aug-26	0			03-Aug-26	11-Aug-26	03-Aug-26	11-Aug-26	Not Started
CON-6110	Install Milling Work - 1st Floor	7	7	03-Aug-26	11-Aug-26	47			03-Aug-26	11-Aug-26	08-Oct-26	19-Oct-26	Not Started
CON-6120	Install Data Rack	7	7	10-Aug-26	18-Aug-26	0			10-Aug-26	18-Aug-26	10-Aug-26	18-Aug-26	Not Started
CON-6130	Install Intrusion Alarm System Components - Lower Roof	7	7	10-Aug-26	18-Aug-26	23			10-Aug-26	18-Aug-26	11-Sep-26	21-Sep-26	Not Started
CON-6140	Install IPDVS System Components - 4th Floor	7	7	10-Aug-26	18-Aug-26	23			10-Aug-26	18-Aug-26	11-Sep-26	21-Sep-26	Not Started
CON-6150	Install Fire Alarm Devices - 3rd Floor	7	7	10-Aug-26	18-Aug-26	31			10-Aug-26	18-Aug-26	23-Sep-26	01-Oct-26	Not Started
CON-6160	Install Data & Video Intercome Systems - 1st Floor	7	7	12-Aug-26	20-Aug-26	0			12-Aug-26	20-Aug-26	12-Aug-26	20-Aug-26	Not Started
CON-6170	Install Furniture - 1st Floor	7	7	12-Aug-26	20-Aug-26	40			12-Aug-26	20-Aug-26	08-Oct-26	19-Oct-26	Not Started
CON-6180	Electrical Testing and Commissioning	5	5	12-Aug-26	16-Aug-26	78			12-Aug-26	16-Aug-26	29-Oct-26	02-Nov-26	Not Started
CON-6190	Install Voice Cabinet	7	7	19-Aug-26	27-Aug-26	0			19-Aug-26	27-Aug-26	19-Aug-26	27-Aug-26	Not Started
CON-6200	Install IPDVS System Components - Lower Roof	7	7	19-Aug-26	27-Aug-26	23			19-Aug-26	27-Aug-26	22-Sep-26	30-Sep-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-6210	Install Fire Alarm Devices - 4th Floor	7	7	19-Aug-26	27-Aug-26	31			19-Aug-26	27-Aug-26	02-Oct-26	13-Oct-26	Not Started
CON-6220	Install Voice Systems Components - 1st Floor	7	7	21-Aug-26	31-Aug-26	0			21-Aug-26	31-Aug-26	21-Aug-26	31-Aug-26	Not Started
CON-6230	Install Final Coat Painting - 1st Floor	7	7	21-Aug-26	31-Aug-26	40			21-Aug-26	31-Aug-26	20-Oct-26	28-Oct-26	Not Started
CON-6240	Install Fire Alarm Devices - Lower Roof	7	7	28-Aug-26	08-Sep-26	31			28-Aug-26	08-Sep-26	14-Oct-26	22-Oct-26	Not Started
CON-6250	MDF & IDF Rooms Testing and Inspection (Before 3-Sep-26)	7	7	28-Aug-26	03-Sep-26	0			28-Aug-26	03-Sep-26	28-Aug-26	03-Sep-26	Not Started
CON-6260	Install Public Address and Clock Systems Components - 1st Floor	7	7	01-Sep-26	10-Sep-26	0			01-Sep-26	10-Sep-26	01-Sep-26	10-Sep-26	Not Started
CON-6270	Install Signage - 1st Floor	3	3	01-Sep-26	03-Sep-26	40			01-Sep-26	03-Sep-26	29-Oct-26	02-Nov-26	Not Started
CON-6280	Install Auxiliary Signal System Components - 1st Floor	7	7	11-Sep-26	21-Sep-26	0			11-Sep-26	21-Sep-26	11-Sep-26	21-Sep-26	Not Started
CON-6290	Install Intrusion Alarm System Components - 1st Floor	7	7	22-Sep-26	30-Sep-26	0			22-Sep-26	30-Sep-26	22-Sep-26	30-Sep-26	Not Started
CON-6300	Install IPDVS System Components - 1st Floor	12	12	01-Oct-26	19-Oct-26	0			01-Oct-26	19-Oct-26	01-Oct-26	19-Oct-26	Not Started
CON-6310	Install Fire Alarm Devices - 1st Floor	7	7	20-Oct-26	28-Oct-26	3			20-Oct-26	28-Oct-26	23-Oct-26	02-Nov-26	Not Started
CON-6320	IPDV System Testing and Inspection (Before 2-Nov-26)	10	10	20-Oct-26	02-Nov-26	0			20-Oct-26	02-Nov-26	20-Oct-26	02-Nov-26	Not Started
CON-6330	Install Magnetic Induction Loop W	5	5	21-Apr-26	27-Apr-26	107			21-Apr-26	27-Apr-26	23-Sep-26	29-Sep-26	Not Started
CON-6340	Install Cafeteria Flooring	10	10	28-Apr-26	11-May-26	107			28-Apr-26	11-May-26	30-Sep-26	14-Oct-26	Not Started
CON-6350	Install Cafeteria Assembly	15	15	12-May-26	02-Jun-26	107			12-May-26	02-Jun-26	15-Oct-26	04-Nov-26	Not Started
COR-1000	Coordination With CON-ED For Temporary Electrical Power	10	10	01-Apr-25	14-Apr-25	2			01-Apr-25	14-Apr-25	03-Apr-25	16-Apr-25	Not Started
COR-1010	Scheduling With CON-ED For Temporary Electrical Power	7	7	15-Apr-25	23-Apr-25	2			15-Apr-25	23-Apr-25	17-Apr-25	25-Apr-25	Not Started
COR-1020	Procurement From CON-ED For Temporary Electrical Power	20	20	24-Apr-25	13-May-25	2			24-Apr-25	13-May-25	26-Apr-25	15-May-25	Not Started
COR-1030	CON-ED Work For Temporary Electrical Power	10	10	14-May-25	28-May-25	2			14-May-25	28-May-25	16-May-25	30-May-25	Not Started
COR-1040	Available Temporary Electrical Power For Testing MEP Equipment	0	0		28-May-25	2				28-May-25		30-May-25	Not Started
COR-1050	Coordination With CON-ED For Trasnformers Work	10	10	21-Nov-25	05-Dec-25	96			21-Nov-25	05-Dec-25	13-Apr-26	24-Apr-26	Not Started
COR-1060	CON-ED to Provide (1) 27KV Feeder To Transformer Vault	30	30	06-Dec-25	04-Jan-26	142			06-Dec-25	04-Jan-26	27-Apr-26	26-May-26	Not Started
COR-1070	CON-ED to Furnish & Deliver (1) New "V11-6 Transformer Vault	120	120	05-Jan-26	04-May-26	142			05-Jan-26	04-May-26	27-May-26	23-Sep-26	Not Started
MIL-1000	NTP	0	0	02-Dec-24		0			02-Dec-24		02-Dec-24		Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
MIL-1010	Project Duration (From NTP till TCO) = 730 CDs	730	730	02-Dec-24	01-Dec-26	0			02-Dec-24	01-Dec-26	02-Dec-24	01-Dec-26	Not Started
MIL-1020	Building Tight	0	0		05-Mar-26	0				05-Mar-26		05-Mar-26	Not Started
MIL-1030	TCO	0	0		01-Dec-26*	0				01-Dec-26		01-Dec-26	Not Started
MIL-1040	Substantial Completion	0	0		01-Mar-27*	0				01-Mar-27		01-Mar-27	Not Started
MIL-1050	Final Completion	0	0		29-Jun-27*	0				29-Jun-27		29-Jun-27	Not Started
MIL-1060	IDF and MDF Rooms Ready	0	0		03-Sep-26*	0				03-Sep-26		03-Sep-26	Not Started
MIL-1070	IPDVS System Installed	0	0		02-Nov-26*	0				02-Nov-26		02-Nov-26	Not Started
PER-1000	Obtain Construction Fences Permit	3	3	01-Apr-25	03-Apr-25	40			01-Apr-25	03-Apr-25	28-May-25	30-May-25	Not Started
PER-1010	Obtain CCD1	3	3	01-Apr-25	03-Apr-25	40			01-Apr-25	03-Apr-25	28-May-25	30-May-25	Not Started
PER-1020	Obtain Sidewalk Shed Permits	3	3	01-Apr-25	03-Apr-25	40			01-Apr-25	03-Apr-25	28-May-25	30-May-25	Not Started
PER-1030	Meeting With SCA to Review The Permit Requirements	14	14	01-Apr-25	18-Apr-25	22			01-Apr-25	18-Apr-25	01-May-25	20-May-25	Not Started
PER-1040	Prepare & Submit Permit Waiver Requests to SCA Chief Project Officer	5	5	01-Apr-25	07-Apr-25	38			01-Apr-25	07-Apr-25	23-May-25	30-May-25	Not Started
PER-1050	Prepare & Submit FDNY Fuel Permit	10	10	01-Apr-25	14-Apr-25	19			01-Apr-25	14-Apr-25	28-Apr-25	09-May-25	Not Started
PER-1060	Obtain Builders Pavement Permit	10	10	01-Apr-25	14-Apr-25	33			01-Apr-25	14-Apr-25	16-May-25	30-May-25	Not Started
PER-1070	Obtain Excavation Permit	15	15	01-Apr-25	21-Apr-25	28			01-Apr-25	21-Apr-25	09-May-25	30-May-25	Not Started
PER-1080	Obtain Permit to Enter (PTE)	10	10	01-Apr-25	14-Apr-25	33			01-Apr-25	14-Apr-25	16-May-25	30-May-25	Not Started
PER-1090	Review & Approve FDNY Fuel Permit	21	21	15-Apr-25	05-May-25	27			15-Apr-25	05-May-25	12-May-25	01-Jun-25	Not Started
PER-1100	DOB Permit & Insurance	21	21	01-May-25	30-May-25	0			01-May-25	30-May-25	01-May-25	30-May-25	Not Started
PER-1110	SCA Work Notification	7	7	21-May-25	30-May-25	0			21-May-25	30-May-25	21-May-25	30-May-25	Not Started
PER-1120	No Site Access	180	180	02-Dec-24	30-May-25	0			02-Dec-24	30-May-25	02-Dec-24	30-May-25	Not Started
PRO-1000	Procure & Deliver Kitchen Equipment	180	180	19-Apr-25	15-Oct-25	376			19-Apr-25	15-Oct-25	30-Apr-26	26-Oct-26	Not Started
PRO-1010	Procure & Deliver Furnitures	130	130	19-Apr-25	26-Aug-25	218			19-Apr-25	26-Aug-25	23-Nov-25	01-Apr-26	Not Started
PRO-1020	Procure & Deliver Mechanical Piping	70	70	21-Mar-25	29-May-25	447			21-Mar-25	29-May-25	11-Jun-26	19-Aug-26	Not Started
PRO-1030	Procure & Deliver Mechanical Ducts	70	70	19-Apr-25	27-Jun-25	251			19-Apr-25	27-Jun-25	26-Dec-25	05-Mar-26	Not Started
PRO-1050	Procure & Deliver Electrical Equipment	130	130	19-Apr-25	26-Aug-25	275			19-Apr-25	26-Aug-25	19-Jan-26	28-May-26	Not Started
PRO-1060	Procure & Deliver Plumbing Fixtures	100	100	19-Apr-25	27-Jul-25	401			19-Apr-25	27-Jul-25	25-May-26	01-Sep-26	Not Started
PRO-1070	Procure & Deliver Doors	50	50	19-Apr-25	07-Jun-25	276			19-Apr-25	07-Jun-25	20-Jan-26	10-Mar-26	Not Started
PRO-1110	Procure & Deliver Fire Detectors & Alarms	60	60	19-Apr-25	17-Jun-25	441			19-Apr-25	17-Jun-25	04-Jul-26	01-Sep-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
PRO-1120	Procure & Deliver Erosion Control and Sedimentation Devices	25	25	01-Jan-25	25-Jan-25	136			01-Jan-25	25-Jan-25	17-May-25	10-Jun-25	Not Started
PRO-1140	Procure & Deliver Lighting Fixtures	60	60	05-Feb-25	05-Apr-25	431			05-Feb-25	05-Apr-25	12-Apr-26	10-Jun-26	Not Started
PRO-1150	Procure & Deliver Gypsum Board	150	150	19-Apr-25	15-Sep-25	178			19-Apr-25	15-Sep-25	14-Oct-25	12-Mar-26	Not Started
PRO-1160	Procure & Deliver Floorings	80	80	19-Apr-25	07-Jul-25	260			19-Apr-25	07-Jul-25	04-Jan-26	24-Mar-26	Not Started
PRO-1170	Procure & Deliver Acosutical Ceiling Tiles	120	120	21-Mar-25	18-Jul-25	275			21-Mar-25	18-Jul-25	21-Dec-25	19-Apr-26	Not Started
PRO-1190	Procure & Deliver Toilet Accessories	100	100	19-Apr-25	27-Jul-25	401			19-Apr-25	27-Jul-25	25-May-26	01-Sep-26	Not Started
PRO-1200	Procure & Deliver Elevator Machine	150	150	06-Mar-25	02-Aug-25	387			06-Mar-25	02-Aug-25	28-Mar-26	24-Aug-26	Not Started
PRO-1210	Procure & Deliver Signs	70	70	19-Apr-25	27-Jun-25	466			19-Apr-25	27-Jun-25	29-Jul-26	06-Oct-26	Not Started
PRO-1220	Procure & Deliver Windows	154	154	09-Apr-25	09-Sep-25	170			09-Apr-25	09-Sep-25	26-Sep-25	26-Feb-26	Not Started
PRO-1250	Procure & Deliver Plumbing Pipes	60	60	19-Apr-25	17-Jun-25	432			19-Apr-25	17-Jun-25	25-Jun-26	23-Aug-26	Not Started
PRO-1260	Procure & Deliver Electrical Wires & Conduits	130	130	19-Apr-25	26-Aug-25	198			19-Apr-25	26-Aug-25	03-Nov-25	12-Mar-26	Not Started
PRO-1270	Procure & Deliver Mechanical Pumps	70	70	19-Apr-25	27-Jun-25	461			19-Apr-25	27-Jun-25	24-Jul-26	01-Oct-26	Not Started
PRO-1280	Procure & Deliver Fire Protection Pumps	70	70	19-Apr-25	27-Jun-25	363			19-Apr-25	27-Jun-25	17-Apr-26	25-Jun-26	Not Started
PRO-1290	Procure & Deliver Plumbing Pumps	250	250	19-Apr-25	24-Dec-25	301			19-Apr-25	24-Dec-25	14-Feb-26	21-Oct-26	Not Started
PRO-1310	Procure & Deliver Telecommunication System	60	60	19-Apr-25	17-Jun-25	418			19-Apr-25	17-Jun-25	11-Jun-26	09-Aug-26	Not Started
PRO-1330	Procure & Deliver Cameras	60	60	06-Mar-25	04-May-25	464			06-Mar-25	04-May-25	13-Jun-26	11-Aug-26	Not Started
PRO-1380	Procure & Deliver Roof Dunnage	100	100	19-Apr-25	27-Jul-25	161			19-Apr-25	27-Jul-25	27-Sep-25	04-Jan-26	Not Started
PRO-1410	Procure & Deliver Door Frames	70	70	19-Apr-25	27-Jun-25	256			19-Apr-25	27-Jun-25	31-Dec-25	10-Mar-26	Not Started
PRO-1420	Procure & Deliver Painting	70	70	19-Apr-25	27-Jun-25	265			19-Apr-25	27-Jun-25	09-Jan-26	19-Mar-26	Not Started
PRO-1470	Procure & Deliver Cabinet Heaters	126	126	19-Apr-25	22-Aug-25	396			19-Apr-25	22-Aug-25	20-May-26	22-Sep-26	Not Started
PRO-1530	Procure & Deliver Hydraulic Vertical Wheelchair Lift	90	90	19-Apr-25	17-Jul-25	426			19-Apr-25	17-Jul-25	19-Jun-26	16-Sep-26	Not Started
PRO-1560	Procure & Deliver Gymnasium Equipment	180	180	19-Apr-25	15-Oct-25	362			19-Apr-25	15-Oct-25	16-Apr-26	12-Oct-26	Not Started
PRO-1580	Procure & Deliver Metal Deck	120	120	19-Apr-25	16-Aug-25	138			19-Apr-25	16-Aug-25	04-Sep-25	01-Jan-26	Not Started
PRO-1590	Procure & Deliver Steel Columns	120	120	19-Apr-25	16-Aug-25	145			19-Apr-25	16-Aug-25	11-Sep-25	08-Jan-26	Not Started
PRO-1600	Procure & Deliver Steel Framing	60	60	19-Apr-25	17-Jun-25	205			19-Apr-25	17-Jun-25	10-Nov-25	08-Jan-26	Not Started
PRO-1630	Procure & Deliver Wood Flooring	120	120	19-Apr-25	16-Aug-25	264			19-Apr-25	16-Aug-25	08-Jan-26	07-May-26	Not Started
SUB-1000	Prepare & Submit Split Heat Pump System - SUB	60	60	02-Dec-24	27-Feb-25	385			02-Dec-24	27-Feb-25	16-Jun-26	10-Sep-26	Not Started
SUB-1010	Prepare & Submit Thermometers	40	40	02-Dec-24	29-Jan-25	399			02-Dec-24	29-Jan-25	08-Jul-26	01-Sep-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
SUB-1020	Prepare & Submit Pressure Gages	40	40	02-Dec-24	29-Jan-25	334			02-Dec-24	29-Jan-25	03-Apr-26	29-May-26	Not Started
SUB-1030	Prepare & Submit Floor Drains	40	40	02-Dec-24	29-Jan-25	213			02-Dec-24	29-Jan-25	07-Oct-25	04-Dec-25	Not Started
SUB-1040	Prepare & Submit Hangers & Supports	40	40	02-Dec-24	29-Jan-25	220			02-Dec-24	29-Jan-25	17-Oct-25	15-Dec-25	Not Started
SUB-1050	Prepare & Submit Fire & Jockey Pumps	81	81	02-Dec-24	28-Mar-25	248			02-Dec-24	28-Mar-25	28-Nov-25	26-Mar-26	Not Started
SUB-1060	Prepare & Submit Interior Signage Shop Drawings	81	81	02-Dec-24	28-Mar-25	318			02-Dec-24	28-Mar-25	12-Mar-26	07-Jul-26	Not Started
SUB-1070	Prepare & Submit Ceramic Tiles Product Data	81	81	02-Dec-24	28-Mar-25	178			02-Dec-24	28-Mar-25	18-Aug-25	12-Dec-25	Not Started
SUB-1080	Prepare & Submit Door Hardware Submittal	81	81	02-Dec-24	28-Mar-25	175			02-Dec-24	28-Mar-25	13-Aug-25	09-Dec-25	Not Started
SUB-1090	Prepare & Submit Painting	81	81	02-Dec-24	28-Mar-25	182			02-Dec-24	28-Mar-25	22-Aug-25	18-Dec-25	Not Started
SUB-1100	Prepare & Submit Door & Frame Corners Samples	81	81	02-Dec-24	28-Mar-25	175			02-Dec-24	28-Mar-25	13-Aug-25	09-Dec-25	Not Started
SUB-1110	Prepare & Submit Roof Drains & Clean Outs	81	81	02-Dec-24	28-Mar-25	169			02-Dec-24	28-Mar-25	05-Aug-25	01-Dec-25	Not Started
SUB-1120	Prepare & Submit Flashing & Sheet Metal Shop Drawing	81	81	02-Dec-24	28-Mar-25	310			02-Dec-24	28-Mar-25	02-Mar-26	24-Jun-26	Not Started
SUB-1130	Prepare & Submit Perimeter Foundation Insulation Product Data	81	81	02-Dec-24	28-Mar-25	123			02-Dec-24	28-Mar-25	29-May-25	23-Sep-25	Not Started
SUB-1140	Prepare & Submit Crystalline Waterproofing Product Data	81	81	02-Dec-24	28-Mar-25	192			02-Dec-24	28-Mar-25	08-Sep-25	05-Jan-26	Not Started
SUB-1150	Prepare & Submit Suspension Assembly Shop Drawings	81	81	02-Dec-24	28-Mar-25	192			02-Dec-24	28-Mar-25	08-Sep-25	05-Jan-26	Not Started
SUB-1160	Prepare & Submit Certification of Material	81	81	02-Dec-24	28-Mar-25	55			02-Dec-24	28-Mar-25	21-Feb-25	16-Jun-25	Not Started
SUB-1170	Prepare & Submit Concrete Reinforcement	30	30	02-Dec-24	14-Jan-25	106			02-Dec-24	14-Jan-25	05-May-25	16-Jun-25	Not Started
SUB-1180	Prepare & Submit Formwork Shop Drawings	81	81	02-Dec-24	28-Mar-25	189			02-Dec-24	28-Mar-25	03-Sep-25	30-Dec-25	Not Started
SUB-1190	Prepare & Submit Planting Schedule	81	81	02-Dec-24	28-Mar-25	381			02-Dec-24	28-Mar-25	10-Jun-26	05-Oct-26	Not Started
SUB-1200	Prepare & Submit Site Furnishings Shop Drawings	15	15	02-Dec-24	20-Dec-24	101			02-Dec-24	20-Dec-24	28-Apr-25	16-May-25	Not Started
SUB-1210	Prepare & Submit Ductile Iron Pipes	37	37	02-Dec-24	24-Jan-25	331			02-Dec-24	24-Jan-25	31-Mar-26	20-May-26	Not Started
SUB-1220	Prepare & Submit Catch Basin Shop Drawings	81	81	02-Dec-24	28-Mar-25	326			02-Dec-24	28-Mar-25	24-Mar-26	17-Jul-26	Not Started
SUB-1230	Prepare & Submit Steel Curb Facing Shop Drawing	81	81	02-Dec-24	28-Mar-25	359			02-Dec-24	28-Mar-25	08-May-26	02-Sep-26	Not Started
SUB-1240	Prepare & Submit Asphaltic Concrete Paving	81	81	02-Dec-24	28-Mar-25	353			02-Dec-24	28-Mar-25	30-Apr-26	25-Aug-26	Not Started
SUB-1250	Prepare & Submit SSDS Geotextile	40	40	02-Dec-24	29-Jan-25	108			02-Dec-24	29-Jan-25	07-May-25	03-Jul-25	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
SUB-1260	Prepare & Submit Gas Vapor Barrier Submittal & Inspection Schedule	81	81	02-Dec-24	28-Mar-25	71			02-Dec-24	28-Mar-25	17-Mar-25	10-Jul-25	Not Started
SUB-1270	Prepare & Submit Existing Conditions Survey	10	10	02-Dec-24	13-Dec-24	115			02-Dec-24	13-Dec-24	16-May-25	30-May-25	Not Started
SUB-1280	Prepare & Submit Construction Indoor Air Quality Management Plan	81	81	02-Dec-24	28-Mar-25	30			02-Dec-24	28-Mar-25	15-Jan-25	09-May-25	Not Started
SUB-1290	Prepare & Submit Site Safety Plan	2	2	02-Dec-24	03-Dec-24	67			02-Dec-24	03-Dec-24	11-Mar-25	12-Mar-25	Not Started
SUB-1300	Prepare & Submit CWM Plan	81	81	02-Dec-24	28-Mar-25	30			02-Dec-24	28-Mar-25	15-Jan-25	09-May-25	Not Started
SUB-1310	Prepare & Submit Heating Plan	81	81	02-Dec-24	28-Mar-25	358			02-Dec-24	28-Mar-25	07-May-26	01-Sep-26	Not Started
SUB-1320	Prepare & Submit Sample Classroom Materials	81	81	02-Dec-24	28-Mar-25	219			02-Dec-24	28-Mar-25	16-Oct-25	12-Feb-26	Not Started
SUB-1330	Prepare & Submit Electrical Shop Drawings	81	81	02-Dec-24	28-Mar-25	136			02-Dec-24	28-Mar-25	17-Jun-25	10-Oct-25	Not Started
SUB-1340	Prepare & Submit Plumbing Shop Drawings	81	81	02-Dec-24	28-Mar-25	205			02-Dec-24	28-Mar-25	25-Sep-25	23-Jan-26	Not Started
SUB-1350	Prepare & Submit Concrete Shop Drawings	30	30	02-Dec-24	14-Jan-25	240			02-Dec-24	14-Jan-25	17-Nov-25	30-Dec-25	Not Started
SUB-1360	Prepare & Submit Elevator Machine	50	50	02-Dec-24	12-Feb-25	265			02-Dec-24	12-Feb-25	23-Dec-25	06-Mar-26	Not Started
SUB-1370	Prepare & Submit Gypsum Board	81	81	02-Dec-24	28-Mar-25	122			02-Dec-24	28-Mar-25	28-May-25	22-Sep-25	Not Started
SUB-1380	Prepare & Submit Floorings	81	81	02-Dec-24	28-Mar-25	178			02-Dec-24	28-Mar-25	18-Aug-25	12-Dec-25	Not Started
SUB-1390	Prepare & Submit Acosutical Ceiling Tiles	60	60	02-Dec-24	27-Feb-25	189			02-Dec-24	27-Feb-25	03-Sep-25	28-Nov-25	Not Started
SUB-1400	Prepare & Submit Toilet Accessories	81	81	02-Dec-24	28-Mar-25	274			02-Dec-24	28-Mar-25	07-Jan-26	01-May-26	Not Started
SUB-1410	Prepare & Submit Millwork	81	81	02-Dec-24	28-Mar-25	333			02-Dec-24	28-Mar-25	02-Apr-26	28-Jul-26	Not Started
SUB-1420	Prepare & Submit Lighting Fixtures	30	30	02-Dec-24	14-Jan-25	295			02-Dec-24	14-Jan-25	06-Feb-26	20-Mar-26	Not Started
SUB-1430	Prepare & Submit Furniture	81	81	02-Dec-24	28-Mar-25	150			02-Dec-24	28-Mar-25	09-Jul-25	31-Oct-25	Not Started
SUB-1440	Prepare & Submit Mechanical Ducts	81	81	02-Dec-24	28-Mar-25	172			02-Dec-24	28-Mar-25	08-Aug-25	04-Dec-25	Not Started
SUB-1450	Prepare & Submit Mechanical Piping	60	60	02-Dec-24	27-Feb-25	308			02-Dec-24	27-Feb-25	26-Feb-26	20-May-26	Not Started
SUB-1460	Prepare & Submit Erosion Control and Sedimentation Plan	7	7	02-Dec-24	10-Dec-24	94			02-Dec-24	10-Dec-24	17-Apr-25	25-Apr-25	Not Started
SUB-1470	Prepare & Submit QCP	30	30	02-Dec-24	14-Jan-25	81			02-Dec-24	14-Jan-25	31-Mar-25	09-May-25	Not Started
SUB-1480	Prepare & Submit Concrete Mix Design	30	30	02-Dec-24	14-Jan-25	240			02-Dec-24	14-Jan-25	17-Nov-25	30-Dec-25	Not Started
SUB-1490	Prepare & Submit Electrical Equipment, Conduits, and Cables	20	20	02-Dec-24	30-Dec-24	197			02-Dec-24	30-Dec-24	15-Sep-25	10-Oct-25	Not Started
SUB-1500	Prepare & Submit Plumbing Fixtures	81	81	02-Dec-24	28-Mar-25	274			02-Dec-24	28-Mar-25	07-Jan-26	01-May-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
SUB-1510	Prepare & Submit Baseline Schedule	52	52	02-Dec-24	14-Feb-25	59			02-Dec-24	14-Feb-25	27-Feb-25	09-May-25	Not Started
SUB-1520	Prepare & Submit Wood Doors	81	81	02-Dec-24	28-Mar-25	188			02-Dec-24	28-Mar-25	02-Sep-25	29-Dec-25	Not Started
SUB-1530	Prepare & Submit Fire Protection Shop Drawings	81	81	02-Dec-24	28-Mar-25	248			02-Dec-24	28-Mar-25	28-Nov-25	26-Mar-26	Not Started
SUB-1540	Prepare & Submit Fire Detectors & Alarms	81	81	02-Dec-24	28-Mar-25	303			02-Dec-24	28-Mar-25	19-Feb-26	12-Jun-26	Not Started
SUB-1550	Prepare & Submit Kitchen Equipment	81	81	02-Dec-24	28-Mar-25	257			02-Dec-24	28-Mar-25	11-Dec-25	08-Apr-26	Not Started
SUB-1560	Prepare & Submit Signs	81	81	02-Dec-24	28-Mar-25	318			02-Dec-24	28-Mar-25	12-Mar-26	07-Jul-26	Not Started
SUB-1570	Prepare & Submit Windows	73	73	02-Dec-24	18-Mar-25	118			02-Dec-24	18-Mar-25	21-May-25	04-Sep-25	Not Started
SUB-1580	Prepare & Submit Telecommunication System Drawings	81	81	02-Dec-24	28-Mar-25	287			02-Dec-24	28-Mar-25	27-Jan-26	20-May-26	Not Started
SUB-1590	Prepare & Submit Internet Protocol Digital Video Surveillance System using Digital Cameras	50	50	02-Dec-24	12-Feb-25	320			02-Dec-24	12-Feb-25	16-Mar-26	22-May-26	Not Started
SUB-1600	Prepare & Submit Roof Dunnage	81	81	02-Dec-24	28-Mar-25	111			02-Dec-24	28-Mar-25	12-May-25	05-Sep-25	Not Started
SUB-1610	Prepare & Submit Switch Gears Product Data	20	20	02-Dec-24	30-Dec-24	410			02-Dec-24	30-Dec-24	23-Jul-26	19-Aug-26	Not Started
SUB-1620	Prepare & Submit Unit Cabinet Heaters	60	60	02-Dec-24	27-Feb-25	292			02-Dec-24	27-Feb-25	03-Feb-26	28-Apr-26	Not Started
SUB-1630	Prepare & Submit Gymnasium Equipment	81	81	02-Dec-24	28-Mar-25	247			02-Dec-24	28-Mar-25	26-Nov-25	25-Mar-26	Not Started
SUB-1640	Prepare & Submit Underground Coordination Drawings	50	50	02-Dec-24	12-Feb-25	37			02-Dec-24	12-Feb-25	27-Jan-25	07-Apr-25	Not Started
SUB-1650	Prepare & Submit 1st Floor MEP Coordination Drawings	75	75	02-Dec-24	20-Mar-25	151			02-Dec-24	20-Mar-25	10-Jul-25	24-Oct-25	Not Started
SUB-1660	Prepare & Submit 2nd Floor MEP Coordination Drawings	75	75	02-Dec-24	20-Mar-25	155			02-Dec-24	20-Mar-25	16-Jul-25	30-Oct-25	Not Started
SUB-1670	Prepare & Submit 3rd Floor MEP Coordination Drawings	75	75	02-Dec-24	20-Mar-25	155			02-Dec-24	20-Mar-25	16-Jul-25	30-Oct-25	Not Started
SUB-1680	Prepare & Submit 4th Floor MEP Coordination Drawings	75	75	02-Dec-24	20-Mar-25	171			02-Dec-24	20-Mar-25	07-Aug-25	24-Nov-25	Not Started
SUB-1690	Prepare & Submit 5th Floor MEP Coordination Drawings	75	75	02-Dec-24	20-Mar-25	179			02-Dec-24	20-Mar-25	19-Aug-25	05-Dec-25	Not Started
SUB-1700	Prepare & Submit Environmental Site Assessment Reports	81	81	02-Dec-24	28-Mar-25	30			02-Dec-24	28-Mar-25	15-Jan-25	09-May-25	Not Started
SUB-1710	Prepare & Submit Selective Removals & Demoloition	81	81	02-Dec-24	28-Mar-25	378			02-Dec-24	28-Mar-25	05-Jun-26	30-Sep-26	Not Started
SUB-1720	Prepare & Submit Foundation Shop Drawings	5	5	02-Dec-24	06-Dec-24	191			02-Dec-24	06-Dec-24	05-Sep-25	11-Sep-25	Not Started
SUB-1730	Prepare & Submit Chain Link Fences & Gates Drawings	81	81	02-Dec-24	28-Mar-25	35			02-Dec-24	28-Mar-25	23-Jan-25	16-May-25	Not Started
SUB-1740	Prepare & Submit Unit Masonry	81	81	02-Dec-24	28-Mar-25	297			02-Dec-24	28-Mar-25	10-Feb-26	04-Jun-26	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
SUB-1750	Prepare & Submit Structure Steel Drawings	81	81	02-Dec-24	28-Mar-25	100			02-Dec-24	28-Mar-25	25-Apr-25	20-Aug-25	Not Started
SUB-1760	Prepare & Submit Metal Deck Product Data	81	81	02-Dec-24	28-Mar-25	95			02-Dec-24	28-Mar-25	18-Apr-25	13-Aug-25	Not Started
SUB-1770	Prepare & Submit Security Screens & Barriers	81	81	02-Dec-24	28-Mar-25	214			02-Dec-24	28-Mar-25	08-Oct-25	05-Feb-26	Not Started
SUB-1780	Prepare & Submit Wood Flooring	81	81	02-Dec-24	28-Mar-25	181			02-Dec-24	28-Mar-25	21-Aug-25	17-Dec-25	Not Started
SUB-1790	Prepare & Submit Visual Display Boards	81	81	02-Dec-24	28-Mar-25	308			02-Dec-24	28-Mar-25	26-Feb-26	22-Jun-26	Not Started
SUB-1800	Prepare & Submit Fire Extinguishers & Cabinets	81	81	02-Dec-24	28-Mar-25	298			02-Dec-24	28-Mar-25	11-Feb-26	05-Jun-26	Not Started
SUB-1810	Prepare & Submit Stationary Metal Wall Louvers	73	73	02-Dec-24	18-Mar-25	118			02-Dec-24	18-Mar-25	21-May-25	04-Sep-25	Not Started
SUB-1820	Prepare & Submit Platform Curtains & Auditorium Window Curtains	81	81	02-Dec-24	28-Mar-25	214			02-Dec-24	28-Mar-25	08-Oct-25	05-Feb-26	Not Started
SUB-1830	Prepare & Submit Domestic Equipment	81	81	02-Dec-24	28-Mar-25	257			02-Dec-24	28-Mar-25	11-Dec-25	08-Apr-26	Not Started
SUB-1840	Prepare & Submit Manufactured Wood Casework	81	81	02-Dec-24	28-Mar-25	150			02-Dec-24	28-Mar-25	09-Jul-25	31-Oct-25	Not Started
SUB-1850	Prepare & Submit Hydraulic Vertical Wheelchair Lifts	81	81	02-Dec-24	28-Mar-25	292			02-Dec-24	28-Mar-25	03-Feb-26	28-May-26	Not Started
SUB-1860	Prepare & Submit Switch & Panel Boards	81	81	02-Dec-24	28-Mar-25	349			02-Dec-24	28-Mar-25	24-Apr-26	19-Aug-26	Not Started
SUB-1870	Prepare & Submit Overcurrent Protective Devices Data	81	81	02-Dec-24	28-Mar-25	376			02-Dec-24	28-Mar-25	03-Jun-26	28-Sep-26	Not Started
SUB-1880	Prepare & Submit Pumping Apparatus & Tanks	81	81	02-Dec-24	28-Mar-25	241			02-Dec-24	28-Mar-25	18-Nov-25	17-Mar-26	Not Started
SUB-1890	Prepare & Submit Emergency Generator System Accessories	81	81	02-Dec-24	28-Mar-25	364			02-Dec-24	28-Mar-25	15-May-26	10-Sep-26	Not Started
SUB-1900	Prepare & Submit Unit Heaters/Cabinet Heaters Equipment	81	81	02-Dec-24	28-Mar-25	271			02-Dec-24	28-Mar-25	02-Jan-26	28-Apr-26	Not Started
SUB-1910	Prepare & Submit Temperature Control System	81	81	02-Dec-24	28-Mar-25	307			02-Dec-24	28-Mar-25	25-Feb-26	18-Jun-26	Not Started
SUB-1920	Prepare & Submit Air Outlets & Inlets	81	81	02-Dec-24	28-Mar-25	325			02-Dec-24	28-Mar-25	23-Mar-26	16-Jul-26	Not Started
SUB-1930	Prepare & Submit Final Underground Coordination Drawings	37	37	06-Mar-25	25-Apr-25	38			06-Mar-25	25-Apr-25	29-Apr-25	20-Jun-25	Not Started
SUB-1940	Review & Approve Door Hardware Submittal	21	21	29-Mar-25	18-Apr-25	256			29-Mar-25	18-Apr-25	10-Dec-25	30-Dec-25	Not Started
SUB-1950	Review & Approve Gas Vapor Barrier Submittal & Inspection Schedule	21	21	29-Mar-25	18-Apr-25	104			29-Mar-25	18-Apr-25	11-Jul-25	31-Jul-25	Not Started
SUB-1960	Prepare & Submit Record Documents	81	81	13-Jul-26	04-Nov-26	63			13-Jul-26	04-Nov-26	09-Oct-26	08-Feb-27	Not Started

© Oracle Corporation

All Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
Total		644	644	02-Dec-24	29-Jun-27	0			02-Dec-24	29-Jun-27	02-Dec-24	29-Jun-27	

© Oracle Corporation

APPENDIX 8
– Total Float Report

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
PER-1120	No Site Access	180	02-Dec-24	30-May-25	Not Started	0
CON-1000	Mobilization	5	02-Jun-25	06-Jun-25	Not Started	0
CON-1010	Install Site Fence	2	09-Jun-25	10-Jun-25	Not Started	0
CON-1030	Install Erosion Control Devices - Stage 1	2	11-Jun-25	12-Jun-25	Not Started	0
CON-1040	Remove Existing Asphalt Pavement and Subbase	2	13-Jun-25	16-Jun-25	Not Started	0
CON-1050	Install Remove Existing Concrete Pavement and Subbase	2	13-Jun-25	16-Jun-25	Not Started	0
CON-1060	Prepare Temporary Staging & Storage Area - Stage 1	3	17-Jun-25	20-Jun-25	Not Started	0
CON-1250	Install Construction Entrance - Stage 2	1	30-Sep-25	30-Sep-25	Not Started	0
CON-1260	Install Erosion Control Devices - Stage 2	2	01-Oct-25	02-Oct-25	Not Started	0
CON-1270	Prepare Temporary Staging & Storage Area - Stage 2	2	01-Oct-25	02-Oct-25	Not Started	0
CON-1070	Survey and Verify All Underground Utilities	3	23-Jun-25	25-Jun-25	Not Started	0
CON-1960	Pour Concrete Topping Slab	4	21-Jan-26	26-Jan-26	Not Started	0
CON-2220	Install Hot Fluid-Applied Rubberized Asphalt Fabric-Reinforced Roofing Membrane	5	27-Jan-26	02-Feb-26	Not Started	0
CON-2510	Install Fabric Reinforcing Sheet	4	03-Feb-26	06-Feb-26	Not Started	0
CON-2770	Install Protection Sheet and Roof Barrier	4	09-Feb-26	12-Feb-26	Not Started	0
CON-2890	Install 1/2" Drainage Panel	4	13-Feb-26	19-Feb-26	Not Started	0
CON-3180	Install 8" Roof Insulation (R-40 Min) Multi-Layered and Staggered	5	20-Feb-26	26-Feb-26	Not Started	0
CON-3350	Install Filter Fabric	3	27-Feb-26	03-Mar-26	Not Started	0
CON-4420	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - Cellar Floor	7	09-Apr-26	17-Apr-26	Not Started	0
CON-4580	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 2nd Floor	7	20-Apr-26	28-Apr-26	Not Started	0
CON-4690	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 3rd Floor	7	29-Apr-26	07-May-26	Not Started	0
CON-4830	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 4th Floor	7	08-May-26	18-May-26	Not Started	0
CON-4960	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - Lower Roof	7	19-May-26	28-May-26	Not Started	0
CON-5810	Install Ceiling Hangers - 1st Floor	5	07-Jul-26	13-Jul-26	Not Started	0
CON-4590	Install Acoustical Ceiling Tiles- Cellar Floor	7	20-Apr-26	28-Apr-26	Not Started	0
CON-5920	Install Gypsum Board Ceiling - 1st Floor	7	14-Jul-26	22-Jul-26	Not Started	0
CON-4600	Install Gypsum Board Ceiling- Cellar Floor	7	20-Apr-26	28-Apr-26	Not Started	0
CON-5930	Install Acoustical Ceiling Tiles - 1st Floor	7	14-Jul-26	22-Jul-26	Not Started	0
CON-5940	Install Wood Slat Ceiling - 1st Floor	7	14-Jul-26	22-Jul-26	Not Started	0
CON-5950	MCP-Wood Slat Ceiling Panel - 1st Floor	7	14-Jul-26	22-Jul-26	Not Started	0
CON-4860	Install Flooring - Cellar Floor	7	08-May-26	18-May-26	Not Started	0
CON-5000	Install Flooring - 2nd Floor	7	19-May-26	28-May-26	Not Started	0
CON-1320	Install Non-Woven Geotextile Layer - Below 1st Floor SOG	3	27-Oct-25	29-Oct-25	Not Started	0
CON-1330	Install Gas Permeable Aggregate Layer - Below 1st Floor SOG	3	30-Oct-25	03-Nov-25	Not Started	0
CON-1350	Install VI-20 Geomembrane Gas Permeable Aggregate Layer - Below 1st Floor SOG	3	04-Nov-25	06-Nov-25	Not Started	0
CON-1360	Install 60 Dry Mils of Liquid Boot - Below 1st Floor SOG	3	07-Nov-25	12-Nov-25	Not Started	0
CON-1370	Install Liquid Boot Ultrashield G-1000 - Below 1st Floor SOG	2	13-Nov-25	14-Nov-25	Not Started	0
CON-1080	Excavation	7	26-Jun-25	07-Jul-25	Not Started	0
CON-1090	F/R/P Cellar Wall Footings	6	08-Jul-25	15-Jul-25	Not Started	0
CON-1100	F/R/P Cellar Retaining Wall	8	16-Jul-25	25-Jul-25	Not Started	0
CON-1180	F/R/P Slab on Grade - Cellar	4	11-Aug-25	14-Aug-25	Not Started	0
CON-1190	F/R/P First Floor Slab - Cellar Side	5	15-Aug-25	21-Aug-25	Not Started	0
CON-1220	Curing For The First Floor Slab	28	22-Aug-25	18-Sep-25	Not Started	0

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-1240	Backfilling	7	19-Sep-25	29-Sep-25	Not Started	0
CON-1280	F/R/P First Floor Foundation	7	03-Oct-25	14-Oct-25	Not Started	0
CON-1310	Backfilling	5	20-Oct-25	24-Oct-25	Not Started	0
CON-1380	F/R/P First Floor SOG	4	17-Nov-25	20-Nov-25	Not Started	0
CON-1110	Install Non-Woven Geotextile Layer - Below Cellar	2	28-Jul-25	29-Jul-25	Not Started	0
CON-1130	Install Gas Permeable Aggregate Layer- Below Cellar	2	30-Jul-25	31-Jul-25	Not Started	0
CON-1150	Install VI-20 Geomembrane Gas Permeable Aggregate Layer - Below Cellar	2	01-Aug-25	04-Aug-25	Not Started	0
CON-1160	Install 60 Dry Mils of Liquid Boot - Below Cellar	2	05-Aug-25	06-Aug-25	Not Started	0
CON-1170	Install Liquid Boot Ultrashield G-1000 - Below Cellar	2	07-Aug-25	08-Aug-25	Not Started	0
CON-1140	Install 6" C.I Pipe - Below Cellar	2	30-Jul-25	31-Jul-25	Not Started	0
CON-1300	Insulate First Floor Foundations	3	15-Oct-25	17-Oct-25	Not Started	0
CON-1400	F/R/P Concrete Slab - 2nd Floor	5	21-Nov-25	28-Nov-25	Not Started	0
CON-1430	F/R/P Columns & Shear Walls From Second Floor To Third Floor	3	01-Dec-25	03-Dec-25	Not Started	0
CON-1440	F/R/P Concrete Slab - 3rd Floor	5	04-Dec-25	10-Dec-25	Not Started	0
CON-1460	F/R/P Columns & Shear Walls From Third Floor To Fourth Floor	3	11-Dec-25	15-Dec-25	Not Started	0
CON-1490	F/R/P Concrete Slab - 4th Floor	4	16-Dec-25	19-Dec-25	Not Started	0
CON-1540	Install Mainroof Posts and Framing	7	22-Dec-25	31-Dec-25	Not Started	0
CON-1620	F/R/P Concrete Deck Slab - Upper Roof	5	02-Jan-26	08-Jan-26	Not Started	0
CON-1710	Install Dunnage Framing - Upper Roof	7	09-Jan-26	20-Jan-26	Not Started	0
CON-5120	Rough-in Duct Work -VAV Devices & Diffusers - 1st Floor	5	29-May-26	04-Jun-26	Not Started	0
CON-5290	Rough-in Power Conduits & Wires - 1st Floor	5	05-Jun-26	11-Jun-26	Not Started	0
CON-5470	Rough-in Low Voltage Conduits & Wires - 1st Floor	5	12-Jun-26	18-Jun-26	Not Started	0
CON-6100	Install Lighting Fixtures - 1st Floor	7	03-Aug-26	11-Aug-26	Not Started	0
CON-5820	Install Bacnet Data Enclosure	7	10-Jul-26	20-Jul-26	Not Started	0
CON-5960	Install PA Rack	7	21-Jul-26	29-Jul-26	Not Started	0
CON-6040	Install Voice Rack	7	30-Jul-26	07-Aug-26	Not Started	0
CON-6120	Install Data Rack	7	10-Aug-26	18-Aug-26	Not Started	0
CON-6190	Install Voice Cabinet	7	19-Aug-26	27-Aug-26	Not Started	0
CON-5150	Install Voice Cabinet	7	29-May-26	08-Jun-26	Not Started	0
CON-5340	Install Data Equipment Rack	7	09-Jun-26	17-Jun-26	Not Started	0
CON-5540	Install Data Cabinet Patch Panel Rack	7	18-Jun-26	29-Jun-26	Not Started	0
CON-5690	Install Vertical Wire Manager	7	30-Jun-26	09-Jul-26	Not Started	0
CON-5640	Rough-in Plumbing Pipes - 1st Floor	5	22-Jun-26	26-Jun-26	Not Started	0
CON-6160	Install Data & Video Intercome Systems - 1st Floor	7	12-Aug-26	20-Aug-26	Not Started	0
CON-6220	Install Voice Systems Components - 1st Floor	7	21-Aug-26	31-Aug-26	Not Started	0
CON-6260	Install Public Address and Clock Systems Components - 1st Floor	7	01-Sep-26	10-Sep-26	Not Started	0
CON-5680	Rough-in Sprinkler Piping - 1st Floor	5	29-Jun-26	06-Jul-26	Not Started	0
CON-5780	Install Sprinkler Heads - 1st Floor	2	02-Jul-26	06-Jul-26	Not Started	0
CON-6280	Install Auxiliary Signal System Components - 1st Floor	7	11-Sep-26	21-Sep-26	Not Started	0
CON-6290	Install Intrusion Alarm System Components - 1st Floor	7	22-Sep-26	30-Sep-26	Not Started	0
CON-6300	Install IPDVS System Components - 1st Floor	12	01-Oct-26	19-Oct-26	Not Started	0
CON-4730	Install First Coat Painting - Cellar Floor	7	29-Apr-26	07-May-26	Not Started	0
CON-6030	Install First Coat Painting - 1st Floor	7	23-Jul-26	31-Jul-26	Not Started	0
CON-3650	Install Walls GWB-Mockup Room	3	06-Mar-26	10-Mar-26	Not Started	0

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-3850	Install Door Frames-Mockup Room	2	11-Mar-26	12-Mar-26	Not Started	0
CON-3950	Install Gypsum Board Ceiling -Mockup Room	3	13-Mar-26	17-Mar-26	Not Started	0
CON-4070	Install Doors & Hardware-Mockup Room	2	18-Mar-26	19-Mar-26	Not Started	0
CON-4160	Paint First coat -Mockup Room	3	20-Mar-26	24-Mar-26	Not Started	0
CON-4230	Flooring Finishes-Mockup Room	3	25-Mar-26	27-Mar-26	Not Started	0
CON-4290	Paint Second coat-Mockup Room	3	30-Mar-26	01-Apr-26	Not Started	0
CON-4360	Install Furniture & Signs -Mockup Room	3	02-Apr-26	06-Apr-26	Not Started	0
CON-4390	Mockup Room Inspection & Punchlist	2	07-Apr-26	08-Apr-26	Not Started	0
CON-1210	Install MEP Hangers - 1st Floor - Cellar Side	2	20-Aug-25	21-Aug-25	Not Started	0
CON-3490	Upper Roofing Testing	2	04-Mar-26	05-Mar-26	Not Started	0
MIL-1020	Building Tight	0		05-Mar-26	Not Started	0
MIL-1000	NTP	0	02-Dec-24		Not Started	0
MIL-1010	Project Duration (From NTP till TCO) = 730 CDs	730	02-Dec-24	01-Dec-26	Not Started	0
MIL-1030	TCO	0		01-Dec-26*	Not Started	0
MIL-1040	Substantial Completion	0		01-Mar-27*	Not Started	0
MIL-1050	Final Completion	0		29-Jun-27*	Not Started	0
CON-6250	MDF & IDF Rooms Testing and Inspection (Before 3-Sep-26)	7	28-Aug-26	03-Sep-26	Not Started	0
CON-6320	IPDV System Testing and Inspection (Before 2-Nov-26)	10	20-Oct-26	02-Nov-26	Not Started	0
CLO-1000	Pre-Final Clean-Out	2	03-Nov-26	04-Nov-26	Not Started	0
CLO-1010	Pre-TCO Inspection	4	05-Nov-26	08-Nov-26	Not Started	0
CLO-1020	Pre-TCO Punchlist	15	09-Nov-26	01-Dec-26	Not Started	0
CLO-1030	Pre-Final Clean-Out	2	02-Dec-26	03-Dec-26	Not Started	0
CLO-1040	Pre-Substantial Completion Inspection	10	04-Dec-26	13-Dec-26	Not Started	0
CLO-1050	Pre-Substantial Punchlist	52	14-Dec-26	01-Mar-27	Not Started	0
CLO-1080	Pre-Final Punchlist	75	15-Mar-27	29-Jun-27	Not Started	0
PER-1110	SCA Work Notification	7	21-May-25	30-May-25	Not Started	0
PER-1100	DOB Permit & Insurance	21	01-May-25	30-May-25	Not Started	0
MIL-1060	IDF and MDF Rooms Ready	0		03-Sep-26*	Not Started	0
MIL-1070	IPDVS System Installed	0		02-Nov-26*	Not Started	0
CON-1020	Install Construction Entrance - Stage 1	1	09-Jun-25	09-Jun-25	Not Started	1
CON-1340	Install 6" C.I Pipe - Below 1st Floor SOG	2	30-Oct-25	31-Oct-25	Not Started	1
CLO-1060	Pre-Final Clean-Out	2	02-Mar-27	03-Mar-27	Not Started	1
CLO-1070	Pre-Final Completion Inspection	10	04-Mar-27	13-Mar-27	Not Started	1
CON-1600	Install Dunnage Framing - Lower Roof	4	31-Dec-25	06-Jan-26	Not Started	2
CON-1550	F/R/P Concrete Columns From Fourth Slab to Lower Roof Slab- 4th Floor	2	22-Dec-25	23-Dec-25	Not Started	2
CON-1560	F/R/P Concrete Slab- Lower Roof	4	24-Dec-25	30-Dec-25	Not Started	2
COR-1010	Scheduling With CON-ED For Temporary Electrical Power	7	15-Apr-25	23-Apr-25	Not Started	2
COR-1000	Coordination With CON-ED For Temporary Electrical Power	10	01-Apr-25	14-Apr-25	Not Started	2
COR-1020	Procurement From CON-ED For Temporary Electrical Power	20	24-Apr-25	13-May-25	Not Started	2
COR-1030	CON-ED Work For Temporary Electrical Power	10	14-May-25	28-May-25	Not Started	2
COR-1040	Available Temporary Electrical Power For Testing MEP Equipment	0		28-May-25	Not Started	2
CON-1700	F/R/P Columns and Slab of The Bulkheads	4	09-Jan-26	14-Jan-26	Not Started	3
CON-1680	Install Floor Drains - Upper Roof	2	07-Jan-26	08-Jan-26	Not Started	3
CON-6310	Install Fire Alarm Devices - 1st Floor	7	20-Oct-26	28-Oct-26	Not Started	3
CON-1670	Install MEP Hangers - Upper Roof	2	07-Jan-26	08-Jan-26	Not Started	7
CON-1580	Install Floor Drains - Lower Roof	2	29-Dec-25	30-Dec-25	Not Started	7

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-1590	Install Penthouse Posts and Roof Framing	3	31-Dec-25	05-Jan-26	Not Started	8
CON-1780	Install Scaffolding - North Elevation	4	14-Jan-26	20-Jan-26	Not Started	10
CON-1950	Install Scaffolding - East Elevation	2	21-Jan-26	22-Jan-26	Not Started	10
CON-2080	Install Scaffolding - South Elevation	4	23-Jan-26	28-Jan-26	Not Started	10
CON-2310	Scaffolding Inspection & Sign-Off -South Elevation	2	29-Jan-26	30-Jan-26	Not Started	10
CON-2430	Install 5/8 Sheathing -South Elevation	4	02-Feb-26	05-Feb-26	Not Started	10
CON-2660	Install 6" Semi-Rigid Mineral Wool System -South Elevation	4	06-Feb-26	11-Feb-26	Not Started	10
CON-2830	Install Window Frames & Windows / Storefronts -South Elevation	5	12-Feb-26	19-Feb-26	Not Started	10
CON-1630	Pour Concrete Topping Slab	3	07-Jan-26	09-Jan-26	Not Started	10
CON-1740	Install Hot Fluid-Applied Rubberized Asphalt Fabric-Reinforced Roofing Membrane	4	12-Jan-26	15-Jan-26	Not Started	10
CON-1860	Install Fabric Reinforcing Sheet	4	16-Jan-26	22-Jan-26	Not Started	10
CON-2090	Install Protection Sheet and Roof Barrier	3	23-Jan-26	27-Jan-26	Not Started	10
CON-2250	Install 1/2" Drainage Panel	3	28-Jan-26	30-Jan-26	Not Started	10
CON-2450	Install 8" Roof Insulation (R-40 Min) Multi-Layered and Staggered	5	02-Feb-26	06-Feb-26	Not Started	10
CON-2760	Install Filter Fabric	3	09-Feb-26	11-Feb-26	Not Started	10
CON-5240	Layout - 1st Floor	2	05-Jun-26	08-Jun-26	Not Started	10
CON-5300	Install Top & Bottom Tracks - 1st Floor	2	09-Jun-26	10-Jun-26	Not Started	10
CON-5450	Install Steel Studs - 1st Floor	4	11-Jun-26	16-Jun-26	Not Started	10
CON-5500	Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 1st Floor	7	17-Jun-26	26-Jun-26	Not Started	10
CON-2880	Lower Roofing Testing	5	12-Feb-26	19-Feb-26	Not Started	10
CON-1730	F/R/P Parapets - Upper Roof	3	09-Jan-26	13-Jan-26	Not Started	10
CON-1570	Install MEP Hangers - Lower Roof	2	29-Dec-25	30-Dec-25	Not Started	11
CON-1520	Install Floor Drains - 4th Floor	2	18-Dec-25	19-Dec-25	Not Started	11
CON-4610	Install Doors- Cellar Floor	3	20-Apr-26	22-Apr-26	Not Started	11
CON-1610	F/R/P Parapets - Lower Roof	3	31-Dec-25	05-Jan-26	Not Started	11
CON-2320	Install Scaffolding - West Elevation	2	29-Jan-26	30-Jan-26	Not Started	12
CON-2440	Scaffolding Inspection & Sign-Off - West Elevation	2	02-Feb-26	03-Feb-26	Not Started	12
CON-2580	Install 5/8 Sheathing - West Elevation	3	04-Feb-26	06-Feb-26	Not Started	12
CON-2750	Install 6" Semi-Rigid Mineral Wool System - West Elevation	3	09-Feb-26	11-Feb-26	Not Started	12
CON-2860	Install Window Frames & Windows / Storefronts - West Elevation	3	12-Feb-26	17-Feb-26	Not Started	12
CON-1470	Install Floor Drains - 3rd Floor	2	11-Dec-25	12-Dec-25	Not Started	14
CON-1230	F/R/P Columns & Shear Walls From First Level To Second Level - Cellar Area	4	22-Aug-25	27-Aug-25	Not Started	15
CON-1510	Install MEP Hangers - 4th Floor	2	18-Dec-25	19-Dec-25	Not Started	15
CON-4640	Install Doors- 2nd Floor	3	23-Apr-26	27-Apr-26	Not Started	15
CON-1940	Scaffolding Inspection & Sign-Off -North Elevation	2	21-Jan-26	22-Jan-26	Not Started	16
CON-2060	Install 5/8 Sheathing -North Elevation	4	23-Jan-26	28-Jan-26	Not Started	16
CON-2300	Install 6" Semi-Rigid Mineral Wool System -North Elevation	4	29-Jan-26	03-Feb-26	Not Started	16
CON-2540	Install Window Frames & Windows / Storefronts -North Elevation	5	04-Feb-26	10-Feb-26	Not Started	16
CON-2070	Scaffolding Inspection & Sign-Off - East Elevation	2	23-Jan-26	26-Jan-26	Not Started	18
CON-2210	Install 5/8 Sheathing - East Elevation	3	27-Jan-26	29-Jan-26	Not Started	18
CON-2350	Install 6" Semi-Rigid Mineral Wool System - East Elevation	3	30-Jan-26	03-Feb-26	Not Started	18
CON-2570	Install Window Frames & Windows / Storefronts - East Elevation	3	04-Feb-26	06-Feb-26	Not Started	18
PER-1050	Prepare & Submit FDNY Fuel Permit	10	01-Apr-25	14-Apr-25	Not Started	19

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-1450	Install MEP Hangers - 3rd Floor	2	09-Dec-25	10-Dec-25	Not Started	20
CON-5910	Install MDF Telephone System Backboard	7	10-Jul-26	20-Jul-26	Not Started	21
CON-6020	Install Telecom Panel	7	21-Jul-26	29-Jul-26	Not Started	21
CON-1420	Install Floor Drains - 2nd Floor	2	26-Nov-25	28-Nov-25	Not Started	22
PER-1030	Meeting With SCA to Review The Permit Requirements	14	01-Apr-25	18-Apr-25	Not Started	22
CON-4700	Install Acoustical Ceiling Tiles - 2nd Floor	7	29-Apr-26	07-May-26	Not Started	23
CON-4840	Install Gypsum Board Ceiling - 3rd Floor	7	08-May-26	18-May-26	Not Started	23
CON-4970	Install Acoustical Ceiling Tiles - 4th Floor	7	19-May-26	28-May-26	Not Started	23
CON-5100	Install Gypsum Board Ceiling - Lower Roof	7	29-May-26	08-Jun-26	Not Started	23
CON-4710	Install Gypsum Board Ceiling - 2nd Floor	7	29-Apr-26	07-May-26	Not Started	23
CON-4850	Install Acoustical Ceiling Tiles - 3rd Floor	7	08-May-26	18-May-26	Not Started	23
CON-4980	Install Gypsum Board Ceiling- 4th Floor	7	19-May-26	28-May-26	Not Started	23
CON-4990	Install TECTUM WOOD Fiber Composition Ceiling Tiles- 4th Floor	7	19-May-26	28-May-26	Not Started	23
CON-4870	Install Lighting Fixtures - Cellar Floor	7	08-May-26	18-May-26	Not Started	23
CON-5020	Install Lighting Fixtures - 2nd Floor	7	19-May-26	28-May-26	Not Started	23
CON-5140	Install Lighting Fixtures - 3rd Floor	7	29-May-26	08-Jun-26	Not Started	23
CON-5330	Install Lighting Fixtures - 4th Floor	7	09-Jun-26	17-Jun-26	Not Started	23
CON-5530	Install Lighting Fixtures - Lower Roof	7	18-Jun-26	29-Jun-26	Not Started	23
CON-5030	Install Data & Video Intercome Systems -Cellar Floor	7	19-May-26	28-May-26	Not Started	23
CON-5160	Install Data & Video Intercome Systems - 2nd Floor	7	29-May-26	08-Jun-26	Not Started	23
CON-5350	Install Data & Video Intercome Systems - 3rd Floor	7	09-Jun-26	17-Jun-26	Not Started	23
CON-5550	Install Data & Video Intercome Systems - 4th Floor	7	18-Jun-26	29-Jun-26	Not Started	23
CON-5700	Install Data & Video Intercome Systems - Lower Roof	7	30-Jun-26	09-Jul-26	Not Started	23
CON-5170	Install Voice Systems Components -Cellar Floor	7	29-May-26	08-Jun-26	Not Started	23
CON-5360	Install Voice Systems Components - 2nd Floor	7	09-Jun-26	17-Jun-26	Not Started	23
CON-5560	Install Voice Systems Components - 3rd Floor	7	18-Jun-26	29-Jun-26	Not Started	23
CON-5710	Install Voice Systems Components - 4th Floor	7	30-Jun-26	09-Jul-26	Not Started	23
CON-5840	Install Voice Systems Components - Lower Roof	7	10-Jul-26	20-Jul-26	Not Started	23
CON-5370	Install Public Address and Clock Systems Components -Cellar Floor	7	09-Jun-26	17-Jun-26	Not Started	23
CON-5570	Install Public Address and Clock Systems Components - 2nd Floor	7	18-Jun-26	29-Jun-26	Not Started	23
CON-5720	Install Public Address and Clock Systems Components - 3rd Floor	7	30-Jun-26	09-Jul-26	Not Started	23
CON-5850	Install Public Address and Clock Systems Components - 4th Floor	7	10-Jul-26	20-Jul-26	Not Started	23
CON-5970	Install Public Address and Clock Systems Components - Lower Roof	7	21-Jul-26	29-Jul-26	Not Started	23
CON-5580	Install Auxiliary Signal System Components - Cellar Floor	7	18-Jun-26	29-Jun-26	Not Started	23
CON-5730	Install Auxiliary Signal System Components - 2nd Floor	7	30-Jun-26	09-Jul-26	Not Started	23
CON-5860	Install Auxiliary Signal System Components - 3rd Floor	7	10-Jul-26	20-Jul-26	Not Started	23
CON-5980	Install Auxiliary Signal System Components - 4th Floor	7	21-Jul-26	29-Jul-26	Not Started	23
CON-6050	Install Auxiliary Signal System Components - Lower Roof	7	30-Jul-26	07-Aug-26	Not Started	23
CON-5740	Install Intrusion Alarm System Components- Cellar Floor	7	30-Jun-26	09-Jul-26	Not Started	23
CON-5870	Install Intrusion Alarm System Components - 2nd Floor	7	10-Jul-26	20-Jul-26	Not Started	23

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-5990	Install Intrusion Alarm System Components - 3rd Floor	7	21-Jul-26	29-Jul-26	Not Started	23
CON-6060	Install Intrusion Alarm System Components - 4th Floor	7	30-Jul-26	07-Aug-26	Not Started	23
CON-6130	Install Intrusion Alarm System Components - Lower Roof	7	10-Aug-26	18-Aug-26	Not Started	23
CON-5880	Install IPDVS System Components - Cellar Floor	7	10-Jul-26	20-Jul-26	Not Started	23
CON-6000	Install IPDVS System Components - 2nd Floor	7	21-Jul-26	29-Jul-26	Not Started	23
CON-6070	Install IPDVS System Components - 3rd Floor	7	30-Jul-26	07-Aug-26	Not Started	23
CON-6140	Install IPDVS System Components - 4th Floor	7	10-Aug-26	18-Aug-26	Not Started	23
CON-6200	Install IPDVS System Components - Lower Roof	7	19-Aug-26	27-Aug-26	Not Started	23
CON-4880	Install First Coat Painting - 2nd Floor	7	08-May-26	18-May-26	Not Started	23
CON-5050	Install First Coat Painting - 3rd Floor	7	19-May-26	28-May-26	Not Started	23
CON-5190	Install First Coat Painting - 4th Floor	7	29-May-26	08-Jun-26	Not Started	23
CON-5390	Install First Coat Painting - Lower Roof	7	09-Jun-26	17-Jun-26	Not Started	23
CON-1390	Install Floor Drains - 1st Floor	2	19-Nov-25	20-Nov-25	Not Started	25
CON-1290	F/R/P Columns From First Level To Second Level - First Level Area	5	07-Oct-25	14-Oct-25	Not Started	26
CON-1410	Install MEP Hangers - 2nd Floor	2	26-Nov-25	28-Nov-25	Not Started	26
CON-5310	Install CMU - 1st Floor	3	09-Jun-26	11-Jun-26	Not Started	27
PER-1090	Review & Approve FDNY Fuel Permit	21	15-Apr-25	05-May-25	Not Started	27
PER-1070	Obtain Excavation Permit	15	01-Apr-25	21-Apr-25	Not Started	28
SUB-1280	Prepare & Submit Construction Indoor Air Quality Management Plan	81	02-Dec-24	28-Mar-25	Not Started	30
SUB-1300	Prepare & Submit CWM Plan	81	02-Dec-24	28-Mar-25	Not Started	30
SUB-1700	Prepare & Submit Environmental Site Assessment Reports	81	02-Dec-24	28-Mar-25	Not Started	30
CON-6010	Install Fire Alarm Devices- Cellar Floor	7	21-Jul-26	29-Jul-26	Not Started	31
CON-6080	Install Fire Alarm Devices - 2nd Floor	7	30-Jul-26	07-Aug-26	Not Started	31
CON-6150	Install Fire Alarm Devices - 3rd Floor	7	10-Aug-26	18-Aug-26	Not Started	31
CON-6210	Install Fire Alarm Devices - 4th Floor	7	19-Aug-26	27-Aug-26	Not Started	31
CON-6240	Install Fire Alarm Devices - Lower Roof	7	28-Aug-26	08-Sep-26	Not Started	31
CON-1120	Insulate Cellar Retaining Wall	5	28-Jul-25	01-Aug-25	Not Started	33
PER-1060	Obtain Builders Pavement Permit	10	01-Apr-25	14-Apr-25	Not Started	33
PER-1080	Obtain Permit to Enter (PTE)	10	01-Apr-25	14-Apr-25	Not Started	33
CON-1690	Layout - Cellar Floor	2	09-Jan-26	12-Jan-26	Not Started	34
CON-1760	Install Top & Bottom Tracks - Cellar Floor	2	13-Jan-26	14-Jan-26	Not Started	34
CON-1850	Rough-in Duct Work -VAV Devices & Diffusers - Cellar Floor	5	15-Jan-26	22-Jan-26	Not Started	34
CON-2930	F/R/P Concrete Pads - Fuel Tank Room	3	13-Feb-26	18-Feb-26	Not Started	34
CON-3040	Install Fuel Oil Transfer Pump (FP-1) - Fuel Tank Room	4	19-Feb-26	24-Feb-26	Not Started	34
CON-3300	Install Fuel Oil Filtration System (FFS-1) - Fuel Tank Room	4	25-Feb-26	02-Mar-26	Not Started	34
CON-3450	Install 275 GAL NYC Fuel Tank With 200% Secondary Containment	6	03-Mar-26	10-Mar-26	Not Started	34
CON-3820	Install Fuel Oil Pipings	3	11-Mar-26	13-Mar-26	Not Started	34
CON-3980	Install 55 GAL Spill Tank with Sensor Alarm	3	16-Mar-26	18-Mar-26	Not Started	34
CON-4100	Install Oil Leak Detector CAC	2	19-Mar-26	20-Mar-26	Not Started	34
CON-2160	Rough-in Power Conduits & Wires - Cellar Floor	5	23-Jan-26	29-Jan-26	Not Started	34
CON-2410	Rough-in Low Voltage Conduits & Wires - Cellar Floor	5	30-Jan-26	05-Feb-26	Not Started	34
CON-2710	Rough-in Plumbing Pipes- Cellar Floor	5	06-Feb-26	12-Feb-26	Not Started	34
CON-3210	Install Ceiling Hangers - Cellar Floor	5	23-Feb-26	27-Feb-26	Not Started	35
CON-1720	Rough-in Duct Risers - Cellar Floor	3	09-Jan-26	13-Jan-26	Not Started	35

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-2990	Rough-in Sprinkler Piping - Cellar Floor	5	13-Feb-26	20-Feb-26	Not Started	35
SUB-1730	Prepare & Submit Chain Link Fences & Gates Drawings	81	02-Dec-24	28-Mar-25	Not Started	35
SUB-1640	Prepare & Submit Underground Coordination Drawings	50	02-Dec-24	12-Feb-25	Not Started	37
SUB-1930	Prepare & Submit Final Underground Coordination Drawings	37	06-Mar-25	25-Apr-25	Not Started	38
PER-1040	Prepare & Submit Permit Waiver Requests to SCA Chief Project Officer	5	01-Apr-25	07-Apr-25	Not Started	38
CON-6090	Install Flooring - 1st Floor	7	03-Aug-26	11-Aug-26	Not Started	40
CON-6230	Install Final Coat Painting - 1st Floor	7	21-Aug-26	31-Aug-26	Not Started	40
CON-6170	Install Furniture - 1st Floor	7	12-Aug-26	20-Aug-26	Not Started	40
CON-6270	Install Signage - 1st Floor	3	01-Sep-26	03-Sep-26	Not Started	40
PER-1000	Obtain Construction Fences Permit	3	01-Apr-25	03-Apr-25	Not Started	40
PER-1010	Obtain CCD1	3	01-Apr-25	03-Apr-25	Not Started	40
PER-1020	Obtain Sidewalk Shed Permits	3	01-Apr-25	03-Apr-25	Not Started	40
APP-1510	Review & Approve Construction Indoor Air Quality Management Plan	21	29-Mar-25	18-Apr-25	Not Started	44
APP-1520	Review & Approve CWM Plan	21	29-Mar-25	18-Apr-25	Not Started	44
APP-1720	Review & Approve Environmental Site Assessment Reports	21	29-Mar-25	18-Apr-25	Not Started	44
CON-6110	Install Milling Work - 1st Floor	7	03-Aug-26	11-Aug-26	Not Started	47
CON-2100	Install Steel Studs - Cellar Floor	4	23-Jan-26	28-Jan-26	Not Started	49
CON-2360	Install Steel Studs - 2nd Floor	4	30-Jan-26	04-Feb-26	Not Started	51
CON-2130	Rough-in Duct Work -VAV Devices & Diffusers - 2nd Floor	5	23-Jan-26	29-Jan-26	Not Started	51
APP-1740	Review & Approve Chain Link Fences & Gates Drawings	21	29-Mar-25	18-Apr-25	Not Started	51
CON-2670	Install Steel Studs - 3rd Floor	4	06-Feb-26	11-Feb-26	Not Started	53
CON-2390	Rough-in Duct Work -VAV Devices & Diffusers - 3rd Floor	5	30-Jan-26	05-Feb-26	Not Started	53
CON-4720	Install Electric Wall Convectors - 2nd Floor	3	29-Apr-26	01-May-26	Not Started	53
CON-4770	Install Electric Wall Convectors - 3rd Floor	3	04-May-26	06-May-26	Not Started	53
CON-4810	Install Electric Wall Convectors - 4th Floor	3	07-May-26	11-May-26	Not Started	53
CON-4930	Install Electric Wall Convectors - 1st Floor	3	12-May-26	14-May-26	Not Started	53
CON-2720	Install Electrical Panels - Cellar Floor	5	06-Feb-26	12-Feb-26	Not Started	53
CON-2980	Install Electrical Panels - 2nd Floor	5	13-Feb-26	20-Feb-26	Not Started	53
CON-3260	Install Electrical Panels - 3rd Floor	5	23-Feb-26	27-Feb-26	Not Started	53
CON-3420	Install Electrical Panels - 4th Floor	5	02-Mar-26	06-Mar-26	Not Started	53
CON-3710	Install Electrical Panels - Lower Roof	5	09-Mar-26	13-Mar-26	Not Started	53
CON-4000	Install Electrical Panels - 1st Floor	5	16-Mar-26	20-Mar-26	Not Started	53
CON-1750	Layout - 2nd Floor	2	13-Jan-26	14-Jan-26	Not Started	54
CON-1840	Install Top & Bottom Tracks - 2nd Floor	2	15-Jan-26	16-Jan-26	Not Started	54
APP-1200	Review & Approve Underground Coordination Drawings	21	13-Feb-25	05-Mar-25	Not Started	54
CON-2900	Install Steel Studs - 4th Floor	4	13-Feb-26	19-Feb-26	Not Started	55
CON-2680	Rough-in Duct Work -VAV Devices & Diffusers - 4th Floor	5	06-Feb-26	12-Feb-26	Not Started	55
SUB-1160	Prepare & Submit Certification of Material	81	02-Dec-24	28-Mar-25	Not Started	55
CON-3200	Install Steel Studs - Lower Roof	4	23-Feb-26	26-Feb-26	Not Started	57
CON-2920	Rough-in Duct Work -VAV Devices & Diffusers - Lower Roof	5	13-Feb-26	20-Feb-26	Not Started	57
SUB-1510	Prepare & Submit Baseline Schedule	52	02-Dec-24	14-Feb-25	Not Started	59
CON-3380	Install Ceiling Hangers - 2nd Floor	5	02-Mar-26	06-Mar-26	Not Started	60
CON-4910	Install Doors- 1st Floor	3	29-Jun-26	01-Jul-26	Not Started	61
CON-3680	Install Ceiling Hangers - 3rd Floor	5	09-Mar-26	13-Mar-26	Not Started	62
CON-5110	Install Flooring - 3rd Floor	7	29-May-26	08-Jun-26	Not Started	63

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-5320	Install Flooring - 4th Floor	7	09-Jun-26	17-Jun-26	Not Started	63
CON-5520	Install Flooring - Lower Roof	7	18-Jun-26	29-Jun-26	Not Started	63
CON-3270	Rough-in Sprinkler Piping - 2nd Floor	5	23-Feb-26	27-Feb-26	Not Started	63
CON-5200	Install Final Coat Painting - Cellar Floor	7	29-May-26	08-Jun-26	Not Started	63
CON-5400	Install Final Coat Painting - 2nd Floor	7	09-Jun-26	17-Jun-26	Not Started	63
CON-5600	Install Final Coat Painting - 3rd Floor	7	18-Jun-26	29-Jun-26	Not Started	63
CON-5760	Install Final Coat Painting - 4th Floor	7	30-Jun-26	09-Jul-26	Not Started	63
CON-5900	Install Final Coat Painting - Lower Roof	7	10-Jul-26	20-Jul-26	Not Started	63
CON-5070	Install Furniture - Cellar Floor	7	19-May-26	28-May-26	Not Started	63
CON-5220	Install Furniture - 2nd Floor	7	29-May-26	08-Jun-26	Not Started	63
CON-5420	Install Furniture - 3rd Floor	7	09-Jun-26	17-Jun-26	Not Started	63
CON-5620	Install Furniture - 4th Floor	7	18-Jun-26	29-Jun-26	Not Started	63
CON-5770	Install Furniture - Lower Roof	7	30-Jun-26	09-Jul-26	Not Started	63
SUB-1960	Prepare & Submit Record Documents	81	13-Jul-26	04-Nov-26	Not Started	63
CON-1830	Layout - 3rd Floor	2	15-Jan-26	16-Jan-26	Not Started	64
CON-1890	Install Top & Bottom Tracks - 3rd Floor	2	20-Jan-26	21-Jan-26	Not Started	64
CON-3970	Install Ceiling Hangers - 4th Floor	5	16-Mar-26	20-Mar-26	Not Started	64
CON-4200	Install Ceiling Hangers - Lower Roof	5	23-Mar-26	27-Mar-26	Not Started	66
SUB-1290	Prepare & Submit Site Safety Plan	2	02-Dec-24	03-Dec-24	Not Started	67
CON-2400	Rough-in Power Conduits & Wires - 2nd Floor	5	30-Jan-26	05-Feb-26	Not Started	68
CON-2690	Rough-in Power Conduits & Wires - 3rd Floor	5	06-Feb-26	12-Feb-26	Not Started	68
CON-2940	Rough-in Power Conduits & Wires - 4th Floor	5	13-Feb-26	20-Feb-26	Not Started	68
CON-3230	Rough-in Power Conduits & Wires - Lower Roof	5	23-Feb-26	27-Feb-26	Not Started	68
CON-2700	Rough-in Low Voltage Conduits & Wires - 2nd Floor	5	06-Feb-26	12-Feb-26	Not Started	68
CON-2950	Rough-in Low Voltage Conduits & Wires - 3rd Floor	5	13-Feb-26	20-Feb-26	Not Started	68
CON-3240	Rough-in Low Voltage Conduits & Wires - 4th Floor	5	23-Feb-26	27-Feb-26	Not Started	68
CON-3390	Rough-in Low Voltage Conduits & Wires - Lower Roof	5	02-Mar-26	06-Mar-26	Not Started	68
CON-2970	Rough-in Plumbing Pipes - 2nd Floor	5	13-Feb-26	20-Feb-26	Not Started	68
CON-3250	Rough-in Plumbing Pipes - 3rd Floor	5	23-Feb-26	27-Feb-26	Not Started	68
CON-3410	Rough-in Plumbing Pipes - 4th Floor	5	02-Mar-26	06-Mar-26	Not Started	68
CON-3700	Rough-in Plumbing Pipes - Lower Roof	5	09-Mar-26	13-Mar-26	Not Started	68
CON-3430	Rough-in Sprinkler Piping - 3rd Floor	5	02-Mar-26	06-Mar-26	Not Started	68
CON-3720	Rough-in Sprinkler Piping - 4th Floor	5	09-Mar-26	13-Mar-26	Not Started	68
CON-4010	Rough-in Sprinkler Piping - Lower Roof	5	16-Mar-26	20-Mar-26	Not Started	68
CON-1880	Layout - 4th Floor	2	20-Jan-26	21-Jan-26	Not Started	69
CON-2020	Install Top & Bottom Tracks - 4th Floor	2	22-Jan-26	23-Jan-26	Not Started	69
CON-5630	Install Gym Flooring	10	18-Jun-26	02-Jul-26	Not Started	69
CON-5800	Install Gym Equipment	15	06-Jul-26	24-Jul-26	Not Started	69
CON-4890	Install Milling Work - Cellar Floor	7	08-May-26	18-May-26	Not Started	70
CON-5060	Install Milling Work - 2nd Floor	7	19-May-26	28-May-26	Not Started	70
CON-5210	Install Milling Work - 3rd Floor	7	29-May-26	08-Jun-26	Not Started	70
CON-5410	Install Milling Work - 4th Floor	7	09-Jun-26	17-Jun-26	Not Started	70
CON-5610	Install Milling Work - Lower Roof	7	18-Jun-26	29-Jun-26	Not Started	70
CON-4120	Install Sprinkler Heads - Lower Roof	2	19-Mar-26	20-Mar-26	Not Started	71
SUB-1260	Prepare & Submit Gas Vapor Barrier Submittal & Inspection Schedule	81	02-Dec-24	28-Mar-25	Not Started	71
CON-5040	Install Plumbing Fixtures - Cellar Floor	7	19-May-26	28-May-26	Not Started	73
CON-5180	Install Plumbing Fixtures - 2nd Floor	7	29-May-26	08-Jun-26	Not Started	73
CON-5380	Install Plumbing Fixtures - 3rd Floor	7	09-Jun-26	17-Jun-26	Not Started	73

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-5590	Install Plumbing Fixtures - 4th Floor	7	18-Jun-26	29-Jun-26	Not Started	73
CON-5750	Install Plumbing Fixtures - Lower Roof	7	30-Jun-26	09-Jul-26	Not Started	73
CON-5890	Install Plumbing Fixtures - 1st Floor	7	10-Jul-26	20-Jul-26	Not Started	73
CON-2010	Layout - Lower Roof	2	22-Jan-26	23-Jan-26	Not Started	74
CON-2200	Install Top & Bottom Tracks - Lower Roof	2	26-Jan-26	27-Jan-26	Not Started	74
CON-3900	Install Sprinkler Heads - 4th Floor	2	12-Mar-26	13-Mar-26	Not Started	74
CON-5670	Install Hot Water Circulator Pump (CP-1) / (CP-2)	4	29-Jun-26	02-Jul-26	Not Started	75
CON-5790	Install Grease Interceptor (GI-1) / (GI-2)	4	06-Jul-26	09-Jul-26	Not Started	75
CON-5830	Install Kitchen Equipment	7	10-Jul-26	20-Jul-26	Not Started	75
CON-3510	Install Sprinkler Heads - 3rd Floor	2	05-Mar-26	06-Mar-26	Not Started	77
CON-6180	Electrical Testing and Commissioning	5	12-Aug-26	16-Aug-26	Not Started	78
CON-1480	Install Elevator Hoist Pad	3	11-Dec-25	15-Dec-25	Not Started	79
CON-1500	Erect Material Hoist	2	16-Dec-25	17-Dec-25	Not Started	79
CON-1530	Drop Test & Sign-Off	2	18-Dec-25	19-Dec-25	Not Started	79
CON-3330	Install Sprinkler Heads - 2nd Floor	2	26-Feb-26	27-Feb-26	Not Started	80
APP-1440	Review & Approve Certification of Material	21	29-Mar-25	18-Apr-25	Not Started	80
SUB-1470	Prepare & Submit QCP	30	02-Dec-24	14-Jan-25	Not Started	81
CON-2380	Install AC-204 - 2nd Floor	3	30-Jan-26	03-Feb-26	Not Started	82
CON-5460	Install Heat Pump Unit (HP-R02) - Roof	4	11-Jun-26	16-Jun-26	Not Started	82
CON-5250	Install Heat Pump Unit (HP-108 B) - 1st Floor	4	05-Jun-26	10-Jun-26	Not Started	82
CON-5130	Rough-in Refrigerant Piping - 1st Floor	5	29-May-26	04-Jun-26	Not Started	82
CON-4680	Install Doors- 3rd Floor	3	28-Apr-26	30-Apr-26	Not Started	82
CON-3120	Install Sprinkler Heads - Cellar Floor	2	19-Feb-26	20-Feb-26	Not Started	83
CON-5430	Install Signage- Cellar Floor	3	09-Jun-26	11-Jun-26	Not Started	83
CON-5480	Install Signage - 2nd Floor	3	12-Jun-26	16-Jun-26	Not Started	83
CON-5510	Install Signage - 3rd Floor	3	17-Jun-26	22-Jun-26	Not Started	83
CON-5650	Install Signage - 4th Floor	3	23-Jun-26	25-Jun-26	Not Started	83
CON-5660	Install Signage - Lower Roof	3	26-Jun-26	30-Jun-26	Not Started	83
CON-2110	Install AC-C17.1 - Cellar	3	23-Jan-26	27-Jan-26	Not Started	84
CON-2120	Install AC-C17.2 - Cellar	3	23-Jan-26	27-Jan-26	Not Started	84
CON-5260	Install Electrical Heat Air Curtain - 1st Floor	2	05-Jun-26	08-Jun-26	Not Started	84
CON-5280	Install Electric Unit Heater - 1st Floor	2	05-Jun-26	08-Jun-26	Not Started	84
CON-2910	Install AC-412 - 4th Floor	3	13-Feb-26	18-Feb-26	Not Started	86
CON-4750	Install Doors- 4th Floor	3	01-May-26	05-May-26	Not Started	86
APP-1210	Review & Approve Baseline Schedule	21	15-Feb-25	07-Mar-25	Not Started	86
CON-5010	Install Electric Cabinet Heaters - Cellar Floor	3	19-May-26	21-May-26	Not Started	87
CON-5080	Install Electric Cabinet Heaters - 2nd Floor	3	22-May-26	27-May-26	Not Started	87
CON-5090	Install Electric Cabinet Heaters - 3rd Floor	3	28-May-26	01-Jun-26	Not Started	87
CON-5230	Install Electric Cabinet Heaters - 4th Floor	3	02-Jun-26	04-Jun-26	Not Started	87
CON-5270	Install Electric Cabinet Heaters - Lower Roof	3	05-Jun-26	09-Jun-26	Not Started	87
CON-5440	Install Electric Cabinet Heaters - Upper Roof	3	10-Jun-26	12-Jun-26	Not Started	87
CON-5490	Install Electric Cabinet Heaters - 1st Roof	3	15-Jun-26	17-Jun-26	Not Started	87
CON-1810	Rough-in Electrical Risers (Power & Low Voltage) - Cellar Floor	3	14-Jan-26	16-Jan-26	Not Started	88
CON-1910	Rough-in Electrical Risers (Power & Low Voltage) - 2nd Floor	3	20-Jan-26	22-Jan-26	Not Started	88
CON-2170	Rough-in Electrical Risers (Power & Low Voltage) - 3rd Floor	3	23-Jan-26	27-Jan-26	Not Started	88
CON-2270	Rough-in Electrical Risers (Power & Low Voltage) - 4th Floor	3	28-Jan-26	30-Jan-26	Not Started	88
CON-2470	Rough-in Electrical Risers (Power & Low Voltage) - Lower Roof	3	02-Feb-26	04-Feb-26	Not Started	88
CON-2600	Rough-in Electrical Risers (Power & Low	3	05-Feb-26	09-Feb-26	Not Started	88

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
	voltage) - 1st Floor					
CON-1920	Rough-in Plumbing Risers - Cellar Floor	3	20-Jan-26	22-Jan-26	Not Started	88
CON-2180	Rough-in Plumbing Risers - 2nd Floor	3	23-Jan-26	27-Jan-26	Not Started	88
CON-2280	Rough-in Plumbing Risers - 3rd Floor	3	28-Jan-26	30-Jan-26	Not Started	88
CON-2480	Rough-in Plumbing Risers - 4th Floor	3	02-Feb-26	04-Feb-26	Not Started	88
CON-2630	Rough-in Plumbing Risers - Lower Roof	3	05-Feb-26	09-Feb-26	Not Started	88
CON-2780	Rough-in Plumbing Risers - 1st Floor	3	10-Feb-26	12-Feb-26	Not Started	88
CON-1820	Rough-in SSDS Risers - Cellar Floor	3	14-Jan-26	16-Jan-26	Not Started	88
CON-1930	Rough-in SSDS Risers - 2nd Floor	3	20-Jan-26	22-Jan-26	Not Started	88
CON-2190	Rough-in SSDS Risers - 3rd Floor	3	23-Jan-26	27-Jan-26	Not Started	88
CON-2290	Rough-in SSDS Risers - 4th Floor	3	28-Jan-26	30-Jan-26	Not Started	88
CON-2490	Rough-in SSDS Risers - Lower Roof	3	02-Feb-26	04-Feb-26	Not Started	88
CON-2640	Rough-in SSDS Risers - 1st Floor	3	05-Feb-26	09-Feb-26	Not Started	88
CON-1200	Install Floor Drains - Cellar Floor	2	15-Aug-25	18-Aug-25	Not Started	88
CON-2960	Install Main Ground Bus	3	13-Feb-26	18-Feb-26	Not Started	89
CON-3110	Install Sprinkler Booster Pumps	4	19-Feb-26	24-Feb-26	Not Started	89
CON-3060	Install Sprinkler Booster Panel	3	19-Feb-26	23-Feb-26	Not Started	90
CON-3070	Install Jockey Pump	3	19-Feb-26	23-Feb-26	Not Started	90
CON-4800	Install Doors- Lower Roof	3	06-May-26	08-May-26	Not Started	90
SUB-1460	Prepare & Submit Erosion Control and Sedimentation Plan	7	02-Dec-24	10-Dec-24	Not Started	94
SUB-1760	Prepare & Submit Metal Deck Product Data	81	02-Dec-24	28-Mar-25	Not Started	95
APP-1930	Review & Approve Record Documents	21	05-Nov-26	25-Nov-26	Not Started	96
COR-1050	Coordination With CON-ED For Trasnformers Work	10	21-Nov-25	05-Dec-25	Not Started	96
CON-3580	Install The Transformer Vault	3	05-May-26	07-May-26	Not Started	98
CON-4480	Install Traffic Control Devices - 63rd Street	1	08-May-26	08-May-26	Not Started	98
CON-4500	Mill & Remove Existing Asphalt Pavement - 63rd Street	2	11-May-26	12-May-26	Not Started	98
CON-4570	Excavation For The Full Depth Asphalt Pavement Replacement - 63rd Street	2	13-May-26	14-May-26	Not Started	98
CON-4630	Install 6-IN Gravel - 63rd Street	2	15-May-26	18-May-26	Not Started	98
CON-4650	Sawcut & Apply Tack Coat - Before Concrete Base Course - 63rd Street	2	19-May-26	20-May-26	Not Started	98
CON-4670	Install 6-IN Concrete Base Course - 63rd Street	2	21-May-26	22-May-26	Not Started	98
CON-4740	Sawcut & Apply Tack Coat - Before Leveling Course - 63rd Street	2	26-May-26	27-May-26	Not Started	98
CON-4760	Install Leveling Course - 63rd Street	2	28-May-26	29-May-26	Not Started	98
CON-4790	Install 1.5-Inch Asphalt Binder Course - 63rd Street	2	01-Jun-26	02-Jun-26	Not Started	98
CON-4820	Install 1.5-Inch Thick Asphalt Surface Course - 63rd Street	2	03-Jun-26	04-Jun-26	Not Started	98
CON-4920	Install Pavement Markings - 63rd Street	2	05-Jun-26	08-Jun-26	Not Started	98
CON-4950	Remove Traffic Control Devices - 63rd Street	1	11-Jun-26	11-Jun-26	Not Started	98
CON-4940	Remove and Replace Existing Pedestrian Ramps -63rd Street	2	09-Jun-26	10-Jun-26	Not Started	98
APP-1000	Review & Approve Site Safety Plan	21	04-Dec-24	24-Dec-24	Not Started	99
SUB-1750	Prepare & Submit Structure Steel Drawings	81	02-Dec-24	28-Mar-25	Not Started	100
SUB-1200	Prepare & Submit Site Furnishings Shop Drawings	15	02-Dec-24	20-Dec-24	Not Started	101
SUB-1950	Review & Approve Gas Vapor Barrier Submittal & Inspection Schedule	21	29-Mar-25	18-Apr-25	Not Started	104
SUB-1170	Prepare & Submit Concrete Reinforcement	30	02-Dec-24	14-Jan-25	Not Started	106
CON-3520	Install Storm Inlet 1	1	06-Mar-26	06-Mar-26	Not Started	107
CON-3530	Install Storm Inlet 2	1	06-Mar-26	06-Mar-26	Not Started	107
CON-3540	Install 60 LF of 8-IN DIP [Storm Inlet 1 to Storm Inlet 2]	1	06-Mar-26	06-Mar-26	Not Started	107

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-3660	Install 33 LF of 8-IN DIP [Storm Inlet 2 to Catch Basin 2]	1	09-Mar-26	09-Mar-26	Not Started	107
CON-3670	Install Catch Basin 2	1	09-Mar-26	09-Mar-26	Not Started	107
CON-3730	Install Grit Champer-1	2	10-Mar-26	11-Mar-26	Not Started	107
CON-3740	Install 106 LF of 12-IN DIP [Catch Basin 2 to Grit Champer-1]	2	10-Mar-26	11-Mar-26	Not Started	107
CON-3920	Install Stormwater Retention System	3	13-Mar-26	17-Mar-26	Not Started	107
CON-3880	Install 3-LF of 12-IN DIP [Grit Champer-1 to Stormwater Retention System]	1	12-Mar-26	12-Mar-26	Not Started	107
CON-4030	Install 3-LF of 12-IN DIP [Stormwater Retention System to Overflow Storm Manhole-1]	1	18-Mar-26	18-Mar-26	Not Started	107
CON-4080	Install 43.8 LF of 6-IN DIP [Overflow Storm Manhole-1 to Existing 30-IN x 45IN Combined Sewer]	2	19-Mar-26	20-Mar-26	Not Started	107
CON-4040	Install Overflow Storm Manhole-1	1	18-Mar-26	18-Mar-26	Not Started	107
CON-4130	Connect Sewer System To The Existing Sewer Line	1	20-Mar-26	20-Mar-26	Not Started	107
CON-4170	Prepare & Compact Subgrade Layer	3	23-Mar-26	25-Mar-26	Not Started	107
CON-4240	Install 6-IN Thick Crushed Stone	5	26-Mar-26	01-Apr-26	Not Started	107
CON-4330	F/R/P Concrete Pavement	6	02-Apr-26	09-Apr-26	Not Started	107
CON-4450	Install Concrete Pavers	4	10-Apr-26	15-Apr-26	Not Started	107
CON-4550	Install Site Gates	3	16-Apr-26	20-Apr-26	Not Started	107
CON-3030	Install Terra Cotta Panel Rainscreen - West Elevation	6	18-Feb-26	25-Feb-26	Not Started	107
CON-3320	Paint Exterior Elevation @ Window Sections - West Elevation	2	26-Feb-26	27-Feb-26	Not Started	107
CON-3360	Scaffolding Removal Inspection & Sign-Off - West Elevation	2	02-Mar-26	03-Mar-26	Not Started	107
CON-3460	Dismantle Scaffolding - West Elevation	2	04-Mar-26	05-Mar-26	Not Started	107
CON-6330	Install Magnetic Induction Loop Wires at Cafete	5	21-Apr-26	27-Apr-26	Not Started	107
CON-6340	Install Cafeteria Flooring	10	28-Apr-26	11-May-26	Not Started	107
CON-6350	Install Cafeteria Assembly	15	12-May-26	02-Jun-26	Not Started	107
CON-2840	Install Metal Clip System - West Elevation	2	12-Feb-26	13-Feb-26	Not Started	108
SUB-1250	Prepare & Submit SSDS Geotextile	40	02-Dec-24	29-Jan-25	Not Started	108
CON-3860	Install Storm Manhole-2	1	12-Mar-26	12-Mar-26	Not Started	109
CON-3870	Install 9-LF of 12-IN DIP [Grit Champer-1 to Storm Manhole-2]	1	12-Mar-26	12-Mar-26	Not Started	109
CON-3910	Install 10-IN DIP Roof Leader	1	13-Mar-26	13-Mar-26	Not Started	109
CON-3930	Install Catch Basin 2	1	13-Mar-26	13-Mar-26	Not Started	109
CON-3140	Install Terra Cotta Panel Rainscreen -South Elevation	10	20-Feb-26	05-Mar-26	Not Started	110
CON-3600	Paint Exterior Elevation @ Window Sections -South Elevation	3	06-Mar-26	10-Mar-26	Not Started	110
CON-3790	Scaffolding Removal Inspection & Sign-Off -South Elevation	2	11-Mar-26	12-Mar-26	Not Started	110
CON-3940	Dismantle Scaffolding -South Elevation	3	13-Mar-26	17-Mar-26	Not Started	110
CON-2740	Install Terra Cotta Panel Rainscreen - East Elevation	6	09-Feb-26	17-Feb-26	Not Started	111
CON-3010	Paint Exterior Elevation @ Window Sections - East Elevation	2	18-Feb-26	19-Feb-26	Not Started	111
CON-3130	Scaffolding Removal Inspection & Sign-Off - East Elevation	2	20-Feb-26	23-Feb-26	Not Started	111
CON-3280	Dismantle Scaffolding - East Elevation	2	24-Feb-26	25-Feb-26	Not Started	111
CON-3830	Install 6 Sets of 4#500MCM IN 4" RGS Conduits & 3 Spare 4" RGS Conduits Encased In Concrete	3	08-May-26	12-May-26	Not Started	111
CON-3990	CON-ED to Insulate 6 Sets of 4#500MCM IN 4" RGS Conduits	3	13-May-26	15-May-26	Not Started	111
CON-4110	CON-ED to Connect The 6 Sets of 4#500MCM to The Customer End Box	2	18-May-26	19-May-26	Not Started	111
CON-3840	Install Aluminum Lighting Conductor	3	08-May-26	12-May-26	Not Started	111

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
SUB-1600	Prepare & Submit Roof Dunnage	81	02-Dec-24	28-Mar-25	Not Started	111
CON-2550	Install Metal Clip System - East Elevation	2	04-Feb-26	05-Feb-26	Not Started	112
CON-2850	Install Brick Veneer - West Elevation	2	12-Feb-26	13-Feb-26	Not Started	112
CON-3000	Install Graffiti Resistant Coating At Brick - West Elevation	2	17-Feb-26	18-Feb-26	Not Started	112
CON-2790	Install Terra Cotta Panel Rainscreen -North Elevation	10	11-Feb-26	25-Feb-26	Not Started	113
CON-3310	Paint Exterior Elevation @ Window Sections -North Elevation	3	26-Feb-26	02-Mar-26	Not Started	113
CON-3440	Scaffolding Removal Inspection & Sign-Off -North Elevation	2	03-Mar-26	04-Mar-26	Not Started	113
CON-3500	Dismantle Scaffolding -North Elevation	3	05-Mar-26	09-Mar-26	Not Started	113
CON-2810	Install Metal Clip System -South Elevation	2	12-Feb-26	13-Feb-26	Not Started	113
CON-1770	Install CMU - Cellar Floor	3	13-Jan-26	15-Jan-26	Not Started	114
CON-1870	Install CMU - 2nd Floor	3	16-Jan-26	21-Jan-26	Not Started	114
CON-2030	Install CMU - 3rd Floor	3	22-Jan-26	26-Jan-26	Not Started	114
CON-2230	Install CMU - 4th Floor	3	27-Jan-26	29-Jan-26	Not Started	114
CON-2370	Install CMU - Lower Roof	3	30-Jan-26	03-Feb-26	Not Started	114
CON-3590	Install Telecom Service Point of Entry	3	06-Mar-26	10-Mar-26	Not Started	115
CON-3780	Verizon To Provide Connection	5	11-Mar-26	17-Mar-26	Not Started	115
CON-4050	Install Traffic Control Devices - 14th Avenue	1	18-Mar-26	18-Mar-26	Not Started	115
CON-4090	Mill & Remove Existing Asphalt Pavement - 14th Avenue	2	19-Mar-26	20-Mar-26	Not Started	115
CON-4180	Excavation For The Full Depth Asphalt Pavement Replacement - 14th Avenue	2	23-Mar-26	24-Mar-26	Not Started	115
CON-4220	Install 6-IN Gravel - 14th Avenue	2	25-Mar-26	26-Mar-26	Not Started	115
CON-4260	Sawcut & Apply Tack Coat - Before Concrete Base Course - 14th Avenue	2	27-Mar-26	30-Mar-26	Not Started	115
CON-4270	Install 6-IN Concrete Base Course - 14th Avenue	2	27-Mar-26	30-Mar-26	Not Started	115
CON-4300	Sawcut & Apply Tack Coat - Before Leveling Course - 14th Avenue	2	31-Mar-26	01-Apr-26	Not Started	115
CON-4310	Install Leveling Course - 14th Avenue	2	31-Mar-26	01-Apr-26	Not Started	115
CON-4340	Install 1.5-Inch Asphalt Binder Course - 14th Avenue	2	02-Apr-26	03-Apr-26	Not Started	115
CON-4370	Install 1.5-Inch Thick Asphalt Surface Course - 14th Avenue	2	06-Apr-26	07-Apr-26	Not Started	115
CON-4400	Install Pavement Markings - 14th Avenue	2	08-Apr-26	09-Apr-26	Not Started	115
CON-4470	Remove Traffic Control Devices - 14th Avenue	1	14-Apr-26	14-Apr-26	Not Started	115
CON-4430	Remove and Replace Existing Pedestrian Ramps -14th Avenue	2	10-Apr-26	13-Apr-26	Not Started	115
SUB-1270	Prepare & Submit Existing Conditions Survey	10	02-Dec-24	13-Dec-24	Not Started	115
CON-2520	Install Metal Clip System -North Elevation	2	04-Feb-26	05-Feb-26	Not Started	116
CON-2560	Install Brick Veneer - East Elevation	2	04-Feb-26	05-Feb-26	Not Started	116
CON-2650	Install Graffiti Resistant Coating At Brick - East Elevation	2	06-Feb-26	09-Feb-26	Not Started	116
APP-1100	Review & Approve QCP	21	15-Jan-25	04-Feb-25	Not Started	117
CON-3550	Install Domestic Water Service Piping	3	06-Mar-26	10-Mar-26	Not Started	118
CON-3750	Connect Water Piping To The Existing Water Line	2	11-Mar-26	12-Mar-26	Not Started	118
CON-3560	Install Sewer Piping	3	06-Mar-26	10-Mar-26	Not Started	118
CON-3760	Connect Sewer Piping To The Existing Sewer Line	2	11-Mar-26	12-Mar-26	Not Started	118
CON-2820	Install Brick Veneer -South Elevation	3	12-Feb-26	17-Feb-26	Not Started	118
CON-3020	Install Graffiti Resistant Coating At Brick -South Elevation	2	18-Feb-26	19-Feb-26	Not Started	118
CON-3150	Install Wall Speakers -South Elevation	2	20-Feb-26	23-Feb-26	Not Started	118
CON-4660	Dismantle Hoist	5	27-Apr-26	01-May-26	Not Started	118
CON-4780	Demolish Hoist Pad	5	04-May-26	08-May-26	Not Started	118

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-4900	Hoist In-Fill	5	11-May-26	15-May-26	Not Started	118
SUB-1570	Prepare & Submit Windows	73	02-Dec-24	18-Mar-25	Not Started	118
SUB-1810	Prepare & Submit Stationary Metal Wall Louvers	73	02-Dec-24	18-Mar-25	Not Started	118
CON-3400	Install EMR Panel	4	02-Mar-26	05-Mar-26	Not Started	119
CON-3640	Install Elevator Machines	10	06-Mar-26	19-Mar-26	Not Started	119
CON-4150	Install Elevator Controls	6	20-Mar-26	27-Mar-26	Not Started	119
CON-4280	Install Elevator Cabinets	6	30-Mar-26	06-Apr-26	Not Started	119
CON-2530	Install Brick Veneer -North Elevation	3	04-Feb-26	06-Feb-26	Not Started	121
CON-2730	Install Graffiti Resistant Coating At Brick -North Elevation	2	09-Feb-26	10-Feb-26	Not Started	121
CON-2800	Install Exterior Wall Lights -North Elevation	2	11-Feb-26	12-Feb-26	Not Started	121
SUB-1370	Prepare & Submit Gypsum Board	81	02-Dec-24	28-Mar-25	Not Started	122
SUB-1130	Prepare & Submit Perimeter Foundation Insulation Product Data	81	02-Dec-24	28-Mar-25	Not Started	123
CON-4440	Install Acrylic Court Surfacing	4	10-Apr-26	15-Apr-26	Not Started	128
CON-4510	Install Tree Pit	3	16-Apr-26	20-Apr-26	Not Started	128
CON-4520	Install Elevated Movable Planter	3	21-Apr-26	23-Apr-26	Not Started	128
CON-4530	Install Flag Pole	3	24-Apr-26	28-Apr-26	Not Started	128
CON-4540	Install Backless Site Bench	3	29-Apr-26	01-May-26	Not Started	128
SUB-1330	Prepare & Submit Electrical Shop Drawings	81	02-Dec-24	28-Mar-25	Not Started	136
APP-1020	Review & Approve Erosion Control and Sedimentation Plan	21	11-Dec-24	31-Dec-24	Not Started	136
PRO-1120	Procure & Deliver Erosion Control and Sedimentation Devices	25	01-Jan-25	25-Jan-25	Not Started	136
CON-3570	Install Sanitary Piping	3	06-Mar-26	10-Mar-26	Not Started	138
CON-3770	Connect Sanitary Piping To The Existing Sanitary Line	2	11-Mar-26	12-Mar-26	Not Started	138
APP-1770	Review & Approve Metal Deck Product Data	21	29-Mar-25	18-Apr-25	Not Started	138
PRO-1580	Procure & Deliver Metal Deck	120	19-Apr-25	16-Aug-25	Not Started	138
COR-1060	CON-ED to Provide (1) 27KV Feeder To Transformer Vault	30	06-Dec-25	04-Jan-26	Not Started	142
COR-1070	CON-ED to Furnish & Deliver (1) New "V11-6 Transformer Vault	120	05-Jan-26	04-May-26	Not Started	142
CON-3610	Install Air Layer	3	06-Mar-26	10-Mar-26	Not Started	145
CON-3810	Install Mineral Water Retention Layer	5	11-Mar-26	17-Mar-26	Not Started	145
CON-4060	Install 18" Wide Filter Fabric Strip	3	18-Mar-26	20-Mar-26	Not Started	145
CON-4190	Install Extensive Growing Media	6	23-Mar-26	30-Mar-26	Not Started	145
CON-4320	Install Sedum Mat	7	31-Mar-26	08-Apr-26	Not Started	145
APP-1760	Review & Approve Structure Steel Drawings	21	29-Mar-25	18-Apr-25	Not Started	145
PRO-1590	Procure & Deliver Steel Columns	120	19-Apr-25	16-Aug-25	Not Started	145
CON-3170	Install Paver Pedestal System	5	20-Feb-26	26-Feb-26	Not Started	149
CON-3340	Install Concrete Pavers	7	27-Feb-26	09-Mar-26	Not Started	149
APP-1040	Review & Approve Site Furnishings Shop Drawings	21	21-Dec-24	10-Jan-25	Not Started	149
CON-2420	Install Service End Box	4	30-Jan-26	04-Feb-26	Not Started	150
CON-2610	Install Switch Boards (SWBD-1, SWBD-2, SWBD-3)	10	05-Feb-26	19-Feb-26	Not Started	150
CON-3190	Install Main Service Switch Board (MSS#1 & MSS#2)	8	20-Feb-26	03-Mar-26	Not Started	150
CON-3480	Install TAP Section	3	04-Mar-26	06-Mar-26	Not Started	150
CON-3690	Install Dry-Type Transformer	6	09-Mar-26	16-Mar-26	Not Started	150
CON-4020	Install 2 Current Transformers (C/T)	4	17-Mar-26	20-Mar-26	Not Started	150
CON-4210	Install Power and Lighting Panels	3	23-Mar-26	25-Mar-26	Not Started	150
SUB-1430	Prepare & Submit Furniture	81	02-Dec-24	28-Mar-25	Not Started	150
SUB-1840	Prepare & Submit Manufactured Wood Casework	81	02-Dec-24	28-Mar-25	Not Started	150

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-1790	Rough-in Refrigerant Piping - Cellar Floor	5	14-Jan-26	21-Jan-26	Not Started	151
CON-2040	Rough-in Refrigerant Piping - 2nd Floor	5	22-Jan-26	28-Jan-26	Not Started	151
CON-2330	Rough-in Refrigerant Piping - 3rd Floor	5	29-Jan-26	04-Feb-26	Not Started	151
CON-2590	Rough-in Refrigerant Piping - 4th Floor	5	05-Feb-26	11-Feb-26	Not Started	151
CON-2870	Rough-in Refrigerant Piping - Lower Roof	5	12-Feb-26	19-Feb-26	Not Started	151
CON-3890	Install Bacnet Data Enclosure	6	12-Mar-26	19-Mar-26	Not Started	151
CON-4140	Install Switch Boards (SWBD-4, SWBD-5)	4	20-Mar-26	25-Mar-26	Not Started	151
CON-4250	Install Secondary Transformer Disconnect Switch (MSWB-C)	5	26-Mar-26	01-Apr-26	Not Started	151
CON-3630	Install Power Panels	4	06-Mar-26	11-Mar-26	Not Started	151
CON-4350	Install Domestic Hot Water Heat Pump (HWHP-1 & HWHP-2)	4	02-Apr-26	07-Apr-26	Not Started	151
CON-4410	Install Storage Tank (ST-1)	6	08-Apr-26	15-Apr-26	Not Started	151
CON-4560	Install Thermal Expansion Tank (ET-1)	6	16-Apr-26	23-Apr-26	Not Started	151
SUB-1650	Prepare & Submit 1st Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25	Not Started	151
CON-3220	Install Electric Unit Heater - Lower Roof	2	23-Feb-26	24-Feb-26	Not Started	153
APP-1070	Review & Approve Concrete Reinforcement	21	15-Jan-25	04-Feb-25	Not Started	153
CON-3160	Install Air Layer	2	20-Feb-26	23-Feb-26	Not Started	154
CON-3290	Install Mineral Water Retention Layer	4	24-Feb-26	27-Feb-26	Not Started	154
CON-3370	Install 18" Wide Filter Fabric Strip	2	02-Mar-26	03-Mar-26	Not Started	154
CON-3470	Install Extensive Growing Media	5	04-Mar-26	10-Mar-26	Not Started	154
CON-3800	Install Sedum Mat	5	11-Mar-26	17-Mar-26	Not Started	154
CON-3620	Install Paver Pedestal System	6	06-Mar-26	13-Mar-26	Not Started	155
CON-3960	Install Concrete Pavers	8	16-Mar-26	25-Mar-26	Not Started	155
SUB-1660	Prepare & Submit 2nd Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25	Not Started	155
SUB-1670	Prepare & Submit 3rd Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25	Not Started	155
CON-2620	Install Fire Alarm Fused Disconnect Switch	3	05-Feb-26	09-Feb-26	Not Started	157
APP-1170	Review & Approve SSDS Geotextile	21	30-Jan-25	19-Feb-25	Not Started	158
CON-1800	Rough-in Duct Risers - 2nd Floor	3	14-Jan-26	16-Jan-26	Not Started	161
CON-1900	Rough-in Duct Risers - 3rd Floor	3	20-Jan-26	22-Jan-26	Not Started	161
CON-2150	Rough-in Duct Risers - 4th Floor	3	23-Jan-26	27-Jan-26	Not Started	161
CON-2260	Rough-in Duct Risers - Lower Roof	3	28-Jan-26	30-Jan-26	Not Started	161
CON-2460	Rough-in Duct Risers - 1st Floor	3	02-Feb-26	04-Feb-26	Not Started	161
PRO-1380	Procure & Deliver Roof Dunnage	100	19-Apr-25	27-Jul-25	Not Started	161
APP-1700	Review & Approve Roof Dunnage	21	29-Mar-25	18-Apr-25	Not Started	161
SUB-1110	Prepare & Submit Roof Drains & Clean Outs	81	02-Dec-24	28-Mar-25	Not Started	169
CON-3050	Install Domestic Water Booster Pump (DWBP-1)	5	19-Feb-26	25-Feb-26	Not Started	170
APP-1030	Review & Approve Existing Conditions Survey	21	14-Dec-24	03-Jan-25	Not Started	170
APP-1260	Review & Approve Windows	21	19-Mar-25	08-Apr-25	Not Started	170
PRO-1220	Procure & Deliver Windows	154	09-Apr-25	09-Sep-25	Not Started	170
APP-1270	Review & Approve Stationary Metal Wall Louvers	21	19-Mar-25	08-Apr-25	Not Started	170
CON-2140	Install Electric Unit Heater - Cellar Floor	2	23-Jan-26	26-Jan-26	Not Started	171
CON-3090	Install Domestic Cold Water Booster Pump (DWBP-1)	4	19-Feb-26	24-Feb-26	Not Started	171
CON-3100	Install Duplex Sewage Ejector Pump (SE-1)	4	19-Feb-26	24-Feb-26	Not Started	171
CON-4380	Elevators Testing and Commissioning	5	07-Apr-26	11-Apr-26	Not Started	171
CON-4460	Elevator DOB Inspection	5	12-Apr-26	16-Apr-26	Not Started	171
CON-4490	Elevator Equipment Use Permit	5	17-Apr-26	21-Apr-26	Not Started	171
CON-4620	Elevator Final Sign-off	5	22-Apr-26	26-Apr-26	Not Started	171
SUB-1680	Prepare & Submit 4th Floor MEP Coordination	75	02-Dec-24	20-Mar-25	Not Started	171

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
	Drawings					
SUB-1440	Prepare & Submit Mechanical Ducts	81	02-Dec-24	28-Mar-25	Not Started	172
SUB-1080	Prepare & Submit Door Hardware Submittal	81	02-Dec-24	28-Mar-25	Not Started	175
SUB-1100	Prepare & Submit Door & Frame Corners Samples	81	02-Dec-24	28-Mar-25	Not Started	175
CON-3080	Install Water Filter Devices	3	19-Feb-26	23-Feb-26	Not Started	178
SUB-1070	Prepare & Submit Ceramic Tiles Product Data	81	02-Dec-24	28-Mar-25	Not Started	178
SUB-1380	Prepare & Submit Floorings	81	02-Dec-24	28-Mar-25	Not Started	178
APP-1570	Review & Approve Gypsum Board	21	29-Mar-25	18-Apr-25	Not Started	178
PRO-1150	Procure & Deliver Gypsum Board	150	19-Apr-25	15-Sep-25	Not Started	178
APP-1410	Review & Approve Perimeter Foundation Insulation Product Data	21	29-Mar-25	18-Apr-25	Not Started	179
SUB-1690	Prepare & Submit 5th Floor MEP Coordination Drawings	75	02-Dec-24	20-Mar-25	Not Started	179
SUB-1780	Prepare & Submit Wood Flooring	81	02-Dec-24	28-Mar-25	Not Started	181
SUB-1090	Prepare & Submit Painting	81	02-Dec-24	28-Mar-25	Not Started	182
CON-1660	Install Emergency Generator - Lower Roof	10	07-Jan-26	21-Jan-26	Not Started	186
CON-2240	Obtain Emergency Generator Permit	5	26-Jan-26	30-Jan-26	Not Started	187
SUB-1520	Prepare & Submit Wood Doors	81	02-Dec-24	28-Mar-25	Not Started	188
CON-1970	Install RTU-1 - Upper Roof	6	21-Jan-26	28-Jan-26	Not Started	189
CON-1980	Install RTU-3 - Upper Roof	6	21-Jan-26	28-Jan-26	Not Started	189
CON-1990	Install RTU-4 - Upper Roof	6	21-Jan-26	28-Jan-26	Not Started	189
SUB-1180	Prepare & Submit Formwork Shop Drawings	81	02-Dec-24	28-Mar-25	Not Started	189
SUB-1390	Prepare & Submit Acosutical Ceiling Tiles	60	02-Dec-24	27-Feb-25	Not Started	189
CON-2000	Install Fans - Upper Roof	4	21-Jan-26	26-Jan-26	Not Started	191
SUB-1720	Prepare & Submit Foundation Shop Drawings	5	02-Dec-24	06-Dec-24	Not Started	191
CON-1640	Install RTU-2 - Lower Roof	6	07-Jan-26	14-Jan-26	Not Started	192
SUB-1140	Prepare & Submit Crystalline Waterproofing Product Data	81	02-Dec-24	28-Mar-25	Not Started	192
SUB-1150	Prepare & Submit Suspension Assembly Shop Drawings	81	02-Dec-24	28-Mar-25	Not Started	192
CON-1650	Install Fans - Lower Roof	4	07-Jan-26	12-Jan-26	Not Started	196
SUB-1490	Prepare & Submit Electrical Equipment, Conduits, and Cables	20	02-Dec-24	30-Dec-24	Not Started	197
APP-1550	Review & Approve Electrical Shop Drawings	21	29-Mar-25	18-Apr-25	Not Started	198
PRO-1260	Procure & Deliver Electrical Wires & Conduits	130	19-Apr-25	26-Aug-25	Not Started	198
SUB-1340	Prepare & Submit Plumbing Shop Drawings	81	02-Dec-24	28-Mar-25	Not Started	205
PRO-1600	Procure & Deliver Steel Framing	60	19-Apr-25	17-Jun-25	Not Started	205
SUB-1030	Prepare & Submit Floor Drains	40	02-Dec-24	29-Jan-25	Not Started	213
SUB-1770	Prepare & Submit Security Screens & Barriers	81	02-Dec-24	28-Mar-25	Not Started	214
SUB-1820	Prepare & Submit Platform Curtains & Auditorium Window Curtains	81	02-Dec-24	28-Mar-25	Not Started	214
APP-1610	Review & Approve Furniture	21	29-Mar-25	18-Apr-25	Not Started	218
PRO-1010	Procure & Deliver Furnitures	130	19-Apr-25	26-Aug-25	Not Started	218
APP-1840	Review & Approve Manufactured Wood Casework	21	29-Mar-25	18-Apr-25	Not Started	218
SUB-1320	Prepare & Submit Sample Classroom Materials	81	02-Dec-24	28-Mar-25	Not Started	219
SUB-1040	Prepare & Submit Hangers & Supports	40	02-Dec-24	29-Jan-25	Not Started	220
APP-1280	Review & Approve 1st Floor Coordination Drawings	21	21-Mar-25	10-Apr-25	Not Started	220
APP-1290	Review & Approve 2nd Floor Coordination Drawings	21	21-Mar-25	10-Apr-25	Not Started	224
APP-1300	Review & Approve 3rd Floor Coordination Drawings	21	21-Mar-25	10-Apr-25	Not Started	224
SUB-1350	Prepare & Submit Concrete Shop Drawings	30	02-Dec-24	14-Jan-25	Not Started	240
SUB-1480	Prepare & Submit Concrete Mix Design	30	02-Dec-24	14-Jan-25	Not Started	240
SUB-1880	Prepare & Submit Pumping Apparatus & Tanks	81	02-Dec-24	28-Mar-25	Not Started	241

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
SUB-1630	Prepare & Submit Gymnasium Equipment	81	02-Dec-24	28-Mar-25	Not Started	247
SUB-1050	Prepare & Submit Fire & Jockey Pumps	81	02-Dec-24	28-Mar-25	Not Started	248
APP-1390	Review & Approve Roof Drains & Clean Outs	21	29-Mar-25	18-Apr-25	Not Started	248
SUB-1530	Prepare & Submit Fire Protection Shop Drawings	81	02-Dec-24	28-Mar-25	Not Started	248
APP-1310	Review & Approve 4th Floor Coordination Drawings	21	21-Mar-25	10-Apr-25	Not Started	249
APP-1620	Review & Approve Mechanical Ducts	21	29-Mar-25	18-Apr-25	Not Started	251
PRO-1030	Procure & Deliver Mechanical Ducts	70	19-Apr-25	27-Jun-25	Not Started	251
SUB-1940	Review & Approve Door Hardware Submittal	21	29-Mar-25	18-Apr-25	Not Started	256
PRO-1410	Procure & Deliver Door Frames	70	19-Apr-25	27-Jun-25	Not Started	256
APP-1380	Review & Approve Door & Frame Corners Samples	21	29-Mar-25	18-Apr-25	Not Started	256
SUB-1550	Prepare & Submit Kitchen Equipment	81	02-Dec-24	28-Mar-25	Not Started	257
SUB-1830	Prepare & Submit Domestic Equipment	81	02-Dec-24	28-Mar-25	Not Started	257
APP-1350	Review & Approve Ceramic Tiles Product Data	21	29-Mar-25	18-Apr-25	Not Started	260
APP-1580	Review & Approve Floorings	21	29-Mar-25	18-Apr-25	Not Started	260
PRO-1160	Procure & Deliver Floorings	80	19-Apr-25	07-Jul-25	Not Started	260
APP-1320	Review & Approve 5th Floor Coordination Drawings	21	21-Mar-25	10-Apr-25	Not Started	262
APP-1790	Review & Approve Wood Flooring	21	29-Mar-25	18-Apr-25	Not Started	264
PRO-1630	Procure & Deliver Wood Flooring	120	19-Apr-25	16-Aug-25	Not Started	264
PRO-1420	Procure & Deliver Painting	70	19-Apr-25	27-Jun-25	Not Started	265
APP-1370	Review & Approve Painting	21	29-Mar-25	18-Apr-25	Not Started	265
SUB-1360	Prepare & Submit Elevator Machine	50	02-Dec-24	12-Feb-25	Not Started	265
CON-2050	Emergency Generator Electric Load Test	3	22-Jan-26	24-Jan-26	Not Started	270
CON-2500	Emergency Generator Final Sign-off	0		30-Jan-26	Not Started	271
SUB-1900	Prepare & Submit Unit Heaters/Cabinet Heaters Equipment	81	02-Dec-24	28-Mar-25	Not Started	271
CON-2340	HVAC System Testing and Commissioning	5	29-Jan-26	02-Feb-26	Not Started	273
SUB-1400	Prepare & Submit Toilet Accessories	81	02-Dec-24	28-Mar-25	Not Started	274
SUB-1500	Prepare & Submit Plumbing Fixtures	81	02-Dec-24	28-Mar-25	Not Started	274
APP-1230	Review & Approve Acosutical Ceiling Tiles	21	28-Feb-25	20-Mar-25	Not Started	275
PRO-1170	Procure & Deliver Acosutical Ceiling Tiles	120	21-Mar-25	18-Jul-25	Not Started	275
PRO-1050	Procure & Deliver Electrical Equipment	130	19-Apr-25	26-Aug-25	Not Started	275
APP-1640	Review & Approve Wood Doors	21	29-Mar-25	18-Apr-25	Not Started	276
PRO-1070	Procure & Deliver Doors	50	19-Apr-25	07-Jun-25	Not Started	276
APP-1450	Review & Approve Formwork Shop Drawings	21	29-Mar-25	18-Apr-25	Not Started	277
APP-1010	Review & Approve Foundation Shop Drawings	21	07-Dec-24	27-Dec-24	Not Started	279
APP-1420	Review & Approve Crystalline Waterproofing Product Data	21	29-Mar-25	18-Apr-25	Not Started	283
APP-1430	Review & Approve Suspension Assembly Shop Drawings	21	29-Mar-25	18-Apr-25	Not Started	283
APP-1050	Review & Approve Electrical Equipment, Conduits, and Cables	21	31-Dec-24	20-Jan-25	Not Started	286
SUB-1580	Prepare & Submit Telecommunication System Drawings	81	02-Dec-24	28-Mar-25	Not Started	287
SUB-1620	Prepare & Submit Unit Cabinet Heaters	60	02-Dec-24	27-Feb-25	Not Started	292
SUB-1850	Prepare & Submit Hydraulic Vertical Wheelchair Lifts	81	02-Dec-24	28-Mar-25	Not Started	292
SUB-1420	Prepare & Submit Lighting Fixtures	30	02-Dec-24	14-Jan-25	Not Started	295
SUB-1740	Prepare & Submit Unit Masonry Product Data	81	02-Dec-24	28-Mar-25	Not Started	297
SUB-1800	Prepare & Submit Fire Extinguishers & Cabinets	81	02-Dec-24	28-Mar-25	Not Started	298
APP-1560	Review & Approve Plumbing Shop Drawings	21	29-Mar-25	18-Apr-25	Not Started	301
PRO-1290	Procure & Deliver Plumbing Pumps	250	19-Apr-25	24-Dec-25	Not Started	301
SUB-1540	Prepare & Submit Fire Detectors & Alarms	81	02-Dec-24	28-Mar-25	Not Started	303

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
SUB-1910	Prepare & Submit Temperature Control System	81	02-Dec-24	28-Mar-25	Not Started	307
SUB-1450	Prepare & Submit Mechanical Piping	60	02-Dec-24	27-Feb-25	Not Started	308
SUB-1790	Prepare & Submit Visual Display Boards	81	02-Dec-24	28-Mar-25	Not Started	308
APP-1150	Review & Approve Floor Drains	21	30-Jan-25	19-Feb-25	Not Started	309
SUB-1120	Prepare & Submit Flashing & Sheet Metal Shop Drawing	81	02-Dec-24	28-Mar-25	Not Started	310
APP-1780	Review & Approve Security Screens & Barriers	21	29-Mar-25	18-Apr-25	Not Started	314
APP-1820	Review & Approve Platform Curtains & Auditorium Window Curtains	21	29-Mar-25	18-Apr-25	Not Started	314
SUB-1060	Prepare & Submit Interior Signage Shop Drawings	81	02-Dec-24	28-Mar-25	Not Started	318
SUB-1560	Prepare & Submit Signs	81	02-Dec-24	28-Mar-25	Not Started	318
APP-1160	Review & Approve Hangers & Supports	21	30-Jan-25	19-Feb-25	Not Started	320
SUB-1590	Prepare & Submit Internet Protocol Digital Video Surveillance System using Digital Cameras	50	02-Dec-24	12-Feb-25	Not Started	320
APP-1540	Review & Approve Sample Classroom Materials	21	29-Mar-25	18-Apr-25	Not Started	321
SUB-1920	Prepare & Submit Air Outlets & Inlets	81	02-Dec-24	28-Mar-25	Not Started	325
SUB-1220	Prepare & Submit Catch Basin Shop Drawings	81	02-Dec-24	28-Mar-25	Not Started	326
SUB-1210	Prepare & Submit Ductile Iron Pipes	37	02-Dec-24	24-Jan-25	Not Started	331
SUB-1410	Prepare & Submit Millwork	81	02-Dec-24	28-Mar-25	Not Started	333
SUB-1020	Prepare & Submit Pressure Gages	40	02-Dec-24	29-Jan-25	Not Started	334
SUB-1860	Prepare & Submit Switch & Panel Boards	81	02-Dec-24	28-Mar-25	Not Started	349
APP-1080	Review & Approve Concrete Shop Drawings	21	15-Jan-25	04-Feb-25	Not Started	350
APP-1110	Review & Approve Concrete Mix Design	21	15-Jan-25	04-Feb-25	Not Started	350
SUB-1240	Prepare & Submit Asphaltic Concrete Paving	81	02-Dec-24	28-Mar-25	Not Started	353
APP-1880	Review & Approve Pumping Apparatus & Tanks	21	29-Mar-25	18-Apr-25	Not Started	354
SUB-1310	Prepare & Submit Heating Plan	81	02-Dec-24	28-Mar-25	Not Started	358
SUB-1230	Prepare & Submit Steel Curb Facing Shop Drawing	81	02-Dec-24	28-Mar-25	Not Started	359
APP-1710	Review & Approve Gymnasium Equipment	21	29-Mar-25	18-Apr-25	Not Started	362
PRO-1560	Procure & Deliver Gymnasium Equipment	180	19-Apr-25	15-Oct-25	Not Started	362
APP-1330	Review & Approve Fire & Jockey Pumps	21	29-Mar-25	18-Apr-25	Not Started	363
APP-1650	Review & Approve Fire Protection Shop Drawings	21	29-Mar-25	18-Apr-25	Not Started	363
PRO-1280	Procure & Deliver Fire Protection Pumps	70	19-Apr-25	27-Jun-25	Not Started	363
SUB-1890	Prepare & Submit Emergency Generator System Accessories	81	02-Dec-24	28-Mar-25	Not Started	364
APP-1670	Review & Approve Kitchen Equipment	21	29-Mar-25	18-Apr-25	Not Started	376
PRO-1000	Procure & Deliver Kitchen Equipment	180	19-Apr-25	15-Oct-25	Not Started	376
APP-1830	Review & Approve Domestic Equipment	21	29-Mar-25	18-Apr-25	Not Started	376
SUB-1870	Prepare & Submit Overcurrent Protective Devices Data	81	02-Dec-24	28-Mar-25	Not Started	376
SUB-1710	Prepare & Submit Selective Removals & Demoloition	81	02-Dec-24	28-Mar-25	Not Started	378
SUB-1190	Prepare & Submit Planting Schedule	81	02-Dec-24	28-Mar-25	Not Started	381
SUB-1000	Prepare & Submit Split Heat Pump System - SUB	60	02-Dec-24	27-Feb-25	Not Started	385
APP-1180	Review & Approve Elevator Machine	21	13-Feb-25	05-Mar-25	Not Started	387
PRO-1200	Procure & Deliver Elevator Machine	150	06-Mar-25	02-Aug-25	Not Started	387
PRO-1470	Procure & Deliver Cabinet Heaters	126	19-Apr-25	22-Aug-25	Not Started	396
APP-1900	Review & Approve Unit Heaters/Cabinet Heaters Equipment	21	29-Mar-25	18-Apr-25	Not Started	396
SUB-1010	Prepare & Submit Thermometers	40	02-Dec-24	29-Jan-25	Not Started	399
APP-1590	Review & Approve Toilet Accessories	21	29-Mar-25	18-Apr-25	Not Started	401
APP-1630	Review & Approve Plumbing Fixtures	21	29-Mar-25	18-Apr-25	Not Started	401

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
PRO-1190	Procure & Deliver Toilet Accessories	100	19-Apr-25	27-Jul-25	Not Started	401
PRO-1060	Procure & Deliver Plumbing Fixtures	100	19-Apr-25	27-Jul-25	Not Started	401
SUB-1610	Prepare & Submit Switch Gears Product Data	20	02-Dec-24	30-Dec-24	Not Started	410
APP-1690	Review & Approve Telecommunication System Drawings	21	29-Mar-25	18-Apr-25	Not Started	418
PRO-1310	Procure & Deliver Telecommunication System	60	19-Apr-25	17-Jun-25	Not Started	418
APP-1250	Review & Approve Unit Cabinet Heaters	21	28-Feb-25	20-Mar-25	Not Started	425
PRO-1530	Procure & Deliver Hydraulic Vertical Wheelchair Lift	90	19-Apr-25	17-Jul-25	Not Started	426
APP-1850	Review & Approve Hydraulic Vertical Wheelchair Lifts	21	29-Mar-25	18-Apr-25	Not Started	426
APP-1090	Review & Approve Lighting Fixtures	21	15-Jan-25	04-Feb-25	Not Started	431
PRO-1140	Procure & Deliver Lighting Fixtures	60	05-Feb-25	05-Apr-25	Not Started	431
PRO-1250	Procure & Deliver Plumbing Pipes	60	19-Apr-25	17-Jun-25	Not Started	432
APP-1750	Review & Approve Unit Masonry Product Data	21	29-Mar-25	18-Apr-25	Not Started	433
APP-1810	Review & Approve Fire Extinguishers & Cabinets	21	29-Mar-25	18-Apr-25	Not Started	436
APP-1660	Review & Approve Fire Detectors & Alarms	21	29-Mar-25	18-Apr-25	Not Started	441
PRO-1110	Procure & Deliver Fire Detectors & Alarms	60	19-Apr-25	17-Jun-25	Not Started	441
APP-1240	Review & Approve Mechanical Piping	21	28-Feb-25	20-Mar-25	Not Started	447
PRO-1020	Procure & Deliver Mechanical Piping	70	21-Mar-25	29-May-25	Not Started	447
APP-1910	Review & Approve Temperature Control System	21	29-Mar-25	18-Apr-25	Not Started	447
APP-1800	Review & Approve Visual Display Boards	21	29-Mar-25	18-Apr-25	Not Started	451
APP-1400	Review & Approve Flashing & Sheet Metal Shop Drawing	21	29-Mar-25	18-Apr-25	Not Started	453
PRO-1270	Procure & Deliver Mechanical Pumps	70	19-Apr-25	27-Jun-25	Not Started	461
PRO-1330	Procure & Deliver Cameras	60	06-Mar-25	04-May-25	Not Started	464
APP-1190	Review & Approve Internet Protocol Digital Video Surveillance System using Digital Cameras	21	13-Feb-25	05-Mar-25	Not Started	464
APP-1340	Review & Approve Interior Signage Shop Drawings	21	29-Mar-25	18-Apr-25	Not Started	466
APP-1680	Review & Approve Signs	21	29-Mar-25	18-Apr-25	Not Started	466
PRO-1210	Procure & Deliver Signs	70	19-Apr-25	27-Jun-25	Not Started	466
APP-1920	Review & Approve Air Outlets & Inlets	21	29-Mar-25	18-Apr-25	Not Started	475
APP-1470	Review & Approve Catch Basin Shop Drawings	21	29-Mar-25	18-Apr-25	Not Started	478
APP-1120	Review & Approve Ductile Iron Pipes	21	25-Jan-25	14-Feb-25	Not Started	481
APP-1140	Review & Approve Pressure Gages	21	30-Jan-25	19-Feb-25	Not Started	487
APP-1600	Review & Approve Millwork	21	29-Mar-25	18-Apr-25	Not Started	487
APP-1860	Review & Approve Switch & Panel Boards	21	29-Mar-25	18-Apr-25	Not Started	509
APP-1490	Review & Approve Asphaltic Concrete Paving	21	29-Mar-25	18-Apr-25	Not Started	515
APP-1530	Review & Approve Heating Plan	21	29-Mar-25	18-Apr-25	Not Started	522
APP-1480	Review & Approve Steel Curb Facing Shop Drawing	21	29-Mar-25	18-Apr-25	Not Started	523
APP-1890	Review & Approve Emergency Generator System Accessories	21	29-Mar-25	18-Apr-25	Not Started	531
APP-1870	Review & Approve Overcurrent Protective Devices Data	21	29-Mar-25	18-Apr-25	Not Started	549
APP-1730	Review & Approve Selective Removals & Demoloition	21	29-Mar-25	18-Apr-25	Not Started	551
APP-1460	Review & Approve Planting Schedule	21	29-Mar-25	18-Apr-25	Not Started	556
APP-1220	Review & Approve Split Heat Pump System - SUB	21	28-Feb-25	20-Mar-25	Not Started	560
APP-1130	Review & Approve Thermometers	21	30-Jan-25	19-Feb-25	Not Started	580
APP-1060	Review & Approve Switch Gears Product Data	21	31-Dec-24	20-Jan-25	Not Started	597

APPENDIX 9
– Schedule Log

Scheduling/Leveling Report - 2024-12-16 16:39:29 - PM.EXE
==========

Default Project.....IS82.BL00
Use scheduling options from.....IS82.BL00

Projects:
IS82.BL00.....IS
082K New Building Design No. 093937 - Baseline Schedule Rev 00

Scheduling/Leveling Settings:

General

Scheduling .....Yes
Leveling .....No
Ignore relationships to and from other projects .....No
Make open-ended activities critical .....No
Use Expected Finish Dates .....Yes
Schedule automatically when a change affects dates .....No
Level resources during scheduling .....No
Recalculate assignment costs after scheduling .....No
When scheduling progressed activities use .....Retained
Logic
Calculate start-to-start lag from .....Early Start
Define critical activities as .....Longest
Path
Compute Total Float As .....Finish
Float
Calculate float based on finish date of .....Each
project
Calendar for scheduling Relationship Lag .....Predecessor
Activity Calendar

Advanced

Calculate multiple float paths.....No

Statistics:

Projects.....1
Activities.....797
Not Started.....797
In Progress.....0
Completed.....0
Relationships.....1385
Activities with Constraint.....5
Project: IS82.BL00 Activity: MIL-1030 TCO
Project: IS82.BL00 Activity: MIL-1040
Substantial Completion

```
                Project:        IS82.BL00       Activity:       MIL-1050
Final Completion
                Project:        IS82.BL00       Activity:       MIL-1060        IDF
and MDF Rooms Ready
                Project:        IS82.BL00       Activity:       MIL-1070
IPDVS System Installed

Errors:
-------
Warnings:
---------
        Activities without predecessors.................................1
                Project:        IS82.BL00       Activity:       MIL-1000        NTP

        Activities without successors...................................1
                Project:        IS82.BL00       Activity:       MIL-1050
Final Completion

        Out-of-sequence activities.....................................0

        Activities with Actual Dates > Data Date.......................0

        Milestone Activities with invalid relationships.................0

        Finish milestone and predecessors have different calendars.......4
                Project:        IS82.BL00       Activity:       CON-2500
Emergency Generator Final Sign-off
                Project:        IS82.BL00       Activity:       MIL-1030        TCO
                Project:        IS82.BL00       Activity:       MIL-1040
Substantial Completion
                Project:        IS82.BL00       Activity:       MIL-1060        IDF
and MDF Rooms Ready

Scheduling/Leveling Results:
----------------------------
        # Projects Scheduled/Leveled...................................1
        # Activities Scheduled/Leveled.................................797
        # Relationships with other projects............................0
        Data Date.....................................................02-Dec-24
        Earliest Early Start Date.....................................02-Dec-24
        Latest Early Finish Date......................................29-Jun-27
Exceptions:
-----------
        Critical Activities...........................................100
                Project:        IS82.BL00       Activity:       CLO-1000
Pre-Final Clean-Out
                Project:        IS82.BL00       Activity:       CLO-1010
Pre-TCO Inspection
                Project:        IS82.BL00       Activity:       CLO-1020
Pre-TCO Punchlist
```

Project: IS82.BL00 Activity: CLO-1030
Pre-Final Clean-Out
Project: IS82.BL00 Activity: CLO-1040
Pre-Substantial Completion Inspection
Project: IS82.BL00 Activity: CLO-1050
Pre-Substantial Punchlist
Project: IS82.BL00 Activity: CLO-1060
Pre-Final Clean-Out
Project: IS82.BL00 Activity: CLO-1070
Pre-Final Completion Inspection
Project: IS82.BL00 Activity: CLO-1080
Pre-Final Punchlist
Project: IS82.BL00 Activity: CON-1000
Mobilization
Project: IS82.BL00 Activity: CON-1010
Install Site Fence
Project: IS82.BL00 Activity: CON-1030
Install Erosion Control Devices - Stage 1
Project: IS82.BL00 Activity: CON-1040
Remove Existing Asphalt Pavement and Subbase
Project: IS82.BL00 Activity: CON-1050
Install Remove Existing Concrete Pavement and Subbase
Project: IS82.BL00 Activity: CON-1060
Prepare Temporary Staging & Storage Area - Stage 1
Project: IS82.BL00 Activity: CON-1070
Survey and Verify All Underground Utilities
Project: IS82.BL00 Activity: CON-1080
Excavation
Project: IS82.BL00 Activity: CON-1090
F/R/P Cellar Wall Footings
Project: IS82.BL00 Activity: CON-1100
F/R/P Cellar Retaining Wall
Project: IS82.BL00 Activity: CON-1110
Install Non-Woven Geotextile Layer - Below Cellar
Project: IS82.BL00 Activity: CON-1130
Install Gas Permeable Aggregate Layer- Below Cellar
Project: IS82.BL00 Activity: CON-1140
Install 6" C.I Pipe - Below Cellar
Project: IS82.BL00 Activity: CON-1150
Install VI-20 Geomembrane Gas Permeable Aggregate Layer - Below Cellar
Project: IS82.BL00 Activity: CON-1160
Install 60 Dry Mils of Liquid Boot - Below Cellar
Project: IS82.BL00 Activity: CON-1170
Install Liquid Boot Ultrashield G-1000 - Below Cellar
Project: IS82.BL00 Activity: CON-1180
F/R/P Slab on Grade - Cellar
Project: IS82.BL00 Activity: CON-1190
F/R/P First Floor Slab - Cellar Side
Project: IS82.BL00 Activity: CON-1210
Install MEP Hangers - 1st Floor - Cellar Side

Project: IS82.BL00 Activity: CON-1220
Curing For The First Floor Slab
Project: IS82.BL00 Activity: CON-1240
Backfilling
Project: IS82.BL00 Activity: CON-1250
Install Construction Entrance - Stage 2
Project: IS82.BL00 Activity: CON-1260
Install Erosion Control Devices - Stage 2
Project: IS82.BL00 Activity: CON-1270
Prepare Temporary Staging & Storage Area - Stage 2
Project: IS82.BL00 Activity: CON-1280
F/R/P First Floor Foundation
Project: IS82.BL00 Activity: CON-1300
Insulate First Floor Foundations
Project: IS82.BL00 Activity: CON-1310
Backfilling
Project: IS82.BL00 Activity: CON-1320
Install Non-Woven Geotextile Layer - Below 1st Floor SOG
Project: IS82.BL00 Activity: CON-1330
Install Gas Permeable Aggregate Layer - Below 1st Floor SOG
Project: IS82.BL00 Activity: CON-1350
Install VI-20 Geomembrane Gas Permeable Aggregate Layer - Below 1st Floor SOG
Project: IS82.BL00 Activity: CON-1360
Install 60 Dry Mils of Liquid Boot - Below 1st Floor SOG
Project: IS82.BL00 Activity: CON-1370
Install Liquid Boot Ultrashield G-1000 - Below 1st Floor SOG
Project: IS82.BL00 Activity: CON-1380
F/R/P First Floor SOG
Project: IS82.BL00 Activity: CON-1400
F/R/P Concrete Slab - 2nd Floor
Project: IS82.BL00 Activity: CON-1430
F/R/P Columns & Shear Walls From Second Floor To Third Floor
Project: IS82.BL00 Activity: CON-1440
F/R/P Concrete Slab - 3rd Floor
Project: IS82.BL00 Activity: CON-1460
F/R/P Columns & Shear Walls From Third Floor To Fourth Floor
Project: IS82.BL00 Activity: CON-1490
F/R/P Concrete Slab - 4th Floor
Project: IS82.BL00 Activity: CON-1540
Install Mainroof Posts and Framing
Project: IS82.BL00 Activity: CON-1620
F/R/P Concrete Deck Slab - Upper Roof
Project: IS82.BL00 Activity: CON-1710
Install Dunnage Framing - Upper Roof
Project: IS82.BL00 Activity: CON-1960 Pour
Concrete Topping Slab
Project: IS82.BL00 Activity: CON-2220
Install Hot Fluid-Applied Rubberized Asphalt Fabric-Reinforced Roofing Membrane
Project: IS82.BL00 Activity: CON-2510
Install Fabric Reinforcing Sheet

Project: IS82.BL00 Activity: CON-2770
Install Protection Sheet and Roof Barrier
Project: IS82.BL00 Activity: CON-2890
Install 1/2" Drainage Panel
Project: IS82.BL00 Activity: CON-3180
Install 8" Roof Insulation (R-40 Min) Multi-Layered and Staggered
Project: IS82.BL00 Activity: CON-3350
Install Filter Fabric
Project: IS82.BL00 Activity: CON-3490
Upper Roofing Testing
Project: IS82.BL00 Activity: CON-3650
Install Walls GWB-Mockup Room
Project: IS82.BL00 Activity: CON-3850
Install Door Frames-Mockup Room
Project: IS82.BL00 Activity: CON-3950
Install Gypsum Board Ceiling -Mockup Room
Project: IS82.BL00 Activity: CON-4070
Install Doors & Hardware-Mockup Room
Project: IS82.BL00 Activity: CON-4160
Paint First coat -Mockup Room
Project: IS82.BL00 Activity: CON-4230
Flooring Finishes-Mockup Room
Project: IS82.BL00 Activity: CON-4290
Paint Second coat-Mockup Room
Project: IS82.BL00 Activity: CON-4360
Install Furniture & Signs -Mockup Room
Project: IS82.BL00 Activity: CON-4390
Mockup Room Inspection & Punchlist
Project: IS82.BL00 Activity: CON-4420
Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - Cellar Floor
Project: IS82.BL00 Activity: CON-4580
Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 2nd Floor
Project: IS82.BL00 Activity: CON-4690
Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 3rd Floor
Project: IS82.BL00 Activity: CON-4830
Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - 4th Floor
Project: IS82.BL00 Activity: CON-4960
Install 5/8 Mold & Moisture Resistant / Abuse Resistant Gybsum Board - Lower Roof
Project: IS82.BL00 Activity: CON-5120
Rough-in Duct Work -VAV Devices & Diffusers - 1st Floor
Project: IS82.BL00 Activity: CON-5290
Rough-in Power Conduits & Wires - 1st Floor
Project: IS82.BL00 Activity: CON-5470
Rough-in Low Voltage Conduits & Wires - 1st Floor
Project: IS82.BL00 Activity: CON-5640
Rough-in Plumbing Pipes - 1st Floor
Project: IS82.BL00 Activity: CON-5680
Rough-in Sprinkler Piping - 1st Floor
Project: IS82.BL00 Activity: CON-5780
Install Sprinkler Heads - 1st Floor

```
                Project:        IS82.BL00       Activity:       CON-5810
Install Ceiling Hangers - 1st Floor
                Project:        IS82.BL00       Activity:       CON-5920
Install Gypsum Board Ceiling - 1st Floor
                Project:        IS82.BL00       Activity:       CON-5930
Install Acoustical Ceiling Tiles - 1st Floor
                Project:        IS82.BL00       Activity:       CON-5940
Install Wood Slat Ceiling - 1st Floor
                Project:        IS82.BL00       Activity:       CON-5950
MCP-Wood Slat Ceiling Panel - 1st Floor
                Project:        IS82.BL00       Activity:       CON-6030
Install First Coat Painting - 1st Floor
                Project:        IS82.BL00       Activity:       CON-6100
Install Lighting Fixtures - 1st Floor
                Project:        IS82.BL00       Activity:       CON-6160
Install Data & Video Intercome Systems - 1st Floor
                Project:        IS82.BL00       Activity:       CON-6220
Install Voice Systems Components  - 1st Floor
                Project:        IS82.BL00       Activity:       CON-6260
Install Public Address and Clock Systems Components - 1st Floor
                Project:        IS82.BL00       Activity:       CON-6280
Install Auxiliary Signal System Components - 1st Floor
                Project:        IS82.BL00       Activity:       CON-6290
Install Intrusion Alarm System Components - 1st Floor
                Project:        IS82.BL00       Activity:       CON-6300
Install IPDVS System Components - 1st Floor
                Project:        IS82.BL00       Activity:       CON-6320        IPDV
System Testing and Inspection (Before 2-Nov-26)
                Project:        IS82.BL00       Activity:       MIL-1000        NTP
                Project:        IS82.BL00       Activity:       MIL-1020
Building Tight
                Project:        IS82.BL00       Activity:       MIL-1030        TCO
                Project:        IS82.BL00       Activity:       MIL-1040
Substantial Completion
                Project:        IS82.BL00       Activity:       MIL-1050
Final Completion
                Project:        IS82.BL00       Activity:       PER-1100        DOB
Permit & Insurance
                Project:        IS82.BL00       Activity:       PER-1110        SCA
Work Notification
                Project:        IS82.BL00       Activity:       PER-1120        No
Site Access

        Activities with unsatisfied constraints.....................0

        Activities with unsatisfied relationships...................0

        Activities with external dates..............................0
```
