April 7, 2025

ONE PENN CENTER
1617 JFK BOULEVARD
SUITE 475
PHILADELPHIA, PA
215.814.6400
fax: 215.814.6440
philadelphia@traunerconsulting.com
www.traunerconsulting.com

Timothy Costello
Project Officer
New York City School Construction Authority
25-01 Jackson Avenue
Long Island City, NY 11101

SENT VIA EMAIL TO:
tcostello@nycsca.org

RE: PS-IS 341Q - Queens
Contract#: C000080867
Resubmitted Baseline Schedule Review
File Name: P026453.BL01
TRAUNER Project No. 3010

Dear Mr. Costello:

This letter reviews the Resubmission of the Baseline Project Schedule submitted by Navillus Contracting (Navillus) for the PS-IS 341Q – New School Building, which was received on March 24, 2025.

Navillus has addressed all comments from the review of the Detailed Baseline Schedule. It is recommended that the SCA accept this submission, and Navillus should use this schedule to prepare and submit Update No. 1.

Please contact me with any questions.

Sincerely,
TRAUNER CONSULTING SERVICES, INC.

Mark Nagata, PSP
Principal

MN/LM

cc: Hosam Awad

Navillus Contracting
633 3rd Avenue, 17th Floor
New York, New York 10017
P: +12127501808

Project: 2919-00 PS 341Q
1-55 54th Ave
Long Island City, New York 11101

Submittal #S01311-001.002 - Baseline Schedule
S01311 - Progress Schedule

Revision	002	**Submittal Manager**	Nisha Pawar (Navillus Contracting)
Status	Open	**Date Created**	Mar 24, 2025
Issue Date	Mar 24, 2025	**Spec Section**	S01311 - Progress Schedule
Responsible Contractor	Navillus Contracting	**Received From**	
Received Date		**Submit By**	
Final Due Date	Apr 7, 2025	**Lead Time**	
		Cost Code	
Location		**Type**	Document
Submittal Package			
Approvers			
Ball in Court	Nisha Pawar (Navillus Contracting)		
Distribution	David King (Navillus Contracting)		
Description			

Submittal Workflow

Name	Sent Date	Due Date	Returned Date	Response	Attachments
General Information Attachments					Response to PSIS341Q Baseline Rev#00 Comments.pdf PSIS 341Q 048 New Building - Baseline Schedule - Rev01.pdf
Nisha Pawar		Apr 7, 2025		Pending	

No	Comment Description	Baseline PS/IS 341Q - Comments
III. Contract Requirements		
	A. Contract Completion Dates	
	On September 26, 2024, the SCA issued the project's Notice-to-Proceed (NTP) letter. You have been awarded the above contract in the amount of $74,725,000.00. This contract shall henceforth be identified by the above description, contract # : C000080867, which shall be used in communications relating to this contract. You are directed to commence the work of this contract on the NTP date of 9/30/2024. This contract requires completion of the work within 930 consecutive calendar days of the NTP date, thus establishing a substantial completion date of 4/17/2027 and a final completion date of 8/15/2027. I will be contacting you shortly to schedule a preconstruction meeting. Your key project personnel and major subcontractors will be required to attend this meeting. Prior to the start of the work, you are to obtain all required permits and submit evidence of all contractor-provided insurance in accordance with the contract documents. You will not be permitted to start any work for which required contractor provided insurance is not submitted. No extension of time will be granted for failure to secure insurance in a timely manner. You will be required to maintain all such coverage for the duration of your contract work. The letter identified an NTP date of September 30, 2024, which is also the NTP date in the Baseline Schedule. This establishes a Contract Substantial Completion date of April 17, 2027, and a Contract Final Completion date of August 15, 2027. Table No. 1 compares the Contract Milestone Completion dates to the same dates forecasted in the Baseline Schedule.	Noted.

Table No. 1:
Comparison of Contract Milestone Dates to Baseline Schedule Dates

Act ID	Activity Name	Contract	Baseline Schedule	Diff. Late/ (Early)
MIL-1600	*MDF Work Finish*	7/21/2026	7/21/2026	0
MIL-1610	*IDF Work Finish*	7/21/2026	7/21/2026	0
MIL-1620	*IPDVS Work Finish*	9/19/2026	9/18/2026	(1)
MIL-1510	*TCO*	10/19/2026	10/19/2026	0
MIL-1550	*Substantial Completion*	4/17/2027	4/17/2027	0
MIL-1560	*Final Completion*	8/15/2027	8/15/2027	0

The Baseline Schedule forecasts that IPDVS will be completed one calendar day earlier than required by the Contract. MDF, IDF, TCO Substantial Completion and Final Completion will occur on the same day as required by the Contract.	
B. Phasing Exhibit Requirements	
This section reviews the Phasing Exhibit and its requirements for the project schedule. 1) All work prior to school occupancy may be performed during normal working hours. All work subsequent to school occupancy shall be performed after normal school hours. 2) The Contractor is fully aware that portions of this work will be performed in a school facility operating during times indicated below. The School Construction Authority will cease any construction operations causing excessive noise, dust or similar disruptions during hours in which they are allowed to work and school is in session. 3) Normal school hours are: • 7:00AM to 3:00PM Monday through Friday- School Year. • 8:00AM to 1:00PM Saturday- School Year. • 8:00AM to 2:30PM Monday through Friday- Summer School (July & August). • 8:00AM to 2:30PM Saturday- Summer School (July & August). 4) After-school activities hours are: • 3:00PM to 6:00PM Monday through Friday- School Year. • 1:00PM to 6:00PM Saturday-School Year. • 2:30PM to 6:00PM Monday through Friday-Summer School (July & August). • 2:30PM to 6:00PM Saturday- Summer School (July & August). 5) After School Occupancy, the Contractor shall take all precautions necessary to ensure that the construction operation will in no way interrupt or otherwise affect the activities of the school. All activities in the Baseline Schedule are assigned to one or two calendars: the "P026453 – 5 Days Calendar" and the "P026453 – 7 Days Calendar". The "P026453 – 5 Days Calendar" is a 5-workday, 8-hour per day calendar with hours between 8:00 a.m. and 4:00 p.m. and includes basic holidays. This calendar assignment is appropriate for all work being performed prior to occupancy.	Noted.
The "P026453 – 7 Days Calendar" is a 7-workday, 8-hour-per-day calendar without holidays. It includes a number of activities, including submittal review, inspections, mock-ups, and permits. These activities should be assigned to a 5-day calendar with holidays. Navillus should revise the calendar assignment for these activities to a 5-day workweek.	As per specification section S01300 – Submittals, point 1.07.B, the review and approval of submittals should be completed within 21 calendar days, excluding holidays. B. The Authority will review and return to the Contractor satisfactorily prepared Submittals within twenty-one (21) calendar days (excluding National Holidays) after receipt by the Design Professional of Record (or other SCA department depending on submittal type), including transmittal time. The mockups, inspections, and permits are now assigned to a 5-day calendar.

<table>
<tr>
<td>Navillus should also confirm that the Baseline Schedule accounts for any work activities that may need to be completed after occupancy and after normal school hours.</td>
<td>Confirmed, the baseline schedule does not include any construction work beyond the TCO and substantial completion.</td>
</tr>
<tr>
<td>It does not appear that Navillus has included 20 lost production days in its Baseline Schedule. Navillus should add the lost production days to the Project Calendars in its next schedule submission or show how the schedule accounts for the 20 lost production days.</td>
<td>The following days have been incorporated as closed in the calendar after the TCO dates:
<table>
<tr><th>No</th><th>Date</th><th>No</th><th>Date</th></tr>
<tr><td>1</td><td>6-Nov-26</td><td>11</td><td>3-Feb-27</td></tr>
<tr><td>2</td><td>16-Nov-26</td><td>12</td><td>11-Feb-27</td></tr>
<tr><td>3</td><td>24-Nov-26</td><td>13</td><td>24-Feb-27</td></tr>
<tr><td>4</td><td>3-Dec-26</td><td>14</td><td>4-Mar-27</td></tr>
<tr><td>5</td><td>8-Dec-26</td><td>15</td><td>11-Mar-27</td></tr>
<tr><td>6</td><td>16-Dec-26</td><td>16</td><td>16-Mar-27</td></tr>
<tr><td>7</td><td>31-Dec-26</td><td>17</td><td>24-Mar-27</td></tr>
<tr><td>8</td><td>6-Jan-27</td><td>18</td><td>1-Apr-27</td></tr>
<tr><td>9</td><td>14-Jan-27</td><td>19</td><td>6-Apr-27</td></tr>
<tr><td>10</td><td>27-Jan-27</td><td>20</td><td>20-Apr-27</td></tr>
</table>
</td>
</tr>
<tr>
<td>Navillus included the following milestone in the Baseline Schedule for the security guard start date.


The security guard start date of October 30, 2024, complies with Phasing Exhibit item 7.</td>
<td>Noted.</td>
</tr>
<tr>
<td>8) After School Occupancy, no deliveries, crane or hoisting activities will be permitted during normal school hours.
9) After School Occupancy, all hot work, and potable water disinfection shall be done when the building is vacant.
Navillus should confirm that the Baseline Schedule accounts for the above restrictions after the school is occupied.</td>
<td>Confirmed, the baseline schedule does not include any construction work beyond the TCO and substantial completion.</td>
</tr>
<tr>
<td>Navillus included activities for coordination with Con Ed. Navillus should confirm that the
Baseline Schedule accounts for coordination with all utility companies required to meet the
project's requirements.
For example, a screenshot of the Con Ed activities in the Baseline Schedule below.</td>
<td>The following activities have been incorporated into the schedule to reflect CON-ED work from June 24th, 2026, to August 17th, 2026, following the switchgear installation:
1. CON-8060 “CON-ED - Switchgear Inspection”</td>
</tr>
</table>

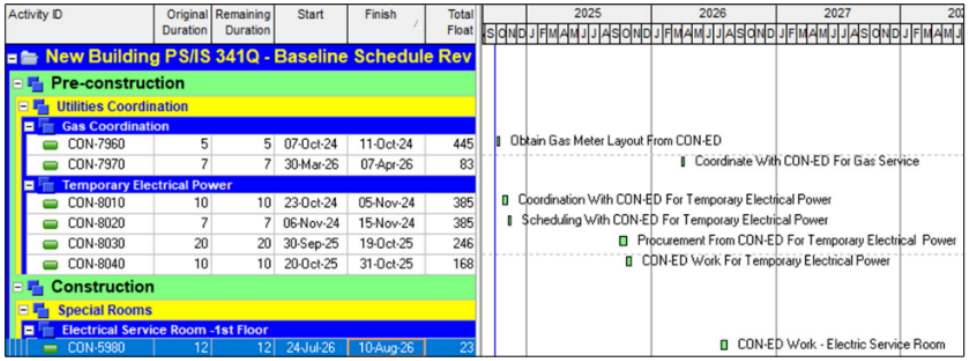 Currently, Navillus shows a 2-week work activity for Con Ed to perform its work in the electric service room. Typically, Con Ed's work for a line project like this one includes Con Ed (1) inspecting the switchgear, (2) pulling power cables to the building, (3) terminating the power cables, and (4) energizing the building. Based on experience from other SCA projects, Con Ed's effort to pull and terminate cable and to energize the building typically takes 6 weeks. If Navillus believes that Con Ed will not require 6 weeks to perform this work, then it should provide a detailed explanation of why it believes Con Ed will complete this work in less time. Navillus should add activities for these efforts and all other tasks that Con Ed needs to perform to provide permanent power to the project.	2. CON-8070 "CON-ED - Pull Power Cable to the Building" 3. CON-8080 "CON-ED - Terminate Power Cables" 4. CON-8090 "CON-ED - Energize to the Building"
Navillus included one activity in its Baseline Schedule for the protection of utilities from September 30, 2025 to October 19, 2026. Navillus should also confirm that the Baseline schedule also accounts for overhead and underground utility protection on the project.	The following activity has been incorporated to account for underground and overhead protection: CON-7740 – Protection of All Overhead & Underground Utilities.
The Baseline Schedule does not include activities for protecting and restoring adjacent properties. Navillus should include these activities in its Baseline Schedule resubmission and ensure that the added activities comply with Phasing Exhibit 15.	Activity **CON-9000 – Protection & Restoration of Adjacent Properties to Original Condition** has been incorporated into the schedule as a level of effort to represent the protection of adjacent properties throughout the construction phase.
The Phasing Exhibit requires that the MDF/IDF room be complete 90 days prior to TCO, which is July 21, 2026. The Phasing Exhibit requires that the IPDVS room is completed 30 days prior to TCO, which is September 19, 2026. The Baseline Schedule includes the following milestones for MDF, IDF, and IPDVS completion.	Noted.

 The MDF/IDF and IPDVS milestone dates comply with the Phasing Exhibit.	
19) Within twenty (20) consecutive calendar days from the start date indicated by the Notice to Proceed (NTP) the contractor and their Filing Representative shall attend a meeting with SCA to review the permit requirements. 20) The contractor shall provide the SCA Chief Project Officer with all permit waiver requests prior to submission to BCC for approval. The Baseline Schedule includes the following activities for the permit requirements meeting and the permit waiver requests. The completion dates comply with the Phasing Exhibit items 19 and 20.	Noted.
Phasing Exhibit 21 requires the submittals listed above to be submitted within 120 CCDs from the NTP, which is January 28, 2025. The Baseline Schedule includes all submittals listed in Exhibit 21 and forecasts that they will be submitted before or on January 28, 2025.	Noted.
The Baseline Schedule depicts mobilization starting on September 30, 2025, 365 calendar days after NTP. The mobilization start date complies with Phasing Exhibit item 23.	Noted.
The Baseline Schedule does not include activities for the steel plate protection over the NYPA easements. Navillus should confirm the Baseline Schedule accounts for this work or add activities as necessary.	Activity CON-9010 – Remove Steel Plate Protection over NYPA Easement - Playground Area & Fences - Building Perimeter has been incorporated to reflect the removal of the steel plate, which was initially installed by the Phase 1 contractor.
The Baseline Schedule includes the following permit activities.	Activity PRE-2660 – Obtain NYPA Permit has been incorporated into the schedule, while PRE-2650 – Obtain Permit to Enter (PTE) Amtrak was already included.



Activity ID	OD	RD	Start	Finish	Total Float
PRE-2600	5	5	30-Sep-24	04-Oct-24	445
PRE-2590	14	14	30-Sep-24	18-Oct-24	231
PRE-1660	3	3	27-Sep-25	29-Sep-25	0
PRE-1460	3	3	25-Sep-25	29-Sep-25	0
PRE-2570	3	3	25-Sep-25	29-Sep-25	0
PRE-2630	10	10	16-Sep-25	29-Sep-25	0
PRE-2640	15	15	15-Sep-25	29-Sep-25	0
PRE-2650	10	10	16-Sep-25	29-Sep-25	0
PRE-2610	10	10	06-Oct-25	20-Oct-25	185
PRE-2620	21	21	21-Oct-25	10-Nov-25	272
PER-2640	5	5	28-May-26	03-Jun-26	94
PER-2650	10	10	09-Jun-26	18-Jun-26	123

The Baseline Schedule does not include specific activities for permits from Amtrak and NYPA. Navillus should add activities for these permit requirements in its Baseline Schedule resubmission or explain why they are unnecessary.

Phase I – New Building Occupancy with TCO

1) Work within this phase includes but is not limited to construction of the new building, including completion of all site work, general construction, HVAC, plumbing, electrical, fire protection, life safety systems, with only punch list work remaining. At the completion of this phase, the contractor will be responsible to obtain a Temporary Certificate of Occupancy (TCO) from the Department of Buildings for the New Building. This phase cannot be declared complete until the TCO is obtained.

2) Work indicated in Phase I including obtaining the TCO shall be completed within **750** continuous calendar days (CCDs) from the start date indicated by the Notice to Proceed (NTP). **Additional liquidated damages shall be assessed in the amount of Five Thousand ($5,000.00) Dollars for each continuous calendar day that the contractor does not meet completion date as indicated above.** These liquidated damages are in addition to all other liquidated damages under subject contract.

The Contract requires TCO within 750 CCDs from the NTP, which is October 20, 2026.
The Baseline Schedule forecasts TCO on October 19, 2026, which complies with the Contract requirements.

Noted.

C. Specification Compliance:

Section S01311 – Progress Schedule

Specification Section S01311, Progress Schedule, requires that the Baseline Schedule contains certain salient features, such as milestone dates or the delivery of Owner-furnished equipment.

1. Contract major milestones as indicated in Article 1.07 must be identified, and included in the Detailed Project Schedule.

article 1.07 identifies 58 milestones. Of the 58 required milestones, the Baseline Schedule is missing 31 milestones. These milestones are listed below. as shown below.

- Submit Complete Permit Application
- Issuance of Permit (separate milestones for each permit)

Incorporated, please refer to the following milestones:

1. MIL-2532 “Submit Complete Permit Application”.
2. MIL-2832 “Issuance of Excavation & Shoring Permit”.
3. MIL-2842 “Issuance of Builders Pavement Permit”.
4. MIL-2852” Issuance of Permit to Enter (PTE)”.
5. MIL-2862 “Issuance of NYPA Permit”.

- Complete Subcontractor 'Buyout', including fabrication and delivery
- Deliveries of all owner-furnished equipment and/or materials
- Start Installation of Scaffolding
- All Phasing Exhibit Contract Milestones
- Start Foundation
- Start Below Grade Plumbing and Other Utilities
- Place Steel Mill Order
- Start Concrete Placement
- P&D - Connection to Roof Drains
- Start Mechanical Distribution Lines
- Start Suspended Ceiling Grid
- Start Low Voltage
- Start Kitchen
- Start Mechanical and Electrical System Commissioning
- Finish HVAC
- Finish Fire Alarm Signoff
- Finish Mechanical and Electrical System Commissioning
- Finishes and Ceiling Complete
- Finish Painting
- Finish Scaffolding Removal
- Permanent Power Available
- Elevator Ready for Testing
- Building HVAC Flush-out
- Inspections
- Green Schools Compliance Submission
- Performance test for all mechanical equipment and low voltage systems
- Commissioning for all mechanical equipment and low voltage systems
- Submission of Operations and Maintenance Manuals
- Provision of Training Schedules (30 days prior to start of Training)

6. MIL-2872 "Issuance of Construction Fences Permit".
7. MIL-2882 "Issuance of Sidewalk Shed Permits"
8. MIL-2892 "Issuance of CCD1"
9. MIL-2902 "Issuance of DOB Permit & Insurance"
10. MIL-2542 "Complete Subcontractor 'Buyout'"
11. MIL-2622 "Deliveries of all owner-furnished equipment and/or materials"
12. MIL-1830 "Crane Mobilization-Precast Sandwich Panels Installation Start"
13. MIL-1840 "Crane Mobilization-Precast Sandwich Panels Installation Finish"
14. Phasing exhibit milestones are already on the schedule.
15. MIL-2812 "Start Foundation".
16. MIL-2562 "Start Below Grade Plumbing and Other Utilities".
17. MIL-2572 "Place Steel Mill Order.
18. MIL-2582 "Start Concrete Placement".
19. MIL-2592 "P&D - Connection to Roof Drains"
20. MIL-2602 "Start Mechanical Distribution Lines".
21. MIL-2612 "Start Suspended Ceiling Grid".
22. MIL-2712 "Start Low Voltage".
23. MIL-2722 "Start Kitchen".
24. MIL-2732 "Start Mechanical and Electrical System Commissioning".
25. MIL-2632 "Finish HVAC".
26. MIL-2642 "Finish Fire Alarm Signoff".
27. MIL-2652 "Finish Mechanical and Electrical System Commissioning"
28. MIL-2662 "Finishes and Ceiling Complete"

	29. MIL-2672 “Finish Painting”. 30. MIL-2742 “Permanent Power Available” 31. MIL-2822 “Elevator Ready for Testing” 32. MIL-2692 “Building HVAC Flush-out” 33. MIL-2762 “Green Schools Compliance Submission”. 34. MIL-2772 “Performance test for all mechanical equipment and low voltage systems 35. MIL-2792 “Commissioning for all mechanical equipment and low voltage systems” 36. MIL-2782 “Submission of Operations and Maintenance Manuals” 37. MIL-2802 “Provision of Training Schedules (30 days prior to start of Training)”
Navillus should add these missing milestone activities in its resubmission of the Baseline Schedule and ensure that they have appropriate predecessors. 2. All submittal, owner review & approval, purchase, manufacture, and delivery activities for all major materials and equipment. Section 1.04 F.2 lists the following requirements for submittals. The following submittals are missing from the Baseline Schedule. • Section 02090 ENVIRONMENTAL MANAGEMENT OF EXCAVATED MATERIAL AND FILL/BACKFILL • Section 02260 EXCAVATION SUPPORT AND MONITORING • Section 05700 ORNAMENTAL METAL • Section 05710 STEEL STAIRS • Section 08330 COILING DOORS, GRILLES AND SHUTTERS • Section 08411 ALUMINUM FRAMED ENTRANCES AND STOREFRONTS • Section 08521 FIRE RATED GLAZING SYSTEMS • Section 08730 THRESHOLDS, WEATHERSTRIPPING AND SEALS • Section 08800 MISCELLANEOUS GLAZING • Section 09860 GRAFITI RESISTANT COATINGS	Incorporated, all the missing Submittals were added.

• Section 09800 SPECIAL COATINGS • Section 10350 FLAGPOLE • Section 10415 BULLETIN BOARDS, GLAZED DISPLAY BOARDS, DISPLAY CABINETS & CASES • Section 10605 WIRE MESH WORK • Section 10675 METAL STORAGE SHELVING • Section 10830 MIRRORS • Section 10840 GRAB BARS • Section 11500 SHOP EQUIPMENT • Section 12761 BLEACHERS • Section 15412 VALVES • Section 15414 TESTS • Section 15431 TAGS, CHARTS, AND IDENTIFICATION • Section 15432 MISCELLANEOUS • Section 15511 VALVES (HVAC) • Section 15512 PIPING INSULATION • Section 15513 EQUIPMENT INSULATION • Section 15514 DUCTWORK INSULATION • Section 15515 HYDRONIC SPECIALTIES • Section 15517 WATER TREATMENT FOR HYDRONIC SYSTEMS • Section 15570 BOILER ACCESSORIES • Section 15575 BREECHING CHIMNEY CONNECTORS AND CHIMNEYS • Section 15670 PLATE HEAT EXCHANGERS • Section 15792 COILS • Section 15835 CONVECTORS • Section 15838 FAN COIL UNITS • Section 15839 DOOR AIR CURTAINS • Section 15860 CENTRIFUGAL FANS • Section 15885 AIR FILTERS • Section 15910 DUCT ACCESSORIES • Section 15915 DAMPER ASSEMBLIES • Section 15930 VARIABLE AIR TERMINALS	

• Section 15935 AIR HANDLING UNITS FOR PUBLIC ASSEMBLY SPACES • Section 15973 FACILITY MANAGEMENT SYSTEMS INTEGRATION • Section 16145 LIGHTING CONTROL DEVICES • Section 16289 SURGE PROTECTIVE DEVICES • Section 16420 SERVICE ENTRANCE EQUIPMENT • Section 16441 ENCLOSED SWITCHES • Section 16480 MOTORS, MOTOR CONTROL CENTERS, STARTERS AND • CONTROL EQUIPMENT • Section 16670 LIGHTNING PROTECTION • Section 16728 FIBER OPTIC CABLING SYSTEM • Section 16770 SOUND, INTERCOM & TEACHER ACTIVATED SECURITY SYSTEM • Section 16771 SOUND, INTERCOM & TEACHER ACTIVATED SECURITY SYSTEM • Section 16791 SELF-CORRECTIVE CLOCK SYSTEM • Section 16855 HEAT TRACE CABLE SYSTEM Navillus should add the missing submittals and all associated construction activities to the Baseline Schedule when it resubmits it.	
The Baseline Schedule does not appear to include activities representing any owner-furnished equipment or material. Navillus should confirm that the schedule includes such equipment or add activities as necessary.	Incorporated, Owner furnished furniture activities were added to the schedule • CON-9020 “Install Furniture & Milling Work (Owner Provided & Installed) -1st Floor” • CON-9030 “Install Furniture & Milling Work (Owner Provided & Installed) -2nd Floor” • CON-9040 “Install Furniture & Milling Work (Owner Provided & Installed) -3rd Floor” • CON-9050 “Install Furniture & Milling Work (Owner Provided & Installed) -4th Floor” • CON-9060 “Install Furniture & Milling Work (Owner Provided & Installed) -5th Floor”
The Baseline Schedule includes three construction activities with original durations greater than 10 working days.	Incorporated, all the durations of the construction activities are below 10 days.

Section 1.04I stated the following concerning predecessors and successors. I. Activity Relationships shall be assigned to clearly establish predecessor and successor relationships to each activity. Open ended activities are not permitted with the exception of the first and last activities in the network, the first activity being NOTICE TO PROCEED and the last being FINAL COMPLETION. The use of relationship lag times is discouraged and only permitted with approval by the Authority; use of negative lag is never permitted. The Baseline Schedule includes two activities, the first and the last, that are missing a relationship, which is acceptable. It does not have any activities with relationship lag	Noted.
Section 1.05A describes activity coding. activity Coding in the Baseline schedule is incomplete. In its resubmission of the Baseline Schedule, Navillus should add the five-level coding structure for all activities.	Incorporated, all activity codes are added to the schedule.
Section 1.06A states that the WBS levels must be integrated into all P6 Schedules. A. A multi-level hierarchal WBS shall be incorporated in all P6 schedules. An initial, proposed WBS Structure must be submitted with the Preliminary Project Schedule. The levels (nodes) shall include, but not be limited to: LEVEL 01 - is the Contract or Project Level LEVEL 02 - shall have a minimum of four nodes; Pre-Construction, Procurement, Construction or Phase of Construction, and Closeout LEVEL 03 - Specification Section T The Baseline Schedule includes all three nodes.	Noted.
2. Additional Specification Requirements	
a. Specification S01426	

Specification Section S01426 requires Navillus to provide a complete sample classroom for approval to the SCA prior to beginning finish work for all classrooms. A complete sample of a typical classroom that incorporates all of the individual materials, furnishings, equipment and finishes shall be constructed. The Sample Classroom will serve to establish an acceptable level of quality. The Authority will have an opportunity to view and approve the finished room before the Contractor begins the finish production work for classrooms throughout the building. The Baseline Schedule includes submittal activities for the sample classroom and the following construction activities.	Noted.
The Baseline Schedule includes submittal activities for the sample classroom and the following construction activities. However, none of the install gypsum wall board activities include the in-wall inspection as a predecessor. Navillus should either add in-wall inspection activities for each floor and show them as predecessors to the start of the gypsum wall board installation activities or explain why in-wall inspection activities are not necessary in the resubmission of the Baseline Schedule.	Incorporated, In-wall inspection activities were added before gypsum wall installation. Please refer to: 1. CON-9070 “In-Wall Inspection-2nd Floor” 2. CON-9080 “In-Wall Inspection -3rd Floor”. 3. CON-9090 “In-Wall Inspection -4th Floor” 4. CON-9100 “In-wall Inspections -5th Floor” 5. CON-9110 “In-Wall Inspection -1st Floor”
b. Specification S01426	
Specification Section 05120 STRUCTURAL STEEL requires that the MEP dunnage submittals must be submitted after the MEP units have been approved. The Baseline Schedule depicts the AHU and chiller review finishing after dunnage submittals. Navillus should ensure that the AHU units are approved before submitting the dunnage steel when resubmitting the baseline schedule.	Incorporated, the MEP dunnage activities were pushed after the approval of MEP unit.
c. Specification Section S01560	

In specification Section S01560 INSTALLATION SEQUENCE OF FINISH MATERIALS S01560, item 1.05 requires that type 1 finishes be installed prior to type 2. The Baseline Schedule depicts acoustical ceilings (Type 2) being installed before the final coat of painting (Type 1) on all floors. Navillus should correct this sequence in its Baseline Schedule resubmission.	Incorporated, the sequence of work was corrected as stated.
d. Specification Section S08710	
Specification Section S08710, FINISH HARDWARE, requires the contractor to provide a key-cutting machine one month prior to turnover. 3. Commercial Duty, Automatic, Key Cutting Machine with Blanks & Cylinders: One month prior to turnover, the contractor shall supply to the principal: a. One (1) commercial duty, automatic key cutting machine and a separate grinder with one wire wheel and one fine grinding wheel. b. 300 of each manufacturer's cylinder key blanks for each type of cylinder keyway used in the building. This shall also include key blanks for loose furniture & equipment keys. c. 10% attic stock of manufacturer's cylinders with keys for each type of different cylinder keyway used in the building. The Baseline Schedule does not include any activities for key cutting machine. In its resubmission of the Baseline Schedule, Navillus should include the submission of a key cutting machine one month prior to SCA takeover or confirm the Baseline Schedule accounts for this requirement and identify where this work is located.	Incorporated, key cutting machine procurement activity was added to the schedule and the key machine planned to be delivered before TCO by one month • PRO-2000 "Procure & Deliver Key Cutting Machine".

e. Specification Section 02090	
<table><tr><th>Item No.</th><th>Paragraph No.</th><th>SUBMITTAL</th><th>Due Date</th></tr><tr><td>1</td><td>1.05A</td><td>Soil Sampling Plan</td><td>4 weeks before sampling</td></tr><tr><td>2</td><td>1.05B</td><td>Excavated Material Disposal Plan</td><td>4 weeks before excavation</td></tr><tr><td>3</td><td>1.05C</td><td>Backfill and Reuse Plan</td><td>4 weeks before backfilling</td></tr></table> The Baseline Schedule does not include the submission of any of the above plans, nor does it include soil sampling activities. Navillus should include activities representing the plans depicted above in its Baseline Schedule resubmission.	Incorporated, the submittal and approval of the previous plans were added in addition to the soil sampling. • SUB-2900 “Prepare & Submit Excavated Material Disposal Plan” • APP-2900 “Review & Approve Excavated Material Disposal Plan” • SUB-4050 “Prepare & Submit Soil Sampling Plan” • APP-4050 “Review & Approve Soil Sampling Plan” • SUB-2910 “Prepare & Submit Backfill & Resue Plan” • APP-2910 “Review & Approve Backfill & Resue Plan” • CON-9120 “Soli Sampling”
f. Specification Section 16010	
Below are all of the switchgear-related activities in the Baseline Schedule. Note that these activities only depict procurement of the switchgear. The Baseline Schedule does not appear to include an activity for the installation of the switchgear. In the resubmission of the Baseline Schedule, Navillus should ensure that it includes a switchgear installation activity.	Incorporated: The switchgear activity has been added to the schedule. Please refer to CON-9130 – "Install Switchgear - Electric Service Room"

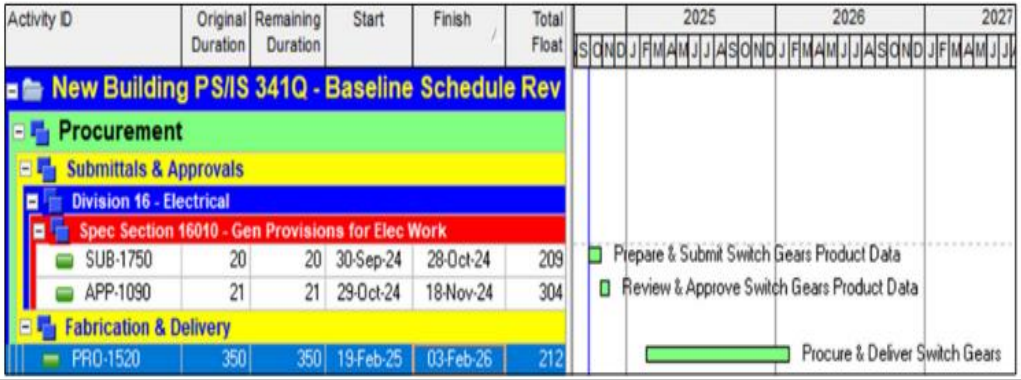

g. Specification Section 16785

Specification Section 16785 INTERNET PROTOCOL DIGITAL VIDEO SURVEILLANCE requires an additional 14 calendar days of review time for the IPDVS system shop drawings. The IPDVS review in the Baseline Schedule is 21 days. This review time should be revised to 35 days.	Incorporated, the review duration of IPDVS activity was changed to 35 days • APP-1220 "Review & Approve Internet Protocol Digital Video Surveillance System using Digital Cameras" Duration "35"

D. Critical Path & Near-Critical Path Review

The critical path is the longest path of activities through a schedule that establishes when the project will finish. The Baseline Schedule's critical path can be identified in the Primavera P6 software using the longest path filter. The critical path of the Baseline Schedule should be continuous, beginning on the data date and ending with the last activity on the project. The critical path begins with the NTP on September 30, 2024, followed 365 delay to site access, through September 29, 2025. The path continues with mobilization and the start of construction followed by foundation and underground utility work, followed by the slab on grade through November 12, 2025. The path continues with building structure installations through February 5, 2026, followed by precast panel installation on the elevations and windows. The path continues with fluid applied membrane on the roof and 5th floor along with roof work followed by the building watertight milestones on April 16, 2026. Next the critical path goes through drywall work,	Noted.

	paint, auxiliary systems, furniture & millwork at all floors. The path continues with cafeteria equipment, 1st floor signage, and TCO punchlist/TCO through October 19, 2026. The path concludes with pre-substantial punchlist and Substantial completion on April 17, 2027. Lastly, closeout activities and Final Completion are critical through August 15, 2027. The image below depicts the critical path along with three near-critical paths.	
	E. Additional Comments	
a. Testing and Commissioning		
21	The Baseline Schedule includes the following WBS breakout for testing and commissioning. 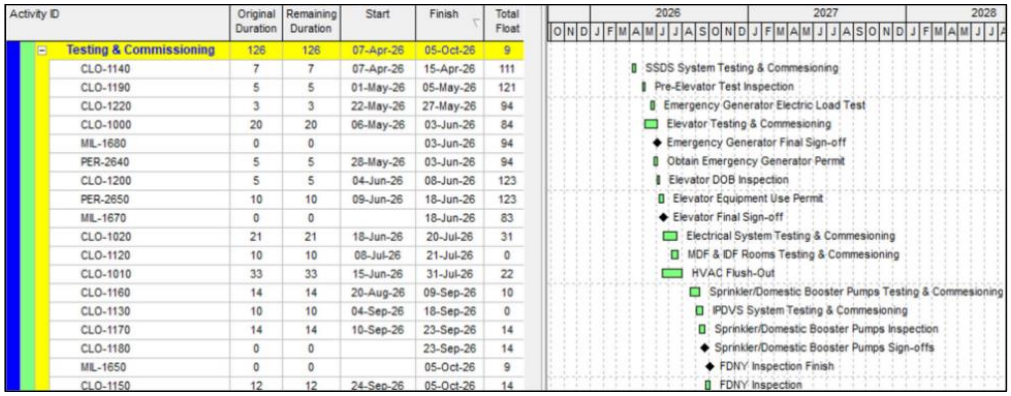 However, no additional details are provided for testing or commissioning activities. There are multiple MEP systems that require testing before TCO. Typically, on SCA projects, there are a collection of equipment and systems that need to be tested after permanent power and before TCO can be issued. Some of those tests are listed below. • Air Handing Unit (AHU) Testing, • Elevator Sump Pump Testing, • Elevator Testing,	Incorporated: All necessary systems testing and commissioning have been added to the schedule. Please refer to: 1. CLO-1230 “Air Handling Unit Testing & Commissioning”. 2. CLO-1240 “Elevator Sump Pump Testing & Commissioning”. 3. CLO-1000 “Elevator Testing & Commissioning”. 4. CLO-1160 “Sprinkler/Domestic Booster Pumps Testing & Commissioning”. 5. CLO-1250 “Emergency Generator Testing & Commissioning”. 6. CLO-1260 “HVAC Split System Testing & Commissioning” 7. CLO-1270 “Water Heater Testing & Commissioning”. 8. CLO-1280 “Fire Alarm Testing & Commissioning” 9. CLO-1290 “Glycol System Testing & Commissioning”.

	• Domestic Water Booster Pump Testing, • Fire Pump Testing, • Emergency Generator Testing, • HVAC Split System Testing, • Water Heater Testing, • Fire Alarm Testing, • Glycol System Testing Navillus should confirm that the Baseline Schedule accounts for all required systems testing or add activities as necessary. Navillus should also confirm that the Baseline Schedule accounts for all required systems commissioning or add activities as necessary.	
b. Elevator Work		
The work prior to the start of elevator work consists of steel/concrete columns, metal framing/deck from the 1st through the 5th. Once elevator work has been completed, it undergoes testing and commissioning. The Baseline Schedule does not specifically mention the installation of the elevator shaft or cab. Also, typically the elevator shaft construction would start after the building or elevator room is watertight. The building is forecast to be watertight on April 16, 2026, which is after most of the elevator work has been completed. Navillus should confirm their sequence of elevator work is correct or make changes to its resubmission of the Baseline Schedule.		Incorporated: All elevator work has been rescheduled to follow building tight, and the elevator shaft installation has been added.
c. Activity Sequencing		
The installation of floor tile at the first floor should not be a successor to the wood floor procurement. Navillus should also confirm that the duration of three days for the wood flooring in the gym is sufficient.		Incorporated: The relationship has been corrected, and the duration of wood flooring has been increased.

Below is a screenshot of the WBS structure node for floors 1 through 5. 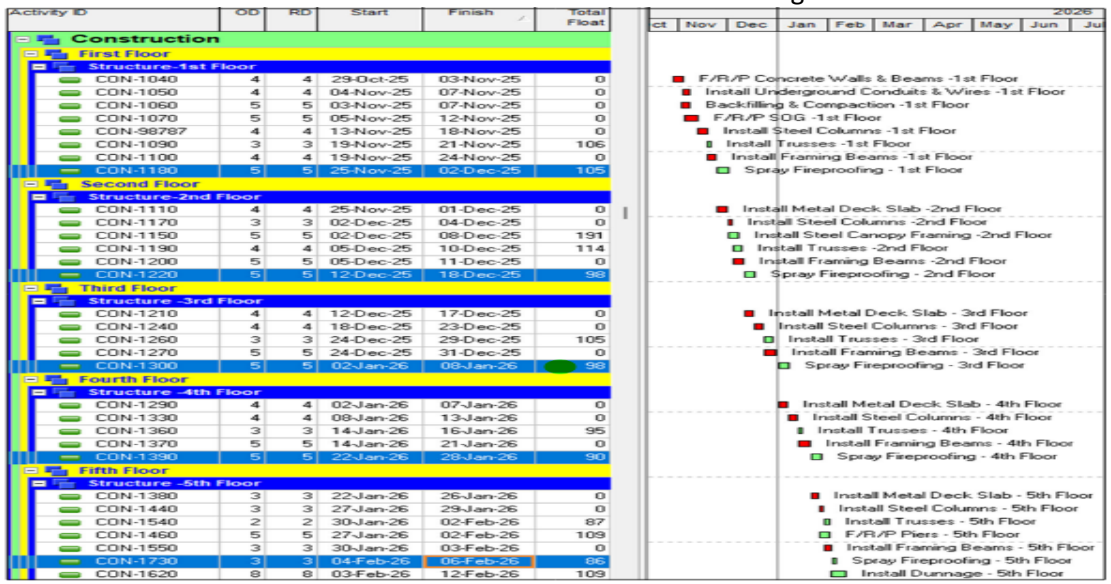 The Baseline Schedule shows that Navillus plans to install the spray-on fireproofing on five separate weeks, a week per floor. However, Navillus shows the spray-on fireproofing being installed at the same time as the structural steel for the floor directly above is also being erected. In its resubmission of the Baseline Schedule, Navillus should confirm that this planned timing of the spray-on fireproofing and erection complies with NYC safety standards or it should revise the schedule accordingly.	Incorporated, spray-fireproofing activities were pushed after finishing the metal structure.
d. Missing Work	
The Baseline Schedule only contains an "Obtain Excavation & Shoring Permit" and an "Excavation – Drainage Work – Building Perimeter" activity. There are building excavation activities. In the resubmission of the Baseline Schedule, Navillus should either add building excavation activities or explain why they are not needed.	Incorporated, preliminary excavations & footing excavation for fence and playground equipment were added • CON-9140 "Excavation" • CON-9160 "Excavate for Footings - Playground Area & Fences - Building Perimeter"
e. Short Building Foundation Duration	

This 29-calendar-day foundation construction duration from October 15, 2025 to November 12, 2025, seems aggressive for the construction of the building foundation. In its resubmission of the Baseline Schedule, Navillus should provide a detailed explanation of the resources and number of crews it plans to use to complete this work in 29 calendar days or it should revise this work accordingly.	Incorporated: The durations for SOG and Concrete Beams & Walls have been increased.
f. Addendum 4	
The Baseline Schedule does not include any activities for the theatrical lighting. Navillus should add activities for the LED theatrical lighting in the gymatorium.	Incorporated, Activity CON-9150 “Install LED Theatrical Lighting -Gymnatorium” was added.
The Baseline Schedule does not include any activities for the 8-inch combined water service from 2nd Street or the 6-inch water service from 54th Avenue. Navillus should add activities as necessary to the schedule or confirm that the Baseline Schedule includes the required water service.	Incorporated, Activities CON-9170 “Install 8" Combined Water Service (2nd Street)- Drainage Work - Building Perimeter” & CON-9180 “Install 6" Fire Water Service (54th Avenue Street)- Drainage Work - Building Perimeter” were added to the schedule

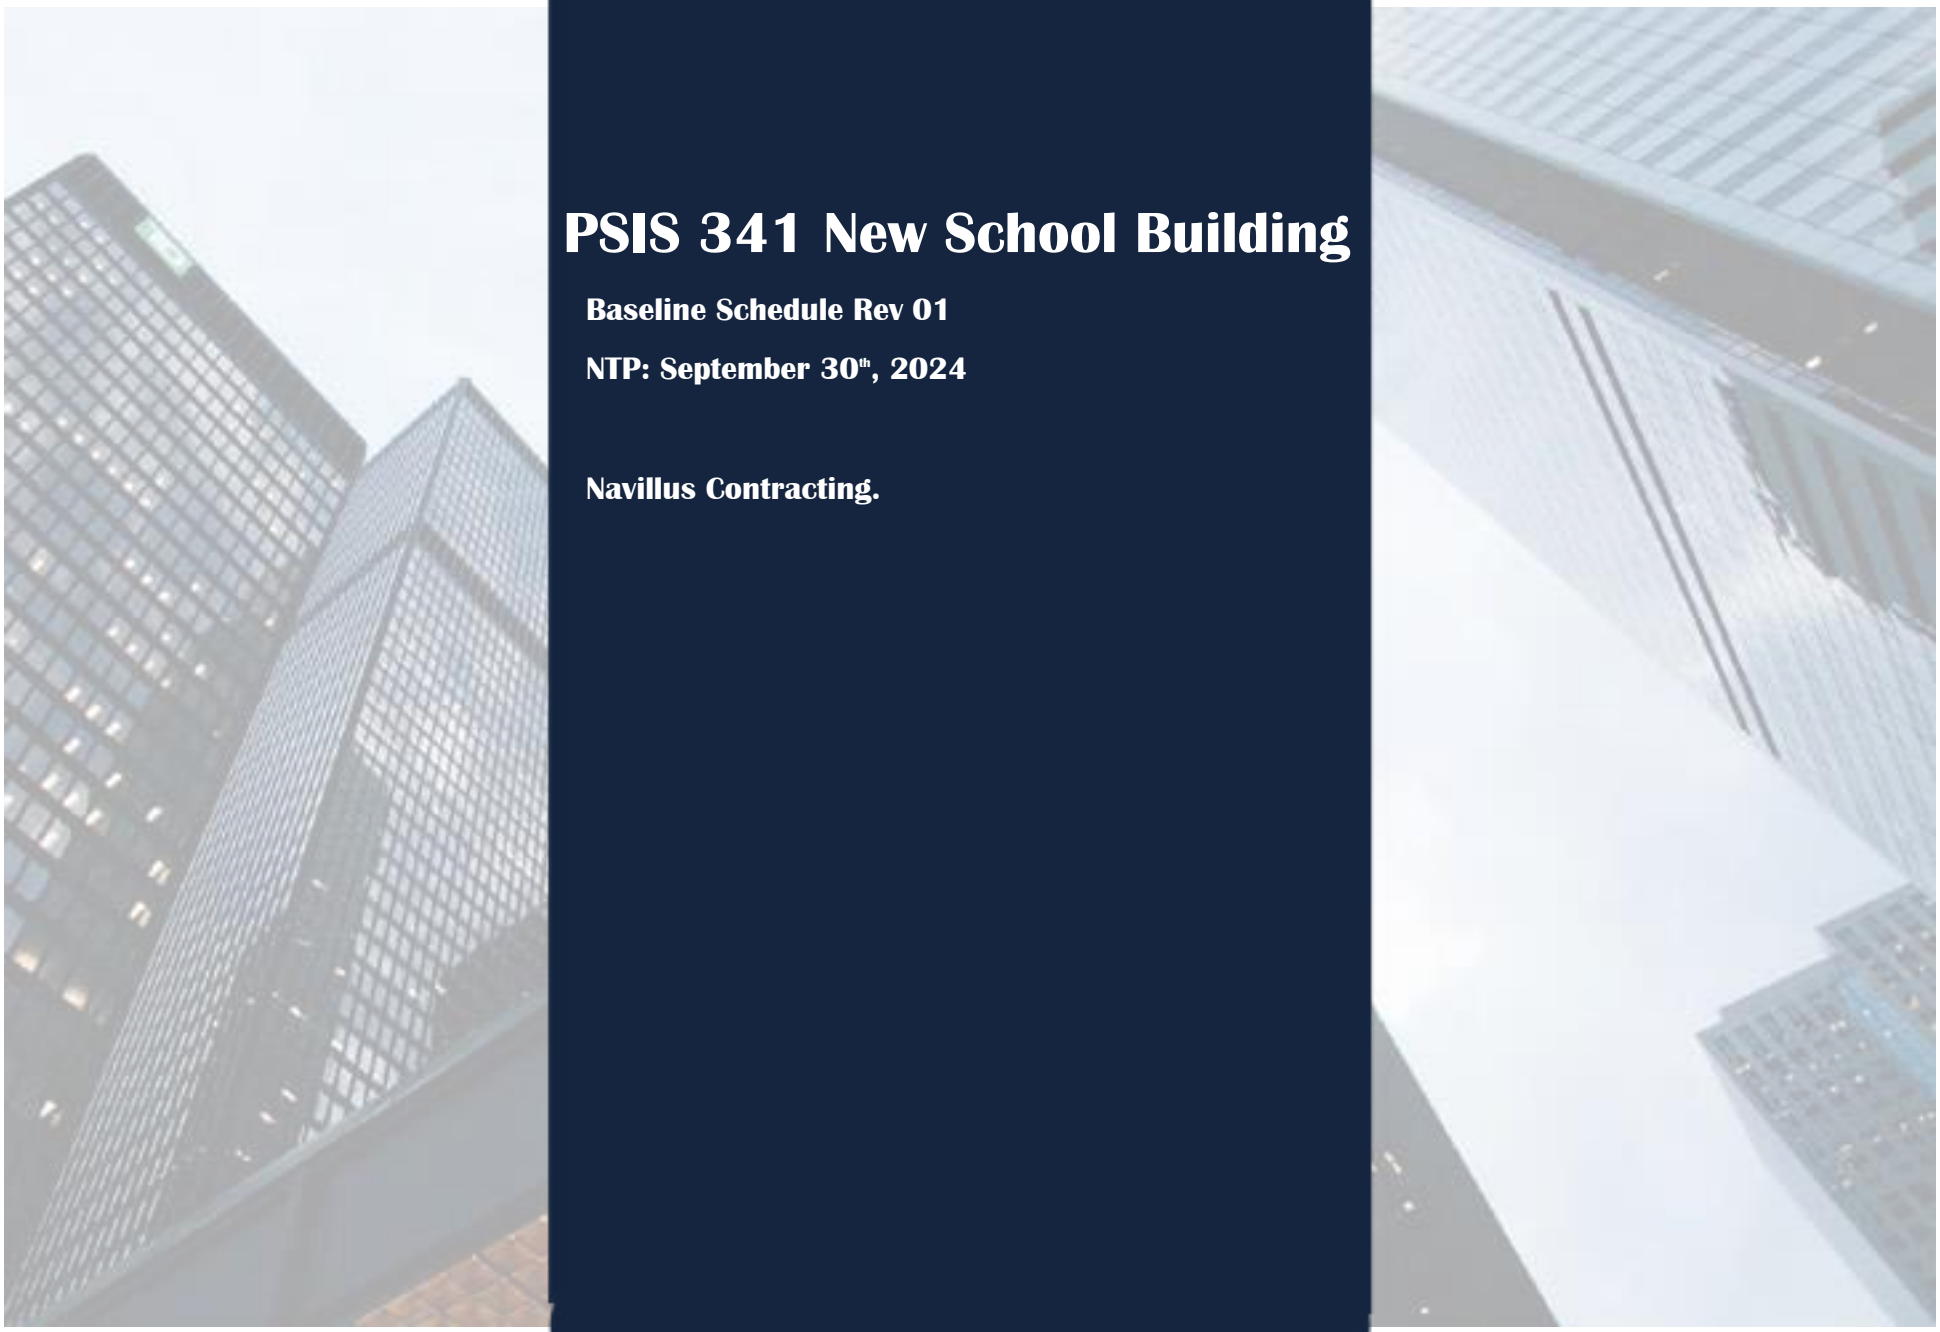

PSIS 341 New School Building

Baseline Schedule Rev 01

NTP: September 30th, 2024

Navillus Contracting.

PROJECS

TABLE OF CONTENTS

1 PROJECT DESCRIPTION 2
2 SCHEDULE METHODOLOGY 2
3 PROJECT DATA 2
4 ACTIVITIES ID STRUCTURE 2
5 WORK BREAKDOWN STRUCTURE 3
6 ACTIVITY CODES 3
7 PROJECT STATISTICS AND INFORMATION 13
8 KEY DATES & MILESTONES 13
9 STRATEGY OF WORKS 14
10 LONGEST PATH 14
11 ONE MONTH LOOKAHEAD 14
12 NEAR CRITICAL PATH 15
13 APPENDICES 16

1 Project Description

The work under this contract consists of construction works for the new school building starting with the superstructure steel and concrete works in addition to mechanical, electrical, architectural.

2 Schedule Methodology

This Schedule serves as the Project Baseline Schedule Rev 01. Primavera P6 was utilized as scheduling software. Schedule was utilized by developing the Critical Path Method (CPM). Durations were based on contractor best practice productivity from previous projects.

3 Project Data

NTP	September 30th, 2024
Construction Start	September 30th ,2025
TCO	October 19th ,2026
Substantial Completion Date	April 17th ,2027
Final Completion Date	August 15th ,2027

4 Activities ID Structure

Each activity has a unique ID and description based on letters and numbering criteria. The table below modifies the IDs applied to the activities:

Reference	Prefix	-	Suffix	Increment value
ID	AAA	Separator	0000	10

A=Alphabets
0=Number

4.1 Prefix

The below table is showing the three letters structure for the ID Prefix. Those letters were based on the scope, WBS, or activity type.

ID	Prefix
MIL	Key dates & Milestones
SUB	Submittals
APP	Approvals
DES	Design
PRO	Procurement
CON	Construction
CLO	Close-out

4.2 Suffix

It consists of four-digit numbers starting with value of 1000.

4.3 Increment value

It works as a counter for project activities with increment value of 10.

5 Work Breakdown Structure

The Project WBS was broken down into the presented levels below:

Pre-construction

This level contains Project Key dates and Milestones, Permits, mobilization activities and utilities coordination.

Procurement:

This level consists of different contractor's Submittals followed by Review/Approvals, as well as the fabrication, procurement and delivery of all item included in the project.

Construction:

This level consists of all the construction work under the scope of this project.

Close-Out:

This level consists of the close out activities including final inspection, punch list, final clean-up & demobilization.
Please refer to Appendix 1.

6 Activity Codes

The following activity codes are added to the project schedule:

- **P026453 - LOCN**

Code Value	Description
SITE	Site Work
FIRSTFL	First Floor
SECONDF	Second Floor
THIRD	Third Floor
FOURTH	Fourth Floor
FIFTHFL	Fifth Floor
ROOF	Roof
BULKHEA	Bulkhead
WESTELE	West Elevation
SOUTHEL	South Elevation
EASTELE	East Elevation
NORTHEL	North Elevation
MATERIA	Material Hoist Elevation

- **P026453 - AREA**

Code Value	Description
STE	Site Area
BLDG	Building Area
ELEV	Elevation Area

- **P026453 - PHAS**

Code Value	Description
Code Value	Description
PRECON	Preconstruction
PRECON.MIL	Milestones
PRECON.MIL.MAJMIL	Major Milestones
PRECON.MIL.CONTMIL	Contract Milestones
PRECON.PERM	Permits
PRECON.MOB	Mobilization
PRECON.UTILITY	Utilities Coordination
PRECON.UTILITY.GASCOOR	Gas Coordination
PRECON.UTILITY.TEMPPOR	Temporary Power Coordination

PRO	Procurement
PRO.SUB&APP	Submittals & Approvals
PRO.SUB&APP.DIV1	Division 01 - General Requirements
PRO.SUB&APP.DIV1.S01300	Spec Section S01300 - Submittals
PRO.SUB&APP.DIV1.S01311	Spec Section S01311 - Progress Schedule
PRO.SUB&APP.DIV1.S01352	Spec Section S01352 - Sustainability Requirements
PRO.SUB&APP.DIV1.S01400	Spec Section S01400 - Quality Control
PRO.SUB&APP.DIV1.S01426	Spec Section S01426 - Sample Classroom
PRO.SUB&APP.DIV1.S01500	Spec Section S01500 - Temporary Facilities and Controls
PRO.SUB&APP.DIV1.S01524	Spec Section S01524 - Construction Waste Management
PRO.SUB&APP.DIV1.S01535	Spec Section S01535 - Safety Program
PRO.SUB&APP.DIV1.S01550	Spec Section S01550 - Indoor Air Quality (IAQ) Requirements
PRO.SUB&APP.DIV1.S01560	Spec Section S01560 - Installation Sequence of Finish Materials
PRO.SUB&APP.DIV1.S01630	Spec Section S01630 - Product Substitutions
PRO.SUB&APP.DIV1.S01650	Spec Section S01650 - Facility Start-Up, Demonstration, and Training
PRO.SUB&APP.DIV1.S01660	Spec Section S01660 - Supplemental Comissioning Requirements
PRO.SUB&APP.DIV1.S01720	Spec Section S01720 - Record Documents
PRO.SUB&APP.DIV2	Division 02 - Site Work
PRO.SUB&APP.DIV2.02010	Spec Section 02010 - Environmental Site Assessment Reports
PRO.SUB&APP.DIV2.02070	Spec Section 02070 - Selective Removals & Demoloition
PRO.SUB&APP.DIV2.02100	Spec Section 02100 - Site Preparation
PRO.SUB&APP.DIV2.02200	Spec Section 02200 - Earthwork
PRO.SUB&APP.DIV2.02220	Spec Section 02220 - Gas Vapor Barrier (Fluid Applied)
PRO.SUB&APP.DIV2.02221	Spec Section 02221 - Sub-Slab Depressurization System
PRO.SUB&APP.DIV2.02250	Spec Section 02250 - Foundation & Other Change Adjustements
PRO.SUB&APP.DIV2.02511	Spec Section 02511 - Asphaltic Concrete Paving
PRO.SUB&APP.DIV2.02513	Spec Section 02513 - Sidewalk and Street Paving
PRO.SUB&APP.DIV2.02521	Spec Section 02521 - Concrete Curbs and Pavements
PRO.SUB&APP.DIV2.02721	Spec Section 02721 - Trench Drains

PRO.SUB&APP.DIV2.02722	Spec Section 02722 - PC Basins, Detention Basins, and Manholes
PRO.SUB&APP.DIV2.02723	Spec Section 02723 - Storm Drainage Systems
PRO.SUB&APP.DIV2.02831	Spec Section 02831 - Chain Link Fences & Gates
PRO.SUB&APP.DIV2.02860	Spec Section 02860 - Early Childhood Playground Equipment
PRO.SUB&APP.DIV2.02862	Spec Section 02862 - Outdoor Game Equipment
PRO.SUB&APP.DIV2.02870	Spec Section 02870 - Site Furnishings
PRO.SUB&APP.DIV2.02900	Spec Section 02900 - Landscaping
PRO.SUB&APP.DIV3	Division 03 - Concrete
PRO.SUB&APP.DIV3.03100	Spec Section 03100 - Concrete Formwork
PRO.SUB&APP.DIV3.03200	Spec Section 03200 - Concrete Reinforcement
PRO.SUB&APP.DIV3.03300	Spec Section 03300 - Cast in Place Concrete
PRO.SUB&APP.DIV3.03450	Spec Section 03450 - Precast Architectural Concrete
PRO.SUB&APP.DIV3.03542	Spec Section 03542 - Cement Based Self Leveling Underlayment
PRO.SUB&APP.DIV5-1	Division 04 - Masonry
PRO.SUB&APP.DIV5-1.05170	Spec Section 04200 - Unit Masonry
PRO.SUB&APP.DIV5-1.05500	Spec Section 04435 - Cast Stone
PRO.SUB&APP.DIV5	Division 05 - Metals
PRO.SUB&APP.DIV5.05120	Spec Section 05120 - Structural Steel
PRO.SUB&APP.DIV5.05170	Spec Section 05170 - Support System for Suspended Ceilings
PRO.SUB&APP.DIV5.05300	Spec Section 05300 - Metal Deck
PRO.SUB&APP.DIV5.05500	Spec Section 05500 - Metal Fabrications
PRO.SUB&APP.DIV5.05810	Spec Section 05810 - Prefabricated Expansion Joint Covers
PRO.SUB&APP.DIV6	Division 06 - Wood & Plastics
PRO.SUB&APP.DIV6.06200	Spec Section 06200 - Finish Carpentry
PRO.SUB&APP.DIV6.06410	Spec Section 06410 - Custom Casework
PRO.SUB&APP.DIV7	Division 07 - Thermal & Moisture Protection
PRO.SUB&APP.DIV7.07147	Spec Section 07147 - Crystalline Waterproofing
PRO.SUB&APP.DIV7.07211	Spec Section 07211 - Perimeter Foundation Insulation
PRO.SUB&APP.DIV7.07271	Spec Section 07271 - Self Adhering Sheet Air Barriers
PRO.SUB&APP.DIV7.07414	Spec Section 07414 - Metal Plate Wall Panels
PRO.SUB&APP.DIV7.07560	Spec Section 07560 - Fluid Applied Protected Membrane Roofing

PRO.SUB&APP.DIV7.07600	Spec Section 07600 - Flashing and Sheet Metal
PRO.SUB&APP.DIV7.07720	Spec Section 07720 - Roof Accessories
PRO.SUB&APP.DIV8	Division 08 - Doors & Windows
PRO.SUB&APP.DIV8.08110	Spec Section 08110 - Steel Doors and Frames
PRO.SUB&APP.DIV8.08210	Spec Section 08210 - Wood Doors
PRO.SUB&APP.DIV8.08524	Spec Section 08524 - Aluminum Windows & Entrances
PRO.SUB&APP.DIV8.08662	Spec Section 08662 - Security Screens & Barriers
PRO.SUB&APP.DIV8.08710	Spec Section 08710 - Finish Hardware
PRO.SUB&APP.DIV9	Division 09 - Finishes
PRO.SUB&APP.DIV9.09260	Spec Section 09260 - Gypsum Board Assemblies
PRO.SUB&APP.DIV9.09310	Spec Section 09310 - Ceramic Tiles
PRO.SUB&APP.DIV9.09510	Spec Section 09510 - Acoustical Ceilings
PRO.SUB&APP.DIV9.09590	Spec Section 09590 - Wood Flooring
PRO.SUB&APP.DIV9.09650	Spec Section 09650 - Resilient Flooring
PRO.SUB&APP.DIV9.09900	Spec Section 09900 - Painting
PRO.SUB&APP.DIV10	Division 10 - Specialties
PRO.SUB&APP.DIV10.10100	Spec Section 10100 - Visual Display Boards
PRO.SUB&APP.DIV10.10400	Spec Section 10400 - Identification Devices
PRO.SUB&APP.DIV10.10505	Spec Section 10505 - Metal Lockers
PRO.SUB&APP.DIV10.10522	Spec Section 10522 - Fire Extinguishers & Cabinets
PRO.SUB&APP.DIV10.10720	Spec Section 10720 - Window Guards
PRO.SUB&APP.DIV10.10810	Spec Section 10810 - Toilet & Bath Accessories
PRO.SUB&APP.DIV11	Division 11 - Equipment
PRO.SUB&APP.DIV11.11050	Spec Section 11050 - Library Equipment
PRO.SUB&APP.DIV11.11061	Spec Section 11061 - Platform Curtains & Auditorium Window Curtains
PRO.SUB&APP.DIV11.11172	Spec Section 11172 - Waste Handling Equipment
PRO.SUB&APP.DIV11.11400	Spec Section 11400 - Food Service Equipment
PRO.SUB&APP.DIV11.11450	Spec Section 11450 - Domestic Type Equipment
PRO.SUB&APP.DIV11.11480	Spec Section 11480 - Gymnasium Equipment
PRO.SUB&APP.DIV11.11600	Spec Section 11600 - Laboratory Equipement
PRO.SUB&APP.DIV12	Division 12 - Furnishings
PRO.SUB&APP.DIV12.12302	Spec Section 12302 - Manufactured Wood Casework
PRO.SUB&APP.DIV13	Division 13 - Special Construction
PRO.SUB&APP.DIV13.13487	Spec Section 13487 - Concrete Floating Floor Assembly

PRO.SUB&APP.DIV14	Division 14 - Conveying Systems
PRO.SUB&APP.DIV14.14211	Spec Section 14211 - Geared Traction Passenger Elevators
PRO.SUB&APP.DIV14.14420	Spec Section 14420 - Hydraulic Vertical Wheelchair Lifts
PRO.SUB&APP.DIV15A	Division 15A - Fire Protection
PRO.SUB&APP.DIV15A.15330	Spec Section 15330 - Sprinkler System
PRO.SUB&APP.DIV15A.15333	Spec Section 15333 - Fire Pumps - Sprinkler Booster Pumps
PRO.SUB&APP.DIV15B	Division 15B - Plumbing
PRO.SUB&APP.DIV15B.15410	Spec Section 15410 - Plumbing Piping
PRO.SUB&APP.DIV15B.15411	Spec Section 15411 - Hangers and Supports
PRO.SUB&APP.DIV15B.15415	Spec Section 15415 - Drainage
PRO.SUB&APP.DIV15B.15416	Spec Section 15416 - Gas Piping System
PRO.SUB&APP.DIV15B.15417	Spec Section 15417 - Cold Water Supply
PRO.SUB&APP.DIV15B.15418	Spec Section 15418 - Hot Water Supply
PRO.SUB&APP.DIV15B.15440	Spec Section 15440 - Plumbing Fixtures
PRO.SUB&APP.DIV15B.15451	Spec Section 15451 - Water Heaters
PRO.SUB&APP.DIV15B.15453	Spec Section 15453 - Pumping Apparatus & Tanks
PRO.SUB&APP.DIV15C	Division 15C - Mechanical
PRO.SUB&APP.DIV15C.15510	Spec Section 15510 - HVAC Piping
PRO.SUB&APP.DIV15C.15660	Spec Section 15660 - Packaged Modular Outdoor Chillers
PRO.SUB&APP.DIV15C.15565	Spec Section 15565 - Hot Water Condensing Boilers
PRO.SUB&APP.DIV15C.15783	Spec Section 15783 - Split Heat Pump System
PRO.SUB&APP.DIV15C.15836	Spec Section 15836 - Unit Heaters Cabinet Heaters
PRO.SUB&APP.DIV15C.15852	Spec Section 15852 - Air Handling Units
PRO.SUB&APP.DIV15C.15891	Spec Section 15891 - Metal Ductwork
PRO.SUB&APP.DIV15C.15540	Spec Section 15540 - HVAC Pumps
PRO.SUB&APP.DIV15C.15590	Spec Section 15590 - Emergency Generator System Accessories
PRO.SUB&APP.DIV15C.15940	Spec Section 15940 - Air Outlets & Inlets
PRO.SUB&APP.DIV15C.15970	Spec Section 15970 - Temperature Control System
PRO.SUB&APP.DIV15C.15594	Spec Section 15594 - Fuel Storage Equipment
PRO.SUB&APP.DIV15C.15596	Spec Section 15596 - Natural Gas Leak Detection Equipment
PRO.SUB&APP.DIV16	Division 16 - Electrical
PRO.SUB&APP.DIV16.16010	Spec Section 16010 - Gen Provisions for Elec Work

PRO.SUB&APP.DIV16.16120	Spec Section 16120 - Wiring Systems
PRO.SUB&APP.DIV16.16231	Spec Section 16231- Emergency Generator System
PRO.SUB&APP.DIV16.16425	Spec Section 16425 - Switch Boards & Panel Boards
PRO.SUB&APP.DIV16.16471	Spec Section 16471 - Auditorium & Television Studio Dimming System
PRO.SUB&APP.DIV16.16475	Spec Section 16475 - Overcurrent Protective Devices
PRO.SUB&APP.DIV16.16502	Spec Section 16502 - Interior Lighting Fixtures
PRO.SUB&APP.DIV16.16520	Spec Section 16520 - Illuminated Exit Sign
PRO.SUB&APP.DIV16.16720	Spec Section 16720 - Fire Detection Alarm System with COC
PRO.SUB&APP.DIV16.16785	Spec Section 16785 - Internet Protocol Digital Video Surveillance System using Digital Cameras
PRO.FAB&DEL	Fabrication & Delivery
CONSTR	Construction
CONSTR.FIRSTFL	First Floor
CONSTR.FIRSTFL.STR-1	SSDS
CONSTR.FIRSTFL.STR	Structure-1st Floor
CONSTR.FIRSTFL.MECH	Mechanical-1st Floor
CONSTR.FIRSTFL.MECH.HVAC	HVAC Rough-ins
CONSTR.FIRSTFL.MECH.MECHEQ	Mechanical Equipment
CONSTR.FIRSTFL.PLUMB	Plumbing-1st Floor
CONSTR.FIRSTFL.FIREPRO	Fire Protection-1st Floor
CONSTR.FIRSTFL.ELEC	Electrical-1st Floor
CONSTR.FIRSTFL.ARCH	Architecture-1st Floor
CONSTR.FIRSTFL.ARCH.INTWLLS	Interior Walls
CONSTR.FIRSTFL.ARCH.CEILL	Ceiling
CONSTR.FIRSTFL.ARCH.FINSHES	Finishes
CONSTR.SECOND	Second Floor
CONSTR.SECOND.STR	Structure-2nd Floor
CONSTR.SECOND.MECH	Mechanical-2nd Floor
CONSTR.SECOND.MECH.HVAC	HVAC Rough-ins
CONSTR.SECOND.MECH.MECHEQ	Mechanical Equipment
CONSTR.SECOND.PLUMB	Plumbing-2nd Floor
CONSTR.SECOND.FIREPRO	Fire Protection-2nd Floor
CONSTR.SECOND.ELEC	Electrical-2nd Floor
CONSTR.SECOND.ARCH	Architecture-2nd Floor
CONSTR.SECOND.ARCH.INTWLLS	Interior Walls
CONSTR.SECOND.ARCH.CEILL	Ceiling
CONSTR.SECOND.ARCH.FINSHES	Finishes
CONSTR.THIRD	Third Floor
CONSTR.THIRD.STR	Structure-3rd Floor
CONSTR.THIRD.MECH	Mechanical-3rd Floor
CONSTR.THIRD.MECH.HVAC	HVAC Rough-ins
CONSTR.THIRD.MECH.MECHEQ	Mechanical Equipment
CONSTR.THIRD.PLUMB	Plumbing-3rd Floor
CONSTR.THIRD.FIREPRO	Fire Protection-3rd Floor

CONSTR.THIRD.ELEC	Electrical-3rd Floor
CONSTR.THIRD.ARCH	Architecture-3rd Floor
CONSTR.THIRD.ARCH.INTWLLS	Interior Walls
CONSTR.THIRD.ARCH.CEILL	Ceiling
CONSTR.THIRD.ARCH.FINSHES	Finishes
CONSTR.FOURTH	Fourth Floor
CONSTR.FOURTH.STR	Structure-4th Floor
CONSTR.FOURTH.MATHOIS	Material Hoist
CONSTR.FOURTH.MECH	Mechanical-4th Floor
CONSTR.FOURTH.MECH.HVAC	HVAC Rough-ins
CONSTR.FOURTH.MECH.MECHEQ	Mechanical Equipment
CONSTR.FOURTH.PLUMB	Plumbing-4th Floor
CONSTR.FOURTH.FIREPRO	Fire Protection-4th Floor
CONSTR.FOURTH.ELEC	Electrical-4th Floor
CONSTR.FOURTH.ARCH	Architecture-4th Floor
CONSTR.FOURTH.ARCH.INTWLLS	Interior Walls
CONSTR.FOURTH.ARCH.CEILL	Ceiling
CONSTR.FOURTH.ARCH.FINSHES	Finishes
CONSTR.FIFTH	Fifth Floor
CONSTR.FIFTH.STR	Structure-5th Floor
CONSTR.FIFTH.MECH	Mechanical-5th Floor
CONSTR.FIFTH.MECH.HVAC	HVAC Rough-ins
CONSTR.FIFTH.MECH.MECHEQ	Mechanical Equipment
CONSTR.FIFTH.PLUMB	Plumbing-5th Floor
CONSTR.FIFTH.FIREPRO	Fire Protection-5th Floor
CONSTR.FIFTH.ELEC	Electrical-5th Floor
CONSTR.FIFTH.ARCH	Architecture-5th Floor
CONSTR.FIFTH.ARCH.INTWLLS	Interior Walls
CONSTR.FIFTH.ARCH.CEILL	Ceiling
CONSTR.FIFTH.ARCH.FINSHES	Finishes
CONSTR.ROOF	Roof Floor
CONSTR.ROOF.STR	Structure -Roof
CONSTR.ROOF.MECH	Mechanical -Roof
CONSTR.ROOF.ELEC	Electrical -Roof
CONSTR.ROOF.FREPRT	Fire Protection -Roof
CONSTR.BULKHED	Bulkhead
CONSTR.BULKHED.STR	Structure -Bulkhead
CONSTR.BULKHED.FIREPRO	Mechanical -Bulkhead
CONSTR.ELEV	Elevations
CONSTR.ELEV.WESTELV	West Elevation
CONSTR.ELEV.SOUTHEL	South Elevation
CONSTR.ELEV.EASTELE	East Elevation
CONSTR.ELEV.NORTHEL	North Elevation
CONSTR.ELEV.MATHOIS	Material Hoist Elevation
CONSTR.ROOFING	Roofing
CONSTR.ROOFING.5thFLR	5th Floor
CONSTR.ROOFING.MAINROF	Main Roof
CONSTR.SPECIAL	Special Rooms
CONSTR.SPECIAL.ELECSWI	Fuel Oil Room-1st Floor
CONSTR.SPECIAL.ELECSRO	Electrical Service Room - 1st Floor
CONSTR.SPECIAL.MDFRM	MDF Room 127A -1st Floor
CONSTR.SPECIAL.GYM	Gymatorium - 4th Floor
CONSTR.SPECIAL.BOILERM	Boiler Room - 5th Floor

CONSTR.SPECIAL.ELEVRM	Elevator Machine Room - Roof Floor
CONSTR.MOCKUP	Mockup Room
CONSTR.SITEWOR	Site Work
CONSTR.SITEWOR.54tTHAV	54th Avenue Street
CONSTR.SITEWOR.2NDST	2ND Street
CONSTR.SITEWOR.PREM	Perimeter of New Building
CLO	Close-Outs
CLO.INSPEC	Inspections
CLO.TESTING	Testing
CLO.TCO	TCO
Code Value	Description

- **Subcontractors Trades**

Code Value	Description
GEN	General
PRECON	Preconstruction
PRECON.SUB	Submittals
PRECON.APP	Approvals
PRECON.PERM	Permits
PRECON.PRO	Procurements
PRECON.UTILITY	Utilities Coordination
PRE&DEM	Preliminary
SSDS	SSDS System
UNDEREL	SOG
FLOORDR	Floor Drains
STEEL	Structural Steel Work
SLABS	Metal Deck Concrete Slabs
MEPHANG	MEP Hangers
FIREPRO	Fireproofing Spray
MATHOIS	Material Hoist
TEMPSTA	Temporary Standpipe
LAYOUT	Layout
MASON	Masonry
DCTRIS	Duct Risers
MECHRIS	Mechanical Risers
DUCTLEK	Duct Leak Test
DUCTRO	Duct Rough-ins
T&BTRAC	Top & Bottom Track
VAVBOX	VAV Boxes & Sound Attenuator
PLUMRIS	Plumbing Risers
INTFRAM	Interior Wall Framing
ELECRIS	Electrical Risers
ELECRIS.POWRIS	Power Risers
ELECRIS.LOWVOL	Low Voltage Risers
MECHPIP	Mechanical Piping Rough-ins
MECHPIP.HWPIPIN	Hot Water Piping
MECHPIP.CHGLPIP	Chilled Glycol Piping
MECHPIP.REFRIGR	Refrigerant Piping
ELEV	Elevations
ELEV.MOCK	Elevations Mock-Up
ELEV.PRESP	Precast Sandwich Panel
ELEV.WINDOWS	Windows
MEPEQ	MEP Equipment
SPECROM	Special Rooms
SPECROM.ELEVMAC	Elevator Machine Room-Roof Floor
SPECROM.IDFRO	IDF ROOM
SPECROM.BOILER	Boiler Room-5th Floor

SPECROM.MDF	MDF Room -1st Floor
SPECROM.ELECROM	Electrical Service Room-1st Floor
SPECROM.FUELOIL	Fuel Oil Room-1st Floor
SPECROM.(New)	Gymatorium -4th Floor
ELECROU	Electrical Rough-ins
ELECROU.COND	Conduits Rough-ins
ELECROU.COND.POWERRO	Power Conduits
ELECROU.COND.LOWVOLT	Low Voltage Conduits
ELECROU.WIREPUL	Wire Pulling
ELECROU.WIREPUL.POWER	Power Wires
ELECROU.WIREPUL.LOWVOLT	Low Voltage Wires
ROOFTOP	Roof Top Units
CEILFRA	Ceiling Framing
ROOFING	Roofing
ROOFING.5thROOF	5th Floor Roof
ROOFING.MAINROO	Main Roof
ELEFI	Electrical Finishes
ELEFI.WIRD	Wiring Devices
ELEFI.LIGHFI	Lighting Fixtures
ELEFI.IPDVSD	IPDVS Devices
ELEFI.FIALASD	Fire Alarm Sensors and Devices
PLUMBRO	Plumbing Piping Rough-ins
PLUMBRO.Gas	Gas Piping
PLUMBRO.WATER	Water Piping
PLUMBRO.SANITAR	Sanitary Piping
PLUMBRO.STORM	Storm Piping
PLUMBRO.TESTING	Plumbing Testing
PLUMBRO.PLUMBIN	Plumbing Insulation
PLUMBRO.PUMP	Pumps
PLUMBRO.FUELOIL	Fuel Oil Piping
TESTING	Testing & Commissioning
SPRROUG	Sprinkler Rough-ins
SPRROUG.STANDPI	Stand Pipes
SPRROUG.MAINSPR	Main Sprinkler Pipes
SPRROUG.BRANCH	Branch Sprinkler Pipes
SPRROUG.SPRINKH	Sprinkler Heads
SPRROUG.CONTOLV	Control Valve Assembly
SPRROUG.AIRTEST	Air Testing
SITEWOR	Site Work
SITEWOR.PERIMET	Perimeter of New Building
SITEWOR.202NDST	54th Avenue Street
SITEWOR.10THAVE	2nd Street
DUCTINS	Duct Insulations
MOCKUP	Mockup Room
EMERG	Emergency Generator
GYPBORW	Gypsum Board Walls
FIRESTO	Firestopping
GYPWCEI	Gypsum Board Ceiling
WALLTIL	Wall Tiles
1STCOAT	1st Coat Painting
INTRSYS	Intrusion System
AUXSYS	Auxiliary System
SOUCLSY	Sound Clock System
DOORS&F	Doors & Frames
ACOUSTI	Acoustical Ceiling Tiles
FLOORIN	Flooring
PLUMBFI	Plumbing Finishes
FINLCOA	Final Coat Painting
FURN&MI	Furniture & Milling Work

SIGNAGE	Signages
DEMO	Demobilization

- **TRAD**

Code Value	Description
DIV01	DIV01-General Requirements
DIV02	DIV02-Existing Conditions
DIV03	DIV03-Concrete
DIV04	DIV04-Masonry
DIV05	DIV05-Metals
DIV06	DIV06-Wood & Plastics
DIV07	DIV07-Thermal & Moisture Protection
DIV08	DIV08-Doors & Windows
DIV09	DIV09-Finishes
DIV10	DIV10-Specialties
DIV11	DIV11-Equipment
DIV12	DIV12-Furnishing
DIV13	DIV13-Special Construction
DIV14	DIV14-Conveying Systems
DIV 15A	DIV 15A-Fire Protection
DIV 15B	DIV 15B-Plumbing
DIV 15C	DIV 15C-Mechanical
DIV 16	DIV 16-Electrical

- **RESP**

Code Value	Description
OWNER	SCA / Government
CONC	Navillus
LAB	Farley
CON-ED	CON-ED
GASVAP	EAI Inc.
STELSTR	Weir Welding
PLMB	Eagle 1 Mechanical
HVAC	Grand Mechanical Corp.
CONVSYS	Noble Elevators
ELEC	RMD Electric
FREPROF	Fine Group
ARCH	Coreslab Structures
WINDOW	Basec Corp
FLAG	Poletech
DOOR	Arch Mills
PAINT	Roebell
VCT	Pyramid
STEUTL	MFM Contracting
BATH	Nu-Tech Furnishing
CASEWRK	Elli
BLEACH	ACME
GRILLES	City Gates
FENCE	Eagle Fence
KTCHN	Samtell
MISC	FMB Steel
SHOPEQ	Penn Equipment

7 Project Statistics and Information

7.1 Schedule Summary and Log

Scheduling	Yes
Levelling	No
Ignore relationships to and from other projects	No
Make open-ended activities critical	No
Use Expected Finish Dates	Yes
Schedule automatically when a change affects date	Yes
Level resources during scheduling	No
Recalculate assignment costs after scheduling	Yes
When scheduling progressed activities use	Retained Logic
Calculate start-to-start lag from	Early Start
Define critical activities as Total Float	Longest Path
Compute Total Float As	Finish Float
Calculate float based on finish date of	Each project
Calendar for scheduling Relationship Lag	Predecessor Activity Calendar

7.2 Schedule statistics

Activities	1329
Not Started	1329
In Progress	0
Completed	0
Relationships	3266
Activities with Constraint	6

7.3 Open Ends Activities

Activity ID	Activity Description	Open end Type
MIL-1000	NTP	No Predecessor
MIL-1560	Final Completion	No Successor

7.4 Calendars

P026453 - 5 Days Calendar	5 Working Days* calendar with weekends and holidays. Assigned for some of the activities
P026453 - 7 Days Calendar	Calendar with 7 Working Days assigned for procurement, milestones and similar activities

*Working Hours: 8hrs/day

8 Key dates & Milestones

Activity ID	Activity Name	Start	Finish
MIL-1000	NTP	30-Sep-24	-
MIL-1030	Project Duration(From NTP till TCO)	30-Sep-24	19-Oct-26

MIL-1040	Project Duration(From NTP till Substantial Completion)	30-Sep-24	17-Apr-27
MIL-1770	Project Duration(From NTP till Final Completion)	30-Sep-24	15-Aug-27
CON-9700	Site Access	30-Sep-24	29-Sep-25
MIL-1850	Construction Start	30-Sep-25	-
MIL-1600	MDF Work Finish	-	21-Jul-26*
MIL-1610	IDF Work Finish	-	21-Jul-26*
MIL-1620	IPDVS Work Finish	-	18-Sep-26 *
MIL-1510	TCO	-	19-Oct-26*
MIL-1550	Substantial Completion	-	17-Apr-27*
MIL-1560	Final Completion	-	15-Aug-27*

9 Strategy of works

After the Notice to Proceed (NTP) for the project, site access will be restricted for 365 calendar days. During this period, all necessary submittals, approvals, and permits will be obtained. Followed by preliminary activities such as mobilization and site preparation.

Once these preliminary works are completed, the SSDS system will be implemented, followed by the construction of the slab-on-grade (SOG). The project will then progress to the main structural works, including the installation of steel columns, framing beams, trusses, and metal deck concrete slabs.

Upon completing the structural phase, the project will branch into two parallel paths. The first path focuses on ensuring the building is watertight by installing the elevations, windows, and completing the roofing works. The second path concentrates on the rough-ins, starting with mechanical rough-ins, followed by electrical and plumbing systems.

After achieving a watertight state, a mock-up room will be constructed to initiate the gypsum board work, along with internal architectural, electrical, and mechanical finishes. These tasks will lead to the final project closeout phase.

10 Longest path

The critical path is determined as the schedule longest path, starting with obtaining permits, followed by mobilization and site preparation. This is followed by the implementation of the SSDS system, after which the superstructure works are carried out. Next, the installation of elevations and roofing works ensures the building is sealed. The process continues with the execution of the mockup room, followed by architectural finishes and site works, leading to project closeout and final completion.

Please refer to Appendix # 7.

11 One month lookahead

The one month lookahead contains the project submittals and approvals.

Please refer to Appendix #8.

12 Near Critical Path

The near-critical path includes various mechanical, plumbing, fire protection, electrical, and architectural works across all floors. It also involves the installation of windows and storefronts, as well as work on the MDF room, gymatorium, 2nd Street, and the building perimeter.

Please refer to Appendix #9.

13 Appendices

APPENDIX 1 – WBS Layout

APPENDIX 2 – Full Schedule Layout

APPENDIX 3 – Full Schedule Layout Grouped by LOCN Code

APPENDIX 4 – Full Schedule Layout Grouped by Area Code

APPENDIX 5 – Full Schedule Layout Grouped by PHAS Code

APPENDIX 6 – Full Schedule Layout Grouped by Subcontractor Trades

APPENDIX 7 – Full Schedule Layout Grouped by TRAD Code

APPENDIX 8 – Full Schedule Layout Grouped by RESP Code

APPENDIX 9 – Longest Path Layout

APPENDIX 10 – One Month Lookahead

APPENDIX 11 – Near Critical Path

APPENDIX 12 - Activity Report

APPENDIX 13 – Total Float Report

APPENDIX 14 – Schedule Log

APPENDIX 1
WBS Layout

WBS Layout

Activity ID	Activity Name
	New Building PS/IS 341Q - Baseline Schedule Rev 01
	Pre-construction
	Milestones
	Major Milestones
	Contract Milestones
	Permits
	Mobilization
	Utilities Coordination
	Gas Coordination
	Temporary Electrical Power
	Permanent Electrical Power
	Procurement
	Submittals & Approvals
	Division 01 - General Requirements
	Spec Section S01300 - Submittals
	Spec Section S01311 - Progress Schedule
	Spec Section S01352 - Sustainability Requirements
	Spec Section S01400 - Quality Control
	Spec Section S01426 - Sample Classroom
	Spec Section S01500 - Temporary Facilities and Controls
	Spec Section S01524 - Construction Waste Management
	Spec Section S01535 - Safety Program
	Spec Section S01550 - Indoor Air Quality (IAQ) Requirements
	Spec Section S01560 - Installation Sequence of Finish Materials
	Spec Section S01630 - Product Substitutions
	Spec Section S01650 - Facility Start-Up, Demonstration, and Training
	Spec Section S01660 - Supplemental Commissioning Requirements
	Spec Section S01720 - Record Documents
	Division 02 - Site Work
	Spec Section 02010 - Environmental Site Assessment Reports
	Spec Section 02070 - Selective Removals & Demoloition
	Spec Section 02090 - Environmental Management Of Excavated Material And Fill/Backfill
	Spec Section 02200 - Earthwork
	Spec Section 02100 - Site Preparation
	Spec Section 02220 - Gas Vapor Barrier (Fluid Applied)
	Spec Section 02221 - Sub-Slab Depressurization System
	Spec Section 02250 - Foundation & Other Change Adjustements
	Spec Section 02260 - Excavation Support And Monitoring
	Spec Section 02511 - Asphaltic Concrete Paving
	Spec Section 02513 - Sidewalk and Street Paving
	Spec Section 02521 - Concrete Curbs and Pavements
	Spec Section 02721 - Trench Drains
	Spec Section 02722 - PC Basins, Detention Basins, and Manholes
	Spec Section 02723 - Storm Drainage Systems
	Spec Section 02831 - Chain Link Fences & Gates
	Spec Section 02860 - Early Childhood Playground Equipment
	Spec Section 02862 - Outdoor Game Equipment
	Spec Section 02870 - Site & Street Furnishings
	Spec Section 02900 - Landscaping
	Division 03 - Concrete
	Spec Section 03100 - Concrete Formwork
	Spec Section 03200 - Concrete Reinforcement
	Spec Section 03300 - Cast in Place Concrete
	Spec Section 03450 - Precast Architectural Concrete
	Spec Section 03542 - Cement Based Self Leveling Underlayment
	Division 04 - Masonry
	Spec Section 04200 - Unit Masonry
	Spec Section 04435 - Cast Stone
	Division 05 - Metals
	Spec Section 05120 - Structural Steel
	Spec Section 05170 - Support System for Suspended Ceilings
	Spec Section 05300 - Metal Deck
	Spec Section 05500 - Metal Fabrications
	Spec Section 05710 - Steel Stairs
	Spec Section 05700 - Ornamental Metal
	Spec Section 05810 - Prefabricated Expansion Joint Covers
	Division 06 - Wood & Plastics
	Spec Section 06200 - Finish Carpentry
	Spec Section 06410 - Custom Casework
	Division 07 - Thermal & Moisture Protection
	Spec Section 07147 - Crystalline Waterproofing
	Spec Section 07211 - Perimeter Foundation Insulation

WBS Layout

Activity ID	Activity Name
	Spec Section 07271 - Self Adhering Sheet Air Barriers
	Spec Section 07414 - Metal Plate Wall Panels
	Spec Section 07560 - Fluid Applied Protected Membrane Roofing
	Spec Section 07600 - Flashing and Sheet Metal
	Spec Section 07720 - Roof Accessories
	Division 08 - Doors & Windows
	Spec Section 08110 - Steel Doors and Frames
	Spec Section 08210 - Wood Doors
	Spec Section 08330 - Coiling Doors, Grilles And Shutters
	Spec Section 08411 - Aluminum Framed Entrances And Storefronts
	Spec Section 08521 - Fire Rated Glazing Systems
	Spec Section 08524 - Aluminum Projected Windows
	Spec Section 08662 - Security Screens & Barriers
	Spec Section 08710 - Finish Hardware
	Spec Section 08730 - Thresholds, Weatherstripping And Seals
	Spec Section 08800 - Miscellaneous Glazing
	Division 09 - Finishes
	Spec Section 09260 - Gypsum Board Assemblies
	Spec Section 09310 - Ceramic Tiles
	Spec Section 09510 - Acoustical Ceilings
	Spec Section 09590 - Wood Flooring
	Spec Section 09650 - Resilient Flooring
	Spec Section 09800 - Special Coatings
	Spec Section 09860 - Grafiti Resistant Coatings
	Spec Section 09900 - Painting
	Division 10 - Specialties
	Spec Section 10100 - Visual Display Boards
	Spec Section 10350 - Flagpole
	Spec Section 10400 - Identification Devices
	Spec Section 10415 - Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases
	Spec Section 10505 - Metal Lockers
	Spec Section 10522 - Fire Extinguishers & Cabinets
	Spec Section 10605 - Wire Mesh Work
	Spec Section 10675 - Metal Storage Shelving
	Spec Section 10720 - Window Guards
	Spec Section 10810 - Toilet & Bath Accessories
	Spec Section 10830 - Mirrors
	Spec Section 10840 - Grab Bars
	Division 11 - Equipment
	Spec Section 11050 - Library Equipment
	Spec Section 11061 - Platform Curtains & Auditorium Window Curtains
	Spec Section 11172 - Waste Handling Equipment
	Spec Section 11400 - Food Service Equipment
	Spec Section 11450 - Domestic Type Equipment
	Spec Section 11480 - Gymnasium Equipment
	Spec Section 11500 - Shop Equipment
	Spec Section 11600 - Laboratory Equipment
	Division 12 - Furnishings
	Spec Section 12761 - Bleachers
	Spec Section 12302 - Manufactured Wood Casework
	Division 13 - Special Construction
	Spec Section 13487 - Concrete Floating Floor Assembly
	Division 14 - Conveying Systems
	Spec Section 14211 - Geared Traction Passenger Elevators
	Spec Section 14420 - Hydraulic Vertical Wheelchair Lifts
	Division 15 - Mechanical
	Division 15A - Fire Protection
	Spec Section 15330 - Sprinkler System
	Spec Section 15333 - Fire Pumps - Sprinkler Booster Pumps
	Division 15B - Plumbing & Drainage
	Spec Section 15410 - Plumbing Piping
	Spec Section 15411 - Hangers and Supports
	Spec Section 15412 - Valves
	Spec Section 15414 - Tests
	Spec Section 15415 - Drainage
	Spec Section 15416 - Gas Piping System
	Spec Section 15417 - Cold Water Supply
	Spec Section 15418 - Hot Water Supply
	Spec Section 15431 - Tags, Charts, And Identification
	Spec Section 15432 - Miscellaneous
	Spec Section 15440 - Plumbing Fixtures
	Spec Section 15451 - Water Heaters
	Spec Section 15453 - Pumping Apparatus & Tanks

WBS Layout

Activity ID	Activity Name
	Division 15C - Heating & Ventilation & Air Conditioning
	Spec Section 15510 - HVAC Piping
	Spec Section 15511 - Valves (Hvac)
	Spec Section 15512 - Piping Insulation (Hvac)
	Spec Section 15513 - Equipment Insulation (Hvac)
	Spec Section 15514 - Ductwork Insulation
	Spec Section 15515 - Hydronic Specialties
	Spec Section 15517 - Water Treatment For Hydronic Systems
	Spec Section 15540 - HVAC Pumps
	Spec Section 15565 - Hot Water Condensing Boilers
	Spec Section 15570 - Boiler Accessories
	Spec Section 15575 - Breeching Chimney Connectors And Chimneys
	Spec Section 15792 - Coils
	Spec Section 15835 - Convectors
	Spec Section 15838 - Fan Coil Units
	Spec Section 15839 - Door Air Curtains
	Spec Section 15860 - Centrifugal Fans
	Spec Section 15885 - Air Filters
	Spec Section 15590 - Emergency Generator System Accessories
	Spec Section 15594 - Fuel Storage Equipment
	Spec Section 15596 - Natural Gas Leak Detection Equipment
	Spec Section 15660 - Packaged Modular Outdoor Chillers
	Spec Section 15670 - Plate Heat Exchangers
	Spec Section 15783 - Split Heat Pump System
	Spec Section 15836 - Unit Heaters Cabinet Heaters
	Spec Section 15852 - Air Handling Units
	Spec Section 15891 - Metal Ductwork
	Spec Section 15940 - Air Outlets & Inlets
	Spec Section 15970 - Temperature Control System
	Spec Section 15910 - Duct Accessories
	Spec Section 15915 - Damper Assemblies
	Spec Section 15935 - Air Handling Units For Public Assembly Spaces
	Spec Section 15930 - Variable Air Terminals
	Spec Section 15973 - Facility Management Systems Integration
	Division 16 - Electrical
	Spec Section 16010 - Gen Provisions for Elec Work
	Spec Section 16120 - Wiring Systems
	Spec Section 16145 - Lighting Control Devices
	Spec Section 16231- Emergency Generator System
	Spec Section 16289 - Surge Protective Devices
	Spec Section 16420 - Service Entrance Equipment
	Spec Section 16441- Enclosed Switches
	Spec Section 16480 - Motors, Motor Control Centers, Starters And Control Equipment
	Spec Section 16425 - Switch Boards & Panel Boards
	Spec Section 16471 - Auditorium & Television Studio Dimming System
	Spec Section 16475 - Overcurrent Protective Devices
	Spec Section 16502 - Interior Lighting Fixtures
	Spec Section 16520 - Illuminated Exit Sign
	Spec Section 16670 - Lightning Protection
	Spec Section 16720 - Fire Detection Alarm System with COC
	Spec Section 16728 - Fiber Optic Cabling System
	Spec Section 16770 - Sound, Intercom & Teacher Activated Security System
	Spec Section 16771 - Projection And Interactive Whiteboard Systems
	Spec Section 16785 - Internet Protocol Digital Video Surveillance System using Digital Cameras
	Spec Section 16791 - Self-Corrective Clock System
	Spec Section 16855 - Heat Trace Cable System
	Fabrication & Delivery
	Construction
	First Floor
	SSDS
	Structure-1st Floor
	Mechanical- 1st Floor
	HVAC Rough-ins-1st Floor
	Mechanical Equipment-1st Floor
	Plumbing-1st Floor
	Fire Protection-1st Floor
	Electrical-1st Floor
	Architecture-1st Floor
	Interior Walls-1st Floor
	Ceiling-1st Floor
	Finishes-1st Floor
	Second Floor
	Structure-2nd Floor

WBS Layout

Activity ID	Activity Name
	Material Hoist
	Mechanical-2nd Floor
	HVAC Rough-ins-2nd Floor
	Mechanical Equipment-2nd Floor
	Plumbing-2nd Floor
	Electrical-2nd Floor
	Fire Protection-2nd Floor
	Architecture-2nd Floor
	Interior Walls-2nd Floor
	Ceiling-2nd Floor
	Finishes-2nd Floor
	Third Floor
	Structure -3rd Floor
	Mechanical -3rd Floor
	HVAC Rough-ins -3rd Floor
	Mechanical Equipment -3rd Floor
	Plumbing -3rd Floor
	Electrical -3rd Floor
	Fire Protection -3rd Floor
	Architecture -3rd Floor
	Interior Walls -3rd Floor
	Ceiling -3rd Floor
	Finishes -3rd Floor
	Fourth Floor
	Structure -4th Floor
	Mechanical-4th Floor
	HVAC Rough-ins-4th Floor
	Mechanical Equipment-4th Floor
	Plumbing-4th Floor
	Electrical-4th Floor
	Fire Protection-4th Floor
	Architecture-4th Floor
	Interior Walls-4th Floor
	Ceiling-4th Floor
	Finishes-4th Floor
	Fifth Floor
	Structure -5th Floor
	Mechanical -5th Floor
	HVAC Rough-ins -5th Floor
	Mechanical Equipment -5th Floor
	Plumbing -5th Floor
	Electrical -5th Floor
	Fire Protection -5th Floor
	Architecture -5th Floor
	Interior Walls -5th Floor
	Ceiling -5th Floor
	Finishes -5th Floor
	Roof
	Structure -Roof Floor
	Mechanical-Roof Floor
	Electrical-Roof Floor
	Fire Protection -Roof Floor
	Bulkhead
	Structure-Bulkhead
	Mechanical - Bulkhead
	Elevations
	West Elevation
	South Elevation
	East Elevation
	North Elevation
	Roofing
	5th Floor
	Main Roof
	Special Rooms
	Fuel Oil Room-1st Floor
	Electrical Service Room -1st Floor
	MDF Room 127A -1st Floor
	Gymatorium - 4th Floor
	Boiler Room - 5th Floor
	Elevator Machine Room & Shaft -Roof Floor
	Mockup Room
	Site Work
	54th Avenue Street

WBS Layout

Activity ID	Activity Name
	2ND Street
	Building Perimeter
	Drainage Work
	Playground Area & Fences
	Close-out
	Special Inspection
	Testing & Commissioning
	Demobilization

APPENDIX 2
Full Schedule Layout

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
New Building PS/IS 341Q - Baseline Schedule Rev 01		699	30-Sep-24	15-Aug-27
Pre-construction		699	30-Sep-24	15-Aug-27
Milestones		699	30-Sep-24	15-Aug-27
Major Milestones		699	30-Sep-24	15-Aug-27
MIL-1000	NTP	0	30-Sep-24	
MIL-1030	Project Duration(From NTP till TCO)	750	30-Sep-24	19-Oct-26
MIL-1040	Project Duration(From NTP till Substantial Completion)	930	30-Sep-24	17-Apr-27
MIL-1770	Project Duration(From NTP till Final Completion)	1050	30-Sep-24	15-Aug-27
MIL-2522	Site Access	365	30-Sep-24	29-Sep-25
MIL-1850	Construction Start	0	30-Sep-25	
MIL-1600	MDF Work Finish	0		21-Jul-26*
MIL-1610	IDF Work Finish	0		21-Jul-26*
MIL-1620	IPDVS Work Finish	0		18-Sep-26*
MIL-1510	TCO	0		19-Oct-26*
MIL-1550	Substantial Completion	0		17-Apr-27*
MIL-1560	Final Completion	0		15-Aug-27*
Contract Milestones		638	11-Oct-24	01-Jun-27
MIL-2542	Complete Subcontractor 'Buyout'	0		11-Oct-24
MIL-2572	Place Steel Mill Order	0	20-Feb-25	
MIL-2762	Green Schools Compliance Submission	0		04-Mar-25
MIL-1640	Provide Complete Set of Approved Coordination Drawings	0		23-May-25
MIL-2532	Submit Complete Permit Application	0		29-Sep-25
MIL-2832	Issuance of Excavation & Shoring Permit	0		29-Sep-25
MIL-2842	Issuance of Builders Pavement Permit	0		29-Sep-25
MIL-2852	Issuance of Permit to Enter (PTE)	0		29-Sep-25
MIL-2862	Issuance of NYPA Permit	0		29-Sep-25
MIL-2872	Issuance of Construction Fences Permit	0		29-Sep-25
MIL-2882	Issuance of Sidewalk Shed Permits	0		29-Sep-25
MIL-2892	Issuance of CCD1	0		29-Sep-25
MIL-2902	Issuance of DOB Permit & Insurance	0		29-Sep-25
MIL-1060	Mobilization Start	0	30-Sep-25	
MIL-1710	Complete Mobilization	0		03-Oct-25
MIL-2582	Start Concrete Placement	0	28-Oct-25	
MIL-2812	Start Foundation	0	28-Oct-25	
MIL-2912	Start Concrete Cast In Place Inspection	0	28-Oct-25	
MIL-1810	Crane Mobilization-Steel Installation start	0	05-Dec-25	
MIL-1120	Metal Decking Start	0	22-Dec-25	
MIL-2622	Deliveries of all owner-furnished equipment and/or materials	0		06-Feb-26
MIL-1140	Layout Start	0	23-Feb-26	
MIL-1150	Masonry Walls Start	0	23-Feb-26	
MIL-1180	MEP Risers Start	0	23-Feb-26	
MIL-1210	Duct Rough-ins Start	0	24-Feb-26	
MIL-1160	Top & Bottom Track Start	0	26-Feb-26	
MIL-1830	Crane Mobilization-Precast Sandwich Panels Installation Start	0	05-Mar-26	

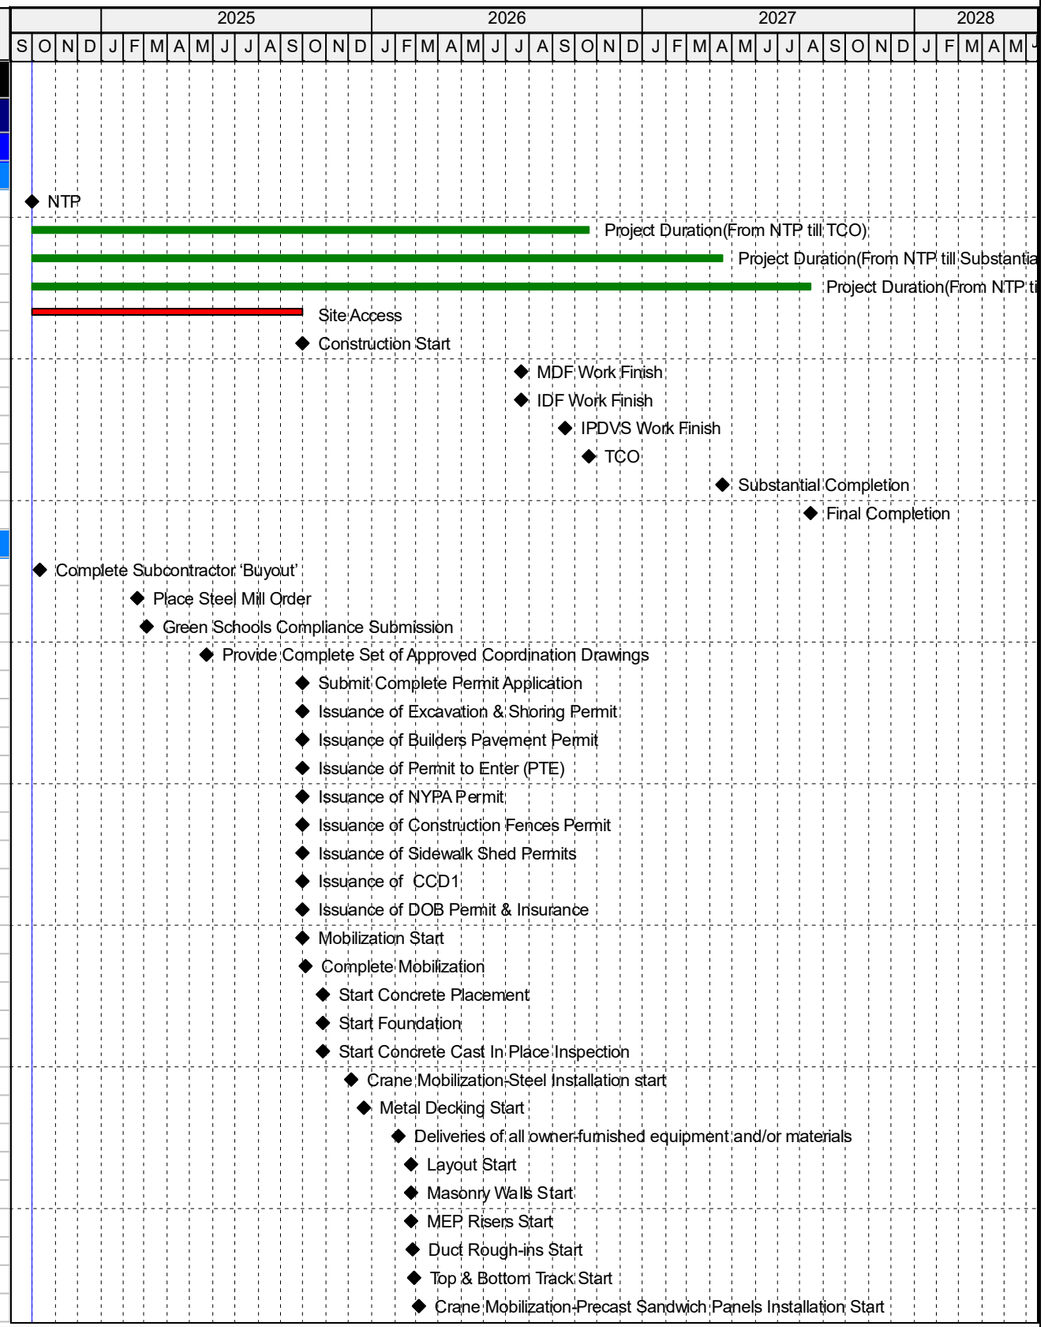

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
MIL-2932	Start Masonry Inspection	0	05-Mar-26	
MIL-1170	Finish Concrete Work	0		11-Mar-26
MIL-1820	Crane Mobilization-Steel Installation Finish	0		12-Mar-26
MIL-2612	Start Suspended Ceiling Grid	0	16-Mar-26	
MIL-1380	Crane Mobilization-Mechanical Subcontractor	78	17-Mar-26	07-Jul-26
MIL-2922	Start Pre -Cast Concrete Inspection	0	25-Mar-26	
MIL-1840	Crane Mobilization-Precast Sandwich Panels Installation Finish	0		06-Apr-26
MIL-1230	5th Floor Roofing Start	0	07-Apr-26	
MIL-2602	Start Mechanical Distribution Lines	0	08-Apr-26	
MIL-1200	Main Roofing Start	0	09-Apr-26	
MIL-1270	Electrical Rough-ins Start	0	09-Apr-26	
MIL-1220	Layout Finish	0		09-Apr-26
MIL-2942	Start In-Wall Inspection	0	10-Apr-26	
MIL-1290	Duct Rough-ins Finish	0		14-Apr-26
MIL-1250	Top & Bottom Track Finish	0		15-Apr-26
MIL-2712	Start Low Voltage	0	16-Apr-26	
MIL-1580	Window Installation Finish	0		28-Apr-26
MIL-1400	Start Site Work	0	29-Apr-26	
MIL-1300	Start Sprinkler Rough-ins	0	04-May-26	
MIL-1340	BLDG Tight	0		06-May-26
MIL-1350	Electrical Rough-ins Finish	0		06-May-26
MIL-1360	Start Mockup Room Work	0	07-May-26	
MIL-1430	Start Architecture Finishes	0	07-May-26	
MIL-1260	Plumbing Rough-ins Start	0	07-May-26	
MIL-1310	5th Floor Roofing Finish	0		13-May-26
MIL-1280	Main Roofing Finish	0		15-May-26
MIL-1410	Mockup Room Ready For Inspection	0		26-May-26
MIL-1420	Finish Mockup Room	0		26-May-26
MIL-1440	Start Gypsum Board	0	27-May-26	
MIL-1320	Plumbing Rough-ins Finish	0		29-May-26
MIL-2952	Finish Standpipe System Inspection	0		05-Jun-26
MIL-1460	Roof Top Units Installations Start	0	08-Jun-26	
MIL-1450	Start 1st Coat Painting	0	10-Jun-26	
MIL-2992	Finish Fuel-Oil Storage & Fuel Oil Piping Systems Inspection	0		11-Jun-26
MIL-1330	Finish Sprinkler Rough-ins	0		22-Jun-26
MIL-2632	Finish HVAC	0		06-Jul-26
MIL-2982	Finish Fire-Resistant Penetrations And Joints Inspection	0		06-Jul-26
MIL-2732	Start Mechanical and Electrical System Commissioning	0	07-Jul-26	
MIL-1480	Roof Top Units Installations Finish	0		14-Jul-26
MIL-2972	Finish Mechanical System Inspection	0		15-Jul-26
MIL-2562	Start Below Grade Plumbing and Other Utilities	0	16-Jul-26	
MIL-2742	Permanent Power Available	0		27-Jul-26
MIL-2592	P&D - Connection to Roof Drains	0	28-Jul-26	
MIL-2692	Building HVAC Flush-out	0		03-Aug-26

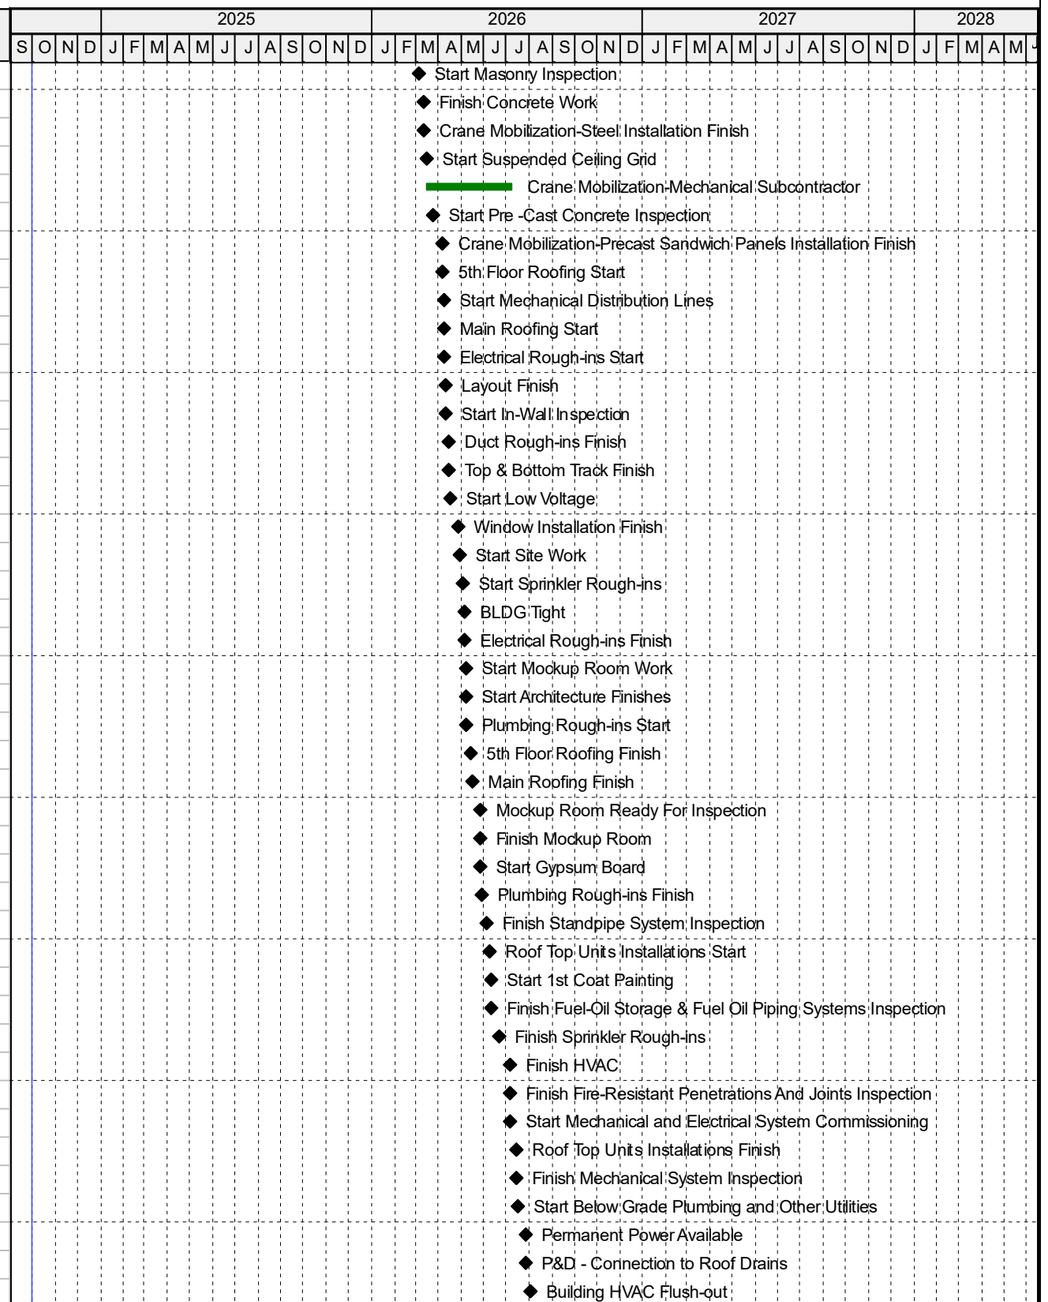

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
MIL-2642	Finish Fire Alarm Signoff	0		07-Aug-26
MIL-2962	Finish Fire Alarm Inspection	0		07-Aug-26
MIL-2802	Provision of Training Schedules (30 days prior to start of Training)	0	10-Aug-26	
MIL-2702	Finish Concrete Work	0		10-Aug-26
MIL-2822	Elevator Ready for Testing	0		11-Aug-26
MIL-2672	Finish Painting	0		28-Aug-26
MIL-2722	Start Kitchen	0	04-Sep-26	
MIL-2662	Finishes and Ceiling Complete	0		04-Sep-26
MIL-1470	Finish Site Work	0		10-Sep-26
MIL-2652	Finish Mechanical and Electrical System Commissioning	0		18-Sep-26
MIL-2772	Performance test for all mechanical equipment and low voltage systems	0		18-Sep-26
MIL-2792	Commissioning for all mechanical equipment and low voltage systems	0		18-Sep-26
MIL-2782	Submission of Operations and Maintenance Manuals	0		01-Jun-27
Permits		279	30-Sep-24	10-Nov-25
PRE-2590	Meeting With SCA to Review The Permit Requirements	14	30-Sep-24	18-Oct-24
PRE-2600	Prepare & Submit Permit Waiver Requests to SCA Chief Project Officer	5	30-Sep-24	04-Oct-24
PRE-2630	Obtain Builders Pavement Permit	10	16-Sep-25	29-Sep-25
PRE-2640	Obtain Excavation & Shoring Permit	10	16-Sep-25	29-Sep-25
PRE-2650	Obtain Permit to Enter (PTE) Amtrak	10	16-Sep-25	29-Sep-25
PRE-2660	Obtain NYPA Permit	10	16-Sep-25	29-Sep-25
PRE-2540	SCA Work Notification	7	23-Sep-25	29-Sep-25
PRE-1660	DOB Permit & Insurance	3	25-Sep-25	29-Sep-25
PRE-1460	Obtain Construction Fences Permit	3	25-Sep-25	29-Sep-25
PRE-2550	Obtain CCD1	3	25-Sep-25	29-Sep-25
PRE-2570	Obtain Sidewalk Shed Permits	3	25-Sep-25	29-Sep-25
PRE-2610	Prepare & Submit FDNY Fuel Permit	10	06-Oct-25	20-Oct-25
PRE-2620	Review & Approve FDNY Fuel Permit	21	21-Oct-25	10-Nov-25
Mobilization		513	30-Sep-24	19-Oct-26
CON-99257	Subcontractor Buyout	10	30-Sep-24	11-Oct-24
MIL-1660	Start Security Guard Services (30 Days From NTP)	0	30-Oct-24	
CON-1000	Mobilization	4	30-Sep-25	03-Oct-25
CON-7740	Protection Of All Overhead & Underground Utilities	263	30-Sep-25	19-Oct-26
CON-9000	Protection & Restoration the adjacent Properties to Original Condition	263	30-Sep-25	19-Oct-26
CON-1080	Install Erosion Control Devices	2	06-Oct-25	07-Oct-25
CON-1010	Install Construction Signs	2	06-Oct-25	07-Oct-25
CON-1030	Install Construction Fences	2	06-Oct-25	07-Oct-25
CON-9120	Soli Sampling	2	06-Oct-25	07-Oct-25
CON-7750	Install Field Offices	5	08-Oct-25	15-Oct-25
CON-9140	Excavation	5	08-Oct-25	15-Oct-25
CON-8390	Install Sidewalk Sheds -South Elevation	4	29-Dec-25	02-Jan-26
CON-8400	Install Sidewalk Sheds -East Elevation	4	29-Dec-25	02-Jan-26
MIL-1720	Start Sidewalk Bridge Installations	0	29-Dec-25	
Utilities Coordination		450	07-Oct-24	27-Jul-26
Gas Coordination		437	07-Oct-24	08-Jul-26

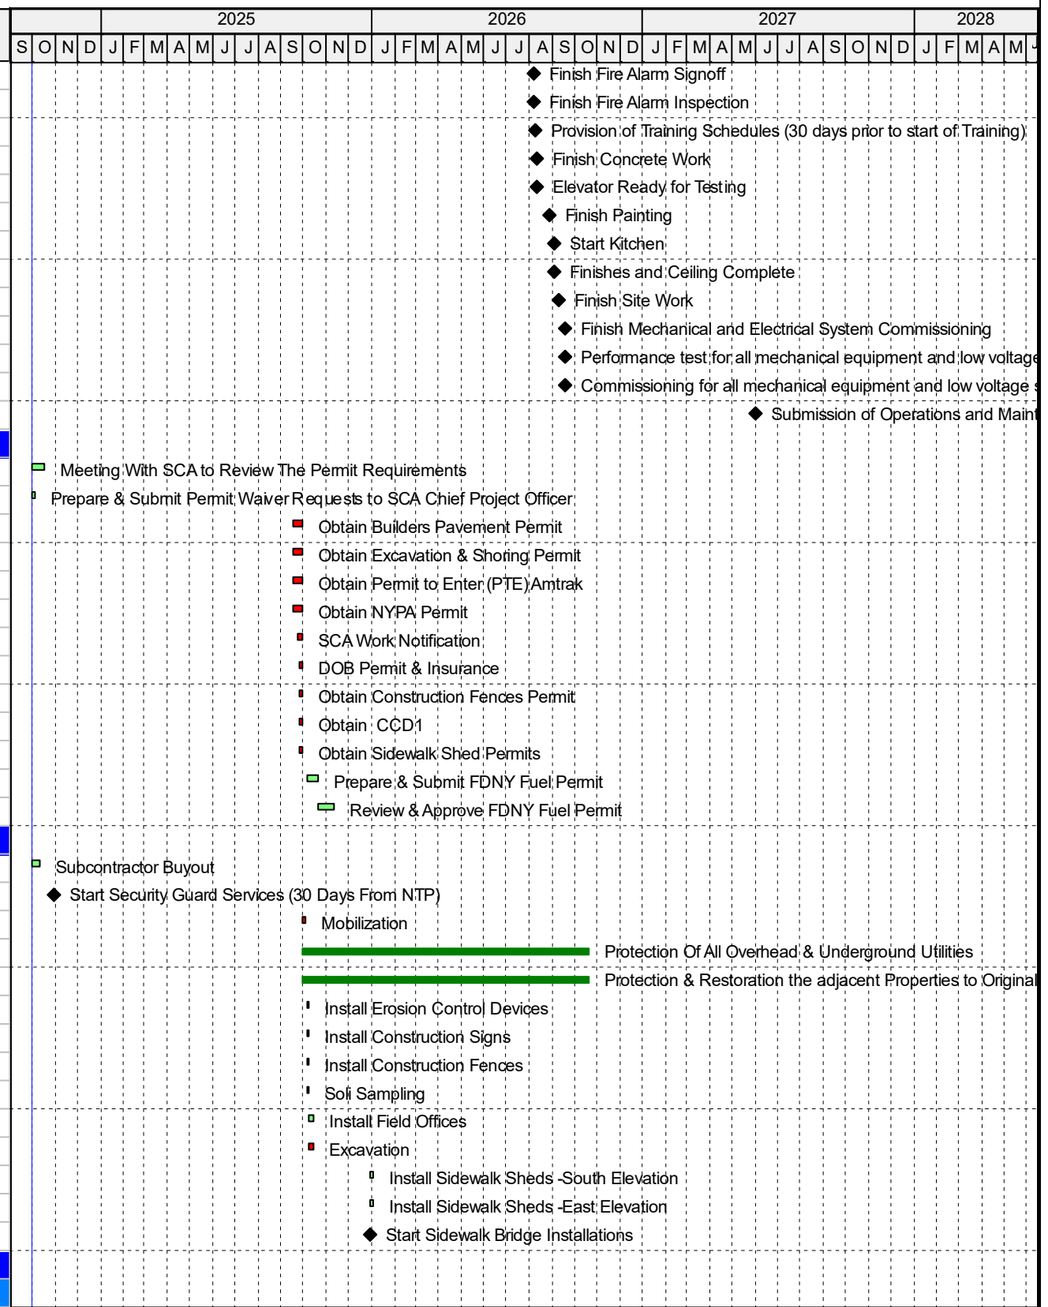

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-7960	Obtain Gas Meter Layout From CON-ED	5	07-Oct-24	11-Oct-24
CON-7970	Coordinate With CON-ED For Gas Service	7	16-Apr-26	24-Apr-26
CON-7990	Gas Authorization	5	24-Jun-26	30-Jun-26
CON-8000	Pink Slip	5	01-Jul-26	08-Jul-26
Temporary Electrical Power		246	07-Nov-24	31-Oct-25
CON-8010	Coordination With CON-ED For Temporary Electrical Power	10	07-Nov-24	21-Nov-24
CON-8020	Scheduling With CON-ED For Temporary Electrical Power	7	22-Nov-24	03-Dec-24
CON-8030	Procurement From CON-ED For Temporary Electrical Power	20	30-Sep-25	19-Oct-25
CON-8040	CON-ED Work For Temporary Electrical Power	10	20-Oct-25	31-Oct-25
CON-8050	Available Temporary Electrical Power For Testing MEP Equipment	0		31-Oct-25
Permanent Electrical Power		29	15-Jun-26	27-Jul-26
CON-8060	CON-ED - Switchgear Inspection	4	15-Jun-26	18-Jun-26
CON-8070	CON-ED - Pull Power Cable to the Building	10	22-Jun-26	06-Jul-26
CON-8080	CON-ED - Terminate Power Cables	10	07-Jul-26	20-Jul-26
CON-8090	CON-ED - Energize to the Building	5	21-Jul-26	27-Jul-26
Procurement		483	15-Oct-24	19-Sep-26
Submittals & Approvals		462	15-Oct-24	19-Aug-26
Division 01 - General Requirements		153	15-Oct-24	23-May-25
Spec Section S01300 - Submittals		153	15-Oct-24	23-May-25
SUB-1410	Prepare & Submit Submittal Schedule	60	15-Oct-24	10-Jan-25
SUB-1780	Prepare & Submit Initial Underground Coordination Drawings	50	15-Oct-24	26-Dec-24
SUB-1790	Prepare & Submit Initial 1st Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1800	Prepare & Submit Initial 2nd Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1810	Prepare & Submit Initial 3rd Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1820	Prepare & Submit Initial 4th Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1830	Prepare & Submit Initial 5th Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
APP-1230	Review & Approve Initial Underground Coordination Drawings	21	27-Dec-24	16-Jan-25
APP-1260	Review & Approve Submittal Schedule	21	11-Jan-25	31-Jan-25
SUB-2270	Prepare & Submit Final Underground Coordination Drawings	37	17-Jan-25	11-Mar-25
APP-1330	Review & Approve Initial 1st Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1340	Review & Approve Initial 2nd Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1350	Review & Approve Initial 3rd Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1360	Review & Approve Initial 4th Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1370	Review & Approve Initial 5th Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
SUB-2280	Prepare & Submit Final 1st Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2290	Prepare & Submit Final 2nd Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2300	Prepare & Submit Final 3rd Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2310	Prepare & Submit Final 4th Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2320	Prepare & Submit Final 5th Floor Coordination Drawings	49	25-Feb-25	02-May-25
APP-2270	Review & Approve Final Foundations Coordination Drawings	21	12-Mar-25	01-Apr-25
APP-2280	Review & Approve Final 1st Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2290	Review & Approve Final 2nd Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2300	Review & Approve Final 3rd Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2310	Review & Approve Final 4th Floor Coordination Drawings	21	03-May-25	23-May-25

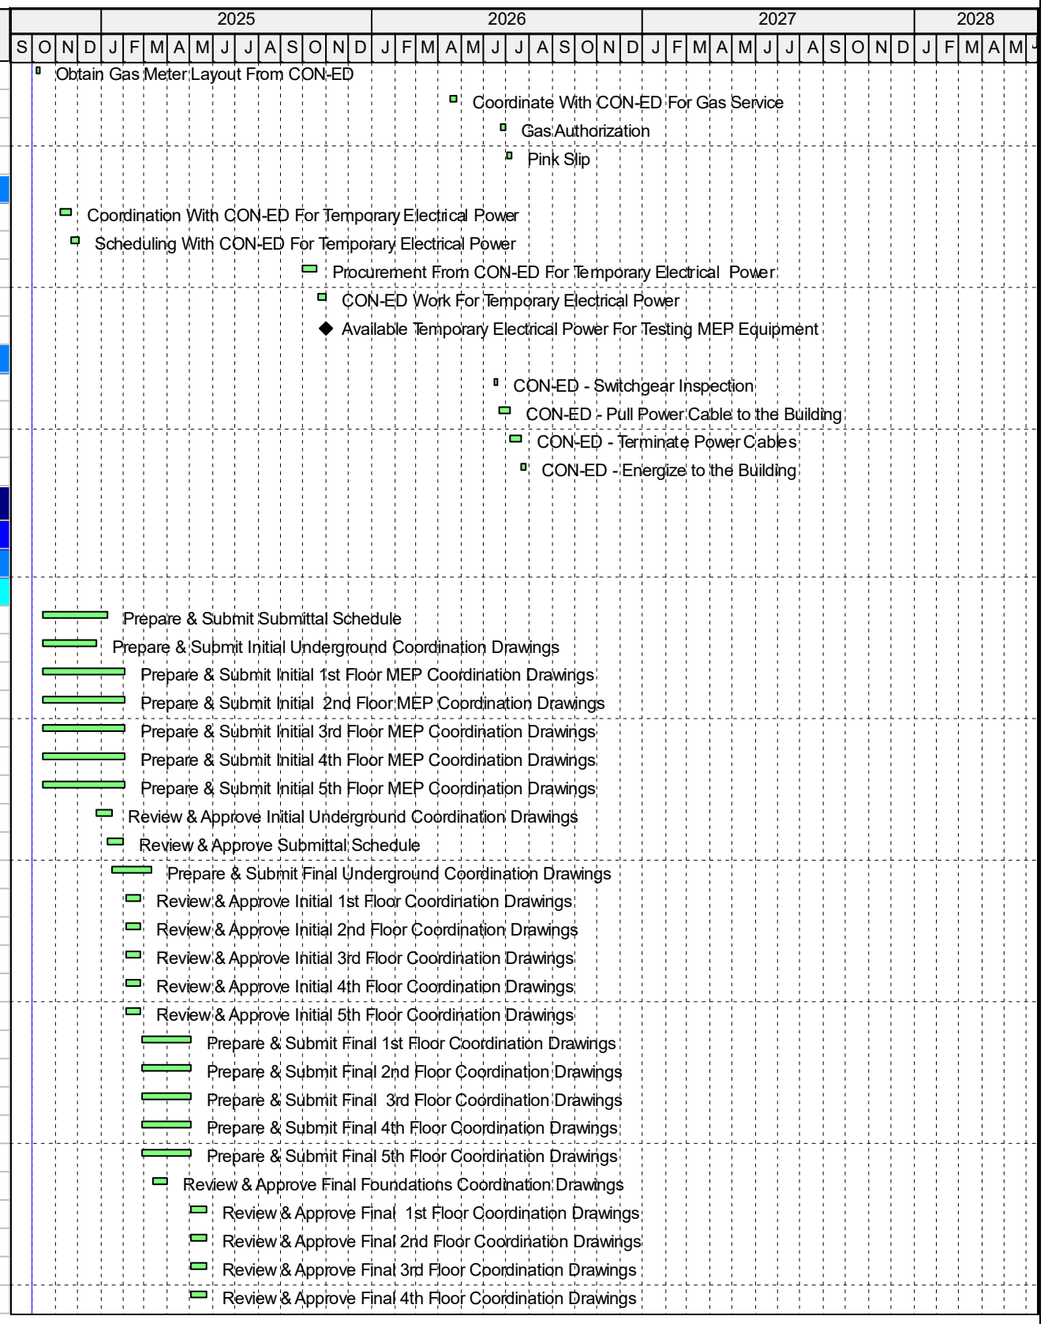

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
APP-2320	Review & Approve Final 5th Floor Coordination Drawings	21	03-May-25	23-May-25
Spec Section S01311 - Progress Schedule		65	15-Oct-24	20-Jan-25
SUB-1610	Prepare & Submit Baseline Schedule	52	15-Oct-24	30-Dec-24
APP-1240	Review & Approve Baseline Schedule	21	31-Dec-24	20-Jan-25
Spec Section S01352 - Sustainability Requirements		24	15-Oct-24	18-Nov-24
SUB-1400	Prepare & Submit Sustainable Materials	10	15-Oct-24	28-Oct-24
APP-1040	Review & Approve Sustainable Materials	21	29-Oct-24	18-Nov-24
Spec Section S01400 - Quality Control		44	15-Oct-24	17-Dec-24
SUB-1570	Prepare & Submit QCP	30	15-Oct-24	26-Nov-24
APP-1130	Review & Approve QCP	21	27-Nov-24	17-Dec-24
Spec Section S01426 - Sample Classroom		95	15-Oct-24	04-Mar-25
SUB-1390	Prepare & Submit Sample Classroom Materials	81	15-Oct-24	11-Feb-25
APP-1640	Review & Approve Sample Classroom Materials	21	12-Feb-25	04-Mar-25
Spec Section S01500 - Temporary Facilities and Controls		95	15-Oct-24	04-Mar-25
SUB-1370	Prepare & Submit Photo Submission - Temporary Fence	15	15-Oct-24	04-Nov-24
SUB-1380	Prepare & Submit Heating Plan	81	15-Oct-24	11-Feb-25
SUB-2340	Prepare & Submit Tree Protection Plan	71	15-Oct-24	28-Jan-25
APP-1060	Review & Approve Photo Submission - Temporary Fence	21	05-Nov-24	25-Nov-24
APP-2340	Review & Approve Tree Protection Plan	21	29-Jan-25	18-Feb-25
APP-1630	Review & Approve Heating Plan	21	12-Feb-25	04-Mar-25
Spec Section S01524 - Construction Waste Management		95	15-Oct-24	04-Mar-25
SUB-1360	Prepare & Submit CWM Plan	81	15-Oct-24	11-Feb-25
APP-1620	Review & Approve CWM Plan	21	12-Feb-25	04-Mar-25
Spec Section S01535 - Safety Program		17	15-Oct-24	06-Nov-24
SUB-1350	Prepare & Submit Site Safety Plan	2	15-Oct-24	16-Oct-24
APP-1000	Review & Approve Site Safety Plan	21	17-Oct-24	06-Nov-24
Spec Section S01550 - Indoor Air Quality (IAQ) Requirements		95	15-Oct-24	04-Mar-25
SUB-1340	Prepare & Submit Construction Indoor Air Quality Management Plan	81	15-Oct-24	11-Feb-25
APP-1610	Review & Approve Construction Indoor Air Quality Management Plan	21	12-Feb-25	04-Mar-25
Spec Section S01560 - Installation Sequence of Finish Materials		95	15-Oct-24	04-Mar-25
SUB-1330	Prepare & Submit Temporary Ventilation Plan	81	15-Oct-24	11-Feb-25
APP-1600	Review & Approve Temporary Ventilation Plan	21	12-Feb-25	04-Mar-25
Spec Section S01630 - Product Substitutions		96	15-Oct-24	05-Mar-25
SUB-1320	Prepare & Submit Product Substitutions	82	15-Oct-24	12-Feb-25
APP-2260	Review & Approve Product Substitutions	21	13-Feb-25	05-Mar-25
Spec Section S01650 - Facility Start-Up, Demonstration, and Training		95	15-Oct-24	04-Mar-25
SUB-1310	Prepare & Submit Training Outline & Schedule	81	15-Oct-24	11-Feb-25
APP-1590	Review & Approve Training Outline & Schedule	21	12-Feb-25	04-Mar-25
Spec Section S01660 - Supplemental Commissioning Requirements		95	15-Oct-24	04-Mar-25
SUB-1840	Prepare & Submit Supplemental Comissioning Requirements	81	15-Oct-24	11-Feb-25
APP-1850	Review & Approve Supplemental Comissioning Requirements	21	12-Feb-25	04-Mar-25
Spec Section S01720 - Record Documents		95	15-Oct-24	04-Mar-25
SUB-1850	Prepare & Submit Record Documents	81	15-Oct-24	11-Feb-25
APP-1860	Review & Approve Record Documents	21	12-Feb-25	04-Mar-25

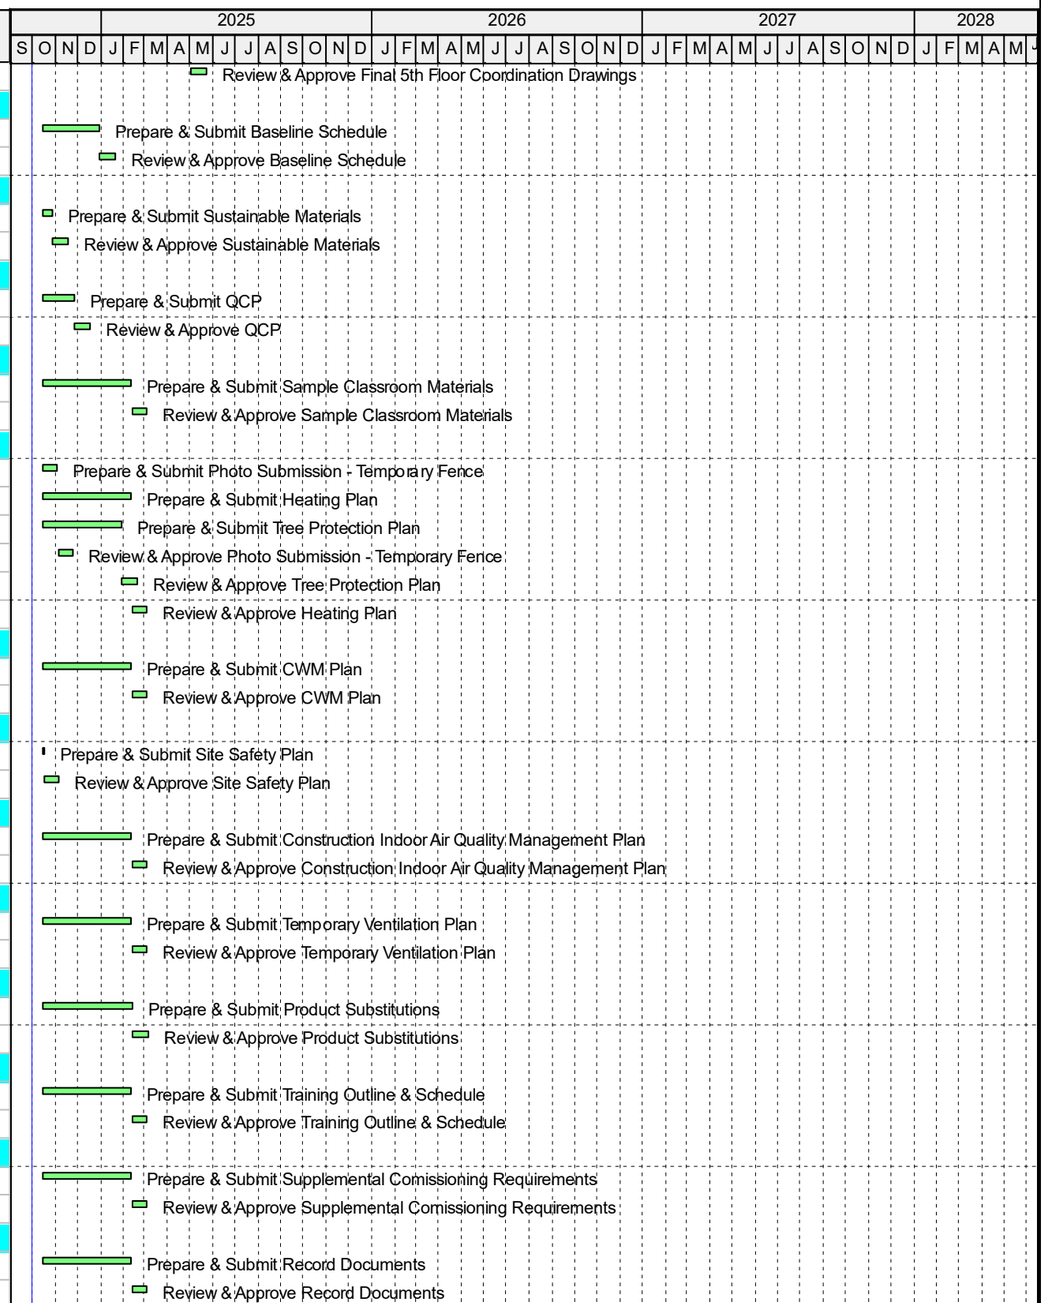

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
Division 02 - Site Work		462	15-Oct-24	19-Aug-26
Spec Section 02010 - Environmental Site Assessment Reports		95	15-Oct-24	04-Mar-25
SUB-1860	Prepare & Submit Environmental Site Assessment Reports	81	15-Oct-24	11-Feb-25
APP-1870	Review & Approve Environmental Site Assessment Reports	21	12-Feb-25	04-Mar-25
Spec Section 02070 - Selective Removals & Demoloition		95	15-Oct-24	04-Mar-25
SUB-1870	Prepare & Submit Selective Removals & Demoloition	81	15-Oct-24	11-Feb-25
APP-1880	Review & Approve Selective Removals & Demoloition	21	12-Feb-25	04-Mar-25
Spec Section 02090 - Environmental Management Of Excavated Material And Fill/Backfil		258	15-Oct-24	24-Oct-25
SUB-2920	Prepare & Submit Documentation of Proper Disposal	81	15-Oct-24	11-Feb-25
APP-2920	Review & Approve Documentation of Proper Disposal	21	12-Feb-25	04-Mar-25
SUB-2900	Prepare & Submit Excavated Material Disposal Plan	71	26-May-25	05-Sep-25
SUB-4050	Prepare & Submit Soil Sampling Plan	71	26-May-25	05-Sep-25
APP-2900	Review & Approve Excavated Material Disposal Plan	21	06-Sep-25	26-Sep-25
APP-4050	Review & Approve Soil Sampling Plan	21	06-Sep-25	26-Sep-25
SUB-2910	Prepare & Submit Backfill & Resue Plan	20	08-Sep-25	03-Oct-25
APP-2910	Review & Approve Backfill & Resue Plan	21	04-Oct-25	24-Oct-25
Spec Section 02200 - Earthwork		21	15-Oct-24	13-Nov-24
SUB-1560	Prepare & Submit Erosion Control and Sedimentation Plan	7	15-Oct-24	23-Oct-24
APP-1020	Review & Approve Erosion Control and Sedimentation Plan	21	24-Oct-24	13-Nov-24
Spec Section 02100 - Site Preparation		24	15-Oct-24	18-Nov-24
SUB-1300	Prepare & Submit Existing Conditions Survey	10	15-Oct-24	28-Oct-24
APP-1030	Review & Approve Existing Conditions Survey	21	29-Oct-24	18-Nov-24
Spec Section 02220 - Gas Vapor Barrier (Fluid Applied)		95	15-Oct-24	04-Mar-25
SUB-1290	Prepare & Submit Gas Vapor Barrier Submittal & Inspection Schedule	81	15-Oct-24	11-Feb-25
APP-1580	Review & Approve Gas Vapor Barrier Submittal & Inspection Schedule	21	12-Feb-25	04-Mar-25
Spec Section 02221 - Sub-Slab Depressurization System		462	15-Oct-24	19-Aug-26
SUB-1280	Prepare & Submit SSDS Geotextile	40	15-Oct-24	11-Dec-24
APP-1200	Review & Approve SSDS Geotextile	21	12-Dec-24	01-Jan-25
SUB-2330	Prepare & Submit Remedial Closure Report	3	27-Jul-26	29-Jul-26
APP-2330	Review & Approve Remedial Closure Report	21	30-Jul-26	19-Aug-26
Spec Section 02250 - Foundation & Other Change Adjustements		19	15-Oct-24	11-Nov-24
SUB-1880	Prepare & Submit Foundation Product Data	5	15-Oct-24	21-Oct-24
APP-1010	Review & Approve Foundation Product Data	21	22-Oct-24	11-Nov-24
Spec Section 02260 - Excavation Support And Monitoring		95	15-Oct-24	04-Mar-25
SUB-2360	Prepare & Submit Adjacent Property and Structures Protection & Monitoring Plan	81	15-Oct-24	11-Feb-25
APP-2360	Review & Approve Adjacent Property and Structures Protection & Monitoring Plan	21	12-Feb-25	04-Mar-25
Spec Section 02511 - Asphaltic Concrete Paving		95	15-Oct-24	04-Mar-25
SUB-1270	Prepare & Submit Asphaltic Concrete Paving	81	15-Oct-24	11-Feb-25
APP-1570	Review & Approve Asphaltic Concrete Paving	21	12-Feb-25	04-Mar-25
Spec Section 02513 - Sidewalk and Street Paving		95	15-Oct-24	04-Mar-25
SUB-1260	Prepare & Submit Steel Curb Facing Shop Drawing	81	15-Oct-24	11-Feb-25
APP-1560	Review & Approve Steel Curb Facing Shop Drawing	21	12-Feb-25	04-Mar-25
Spec Section 02521 - Concrete Curbs and Pavements		95	15-Oct-24	04-Mar-25
SUB-1250	Prepare & Submit Concrete Curbs & Pavements Shop Drawing	81	15-Oct-24	11-Feb-25

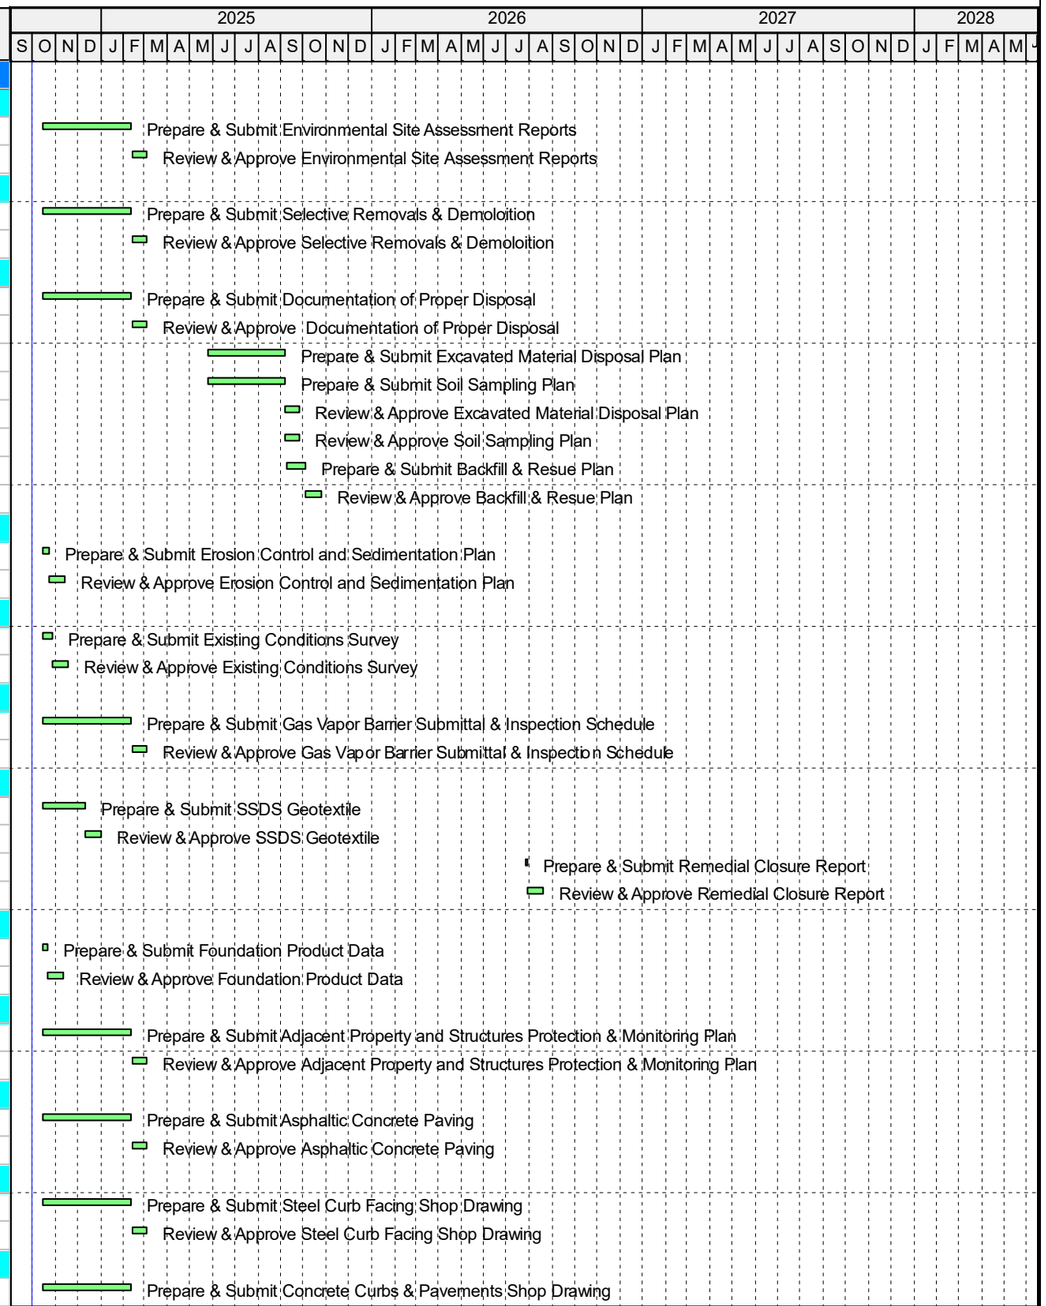

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1550	Review & Approve Concrete Curbs & Pavements Shop Drawing	21	12-Feb-25	04-Mar-25
Spec Section 02721 - Trench Drains		95	15-Oct-24	04-Mar-25
SUB-1890	Prepare & Submit Trench Drains Product Data	81	15-Oct-24	11-Feb-25
APP-1890	Review & Approve Trench Drains Prodcut Data	21	12-Feb-25	04-Mar-25
Spec Section 02722 - PC Basins, Detention Basins, and Manholes		95	15-Oct-24	04-Mar-25
SUB-1240	Prepare & Submit Catch Basin Shop Drawings	81	15-Oct-24	11-Feb-25
APP-1540	Review & Approve Catch Basin Shop Drawings	21	12-Feb-25	04-Mar-25
Spec Section 02723 - Storm Drainage Systems		51	15-Oct-24	27-Dec-24
SUB-1230	Prepare & Submit Ductile Iron Pipes	37	15-Oct-24	06-Dec-24
APP-1150	Review & Approve Ductile Iron Pipes	21	07-Dec-24	27-Dec-24
Spec Section 02831 - Chain Link Fences & Gates		95	15-Oct-24	04-Mar-25
SUB-1900	Prepare & Submit Chain Link Fences & Gates Drawings	81	15-Oct-24	11-Feb-25
APP-1900	Review & Approve Chain Link Fences & Gates Drawings	21	12-Feb-25	04-Mar-25
Spec Section 02860 - Early Childhood Playground Equipment		95	15-Oct-24	04-Mar-25
SUB-1220	Prepare & Submit Playgroung Equipment Shop Drawings	81	15-Oct-24	11-Feb-25
APP-1530	Review & Approve Playgroung Equipment Shop Drawings	21	12-Feb-25	04-Mar-25
Spec Section 02862 - Outdoor Game Equipment		95	15-Oct-24	04-Mar-25
SUB-1910	Prepare & Submit Outdoor Game Equipment	81	15-Oct-24	11-Feb-25
APP-1910	Review & Approve Outdoor Game Equipment	21	12-Feb-25	04-Mar-25
Spec Section 02870 - Site & Street Furnishings		29	15-Oct-24	25-Nov-24
SUB-1210	Prepare & Submit Site Furnishings Shop Drawings	15	15-Oct-24	04-Nov-24
APP-1050	Review & Approve Site Furnishings Shop Drawings	21	05-Nov-24	25-Nov-24
Spec Section 02900 - Landscaping		95	15-Oct-24	04-Mar-25
SUB-1200	Prepare & Submit Planting Schedule	81	15-Oct-24	11-Feb-25
APP-1520	Review & Approve Planting Schedule	21	12-Feb-25	04-Mar-25
Division 03 - Concrete		95	15-Oct-24	04-Mar-25
Spec Section 03100 - Concrete Formwork		95	15-Oct-24	04-Mar-25
SUB-1190	Prepare & Submit Formwork Shop Drawings	81	15-Oct-24	11-Feb-25
APP-1510	Review & Approve Formwork Shop Drawings	21	12-Feb-25	04-Mar-25
Spec Section 03200 - Concrete Reinforcement		44	15-Oct-24	17-Dec-24
SUB-1180	Prepare & Submit Concrete Reinforcement	30	15-Oct-24	26-Nov-24
APP-1100	Review & Approve Concrete Reinforcement	21	27-Nov-24	17-Dec-24
Spec Section 03300 - Cast in Place Concrete		44	15-Oct-24	17-Dec-24
SUB-1450	Prepare & Submit Concrete Shop Drawings	30	15-Oct-24	26-Nov-24
SUB-1580	Prepare & Submit Concrete Mix Design	30	15-Oct-24	26-Nov-24
APP-1110	Review & Approve Concrete Shop Drawings	21	27-Nov-24	17-Dec-24
APP-1140	Review & Approve Concrete Mix Design	21	27-Nov-24	17-Dec-24
Spec Section 03450 - Precast Architectural Concrete		86	15-Oct-24	18-Feb-25
SUB-1920	Prepare & Submit Precast Architectural Concrete	71	15-Oct-24	28-Jan-25
APP-1920	Review & Approve Precast Architectural Concrete	21	29-Jan-25	18-Feb-25
Spec Section 03542 - Cement Based Self Leveling Underlayment		95	15-Oct-24	04-Mar-25
SUB-1170	Prepare & Submit Certification of Material	81	15-Oct-24	11-Feb-25
APP-1500	Review & Approve Certification of Material	21	12-Feb-25	04-Mar-25
Division 04 - Masonry		95	15-Oct-24	04-Mar-25

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
Spec Section 04200 - Unit Masonry		86	15-Oct-24	18-Feb-25
SUB-1930	Prepare & Submit Unit Masonry Product Data	71	15-Oct-24	28-Jan-25
APP-1930	Review & Approve Unit Masonry Product Data	21	29-Jan-25	18-Feb-25
Spec Section 04435 - Cast Stone		95	15-Oct-24	04-Mar-25
SUB-1940	Prepare & Submit Cast Stone Product Data	81	15-Oct-24	11-Feb-25
APP-1940	Review & Approve Cast Stone Product Data	21	12-Feb-25	04-Mar-25
Division 05 - Metals		190	15-Oct-24	18-Jul-25
Spec Section 05120 - Structural Steel		86	15-Oct-24	18-Feb-25
SUB-1950	Prepare & Submit Structure Steel Drawings	71	15-Oct-24	28-Jan-25
APP-1950	Review & Approve Structure Steel Drawings	21	29-Jan-25	18-Feb-25
Spec Section 05170 - Support System for Suspended Ceilings		95	15-Oct-24	04-Mar-25
SUB-1160	Prepare & Submit Suspension Assembly Shop Drawings	81	15-Oct-24	11-Feb-25
APP-1490	Review & Approve Suspension Assembly Shop Drawings	21	12-Feb-25	04-Mar-25
Spec Section 05300 - Metal Deck		95	15-Oct-24	04-Mar-25
SUB-1960	Prepare & Submit Metal Deck Product Data	81	15-Oct-24	11-Feb-25
APP-1960	Review & Approve Metal Deck Product Data	21	12-Feb-25	04-Mar-25
Spec Section 05500 - Metal Fabrications		95	05-Mar-25	18-Jul-25
SUB-1700	Prepare & Submit Roof Dunnage	81	05-Mar-25	27-Jun-25
APP-1810	Review & Approve Roof Dunnage	21	28-Jun-25	18-Jul-25
Spec Section 05710 - Steel Stairs		95	15-Oct-24	04-Mar-25
SUB-4060	Prepare & Submit Steel Stairs Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-4070	Prepare & Submit Steel Stairs Product Data	81	15-Oct-24	11-Feb-25
APP-4060	Review & Approve Steel Stairs Shop Drawings	21	12-Feb-25	04-Mar-25
APP-4070	Review & Approve Steel Stairs Product Data	21	12-Feb-25	04-Mar-25
Spec Section 05700 - Ornamental Metal		95	15-Oct-24	04-Mar-25
SUB-2370	Prepare & Submit Ornamenta Metal Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2930	Prepare & Submit Ornamenta Metal Product Data	81	15-Oct-24	11-Feb-25
APP-2370	Review & Approve Ornamenta Metal Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2930	Review & Approve Ornamenta Metal Product Data	21	12-Feb-25	04-Mar-25
Spec Section 05810 - Prefabricated Expansion Joint Covers		95	15-Oct-24	04-Mar-25
SUB-1970	Prepare & Submit Prefabricated Expansion Joint Covers	81	15-Oct-24	11-Feb-25
APP-1970	Review & Approve Prefabricated Expansion Joint Covers	21	12-Feb-25	04-Mar-25
Division 06 - Wood & Plastics		95	15-Oct-24	04-Mar-25
Spec Section 06200 - Finish Carpentry		95	15-Oct-24	04-Mar-25
SUB-1530	Prepare & Submit Furniture	81	15-Oct-24	11-Feb-25
APP-1720	Review & Approve Furniture	21	12-Feb-25	04-Mar-25
Spec Section 06410 - Custom Casework		95	15-Oct-24	04-Mar-25
SUB-1510	Prepare & Submit Millwork	81	15-Oct-24	11-Feb-25
APP-1710	Review & Approve Millwork	21	12-Feb-25	04-Mar-25
Division 07 - Thermal & Moisture Protection		95	15-Oct-24	04-Mar-25
Spec Section 07147 - Crystalline Waterproofing		95	15-Oct-24	04-Mar-25
SUB-1150	Prepare & Submit Crystalline Waterproofing Product Data	81	15-Oct-24	11-Feb-25
APP-1480	Review & Approve Crystalline Waterproofing Product Data	21	12-Feb-25	04-Mar-25
Spec Section 07211 - Perimeter Foundation Insulation		95	15-Oct-24	04-Mar-25

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1140	Prepare & Submit Perimeter Foundation Insulation Product Data	81	15-Oct-24	11-Feb-25
APP-1470	Review & Approve Perimeter Foundation Insulation Product Data	21	12-Feb-25	04-Mar-25
Spec Section 07271 - Self Adhering Sheet Air Barriers		95	15-Oct-24	04-Mar-25
SUB-1980	Prepare & Submit Self Adhering Sheet Air Barriers	81	15-Oct-24	11-Feb-25
APP-1980	Review & Approve Self Adhering Sheet Air Barriers	21	12-Feb-25	04-Mar-25
Spec Section 07414 - Metal Plate Wall Panels		95	15-Oct-24	04-Mar-25
SUB-1990	Prepare & Submit Metal Plate Wall Panels	81	15-Oct-24	11-Feb-25
SUB-4080	Prepare & Submit Green School Submittal	81	15-Oct-24	11-Feb-25
APP-1990	Review & Approve Metal Plate Wall Panels	21	12-Feb-25	04-Mar-25
APP-4080	Review & Approve Green School Submittal	21	12-Feb-25	04-Mar-25
Spec Section 07560 - Fluid Applied Protected Membrane Roofing		95	15-Oct-24	04-Mar-25
SUB-1130	Prepare & Submit Roofing Membrane Product Data	81	15-Oct-24	11-Feb-25
APP-1460	Review & Approve Roofing Membrane Product Data	21	12-Feb-25	04-Mar-25
Spec Section 07600 - Flashing and Sheet Metal		95	15-Oct-24	04-Mar-25
SUB-1120	Prepare & Submit Flashing & Sheet Metal Shop Drawing	81	15-Oct-24	11-Feb-25
APP-1450	Review & Approve Flashing & Sheet Metal Shop Drawing	21	12-Feb-25	04-Mar-25
Spec Section 07720 - Roof Accessories		95	15-Oct-24	04-Mar-25
SUB-1110	Prepare & Submit Roof Drains & Clean Outs	81	15-Oct-24	11-Feb-25
APP-1440	Review & Approve Roof Drains & Clean Outs	21	12-Feb-25	04-Mar-25
Division 08 - Doors & Windows		95	15-Oct-24	04-Mar-25
Spec Section 08110 - Steel Doors and Frames		95	15-Oct-24	04-Mar-25
SUB-1100	Prepare & Submit Door & Frame Corners Samples	81	15-Oct-24	11-Feb-25
APP-1430	Review & Approve Door & Frame Corners Samples	21	12-Feb-25	04-Mar-25
Spec Section 08210 - Wood Doors		95	15-Oct-24	04-Mar-25
SUB-1620	Prepare & Submit Wood Doors	81	15-Oct-24	11-Feb-25
APP-1750	Review & Approve Wood Doors	21	12-Feb-25	04-Mar-25
Spec Section 08330 - Coiling Doors, Grilles And Shutters		95	15-Oct-24	04-Mar-25
SUB-2960	Prepare & Submit Coiling Doors, Grilles and Shutters Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2970	Prepare & Submit Coiling Doors, Grilles and Shutters Product Data	81	15-Oct-24	11-Feb-25
APP-2960	Review & Approve Coiling Doors, Grilles and Shutters Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2970	Review & Approve Coiling Doors, Grilles and ShuttersProduct Data	21	12-Feb-25	04-Mar-25
Spec Section 08411 - Aluminum Framed Entrances And Storefronts		95	15-Oct-24	04-Mar-25
SUB-2980	Prepare & Submit Aluminum Framed Entrances & Storefronts Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2990	Prepare & Submit Aluminum Framed Entrances & Storefronts Product Data	81	15-Oct-24	11-Feb-25
APP-2980	Review & Approve Aluminum Framed Entrances & Storefronts Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2990	Review & Approve Aluminum Framed Entrances & Storefronts Product Data	21	12-Feb-25	04-Mar-25
Spec Section 08521 - Fire Rated Glazing Systems		95	15-Oct-24	04-Mar-25
SUB-3040	Prepare & Submit Fire Rated Glazing Samples	81	15-Oct-24	11-Feb-25
SUB-3050	Prepare & Submit Fire Rated Glazing Product Data	81	15-Oct-24	11-Feb-25
APP-3040	Review & Approve Fire Rated Glazing Samples	21	12-Feb-25	04-Mar-25
APP-3050	Review & Approve Fire Rated Glazing Product Data	21	12-Feb-25	04-Mar-25
Spec Section 08524 - Aluminum Projected Windows		86	15-Oct-24	18-Feb-25
SUB-1670	Prepare & Submit Aluminum Projected Windows	71	15-Oct-24	28-Jan-25
APP-1310	Review & Approve Aluminum Projected Windows	21	29-Jan-25	18-Feb-25

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
Spec Section 08662 - Security Screens & Barriers		95	15-Oct-24	04-Mar-25
SUB-2000	Prepare & Submit Security Screens & Barriers	81	15-Oct-24	11-Feb-25
APP-2000	Review & Approve Security Screens & Barriers	21	12-Feb-25	04-Mar-25
Spec Section 08710 - Finish Hardware		95	15-Oct-24	04-Mar-25
SUB-1080	Prepare & Submit Door Hardware Submittal	81	15-Oct-24	11-Feb-25
APP-1410	Review & Approve Door Hardware Submittal	21	12-Feb-25	04-Mar-25
Spec Section 08730 - Thresholds, Weatherstripping And Seals		95	15-Oct-24	04-Mar-25
SUB-3000	Prepare & Submit Thresholds, Weatherstripping and Seals Color Samples	81	15-Oct-24	11-Feb-25
SUB-3010	Prepare & Submit Thresholds, Weatherstripping and Seals Product Data	81	15-Oct-24	11-Feb-25
APP-3000	Review & Approve Thresholds, Weatherstripping and Seals Color Samples	21	12-Feb-25	04-Mar-25
APP-3010	Review & Approve Thresholds, Weatherstripping and Seals Product Data	21	12-Feb-25	04-Mar-25
Spec Section 08800 - Miscellaneous Glazing		95	15-Oct-24	04-Mar-25
SUB-3020	Prepare & Submit Miscellaneous Glazing Samples	81	15-Oct-24	11-Feb-25
SUB-3030	Prepare & Submit Miscellaneous Glazing Product Data	81	15-Oct-24	11-Feb-25
APP-3020	Review & Approve Miscellaneous Glazing Samples	21	12-Feb-25	04-Mar-25
APP-3030	Review & Approve Miscellaneous Glazing Product Data	21	12-Feb-25	04-Mar-25
Division 09 - Finishes		95	15-Oct-24	04-Mar-25
Spec Section 09260 - Gypsum Board Assemblies		95	15-Oct-24	04-Mar-25
SUB-1470	Prepare & Submit Gypsum Board	81	15-Oct-24	11-Feb-25
APP-1680	Review & Approve Gypsum Board	21	12-Feb-25	04-Mar-25
Spec Section 09310 - Ceramic Tiles		95	15-Oct-24	04-Mar-25
SUB-1070	Prepare & Submit Ceramic Tiles Product Data	81	15-Oct-24	11-Feb-25
APP-1400	Review & Approve Ceramic Tiles Product Data	21	12-Feb-25	04-Mar-25
Spec Section 09510 - Acoustical Ceilings		74	15-Oct-24	31-Jan-25
SUB-1490	Prepare & Submit Acosutical Ceiling Tiles	60	15-Oct-24	10-Jan-25
APP-1270	Review & Approve Acosutical Ceiling Tiles	21	11-Jan-25	31-Jan-25
Spec Section 09590 - Wood Flooring		95	15-Oct-24	04-Mar-25
SUB-2010	Prepare & Submit Wood Flooring	81	15-Oct-24	11-Feb-25
APP-2010	Review & Approve Wood Flooring	21	12-Feb-25	04-Mar-25
Spec Section 09650 - Resilient Flooring		95	15-Oct-24	04-Mar-25
SUB-1480	Prepare & Submit Floorings	81	15-Oct-24	11-Feb-25
APP-1690	Review & Approve Floorings	21	12-Feb-25	04-Mar-25
Spec Section 09800 - Special Coatings		95	15-Oct-24	04-Mar-25
SUB-3070	Prepare & Submit Special Coating Samples	81	15-Oct-24	11-Feb-25
SUB-3080	Prepare & Submit Special Coating Product Data	81	15-Oct-24	11-Feb-25
APP-3070	Review & Approve Special Coating Samples	21	12-Feb-25	04-Mar-25
APP-3080	Review & Approve Special Coating Product Data	21	12-Feb-25	04-Mar-25
Spec Section 09860 - Grafiti Resistant Coatings		95	15-Oct-24	04-Mar-25
SUB-3060	Prepare & Submit Graffiti Resistant Coating Product Data	81	15-Oct-24	11-Feb-25
APP-3060	Review & Approve Graffiti Resistant Coating Product Data	21	12-Feb-25	04-Mar-25
Spec Section 09900 - Painting		95	15-Oct-24	04-Mar-25
SUB-1090	Prepare & Submit Painting	81	15-Oct-24	11-Feb-25
APP-1420	Review & Approve Painting	21	12-Feb-25	04-Mar-25
Division 10 - Specialties		95	15-Oct-24	04-Mar-25

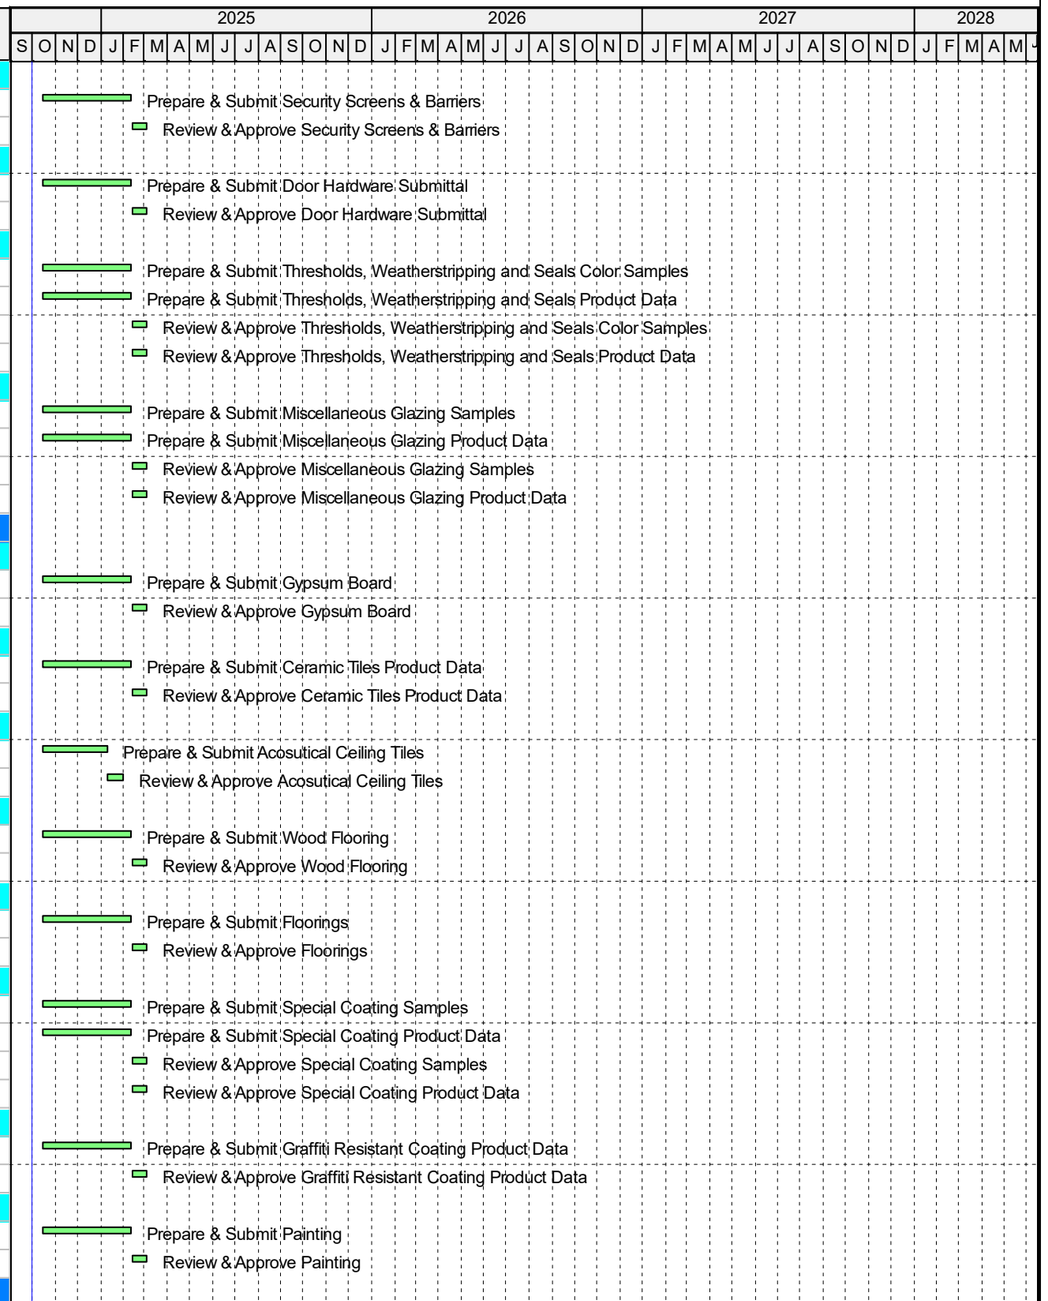

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
Spec Section 10100 - Visual Display Boards		95	15-Oct-24	04-Mar-25
SUB-2020	Prepare & Submit Visual Display Boards	81	15-Oct-24	11-Feb-25
APP-2020	Review & Approve Visual Display Boards	21	12-Feb-25	04-Mar-25
Spec Section 10350 - Flagpole		95	15-Oct-24	04-Mar-25
SUB-3090	Prepare & Submit Flagpole Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3100	Prepare & Submit Flagpole Product Data	81	15-Oct-24	11-Feb-25
APP-3090	Review & Approve Flagpole Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3100	Review & Approve Flagpole Product Data	21	12-Feb-25	04-Mar-25
Spec Section 10400 - Identification Devices		95	15-Oct-24	04-Mar-25
SUB-1060	Prepare & Submit Interior Signage Shop Drawings	81	15-Oct-24	11-Feb-25
APP-1390	Review & Approve Interior Signage Shop Drawings	21	12-Feb-25	04-Mar-25
Spec Section 10415 - Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases		95	15-Oct-24	04-Mar-25
SUB-3110	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals	81	15-Oct-24	11-Feb-25
SUB-3120	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-3130	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	81	15-Oct-24	11-Feb-25
APP-3110	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals	21	12-Feb-25	04-Mar-25
APP-3120	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	21	12-Feb-25	04-Mar-25
APP-3130	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	21	12-Feb-25	04-Mar-25
Spec Section 10505 - Metal Lockers		95	15-Oct-24	04-Mar-25
SUB-2030	Prepare & Submit Metal Lockers	81	15-Oct-24	11-Feb-25
APP-2030	Review & Approve Metal Lockers	21	12-Feb-25	04-Mar-25
Spec Section 10522 - Fire Extinguishers & Cabinets		95	15-Oct-24	04-Mar-25
SUB-2040	Prepare & Submit Fire Extinguishers & Cabinets	81	15-Oct-24	11-Feb-25
APP-2040	Review & Approve Fire Extinguishers & Cabinets	21	12-Feb-25	04-Mar-25
Spec Section 10605 - Wire Mesh Work		95	15-Oct-24	04-Mar-25
SUB-3140	Prepare & Submit Wire Mesh Work Samples	81	15-Oct-24	11-Feb-25
SUB-3150	Prepare & Submit Wire Mesh Work Shop drawings	81	15-Oct-24	11-Feb-25
APP-3140	Review & Approve Wire Mesh Work Samples	21	12-Feb-25	04-Mar-25
APP-3150	Review & Approve Miscellaneous Glazing Shop drawings	21	12-Feb-25	04-Mar-25
Spec Section 10675 - Metal Storage Shelving		95	15-Oct-24	04-Mar-25
SUB-3160	Prepare & Submit Metal Storage Shelving Samples	81	15-Oct-24	11-Feb-25
SUB-3170	Prepare & Submit Metal Storage Shelving Shop drawings	81	15-Oct-24	11-Feb-25
APP-3160	Review & Approve Metal Storage Shelving Samples	21	12-Feb-25	04-Mar-25
APP-3170	Review & Approve Metal Storage Shelving Shop drawings	21	12-Feb-25	04-Mar-25
Spec Section 10720 - Window Guards		87	15-Oct-24	20-Feb-25
SUB-2050	Prepare & Submit Stationary Metal Wall Louvers	73	15-Oct-24	30-Jan-25
APP-1320	Review & Approve Stationary Metal Wall Louvers	21	31-Jan-25	20-Feb-25
Spec Section 10810 - Toilet & Bath Accessories		95	15-Oct-24	04-Mar-25
SUB-1500	Prepare & Submit Toilet Accessories	81	15-Oct-24	11-Feb-25
APP-1700	Review & Approve Toilet Accessories	21	12-Feb-25	04-Mar-25
Spec Section 10830 - Mirrors		95	15-Oct-24	04-Mar-25
SUB-3180	Prepare & Submit Mirrors Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3190	Prepare & Submit Mirrors Product Data	81	15-Oct-24	11-Feb-25
SUB-3200	Prepare & Submit Mirrors Mastic Compatibility Test Reports & Certifications	81	15-Oct-24	11-Feb-25

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
APP-3180	Review & Approve Mirrors Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3190	Review & Approve Mirrors Product Data	21	12-Feb-25	04-Mar-25
APP-3200	Review & Approve Mirrors Mastic Compatibility Test Reports & Certifications	21	12-Feb-25	04-Mar-25
Spec Section 10840 - Grab Bars		95	15-Oct-24	04-Mar-25
SUB-3210	Prepare & Submit Grab Bars Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3220	Prepare & Submit Grab Bars Product Data	81	15-Oct-24	11-Feb-25
APP-3210	Review & Approve Grab Bars Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3220	Review & Approve Grab Bars Product Data	21	12-Feb-25	04-Mar-25
Division 11 - Equipment		95	15-Oct-24	04-Mar-25
Spec Section 11050 - Library Equipment		95	15-Oct-24	04-Mar-25
SUB-2060	Prepare & Submit Library Equipment	81	15-Oct-24	11-Feb-25
APP-2050	Review & Approve Library Equipment	21	12-Feb-25	04-Mar-25
Spec Section 11061 - Platform Curtains & Auditorium Window Curtains		95	15-Oct-24	04-Mar-25
SUB-2070	Prepare & Submit Platform Curtains & Auditorium Window Curtains	81	15-Oct-24	11-Feb-25
APP-2060	Review & Approve Platform Curtains & Auditorium Window Curtains	21	12-Feb-25	04-Mar-25
Spec Section 11172 - Waste Handling Equipment		95	15-Oct-24	04-Mar-25
SUB-2080	Prepare & Submit Waste Handling Equipment	81	15-Oct-24	11-Feb-25
APP-2070	Review & Approve Waste Handling Equipment	21	12-Feb-25	04-Mar-25
Spec Section 11400 - Food Service Equipment		86	15-Oct-24	18-Feb-25
SUB-1650	Prepare & Submit Kitchen Equipment	71	15-Oct-24	28-Jan-25
APP-1780	Review & Approve Kitchen Equipment	21	29-Jan-25	18-Feb-25
Spec Section 11450 - Domestic Type Equipment		95	15-Oct-24	04-Mar-25
SUB-2090	Prepare & Submit Domestic Equipment	81	15-Oct-24	11-Feb-25
APP-2080	Review & Approve Domestic Equipment	21	12-Feb-25	04-Mar-25
Spec Section 11480 - Gymnasium Equipment		95	15-Oct-24	04-Mar-25
SUB-1770	Prepare & Submit Gymnasium Equipment	81	15-Oct-24	11-Feb-25
APP-1840	Review & Approve Gymnasium Equipment	21	12-Feb-25	04-Mar-25
Spec Section 11500 - Shop Equipment		95	15-Oct-24	04-Mar-25
SUB-3230	Prepare & Submit Shop Equipment Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3240	Prepare & Submit Shop Equipment Product Data	81	15-Oct-24	11-Feb-25
APP-3230	Review & Approve Shop Equipment Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3240	Review & Approve Shop Equipment Product Data	21	12-Feb-25	04-Mar-25
Spec Section 11600 - Laboratory Equipment		95	15-Oct-24	04-Mar-25
SUB-2100	Prepare & Submit Laboratory Equipment	81	15-Oct-24	11-Feb-25
APP-2090	Review & Approve Laboratory Equipment	21	12-Feb-25	04-Mar-25
Division 12 - Furnishings		95	15-Oct-24	04-Mar-25
Spec Section 12761 - Bleachers		95	15-Oct-24	04-Mar-25
SUB-3250	Prepare & Submit Bleachers Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3260	Prepare & Submit Bleachers Product Data	81	15-Oct-24	11-Feb-25
SUB-3270	Prepare & Submit Bleachers Manufacturer's Warranty	81	15-Oct-24	11-Feb-25
APP-3250	Review & Approve Bleachers Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3260	Review & Approve Bleachers Product Data	21	12-Feb-25	04-Mar-25
APP-3270	Review & Approve Bleachers Manufacturer's Warranty	21	12-Feb-25	04-Mar-25
Spec Section 12302 - Manufactured Wood Casework		95	15-Oct-24	04-Mar-25

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-2110	Prepare & Submit Manufactured Wood Casework	81	15-Oct-24	11-Feb-25
APP-2100	Review & Approve Manufactured Wood Casework	21	12-Feb-25	04-Mar-25
Division 13 - Special Construction		95	15-Oct-24	04-Mar-25
Spec Section 13487 - Concrete Floating Floor Assembly		95	15-Oct-24	04-Mar-25
SUB-2120	Prepare & Submit Concrete Floating Floor Assembly	81	15-Oct-24	11-Feb-25
APP-2110	Review & Approve Concrete Floating Floor Assembly	21	12-Feb-25	04-Mar-25
Division 14 - Conveying Systems		95	15-Oct-24	04-Mar-25
Spec Section 14211 - Geared Traction Passenger Elevators		86	15-Oct-24	18-Feb-25
SUB-1460	Prepare & Submit Elevator Machine	71	15-Oct-24	28-Jan-25
APP-1210	Review & Approve Elevator Machine	21	29-Jan-25	18-Feb-25
Spec Section 14420 - Hydraulic Vertical Wheelchair Lifts		95	15-Oct-24	04-Mar-25
SUB-2130	Prepare & Submit Hydraulic Vertical Wheelchair Lifts	81	15-Oct-24	11-Feb-25
APP-2120	Review & Approve Hydraulic Vertical Wheelchair Lifts	21	12-Feb-25	04-Mar-25
Division 15 - Mechanical		95	15-Oct-24	04-Mar-25
Division 15A - Fire Protection		95	15-Oct-24	04-Mar-25
Spec Section 15330 - Sprinkler System		95	15-Oct-24	04-Mar-25
SUB-1440	Prepare & Submit Sprinkler System Shop Drawings	81	15-Oct-24	11-Feb-25
APP-1670	Review & Approve Sprinkler System Shop Drawings	21	12-Feb-25	04-Mar-25
Spec Section 15333 - Fire Pumps - Sprinkler Booster Pumps		95	15-Oct-24	04-Mar-25
SUB-1050	Prepare & Submit Fire & Jockey Pumps	81	15-Oct-24	11-Feb-25
SUB-1630	Prepare & Submit Fire Protection Shop Drawings	81	15-Oct-24	11-Feb-25
APP-1380	Review & Approve Fire & Jockey Pumps	21	12-Feb-25	04-Mar-25
APP-1760	Review & Approve Fire Protection Shop Drawings	21	12-Feb-25	04-Mar-25
Division 15B - Plumbing & Drainage		95	15-Oct-24	04-Mar-25
Spec Section 15410 - Plumbing Piping		95	15-Oct-24	04-Mar-25
SUB-1430	Prepare & Submit Plumbing Shop Drawings	81	15-Oct-24	11-Feb-25
APP-1660	Review & Approve Plumbing Shop Drawings	21	12-Feb-25	04-Mar-25
Spec Section 15411 - Hangers and Supports		53	15-Oct-24	01-Jan-25
SUB-1040	Prepare & Submit Hangers & Supports	40	15-Oct-24	11-Dec-24
APP-1190	Review & Approve Hangers & Supports	21	12-Dec-24	01-Jan-25
Spec Section 15412 - Valves		95	15-Oct-24	04-Mar-25
SUB-3280	Prepare & Submit Valves Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3290	Prepare & Submit Valves Product Data	81	15-Oct-24	11-Feb-25
APP-3280	Review & Approve Valves Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3290	Review & Approve Valves Product Data	21	12-Feb-25	04-Mar-25
Spec Section 15414 - Tests		95	15-Oct-24	04-Mar-25
SUB-3300	Prepare & Submit Certification of Tests	81	15-Oct-24	11-Feb-25
SUB-3310	Prepare & Submit Domestic Water Sterilization Plan	81	15-Oct-24	11-Feb-25
APP-3300	Review & Approve Certification of Tests	21	12-Feb-25	04-Mar-25
APP-3310	Review & Approve Domestic Water Sterilization Plan	21	12-Feb-25	04-Mar-25
Spec Section 15415 - Drainage		53	15-Oct-24	01-Jan-25
SUB-1030	Prepare & Submit Floor Drains	40	15-Oct-24	11-Dec-24
APP-1180	Review & Approve Floor Drains	21	12-Dec-24	01-Jan-25
Spec Section 15416 - Gas Piping System		95	15-Oct-24	04-Mar-25

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-2170	Prepare & Submit Gas Pipes	81	15-Oct-24	11-Feb-25
APP-2160	Review & Approve Gas Pipes	21	12-Feb-25	04-Mar-25
Spec Section 15417 - Cold Water Supply		53	15-Oct-24	01-Jan-25
SUB-1020	Prepare & Submit Pressure Gages	40	15-Oct-24	11-Dec-24
APP-1170	Review & Approve Pressure Gages	21	12-Dec-24	01-Jan-25
Spec Section 15418 - Hot Water Supply		53	15-Oct-24	01-Jan-25
SUB-1010	Prepare & Submit Thermometers	40	15-Oct-24	11-Dec-24
APP-1160	Review & Approve Thermometers	21	12-Dec-24	01-Jan-25
Spec Section 15431 - Tags, Charts, And Identification		95	15-Oct-24	04-Mar-25
SUB-3320	Prepare & Submit Tags, Charts & Identifications Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3330	Prepare & Submit Tags, Charts & Identifications Product Data	81	15-Oct-24	11-Feb-25
APP-3320	Review & Approve Tags, Charts & Identifications Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3330	Review & Approve Tags, Charts & Identifications Product Data	21	12-Feb-25	04-Mar-25
Spec Section 15432 - Miscellaneous		95	15-Oct-24	04-Mar-25
SUB-3340	Prepare & Submit Micselianeous Shop Drawing	81	15-Oct-24	11-Feb-25
APP-3340	Review & Approve Micselianeous Shop Drawing	21	12-Feb-25	04-Mar-25
Spec Section 15440 - Plumbing Fixtures		95	15-Oct-24	04-Mar-25
SUB-1600	Prepare & Submit Plumbing Fixtures	81	15-Oct-24	11-Feb-25
APP-1740	Review & Approve Plumbing Fixtures	21	12-Feb-25	04-Mar-25
Spec Section 15451 - Water Heaters		95	15-Oct-24	04-Mar-25
SUB-2180	Prepare & Submit Water Heaters	81	15-Oct-24	11-Feb-25
APP-2170	Review & Approve Water Heaters	21	12-Feb-25	04-Mar-25
Spec Section 15453 - Pumping Apparatus & Tanks		95	15-Oct-24	04-Mar-25
SUB-2190	Prepare & Submit Pumping Apparatus & Tanks	81	15-Oct-24	11-Feb-25
APP-2180	Review & Approve Pumping Apparatus & Tanks	21	12-Feb-25	04-Mar-25
Division 15C - Heating & Ventilation & Air Conditioning		95	15-Oct-24	04-Mar-25
Spec Section 15510 - HVAC Piping		74	15-Oct-24	31-Jan-25
SUB-1550	Prepare & Submit Mechanical Piping	60	15-Oct-24	10-Jan-25
APP-1280	Review & Approve Mechanical Piping	21	11-Jan-25	31-Jan-25
Spec Section 15511 - Valves (Hvac)		95	15-Oct-24	04-Mar-25
SUB-3350	Prepare & Submit Valves (HVAC) Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3360	Prepare & Submit Valves (HVAC) Product Data	81	15-Oct-24	11-Feb-25
APP-3350	Review & Approve Valves (HVAC) Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3360	Review & Approve Valves (HVAC) Product Data	21	12-Feb-25	04-Mar-25
Spec Section 15512 - Piping Insulation (Hvac)		95	15-Oct-24	04-Mar-25
SUB-3370	Prepare & Submit Piping Insulation Schedule Listing Items	81	15-Oct-24	11-Feb-25
APP-3370	Review & Approve Piping Insulation Schedule Listing Items	21	12-Feb-25	04-Mar-25
Spec Section 15513 - Equipment Insulation (Hvac)		95	15-Oct-24	04-Mar-25
SUB-3380	Prepare & Submit Schedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	81	15-Oct-24	11-Feb-25
APP-3380	Review & Approve chedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	21	12-Feb-25	04-Mar-25
Spec Section 15514 - Ductwork Insulation		95	15-Oct-24	04-Mar-25
SUB-3390	Prepare & Submit Schedules Showing Manfacturers's Product Number Duct Work Insulation	81	15-Oct-24	11-Feb-25
APP-3390	Review & Approve chedules Showing Manfacturers's Product Number Duct Work Insulation	21	12-Feb-25	04-Mar-25
Spec Section 15515 - Hydronic Specialties		95	15-Oct-24	04-Mar-25

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-3400	Prepare & Submit Hydronic Specialities Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3410	Prepare & Submit Hydronic Specialities Product Data	81	15-Oct-24	11-Feb-25
APP-3400	Review & Approve Hydronic Specialities Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3410	Review & Approve Hydronic Specialities Product Data	21	12-Feb-25	04-Mar-25
Spec Section 15517 - Water Treatment For Hydronic Systems		95	15-Oct-24	04-Mar-25
SUB-3420	Prepare & Submit Water Treatment Firm	81	15-Oct-24	11-Feb-25
SUB-3430	Prepare & Submit Chemical Products Product Data	81	15-Oct-24	11-Feb-25
APP-3420	Review & Approve Water Treatment Firm	21	12-Feb-25	04-Mar-25
APP-3430	Review & Approve Chemical Products Product Data	21	12-Feb-25	04-Mar-25
Spec Section 15540 - HVAC Pumps		95	15-Oct-24	04-Mar-25
SUB-2200	Prepare & Submit HVAC Pumps	81	15-Oct-24	11-Feb-25
APP-2190	Review & Approve HVAC Pumps	21	12-Feb-25	04-Mar-25
Spec Section 15565 - Hot Water Condensing Boilers		86	15-Oct-24	18-Feb-25
SUB-1730	Prepare & Submit Boilers	71	15-Oct-24	28-Jan-25
APP-1830	Review & Approve Boilers	21	29-Jan-25	18-Feb-25
Spec Section 15570 - Boiler Accessories		86	15-Oct-24	18-Feb-25
SUB-3440	Prepare & Submit Detail of Gag for the Safety Relief Valves	71	15-Oct-24	28-Jan-25
SUB-3450	Prepare & Submit Boiler Accessories Maintenance Data	71	15-Oct-24	28-Jan-25
APP-3440	Review & Approve Detail of Gag for the Safety Relief Valves	21	29-Jan-25	18-Feb-25
APP-3450	Review & Approve Boiler Accessories Maintenance Data	21	29-Jan-25	18-Feb-25
Spec Section 15575 - Breeching Chimney Connectors And Chimneys		95	15-Oct-24	04-Mar-25
SUB-3460	Prepare & Submit Breeching Chimney Connectors and Chimneys Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3470	Prepare & Submit Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	81	15-Oct-24	11-Feb-25
APP-3460	Review & Approve Breeching Chimney Connectors and Chimneys Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3470	Review & Approve Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	21	12-Feb-25	04-Mar-25
Spec Section 15792 - Coils		95	15-Oct-24	04-Mar-25
SUB-3500	Prepare & Submit Coils Maintenance Data	81	15-Oct-24	11-Feb-25
SUB-3510	Prepare & Submit Coils Certifications	81	15-Oct-24	11-Feb-25
APP-3500	Review & Approve Coils Maintenance Data	21	12-Feb-25	04-Mar-25
APP-3510	Review & Approve Coils Certifications	21	12-Feb-25	04-Mar-25
Spec Section 15835 - Convectors		95	15-Oct-24	04-Mar-25
SUB-3520	Prepare & Submit Convectors Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3530	Prepare & Submit Convectors Product Data	81	15-Oct-24	11-Feb-25
APP-3520	Review & Approve Convectors Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3530	Review & Approve Convectors Product Data	21	12-Feb-25	04-Mar-25
Spec Section 15838 - Fan Coil Units		95	15-Oct-24	04-Mar-25
SUB-3540	Prepare & Submit Fan Coils Units Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3550	Prepare & Submit Fan Coils Units Shop Drawings	81	15-Oct-24	11-Feb-25
APP-3540	Review & Approve Fan Coils Units Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3550	Review & Approve Fan Coils Units Shop Drawings	21	12-Feb-25	04-Mar-25
Spec Section 15839 - Door Air Curtains		95	15-Oct-24	04-Mar-25
SUB-3560	Prepare & Submit Door Air Curtains Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3570	Prepare & Submit Door Air Curtains Product Data	81	15-Oct-24	11-Feb-25
APP-3560	Review & Approve Door Air Curtains Shop Drawing	21	12-Feb-25	04-Mar-25

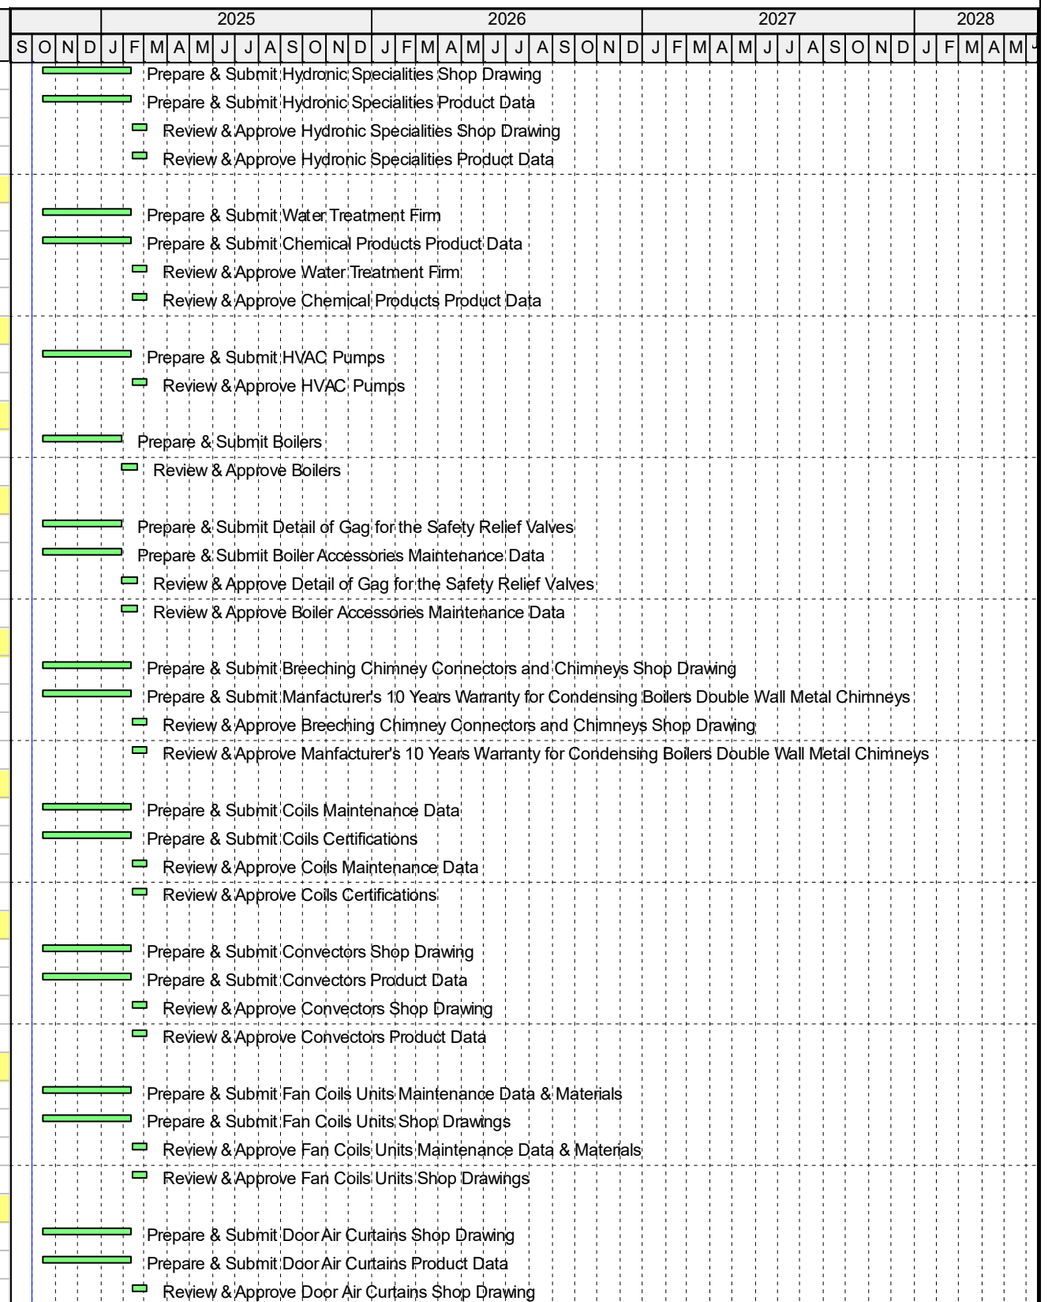

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
APP-3570	Review & Approve Door Air Curtains Product Data	21	12-Feb-25	04-Mar-25
Spec Section 15860 - Centrifugal Fans		95	15-Oct-24	04-Mar-25
SUB-3580	Prepare & Submit Centrifugal Fans Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3590	Prepare & Submit Centrifugal Fans Product Data	81	15-Oct-24	11-Feb-25
SUB-3600	Prepare & Submit Centrifugal Fans Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
APP-3580	Review & Approve Centrifugal Fans Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3590	Review & Approve Centrifugal Fans Product Data	21	12-Feb-25	04-Mar-25
APP-3600	Review & Approve Centrifugal Fans Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
Spec Section 15885 - Air Filters		95	15-Oct-24	04-Mar-25
SUB-3610	Prepare & Submit Air Filters Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3620	Prepare & Submit Air Filters Product Data	81	15-Oct-24	11-Feb-25
SUB-3630	Prepare & Submit Air Filters Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
APP-3610	Review & Approve Air Filters Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3620	Review & Approve Air Filters Product Data	21	12-Feb-25	04-Mar-25
APP-3630	Review & Approve Air Filters Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
Spec Section 15590 - Emergency Generator System Accessories		86	15-Oct-24	18-Feb-25
SUB-2210	Prepare & Submit Emergency Generator System Accessories	71	15-Oct-24	28-Jan-25
APP-2200	Review & Approve Emergency Generator System Accessories	21	29-Jan-25	18-Feb-25
Spec Section 15594 - Fuel Storage Equipment		95	15-Oct-24	04-Mar-25
SUB-2220	Prepare & Submit Fuel Storage Equipment	81	15-Oct-24	11-Feb-25
APP-2210	Review & Approve Fuel Storage Equipment	21	12-Feb-25	04-Mar-25
Spec Section 15596 - Natural Gas Leak Detection Equipment		95	15-Oct-24	04-Mar-25
SUB-2230	Prepare & Submit Natural Gas Leak Detection Equipment	81	15-Oct-24	11-Feb-25
APP-2220	Review & Approve Natural Gas Leak Detection Equipment	21	12-Feb-25	04-Mar-25
Spec Section 15660 - Packaged Modular Outdoor Chillers		86	15-Oct-24	18-Feb-25
SUB-1710	Prepare & Submit Chillers Product Data	71	15-Oct-24	28-Jan-25
APP-1820	Review & Approve Chillers Product Data	21	29-Jan-25	18-Feb-25
Spec Section 15670 - Plate Heat Exchangers		95	15-Oct-24	04-Mar-25
SUB-3480	Prepare & Submit Plate Heat Exchanger Maintenance Data	81	15-Oct-24	11-Feb-25
SUB-3490	Prepare & Submit Plate Heat Exchanger Product Data	81	15-Oct-24	11-Feb-25
APP-3480	Review & Approve Plate Heat Exchanger Maintenance Data	21	12-Feb-25	04-Mar-25
APP-3490	Review & Approve Plate Heat Exchanger Product Data	21	12-Feb-25	04-Mar-25
Spec Section 15783 - Split Heat Pump System		74	15-Oct-24	31-Jan-25
SUB-1000	Prepare & Submit Split Heat Pump System - SUB	60	15-Oct-24	10-Jan-25
APP-1250	Review & Approve Split Heat Pump System - SUB	21	11-Jan-25	31-Jan-25
Spec Section 15836 - Unit Heaters Cabinet Heaters		74	15-Oct-24	31-Jan-25
SUB-1760	Prepare & Submit Unit Cabinet Heaters	60	15-Oct-24	10-Jan-25
APP-1290	Review & Approve Unit Cabinet Heaters	21	11-Jan-25	31-Jan-25
Spec Section 15852 - Air Handling Units		86	15-Oct-24	18-Feb-25
SUB-1720	Prepare & Submit Air Handling Units Product Data	71	15-Oct-24	28-Jan-25
APP-1300	Review & Approve Air Handling Units Product Data	21	29-Jan-25	18-Feb-25
Spec Section 15891 - Metal Ductwork		95	15-Oct-24	04-Mar-25
SUB-1540	Prepare & Submit Mechanical Ducts	81	15-Oct-24	11-Feb-25
APP-1730	Review & Approve Mechanical Ducts	21	12-Feb-25	04-Mar-25

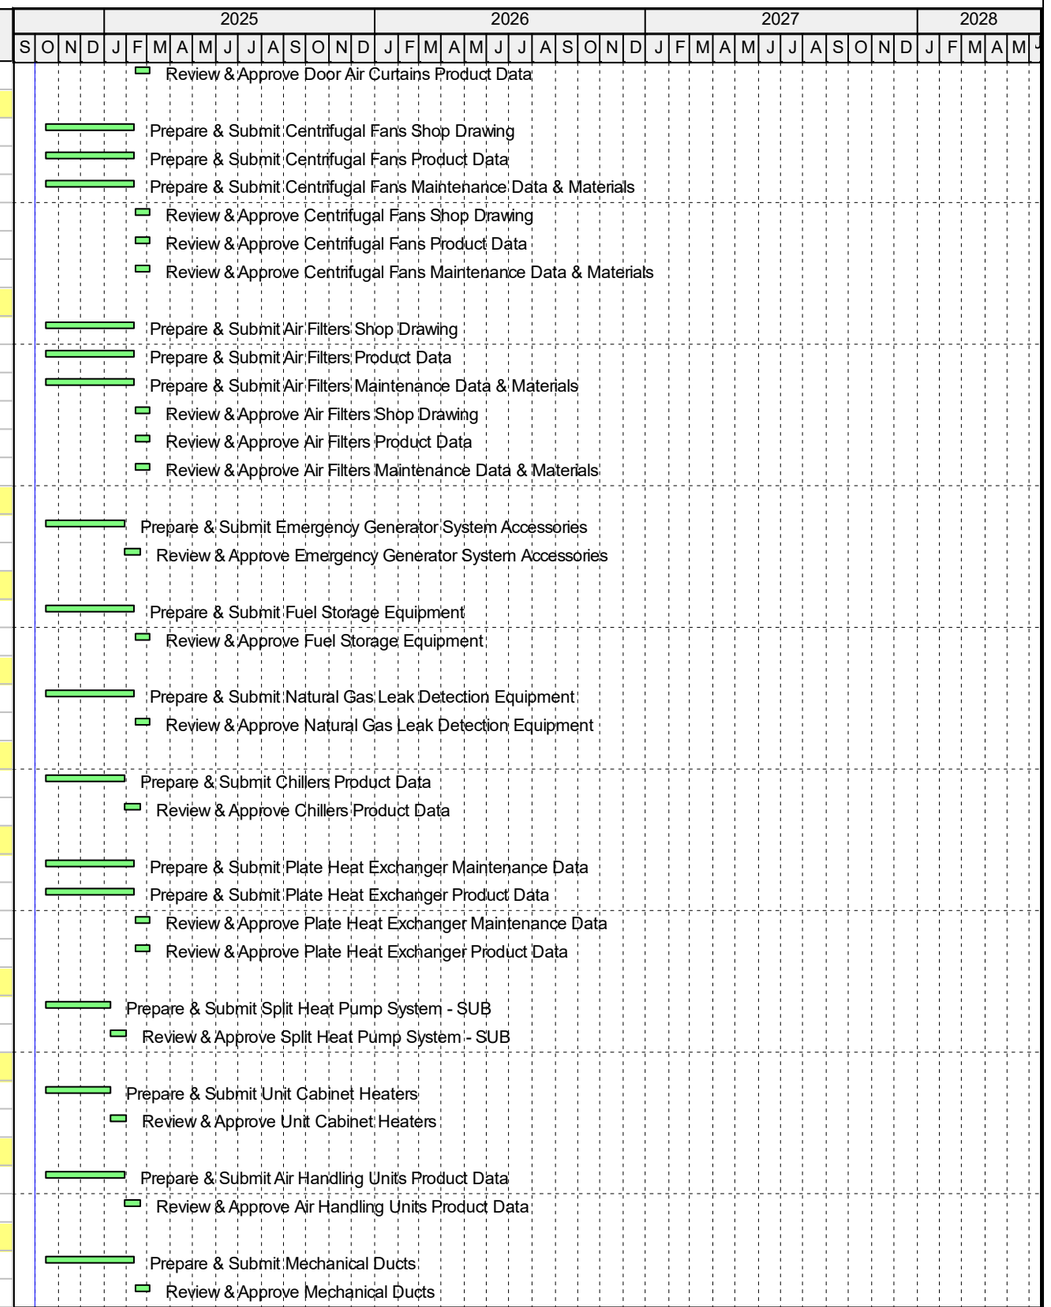

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
Spec Section 15940 - Air Outlets & Inlets		95	15-Oct-24	04-Mar-25
SUB-2260	Prepare & Submit Air Outlets & Inlets	81	15-Oct-24	11-Feb-25
APP-2250	Review & Approve Air Outlets & Inlets	21	12-Feb-25	04-Mar-25
Spec Section 15970 - Temperature Control System		95	15-Oct-24	04-Mar-25
SUB-2250	Prepare & Submit Temperature Control System	81	15-Oct-24	11-Feb-25
APP-2240	Review & Approve Temperature Control System	21	12-Feb-25	04-Mar-25
Spec Section 15910 - Duct Accessories		95	15-Oct-24	04-Mar-25
SUB-3640	Prepare & Submit Duct Accessories Shop Drawing	81	15-Oct-24	11-Feb-25
APP-3640	Review & Approve Duct Accessories Shop Drawing	21	12-Feb-25	04-Mar-25
Spec Section 15915 - Damper Assemblies		95	15-Oct-24	04-Mar-25
SUB-3650	Prepare & Submit Damper Assemblies Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3660	Prepare & Submit Damper Assemblies Product Data	81	15-Oct-24	11-Feb-25
SUB-3670	Prepare & Submit Damper Assemblies Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
APP-3650	Review & Approve Damper Assemblies Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3660	Review & Approve Damper Assemblies Product Data	21	12-Feb-25	04-Mar-25
APP-3670	Review & Approve Damper Assemblies Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
Spec Section 15935 - Air Handling Units For Public Assembly Spaces		95	15-Oct-24	04-Mar-25
SUB-3710	Prepare & Submit AHU for Public Assemblies Sapces Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3720	Prepare & Submit AHU for Public Assemblies Sapces Product Data	81	15-Oct-24	11-Feb-25
SUB-3730	Prepare & Submit AHU for Public Assemblies Sapces Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
APP-3710	Review & Approve AHU for Public Assemblies Sapces Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3720	Review & Approve AHU for Public Assemblies Sapces Product Data	21	12-Feb-25	04-Mar-25
APP-3730	Review & Approve AHU for Public Assemblies Sapces Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
Spec Section 15930 - Variable Air Terminals		95	15-Oct-24	04-Mar-25
SUB-3680	Prepare & Submit Variable Air Terminals Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3690	Prepare & Submit Variable Air Terminals Product Data	81	15-Oct-24	11-Feb-25
SUB-3700	Prepare & Submit Variable Air Terminals Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
APP-3680	Review & Approve Variable Air Terminals Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3690	Review & Approve Variable Air Terminals Product Data	21	12-Feb-25	04-Mar-25
APP-3700	Review & Approve Variable Air Terminals Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
Spec Section 15973 - Facility Management Systems Integration		95	15-Oct-24	04-Mar-25
SUB-3740	Prepare & Submit Control Systems Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3750	Prepare & Submit Truck Network Cable Schematic Diagram	81	15-Oct-24	11-Feb-25
APP-3740	Review & Approve Control Systems Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3750	Review & Approve Truck Network Cable Schematic Diagram	21	12-Feb-25	04-Mar-25
Division 16 - Electrical		95	15-Oct-24	04-Mar-25
Spec Section 16010 - Gen Provisions for Elec Work		95	15-Oct-24	04-Mar-25
SUB-1420	Prepare & Submit Electrical Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1590	Prepare & Submit Electrical Equipment, Conduits, and Cables	20	15-Oct-24	12-Nov-24
SUB-1750	Prepare & Submit Switch Gears Product Data	20	15-Oct-24	12-Nov-24
APP-1080	Review & Approve Electrical Equipment, Conduits, and Cables	21	13-Nov-24	03-Dec-24
APP-1090	Review & Approve Switch Gears Product Data	21	13-Nov-24	03-Dec-24
APP-1650	Review & Approve Electrical Shop Drawings	21	12-Feb-25	04-Mar-25
Spec Section 16120 - Wiring Systems		95	15-Oct-24	04-Mar-25

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1680	Prepare & Submit Telecommunication System Drawings	81	15-Oct-24	11-Feb-25
APP-1800	Review & Approve Telecommunication System Drawings	21	12-Feb-25	04-Mar-25
Spec Section 16145 - Lighting Control Devices		86	15-Oct-24	18-Feb-25
SUB-3760	Prepare & Submit Lighting Control Devices Shop Drawing	71	15-Oct-24	28-Jan-25
SUB-3770	Prepare & Submit Lighting Control Devices Product Data	71	15-Oct-24	28-Jan-25
SUB-3780	Prepare & Submit Lighting Control Devices Warranty	71	15-Oct-24	28-Jan-25
APP-3760	Review & Approve Lighting Control Devices Shop Drawing	21	29-Jan-25	18-Feb-25
APP-3770	Review & Approve Lighting Control Devices Product Data	21	29-Jan-25	18-Feb-25
APP-3780	Review & Approve Lighting Control Devices Warranty	21	29-Jan-25	18-Feb-25
Spec Section 16231- Emergency Generator System		86	15-Oct-24	18-Feb-25
SUB-1740	Prepare & Submit Emergency Generator System Product Data	71	15-Oct-24	28-Jan-25
APP-1070	Review & Approve Emergency Generator System Product Data	21	29-Jan-25	18-Feb-25
Spec Section 16289 - Surge Protective Devices		95	15-Oct-24	04-Mar-25
SUB-3790	Prepare & Submit Surge Protective Devices Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3800	Prepare & Submit Surge Protective Devices Product Data	81	15-Oct-24	11-Feb-25
SUB-3810	Prepare & Submit Surge Protective Devices Warranty	81	15-Oct-24	11-Feb-25
APP-3790	Review & Approve Surge Protective Devices Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3800	Review & Approve Surge Protective Devices Product Data	21	12-Feb-25	04-Mar-25
APP-3810	Review & Approve Surge Protective Devices Warranty	21	12-Feb-25	04-Mar-25
Spec Section 16420 - Service Entrance Equipment		95	15-Oct-24	04-Mar-25
SUB-3820	Prepare & Submit Service Entrance Equipment Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3830	Prepare & Submit Service Entrance Equipment Product Data	81	15-Oct-24	11-Feb-25
SUB-3840	Prepare & Submit Service Entrance Equipment Warranty	81	15-Oct-24	11-Feb-25
APP-3820	Review & Approve Service Entrance Equipment Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3830	Review & Approve Service Entrance Equipment Product Data	21	12-Feb-25	04-Mar-25
APP-3840	Review & Approve Service Entrance Equipment Warranty	21	12-Feb-25	04-Mar-25
Spec Section 16441- Enclosed Switches		95	15-Oct-24	04-Mar-25
SUB-3850	Prepare & Submit Enclosed Switches Product Data	81	15-Oct-24	11-Feb-25
SUB-3860	Prepare & Submit Enclosed Switches Test Reports	81	15-Oct-24	11-Feb-25
APP-3850	Review & Approve Enclosed Switches Product Data	21	12-Feb-25	04-Mar-25
APP-3860	Review & Approve Enclosed Switches Test Reports	21	12-Feb-25	04-Mar-25
Spec Section 16480 - Motors, Motor Control Centers, Starters And Control Equipment		95	15-Oct-24	04-Mar-25
SUB-3870	Prepare & Submit Motors, Motor Control Centers and Starters Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3880	Prepare & Submit Motors, Motor Control Centers and Starters Product Data	81	15-Oct-24	11-Feb-25
SUB-3890	Prepare & Submit Motors, Motor Control Centers and Starters Field Test Reports	81	15-Oct-24	11-Feb-25
APP-3870	Review & Approve Motors, Motor Control Centers and Starters Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3880	Review & Approve Motors, Motor Control Centers and Starters Product Data	21	12-Feb-25	04-Mar-25
APP-3890	Review & Approve Motors, Motor Control Centers and Starters Field Test Reports	21	12-Feb-25	04-Mar-25
Spec Section 16425 - Switch Boards & Panel Boards		95	15-Oct-24	04-Mar-25
SUB-2140	Prepare & Submit Switch & Panel Boards	81	15-Oct-24	11-Feb-25
APP-2130	Review & Approve Switch & Panel Boards	21	12-Feb-25	04-Mar-25
Spec Section 16471 - Auditorium & Television Studio Dimming System		95	15-Oct-24	04-Mar-25
SUB-2150	Prepare & Submit Auditorium & Television Studio Dimming System Product Data	81	15-Oct-24	11-Feb-25
APP-2140	Review & Approve Auditorium & Television Studio Dimming System Product Data	21	12-Feb-25	04-Mar-25

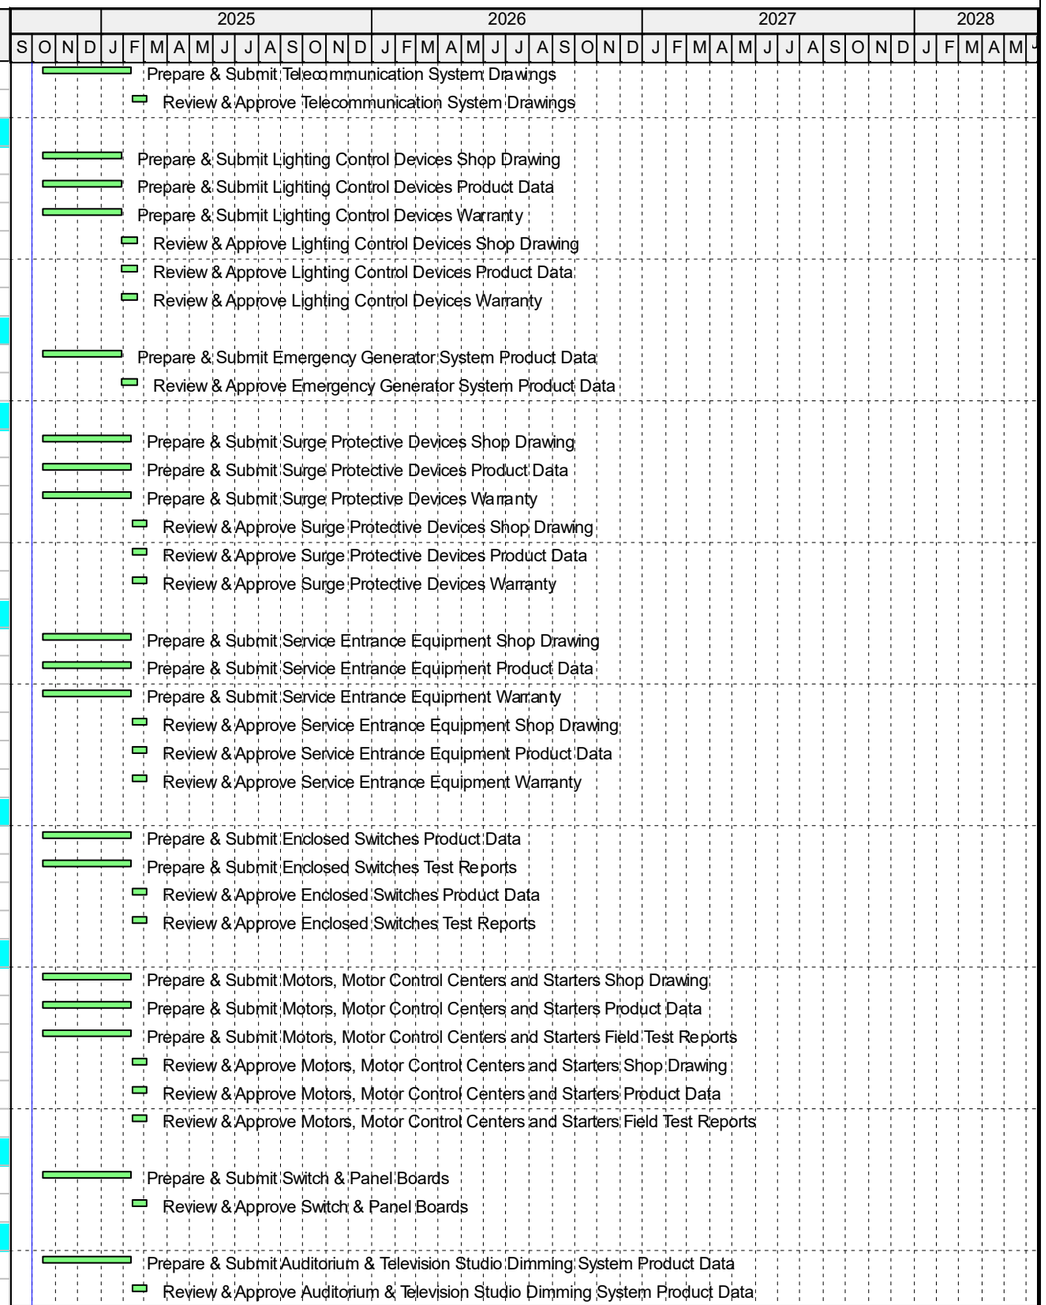

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
Spec Section 16475 - Overcurrent Protective Devices		95	15-Oct-24	04-Mar-25
SUB-2160	Prepare & Submit Overcurrent Protective Devices Data	81	15-Oct-24	11-Feb-25
APP-2150	Review & Approve Overcurrent Protective Devices Data	21	12-Feb-25	04-Mar-25
Spec Section 16502 - Interior Lighting Fixtures		86	15-Oct-24	18-Feb-25
SUB-1520	Prepare & Submit Lighting Fixtures	71	15-Oct-24	28-Jan-25
APP-1120	Review & Approve Lighting Fixtures	21	29-Jan-25	18-Feb-25
Spec Section 16520 - Illuminated Exit Sign		95	15-Oct-24	04-Mar-25
SUB-1660	Prepare & Submit Signs	81	15-Oct-24	11-Feb-25
APP-1790	Review & Approve Signs	21	12-Feb-25	04-Mar-25
Spec Section 16670 - Lightning Protection		95	15-Oct-24	04-Mar-25
SUB-3900	Prepare & Submit Lightning Protection Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3920	Prepare & Submit Lightning Protection Test Reports	81	15-Oct-24	11-Feb-25
APP-3900	Review & Approve Lightning Protection Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3920	Review & Approve Lightning Protection Test Reports	21	12-Feb-25	04-Mar-25
Spec Section 16720 - Fire Detection Alarm System with COC		95	15-Oct-24	04-Mar-25
SUB-1640	Prepare & Submit Fire Detectors & Alarms	81	15-Oct-24	11-Feb-25
APP-1770	Review & Approve Fire Detectors & Alarms	21	12-Feb-25	04-Mar-25
Spec Section 16728 - Fiber Optic Cabling System		95	15-Oct-24	04-Mar-25
SUB-3930	Prepare & Submit Fiber Optic Cabling system Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3940	Prepare & Submit Fiber Optic Cabling system Product Data	81	15-Oct-24	11-Feb-25
SUB-3950	Prepare & Submit Fiber Optic Cabling system Samples	81	15-Oct-24	11-Feb-25
APP-3930	Review & Approve Fiber Optic Cabling system Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3940	Review & Approve Fiber Optic Cabling system Product Data	21	12-Feb-25	04-Mar-25
APP-3950	Review & Approve Fiber Optic Cabling system Samples	21	12-Feb-25	04-Mar-25
Spec Section 16770 - Sound, Intercom & Teacher Activated Security System		95	15-Oct-24	04-Mar-25
SUB-3960	Prepare & Submit Sound, Intercome & Security System Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3970	Prepare & Submit Sound, Intercome & Security System Programming Code and Password for the System	81	15-Oct-24	11-Feb-25
SUB-3980	Prepare & Submit Sound, Intercome & Security System Warranty	81	15-Oct-24	11-Feb-25
APP-3960	Review & Approve Sound, Intercome & Security System Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3970	Review & Approve Sound, Intercome & Security System Programming Code and Password for the System	21	12-Feb-25	04-Mar-25
APP-3980	Review & Approve Sound, Intercome & Security System warranty	21	12-Feb-25	04-Mar-25
Spec Section 16771 - Projection And Interactive Whiteboard Systems		95	15-Oct-24	04-Mar-25
SUB-3990	Prepare & Submit Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	81	15-Oct-24	11-Feb-25
SUB-4000	Prepare & Submit Projection and Interactive Whiteboard Systems Wiring diagram	81	15-Oct-24	11-Feb-25
APP-3990	Review & Approve Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	21	12-Feb-25	04-Mar-25
APP-4000	Review & Approve Projection and Interactive Whiteboard Systems Wiring diagram	21	12-Feb-25	04-Mar-25
Spec Section 16785 - Internet Protocol Digital Video Surveillance System using Digital Cameras		95	15-Oct-24	04-Mar-25
SUB-1690	Prepare & Submit Internet Protocol Digital Video Surveillance System using Digital Cameras	71	15-Oct-24	28-Jan-25
APP-1220	Review & Approve Internet Protocol Digital Video Surveillance System using Digital Cameras	35	29-Jan-25	04-Mar-25
Spec Section 16791 - Self-Corrective Clock System		95	15-Oct-24	04-Mar-25
SUB-4010	Prepare & Submit Self Corrective Clock System Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-4020	Prepare & Submit Self Corrective Clock System Product Data	81	15-Oct-24	11-Feb-25
SUB-4030	Prepare & Submit Self Corrective Clock System Field Test Reports	81	15-Oct-24	11-Feb-25
APP-4010	Review & Approve Self Corrective Clock System Shop Drawing	21	12-Feb-25	04-Mar-25

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
APP-4020	Review & Approve Self Corrective Clock System Product Data	21	12-Feb-25	04-Mar-25
APP-4030	Review & Approve Self Corrective Clock System Field Test Reports	21	12-Feb-25	04-Mar-25
Spec Section 16855 - Heat Trace Cable System		95	15-Oct-24	04-Mar-25
SUB-4040	Prepare & Submit Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	81	15-Oct-24	11-Feb-25
APP-4040	Review & Approve Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	21	12-Feb-25	04-Mar-25
Fabrication & Delivery		475	02-Jun-25	19-Sep-26
PRO-1590	Procure & Deliver Steel Columns	120	02-Jun-25	29-Sep-25
PRO-1120	Procure & Deliver Erosion Control and Sedimentation Devices	25	05-Sep-25	29-Sep-25
PRO-1420	Procure & Deliver Painting	70	30-Sep-25	08-Dec-25
PRO-1410	Procure & Deliver Door Frames	70	30-Sep-25	08-Dec-25
PRO-1200	Procure & Deliver Elevator Machine	112	30-Sep-25	19-Jan-26
PRO-1150	Procure & Deliver Gypsum Board	150	30-Sep-25	26-Feb-26
PRO-1160	Procure & Deliver Floorings	80	30-Sep-25	18-Dec-25
PRO-1170	Procure & Deliver Acosutical Ceiling Tiles	120	30-Sep-25	27-Jan-26
PRO-1190	Procure & Deliver Toilet Accessories	100	30-Sep-25	07-Jan-26
PRO-1000	Procure & Deliver Kitchen Equipment	180	30-Sep-25	28-Mar-26
PRO-1140	Procure & Deliver Lighting Fixtures	60	30-Sep-25	28-Nov-25
PRO-1010	Procure & Deliver Furnitures	130	30-Sep-25	06-Feb-26
PRO-1020	Procure & Deliver Mechanical Piping	70	30-Sep-25	08-Dec-25
PRO-1030	Procure & Deliver Mechanical Ducts	70	30-Sep-25	08-Dec-25
PRO-1050	Procure & Deliver Electrical Equipment	130	30-Sep-25	06-Feb-26
PRO-1060	Procure & Deliver Plumbing Fixtures	100	30-Sep-25	07-Jan-26
PRO-1070	Procure & Deliver Wood Doors	50	30-Sep-25	18-Nov-25
PRO-1090	Procure & Deliver Fire Sprinklers	100	30-Sep-25	07-Jan-26
PRO-1110	Procure & Deliver Fire Detectors & Alarms	60	30-Sep-25	28-Nov-25
PRO-1210	Procure & Deliver Signs	70	30-Sep-25	08-Dec-25
PRO-1220	Procure & Deliver Windows & Storefronts	154	30-Sep-25	02-Mar-26
PRO-1250	Procure & Deliver Plumbing Pipes	60	30-Sep-25	28-Nov-25
PRO-1260	Procure & Deliver Electrical Wires & Conduits	130	30-Sep-25	06-Feb-26
PRO-1270	Procure & Deliver Mechanical Pumps	70	30-Sep-25	08-Dec-25
PRO-1280	Procure & Deliver Fire Protection Pumps	70	30-Sep-25	08-Dec-25
PRO-1290	Procure & Deliver Plumbing Pumps	250	30-Sep-25	06-Jun-26
PRO-1310	Procure & Deliver Telecommunication System	60	30-Sep-25	28-Nov-25
PRO-1330	Procure & Deliver Cameras	60	30-Sep-25	28-Nov-25
PRO-1360	Procure & Deliver Metal Panel Ceilings	120	30-Sep-25	27-Jan-26
PRO-1380	Procure & Deliver Roof Dunnage	100	30-Sep-25	07-Jan-26
PRO-1470	Procure & Deliver Cabinet Heaters	126	30-Sep-25	02-Feb-26
PRO-1480	Procure & Deliver Chillers	170	30-Sep-25	18-Mar-26
PRO-1490	Procure & Deliver Air Handling Units	250	30-Sep-25	06-Jun-26
PRO-1500	Procure & Deliver Boilers	84	30-Sep-25	22-Dec-25
PRO-1510	Procure & Deliver Emergency Generator	290	30-Sep-25	16-Jul-26
PRO-1520	Procure & Deliver Switch Gears	250	30-Sep-25	06-Jun-26
PRO-1530	Procure & Deliver Hydraulic Vertical Wheelchair Lift	90	30-Sep-25	28-Dec-25
PRO-1560	Procure & Deliver Gymnasium Equipment	180	30-Sep-25	28-Mar-26

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
PRO-1570	Procure & Deliver Precast Sandwich Panels	112	30-Sep-25	19-Jan-26
PRO-1580	Procure & Deliver Metal Deck	70	30-Sep-25	08-Dec-25
PRO-1600	Procure & Deliver Trusses	60	30-Sep-25	28-Nov-25
PRO-1610	Procure & Deliver Prefabricated Expansion Joint Covers	60	30-Sep-25	28-Nov-25
PRO-1620	Procure & Deliver Security Screens & Barriers	60	30-Sep-25	28-Nov-25
PRO-1630	Procure & Deliver Wood Flooring	120	30-Sep-25	27-Jan-26
PRO-1640	Procure & Deliver Concrete Floating Floor Assembly	120	30-Sep-25	27-Jan-26
PRO-1660	Procure & Deliver Auditorium Television Studio Dimming System	90	30-Sep-25	28-Dec-25
PRO-2010	Procure & Deliver Steel Stairs Components	120	30-Sep-25	27-Jan-26
PRO-2020	Procure & Deliver Flagpole	60	30-Sep-25	28-Nov-25
PRO-2030	Procure & Deliver Bleachers	130	30-Sep-25	06-Feb-26
PRO-2040	Procure & Deliver VAV Units	170	30-Sep-25	18-Mar-26
PRO-2050	Procure & Deliver Furnitures (Owner Responsibility)	130	30-Sep-25	06-Feb-26
PRO-1450	Procure & Deliver Playground Equipment	60	09-Dec-25	06-Feb-26
PRO-1990	Procure & Deliver Gas Meter Rig	60	25-Apr-26	23-Jun-26
PRO-2000	Procure & Deliver Key Cutting Machine	74	08-Jul-26	19-Sep-26
Construction		231	16-Oct-25	17-Sep-26
First Floor		227	16-Oct-25	11-Sep-26
SSDS		8	16-Oct-25	27-Oct-25
CON-9898	Install Gas Permeable Aggregate -1st Floor	3	16-Oct-25	20-Oct-25
CON-98947	Install 4" slotted schedule 80 PVC Piping -1st Floor	3	16-Oct-25	20-Oct-25
CON-9888	Install Liquid Boot VI-20 Geomembrane -1st Floor	2	21-Oct-25	22-Oct-25
CON-1020	Install 60 Dry MILS Liquid Boot -1st Floor	3	23-Oct-25	27-Oct-25
CON-9777	Install Liquid Ultrashield G-1000 -1st Floor	2	24-Oct-25	27-Oct-25
Structure-1st Floor		89	28-Oct-25	09-Mar-26
CON-1040	F/R/P Concrete Walls & Beams -1st Floor	10	28-Oct-25	10-Nov-25
CON-1050	Install Underground Conduits & Wires -1st Floor	6	12-Nov-25	19-Nov-25
CON-1060	Backfilling & Compaction -1st Floor	6	12-Nov-25	19-Nov-25
CON-1070	F/R/P SOG -1st Floor	10	20-Nov-25	04-Dec-25
CON-98787	Install Steel Columns -1st Floor	7	05-Dec-25	15-Dec-25
CON-1090	Install Trusses -1st Floor	3	16-Dec-25	18-Dec-25
CON-1100	Install Framing Beams -1st Floor	4	16-Dec-25	19-Dec-25
CON-99277	Install Steel Stairs -1st Floor	7	28-Jan-26	05-Feb-26
CON-1180	Spray Fireproofing - 1st Floor	5	03-Mar-26	09-Mar-26
Mechanical- 1st Floor		164	22-Dec-25	17-Aug-26
HVAC Rough-ins-1st Floor		134	22-Dec-25	06-Jul-26
CON-1130	Install MEP Hangers & Sleeves- 2nd Floor	4	22-Dec-25	26-Dec-25
CON-2900	Install Duct Risers-1st Floor	1	07-Apr-26	07-Apr-26
CON-3060	Install Mechanical Piping Risers-1st Floor	2	08-Apr-26	09-Apr-26
CON-3070	Duct Leak Test -1st Floor	1	08-Apr-26	08-Apr-26
CON-3120	Rough-in Duct Work -1st Floor	4	09-Apr-26	14-Apr-26
CON-3460	Rough-in Hot Water Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3470	Rough-in Hot Glycol Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3480	Rough-in Chilled Glycol Piping-1st Floor	4	15-Apr-26	20-Apr-26

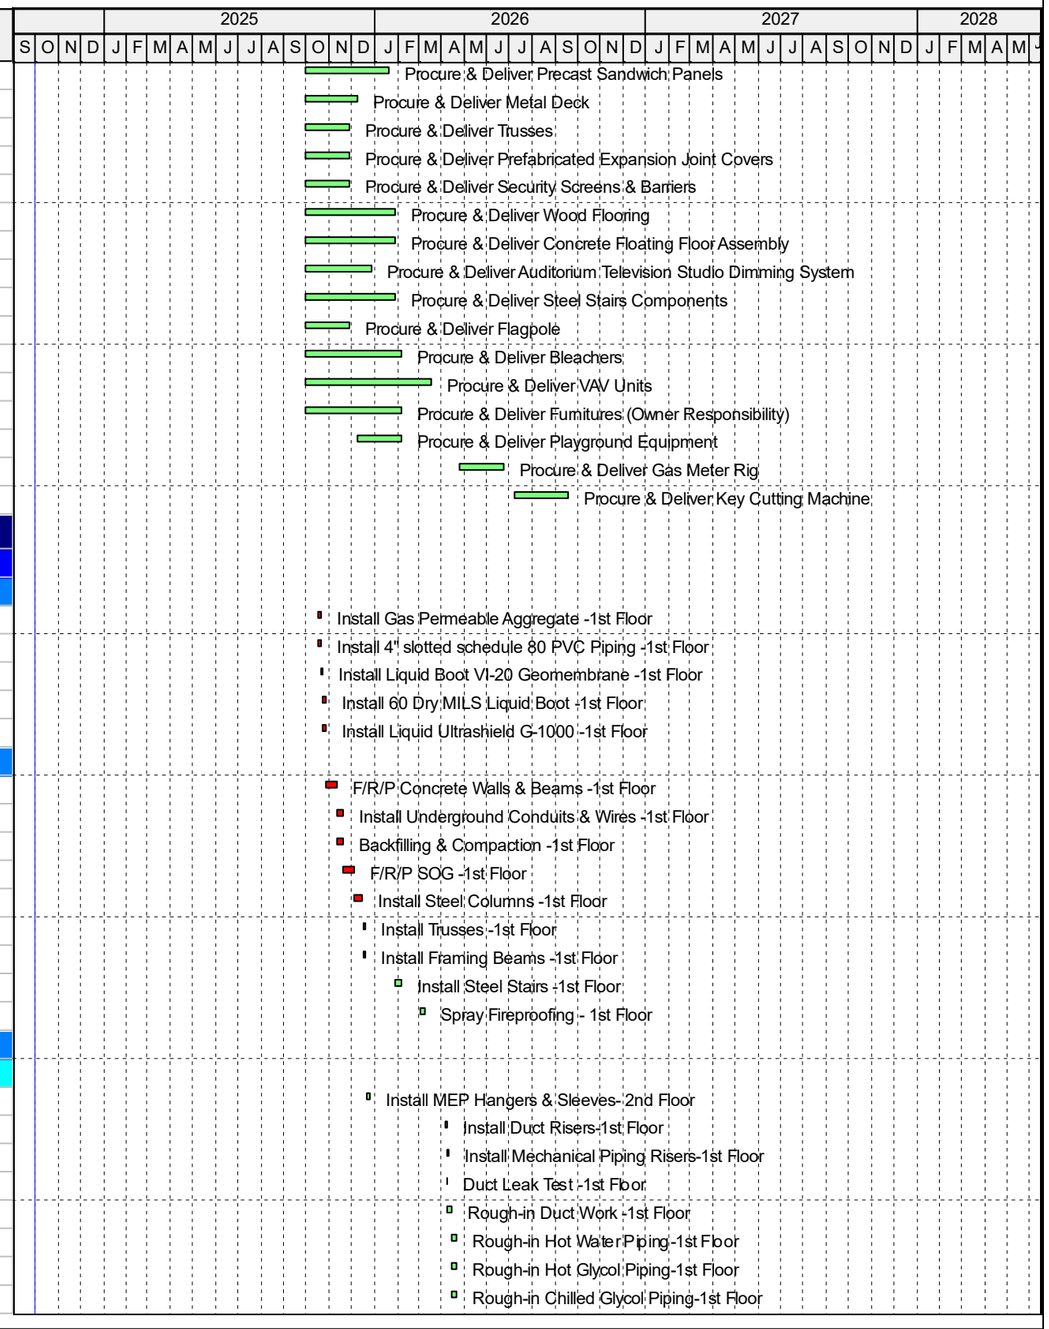

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3490	Rough-in Refrigerant Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3970	Install VAV Boxes & Sound Attenuator Devices- 1st Floor	5	16-Apr-26	22-Apr-26
CON-4840	Install Duct Insulation -1st Floor	8	24-Jun-26	06-Jul-26
Mechanical Equipment-1st Floor		30	07-Jul-26	17-Aug-26
CON-4670	Install Exhaust Fans -1st Floor	5	07-Jul-26	13-Jul-26
CON-4870	Install Cabinet Unit Heaters With Fan CUH-1st Floor	3	14-Jul-26	16-Jul-26
CON-4880	Install Motorized Fire/Smoke Damper FSD - Mechanical Work - 1st Floor	7	14-Jul-26	22-Jul-26
CON-5070	Install Electric Unit Heaters -1st Floor	7	17-Jul-26	27-Jul-26
CON-5150	Install Air Conditioning Unit AC - Mechanical Work - 1st Floor	4	23-Jul-26	28-Jul-26
CON-5320	Install Door Curtains DC - Mechanical Work - 1st Floor	7	29-Jul-26	06-Aug-26
CON-5490	Install Convector Heater CV - Mechanical Work - 1st Floor	7	07-Aug-26	17-Aug-26
Plumbing-1st Floor		177	27-Nov-25	12-Aug-26
CON-4920	Install Floor Drains & Clean-outs -1st Floor	5	27-Nov-25	04-Dec-25
CON-3140	Install Plumbing Risers -1st Floor	2	10-Apr-26	13-Apr-26
CON-3230	Install SSDS Risers -SSDS System -1st Floor	2	14-Apr-26	15-Apr-26
CON-4460	Rough-in Gas Risers -1st Floor	4	07-May-26	12-May-26
CON-4590	Rough-in Domestic Water Piping-1st Floor	4	13-May-26	18-May-26
CON-4690	Rough-in Sanitary & Vent Piping -1st Floor	4	19-May-26	22-May-26
CON-4760	Rough-in Storm Piping -1st Floor	4	26-May-26	29-May-26
CON-4940	Install Duplex Domestic Water Booster Pump System (BP-1&BP-2) -1st Floor	8	01-Jun-26	10-Jun-26
CON-4950	Install Duplex Ejector Pump System (EJ-1&EJ-2) -1st Floor	8	01-Jun-26	10-Jun-26
CON-5050	Plumbing Pressure Testing -1st Floor	5	11-Jun-26	17-Jun-26
CON-5210	Plumbing Piping Insulation -1st Floor	5	18-Jun-26	25-Jun-26
CON-5300	Install Grease Interceptors - 1st Floor	5	28-Jul-26	03-Aug-26
CON-6180	Install Plumbing Fixtures-1st Floor	5	06-Aug-26	12-Aug-26
Fire Protection-1st Floor		55	02-Jun-26	19-Aug-26
CON-4910	Install 4" Standpipe -1st Floor	4	02-Jun-26	05-Jun-26
CON-5030	Rough-in Main Sprinkler Piping -1st Floor	5	08-Jun-26	12-Jun-26
CON-5230	Rough-in Branch Sprinkler Piping -1st Floor	5	15-Jun-26	22-Jun-26
CON-5240	Rough-in Sprinkler Heads -1st Floor	5	15-Jun-26	22-Jun-26
CON-5270	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -1st Floor	5	23-Jun-26	29-Jun-26
CON-5410	Sprinklers Air Testing-1st Floor	5	30-Jun-26	07-Jul-26
CON-5860	Install Sprinkler Booster Pump (SBP-1) -1st Floor	10	23-Jul-26	05-Aug-26
CON-6100	Install Jockey Pump (JP-1) -1st Floor	10	06-Aug-26	19-Aug-26
Electrical-1st Floor		189	03-Dec-25	02-Sep-26
CON-99327	Install Lightning Protection System-1st Floor	2	03-Dec-25	04-Dec-25
CON-3260	Install Power Risers-1st Floor	2	14-Apr-26	15-Apr-26
CON-3350	Install Low Voltage Risers-1st Floor	2	16-Apr-26	17-Apr-26
CON-3760	Rough-in Power Conduits -1st Floor	4	21-Apr-26	24-Apr-26
CON-3910	Install Grounding System -1st Floor	5	27-Apr-26	01-May-26
CON-3920	Rough-in Low-Voltage Conduits-1st Floor	4	27-Apr-26	30-Apr-26
CON-3930	Power Wires Pulling-1st Floor	4	27-Apr-26	30-Apr-26
CON-4180	Low Voltage Wires Pulling -1st Floor	4	01-May-26	06-May-26
CON-4500	Install SSDS Control Panel -1st Floor	5	07-May-26	13-May-26

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-4470	Install Wiring Devices -1st Floor	7	15-May-26	26-May-26
CON-5940	Install Lighting Fixtures -1st Floor	7	24-Jul-26	03-Aug-26
CON-98937	Install Sound Clock System Components-1st Floor	3	24-Jul-26	28-Jul-26
CON-98887	Install Auxiliary System Components-1st Floor	4	29-Jul-26	03-Aug-26
CON-98837	Install Intrusion System Components-1st Floor	4	04-Aug-26	07-Aug-26
CON-5950	Install Fire alarm Sensors and Devises -1st Floor	3	05-Aug-26	07-Aug-26
CON-6040	Install IPDVS Devices -1st Floor	7	25-Aug-26	02-Sep-26
Architecture-1st Floor		141	23-Feb-26	11-Sep-26
Interior Walls-1st Floor		100	23-Feb-26	15-Jul-26
CON-1430	Install Unit Masonry Mock-Up	1	23-Feb-26	23-Feb-26
CON-1470	Approve Unit Masonry Mock-Up	4	24-Feb-26	27-Feb-26
CON-2910	Layout -1st Floor	3	07-Apr-26	09-Apr-26
CON-3080	Install Top & Bottom Track -1st Floor	4	10-Apr-26	15-Apr-26
CON-3090	Install CMU Walls -1st Floor	3	10-Apr-26	14-Apr-26
CON-3240	Install Wall Steel Studs & Framing -1st Floor	5	16-Apr-26	22-Apr-26
CON-9110	In-Wall Inspection -1st Floor	2	19-May-26	20-May-26
CON-1120	Install Firestopping Mock-Up	2	01-Jun-26	02-Jun-26
CON-1140	Approve Firestopping Mock-Up	2	03-Jun-26	04-Jun-26
MIL-1750	Start Firestopping	0	05-Jun-26	
CON-4450	Install Gypsum Board Walls-1st Floor	6	26-Jun-26	06-Jul-26
CON-4600	Tape Gypsum Board -1st Floor	4	30-Jun-26	06-Jul-26
CON-5390	Install Firestopping-1st Floor	4	30-Jun-26	06-Jul-26
CON-4680	Install Ceramic Wall Tiles at Corridor -1st Floor	7	07-Jul-26	15-Jul-26
Ceiling-1st Floor		100	15-Apr-26	04-Sep-26
CON-3520	Install Ceiling Hangers & Supports -1st Floor	4	15-Apr-26	20-Apr-26
CON-5480	Install Gypsum Board Ceiling -1st Floor	6	08-Jul-26	15-Jul-26
CON-5870	Install Metal Panel Ceiling & Metal Geometric Ceiling -1st Floor	5	23-Jul-26	29-Jul-26
CON-5880	Install Acoustical Ceiling Tiles -1st Floor	5	31-Aug-26	04-Sep-26
Finishes-1st Floor		41	16-Jul-26	11-Sep-26
CON-5720	Install First Coat Painting-1st Floor	5	16-Jul-26	22-Jul-26
CON-5920	Install Door Frames & Doors-1st Floor	5	23-Jul-26	29-Jul-26
CON-6080	Install Flooring Tiles-1st Floor	5	30-Jul-26	05-Aug-26
CON-99267	Install Rolling Doors-1st Floor	3	30-Jul-26	03-Aug-26
CON-6170	Install Final Coat Painting-1st Floor	6	21-Aug-26	28-Aug-26
CON-6300	Install Furniture & Milling Work (Contractor Provided & Installed) -1st Floor	4	31-Aug-26	03-Sep-26
CON-6310	Install Security Screens & Barriers-1st Floor	3	31-Aug-26	02-Sep-26
CON-6320	Install Cafeteria Equipment-1st Floor	4	31-Aug-26	03-Sep-26
CON-9020	Install Furniture & Milling Work (Owner Provided & Installed) -1st Floor	3	31-Aug-26	02-Sep-26
CON-6370	Install Signages-1st Floor	4	04-Sep-26	10-Sep-26
CON-6380	Install Food Service Equipment-1st Floor	5	04-Sep-26	11-Sep-26
Second Floor		187	19-Dec-25	17-Sep-26
Structure-2nd Floor		57	22-Dec-25	16-Mar-26
CON-1110	Install Metal Deck Slab -2nd Floor	4	22-Dec-25	26-Dec-25
CON-1150	Install Steel Canopy Framing -2nd Floor	5	29-Dec-25	05-Jan-26

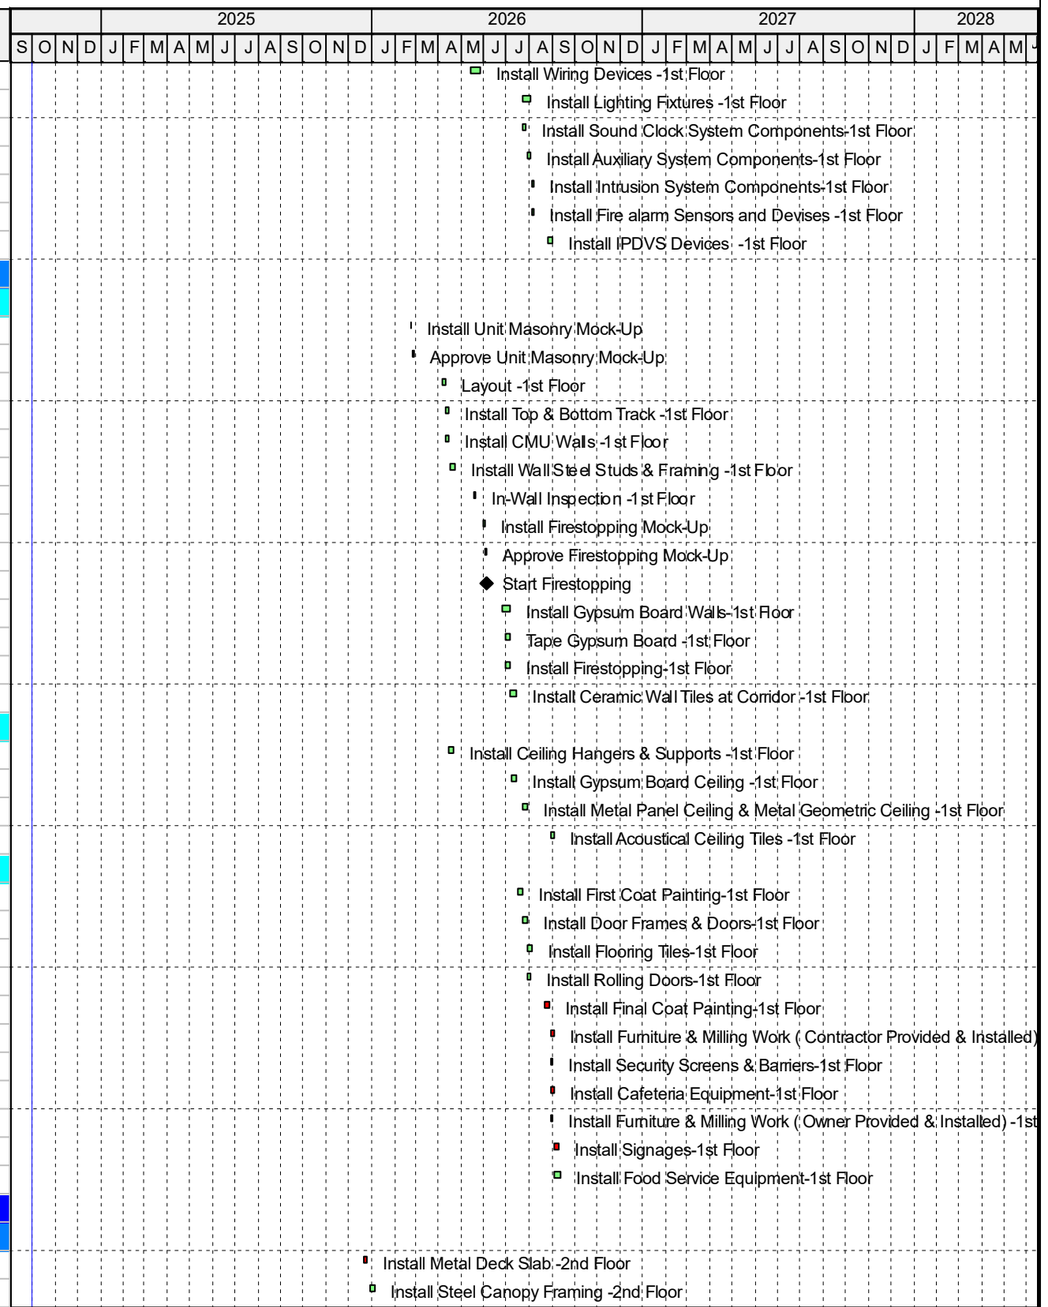

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1170	Install Steel Columns -2nd Floor	3	29-Dec-25	31-Dec-25
CON-1190	Install Trusses -2nd Floor	4	02-Jan-26	07-Jan-26
CON-1200	Install Framing Beams -2nd Floor	5	02-Jan-26	08-Jan-26
CON-99287	Install Steel Stairs -2nd Floor	3	06-Feb-26	10-Feb-26
CON-1220	Spray Fireproofing - 2nd Floor	5	10-Mar-26	16-Mar-26
Material Hoist		182	29-Dec-25	17-Sep-26
CON-1160	Hoist Material Design	10	29-Dec-25	12-Jan-26
CON-1250	Approval of Hoist Design	7	13-Jan-26	19-Jan-26
CON-1280	Install Elevator Hoist Pad	5	20-Jan-26	26-Jan-26
CON-1320	Erect Material Hoist	5	27-Jan-26	02-Feb-26
CON-5040	Dismantle Hoist	2	10-Sep-26	11-Sep-26
CON-5170	Demolish Hoist Pad	2	14-Sep-26	15-Sep-26
CON-5250	Hoist In-Fill	2	16-Sep-26	17-Sep-26
Mechanical-2nd Floor		90	09-Jan-26	18-May-26
HVAC Rough-ins-2nd Floor		90	09-Jan-26	18-May-26
CON-1230	Install MEP Hangers & Sleeves-3rd Floor	4	09-Jan-26	14-Jan-26
CON-1410	Install Duct Risers-2nd Floor	1	23-Feb-26	23-Feb-26
CON-1480	Rough-in Duct Work -2nd Floor	4	24-Feb-26	27-Feb-26
CON-1500	Install Mechanical Piping Risers-2nd Floor	2	24-Feb-26	25-Feb-26
CON-1510	Duct Leak Test -2nd Floor	2	24-Feb-26	25-Feb-26
CON-1850	Rough-in Hot Water Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1860	Rough-in Hot Glycol Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1870	Rough-in Chilled Glycol Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1880	Rough-in Refrigerant Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-3980	Install VAV Boxes & Sound Attenuator Devices-2nd Floor	5	19-Mar-26	25-Mar-26
CON-4070	Install Duct Insulation -2nd Floor	8	07-May-26	18-May-26
Mechanical Equipment-2nd Floor		14	16-Apr-26	05-May-26
CON-2850	Install Electric Unit Heaters -2nd Floor	5	16-Apr-26	22-Apr-26
CON-3150	Install Convector Heater CV - Mechanical Work - 2nd Floor	5	23-Apr-26	29-Apr-26
CON-3450	Install Air Conditioning Unit AC - Mechanical Work - 2nd Floor	4	30-Apr-26	05-May-26
Plumbing-2nd Floor		141	19-Dec-25	14-Jul-26
CON-3160	Install Floor Drains & Clean-outs -2nd Floor	5	19-Dec-25	26-Dec-25
CON-1580	Install Plumbing Risers -2nd Floor	2	26-Feb-26	27-Feb-26
CON-1740	Install SSDS Risers -SSDS System -2nd Floor	2	02-Mar-26	03-Mar-26
CON-2630	Rough-in Gas Risers -2nd Floor	4	06-Apr-26	09-Apr-26
CON-2740	Rough-in Domestic Water Piping -2nd Floor	4	10-Apr-26	15-Apr-26
CON-2870	Rough-in Sanitary & Vent Piping -2nd Floor	4	16-Apr-26	21-Apr-26
CON-3020	Rough-in Storm Piping -2nd Floor	4	22-Apr-26	27-Apr-26
CON-3200	Plumbing Pressure Testing -2nd Floor	5	28-Apr-26	04-May-26
CON-4050	Plumbing Piping Insulation -2nd Floor	5	07-May-26	13-May-26
CON-5570	Install Plumbing Fixtures -2nd Floor	7	06-Jul-26	14-Jul-26
Electrical-2nd Floor		96	02-Mar-26	16-Jul-26
CON-1710	Install Power Risers-2nd Floor	2	02-Mar-26	03-Mar-26
CON-1800	Install Low Voltage Risers-2nd Floor	2	04-Mar-26	05-Mar-26

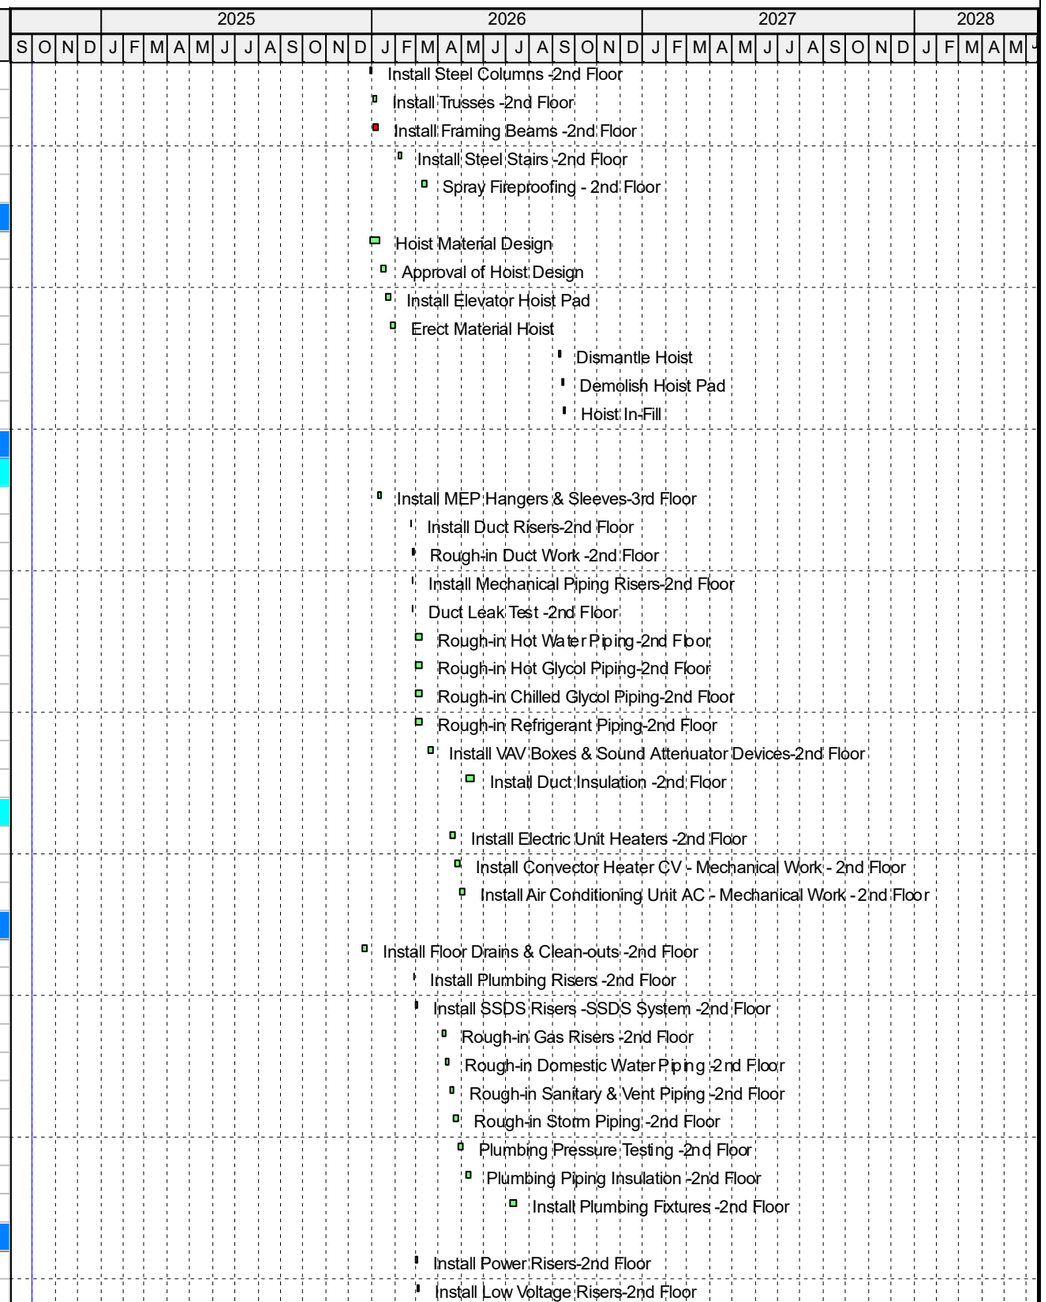

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2180	Rough-in Power Conduits -2nd Floor	6	11-Mar-26	18-Mar-26
CON-2330	Rough-in Low-Voltage Conduits -2nd Floor	6	19-Mar-26	26-Mar-26
CON-2340	Power Wires Pulling -2nd Floor	6	19-Mar-26	26-Mar-26
CON-2490	Low Voltage Wires Pulling -2nd Floor	6	27-Mar-26	03-Apr-26
CON-2520	Install Voice Rack - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2530	Install Data Rack - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2540	Install Ground Bus Bar - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2670	Install Wiring Devices -2nd Floor	7	06-Apr-26	14-Apr-26
CON-2760	Install IPDVS Equipment Rack - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2770	Install Ladder Rack Cable Tray - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2780	Install BACnet Data Cabinet - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-5130	Install Lighting Fixtures -2nd Floor	5	18-Jun-26	25-Jun-26
CON-98797	Install Intrusion System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-98847	Install Auxiliary System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-98897	Install Sound Clock System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-5310	Install Fire alarm Sensors and Devises -2nd Floor	5	26-Jun-26	02-Jul-26
CON-5140	Install IPDVS Devices -2nd Floor	9	06-Jul-26	16-Jul-26
Fire Protection-2nd Floor		106	29-Dec-25	29-May-26
CON-3270	Install Temporary Standpipe	9	29-Dec-25	09-Jan-26
CON-3310	Install 4" Standpipe -2nd Floor	4	04-May-26	07-May-26
CON-3500	Rough-in Main Sprinkler Piping -2nd Floor	5	08-May-26	14-May-26
CON-3670	Rough-in Branch Sprinkler Piping -2nd Floor	5	15-May-26	21-May-26
CON-3680	Rough-in Sprinkler Heads -2nd Floor	5	15-May-26	21-May-26
CON-3720	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -2nd Floor	5	15-May-26	21-May-26
CON-3830	Sprinklers Air Testing-2nd Floor	5	22-May-26	29-May-26
Architecture-2nd Floor		108	23-Feb-26	27-Jul-26
Interior Walls-2nd Floor		78	23-Feb-26	11-Jun-26
CON-1420	Layout -2nd Floor	3	23-Feb-26	25-Feb-26
CON-1520	Install Top & Bottom Track-2nd Floor	4	26-Feb-26	03-Mar-26
CON-1570	Install CMU Walls -2nd Floor	3	02-Mar-26	04-Mar-26
CON-1640	Install Wall Steel Studs & Framing-2nd Floor	5	04-Mar-26	10-Mar-26
CON-9070	In-Wall Inspection-2nd Floor	2	16-Apr-26	17-Apr-26
CON-4030	Install Gypsum Board Walls-2nd Floor	5	27-May-26	02-Jun-26
CON-4200	Tape Gypsum Board -2nd Floor	4	28-May-26	02-Jun-26
CON-4350	Install Ceramic Wall Tiles at Corridor-2nd Floor	7	03-Jun-26	11-Jun-26
CON-4700	Install Firestopping-2nd Floor	3	05-Jun-26	09-Jun-26
Ceiling-2nd Floor		88	16-Mar-26	20-Jul-26
CON-2310	Install Ceiling Hangers & Supports-2nd Floor	4	16-Mar-26	19-Mar-26
CON-4370	Install Gypsum Board Ceiling -2nd Floor	6	03-Jun-26	10-Jun-26
CON-5090	Install Acoustical Ceiling Tiles-2nd Floor	5	14-Jul-26	20-Jul-26
Finishes-2nd Floor		31	11-Jun-26	27-Jul-26
CON-4830	Install First Coat Painting-2nd Floor	5	11-Jun-26	17-Jun-26
CON-5120	Install Door Frames & Doors-2nd Floor	5	18-Jun-26	25-Jun-26
CON-5360	Install Flooring Tiles-2nd Floor	5	26-Jun-26	02-Jul-26

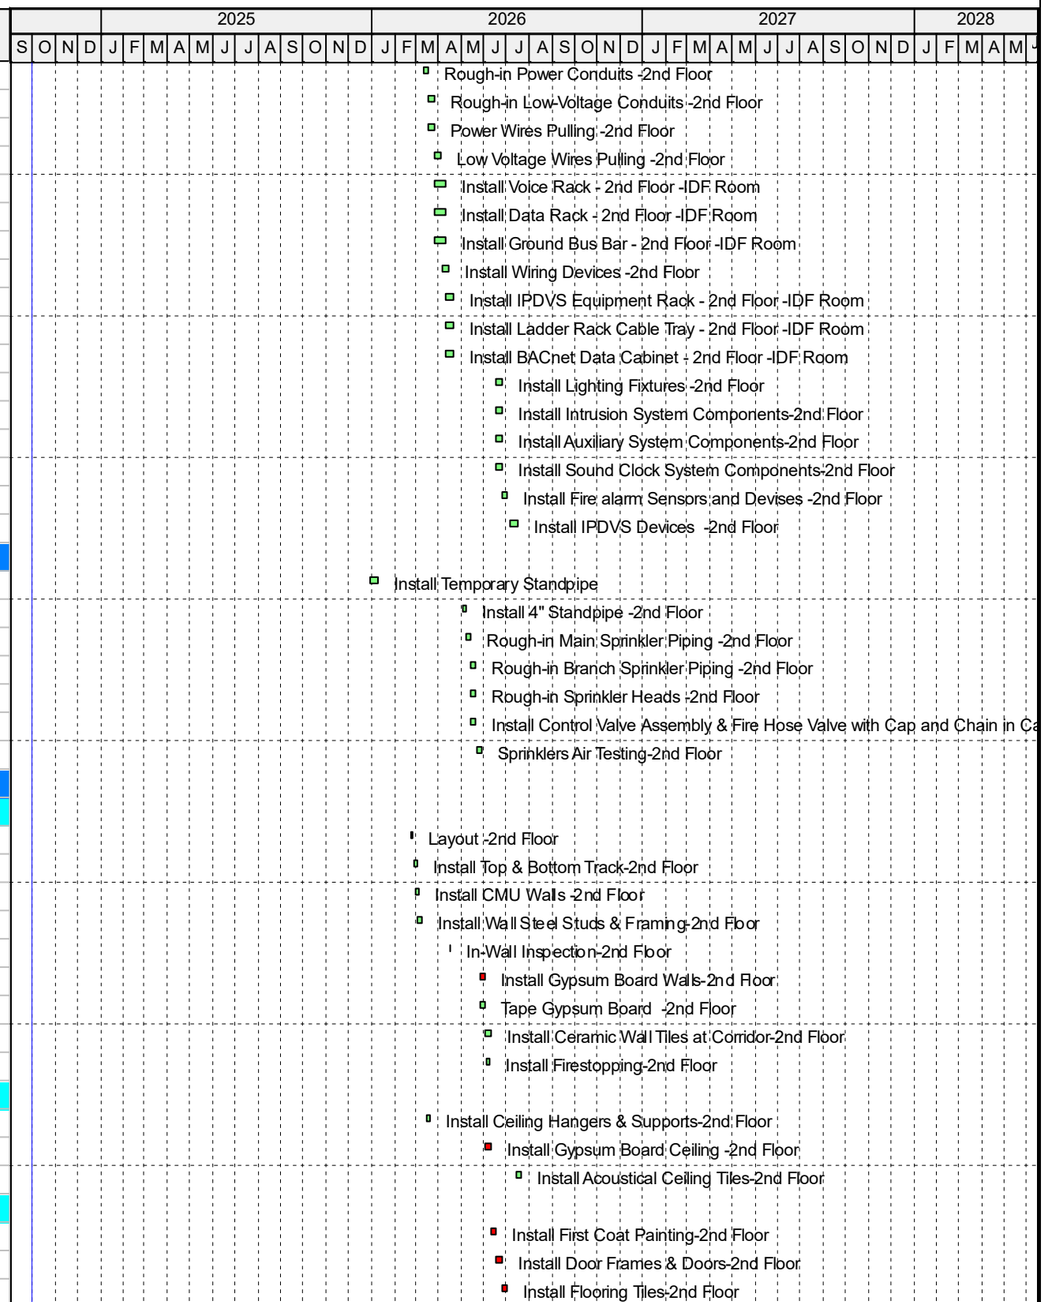

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-5560	Install Final Coat Painting-2nd Floor	6	06-Jul-26	13-Jul-26
CON-5710	Install Furniture & Milling Work (Contractor Provided & Installed) -2nd Floor	5	14-Jul-26	20-Jul-26
CON-9030	Install Furniture & Milling Work (Owner Provided & Installed) -2nd Floor	5	14-Jul-26	20-Jul-26
CON-5820	Install Signages-2nd Floor	5	21-Jul-26	27-Jul-26
Third Floor		144	08-Jan-26	04-Aug-26
Structure -3rd Floor		50	09-Jan-26	23-Mar-26
CON-1210	Install Metal Deck Slab - 3rd Floor	4	09-Jan-26	14-Jan-26
CON-1240	Install Steel Columns - 3rd Floor	4	15-Jan-26	21-Jan-26
CON-1260	Install Trusses - 3rd Floor	3	22-Jan-26	26-Jan-26
CON-1270	Install Framing Beams - 3rd Floor	5	22-Jan-26	28-Jan-26
CON-99297	Install Steel Stairs- 3rd Floor	4	11-Feb-26	17-Feb-26
CON-1300	Spray Fireproofing - 3rd Floor	5	17-Mar-26	23-Mar-26
Mechanical -3rd Floor		129	29-Jan-26	03-Aug-26
HVAC Rough-ins -3rd Floor		85	29-Jan-26	29-May-26
CON-1310	Install MEP Hangers & Sleeves-4th Floor	4	29-Jan-26	03-Feb-26
CON-1490	Install Duct Risers -3rd Floor	2	24-Feb-26	25-Feb-26
CON-1590	Install Mechanical Piping Risers -3rd Floor	2	26-Feb-26	27-Feb-26
CON-1600	Duct Leak Test -3rd Floor	2	26-Feb-26	27-Feb-26
CON-1890	Rough-in Duct Work -3rd Floor	5	02-Mar-26	06-Mar-26
CON-2160	Rough-in Refrigerant Piping-3rd Floor	7	09-Mar-26	17-Mar-26
CON-2130	Rough-in Hot Water Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-2140	Rough-in Hot Glycol Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-2150	Rough-in Chilled Glycol Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-4140	Install VAV Boxes & Sound Attenuator Devices-3rd Floor	5	26-Mar-26	01-Apr-26
CON-4320	Install Duct Insulation -3rd Floor	8	19-May-26	29-May-26
Mechanical Equipment -3rd Floor		70	23-Apr-26	03-Aug-26
CON-3130	Install Electric Unit Heaters -3rd Floor	5	23-Apr-26	29-Apr-26
CON-5060	Install Hot Glycol / Hot Water Cabinet Heater (CUH)-3rd Floor	4	17-Jul-26	22-Jul-26
CON-5280	Install Convector Heater CV - Mechanical Work - 3rd Floor	4	23-Jul-26	28-Jul-26
CON-5450	Install Air Conditioning Unit AC - Mechanical Work - 3rd Floor	4	29-Jul-26	03-Aug-26
Plumbing -3rd Floor		136	08-Jan-26	23-Jul-26
CON-3320	Install Floor Drains & Clean-outs -3rd Floor	5	08-Jan-26	14-Jan-26
CON-1680	Install Plumbing Risers -3rd Floor	2	02-Mar-26	03-Mar-26
CON-1840	Install SSDS Risers -SSDS System -3rd Floor	2	04-Mar-26	05-Mar-26
CON-2750	Rough-in Gas Risers-3rd Floor	4	10-Apr-26	15-Apr-26
CON-2880	Rough-in Domestic Water Piping -3rd Floor	4	16-Apr-26	21-Apr-26
CON-3030	Rough-in Sanitary & Vent Piping -3rd Floor	4	22-Apr-26	27-Apr-26
CON-3170	Rough-in Storm Piping -3rd Floor	4	28-Apr-26	01-May-26
CON-3360	Plumbing Pressure Testing -3rd Floor	5	05-May-26	11-May-26
CON-4190	Plumbing Piping Insulation -3rd Floor	5	14-May-26	20-May-26
CON-5730	Install Plumbing Fixtures -3rd Floor	7	15-Jul-26	23-Jul-26
Electrical -3rd Floor		103	04-Mar-26	29-Jul-26
CON-1820	Install Power Risers-3rd Floor	2	04-Mar-26	05-Mar-26
CON-1950	Install Low Voltage Risers-3rd Floor	2	06-Mar-26	09-Mar-26

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2320	Rough-in Power Conduits-3rd Floor	6	19-Mar-26	26-Mar-26
CON-2640	Install Grounding Bars - 3rd Floor IDF Room	5	27-Mar-26	02-Apr-26
CON-2500	Rough-in Low-Voltage Conduits-3rd Floor	6	27-Mar-26	03-Apr-26
CON-2510	Power Wires Pulling-3rd Floor	6	27-Mar-26	03-Apr-26
CON-2800	Install Data rack - 3rd Floor IDF Room	8	03-Apr-26	14-Apr-26
CON-2830	Install IPDVS Equipment Rack - 3rd Floor IDF Room	4	03-Apr-26	08-Apr-26
CON-2690	Low Voltage Wires Pulling -3rd Floor	6	06-Apr-26	13-Apr-26
CON-3250	Install Voice Rack - 3rd Floor IDF Room	5	15-Apr-26	21-Apr-26
CON-2930	Install Wiring Devices -3rd Floor	7	15-Apr-26	23-Apr-26
CON-3550	Install Cable Ladder - 3rd Floor IDF Room	5	22-Apr-26	28-Apr-26
CON-3570	Install Main Sound Rack - 3rd Floor IDF Room	5	22-Apr-26	28-Apr-26
CON-5370	Install Lighting Fixtures -3rd Floor	6	29-Jun-26	07-Jul-26
CON-5500	Install Fire alarm Sensors and Devises -3rd Floor	8	08-Jul-26	17-Jul-26
CON-5440	Install IPDVS Devices -3rd Floor	9	17-Jul-26	29-Jul-26
Fire Protection -3rd Floor		20	08-May-26	05-Jun-26
CON-3510	Install 4" Standpipe -3rd Floor	4	08-May-26	13-May-26
CON-3690	Rough-in Main Sprinkler Piping-3rd Floor	5	15-May-26	21-May-26
CON-3790	Rough-in Branch Sprinkler Piping -3rd Floor	5	22-May-26	29-May-26
CON-3800	Rough-in Sprinkler Heads -3rd Floor	5	22-May-26	29-May-26
CON-3880	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-3rd Floor	5	22-May-26	29-May-26
CON-4060	Sprinklers Air Testing-3rd Floor	5	01-Jun-26	05-Jun-26
Architecture -3rd Floor		111	26-Feb-26	04-Aug-26
Interior Walls -3rd Floor		82	26-Feb-26	23-Jun-26
CON-1530	Layout -3rd Floor	3	26-Feb-26	02-Mar-26
CON-1650	Install Top & Bottom Track-3rd Floor	4	04-Mar-26	09-Mar-26
CON-1660	Install CMU Walls -3rd Floor	3	05-Mar-26	09-Mar-26
CON-1900	Install Wall Steel Studs & Framing-3rd Floor	5	10-Mar-26	16-Mar-26
CON-9080	In-Wall Inspection -3rd Floor	2	22-Apr-26	23-Apr-26
CON-4360	Install Gypsum Board Walls-3rd Floor	5	03-Jun-26	09-Jun-26
CON-4540	Tape Gypsum Board -3rd Floor	4	04-Jun-26	09-Jun-26
CON-4850	Install Firestopping-3rd Floor	4	10-Jun-26	15-Jun-26
CON-4610	Install Ceramic Wall Tiles at Corridor-3rd Floor	7	12-Jun-26	23-Jun-26
Ceiling -3rd Floor		90	20-Mar-26	28-Jul-26
CON-2390	Install Ceiling Hangers & Supports-3rd Floor	4	20-Mar-26	25-Mar-26
CON-4630	Install Gypsum Board Ceiling-3rd Floor	6	11-Jun-26	18-Jun-26
CON-5330	Install Acoustical Ceiling Tiles-3rd Floor	5	22-Jul-26	28-Jul-26
Finishes -3rd Floor		31	22-Jun-26	04-Aug-26
CON-5110	Install First Coat Painting-3rd Floor	5	22-Jun-26	26-Jun-26
CON-5350	Install Door Frames & Doors-3rd Floor	5	29-Jun-26	06-Jul-26
CON-98807	Install Intrusion System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-98857	Install Auxiliary System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-98907	Install Sound Clock System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-5550	Install Flooring Tiles-3rd Floor	5	07-Jul-26	13-Jul-26
CON-5700	Install Final Coat Painting-3rd Floor	6	14-Jul-26	21-Jul-26

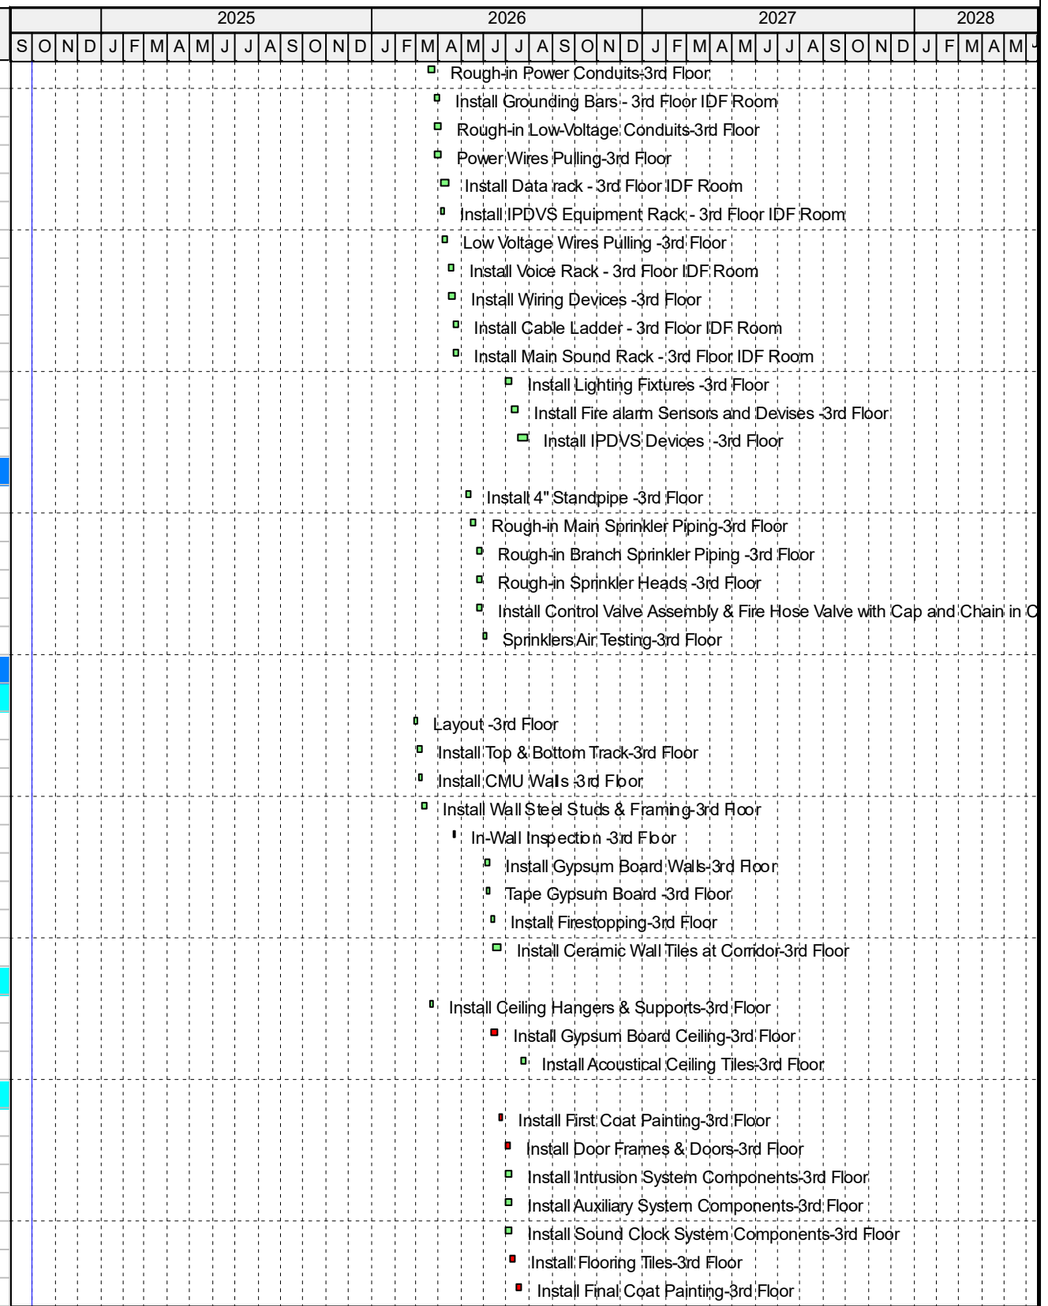

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-99247	Install Laboratory Equipment -3rd Floor	4	14-Jul-26	17-Jul-26
CON-5910	Install Furniture & Milling Work (Contractor Provided & Installed) -3rd Floor	5	22-Jul-26	28-Jul-26
CON-9040	Install Furniture & Milling Work (Owner Provided & Installed) -3rd Floor	5	22-Jul-26	28-Jul-26
CON-6030	Install Signages-3rd Floor	5	29-Jul-26	04-Aug-26
Fourth Floor		137	28-Jan-26	12-Aug-26
Structure -4th Floor		42	29-Jan-26	30-Mar-26
CON-1290	Install Metal Deck Slab - 4th Floor	4	29-Jan-26	03-Feb-26
CON-1330	Install Steel Columns - 4th Floor	4	04-Feb-26	09-Feb-26
CON-1360	Install Trusses - 4th Floor	3	10-Feb-26	12-Feb-26
CON-1370	Install Framing Beams - 4th Floor	5	10-Feb-26	17-Feb-26
CON-99307	Install Steel Stairs - 4th Floor	4	23-Feb-26	26-Feb-26
CON-1390	Spray Fireproofing - 4th Floor	5	24-Mar-26	30-Mar-26
Mechanical-4th Floor		121	17-Feb-26	07-Aug-26
HVAC Rough-ins-4th Floor		81	17-Feb-26	10-Jun-26
CON-1400	Install MEP Hangers & Sleeves-5th Floor	4	17-Feb-26	20-Feb-26
CON-1560	Install Duct Risers -4th Floor	2	26-Feb-26	27-Feb-26
CON-1690	Install Mechanical Piping Risers -4th Floor	2	02-Mar-26	03-Mar-26
CON-1700	Duct Leak Test -4th Floor	2	02-Mar-26	03-Mar-26
CON-2170	Rough-in Duct Work -4th Floor	5	09-Mar-26	13-Mar-26
CON-2290	Rough-in Refrigerant Piping-4th Floor	7	16-Mar-26	24-Mar-26
CON-2260	Rough-in Hot Water Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-2270	Rough-in Hot Glycol Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-2280	Rough-in Chilled Glycol Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-4220	Install VAV Boxes & Sound Attenuator Devices-4th Floor	5	02-Apr-26	08-Apr-26
CON-4570	Install Duct Insulation -4th Floor	8	01-Jun-26	10-Jun-26
Mechanical Equipment-4th Floor		69	30-Apr-26	07-Aug-26
CON-3420	Install Electric Unit Heaters -4th Floor	5	30-Apr-26	06-May-26
CON-5260	Install Cabinet Unit Heater With Fan CUH -4th Floor	4	23-Jul-26	28-Jul-26
CON-5460	Install Convector Heater CV - Mechanical Work - 4th Floor	3	29-Jul-26	31-Jul-26
CON-5620	Install Air Conditioning Unit AC - Mechanical Work - 4th Floor	4	04-Aug-26	07-Aug-26
Plumbing-4th Floor		130	28-Jan-26	03-Aug-26
CON-3530	Install Floor Drains & Clean-outs -4th Floor	5	28-Jan-26	03-Feb-26
CON-1780	Install Plumbing Risers -4th Floor	2	04-Mar-26	05-Mar-26
CON-1970	Install SSDS Risers -SSDS System -4th Floor	2	06-Mar-26	09-Mar-26
CON-2890	Rough-in Gas Risers -4th Floor	4	16-Apr-26	21-Apr-26
CON-3040	Rough-in Domestic Water Piping -4th Floor	4	22-Apr-26	27-Apr-26
CON-3180	Rough-in Sanitary & Vent Piping -4th Floor	4	28-Apr-26	01-May-26
CON-3330	Rough-in Storm Piping -4th Floor	4	04-May-26	07-May-26
CON-3560	Plumbing Pressure Testing -4th Floor	5	12-May-26	18-May-26
CON-4390	Plumbing Piping Insulation -4th Floor	5	21-May-26	28-May-26
CON-5930	Install Plumbing Fixtures -4th Floor	7	24-Jul-26	03-Aug-26
Electrical-4th Floor		110	06-Mar-26	11-Aug-26
CON-1960	Install Power Risers-4th Floor	2	06-Mar-26	09-Mar-26
CON-2040	Install Low Voltage Risers-4th Floor	2	10-Mar-26	11-Mar-26

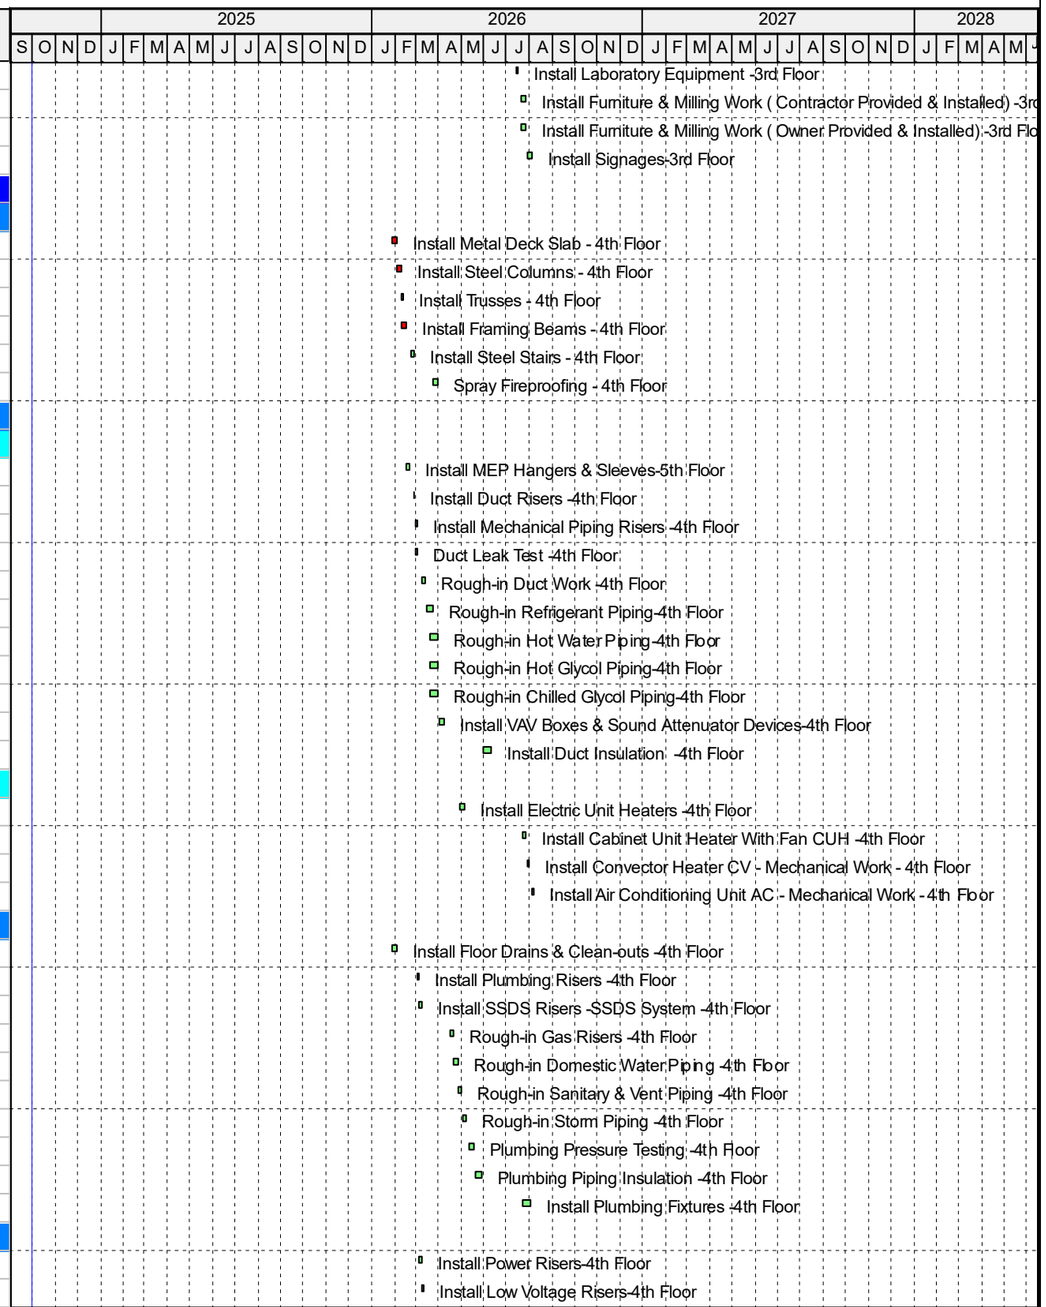

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2480	Rough-in Power Conduits-4th Floor	6	27-Mar-26	03-Apr-26
CON-2810	Install Grounding Bars - 4th Floor IDF Room	5	06-Apr-26	10-Apr-26
CON-2650	Install Data Rack - 4th Floor IDF Room	7	06-Apr-26	14-Apr-26
CON-2660	Install Voice Rack - 4th Floor IDF Room	5	06-Apr-26	10-Apr-26
CON-2700	Rough-in Low-Voltage Conduits-4th Floor	6	06-Apr-26	13-Apr-26
CON-2710	Power Wires Pulling-4th Floor	6	06-Apr-26	13-Apr-26
CON-2820	Install Cable Ladder - 4th Floor IDF Room	5	13-Apr-26	17-Apr-26
CON-2840	Install Main Sound Rack - 34th Floor IDF Room	5	13-Apr-26	17-Apr-26
CON-2940	Low Voltage Wires Pulling-4th Floor	6	15-Apr-26	22-Apr-26
CON-3110	Install IPDVS Equipment Rack - 4th Floor IDF Room	5	20-Apr-26	24-Apr-26
CON-3280	Install Wiring Devices -4th Floor	7	24-Apr-26	04-May-26
CON-5580	Install Lighting Fixtures -4th Floor	6	08-Jul-26	15-Jul-26
CON-98817	Install Intrusion System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-98867	Install Auxiliary System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-98917	Install Sound Clock System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-5660	Install Fire alarm Sensors and Devises -4th Floor	7	20-Jul-26	28-Jul-26
CON-5750	Install IPDVS Devices -4th Floor	9	30-Jul-26	11-Aug-26
Fire Protection-4th Floor		21	14-May-26	12-Jun-26
CON-3650	Install 4" Standpipe -4th Floor	4	14-May-26	19-May-26
CON-3810	Rough-in Main Sprinkler Piping-4th Floor	5	22-May-26	29-May-26
CON-3990	Rough-in Branch Sprinkler Piping -4th Floor	5	01-Jun-26	05-Jun-26
CON-4000	Rough-in Sprinkler Heads -4th Floor	5	01-Jun-26	05-Jun-26
CON-4100	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-4th Floor	5	01-Jun-26	05-Jun-26
CON-4280	Sprinklers Air Testing-4th Floor	5	08-Jun-26	12-Jun-26
Architecture-4th Floor		114	03-Mar-26	12-Aug-26
Interior Walls-4th Floor		86	03-Mar-26	02-Jul-26
CON-1670	Layout -4th Floor	3	03-Mar-26	05-Mar-26
CON-1910	Install Top & Bottom Track-4th Floor	4	10-Mar-26	13-Mar-26
CON-1920	Install CMU Walls -4th Floor	3	10-Mar-26	12-Mar-26
CON-2010	Install Wall Steel Studs & Framing-4th Floor	5	16-Mar-26	20-Mar-26
CON-9090	In-Wall Inspection -4th Floor	7	28-Apr-26	06-May-26
CON-4620	Install Gypsum Board Walls-4th Floor	5	10-Jun-26	16-Jun-26
CON-4720	Tape Gypsum Board -4th Floor	4	11-Jun-26	16-Jun-26
CON-5010	Install Firestopping-4th Floor	4	16-Jun-26	22-Jun-26
CON-4800	Install Ceramic Wall Tiles at Corridor-4th Floor	7	24-Jun-26	02-Jul-26
Ceiling-4th Floor		92	26-Mar-26	05-Aug-26
CON-2550	Install Ceiling Hangers & Supports-4th Floor	4	26-Mar-26	31-Mar-26
CON-4820	Install Gypsum Board Ceiling-4th Floor	6	22-Jun-26	29-Jun-26
CON-5520	Install Acoustical Ceiling Tiles-4th Floor	5	30-Jul-26	05-Aug-26
Finishes-4th Floor		32	29-Jun-26	12-Aug-26
CON-5340	Install First Coat Painting-4th Floor	5	29-Jun-26	06-Jul-26
CON-5540	Install Door Frames & Doors-4th Floor	5	07-Jul-26	13-Jul-26
CON-5690	Install Flooring Tiles-4th Floor	5	14-Jul-26	20-Jul-26
CON-5900	Install Final Coat Painting-4th Floor	6	22-Jul-26	29-Jul-26

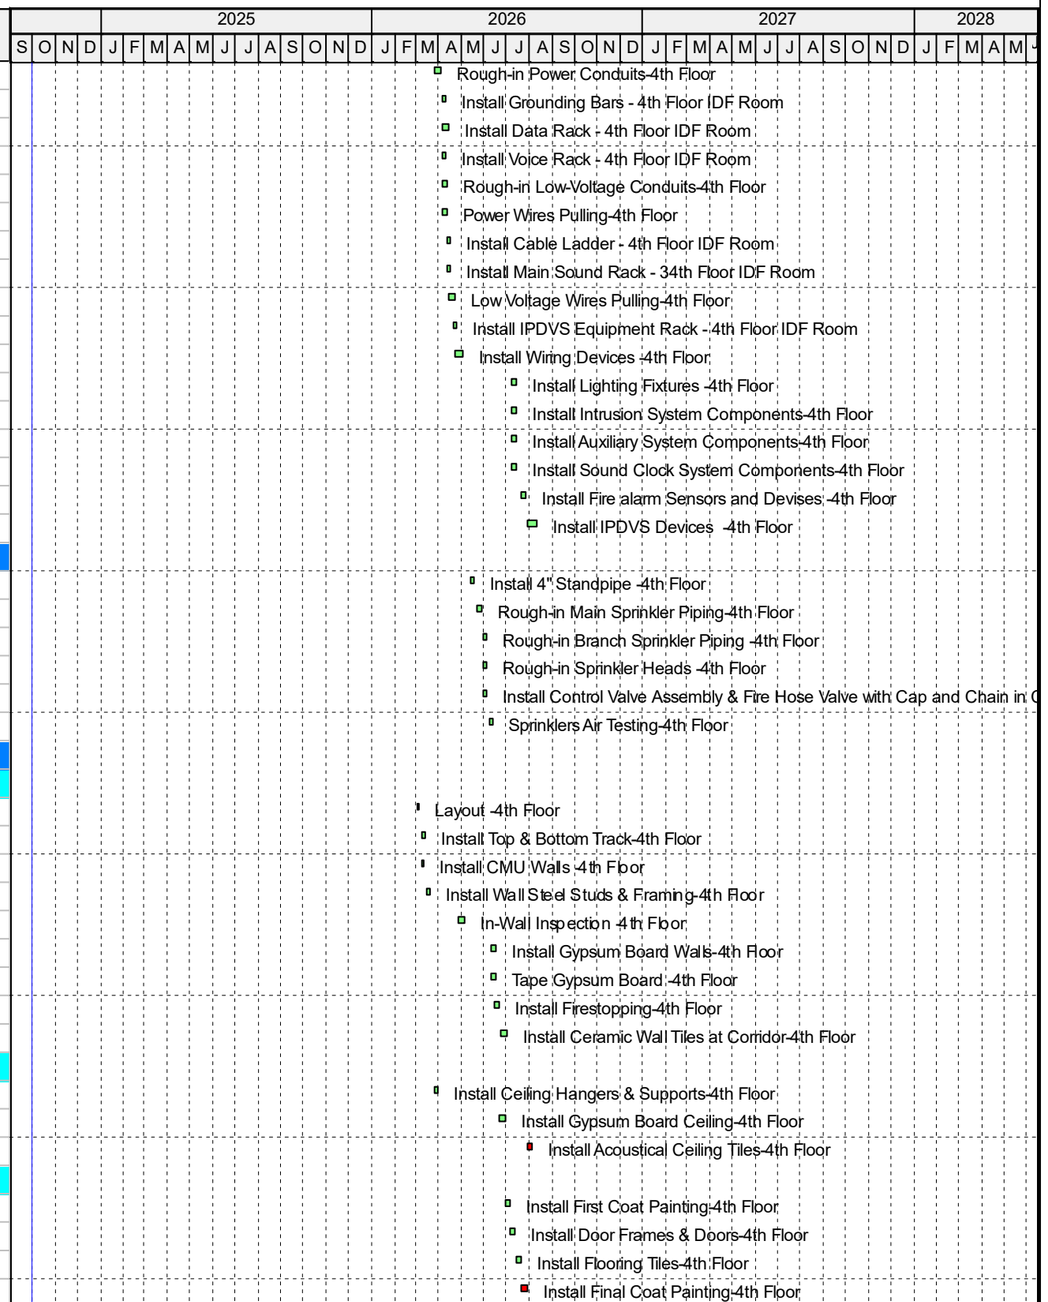

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-6070	Install Furniture & Milling Work (Contractor Provided & Installed) -4th Floor	5	30-Jul-26	05-Aug-26
CON-9050	Install Furniture & Milling Work (Owner Provided & Installed) -4th Floor	5	30-Jul-26	05-Aug-26
CON-6160	Install Signages-4th Floor	5	06-Aug-26	12-Aug-26
Fifth Floor		140	13-Feb-26	02-Sep-26
Structure -5th Floor		32	18-Feb-26	02-Apr-26
CON-1380	Install Metal Deck Slab - 5th Floor	3	18-Feb-26	20-Feb-26
CON-1440	Install Steel Columns - 5th Floor	3	23-Feb-26	25-Feb-26
CON-1460	F/R/P Piers - 5th Floor	5	23-Feb-26	27-Feb-26
CON-1540	Install Trusses - 5th Floor	2	26-Feb-26	27-Feb-26
CON-1550	Install Framing Beams - 5th Floor	3	26-Feb-26	02-Mar-26
CON-99317	Install Steel Stairs - 5th Floor	3	27-Feb-26	03-Mar-26
CON-1620	Install Dunnage - 5th Floor	8	02-Mar-26	11-Mar-26
CON-1730	Spray Fireproofing - 5th Floor	3	31-Mar-26	02-Apr-26
Mechanical -5th Floor		116	27-Feb-26	12-Aug-26
HVAC Rough-ins -5th Floor		81	27-Feb-26	23-Jun-26
CON-1610	Install MEP Hangers & Sleeves-Roof Floor	4	27-Feb-26	04-Mar-26
CON-1630	Install Duct Risers-5th Floor	2	02-Mar-26	03-Mar-26
CON-1790	Install Mechanical Piping Risers-5th Floor	2	04-Mar-26	05-Mar-26
CON-1810	Duct Leak Test -5th Floor	1	04-Mar-26	04-Mar-26
CON-2300	Rough-in Duct Work-5th Floor	5	16-Mar-26	20-Mar-26
CON-2470	Rough-in Refrigerant Piping-5th Floor	7	23-Mar-26	31-Mar-26
CON-2440	Rough-in Hot Water Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-2450	Rough-in Hot Glycol Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-2460	Rough-in Chilled Glycol Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-4330	Install VAV Boxes & Sound Attenuator Devices-5th Floor	5	09-Apr-26	15-Apr-26
CON-4710	Install Duct Insulation -5th Floor	8	11-Jun-26	23-Jun-26
Mechanical Equipment -5th Floor		67	07-May-26	12-Aug-26
CON-3640	Install Electric Unit Heaters -5th Floor	3	07-May-26	11-May-26
CON-5770	Install Air Cooled Condensing Unit ACCU - Mechanical Work - 5th Floor	5	08-Jul-26	14-Jul-26
CON-5430	Install Hot Glycol / Hot Water Cabinet Heater (CUH) -5th Floor	4	29-Jul-26	03-Aug-26
CON-5590	Install Exhaust Fan EF - Mechanical Work - 5th Floor	4	04-Aug-26	07-Aug-26
CON-5630	Install Convector Heater CV - Mechanical Work - 5th Floor	3	10-Aug-26	12-Aug-26
Plumbing -5th Floor		125	13-Feb-26	12-Aug-26
CON-3610	Install Floor Drains & Clean-outs -5th Floor	5	13-Feb-26	20-Feb-26
CON-1940	Install Plumbing Risers-5th Floor	1	06-Mar-26	06-Mar-26
CON-2000	Install SSDS Risers -SSDS System -5th Floor	1	09-Mar-26	09-Mar-26
CON-3050	Rough-in Gas Risers & Piping -5th Floor	4	22-Apr-26	27-Apr-26
CON-3190	Rough-in Domestic Water Piping -5th Floor	4	28-Apr-26	01-May-26
CON-3340	Rough-in Sanitary & Vent Piping -5th Floor	4	04-May-26	07-May-26
CON-3400	Install Hot Water Circulation Pump -5th Floor	5	04-May-26	08-May-26
CON-3410	Install Electric Hot Water Heater (EWH-1) -5th Floor	5	04-May-26	08-May-26
CON-3540	Rough-in Storm Piping -5th Floor	4	08-May-26	13-May-26
CON-3590	Plumbing Pressure Testing -5th Floor	5	14-May-26	20-May-26
CON-4530	Plumbing Piping Insulation -5th Floor	5	29-May-26	04-Jun-26

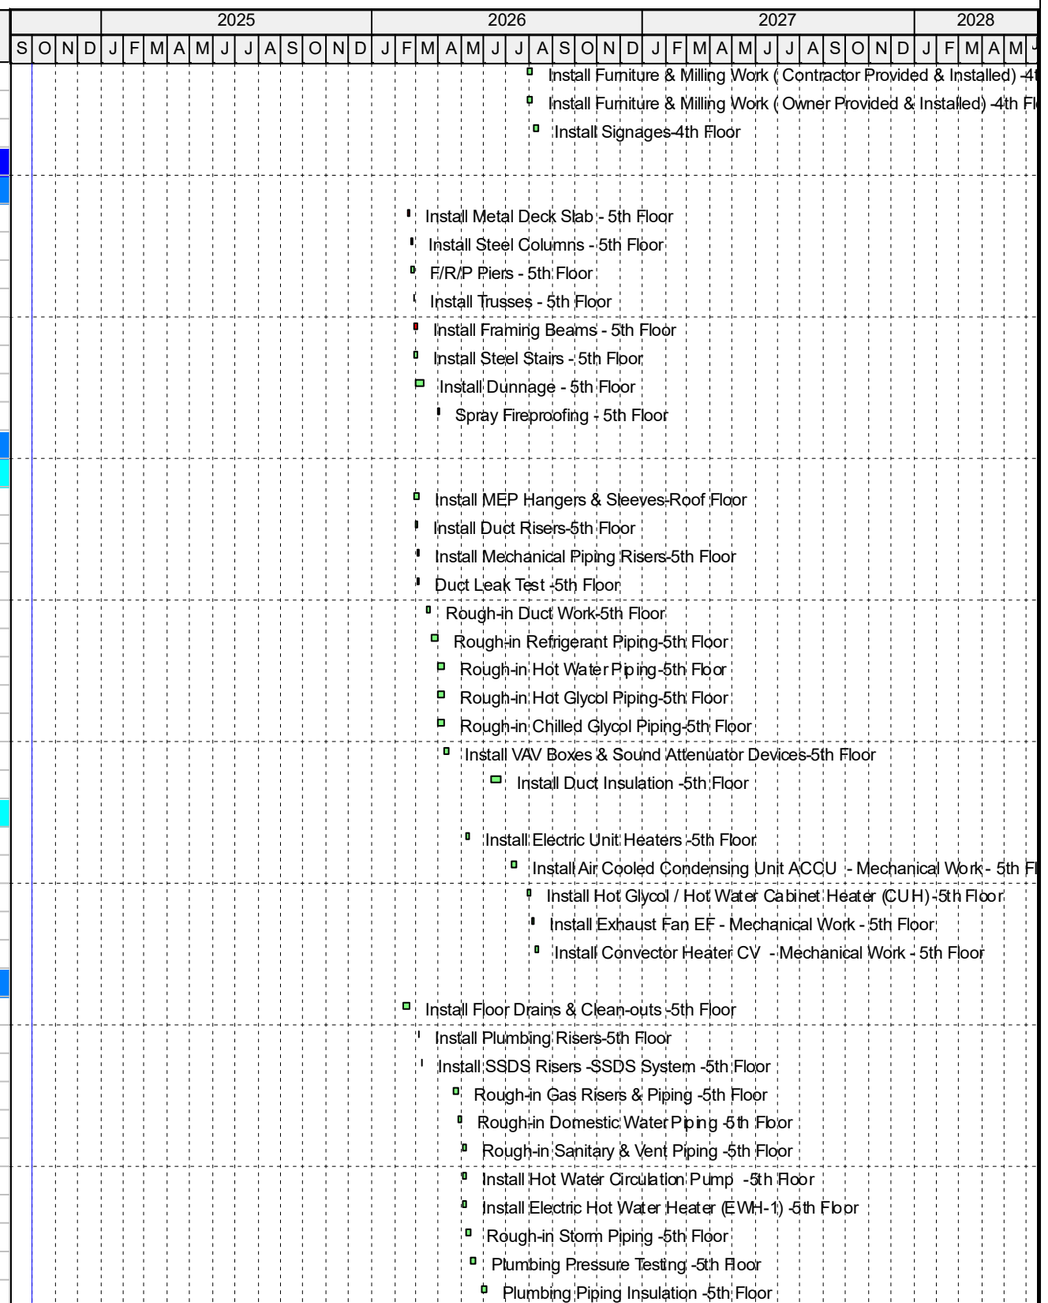

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-6090	Install Plumbing Fixtures -5th Floor	7	04-Aug-26	12-Aug-26
Electrical -5th Floor		117	10-Mar-26	24-Aug-26
CON-2050	Install Power Risers-5th Floor	3	10-Mar-26	12-Mar-26
CON-2100	Install Low Voltage Risers-5th Floor	3	13-Mar-26	17-Mar-26
CON-99337	Install Lightning Protection system -5th Floor	3	13-Mar-26	17-Mar-26
CON-2680	Rough-in Power Conduits -5th Floor	6	06-Apr-26	13-Apr-26
CON-2950	Rough-in Low-Voltage Conduits-5th Floor	6	14-Apr-26	21-Apr-26
CON-2960	Power Wires Pulling-5th Floor	6	14-Apr-26	21-Apr-26
CON-3290	Low Voltage Wires Pulling-5th Floor	6	23-Apr-26	30-Apr-26
CON-3660	Install Wiring Devices -5th Floor	8	05-May-26	14-May-26
CON-5740	Install Lighting Fixtures -5th Floor	6	16-Jul-26	23-Jul-26
CON-98827	Install Intrusion System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-98877	Install Auxiliary System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-98927	Install Sound Clock System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-5830	Install Fire alarm Sensors and Devises -5th Floor	5	29-Jul-26	04-Aug-26
CON-6010	Install IPDVS Devices -5th Floor	9	12-Aug-26	24-Aug-26
Fire Protection -5th Floor		22	20-May-26	22-Jun-26
CON-3770	Install 4" Standpipe -5th Floor	4	20-May-26	26-May-26
CON-4010	Rough-in Main Sprinkler Piping -5th Floor	5	01-Jun-26	05-Jun-26
CON-4230	Rough-in Branch Sprinkler Piping -5th Floor	5	08-Jun-26	12-Jun-26
CON-4240	Rough-in Sprinkler Heads -5th Floor	5	08-Jun-26	12-Jun-26
CON-4340	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -5th Floor	5	08-Jun-26	12-Jun-26
CON-4490	Sprinklers Air Testing-5th Floor	5	15-Jun-26	22-Jun-26
Architecture -5th Floor		126	06-Mar-26	02-Sep-26
Interior Walls -5th Floor		90	06-Mar-26	14-Jul-26
CON-1930	Layout -5th Floor	3	06-Mar-26	10-Mar-26
CON-2030	Install CMU Walls -5th Floor	3	13-Mar-26	17-Mar-26
CON-2020	Install Top & Bottom Track-5th Floor	4	16-Mar-26	19-Mar-26
CON-2200	Install Wall Steel Studs & Framing-5th Floor	5	23-Mar-26	27-Mar-26
CON-9100	In-Wall Inspections -5th Floor	7	04-May-26	12-May-26
CON-4810	Install Gypsum Board Walls-5th Floor	5	17-Jun-26	24-Jun-26
CON-4970	Tape Gypsum Board -5th Floor	4	18-Jun-26	24-Jun-26
CON-5220	Install Firestopping-5th Floor	4	23-Jun-26	26-Jun-26
CON-5080	Install Ceramic Wall Tiles at Corridor-5th Floor	7	06-Jul-26	14-Jul-26
Ceiling -5th Floor		93	01-Apr-26	12-Aug-26
CON-2620	Install Ceiling Hangers & Supports-5th Floor	4	01-Apr-26	06-Apr-26
CON-5100	Install Gypsum Board Ceiling-5th Floor	6	30-Jun-26	08-Jul-26
CON-5670	Install Acoustical Ceiling Tiles-5th Floor	5	06-Aug-26	12-Aug-26
Finishes -5th Floor		40	09-Jul-26	02-Sep-26
CON-5530	Install First Coat Painting -5th Floor	5	09-Jul-26	15-Jul-26
CON-5680	Install Door Frames & Doors -5th Floor	5	16-Jul-26	22-Jul-26
CON-5890	Install Flooring Tiles -5th Floor	5	23-Jul-26	29-Jul-26
CON-6060	Install Final Coat Painting -5th Floor	6	13-Aug-26	20-Aug-26
CON-6150	Install Furniture & Milling Work (Contractor Provided & Installed) -5th Floor	4	21-Aug-26	26-Aug-26

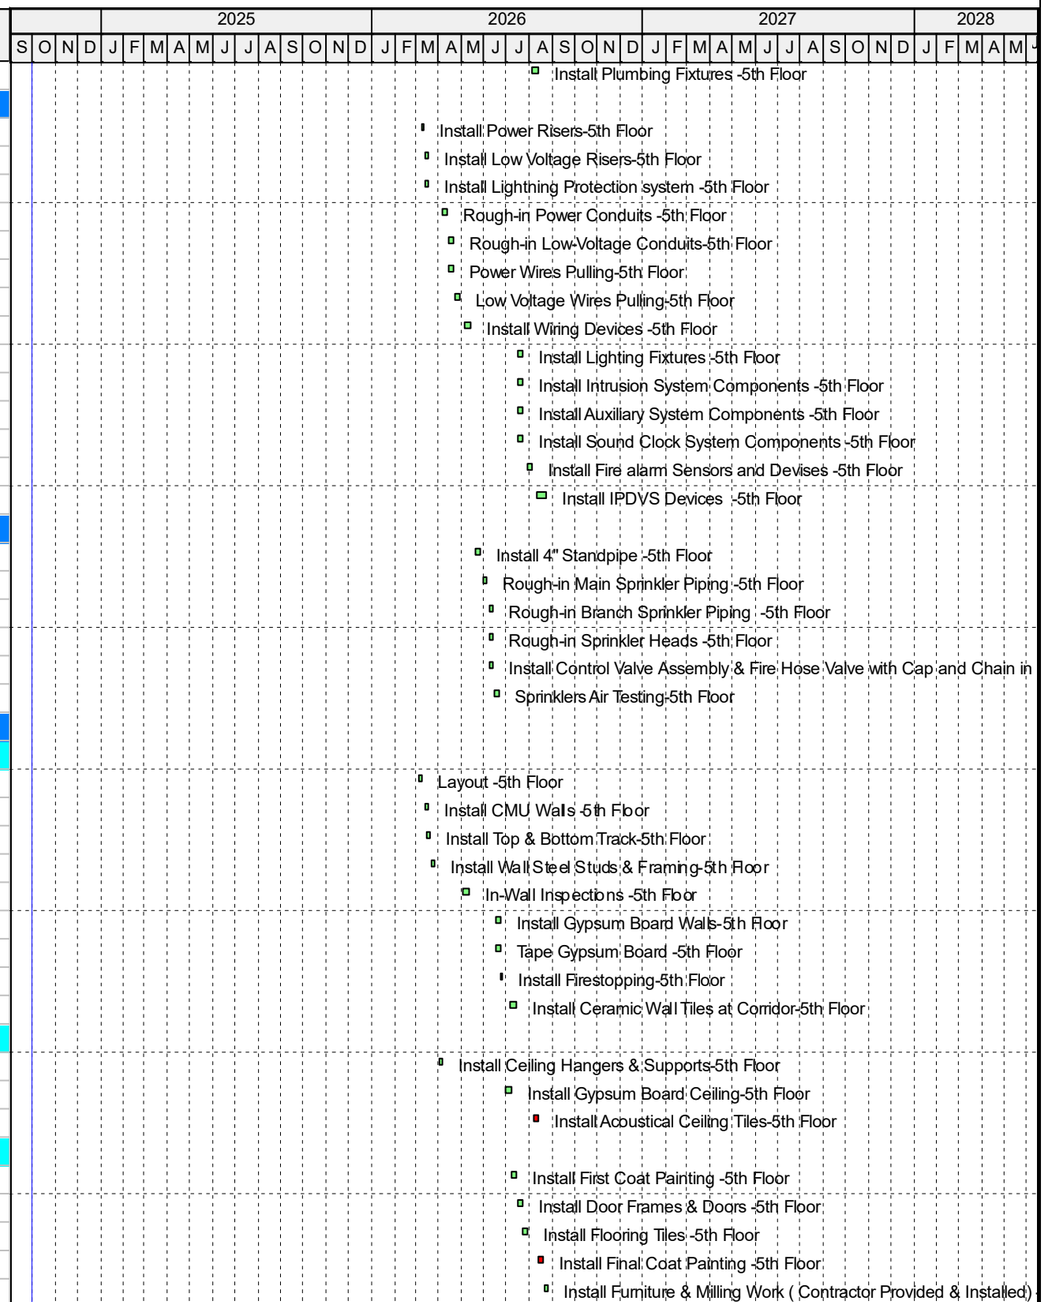

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-9060	Install Furniture & Milling Work (Owner Provided & Installed) -5th Floor	4	21-Aug-26	26-Aug-26
CON-6280	Install Signages- 5th Floor	5	27-Aug-26	02-Sep-26
Roof		106	26-Feb-26	28-Jul-26
Structure -Roof Floor		10	03-Mar-26	16-Mar-26
CON-1720	Install Metal Deck Slab -Roof Floor	2	03-Mar-26	04-Mar-26
CON-1760	Install Dunnage-Roof Floor	8	05-Mar-26	16-Mar-26
Mechanical-Roof Floor		97	26-Feb-26	15-Jul-26
CON-1770	Install Roof Drains & Clean outs -Roof Floor	5	26-Feb-26	04-Mar-26
CON-2250	Install Air Handling Unit AHU-1 -Roof Floor	5	08-Jun-26	12-Jun-26
CON-2560	Install Air Handling Unit AHU-3 -Roof Floor	5	23-Jun-26	29-Jun-26
CON-2720	Install Air Handling Unit AHU-4 -Roof Floor	5	30-Jun-26	07-Jul-26
CON-2860	Install Fume Hood Exhaust -Roof Floor	3	08-Jul-26	10-Jul-26
CON-3000	Install Smoke Purge Fan -Roof Floor	3	13-Jul-26	15-Jul-26
Electrical-Roof Floor		101	05-Mar-26	28-Jul-26
CON-99347	Install Lightning Protection System - Roof Floor	6	05-Mar-26	12-Mar-26
CON-3750	Install Emergency Generator- Roof Floor	4	17-Jul-26	22-Jul-26
CON-5380	Install Generator Connections -Roof Floor	4	23-Jul-26	28-Jul-26
Fire Protection -Roof Floor		23	27-May-26	29-Jun-26
CON-3890	Install 4" Standpipe -Roof	4	27-May-26	01-Jun-26
CON-4250	Rough-in Main Sprinkler Piping -Roof	5	08-Jun-26	12-Jun-26
CON-4430	Rough-in Branch Sprinkler Piping -Roof	5	15-Jun-26	22-Jun-26
CON-4440	Rough-in Sprinkler Heads -Roof	5	15-Jun-26	22-Jun-26
CON-4650	Install 3 Way Roof Manifold -Roof	5	23-Jun-26	29-Jun-26
Bulkhead		76	05-Mar-26	22-Jun-26
Structure-Bulkhead		6	05-Mar-26	12-Mar-26
CON-1750	F/R/P Concrete Columns -Bulkhead	3	05-Mar-26	09-Mar-26
CON-1980	F/R/P Bulkhead Slab -Bulkhead	2	10-Mar-26	11-Mar-26
CON-2060	Install Hoist Beam-Bulkhead	1	12-Mar-26	12-Mar-26
Mechanical - Bulkhead		76	05-Mar-26	22-Jun-26
CON-2070	Install Roof Drains & Clean outs - Mechanical Work - Roof Bulkhead	5	05-Mar-26	11-Mar-26
CON-2190	Install Electric Unit Heater EUH - Mechanical Work - Roof Bulkhead	5	12-Mar-26	18-Mar-26
CON-2120	Install Air Cooled Chiller CH-1 -Roof Floor	7	17-Mar-26	25-Mar-26
CON-2230	Install Emergency Generator -Bulkhead	7	19-Mar-26	27-Mar-26
CON-2350	Install Air Cooled Chiller CH-2 -Roof Floor	7	26-Mar-26	03-Apr-26
CON-2360	Install Smoke Purge Fan SPF - Mechanical Work - Roof Bulkhead	3	26-Mar-26	30-Mar-26
CON-2430	Install Air Handling Unit AHU-2 -Roof Floor	5	15-Jun-26	22-Jun-26
Elevations		44	05-Mar-26	05-May-26
West Elevation		27	05-Mar-26	10-Apr-26
CON-1830	Install Insulated Precast Concrete Sandwich Panel - Mock Up	2	05-Mar-26	06-Mar-26
CON-1990	Approve Insulated Precast Concrete Sandwich Panel - Mock Up	2	09-Mar-26	10-Mar-26
CON-2110	Install & Windows Mock-Up	3	11-Mar-26	13-Mar-26
CON-2210	Approve Windows Mock-Up	2	16-Mar-26	17-Mar-26
CON-2220	Install Storefront System Mock-Up	3	18-Mar-26	20-Mar-26
CON-2240	Approve Storefront System Mock-Up	2	23-Mar-26	24-Mar-26

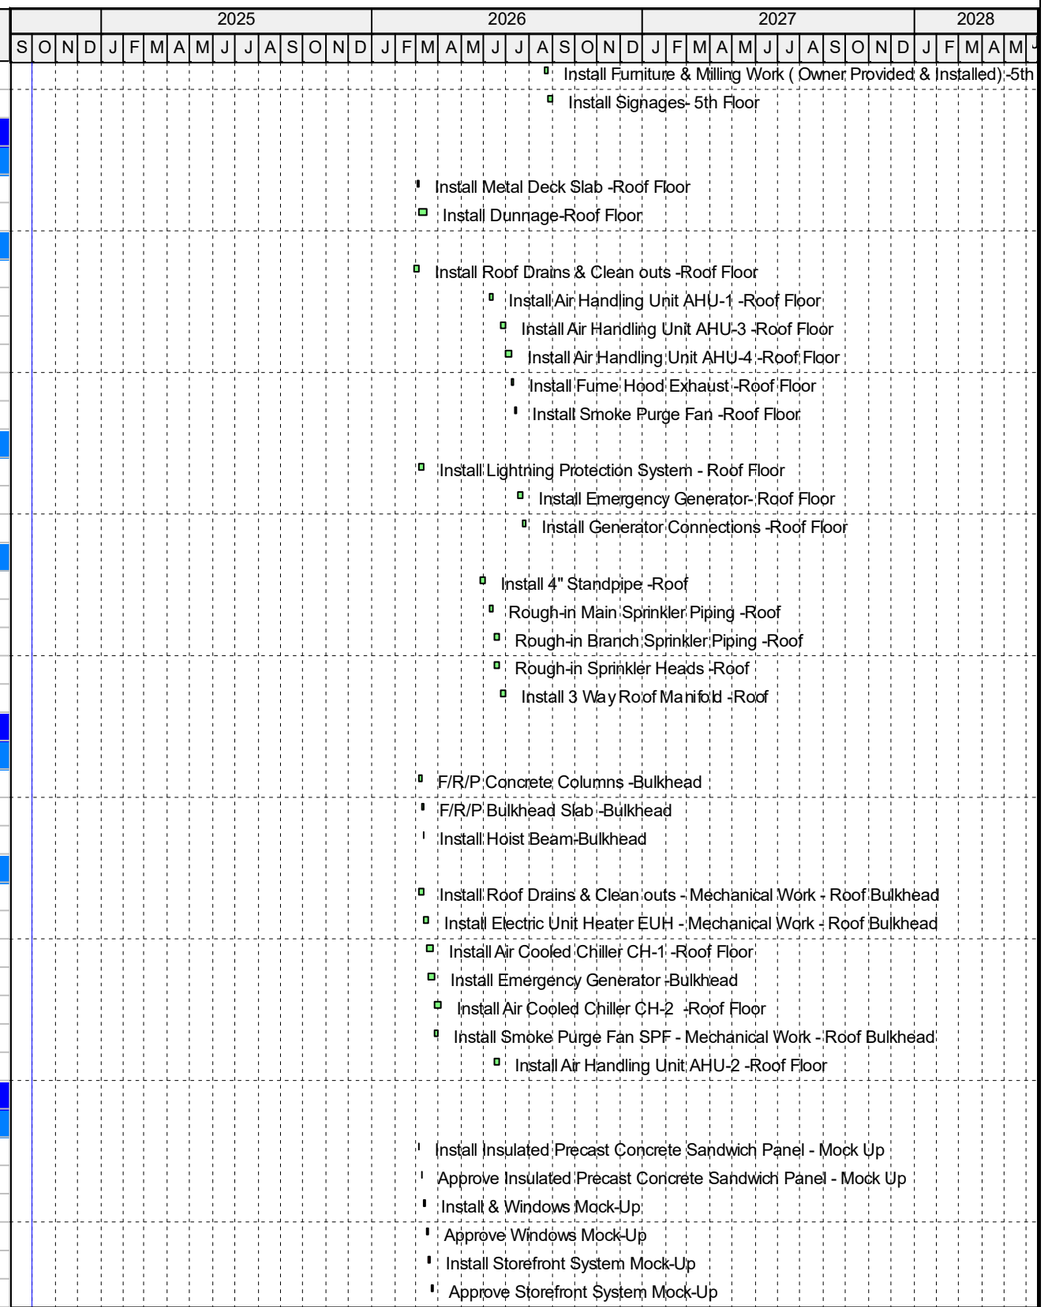

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2380	Install Insulated Precast Concrete Sandwich Panel - West Elevation	3	25-Mar-26	27-Mar-26
CON-2400	Install Windows -West Elevation	5	30-Mar-26	03-Apr-26
CON-2410	Install Storefront System-West Elevation	5	30-Mar-26	03-Apr-26
MIL-1740	Start Windows	0	30-Mar-26	
CON-2570	Field Testing of Windows (5%)	5	06-Apr-26	10-Apr-26
South Elevation		27	25-Mar-26	30-Apr-26
CON-2420	Install Insulated Precast Concrete Sandwich Panel - South Elevation	5	25-Mar-26	31-Mar-26
CON-2590	Install Windows - South Elevation	10	01-Apr-26	14-Apr-26
CON-2600	Install Storefront System- South Elevation	10	01-Apr-26	14-Apr-26
CON-2970	Field Testing of Windows (50%)	5	15-Apr-26	21-Apr-26
CON-99237	Install Flag Pole - South Elevation	10	15-Apr-26	28-Apr-26
CON-3220	Dismantle Sidewalk Sheds- South Elevation	2	29-Apr-26	30-Apr-26
East Elevation		25	01-Apr-26	05-May-26
CON-2610	Install Insulated Precast Concrete Sandwich Panel - East Elevation	4	01-Apr-26	06-Apr-26
CON-2980	Install Windows - East Elevation	8	15-Apr-26	24-Apr-26
CON-2990	Install Storefront System- East Elevation	8	15-Apr-26	24-Apr-26
CON-3370	Field Testing of Windows (90%)	5	27-Apr-26	01-May-26
CON-3630	Dismantle Sidewalk Sheds- East Elevation	2	04-May-26	05-May-26
North Elevation		25	01-Apr-26	05-May-26
CON-2730	Install Insulated Precast Concrete Sandwich Panel - North Elevation	4	01-Apr-26	06-Apr-26
CON-3380	Install Windows -North Elevation	10	15-Apr-26	28-Apr-26
CON-3390	Install Storefront System-North Elevation	10	15-Apr-26	28-Apr-26
MIL-1730	Sidewalk Sheds Dismantle Complete	0		05-May-26
Roofing		29	07-Apr-26	15-May-26
5th Floor		27	07-Apr-26	13-May-26
CON-2920	Pour Sloped Concrete Fill -5th Floor Roof	2	07-Apr-26	08-Apr-26
CON-3210	Install Fluid-Applied Protected Membrane Mock-Up	2	13-Apr-26	14-Apr-26
CON-3300	Approve Fluid-Applied Protected Membrane Mock-Up	4	15-Apr-26	20-Apr-26
CON-3440	Install Hot Fluid Applied Membrane -5th Floor Roof	4	21-Apr-26	24-Apr-26
CON-3580	Install 6" Thick Rigid Insulation -5th Floor Roof	3	27-Apr-26	29-Apr-26
CON-3700	Install Drainage -5th Floor Roof	3	30-Apr-26	04-May-26
CON-3710	Roof Flood Test -5th Floor Roof	4	30-Apr-26	05-May-26
CON-3820	Install Filter Fabric -5th Floor Roof	3	06-May-26	08-May-26
CON-3960	Install Concrete Pavers -5th Floor Roof	3	11-May-26	13-May-26
Main Roof		27	09-Apr-26	15-May-26
CON-3010	Pour Sloped Concrete Fill -Roof Floor	2	09-Apr-26	10-Apr-26
CON-3430	Install Hot Fluid Applied Membrane -Roof Floor	3	21-Apr-26	23-Apr-26
CON-3600	Install Drainage Panels- Roof Floor	3	24-Apr-26	28-Apr-26
CON-3730	Install 6" Thick Rigid Insulation -Roof Floor	3	29-Apr-26	01-May-26
CON-3840	Roof Flood Test -Roof Floor	3	04-May-26	06-May-26
CON-4020	Install Filter Fabric -Roof Floor	3	07-May-26	11-May-26
CON-4210	Install Concrete Pavers -Roof Floor	4	12-May-26	15-May-26
Special Rooms		94	23-Apr-26	04-Sep-26
Fuel Oil Room-1st Floor		10	01-Jun-26	12-Jun-26

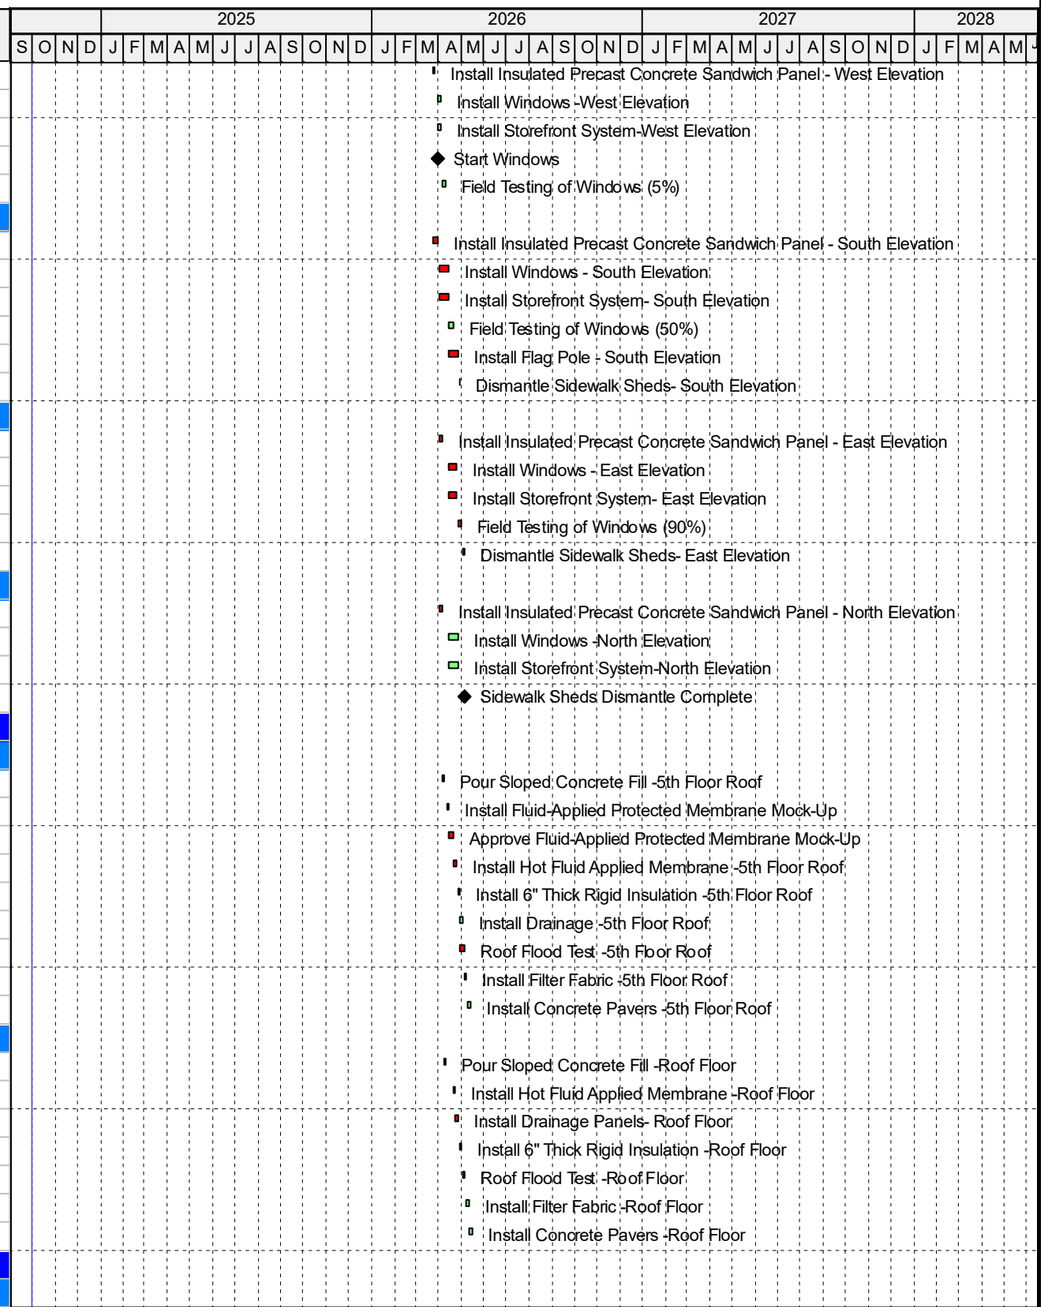

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-4890	F/R/P Concrete Pads -Fuel Oil Room	2	01-Jun-26	02-Jun-26
CON-4900	Rough-in Fuel Oil Piping -Fuel Oil Room	3	01-Jun-26	03-Jun-26
CON-4990	Install Fuel Oil Storage Tank (FOT-1) - Fuel Oil Room	3	03-Jun-26	05-Jun-26
CON-5020	Rough-in Fuel Oil Fill Piping -Fuel Oil Room	3	04-Jun-26	08-Jun-26
CON-5160	Install Fuel Oil Transfer Duplex Pump (FOP-1 & 2) -1st Floor	4	08-Jun-26	11-Jun-26
CON-5200	Rough-in Fuel Oil Vent Piping -Fuel Oil Room	4	09-Jun-26	12-Jun-26
Electrical Service Room -1st Floor		37	23-Apr-26	15-Jun-26
CON-4730	Rough-in Conduits & Wires - Electric Service Room	6	23-Apr-26	30-Apr-26
CON-4960	F/R/P Concrete Pad - Electric Service Room	6	01-May-26	08-May-26
CON-5180	Install Service Switchboard "SS-A"- Electric Service Room	5	11-May-26	15-May-26
CON-5510	Install Leak Detector - Electric Service Room	3	18-May-26	20-May-26
CON-5610	Install Sprinkler Booster Pump - Electric Service Room	4	21-May-26	27-May-26
CON-5640	Install Fire Alarm Normal ATS - Electric Service Room	4	28-May-26	02-Jun-26
CON-5780	Install Motorized Fire/Smoke Damper & Control Panel - Electric Service Room	5	03-Jun-26	09-Jun-26
CON-5790	Install Main Grounding Bus Bar - Electric Service Room	4	03-Jun-26	08-Jun-26
CON-9130	Install Switch Gear - Electric Service Room	5	08-Jun-26	12-Jun-26
CON-5840	Install Electric Unit Heater EUH-6 - Electric Service Room	4	10-Jun-26	15-Jun-26
MDF Room 127A -1st Floor		53	29-Apr-26	15-Jul-26
CON-3740	Install Ground Bus Bar - 1st Floor MDF Room	6	29-Apr-26	06-May-26
CON-4110	Install Voice Rack - 1st Floor MDF Room	6	07-May-26	14-May-26
CON-4510	Install Sound Rack - 1st Floor MDF Room	6	15-May-26	22-May-26
CON-4120	Install Project Connect Cabinet - 1st Floor MDF Room	8	15-May-26	27-May-26
CON-4520	Install Data Rack - 1st Floor MDF Room	6	26-May-26	02-Jun-26
CON-4550	Install UPS- 1st Floor MDF Room	9	03-Jun-26	15-Jun-26
CON-4130	Install BACnet Data Cabinet- 1st Floor MDF Room	9	03-Jun-26	15-Jun-26
CON-4780	Install IPDVS Equipment Rack - 1st Floor MDF Room	6	16-Jun-26	24-Jun-26
CON-4790	Install Ladder Rack Cable Tray- 1st Floor MDF Room	6	25-Jun-26	02-Jul-26
CON-4770	Install PBX - 1st Floor MDF Room	8	06-Jul-26	15-Jul-26
Gymatorium - 4th Floor		39	14-Jul-26	04-Sep-26
CON-5760	Install Wood Floating Floor System -Gymnatorium	10	14-Jul-26	27-Jul-26
CON-5810	Install Wall Pads - Gymnatorium	4	28-Jul-26	31-Jul-26
CON-5970	Install Retractable Basketball Goal Assembly -Gymnatorium	3	03-Aug-26	05-Aug-26
CON-6020	Install 8" Acoustic Block Painted-Gymnatorium	7	06-Aug-26	14-Aug-26
CON-99217	Install Bleachers -Gymnatorium	3	12-Aug-26	14-Aug-26
CON-6230	Install Gym Equipment -Gymnatorium -Gymnatorium	6	17-Aug-26	24-Aug-26
CON-6240	Install Fine Tube Radiator FTR - Gymnatorium	5	17-Aug-26	21-Aug-26
CON-6250	Install Hydraulic Vertical Wheelchair Lift -Gymnatorium	8	17-Aug-26	26-Aug-26
CON-9150	Install LED Theatrical Lighting -Gymnatorium	4	25-Aug-26	28-Aug-26
CON-6390	Install Auditorium Television Studio Dimming System -Gymnatorium	7	27-Aug-26	04-Sep-26
Boiler Room - 5th Floor		26	15-Jul-26	19-Aug-26
CON-5960	F/R/P Concert Pad -Boiler Room	3	15-Jul-26	17-Jul-26
CON-6000	Rough-in Conduits & Wires-Boiler Room	3	20-Jul-26	22-Jul-26
CON-6050	Install Boiler B-1-Boiler Room	5	23-Jul-26	29-Jul-26
CON-6110	Install Boiler B-2-Boiler Room	5	30-Jul-26	05-Aug-26

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-6120	Install Air Separator Units (AS-1 , AS-2 & AS-3)	2	30-Jul-26	31-Jul-26
CON-6130	Install Boiler Condensate ACID Neutralization Tubes -Boiler Room	2	30-Jul-26	31-Jul-26
CON-6200	Install Expansion Tanks (ET-1 , ET-2 & ET-3)	2	03-Aug-26	04-Aug-26
CON-6210	Install Glycol Make-up Units (GF-1 & GF-2 & GF-3)	2	03-Aug-26	04-Aug-26
CON-6220	Install Reduced Pressure Zone (RPZ) Devices -Boiler Room	2	03-Aug-26	04-Aug-26
CON-6260	Install Heat Exchanger -Boiler Room	2	06-Aug-26	07-Aug-26
CON-6290	Install Hot Glycol Units Heaters (UH-5-1, UH-5-2)	2	10-Aug-26	11-Aug-26
CON-6330	Install Heat Pump Electric Hot Water Heater (HPWH#1&2)-Boiler Room	2	12-Aug-26	13-Aug-26
CON-6340	Install Exhaust Fans -Boiler Room	2	14-Aug-26	17-Aug-26
CON-6350	Install Primary Hot Water Pump (GHWP 1 to 3) -Boiler Room	2	14-Aug-26	17-Aug-26
CON-6360	Install Primary Chilled Water Pump (GCHWP-1&2)-Boiler Room	2	14-Aug-26	17-Aug-26
CON-6400	Install Secondary Hot Water Pump(HWP-1&2)-Boiler Room	2	18-Aug-26	19-Aug-26
CON-6410	Install Electric Unit Heater (EUH-3) - Boiler Room	2	18-Aug-26	19-Aug-26
CON-6420	Install Branch Panels (BRPP) -Boiler Room	2	18-Aug-26	19-Aug-26
Elevator Machine Room & Shaft -Roof Floor		61	07-May-26	04-Aug-26
MIL-1760	Start Elevator Work	0	07-May-26	
CON-99357	Install CMU Wall for Shaft -Elevator Machine Room	10	07-May-26	20-May-26
CON-99167	Install Elevator Guide Rails -Elevator Machine Room	8	21-May-26	02-Jun-26
CON-2090	Install Elevator Controller #1 -Elevator Machine Room	10	03-Jun-26	16-Jun-26
CON-2370	Install Elevator Controller #2 -Elevator Machine Room	10	17-Jun-26	01-Jul-26
CON-2580	Install Power Panels -Elevator Machine Room	7	02-Jul-26	13-Jul-26
CON-2790	Rough-in Conduits & Wires-Elevator Machine Room	6	14-Jul-26	21-Jul-26
CON-99157	Install Elevator Sump Pump -Elevator Machine Room	10	14-Jul-26	27-Jul-26
CON-3100	Install Elevator Cabinet (1) -Elevator Machine Room	10	22-Jul-26	04-Aug-26
CON-3620	Install Elevator Cabinet (2) -Elevator Machine Room	10	22-Jul-26	04-Aug-26
Mockup Room		18	07-May-26	02-Jun-26
CON-4040	Install Walls GWB-Mockup Room	3	07-May-26	11-May-26
CON-4270	Install Gypsum Board Ceiling -Mockup Room	3	07-May-26	11-May-26
CON-4380	Install Doors & Hardware-Mockup Room	3	11-May-26	13-May-26
CON-4260	Install Door Frames-Mockup Room	2	12-May-26	13-May-26
CON-4480	Paint First coat -Mockup Room	2	14-May-26	15-May-26
CON-4640	Flooring Finishes-Mockup Room	2	18-May-26	19-May-26
CON-4750	Paint Second coat-Mockup Room	2	20-May-26	21-May-26
CON-4930	Install Furniture & Signs -Mockup Room	2	22-May-26	26-May-26
CON-5000	Mockup Room Inspection & Punchlist	5	27-May-26	02-Jun-26
Site Work		91	01-May-26	10-Sep-26
54th Avenue Street		34	01-May-26	18-Jun-26
CON-3780	Install Traffic Control Devices - 54th Avenue Street	3	01-May-26	05-May-26
CON-3850	Remove Existing Steel Faced Curb - 54th Avenue Street	3	06-May-26	08-May-26
CON-3860	Remove Existing Asphalt - 54th Avenue Street	4	06-May-26	11-May-26
CON-3940	Remove Existing Electrical Manhole - 54th Avenue Street	4	12-May-26	15-May-26
CON-4080	Install 5' Wide Silva Cells Under Concrete Pavement Strip - 54th Avenue Street	4	18-May-26	21-May-26
CON-4150	Pavement Replacement - 54th Avenue Street	4	22-May-26	28-May-26
CON-4290	Install New Steel Faced Curb - 54th Avenue Street	4	29-May-26	03-Jun-26

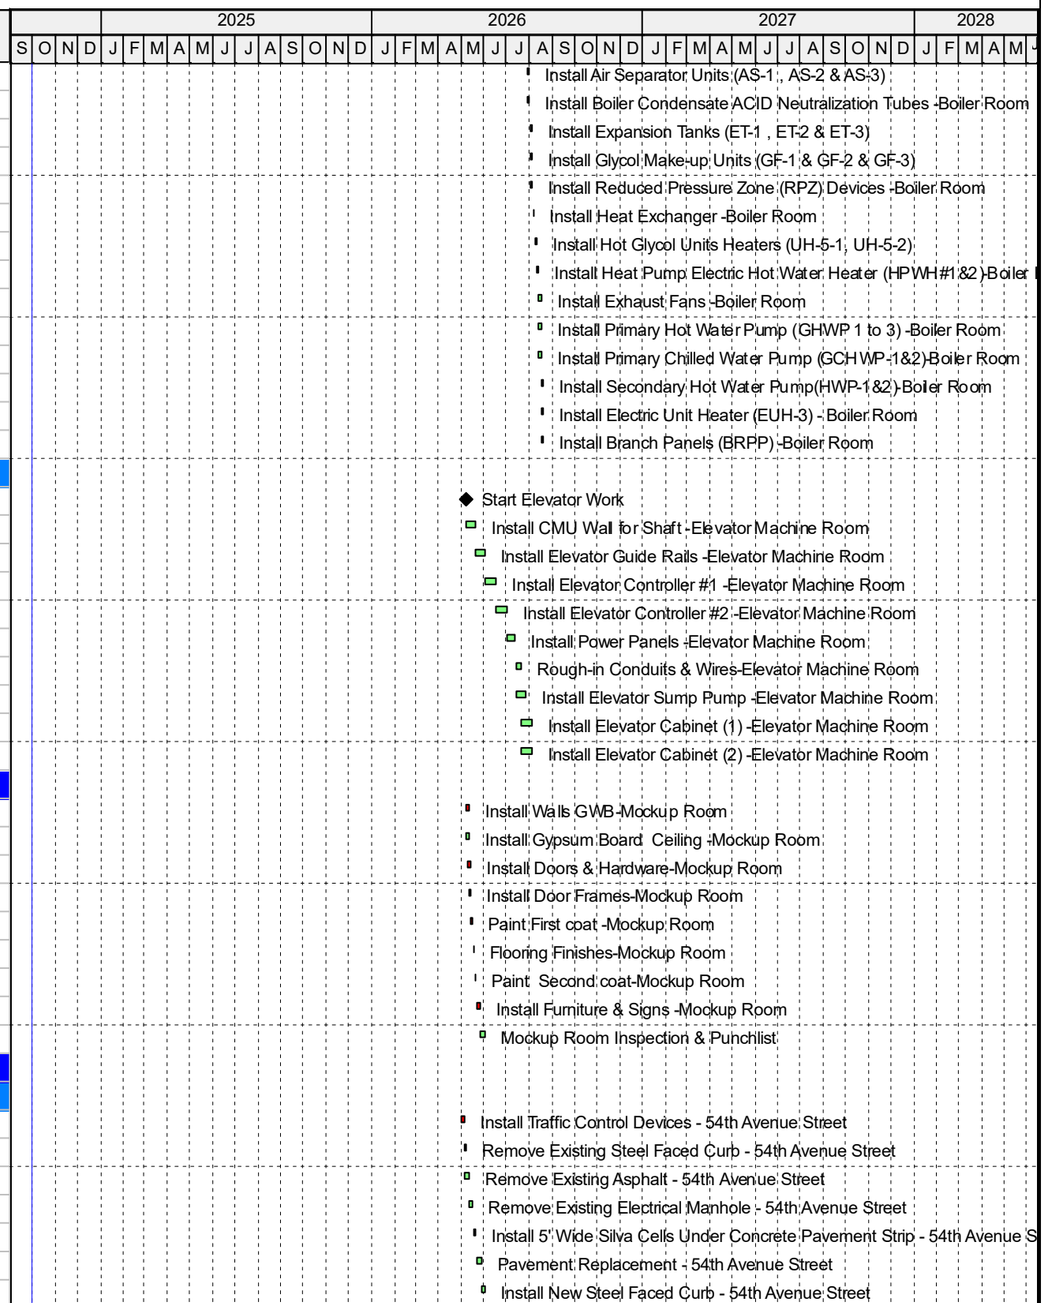

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-4300	Install Pedestrian Ramps With Truncated Domes - 54th Avenue Street	4	29-May-26	03-Jun-26
CON-4400	Install 4" Concrete Sidewalk - 54th Avenue Street	5	04-Jun-26	10-Jun-26
CON-4410	Install 7" Concrete Sidewalk - 54th Avenue Street	5	04-Jun-26	10-Jun-26
CON-4560	Install Pavement Marking - 54th Avenue Street	3	11-Jun-26	15-Jun-26
CON-4580	Remove Traffic Control Devices - 54th Avenue Street	3	16-Jun-26	18-Jun-26
2ND Street		39	06-May-26	01-Jul-26
CON-3870	Install Traffic Control Devices - 2nd Street	5	06-May-26	12-May-26
CON-3900	Remove Existing Sidewalk - 2nd Street	5	13-May-26	19-May-26
CON-3950	Install Pedestrian Ramps With Truncated Domes - 2nd Street	6	20-May-26	28-May-26
CON-4090	Remove Existing Steel Faced Curb - 2nd Street	6	29-May-26	05-Jun-26
CON-4160	Install New Steel Faced Curb - 2nd Street	6	08-Jun-26	15-Jun-26
CON-4170	Install 4" Concrete Sidewalk - 2nd Street	7	08-Jun-26	16-Jun-26
CON-4310	Install 7" Concrete Sidewalk - 2nd Street	6	16-Jun-26	24-Jun-26
CON-4420	Remove Traffic Control Devices - 2nd Street	5	25-Jun-26	01-Jul-26
Building Perimeter		49	02-Jul-26	10-Sep-26
Drainage Work		17	02-Jul-26	27-Jul-26
CON-4660	Excavation - Drainage Work - Building Perimeter	3	02-Jul-26	07-Jul-26
CON-4740	Install Flood Barrier Wall - Drainage Work - Building Perimeter	3	08-Jul-26	10-Jul-26
CON-4860	Install Drilled Caisson Supported Ventilation Structure - Drainage Work - Building Perimeter	3	13-Jul-26	15-Jul-26
CON-4980	Install 4" & 6" & 10" & 12" DIP - Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-9170	Install 8" Combined Water Service (2nd Street)- Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-9180	Install 6" Fire Water Service (54th Avenue Street)- Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-5190	Install Catch Basin - Drainage Work - Building Perimeter	2	21-Jul-26	22-Jul-26
CON-5290	Install Storm Inlet With Hood & Storm Hood - Drainage Work - Building Perimeter	2	23-Jul-26	24-Jul-26
CON-5400	Install Trench Drain - Drainage Work - Building Perimeter	1	27-Jul-26	27-Jul-26
Playground Area & Fences		32	28-Jul-26	10-Sep-26
CON-9160	Excavate for Footings - Playground Area & Fences - Building Perimeter	2	28-Jul-26	29-Jul-26
CON-9010	Remove Steel Plate Protection over NYPA Easement - Playground Area & Fences - Building Perimeter	1	28-Jul-26	28-Jul-26
CON-9190	F/R/P Playground Equipment Footings - Playground Area & Fences - Building Perimeter	2	30-Jul-26	31-Jul-26
CON-5470	Install Flush Concrete Curb - Playground Area & Fences - Building Perimeter	3	03-Aug-26	05-Aug-26
CON-5420	Install Asphalt Pavement - Playground Area & Fences - Building Perimeter	2	04-Aug-26	05-Aug-26
CON-5600	Install Concrete Pavement Pedestrian Ramp With Painted Black Handrails - Playground Area & Fences - Building Perimeter	3	06-Aug-26	10-Aug-26
CON-5650	Install Playground Rubber Tile Safety Surface - Playground Area & Fences - Building Perimeter	3	11-Aug-26	13-Aug-26
CON-5800	Install Painted Asphalt Pavement & Painted Games On Asphalt Surface - Playground Area & Fences - Building Perimeter	3	14-Aug-26	18-Aug-26
CON-5850	Install Colored Athletic Wearing Surface Color - Playground Area & Fences - Building Perimeter	2	19-Aug-26	20-Aug-26
CON-5990	Install Playground Equipment - Playground Area & Fences - Building Perimeter	7	21-Aug-26	31-Aug-26
CON-6140	Install Basketball Hoop - Playground Area & Fences - Building Perimeter	1	01-Sep-26	01-Sep-26
CON-6190	Install Wrought Iron Fence Double Gate - Playground Area - Building Perimeter	3	02-Sep-26	04-Sep-26
CON-6270	Install Chain Link Fence - Playground Area & Fences - Building Perimeter	3	08-Sep-26	10-Sep-26
Close-out		430	28-Oct-25	15-Aug-27
Special Inspection		192	28-Oct-25	04-Aug-26
I-1010	Concrete Cast-IN-Place Inspection	86	28-Oct-25	04-Mar-26
I-1140	Structural Steel Inspection	58	05-Dec-25	02-Mar-26
I-1080	Standpipe System Inspection	111	29-Dec-25	05-Jun-26

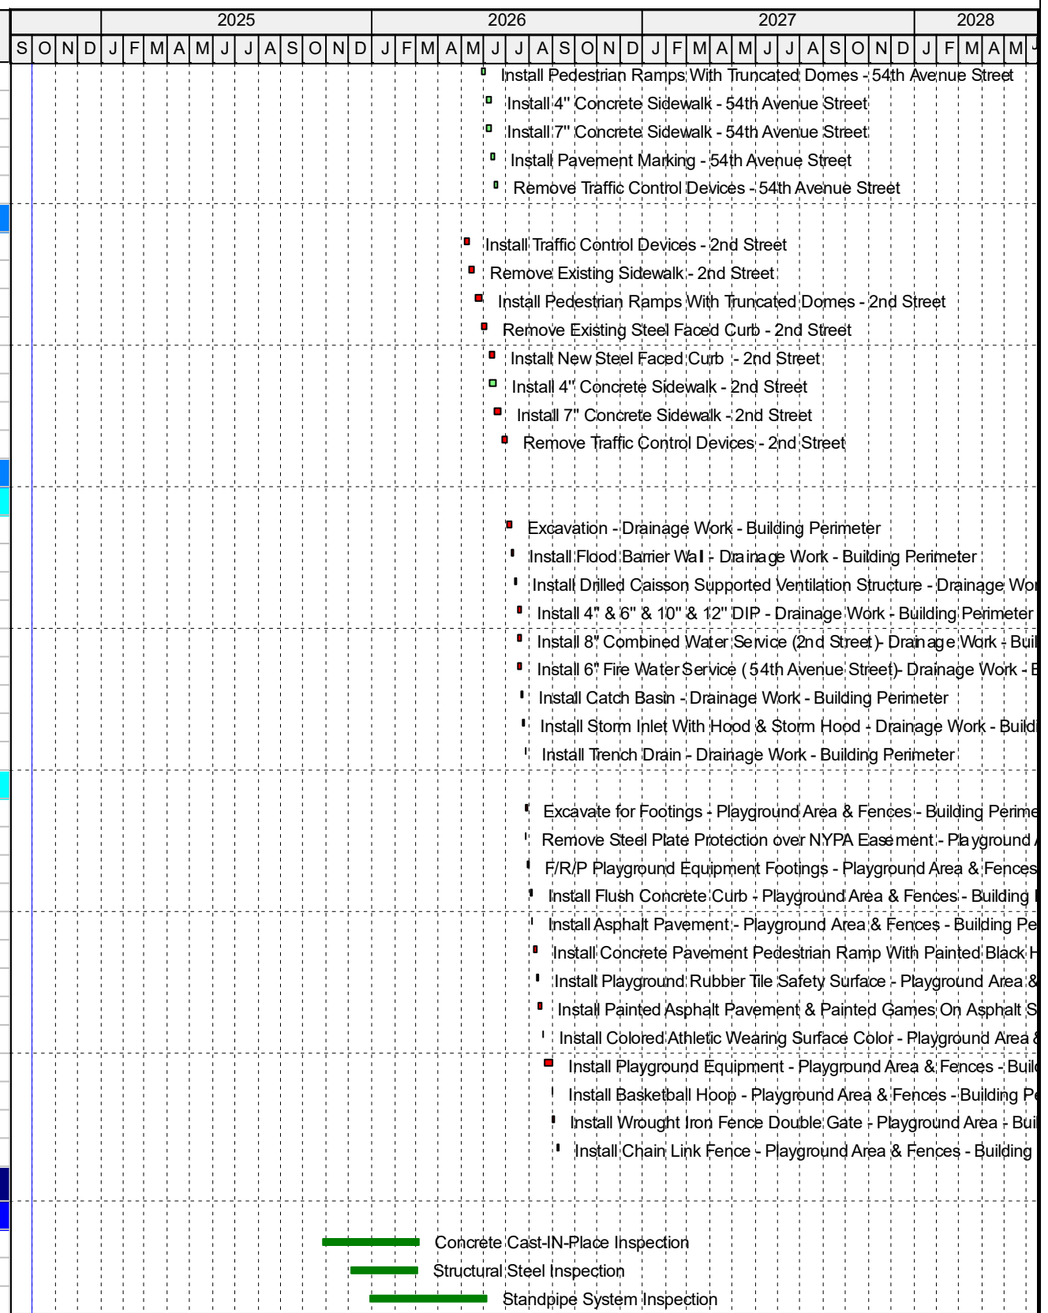

Full Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
I-1020	Masonry Inspection	32	02-Mar-26	14-Apr-26
I-1100	Fire-Resistant Penetrations And Joints Inspection	87	03-Mar-26	06-Jul-26
I-1150	Concrete Precast Inspection	9	25-Mar-26	06-Apr-26
I-1120	Mechanical System Inspection	69	07-Apr-26	15-Jul-26
I-1040	Roofing Flood Testing Inspection	5	30-Apr-26	06-May-26
I-1130	Fire Alarm Inspection	47	28-May-26	04-Aug-26
I-1110	Fuel-Oil Storage & Fuel Oil Piping Systems Inspection	9	01-Jun-26	11-Jun-26
Testing & Commissioning		62	06-Jul-26	30-Sep-26
CLO-1120	MDF & IDF Rooms Testing & Commissioning	12	06-Jul-26	21-Jul-26
CLO-1010	HVAC Flush-Out	20	07-Jul-26	03-Aug-26
CLO-1140	SSDS System Testing & Commissioning	7	16-Jul-26	24-Jul-26
CLO-1240	Elevator Sump Pump Testing & Commissioning	21	28-Jul-26	25-Aug-26
CLO-1270	Water Heater Testing & Commissioning	21	28-Jul-26	25-Aug-26
CLO-1220	Emergency Generator Electric Load Test	3	29-Jul-26	31-Jul-26
PER-2640	Obtain Emergency Generator Permit	5	03-Aug-26	07-Aug-26
CLO-1250	Emergency Generator Testing & Commissioning	21	03-Aug-26	31-Aug-26
CLO-1230	Air Handling Unit Testing & Commissioning	21	04-Aug-26	01-Sep-26
CLO-1190	Pre-Elevator Test Inspection	5	05-Aug-26	11-Aug-26
CLO-1290	Glycol System Testing & Commissioning	21	05-Aug-26	02-Sep-26
MIL-1680	Emergency Generator Final Sign-off	0		07-Aug-26
CLO-1020	Electrical System Testing & Commissioning	21	10-Aug-26	08-Sep-26
CLO-1260	HVAC Split System Testing & Commissioning	21	10-Aug-26	08-Sep-26
CLO-1280	Fire Alarm Testing & Commissioning	21	10-Aug-26	08-Sep-26
CLO-1000	Elevator Testing & Commissioning	20	12-Aug-26	09-Sep-26
CLO-1160	Sprinkler/Domestic Booster Pumps Testing & Commissioning	14	20-Aug-26	09-Sep-26
CLO-1130	IPDVS System Testing & Commissioning	11	03-Sep-26	18-Sep-26
CLO-1170	Sprinkler/Domestic Booster Pumps Inspection	3	10-Sep-26	14-Sep-26
CLO-1200	Elevator DOB Inspection	5	10-Sep-26	16-Sep-26
CLO-1180	Sprinkler/Domestic Booster Pumps Sign-offs	0		14-Sep-26
CLO-1150	FDNY Inspection	12	15-Sep-26	30-Sep-26
PER-2650	Elevator Equipment Use Permit	10	17-Sep-26	30-Sep-26
MIL-1650	FDNY Inspection Finish	0		30-Sep-26
MIL-1670	Elevator Final Sign-off	0		30-Sep-26
Demobilization		214	09-Sep-26	15-Aug-27
CLO-1300	Provide Training	10	09-Sep-26	22-Sep-26
CLO-1030	Pre-Final Clean-Out	5	11-Sep-26	17-Sep-26
CLO-1040	Pre-TCO Inspection	11	18-Sep-26	02-Oct-26
CLO-1110	Pre-TCO Punchlist	10	05-Oct-26	19-Oct-26
CLO-1050	Pre-Substantial Punchlist	105	20-Oct-26	17-Apr-27
CLO-1060	Prepare & Submit O&M Manuals	30	19-Apr-27	01-Jun-27
CLO-1070	Prepare & Submit As-Built Drawings	30	02-Jun-27	15-Jul-27
CLO-1080	Final Inspection	5	16-Jul-27	22-Jul-27
CLO-1090	Final Clean Out	10	23-Jul-27	05-Aug-27
CLO-1100	Demobilization	10	06-Aug-27	15-Aug-27

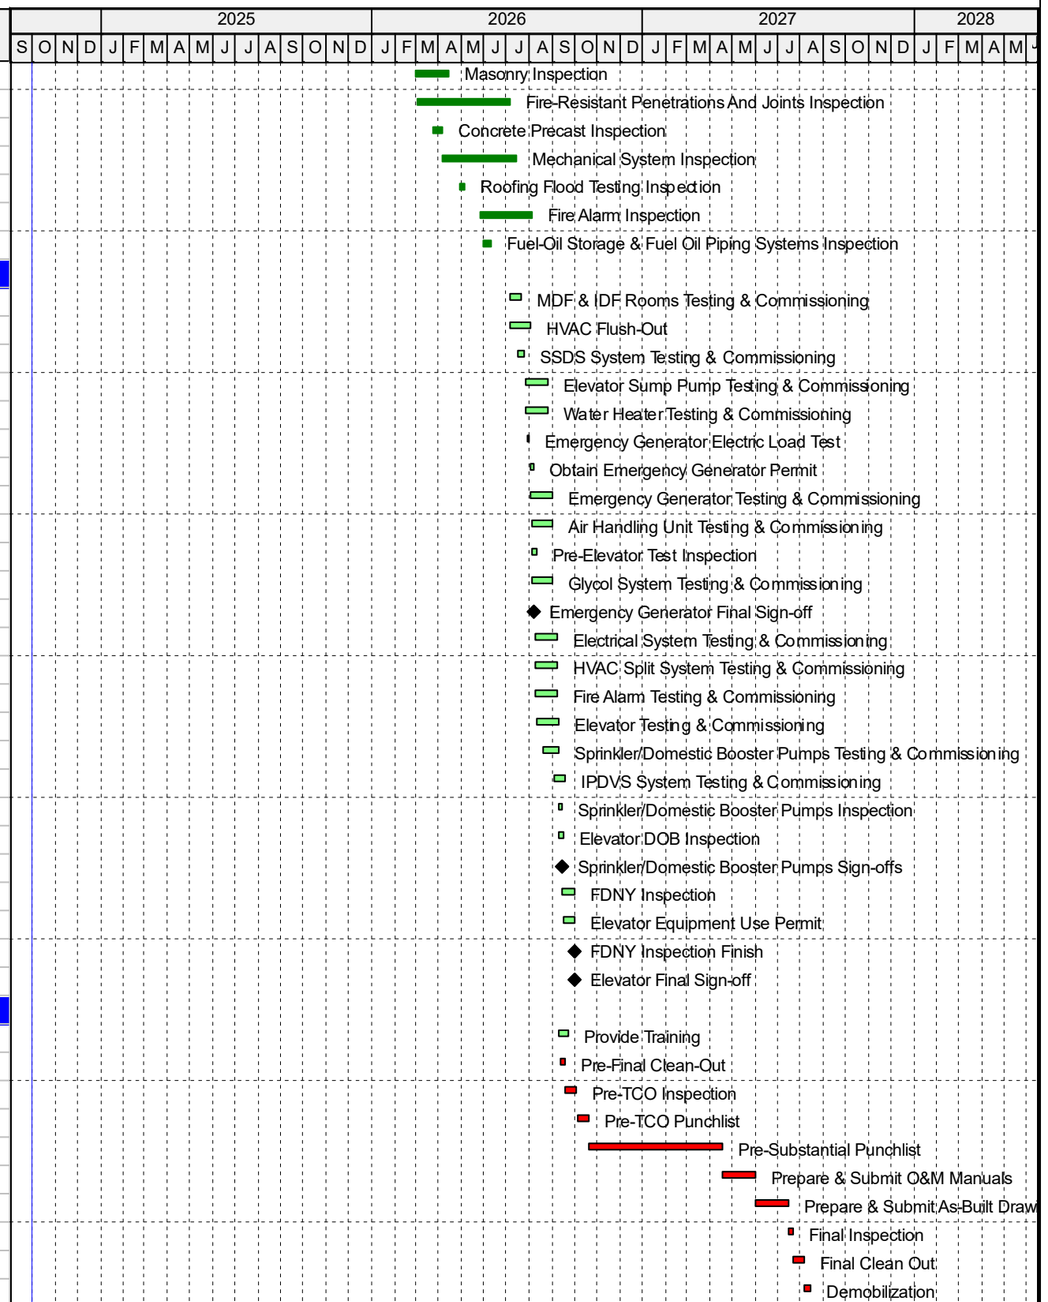

APPENDIX 3
Full Schedule Layout Grouped by LOCN Code

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
Site Work		513	30-Sep-24	19-Oct-26
CON-99257	Subcontractor Buyout	10	30-Sep-24	11-Oct-24
MIL-1660	Start Security Guard Services (30 Days From NTP)	0	30-Oct-24	
CON-1000	Mobilization	4	30-Sep-25	03-Oct-25
CON-7740	Protection Of All Overhead & Underground Utilities	263	30-Sep-25	19-Oct-26
CON-9000	Protection & Restoration the adjacent Properties to Original Condition	263	30-Sep-25	19-Oct-26
CON-1080	Install Erosion Control Devices	2	06-Oct-25	07-Oct-25
CON-1010	Install Construction Signs	2	06-Oct-25	07-Oct-25
CON-1030	Install Construction Fences	2	06-Oct-25	07-Oct-25
CON-9120	Soli Sampling	2	06-Oct-25	07-Oct-25
CON-7750	Install Field Offices	5	08-Oct-25	15-Oct-25
CON-9140	Excavation	5	08-Oct-25	15-Oct-25
CON-3780	Install Traffic Control Devices - 54th Avenue Street	3	01-May-26	05-May-26
CON-3850	Remove Existing Steel Faced Curb - 54th Avenue Street	3	06-May-26	08-May-26
CON-3860	Remove Existing Asphalt - 54th Avenue Street	4	06-May-26	11-May-26
CON-3870	Install Traffic Control Devices - 2nd Street	5	06-May-26	12-May-26
CON-4040	Install Walls GWB-Mockup Room	3	07-May-26	11-May-26
CON-4270	Install Gypsum Board Ceiling -Mockup Room	3	07-May-26	11-May-26
CON-4380	Install Doors & Hardware-Mockup Room	3	11-May-26	13-May-26
CON-4260	Install Door Frames-Mockup Room	2	12-May-26	13-May-26
CON-3940	Remove Existing Electrical Manhole - 54th Avenue Street	4	12-May-26	15-May-26
CON-3900	Remove Existing Sidewalk - 2nd Street	5	13-May-26	19-May-26
CON-4480	Paint First coat -Mockup Room	2	14-May-26	15-May-26
CON-4640	Flooring Finishes-Mockup Room	2	18-May-26	19-May-26
CON-4080	Install 5' Wide Silva Cells Under Concrete Pavement Strip - 54th Avenue Street	4	18-May-26	21-May-26
CON-4750	Paint Second coat-Mockup Room	2	20-May-26	21-May-26
CON-3950	Install Pedestrian Ramps With Truncated Domes - 2nd Street	6	20-May-26	28-May-26
CON-4930	Install Furniture & Signs -Mockup Room	2	22-May-26	26-May-26
CON-4150	Pavement Replacement - 54th Avenue Street	4	22-May-26	28-May-26
CON-5000	Mockup Room Inspection & Punchlist	5	27-May-26	02-Jun-26
CON-4290	Install New Steel Faced Curb - 54th Avenue Street	4	29-May-26	03-Jun-26
CON-4300	Install Pedestrian Ramps With Truncated Domes - 54th Avenue Street	4	29-May-26	03-Jun-26
CON-4090	Remove Existing Steel Faced Curb - 2nd Street	6	29-May-26	05-Jun-26
CON-4400	Install 4" Concrete Sidewalk - 54th Avenue Street	5	04-Jun-26	10-Jun-26
CON-4410	Install 7" Concrete Sidewalk - 54th Avenue Street	5	04-Jun-26	10-Jun-26
CON-4160	Install New Steel Faced Curb - 2nd Street	6	08-Jun-26	15-Jun-26
CON-4170	Install 4" Concrete Sidewalk - 2nd Street	7	08-Jun-26	16-Jun-26
CON-4560	Install Pavement Marking - 54th Avenue Street	3	11-Jun-26	15-Jun-26
CON-4580	Remove Traffic Control Devices - 54th Avenue Street	3	16-Jun-26	18-Jun-26
CON-4310	Install 7" Concrete Sidewalk - 2nd Street	6	16-Jun-26	24-Jun-26
CON-4420	Remove Traffic Control Devices - 2nd Street	5	25-Jun-26	01-Jul-26
CON-4660	Excavation - Drainage Work - Building Perimeter	3	02-Jul-26	07-Jul-26
CON-4740	Install Flood Barrier Wall - Drainage Work - Building Perimeter	3	08-Jul-26	10-Jul-26
CON-4860	Install Drilled Caisson Supported Ventilation Structure - Drainage Work - Building Perimeter	3	13-Jul-26	15-Jul-26

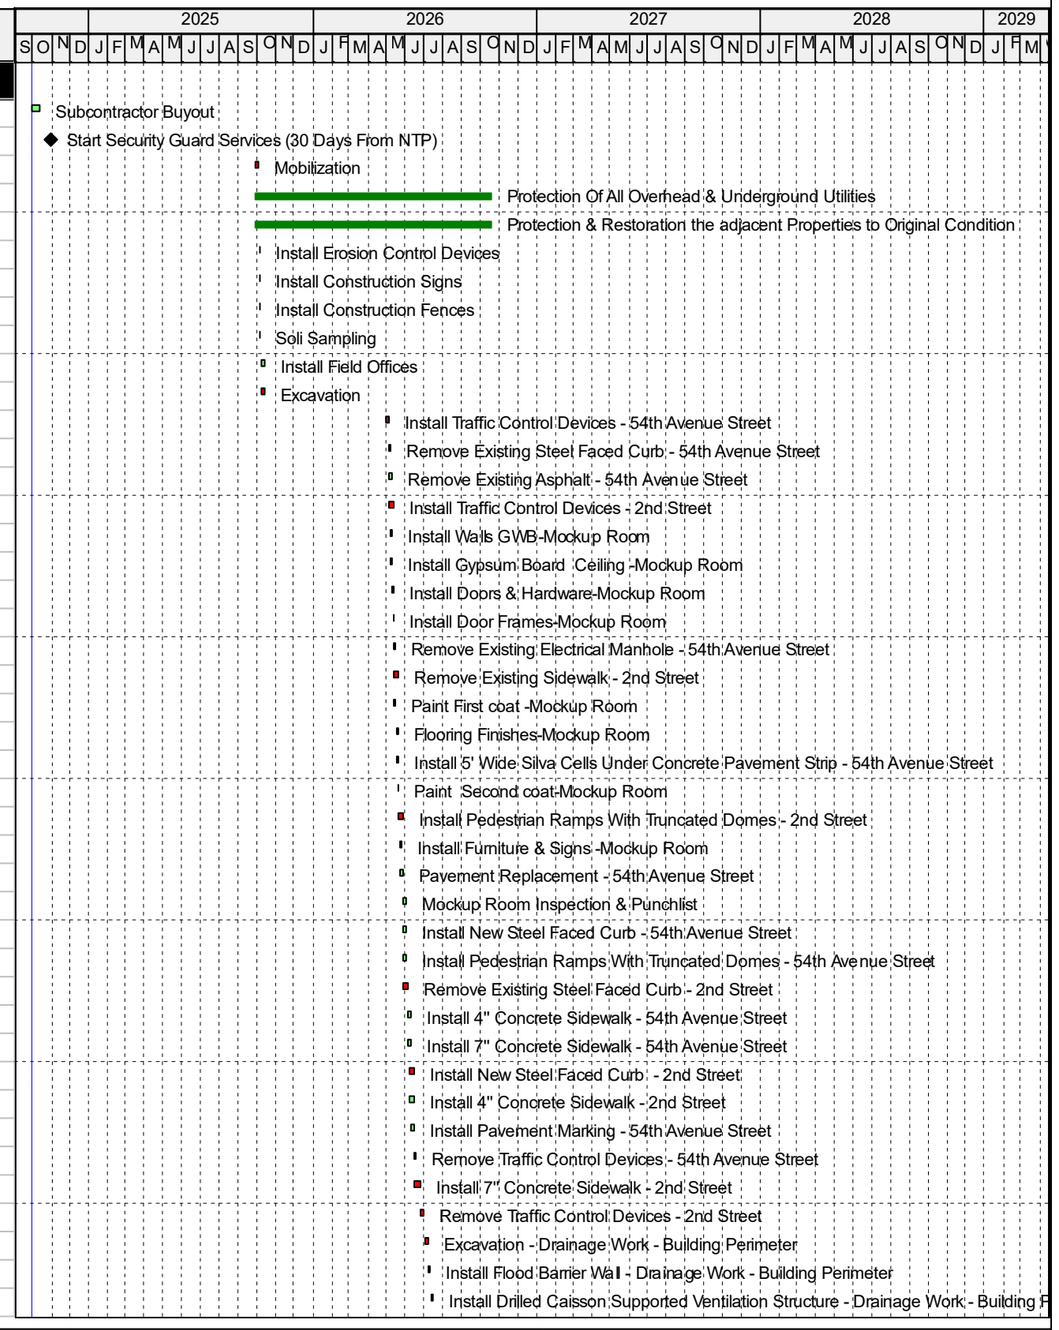

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
CON-4980	Install 4" & 6" & 10" & 12" DIP - Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-9170	Install 8" Combined Water Service (2nd Street)- Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-9180	Install 6" Fire Water Service (54th Avenue Street)- Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-5190	Install Catch Basin - Drainage Work - Building Perimeter	2	21-Jul-26	22-Jul-26
CON-5290	Install Storm Inlet With Hood & Storm Hood - Drainage Work - Building Perimeter	2	23-Jul-26	24-Jul-26
CON-5400	Install Trench Drain - Drainage Work - Building Perimeter	1	27-Jul-26	27-Jul-26
CON-9160	Excavate for Footings - Playground Area & Fences - Building Perimeter	2	28-Jul-26	29-Jul-26
CON-9010	Remove Steel Plate Protection over NYPA Easement - Playground Area & Fences - Building Perimeter	1	28-Jul-26	28-Jul-26
CON-9190	F/R/P Playground Equipment Footings - Playground Area & Fences - Building Perimeter	2	30-Jul-26	31-Jul-26
CON-5470	Install Flush Concrete Curb - Playground Area & Fences - Building Perimeter	3	03-Aug-26	05-Aug-26
CON-5420	Install Asphalt Pavement - Playground Area & Fences - Building Perimeter	2	04-Aug-26	05-Aug-26
CON-5600	Install Concrete Pavement Pedestrian Ramp With Painted Black Handrails - Playground Area & Fences - Building Perimeter	3	06-Aug-26	10-Aug-26
CON-5650	Install Playground Rubber Tile Safety Surface - Playground Area & Fences - Building Perimeter	3	11-Aug-26	13-Aug-26
CON-5800	Install Painted Asphalt Pavement & Painted Games On Asphalt Surface - Playground Area & Fences - Building Perimeter	3	14-Aug-26	18-Aug-26
CON-5850	Install Colored Athletic Wearing Surface Color - Playground Area & Fences - Building Perimeter	2	19-Aug-26	20-Aug-26
CON-5990	Install Playground Equipment - Playground Area & Fences - Building Perimeter	7	21-Aug-26	31-Aug-26
CON-6140	Install Basketball Hoop - Playground Area & Fences - Building Perimeter	1	01-Sep-26	01-Sep-26
CON-6190	Install Wrought Iron Fence Double Gate - Playground Area - Building Perimeter	3	02-Sep-26	04-Sep-26
CON-6270	Install Chain Link Fence - Playground Area & Fences - Building Perimeter	3	08-Sep-26	10-Sep-26
MIL-1470	Finish Site Work	0		10-Sep-26
First Floor		227	16-Oct-25	11-Sep-26
CON-9898	Install Gas Permeable Aggregate -1st Floor	3	16-Oct-25	20-Oct-25
CON-98947	Install 4" slotted schedule 80 PVC Piping -1st Floor	3	16-Oct-25	20-Oct-25
CON-9888	Install Liquid Boot VI-20 Geomembrane -1st Floor	2	21-Oct-25	22-Oct-25
CON-1020	Install 60 Dry MILS Liquid Boot -1st Floor	3	23-Oct-25	27-Oct-25
CON-9777	Install Liquid Ultrashield G-1000 -1st Floor	2	24-Oct-25	27-Oct-25
CON-1040	F/R/P Concrete Walls & Beams -1st Floor	10	28-Oct-25	10-Nov-25
CON-1050	Install Underground Conduits & Wires -1st Floor	6	12-Nov-25	19-Nov-25
CON-1060	Backfilling & Compaction -1st Floor	6	12-Nov-25	19-Nov-25
CON-1070	F/R/P SOG -1st Floor	10	20-Nov-25	04-Dec-25
CON-4920	Install Floor Drains & Clean-outs -1st Floor	5	27-Nov-25	04-Dec-25
CON-99327	Install Lightning Protection System-1st Floor	2	03-Dec-25	04-Dec-25
CON-98787	Install Steel Columns -1st Floor	7	05-Dec-25	15-Dec-25
CON-1090	Install Trusses -1st Floor	3	16-Dec-25	18-Dec-25
CON-1100	Install Framing Beams -1st Floor	4	16-Dec-25	19-Dec-25
CON-1130	Install MEP Hangers & Sleeves- 2nd Floor	4	22-Dec-25	26-Dec-25
CON-99277	Install Steel Stairs -1st Floor	7	28-Jan-26	05-Feb-26
CON-1430	Install Unit Masonry Mock-Up	1	23-Feb-26	23-Feb-26
CON-1470	Approve Unit Masonry Mock-Up	4	24-Feb-26	27-Feb-26
CON-1180	Spray Fireproofing - 1st Floor	5	03-Mar-26	09-Mar-26
CON-2900	Install Duct Risers-1st Floor	1	07-Apr-26	07-Apr-26
CON-2910	Layout -1st Floor	3	07-Apr-26	09-Apr-26
CON-3060	Install Mechanical Piping Risers-1st Floor	2	08-Apr-26	09-Apr-26
CON-3070	Duct Leak Test -1st Floor	1	08-Apr-26	08-Apr-26

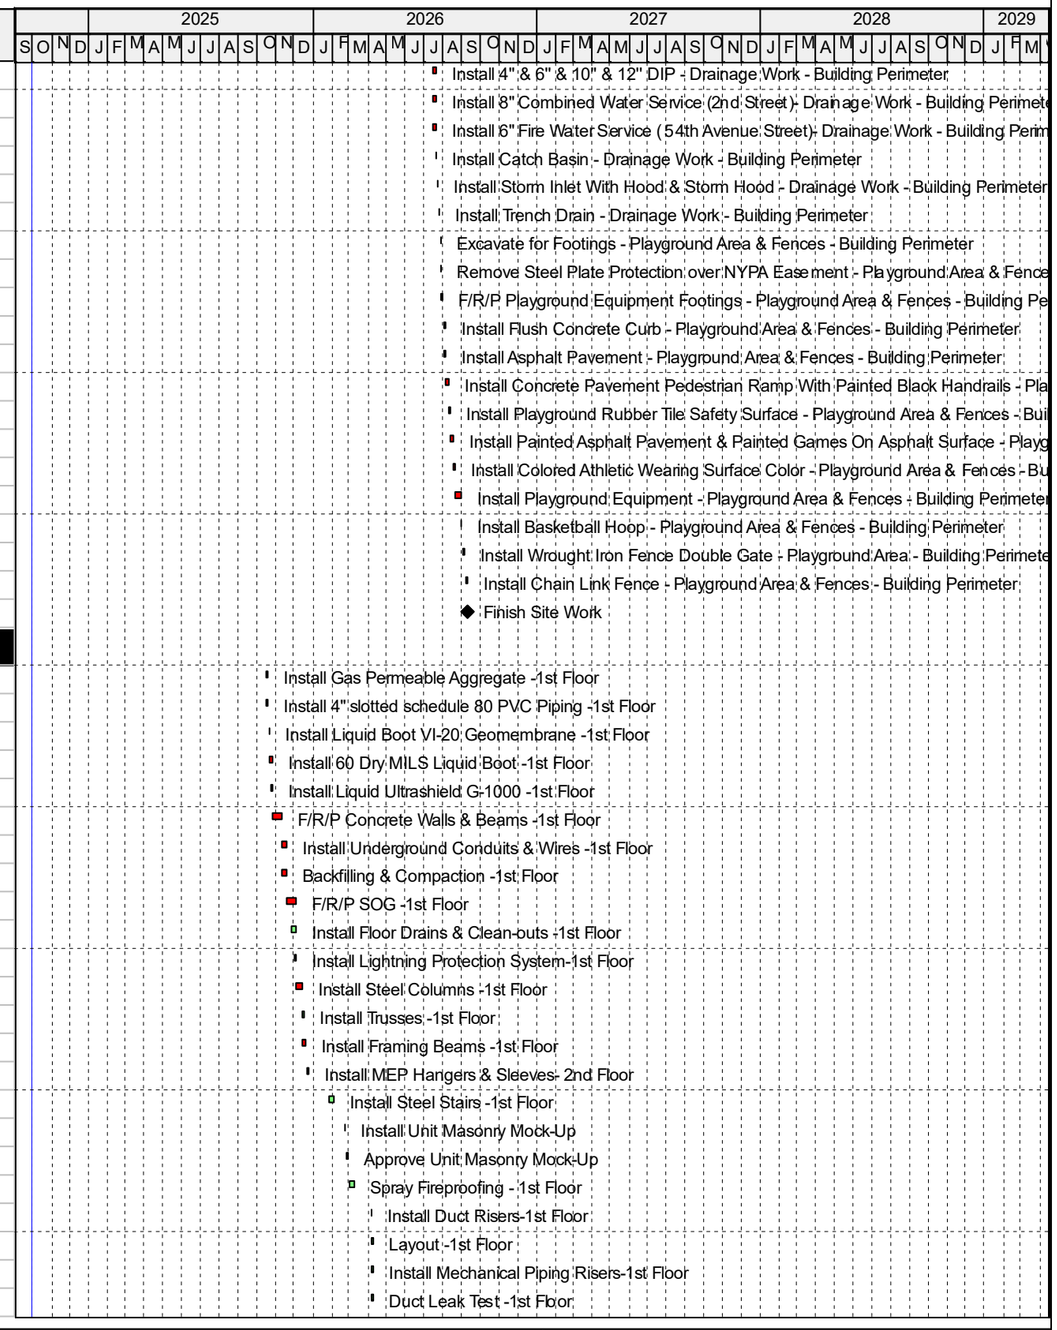

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3120	Rough-in Duct Work -1st Floor	4	09-Apr-26	14-Apr-26
CON-3080	Install Top & Bottom Track -1st Floor	4	10-Apr-26	15-Apr-26
CON-3090	Install CMU Walls -1st Floor	3	10-Apr-26	14-Apr-26
CON-3140	Install Plumbing Risers -1st Floor	2	10-Apr-26	13-Apr-26
CON-3230	Install SSDS Risers -SSDS System -1st Floor	2	14-Apr-26	15-Apr-26
CON-3260	Install Power Risers-1st Floor	2	14-Apr-26	15-Apr-26
CON-3460	Rough-in Hot Water Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3470	Rough-in Hot Glycol Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3480	Rough-in Chilled Glycol Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3490	Rough-in Refrigerant Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3520	Install Ceiling Hangers & Supports -1st Floor	4	15-Apr-26	20-Apr-26
CON-3970	Install VAV Boxes & Sound Attenuator Devices- 1st Floor	5	16-Apr-26	22-Apr-26
CON-3240	Install Wall Steel Studs & Framing -1st Floor	5	16-Apr-26	22-Apr-26
CON-3350	Install Low Voltage Risers-1st Floor	2	16-Apr-26	17-Apr-26
CON-3760	Rough-in Power Conduits -1st Floor	4	21-Apr-26	24-Apr-26
CON-4730	Rough-in Conduits & Wires - Electric Service Room	6	23-Apr-26	30-Apr-26
CON-3910	Install Grounding System -1st Floor	5	27-Apr-26	01-May-26
CON-3920	Rough-in Low-Voltage Conduits-1st Floor	4	27-Apr-26	30-Apr-26
CON-3930	Power Wires Pulling-1st Floor	4	27-Apr-26	30-Apr-26
CON-3740	Install Ground Bus Bar - 1st Floor MDF Room	6	29-Apr-26	06-May-26
CON-4180	Low Voltage Wires Pulling -1st Floor	4	01-May-26	06-May-26
CON-4960	F/R/P Concrete Pad - Electric Service Room	6	01-May-26	08-May-26
CON-4460	Rough-in Gas Risers -1st Floor	4	07-May-26	12-May-26
CON-4110	Install Voice Rack - 1st Floor MDF Room	6	07-May-26	14-May-26
CON-4500	Install SSDS Control Panel -1st Floor	5	07-May-26	13-May-26
CON-5180	Install Service Switchboard "SS-A"- Electric Service Room	5	11-May-26	15-May-26
CON-4590	Rough-in Domestic Water Piping-1st Floor	4	13-May-26	18-May-26
CON-4510	Install Sound Rack - 1st Floor MDF Room	6	15-May-26	22-May-26
CON-4120	Install Project Connect Cabinet - 1st Floor MDF Room	8	15-May-26	27-May-26
CON-4470	Install Wiring Devices -1st Floor	7	15-May-26	26-May-26
CON-5510	Install Leak Detector - Electric Service Room	3	18-May-26	20-May-26
CON-4690	Rough-in Sanitary & Vent Piping -1st Floor	4	19-May-26	22-May-26
CON-9110	In-Wall Inspection -1st Floor	2	19-May-26	20-May-26
CON-5610	Install Sprinkler Booster Pump - Electric Service Room	4	21-May-26	27-May-26
CON-4760	Rough-in Storm Piping -1st Floor	4	26-May-26	29-May-26
CON-4520	Install Data Rack - 1st Floor MDF Room	6	26-May-26	02-Jun-26
CON-5640	Install Fire Alarm Normal ATS - Electric Service Room	4	28-May-26	02-Jun-26
CON-4890	F/R/P Concrete Pads -Fuel Oil Room	2	01-Jun-26	02-Jun-26
CON-4900	Rough-in Fuel Oil Piping -Fuel Oil Room	3	01-Jun-26	03-Jun-26
CON-1120	Install Firestopping Mock-Up	2	01-Jun-26	02-Jun-26
CON-4940	Install Duplex Domestic Water Booster Pump System (BP-1&BP-2) -1st Floor	8	01-Jun-26	10-Jun-26
CON-4950	Install Duplex Ejector Pump System (EJ-1&EJ-2) -1st Floor	8	01-Jun-26	10-Jun-26
CON-4910	Install 4" Standpipe -1st Floor	4	02-Jun-26	05-Jun-26
CON-4990	Install Fuel Oil Storage Tank (FOT-1) - Fuel Oil Room	3	03-Jun-26	05-Jun-26

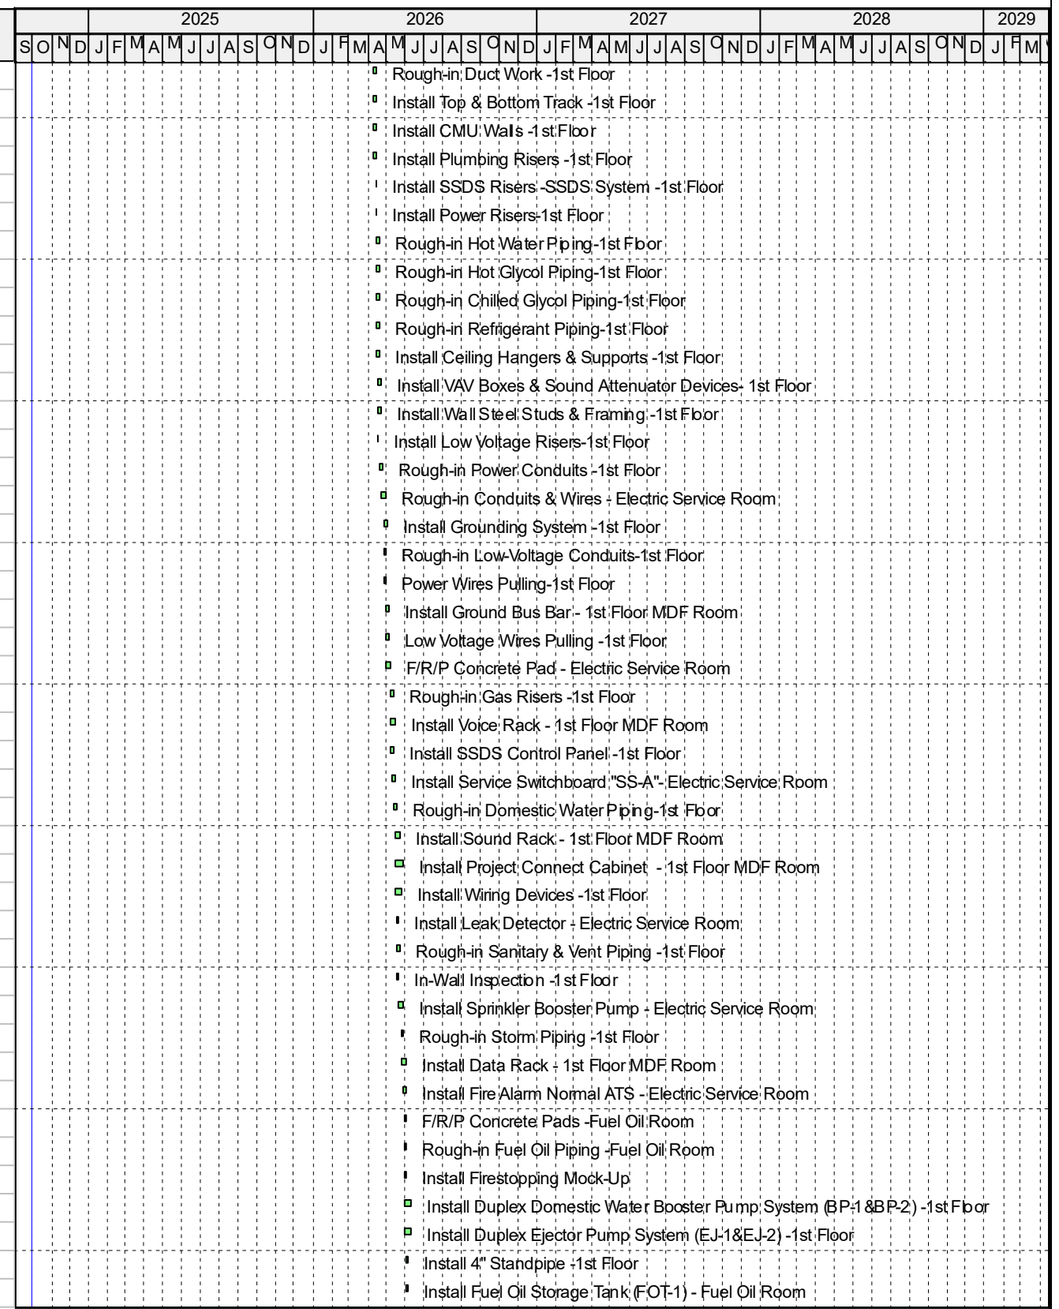

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1140	Approve Firestopping Mock-Up	2	03-Jun-26	04-Jun-26
CON-4550	Install UPS- 1st Floor MDF Room	9	03-Jun-26	15-Jun-26
CON-4130	Install BACnet Data Cabinet- 1st Floor MDF Room	9	03-Jun-26	15-Jun-26
CON-5780	Install Motorized Fire/Smoke Damper & Control Panel - Electric Service Room	5	03-Jun-26	09-Jun-26
CON-5790	Install Main Grounding Bus Bar - Electric Service Room	4	03-Jun-26	08-Jun-26
CON-5020	Rough-in Fuel Oil Fill Piping -Fuel Oil Room	3	04-Jun-26	08-Jun-26
MIL-1750	Start Firestopping	0	05-Jun-26	
CON-5160	Install Fuel Oil Transfer Duplex Pump (FOP-1 & 2) -1st Floor	4	08-Jun-26	11-Jun-26
CON-5030	Rough-in Main Sprinkler Piping -1st Floor	5	08-Jun-26	12-Jun-26
CON-9130	Install Switch Gear - Electric Service Room	5	08-Jun-26	12-Jun-26
CON-5200	Rough-in Fuel Oil Vent Piping -Fuel Oil Room	4	09-Jun-26	12-Jun-26
CON-5840	Install Electric Unit Heater EUH-6 - Electric Service Room	4	10-Jun-26	15-Jun-26
CON-5050	Plumbing Pressure Testing -1st Floor	5	11-Jun-26	17-Jun-26
CON-5230	Rough-in Branch Sprinkler Piping -1st Floor	5	15-Jun-26	22-Jun-26
CON-5240	Rough-in Sprinkler Heads -1st Floor	5	15-Jun-26	22-Jun-26
CON-4780	Install IPDVS Equipment Rack - 1st Floor MDF Room	6	16-Jun-26	24-Jun-26
CON-5210	Plumbing Piping Insulation -1st Floor	5	18-Jun-26	25-Jun-26
CON-5270	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -1st Floor	5	23-Jun-26	29-Jun-26
CON-4840	Install Duct Insulation -1st Floor	8	24-Jun-26	06-Jul-26
CON-4790	Install Ladder Rack Cable Tray- 1st Floor MDF Room	6	25-Jun-26	02-Jul-26
CON-4450	Install Gypsum Board Walls-1st Floor	6	26-Jun-26	06-Jul-26
CON-5410	Sprinklers Air Testing-1st Floor	5	30-Jun-26	07-Jul-26
CON-4600	Tape Gypsum Board -1st Floor	4	30-Jun-26	06-Jul-26
CON-5390	Install Firestopping-1st Floor	4	30-Jun-26	06-Jul-26
CON-4770	Install PBX - 1st Floor MDF Room	8	06-Jul-26	15-Jul-26
CON-4670	Install Exhaust Fans -1st Floor	5	07-Jul-26	13-Jul-26
CON-4680	Install Ceramic Wall Tiles at Corridor -1st Floor	7	07-Jul-26	15-Jul-26
CON-5480	Install Gypsum Board Ceiling -1st Floor	6	08-Jul-26	15-Jul-26
CON-4870	Install Cabinet Unit Heaters With Fan CUH-1st Floor	3	14-Jul-26	16-Jul-26
CON-4880	Install Motorized Fire/Smoke Damper FSD - Mechanical Work - 1st Floor	7	14-Jul-26	22-Jul-26
CON-5720	Install First Coat Painting-1st Floor	5	16-Jul-26	22-Jul-26
CON-5070	Install Electric Unit Heaters -1st Floor	7	17-Jul-26	27-Jul-26
CON-5860	Install Sprinkler Booster Pump (SBP-1) -1st Floor	10	23-Jul-26	05-Aug-26
CON-5870	Install Metal Panel Ceiling & Metal Geometric Ceiling -1st Floor	5	23-Jul-26	29-Jul-26
CON-5920	Install Door Frames & Doors-1st Floor	5	23-Jul-26	29-Jul-26
CON-5150	Install Air Conditioning Unit AC - Mechanical Work - 1st Floor	4	23-Jul-26	28-Jul-26
CON-5940	Install Lighting Fixtures -1st Floor	7	24-Jul-26	03-Aug-26
CON-98937	Install Sound Clock System Components-1st Floor	3	24-Jul-26	28-Jul-26
CON-5300	Install Grease Interceptors - 1st Floor	5	28-Jul-26	03-Aug-26
CON-5320	Install Door Curtains DC - Mechanical Work - 1st Floor	7	29-Jul-26	06-Aug-26
CON-98887	Install Auxiliary System Components-1st Floor	4	29-Jul-26	03-Aug-26
CON-6080	Install Flooring Tiles-1st Floor	5	30-Jul-26	05-Aug-26
CON-99267	Install Rolling Doors-1st Floor	3	30-Jul-26	03-Aug-26
CON-98837	Install Intrusion System Components-1st Floor	4	04-Aug-26	07-Aug-26

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

New Building PS/IS 341Q - Baseline Schedule Rev 01

PROJECS
ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
CON-5950	Install Fire alarm Sensors and Devises -1st Floor	3	05-Aug-26	07-Aug-26
CON-6100	Install Jockey Pump (JP-1) -1st Floor	10	06-Aug-26	19-Aug-26
CON-6180	Install Plumbing Fixtures-1st Floor	5	06-Aug-26	12-Aug-26
CON-5490	Install Convector Heater CV - Mechanical Work - 1st Floor	7	07-Aug-26	17-Aug-26
CON-6170	Install Final Coat Painting-1st Floor	6	21-Aug-26	28-Aug-26
CON-6040	Install IPDVS Devices -1st Floor	7	25-Aug-26	02-Sep-26
MIL-2672	Finish Painting	0		28-Aug-26
CON-5880	Install Acoustical Ceiling Tiles -1st Floor	5	31-Aug-26	04-Sep-26
CON-6300	Install Furniture & Milling Work (Contractor Provided & Installed) -1st Floor	4	31-Aug-26	03-Sep-26
CON-6310	Install Security Screens & Barriers-1st Floor	3	31-Aug-26	02-Sep-26
CON-6320	Install Cafeteria Equipment-1st Floor	4	31-Aug-26	03-Sep-26
CON-9020	Install Furniture & Milling Work (Owner Provided & Installed) -1st Floor	3	31-Aug-26	02-Sep-26
CON-6370	Install Signages-1st Floor	4	04-Sep-26	10-Sep-26
CON-6380	Install Food Service Equipment-1st Floor	5	04-Sep-26	11-Sep-26
MIL-2722	Start Kitchen	0	04-Sep-26	
Second Floor		187	19-Dec-25	17-Sep-26
CON-3160	Install Floor Drains & Clean-outs -2nd Floor	5	19-Dec-25	26-Dec-25
CON-1110	Install Metal Deck Slab -2nd Floor	4	22-Dec-25	26-Dec-25
CON-1150	Install Steel Canopy Framing -2nd Floor	5	29-Dec-25	05-Jan-26
CON-1160	Hoist Material Design	10	29-Dec-25	12-Jan-26
CON-1170	Install Steel Columns -2nd Floor	3	29-Dec-25	31-Dec-25
CON-3270	Install Temporary Standpipe	9	29-Dec-25	09-Jan-26
CON-1190	Install Trusses -2nd Floor	4	02-Jan-26	07-Jan-26
CON-1200	Install Framing Beams -2nd Floor	5	02-Jan-26	08-Jan-26
CON-1230	Install MEP Hangers & Sleeves-3rd Floor	4	09-Jan-26	14-Jan-26
CON-1250	Approval of Hoist Design	7	13-Jan-26	19-Jan-26
CON-1280	Install Elevator Hoist Pad	5	20-Jan-26	26-Jan-26
CON-1320	Erect Material Hoist	5	27-Jan-26	02-Feb-26
CON-99287	Install Steel Stairs -2nd Floor	3	06-Feb-26	10-Feb-26
CON-1410	Install Duct Risers-2nd Floor	1	23-Feb-26	23-Feb-26
CON-1420	Layout -2nd Floor	3	23-Feb-26	25-Feb-26
CON-1480	Rough-in Duct Work -2nd Floor	4	24-Feb-26	27-Feb-26
CON-1500	Install Mechanical Piping Risers-2nd Floor	2	24-Feb-26	25-Feb-26
CON-1510	Duct Leak Test -2nd Floor	2	24-Feb-26	25-Feb-26
CON-1520	Install Top & Bottom Track-2nd Floor	4	26-Feb-26	03-Mar-26
CON-1580	Install Plumbing Risers -2nd Floor	2	26-Feb-26	27-Feb-26
CON-1850	Rough-in Hot Water Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1860	Rough-in Hot Glycol Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1870	Rough-in Chilled Glycol Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1880	Rough-in Refrigerant Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1570	Install CMU Walls -2nd Floor	3	02-Mar-26	04-Mar-26
CON-1710	Install Power Risers-2nd Floor	2	02-Mar-26	03-Mar-26
CON-1740	Install SSDS Risers -SSDS System -2nd Floor	2	02-Mar-26	03-Mar-26
CON-1640	Install Wall Steel Studs & Framing-2nd Floor	5	04-Mar-26	10-Mar-26

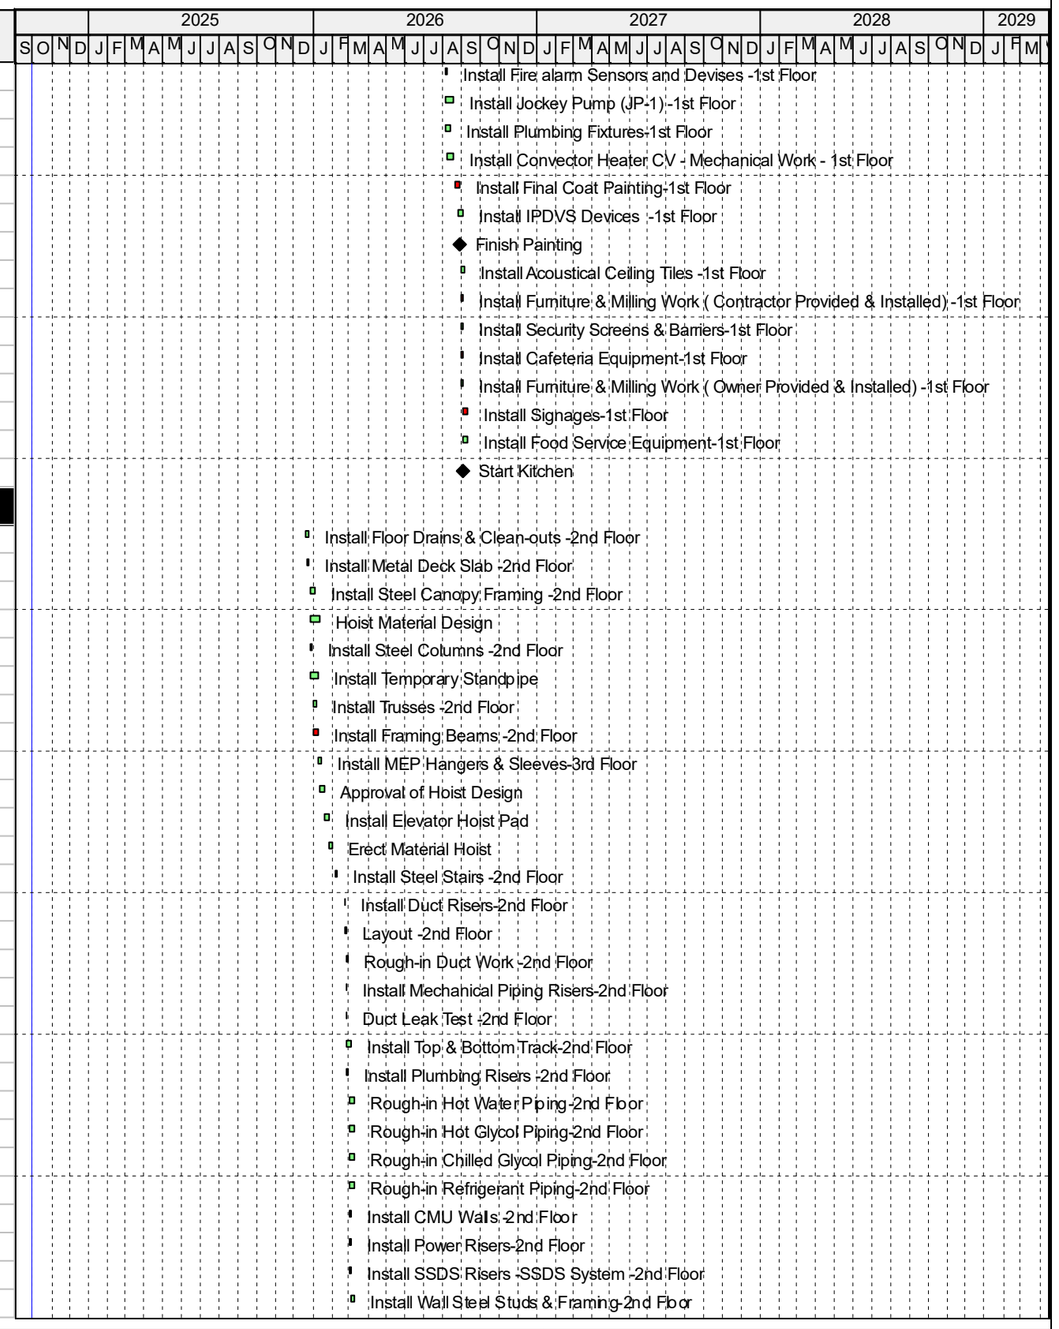

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1800	Install Low Voltage Risers-2nd Floor	2	04-Mar-26	05-Mar-26
CON-1220	Spray Fireproofing - 2nd Floor	5	10-Mar-26	16-Mar-26
CON-2180	Rough-in Power Conduits -2nd Floor	6	11-Mar-26	18-Mar-26
CON-2310	Install Ceiling Hangers & Supports-2nd Floor	4	16-Mar-26	19-Mar-26
CON-3980	Install VAV Boxes & Sound Attenuator Devices-2nd Floor	5	19-Mar-26	25-Mar-26
CON-2330	Rough-in Low-Voltage Conduits -2nd Floor	6	19-Mar-26	26-Mar-26
CON-2340	Power Wires Pulling -2nd Floor	6	19-Mar-26	26-Mar-26
CON-2490	Low Voltage Wires Pulling -2nd Floor	6	27-Mar-26	03-Apr-26
CON-2520	Install Voice Rack - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2530	Install Data Rack - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2540	Install Ground Bus Bar - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2630	Rough-in Gas Risers -2nd Floor	4	06-Apr-26	09-Apr-26
CON-2670	Install Wiring Devices -2nd Floor	7	06-Apr-26	14-Apr-26
CON-2740	Rough-in Domestic Water Piping -2nd Floor	4	10-Apr-26	15-Apr-26
CON-2760	Install IPDVS Equipment Rack - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2770	Install Ladder Rack Cable Tray - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2780	Install BACnet Data Cabinet - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2850	Install Electric Unit Heaters -2nd Floor	5	16-Apr-26	22-Apr-26
CON-2870	Rough-in Sanitary & Vent Piping -2nd Floor	4	16-Apr-26	21-Apr-26
CON-9070	In-Wall Inspection-2nd Floor	2	16-Apr-26	17-Apr-26
CON-3020	Rough-in Storm Piping -2nd Floor	4	22-Apr-26	27-Apr-26
CON-3150	Install Convector Heater CV - Mechanical Work - 2nd Floor	5	23-Apr-26	29-Apr-26
CON-3200	Plumbing Pressure Testing -2nd Floor	5	28-Apr-26	04-May-26
CON-3450	Install Air Conditioning Unit AC - Mechanical Work - 2nd Floor	4	30-Apr-26	05-May-26
CON-3310	Install 4" Standpipe -2nd Floor	4	04-May-26	07-May-26
CON-4050	Plumbing Piping Insulation -2nd Floor	5	07-May-26	13-May-26
CON-4070	Install Duct Insulation -2nd Floor	8	07-May-26	18-May-26
CON-3500	Rough-in Main Sprinkler Piping -2nd Floor	5	08-May-26	14-May-26
CON-3670	Rough-in Branch Sprinkler Piping -2nd Floor	5	15-May-26	21-May-26
CON-3680	Rough-in Sprinkler Heads -2nd Floor	5	15-May-26	21-May-26
CON-3720	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -2nd Floor	5	15-May-26	21-May-26
CON-3830	Sprinklers Air Testing-2nd Floor	5	22-May-26	29-May-26
CON-4030	Install Gypsum Board Walls-2nd Floor	5	27-May-26	02-Jun-26
CON-4200	Tape Gypsum Board -2nd Floor	4	28-May-26	02-Jun-26
CON-4350	Install Ceramic Wall Tiles at Corridor-2nd Floor	7	03-Jun-26	11-Jun-26
CON-4370	Install Gypsum Board Ceiling -2nd Floor	6	03-Jun-26	10-Jun-26
CON-4700	Install Firestopping-2nd Floor	3	05-Jun-26	09-Jun-26
CON-4830	Install First Coat Painting-2nd Floor	5	11-Jun-26	17-Jun-26
CON-5120	Install Door Frames & Doors-2nd Floor	5	18-Jun-26	25-Jun-26
CON-5130	Install Lighting Fixtures -2nd Floor	5	18-Jun-26	25-Jun-26
CON-98797	Install Intrusion System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-98847	Install Auxiliary System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-98897	Install Sound Clock System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-5360	Install Flooring Tiles-2nd Floor	5	26-Jun-26	02-Jul-26

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
CON-5310	Install Fire alarm Sensors and Devises -2nd Floor	5	26-Jun-26	02-Jul-26
CON-5560	Install Final Coat Painting-2nd Floor	6	06-Jul-26	13-Jul-26
CON-5570	Install Plumbing Fixtures -2nd Floor	7	06-Jul-26	14-Jul-26
CON-5140	Install IPDVS Devices -2nd Floor	9	06-Jul-26	16-Jul-26
CON-5090	Install Acoustical Ceiling Tiles-2nd Floor	5	14-Jul-26	20-Jul-26
CON-5710	Install Furniture & Milling Work (Contractor Provided & Installed) -2nd Floor	5	14-Jul-26	20-Jul-26
CON-9030	Install Furniture & Milling Work (Owner Provided & Installed) -2nd Floor	5	14-Jul-26	20-Jul-26
CON-5820	Install Signages-2nd Floor	5	21-Jul-26	27-Jul-26
CON-5040	Dismantle Hoist	2	10-Sep-26	11-Sep-26
CON-5170	Demolish Hoist Pad	2	14-Sep-26	15-Sep-26
CON-5250	Hoist In-Fill	2	16-Sep-26	17-Sep-26
Third Floor		144	08-Jan-26	04-Aug-26
CON-3320	Install Floor Drains & Clean-outs -3rd Floor	5	08-Jan-26	14-Jan-26
CON-1210	Install Metal Deck Slab - 3rd Floor	4	09-Jan-26	14-Jan-26
CON-1240	Install Steel Columns - 3rd Floor	4	15-Jan-26	21-Jan-26
CON-1260	Install Trusses - 3rd Floor	3	22-Jan-26	26-Jan-26
CON-1270	Install Framing Beams - 3rd Floor	5	22-Jan-26	28-Jan-26
CON-1310	Install MEP Hangers & Sleeves-4th Floor	4	29-Jan-26	03-Feb-26
CON-99297	Install Steel Stairs- 3rd Floor	4	11-Feb-26	17-Feb-26
CON-1490	Install Duct Risers -3rd Floor	2	24-Feb-26	25-Feb-26
CON-1530	Layout -3rd Floor	3	26-Feb-26	02-Mar-26
CON-1590	Install Mechanical Piping Risers -3rd Floor	2	26-Feb-26	27-Feb-26
CON-1600	Duct Leak Test -3rd Floor	2	26-Feb-26	27-Feb-26
CON-1890	Rough-in Duct Work -3rd Floor	5	02-Mar-26	06-Mar-26
CON-1680	Install Plumbing Risers -3rd Floor	2	02-Mar-26	03-Mar-26
CON-1650	Install Top & Bottom Track-3rd Floor	4	04-Mar-26	09-Mar-26
CON-1820	Install Power Risers-3rd Floor	2	04-Mar-26	05-Mar-26
CON-1840	Install SSDS Risers -SSDS System -3rd Floor	2	04-Mar-26	05-Mar-26
CON-1660	Install CMU Walls -3rd Floor	3	05-Mar-26	09-Mar-26
CON-1950	Install Low Voltage Risers-3rd Floor	2	06-Mar-26	09-Mar-26
CON-2160	Rough-in Refrigerant Piping-3rd Floor	7	09-Mar-26	17-Mar-26
CON-1900	Install Wall Steel Studs & Framing-3rd Floor	5	10-Mar-26	16-Mar-26
CON-2130	Rough-in Hot Water Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-2140	Rough-in Hot Glycol Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-2150	Rough-in Chilled Glycol Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-1300	Spray Fireproofing - 3rd Floor	5	17-Mar-26	23-Mar-26
CON-2320	Rough-in Power Conduits-3rd Floor	6	19-Mar-26	26-Mar-26
CON-2390	Install Ceiling Hangers & Supports-3rd Floor	4	20-Mar-26	25-Mar-26
CON-4140	Install VAV Boxes & Sound Attenuator Devices-3rd Floor	5	26-Mar-26	01-Apr-26
CON-2640	Install Grounding Bars - 3rd Floor IDF Room	5	27-Mar-26	02-Apr-26
CON-2500	Rough-in Low-Voltage Conduits-3rd Floor	6	27-Mar-26	03-Apr-26
CON-2510	Power Wires Pulling-3rd Floor	6	27-Mar-26	03-Apr-26
CON-2800	Install Data rack - 3rd Floor IDF Room	8	03-Apr-26	14-Apr-26
CON-2830	Install IPDVS Equipment Rack - 3rd Floor IDF Room	4	03-Apr-26	08-Apr-26

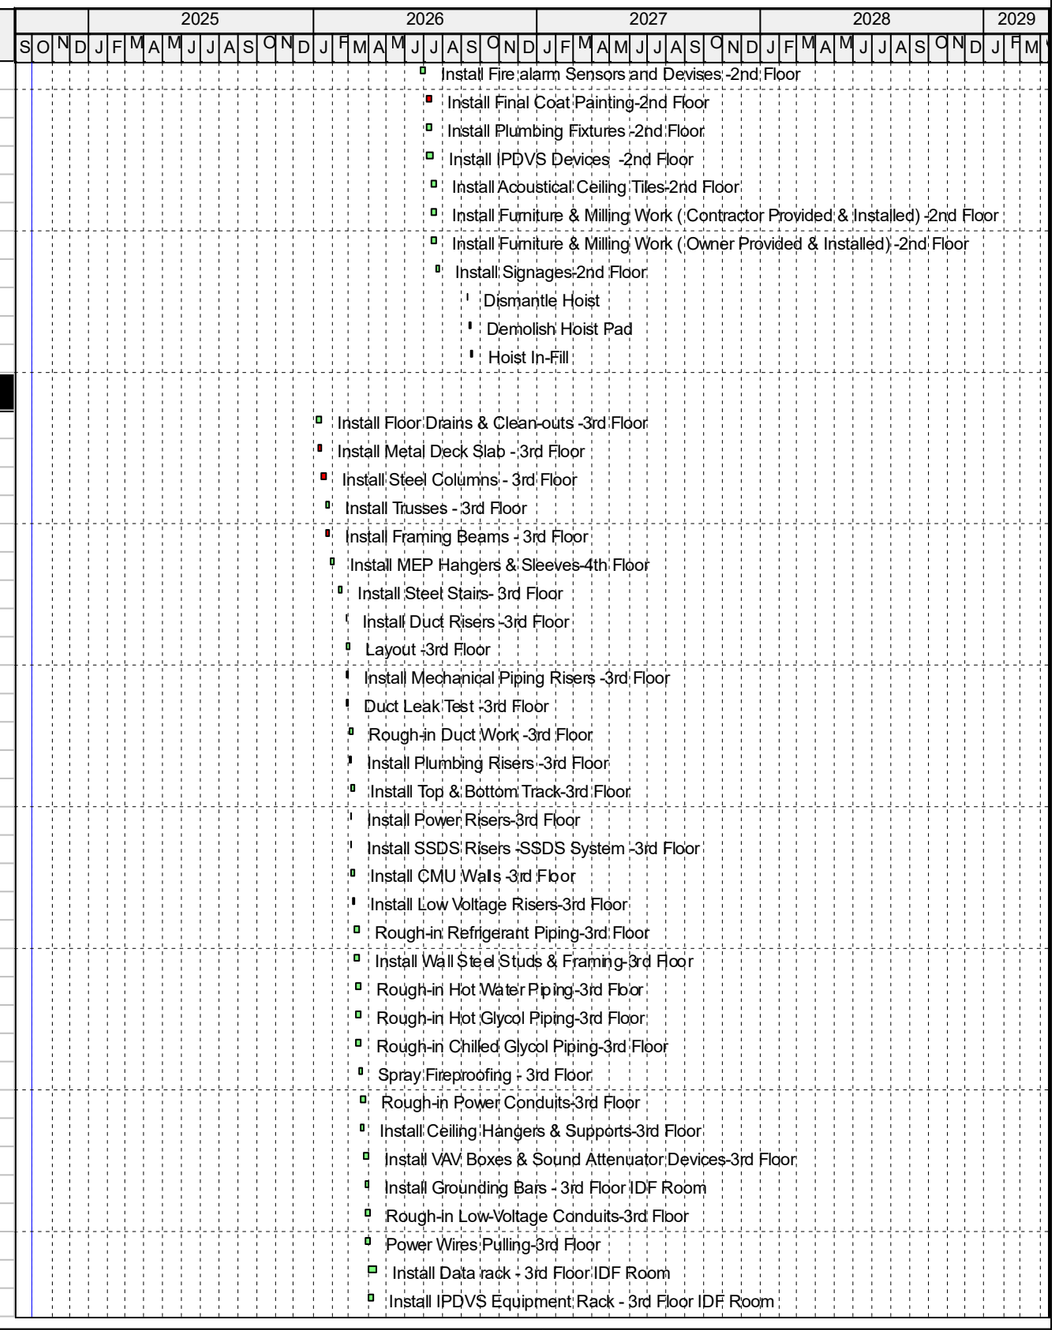

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2690	Low Voltage Wires Pulling -3rd Floor	6	06-Apr-26	13-Apr-26
CON-2750	Rough-in Gas Risers-3rd Floor	4	10-Apr-26	15-Apr-26
CON-3250	Install Voice Rack - 3rd Floor IDF Room	5	15-Apr-26	21-Apr-26
CON-2930	Install Wiring Devices -3rd Floor	7	15-Apr-26	23-Apr-26
CON-2880	Rough-in Domestic Water Piping -3rd Floor	4	16-Apr-26	21-Apr-26
CON-3030	Rough-in Sanitary & Vent Piping -3rd Floor	4	22-Apr-26	27-Apr-26
CON-3550	Install Cable Ladder - 3rd Floor IDF Room	5	22-Apr-26	28-Apr-26
CON-3570	Install Main Sound Rack - 3rd Floor IDF Room	5	22-Apr-26	28-Apr-26
CON-9080	In-Wall Inspection -3rd Floor	2	22-Apr-26	23-Apr-26
CON-3130	Install Electric Unit Heaters -3rd Floor	5	23-Apr-26	29-Apr-26
CON-3170	Rough-in Storm Piping -3rd Floor	4	28-Apr-26	01-May-26
CON-3360	Plumbing Pressure Testing -3rd Floor	5	05-May-26	11-May-26
CON-3510	Install 4" Standpipe -3rd Floor	4	08-May-26	13-May-26
CON-4190	Plumbing Piping Insulation -3rd Floor	5	14-May-26	20-May-26
CON-3690	Rough-in Main Sprinkler Piping-3rd Floor	5	15-May-26	21-May-26
CON-4320	Install Duct Insulation -3rd Floor	8	19-May-26	29-May-26
CON-3790	Rough-in Branch Sprinkler Piping -3rd Floor	5	22-May-26	29-May-26
CON-3800	Rough-in Sprinkler Heads -3rd Floor	5	22-May-26	29-May-26
CON-3880	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-3rd Floor	5	22-May-26	29-May-26
CON-4060	Sprinklers Air Testing-3rd Floor	5	01-Jun-26	05-Jun-26
CON-4360	Install Gypsum Board Walls-3rd Floor	5	03-Jun-26	09-Jun-26
CON-4540	Tape Gypsum Board -3rd Floor	4	04-Jun-26	09-Jun-26
CON-4850	Install Firestopping-3rd Floor	4	10-Jun-26	15-Jun-26
CON-4630	Install Gypsum Board Ceiling-3rd Floor	6	11-Jun-26	18-Jun-26
CON-4610	Install Ceramic Wall Tiles at Corridor-3rd Floor	7	12-Jun-26	23-Jun-26
CON-5110	Install First Coat Painting-3rd Floor	5	22-Jun-26	26-Jun-26
CON-5350	Install Door Frames & Doors-3rd Floor	5	29-Jun-26	06-Jul-26
CON-5370	Install Lighting Fixtures -3rd Floor	6	29-Jun-26	07-Jul-26
CON-98807	Install Intrusion System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-98857	Install Auxiliary System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-98907	Install Sound Clock System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-5550	Install Flooring Tiles-3rd Floor	5	07-Jul-26	13-Jul-26
CON-5500	Install Fire alarm Sensors and Devises -3rd Floor	8	08-Jul-26	17-Jul-26
CON-5700	Install Final Coat Painting-3rd Floor	6	14-Jul-26	21-Jul-26
CON-99247	Install Laboratory Equipment -3rd Floor	4	14-Jul-26	17-Jul-26
CON-5730	Install Plumbing Fixtures -3rd Floor	7	15-Jul-26	23-Jul-26
CON-5060	Install Hot Glycol / Hot Water Cabinet Heater (CUH)-3rd Floor	4	17-Jul-26	22-Jul-26
CON-5440	Install IPDVS Devices -3rd Floor	9	17-Jul-26	29-Jul-26
CON-5330	Install Acoustical Ceiling Tiles-3rd Floor	5	22-Jul-26	28-Jul-26
CON-5910	Install Furniture & Milling Work (Contractor Provided & Installed) -3rd Floor	5	22-Jul-26	28-Jul-26
CON-9040	Install Furniture & Milling Work (Owner Provided & Installed) -3rd Floor	5	22-Jul-26	28-Jul-26
CON-5280	Install Convector Heater CV - Mechanical Work - 3rd Floor	4	23-Jul-26	28-Jul-26
CON-6030	Install Signages-3rd Floor	5	29-Jul-26	04-Aug-26
CON-5450	Install Air Conditioning Unit AC - Mechanical Work - 3rd Floor	4	29-Jul-26	03-Aug-26

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
Fourth Floor		154	28-Jan-26	04-Sep-26
CON-3530	Install Floor Drains & Clean-outs -4th Floor	5	28-Jan-26	03-Feb-26
CON-1290	Install Metal Deck Slab - 4th Floor	4	29-Jan-26	03-Feb-26
CON-1330	Install Steel Columns - 4th Floor	4	04-Feb-26	09-Feb-26
CON-1360	Install Trusses - 4th Floor	3	10-Feb-26	12-Feb-26
CON-1370	Install Framing Beams - 4th Floor	5	10-Feb-26	17-Feb-26
CON-1400	Install MEP Hangers & Sleeves-5th Floor	4	17-Feb-26	20-Feb-26
CON-99307	Install Steel Stairs - 4th Floor	4	23-Feb-26	26-Feb-26
CON-1560	Install Duct Risers -4th Floor	2	26-Feb-26	27-Feb-26
CON-1690	Install Mechanical Piping Risers -4th Floor	2	02-Mar-26	03-Mar-26
CON-1700	Duct Leak Test -4th Floor	2	02-Mar-26	03-Mar-26
CON-1670	Layout -4th Floor	3	03-Mar-26	05-Mar-26
CON-1780	Install Plumbing Risers -4th Floor	2	04-Mar-26	05-Mar-26
CON-1960	Install Power Risers-4th Floor	2	06-Mar-26	09-Mar-26
CON-1970	Install SSDS Risers -SSDS System -4th Floor	2	06-Mar-26	09-Mar-26
CON-2170	Rough-in Duct Work -4th Floor	5	09-Mar-26	13-Mar-26
CON-1910	Install Top & Bottom Track-4th Floor	4	10-Mar-26	13-Mar-26
CON-1920	Install CMU Walls -4th Floor	3	10-Mar-26	12-Mar-26
CON-2040	Install Low Voltage Risers-4th Floor	2	10-Mar-26	11-Mar-26
CON-2290	Rough-in Refrigerant Piping-4th Floor	7	16-Mar-26	24-Mar-26
CON-2010	Install Wall Steel Studs & Framing-4th Floor	5	16-Mar-26	20-Mar-26
CON-2260	Rough-in Hot Water Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-2270	Rough-in Hot Glycol Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-2280	Rough-in Chilled Glycol Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-1390	Spray Fireproofing - 4th Floor	5	24-Mar-26	30-Mar-26
CON-2550	Install Ceiling Hangers & Supports-4th Floor	4	26-Mar-26	31-Mar-26
CON-2480	Rough-in Power Conduits-4th Floor	6	27-Mar-26	03-Apr-26
CON-4220	Install VAV Boxes & Sound Attenuator Devices-4th Floor	5	02-Apr-26	08-Apr-26
CON-2810	Install Grounding Bars - 4th Floor IDF Room	5	06-Apr-26	10-Apr-26
CON-2650	Install Data Rack - 4th Floor IDF Room	7	06-Apr-26	14-Apr-26
CON-2660	Install Voice Rack - 4th Floor IDF Room	5	06-Apr-26	10-Apr-26
CON-2700	Rough-in Low-Voltage Conduits-4th Floor	6	06-Apr-26	13-Apr-26
CON-2710	Power Wires Pulling-4th Floor	6	06-Apr-26	13-Apr-26
CON-2820	Install Cable Ladder - 4th Floor IDF Room	5	13-Apr-26	17-Apr-26
CON-2840	Install Main Sound Rack - 34th Floor IDF Room	5	13-Apr-26	17-Apr-26
CON-2940	Low Voltage Wires Pulling-4th Floor	6	15-Apr-26	22-Apr-26
CON-2890	Rough-in Gas Risers -4th Floor	4	16-Apr-26	21-Apr-26
CON-3110	Install IPDVS Equipment Rack - 4th Floor IDF Room	5	20-Apr-26	24-Apr-26
CON-3040	Rough-in Domestic Water Piping -4th Floor	4	22-Apr-26	27-Apr-26
CON-3280	Install Wiring Devices -4th Floor	7	24-Apr-26	04-May-26
CON-3180	Rough-in Sanitary & Vent Piping -4th Floor	4	28-Apr-26	01-May-26
CON-9090	In-Wall Inspection -4th Floor	7	28-Apr-26	06-May-26
CON-3420	Install Electric Unit Heaters -4th Floor	5	30-Apr-26	06-May-26
CON-3330	Rough-in Storm Piping -4th Floor	4	04-May-26	07-May-26

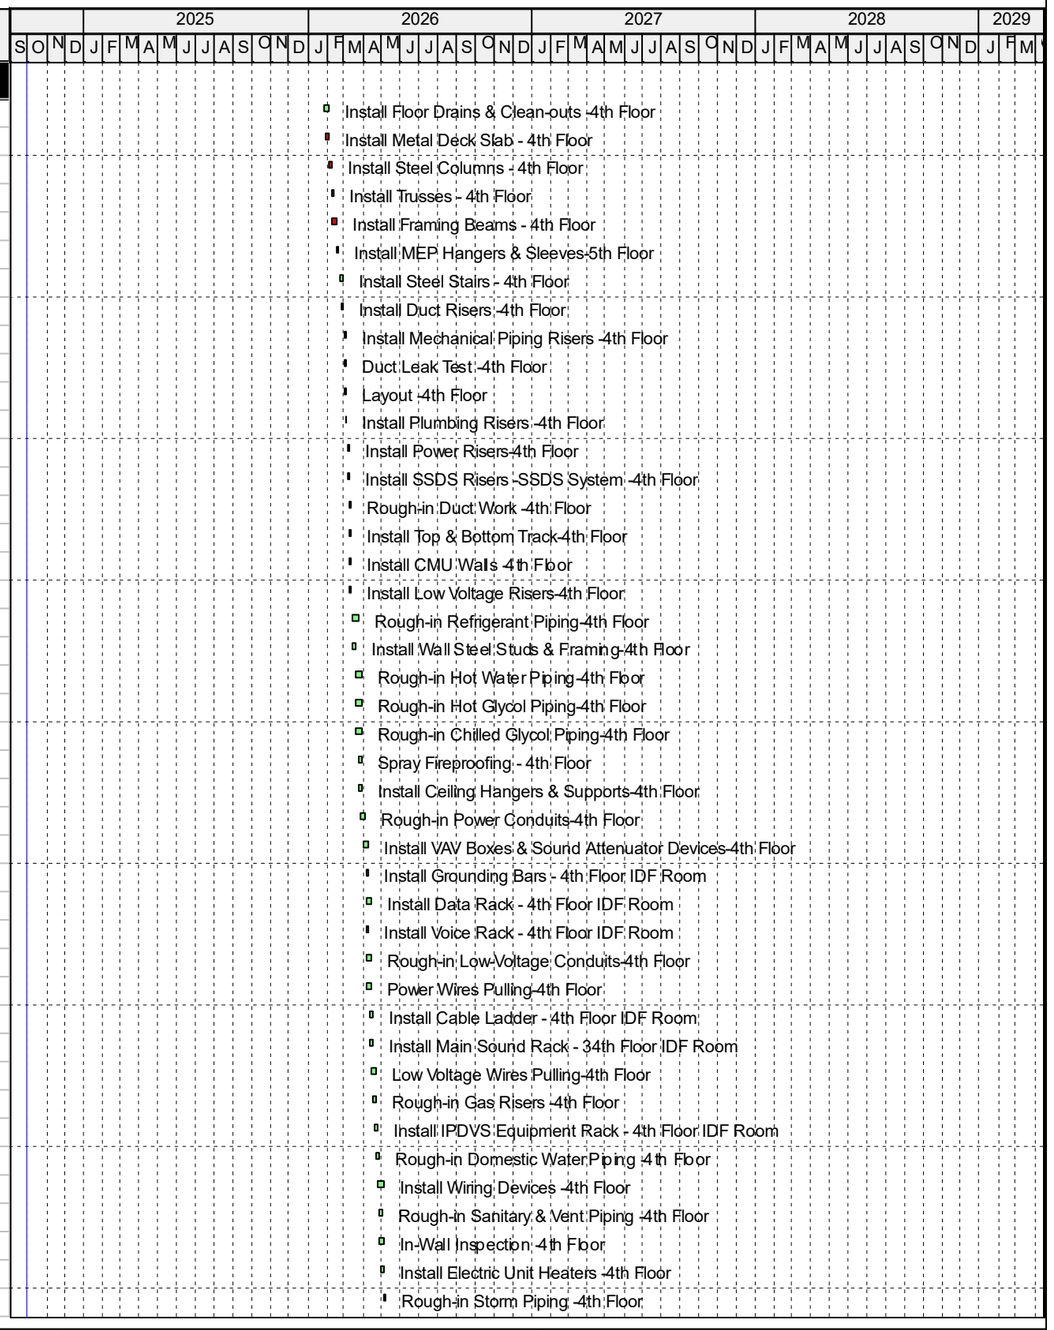

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3560	Plumbing Pressure Testing -4th Floor	5	12-May-26	18-May-26
CON-3650	Install 4" Standpipe -4th Floor	4	14-May-26	19-May-26
CON-4390	Plumbing Piping Insulation -4th Floor	5	21-May-26	28-May-26
CON-3810	Rough-in Main Sprinkler Piping-4th Floor	5	22-May-26	29-May-26
CON-3990	Rough-in Branch Sprinkler Piping -4th Floor	5	01-Jun-26	05-Jun-26
CON-4000	Rough-in Sprinkler Heads -4th Floor	5	01-Jun-26	05-Jun-26
CON-4100	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-4th Floor	5	01-Jun-26	05-Jun-26
CON-4570	Install Duct Insulation -4th Floor	8	01-Jun-26	10-Jun-26
CON-4280	Sprinklers Air Testing-4th Floor	5	08-Jun-26	12-Jun-26
CON-4620	Install Gypsum Board Walls-4th Floor	5	10-Jun-26	16-Jun-26
CON-4720	Tape Gypsum Board -4th Floor	4	11-Jun-26	16-Jun-26
CON-5010	Install Firestopping-4th Floor	4	16-Jun-26	22-Jun-26
CON-4820	Install Gypsum Board Ceiling-4th Floor	6	22-Jun-26	29-Jun-26
CON-4800	Install Ceramic Wall Tiles at Corridor-4th Floor	7	24-Jun-26	02-Jul-26
CON-5340	Install First Coat Painting-4th Floor	5	29-Jun-26	06-Jul-26
CON-5540	Install Door Frames & Doors-4th Floor	5	07-Jul-26	13-Jul-26
CON-5580	Install Lighting Fixtures -4th Floor	6	08-Jul-26	15-Jul-26
CON-98817	Install Intrusion System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-98867	Install Auxiliary System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-98917	Install Sound Clock System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-5690	Install Flooring Tiles-4th Floor	5	14-Jul-26	20-Jul-26
CON-5760	Install Wood Floating Floor System -Gymnatorium	10	14-Jul-26	27-Jul-26
CON-5660	Install Fire alarm Sensors and Devises -4th Floor	7	20-Jul-26	28-Jul-26
CON-5900	Install Final Coat Painting-4th Floor	6	22-Jul-26	29-Jul-26
CON-5260	Install Cabinet Unit Heater With Fan CUH -4th Floor	4	23-Jul-26	28-Jul-26
CON-5930	Install Plumbing Fixtures -4th Floor	7	24-Jul-26	03-Aug-26
CON-5810	Install Wall Pads - Gymnatorium	4	28-Jul-26	31-Jul-26
CON-5460	Install Convector Heater CV - Mechanical Work - 4th Floor	3	29-Jul-26	31-Jul-26
CON-5520	Install Acoustical Ceiling Tiles-4th Floor	5	30-Jul-26	05-Aug-26
CON-6070	Install Furniture & Milling Work (Contractor Provided & Installed) -4th Floor	5	30-Jul-26	05-Aug-26
CON-5750	Install IPDVS Devices -4th Floor	9	30-Jul-26	11-Aug-26
CON-9050	Install Furniture & Milling Work (Owner Provided & Installed) -4th Floor	5	30-Jul-26	05-Aug-26
CON-5970	Install Retractable Basketball Goal Assembly -Gymnatorium	3	03-Aug-26	05-Aug-26
CON-5620	Install Air Conditioning Unit AC - Mechanical Work - 4th Floor	4	04-Aug-26	07-Aug-26
CON-6160	Install Signages-4th Floor	5	06-Aug-26	12-Aug-26
CON-6020	Install 8" Acoustic Block Painted-Gymnatorium	7	06-Aug-26	14-Aug-26
CON-99217	Install Bleachers -Gymnatorium	3	12-Aug-26	14-Aug-26
CON-6230	Install Gym Equipment -Gymnatorium -Gymnatorium	6	17-Aug-26	24-Aug-26
CON-6240	Install Fine Tube Radiator FTR - Gymnatorium	5	17-Aug-26	21-Aug-26
CON-6250	Install Hydraulic Vertical Wheelchair Lift -Gymnatorium	8	17-Aug-26	26-Aug-26
CON-9150	Install LED Theatrical Lighting -Gymnatorium	4	25-Aug-26	28-Aug-26
CON-6390	Install Auditorium Television Studio Dimming System -Gymnatorium	7	27-Aug-26	04-Sep-26
Fifth Floor		140	13-Feb-26	02-Sep-26
CON-3610	Install Floor Drains & Clean-outs -5th Floor	5	13-Feb-26	20-Feb-26

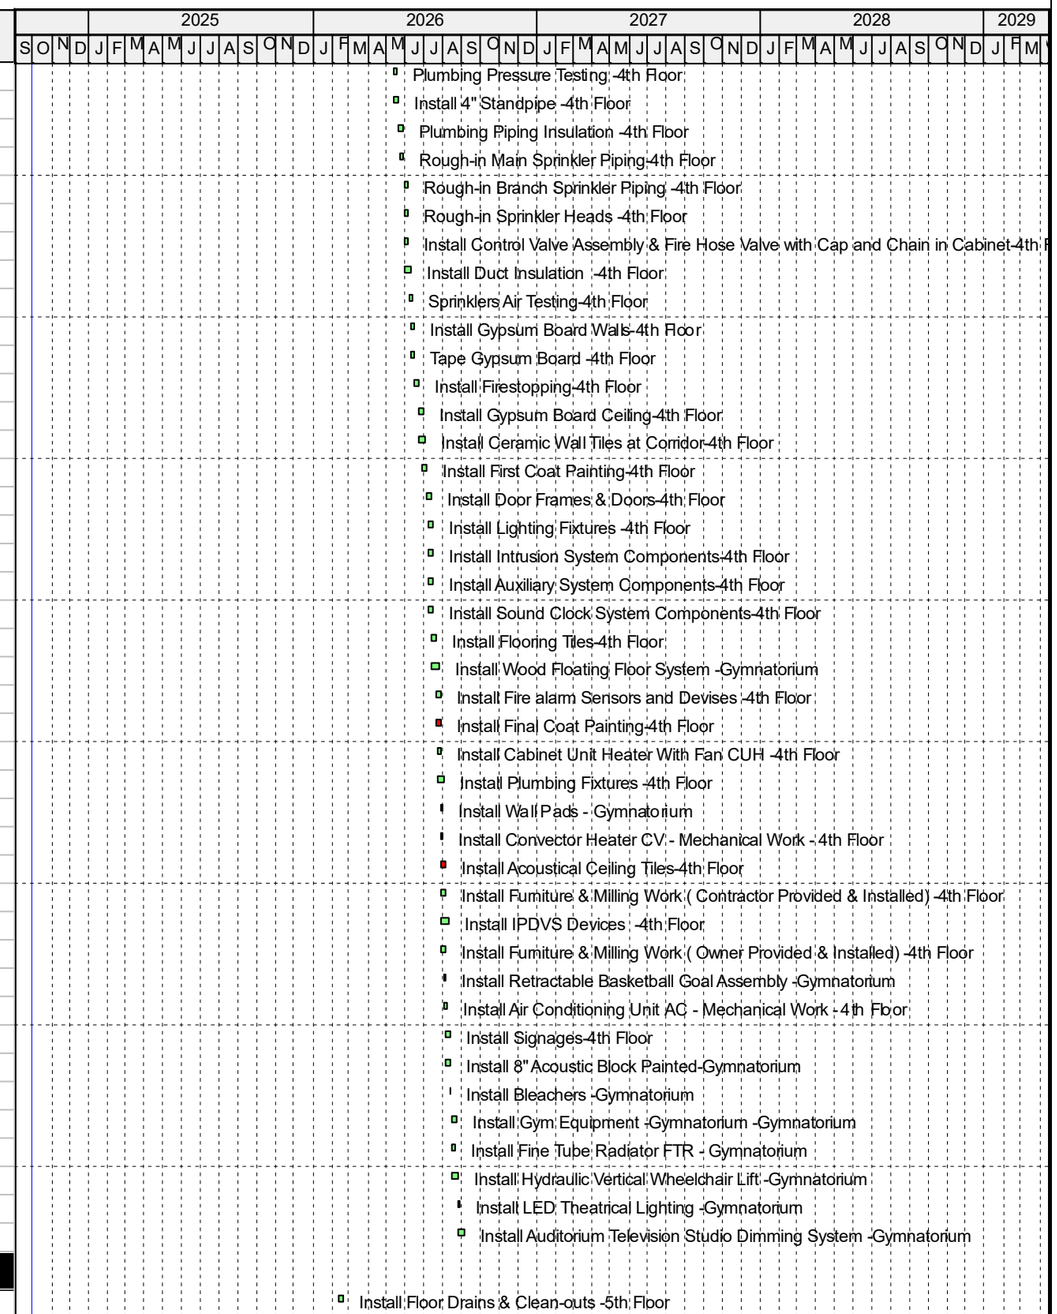

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1380	Install Metal Deck Slab - 5th Floor	3	18-Feb-26	20-Feb-26
CON-1440	Install Steel Columns - 5th Floor	3	23-Feb-26	25-Feb-26
CON-1460	F/R/P Piers - 5th Floor	5	23-Feb-26	27-Feb-26
CON-1540	Install Trusses - 5th Floor	2	26-Feb-26	27-Feb-26
CON-1550	Install Framing Beams - 5th Floor	3	26-Feb-26	02-Mar-26
CON-1610	Install MEP Hangers & Sleeves-Roof Floor	4	27-Feb-26	04-Mar-26
CON-99317	Install Steel Stairs - 5th Floor	3	27-Feb-26	03-Mar-26
CON-1630	Install Duct Risers-5th Floor	2	02-Mar-26	03-Mar-26
CON-1790	Install Mechanical Piping Risers-5th Floor	2	04-Mar-26	05-Mar-26
CON-1810	Duct Leak Test -5th Floor	1	04-Mar-26	04-Mar-26
CON-1930	Layout -5th Floor	3	06-Mar-26	10-Mar-26
CON-1940	Install Plumbing Risers-5th Floor	1	06-Mar-26	06-Mar-26
CON-2000	Install SSDS Risers -SSDS System -5th Floor	1	09-Mar-26	09-Mar-26
CON-2050	Install Power Risers-5th Floor	3	10-Mar-26	12-Mar-26
CON-2030	Install CMU Walls -5th Floor	3	13-Mar-26	17-Mar-26
CON-2100	Install Low Voltage Risers-5th Floor	3	13-Mar-26	17-Mar-26
CON-99337	Install Lightning Protection system -5th Floor	3	13-Mar-26	17-Mar-26
CON-2300	Rough-in Duct Work-5th Floor	5	16-Mar-26	20-Mar-26
CON-2020	Install Top & Bottom Track-5th Floor	4	16-Mar-26	19-Mar-26
CON-2470	Rough-in Refrigerant Piping-5th Floor	7	23-Mar-26	31-Mar-26
CON-2200	Install Wall Steel Studs & Framing-5th Floor	5	23-Mar-26	27-Mar-26
CON-2440	Rough-in Hot Water Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-2450	Rough-in Hot Glycol Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-2460	Rough-in Chilled Glycol Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-1730	Spray Fireproofing - 5th Floor	3	31-Mar-26	02-Apr-26
CON-2620	Install Ceiling Hangers & Supports-5th Floor	4	01-Apr-26	06-Apr-26
CON-2680	Rough-in Power Conduits -5th Floor	6	06-Apr-26	13-Apr-26
CON-2920	Pour Sloped Concrete Fill -5th Floor Roof	2	07-Apr-26	08-Apr-26
CON-4330	Install VAV Boxes & Sound Attenuator Devices-5th Floor	5	09-Apr-26	15-Apr-26
CON-3210	Install Fluid-Applied Protected Membrane Mock-Up	2	13-Apr-26	14-Apr-26
CON-2950	Rough-in Low-Voltage Conduits-5th Floor	6	14-Apr-26	21-Apr-26
CON-2960	Power Wires Pulling-5th Floor	6	14-Apr-26	21-Apr-26
CON-3300	Approve Fluid-Applied Protected Membrane Mock-Up	4	15-Apr-26	20-Apr-26
CON-3440	Install Hot Fluid Applied Membrane -5th Floor Roof	4	21-Apr-26	24-Apr-26
CON-3050	Rough-in Gas Risers & Piping -5th Floor	4	22-Apr-26	27-Apr-26
CON-3290	Low Voltage Wires Pulling-5th Floor	6	23-Apr-26	30-Apr-26
CON-3580	Install 6" Thick Rigid Insulation -5th Floor Roof	3	27-Apr-26	29-Apr-26
CON-3190	Rough-in Domestic Water Piping -5th Floor	4	28-Apr-26	01-May-26
CON-3700	Install Drainage -5th Floor Roof	3	30-Apr-26	04-May-26
CON-3710	Roof Flood Test -5th Floor Roof	4	30-Apr-26	05-May-26
CON-3340	Rough-in Sanitary & Vent Piping -5th Floor	4	04-May-26	07-May-26
CON-3400	Install Hot Water Circulation Pump -5th Floor	5	04-May-26	08-May-26
CON-3410	Install Electric Hot Water Heater (EWH-1) -5th Floor	5	04-May-26	08-May-26
CON-9100	In-Wall Inspections -5th Floor	7	04-May-26	12-May-26

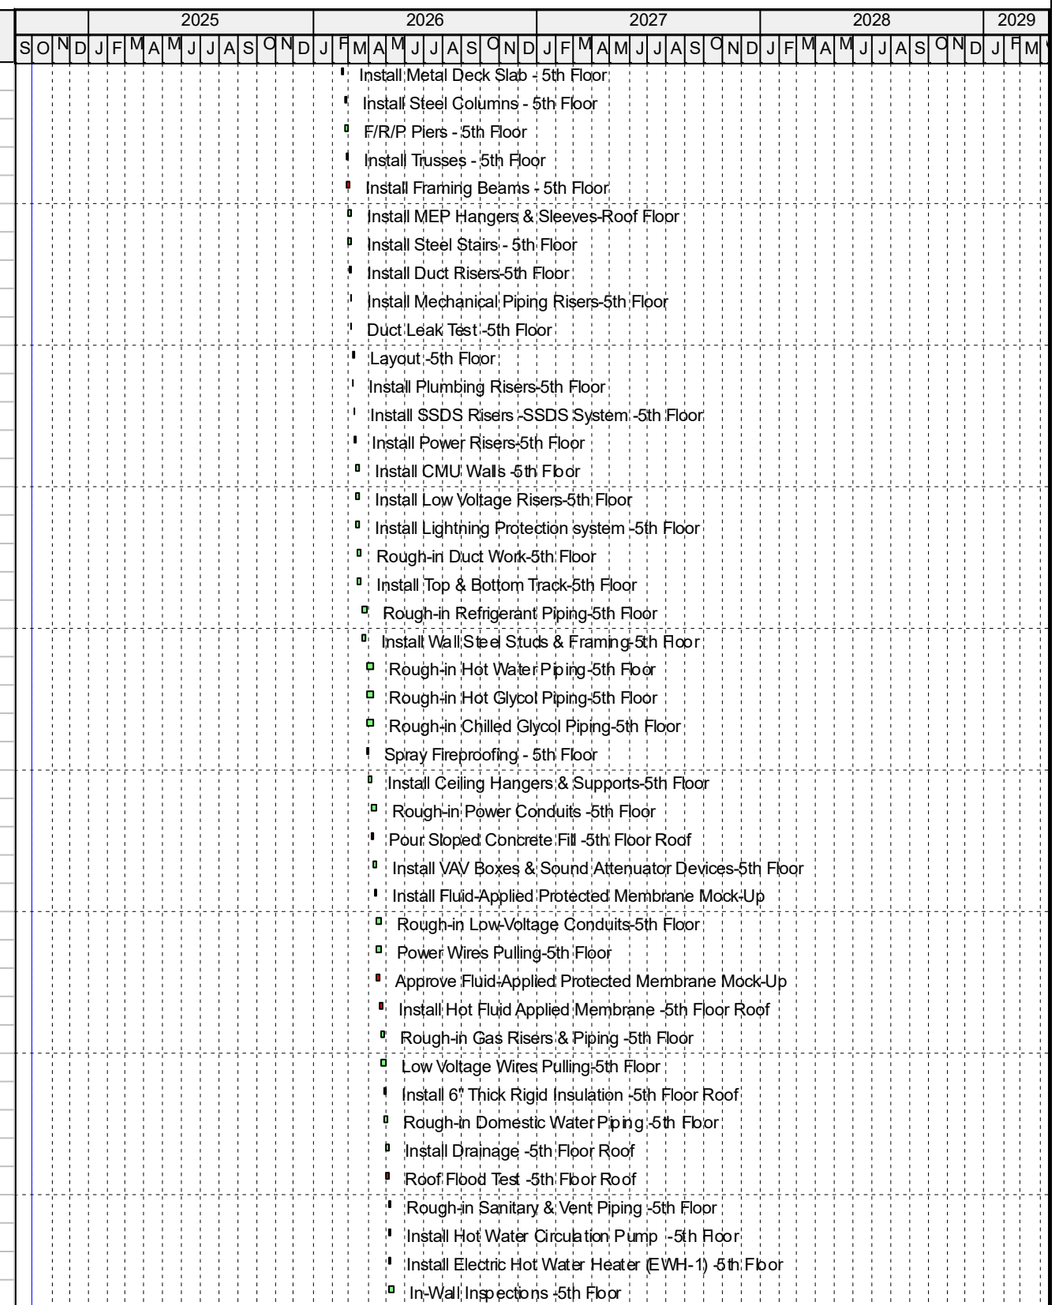

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3660	Install Wiring Devices -5th Floor	8	05-May-26	14-May-26
CON-3820	Install Filter Fabric -5th Floor Roof	3	06-May-26	08-May-26
CON-3640	Install Electric Unit Heaters -5th Floor	3	07-May-26	11-May-26
CON-3540	Rough-in Storm Piping -5th Floor	4	08-May-26	13-May-26
CON-3960	Install Concrete Pavers -5th Floor Roof	3	11-May-26	13-May-26
CON-3590	Plumbing Pressure Testing -5th Floor	5	14-May-26	20-May-26
CON-3770	Install 4" Standpipe -5th Floor	4	20-May-26	26-May-26
CON-4530	Plumbing Piping Insulation -5th Floor	5	29-May-26	04-Jun-26
CON-4010	Rough-in Main Sprinkler Piping -5th Floor	5	01-Jun-26	05-Jun-26
CON-4230	Rough-in Branch Sprinkler Piping -5th Floor	5	08-Jun-26	12-Jun-26
CON-4240	Rough-in Sprinkler Heads -5th Floor	5	08-Jun-26	12-Jun-26
CON-4340	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -5th Floor	5	08-Jun-26	12-Jun-26
CON-4710	Install Duct Insulation -5th Floor	8	11-Jun-26	23-Jun-26
CON-4490	Sprinklers Air Testing-5th Floor	5	15-Jun-26	22-Jun-26
CON-4810	Install Gypsum Board Walls-5th Floor	5	17-Jun-26	24-Jun-26
CON-4970	Tape Gypsum Board -5th Floor	4	18-Jun-26	24-Jun-26
CON-5220	Install Firestopping-5th Floor	4	23-Jun-26	26-Jun-26
CON-5100	Install Gypsum Board Ceiling-5th Floor	6	30-Jun-26	08-Jul-26
CON-5080	Install Ceramic Wall Tiles at Corridor-5th Floor	7	06-Jul-26	14-Jul-26
CON-5770	Install Air Cooled Condensing Unit ACCU - Mechanical Work - 5th Floor	5	08-Jul-26	14-Jul-26
CON-5530	Install First Coat Painting -5th Floor	5	09-Jul-26	15-Jul-26
CON-5960	F/R/P Concert Pad -Boiler Room	3	15-Jul-26	17-Jul-26
CON-5680	Install Door Frames & Doors -5th Floor	5	16-Jul-26	22-Jul-26
CON-5740	Install Lighting Fixtures -5th Floor	6	16-Jul-26	23-Jul-26
CON-98827	Install Intrusion System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-98877	Install Auxiliary System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-98927	Install Sound Clock System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-6000	Rough-in Conduits & Wires-Boiler Room	3	20-Jul-26	22-Jul-26
CON-6050	Install Boiler B-1-Boiler Room	5	23-Jul-26	29-Jul-26
CON-5890	Install Flooring Tiles -5th Floor	5	23-Jul-26	29-Jul-26
CON-5430	Install Hot Glycol / Hot Water Cabinet Heater (CUH)-5th Floor	4	29-Jul-26	03-Aug-26
CON-5830	Install Fire alarm Sensors and Devises -5th Floor	5	29-Jul-26	04-Aug-26
CON-6110	Install Boiler B-2-Boiler Room	5	30-Jul-26	05-Aug-26
CON-6120	Install Air Separator Units (AS-1 , AS-2 & AS-3)	2	30-Jul-26	31-Jul-26
CON-6130	Install Boiler Condensate ACID Neutralization Tubes -Boiler Room	2	30-Jul-26	31-Jul-26
CON-6200	Install Expansion Tanks (ET-1 , ET-2 & ET-3)	2	03-Aug-26	04-Aug-26
CON-6210	Install Glycol Make-up Units (GF-1 & GF-2 & GF-3)	2	03-Aug-26	04-Aug-26
CON-6220	Install Reduced Pressure Zone (RPZ) Devices -Boiler Room	2	03-Aug-26	04-Aug-26
CON-6090	Install Plumbing Fixtures -5th Floor	7	04-Aug-26	12-Aug-26
CON-5590	Install Exhaust Fan EF - Mechanical Work - 5th Floor	4	04-Aug-26	07-Aug-26
CON-6260	Install Heat Exchanger -Boiler Room	2	06-Aug-26	07-Aug-26
CON-5670	Install Acoustical Ceiling Tiles-5th Floor	5	06-Aug-26	12-Aug-26
CON-6290	Install Hot Glycol Units Heaters (UH-5-1, UH-5-2)	2	10-Aug-26	11-Aug-26
CON-5630	Install Convector Heater CV - Mechanical Work - 5th Floor	3	10-Aug-26	12-Aug-26

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
CON-6330	Install Heat Pump Electric Hot Water Heater (HPWH#1&2)-Boiler Room	2	12-Aug-26	13-Aug-26
CON-6010	Install IPDVS Devices -5th Floor	9	12-Aug-26	24-Aug-26
CON-6060	Install Final Coat Painting -5th Floor	6	13-Aug-26	20-Aug-26
CON-6340	Install Exhaust Fans -Boiler Room	2	14-Aug-26	17-Aug-26
CON-6350	Install Primary Hot Water Pump (GHWP 1 to 3) -Boiler Room	2	14-Aug-26	17-Aug-26
CON-6360	Install Primary Chilled Water Pump (GCHWP-1&2)-Boiler Room	2	14-Aug-26	17-Aug-26
CON-6400	Install Secondary Hot Water Pump(HWP-1&2)-Boiler Room	2	18-Aug-26	19-Aug-26
CON-6410	Install Electric Unit Heater (EUH-3) - Boiler Room	2	18-Aug-26	19-Aug-26
CON-6420	Install Branch Panels (BRPP) -Boiler Room	2	18-Aug-26	19-Aug-26
CON-6150	Install Furniture & Milling Work (Contractor Provided & Installed) -5th Floor	4	21-Aug-26	26-Aug-26
CON-9060	Install Furniture & Milling Work (Owner Provided & Installed) -5th Floor	4	21-Aug-26	26-Aug-26
CON-6280	Install Signages- 5th Floor	5	27-Aug-26	02-Sep-26
Roof		111	26-Feb-26	04-Aug-26
CON-1770	Install Roof Drains & Clean outs -Roof Floor	5	26-Feb-26	04-Mar-26
CON-1620	Install Dunnage - 5th Floor	8	02-Mar-26	11-Mar-26
CON-1720	Install Metal Deck Slab -Roof Floor	2	03-Mar-26	04-Mar-26
CON-1760	Install Dunnage-Roof Floor	8	05-Mar-26	16-Mar-26
CON-99347	Install Lightning Protection System - Roof Floor	6	05-Mar-26	12-Mar-26
CON-3010	Pour Sloped Concrete Fill -Roof Floor	2	09-Apr-26	10-Apr-26
CON-3430	Install Hot Fluid Applied Membrane -Roof Floor	3	21-Apr-26	23-Apr-26
CON-3600	Install Drainage Panels- Roof Floor	3	24-Apr-26	28-Apr-26
CON-3730	Install 6" Thick Rigid Insulation -Roof Floor	3	29-Apr-26	01-May-26
CON-3840	Roof Flood Test -Roof Floor	3	04-May-26	06-May-26
CON-4020	Install Filter Fabric -Roof Floor	3	07-May-26	11-May-26
MIL-1760	Start Elevator Work	0	07-May-26	
CON-99357	Install CMU Wall for Shaft -Elevator Machine Room	10	07-May-26	20-May-26
CON-4210	Install Concrete Pavers -Roof Floor	4	12-May-26	15-May-26
CON-99167	Install Elevator Guide Rails -Elevator Machine Room	8	21-May-26	02-Jun-26
CON-3890	Install 4" Standpipe -Roof	4	27-May-26	01-Jun-26
CON-2090	Install Elevator Controller #1 -Elevator Machine Room	10	03-Jun-26	16-Jun-26
CON-2250	Install Air Handling Unit AHU-1 -Roof Floor	5	08-Jun-26	12-Jun-26
CON-4250	Rough-in Main Sprinkler Piping -Roof	5	08-Jun-26	12-Jun-26
CON-4430	Rough-in Branch Sprinkler Piping -Roof	5	15-Jun-26	22-Jun-26
CON-4440	Rough-in Sprinkler Heads -Roof	5	15-Jun-26	22-Jun-26
CON-2370	Install Elevator Controller #2 -Elevator Machine Room	10	17-Jun-26	01-Jul-26
CON-2560	Install Air Handling Unit AHU-3 -Roof Floor	5	23-Jun-26	29-Jun-26
CON-4650	Install 3 Way Roof Manifold -Roof	5	23-Jun-26	29-Jun-26
CON-2720	Install Air Handling Unit AHU-4 -Roof Floor	5	30-Jun-26	07-Jul-26
CON-2580	Install Power Panels -Elevator Machine Room	7	02-Jul-26	13-Jul-26
CON-2860	Install Fume Hood Exhaust -Roof Floor	3	08-Jul-26	10-Jul-26
CON-3000	Install Smoke Purge Fan -Roof Floor	3	13-Jul-26	15-Jul-26
CON-2790	Rough-in Conduits & Wires-Elevator Machine Room	6	14-Jul-26	21-Jul-26
CON-99157	Install Elevator Sump Pump -Elevator Machine Room	10	14-Jul-26	27-Jul-26
CON-3750	Install Emergency Generator- Roof Floor	4	17-Jul-26	22-Jul-26

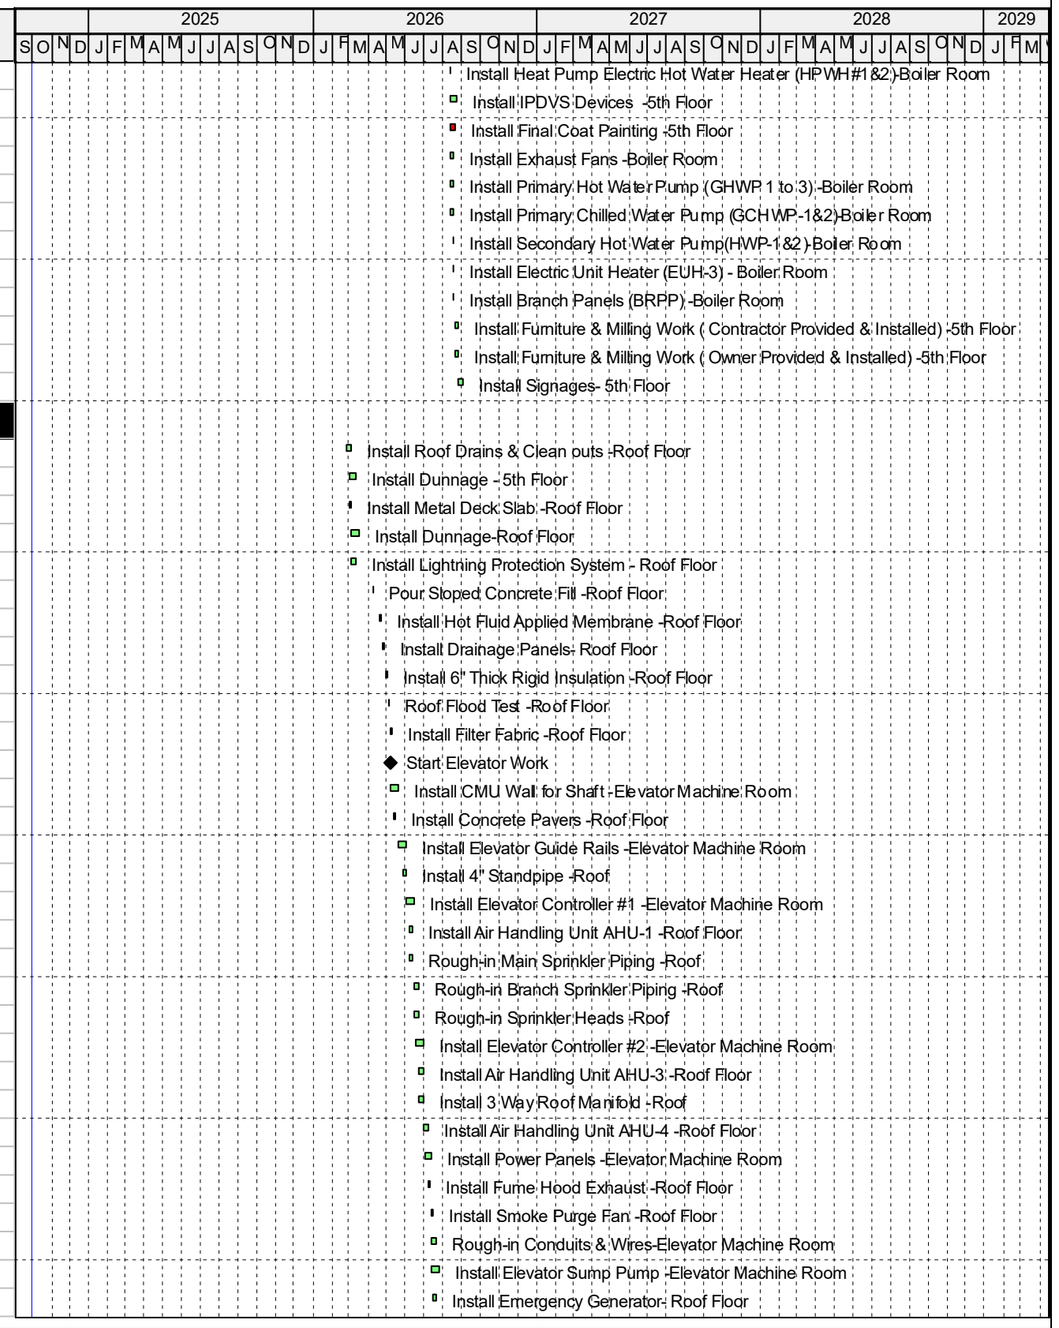

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3100	Install Elevator Cabinet (1) -Elevator Machine Room	10	22-Jul-26	04-Aug-26
CON-3620	Install Elevator Cabinet (2) -Elevator Machine Room	10	22-Jul-26	04-Aug-26
CON-5380	Install Generator Connections -Roof Floor	4	23-Jul-26	28-Jul-26
Bulkhead		76	05-Mar-26	22-Jun-26
CON-1750	F/R/P Concrete Columns -Bulkhead	3	05-Mar-26	09-Mar-26
CON-2070	Install Roof Drains & Clean outs - Mechanical Work - Roof Bulkhead	5	05-Mar-26	11-Mar-26
CON-1980	F/R/P Bulkhead Slab -Bulkhead	2	10-Mar-26	11-Mar-26
CON-2060	Install Hoist Beam-Bulkhead	1	12-Mar-26	12-Mar-26
CON-2190	Install Electric Unit Heater EUH - Mechanical Work - Roof Bulkhead	5	12-Mar-26	18-Mar-26
CON-2120	Install Air Cooled Chiller CH-1 -Roof Floor	7	17-Mar-26	25-Mar-26
CON-2230	Install Emergency Generator -Bulkhead	7	19-Mar-26	27-Mar-26
CON-2350	Install Air Cooled Chiller CH-2 -Roof Floor	7	26-Mar-26	03-Apr-26
CON-2360	Install Smoke Purge Fan SPF - Mechanical Work - Roof Bulkhead	3	26-Mar-26	30-Mar-26
CON-2430	Install Air Handling Unit AHU-2 -Roof Floor	5	15-Jun-26	22-Jun-26
West Elevation		72	29-Dec-25	10-Apr-26
MIL-1720	Start Sidewalk Bridge Installations	0	29-Dec-25	
CON-1830	Install Insulated Precast Concrete Sandwich Panel - Mock Up	2	05-Mar-26	06-Mar-26
CON-1990	Approve Insulated Precast Concrete Sandwich Panel - Mock Up	2	09-Mar-26	10-Mar-26
CON-2110	Install & Windows Mock-Up	3	11-Mar-26	13-Mar-26
CON-2210	Approve Windows Mock-Up	2	16-Mar-26	17-Mar-26
CON-2220	Install Storefront System Mock-Up	3	18-Mar-26	20-Mar-26
CON-2240	Approve Storefront System Mock-Up	2	23-Mar-26	24-Mar-26
CON-2380	Install Insulated Precast Concrete Sandwich Panel - West Elevation	3	25-Mar-26	27-Mar-26
CON-2400	Install Windows -West Elevation	5	30-Mar-26	03-Apr-26
CON-2410	Install Storefront System-West Elevation	5	30-Mar-26	03-Apr-26
MIL-1740	Start Windows	0	30-Mar-26	
CON-2570	Field Testing of Windows (5%)	5	06-Apr-26	10-Apr-26
South Elevation		86	29-Dec-25	30-Apr-26
CON-8390	Install Sidewalk Sheds -South Elevation	4	29-Dec-25	02-Jan-26
CON-2420	Install Insulated Precast Concrete Sandwich Panel - South Elevation	5	25-Mar-26	31-Mar-26
CON-2590	Install Windows - South Elevation	10	01-Apr-26	14-Apr-26
CON-2600	Install Storefront System- South Elevation	10	01-Apr-26	14-Apr-26
CON-2970	Field Testing of Windows (50%)	5	15-Apr-26	21-Apr-26
CON-99237	Install Flag Pole - South Elevation	10	15-Apr-26	28-Apr-26
CON-3220	Dismantle Sidewalk Sheds- South Elevation	2	29-Apr-26	30-Apr-26
East Elevation		89	29-Dec-25	05-May-26
CON-8400	Install Sidewalk Sheds -East Elevation	4	29-Dec-25	02-Jan-26
CON-2610	Install Insulated Precast Concrete Sandwich Panel - East Elevation	4	01-Apr-26	06-Apr-26
CON-2980	Install Windows - East Elevation	8	15-Apr-26	24-Apr-26
CON-2990	Install Storefront System- East Elevation	8	15-Apr-26	24-Apr-26
CON-3370	Field Testing of Windows (90%)	5	27-Apr-26	01-May-26
CON-3630	Dismantle Sidewalk Sheds- East Elevation	2	04-May-26	05-May-26
North Elevation		25	01-Apr-26	05-May-26

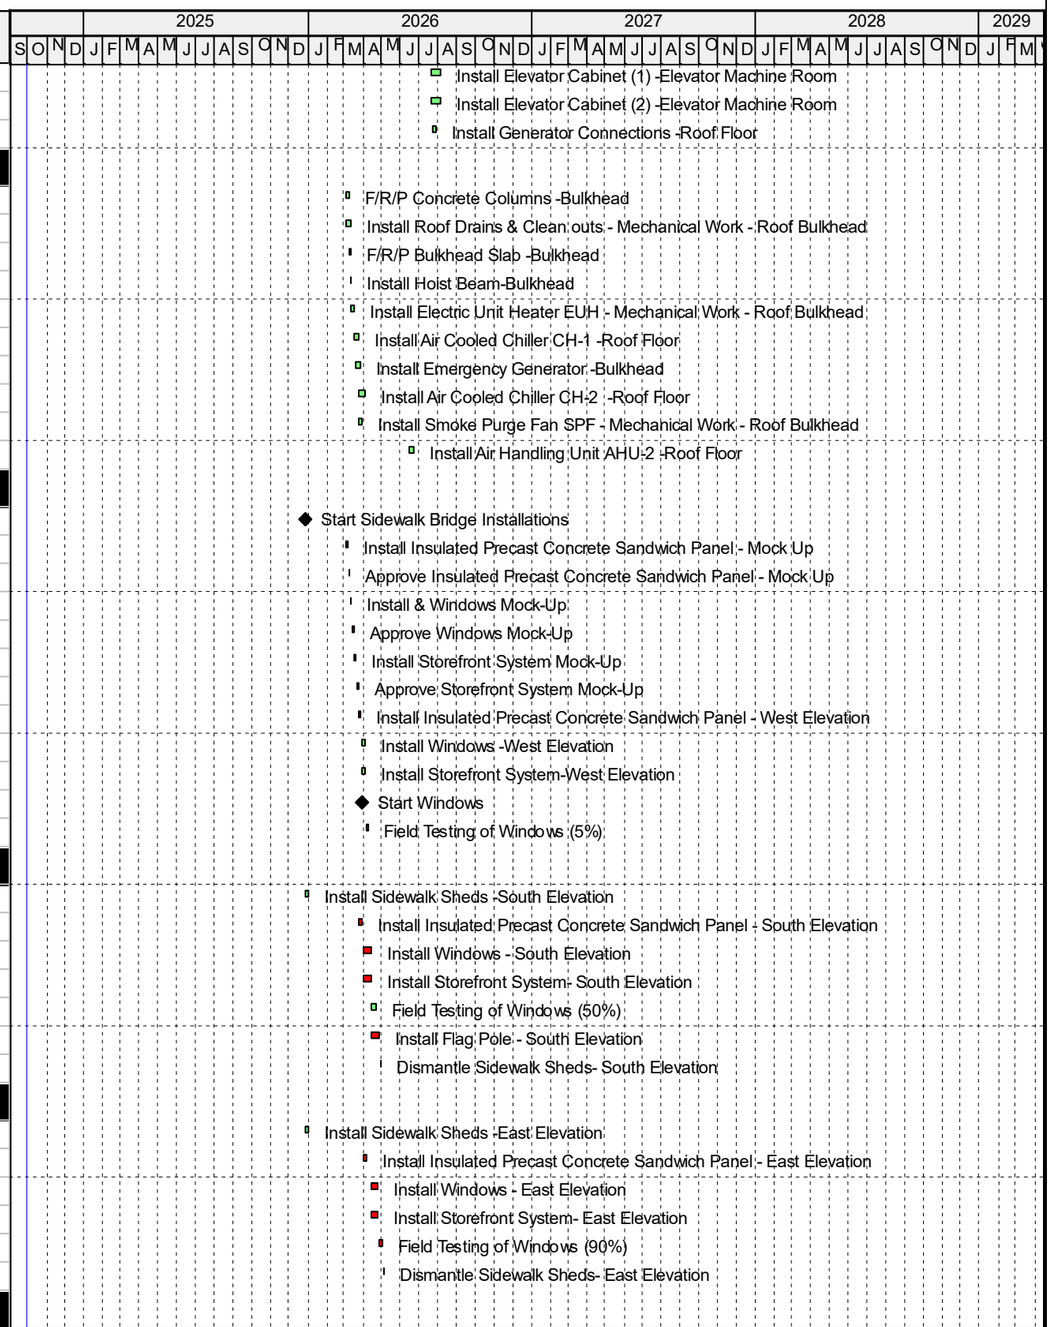

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2730	Install Insulated Precast Concrete Sandwich Panel - North Elevation	4	01-Apr-26	06-Apr-26
CON-3380	Install Windows -North Elevation	10	15-Apr-26	28-Apr-26
CON-3390	Install Storefront System-North Elevation	10	15-Apr-26	28-Apr-26
MIL-1730	Sidewalk Sheds Dismantle Complete	0		05-May-26
No P026453 - LOCN		699	30-Sep-24	15-Aug-27
MIL-1000	NTP	0	30-Sep-24	
MIL-1030	Project Duration(From NTP till TCO)	750	30-Sep-24	19-Oct-26
MIL-1040	Project Duration(From NTP till Substantial Completion)	930	30-Sep-24	17-Apr-27
PRE-2590	Meeting With SCA to Review The Permit Requirements	14	30-Sep-24	18-Oct-24
PRE-2600	Prepare & Submit Permit Waiver Requests to SCA Chief Project Officer	5	30-Sep-24	04-Oct-24
MIL-1770	Project Duration(From NTP till Final Completion)	1050	30-Sep-24	15-Aug-27
MIL-2522	Site Access	365	30-Sep-24	29-Sep-25
CON-7960	Obtain Gas Meter Layout From CON-ED	5	07-Oct-24	11-Oct-24
MIL-2542	Complete Subcontractor 'Buyout'	0		11-Oct-24
SUB-1000	Prepare & Submit Split Heat Pump System - SUB	60	15-Oct-24	10-Jan-25
SUB-1010	Prepare & Submit Thermometers	40	15-Oct-24	11-Dec-24
SUB-1020	Prepare & Submit Pressure Gages	40	15-Oct-24	11-Dec-24
SUB-1030	Prepare & Submit Floor Drains	40	15-Oct-24	11-Dec-24
SUB-1040	Prepare & Submit Hangers & Supports	40	15-Oct-24	11-Dec-24
SUB-1050	Prepare & Submit Fire & Jockey Pumps	81	15-Oct-24	11-Feb-25
SUB-1060	Prepare & Submit Interior Signage Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1070	Prepare & Submit Ceramic Tiles Product Data	81	15-Oct-24	11-Feb-25
SUB-1080	Prepare & Submit Door Hardware Submittal	81	15-Oct-24	11-Feb-25
SUB-1090	Prepare & Submit Painting	81	15-Oct-24	11-Feb-25
SUB-1100	Prepare & Submit Door & Frame Corners Samples	81	15-Oct-24	11-Feb-25
SUB-1110	Prepare & Submit Roof Drains & Clean Outs	81	15-Oct-24	11-Feb-25
SUB-1120	Prepare & Submit Flashing & Sheet Metal Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-1130	Prepare & Submit Roofing Membrane Product Data	81	15-Oct-24	11-Feb-25
SUB-1140	Prepare & Submit Perimeter Foundation Insulation Product Data	81	15-Oct-24	11-Feb-25
SUB-1150	Prepare & Submit Crystalline Waterproofing Product Data	81	15-Oct-24	11-Feb-25
SUB-1160	Prepare & Submit Suspension Assembly Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1170	Prepare & Submit Certification of Material	81	15-Oct-24	11-Feb-25
SUB-1180	Prepare & Submit Concrete Reinforcement	30	15-Oct-24	26-Nov-24
SUB-1190	Prepare & Submit Formwork Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1200	Prepare & Submit Planting Schedule	81	15-Oct-24	11-Feb-25
SUB-1210	Prepare & Submit Site Furnishings Shop Drawings	15	15-Oct-24	04-Nov-24
SUB-1220	Prepare & Submit Playgroung Equipment Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1230	Prepare & Submit Ductile Iron Pipes	37	15-Oct-24	06-Dec-24
SUB-1240	Prepare & Submit Catch Basin Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1250	Prepare & Submit Concrete Curbs & Pavements Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-1260	Prepare & Submit Steel Curb Facing Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-1270	Prepare & Submit Asphaltic Concrete Paving	81	15-Oct-24	11-Feb-25
SUB-1280	Prepare & Submit SSDS Geotextile	40	15-Oct-24	11-Dec-24
SUB-1290	Prepare & Submit Gas Vapor Barrier Submittal & Inspection Schedule	81	15-Oct-24	11-Feb-25

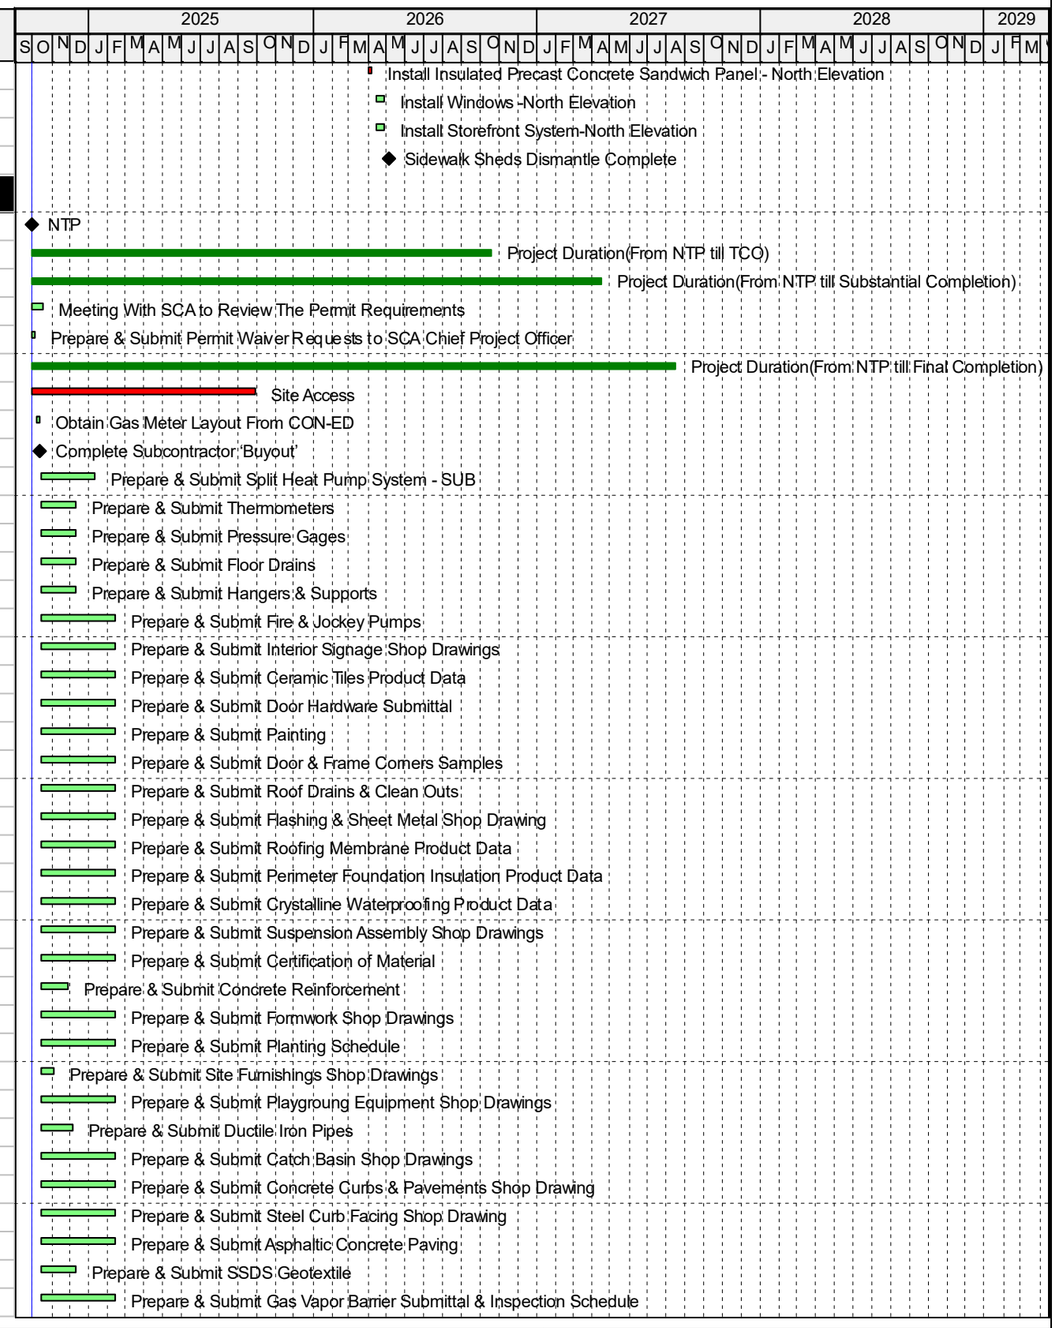

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1300	Prepare & Submit Existing Conditions Survey	10	15-Oct-24	28-Oct-24
SUB-1310	Prepare & Submit Training Outline & Schedule	81	15-Oct-24	11-Feb-25
SUB-1320	Prepare & Submit Product Substitutions	82	15-Oct-24	12-Feb-25
SUB-1330	Prepare & Submit Temporary Ventilation Plan	81	15-Oct-24	11-Feb-25
SUB-1340	Prepare & Submit Construction Indoor Air Quality Management Plan	81	15-Oct-24	11-Feb-25
SUB-1350	Prepare & Submit Site Safety Plan	2	15-Oct-24	16-Oct-24
SUB-1360	Prepare & Submit CWM Plan	81	15-Oct-24	11-Feb-25
SUB-1370	Prepare & Submit Photo Submission - Temporary Fence	15	15-Oct-24	04-Nov-24
SUB-1380	Prepare & Submit Heating Plan	81	15-Oct-24	11-Feb-25
SUB-1390	Prepare & Submit Sample Classroom Materials	81	15-Oct-24	11-Feb-25
SUB-1400	Prepare & Submit Sustainable Materials	10	15-Oct-24	28-Oct-24
SUB-1410	Prepare & Submit Submittal Schedule	60	15-Oct-24	10-Jan-25
SUB-1420	Prepare & Submit Electrical Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1430	Prepare & Submit Plumbing Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1440	Prepare & Submit Sprinkler System Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1450	Prepare & Submit Concrete Shop Drawings	30	15-Oct-24	26-Nov-24
SUB-1460	Prepare & Submit Elevator Machine	71	15-Oct-24	28-Jan-25
SUB-1470	Prepare & Submit Gypsum Board	81	15-Oct-24	11-Feb-25
SUB-1480	Prepare & Submit Floorings	81	15-Oct-24	11-Feb-25
SUB-1490	Prepare & Submit Acosutical Ceiling Tiles	60	15-Oct-24	10-Jan-25
SUB-1500	Prepare & Submit Toilet Accessories	81	15-Oct-24	11-Feb-25
SUB-1510	Prepare & Submit Millwork	81	15-Oct-24	11-Feb-25
SUB-1520	Prepare & Submit Lighting Fixtures	71	15-Oct-24	28-Jan-25
SUB-1530	Prepare & Submit Furniture	81	15-Oct-24	11-Feb-25
SUB-1540	Prepare & Submit Mechanical Ducts	81	15-Oct-24	11-Feb-25
SUB-1550	Prepare & Submit Mechanical Piping	60	15-Oct-24	10-Jan-25
SUB-1560	Prepare & Submit Erosion Control and Sedimentation Plan	7	15-Oct-24	23-Oct-24
SUB-1570	Prepare & Submit QCP	30	15-Oct-24	26-Nov-24
SUB-1580	Prepare & Submit Concrete Mix Design	30	15-Oct-24	26-Nov-24
SUB-1590	Prepare & Submit Electrical Equipment, Conduits, and Cables	20	15-Oct-24	12-Nov-24
SUB-1600	Prepare & Submit Plumbing Fixtures	81	15-Oct-24	11-Feb-25
SUB-1610	Prepare & Submit Baseline Schedule	52	15-Oct-24	30-Dec-24
SUB-1620	Prepare & Submit Wood Doors	81	15-Oct-24	11-Feb-25
SUB-1630	Prepare & Submit Fire Protection Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1640	Prepare & Submit Fire Detectors & Alarms	81	15-Oct-24	11-Feb-25
SUB-1650	Prepare & Submit Kitchen Equipment	71	15-Oct-24	28-Jan-25
SUB-1660	Prepare & Submit Signs	81	15-Oct-24	11-Feb-25
SUB-1670	Prepare & Submit Aluminum Projected Windows	71	15-Oct-24	28-Jan-25
SUB-1680	Prepare & Submit Telecommunication System Drawings	81	15-Oct-24	11-Feb-25
SUB-1690	Prepare & Submit Internet Protocol Digital Video Surveillance System using Digital Cameras	71	15-Oct-24	28-Jan-25
SUB-1710	Prepare & Submit Chillers Product Data	71	15-Oct-24	28-Jan-25
SUB-1720	Prepare & Submit Air Handling Units Product Data	71	15-Oct-24	28-Jan-25
SUB-1730	Prepare & Submit Boilers	71	15-Oct-24	28-Jan-25
SUB-1740	Prepare & Submit Emergency Generator System Product Data	71	15-Oct-24	28-Jan-25

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1750	Prepare & Submit Switch Gears Product Data	20	15-Oct-24	12-Nov-24
SUB-1760	Prepare & Submit Unit Cabinet Heaters	60	15-Oct-24	10-Jan-25
SUB-1770	Prepare & Submit Gymnasium Equipment	81	15-Oct-24	11-Feb-25
SUB-1780	Prepare & Submit Initial Underground Coordination Drawings	50	15-Oct-24	26-Dec-24
SUB-1790	Prepare & Submit Initial 1st Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1800	Prepare & Submit Initial 2nd Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1810	Prepare & Submit Initial 3rd Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1820	Prepare & Submit Initial 4th Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1830	Prepare & Submit Initial 5th Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1840	Prepare & Submit Supplemental Comissioning Requirements	81	15-Oct-24	11-Feb-25
SUB-1850	Prepare & Submit Record Documents	81	15-Oct-24	11-Feb-25
SUB-1860	Prepare & Submit Environmental Site Assessment Reports	81	15-Oct-24	11-Feb-25
SUB-1870	Prepare & Submit Selective Removals & Demoloition	81	15-Oct-24	11-Feb-25
SUB-1880	Prepare & Submit Foundation Product Data	5	15-Oct-24	21-Oct-24
SUB-1890	Prepare & Submit Trench Drains Product Data	81	15-Oct-24	11-Feb-25
SUB-1900	Prepare & Submit Chain Link Fences & Gates Drawings	81	15-Oct-24	11-Feb-25
SUB-1910	Prepare & Submit Outdoor Game Equipment	81	15-Oct-24	11-Feb-25
SUB-1920	Prepare & Submit Precast Architectural Concrete	71	15-Oct-24	28-Jan-25
SUB-1930	Prepare & Submit Unit Masonry Product Data	71	15-Oct-24	28-Jan-25
SUB-1940	Prepare & Submit Cast Stone Product Data	81	15-Oct-24	11-Feb-25
SUB-1950	Prepare & Submit Structure Steel Drawings	71	15-Oct-24	28-Jan-25
SUB-1960	Prepare & Submit Metal Deck Product Data	81	15-Oct-24	11-Feb-25
SUB-1970	Prepare & Submit Prefabricated Expansion Joint Covers	81	15-Oct-24	11-Feb-25
SUB-1980	Prepare & Submit Self Adhering Sheet Air Barriers	81	15-Oct-24	11-Feb-25
SUB-1990	Prepare & Submit Metal Plate Wall Panels	81	15-Oct-24	11-Feb-25
SUB-2000	Prepare & Submit Security Screens & Barriers	81	15-Oct-24	11-Feb-25
SUB-2010	Prepare & Submit Wood Flooring	81	15-Oct-24	11-Feb-25
SUB-2020	Prepare & Submit Visual Display Boards	81	15-Oct-24	11-Feb-25
SUB-2030	Prepare & Submit Metal Lockers	81	15-Oct-24	11-Feb-25
SUB-2040	Prepare & Submit Fire Extinguishers & Cabinets	81	15-Oct-24	11-Feb-25
SUB-2050	Prepare & Submit Stationary Metal Wall Louvers	73	15-Oct-24	30-Jan-25
SUB-2060	Prepare & Submit Library Equipment	81	15-Oct-24	11-Feb-25
SUB-2070	Prepare & Submit Platform Curtains & Auditorium Window Curtains	81	15-Oct-24	11-Feb-25
SUB-2080	Prepare & Submit Waste Handling Equipment	81	15-Oct-24	11-Feb-25
SUB-2090	Prepare & Submit Domestic Equipment	81	15-Oct-24	11-Feb-25
SUB-2100	Prepare & Submit Laboratory Equipment	81	15-Oct-24	11-Feb-25
SUB-2110	Prepare & Submit Manufactured Wood Casework	81	15-Oct-24	11-Feb-25
SUB-2120	Prepare & Submit Concrete Floating Floor Assembly	81	15-Oct-24	11-Feb-25
SUB-2130	Prepare & Submit Hydraulic Vertical Wheelchair Lifts	81	15-Oct-24	11-Feb-25
SUB-2140	Prepare & Submit Switch & Panel Boards	81	15-Oct-24	11-Feb-25
SUB-2150	Prepare & Submit Auditorium & Television Studio Dimming System Product Data	81	15-Oct-24	11-Feb-25
SUB-2160	Prepare & Submit Overcurrent Protective Devices Data	81	15-Oct-24	11-Feb-25
SUB-2170	Prepare & Submit Gas Pipes	81	15-Oct-24	11-Feb-25
SUB-2180	Prepare & Submit Water Heaters	81	15-Oct-24	11-Feb-25

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

New Building PS/IS 341Q - Baseline Schedule Rev 01

NAVILLUS BUILDING THE WORLD AROUND YOU

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-2190	Prepare & Submit Pumping Apparatus & Tanks	81	15-Oct-24	11-Feb-25
SUB-2200	Prepare & Submit HVAC Pumps	81	15-Oct-24	11-Feb-25
SUB-2210	Prepare & Submit Emergency Generator System Accessories	71	15-Oct-24	28-Jan-25
SUB-2220	Prepare & Submit Fuel Storage Equipment	81	15-Oct-24	11-Feb-25
SUB-2230	Prepare & Submit Natural Gas Leak Detection Equipment	81	15-Oct-24	11-Feb-25
SUB-2250	Prepare & Submit Temperature Control System	81	15-Oct-24	11-Feb-25
SUB-2260	Prepare & Submit Air Outlets & Inlets	81	15-Oct-24	11-Feb-25
SUB-2340	Prepare & Submit Tree Protection Plan	71	15-Oct-24	28-Jan-25
SUB-2360	Prepare & Submit Adjacent Property and Structures Protection & Monitoring Plan	81	15-Oct-24	11-Feb-25
SUB-2370	Prepare & Submit Ornamenta Metal Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2920	Prepare & Submit Documentation of Proper Disposal	81	15-Oct-24	11-Feb-25
SUB-2930	Prepare & Submit Ornamenta Metal Product Data	81	15-Oct-24	11-Feb-25
SUB-2960	Prepare & Submit Coiling Doors, Grilles and Shutters Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2970	Prepare & Submit Coiling Doors, Grilles and Shutters Product Data	81	15-Oct-24	11-Feb-25
SUB-2980	Prepare & Submit Aluminum Framed Entrances & Storefronts Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2990	Prepare & Submit Aluminum Framed Entrances & Storefronts Product Data	81	15-Oct-24	11-Feb-25
SUB-3000	Prepare & Submit Thresholds, Weatherstripping and Seals Color Samples	81	15-Oct-24	11-Feb-25
SUB-3010	Prepare & Submit Thresholds, Weatherstripping and Seals Product Data	81	15-Oct-24	11-Feb-25
SUB-3020	Prepare & Submit Miscellaneous Glazing Samples	81	15-Oct-24	11-Feb-25
SUB-3030	Prepare & Submit Miscellaneous Glazing Product Data	81	15-Oct-24	11-Feb-25
SUB-3040	Prepare & Submit Fire Rated Glazing Samples	81	15-Oct-24	11-Feb-25
SUB-3050	Prepare & Submit Fire Rated Glazing Product Data	81	15-Oct-24	11-Feb-25
SUB-3060	Prepare & Submit Graffiti Resistant Coating Product Data	81	15-Oct-24	11-Feb-25
SUB-3070	Prepare & Submit Special Coating Samples	81	15-Oct-24	11-Feb-25
SUB-3080	Prepare & Submit Special Coating Product Data	81	15-Oct-24	11-Feb-25
SUB-3090	Prepare & Submit Flagpole Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3100	Prepare & Submit Flagpole Product Data	81	15-Oct-24	11-Feb-25
SUB-3110	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals	81	15-Oct-24	11-Feb-25
SUB-3120	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-3130	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	81	15-Oct-24	11-Feb-25
SUB-3140	Prepare & Submit Wire Mesh Work Samples	81	15-Oct-24	11-Feb-25
SUB-3150	Prepare & Submit Wire Mesh Work Shop drawings	81	15-Oct-24	11-Feb-25
SUB-3160	Prepare & Submit Metal Storage Shelving Samples	81	15-Oct-24	11-Feb-25
SUB-3170	Prepare & Submit Metal Storage Shelving Shop drawings	81	15-Oct-24	11-Feb-25
SUB-3180	Prepare & Submit Mirrors Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3190	Prepare & Submit Mirrors Product Data	81	15-Oct-24	11-Feb-25
SUB-3200	Prepare & Submit Mirrors Mastic Compatibility Test Reports & Certifications	81	15-Oct-24	11-Feb-25
SUB-3210	Prepare & Submit Grab Bars Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3220	Prepare & Submit Grab Bars Product Data	81	15-Oct-24	11-Feb-25
SUB-3230	Prepare & Submit Shop Equipment Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3240	Prepare & Submit Shop Equipment Product Data	81	15-Oct-24	11-Feb-25
SUB-3250	Prepare & Submit Bleachers Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3260	Prepare & Submit Bleachers Product Data	81	15-Oct-24	11-Feb-25
SUB-3270	Prepare & Submit Bleachers Manufacturer's Warranty	81	15-Oct-24	11-Feb-25

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-3280	Prepare & Submit Valves Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3290	Prepare & Submit Valves Product Data	81	15-Oct-24	11-Feb-25
SUB-3300	Prepare & Submit Certification of Tests	81	15-Oct-24	11-Feb-25
SUB-3310	Prepare & Submit Domestic Water Sterilization Plan	81	15-Oct-24	11-Feb-25
SUB-3320	Prepare & Submit Tags, Charts & Identifications Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3330	Prepare & Submit Tags, Charts & Identifications Product Data	81	15-Oct-24	11-Feb-25
SUB-3340	Prepare & Submit Micselianeous Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3350	Prepare & Submit Valves (HVAC) Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3360	Prepare & Submit Valves (HVAC) Product Data	81	15-Oct-24	11-Feb-25
SUB-3370	Prepare & Submit Piping Insulation Schedule Listing Items	81	15-Oct-24	11-Feb-25
SUB-3380	Prepare & Submit Schedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	81	15-Oct-24	11-Feb-25
SUB-3390	Prepare & Submit Schedules Showing Manfacturers's Product Number Duct Work Insulation	81	15-Oct-24	11-Feb-25
SUB-3400	Prepare & Submit Hydronic Specialities Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3410	Prepare & Submit Hydronic Specialities Product Data	81	15-Oct-24	11-Feb-25
SUB-3420	Prepare & Submit Water Treatment Firm	81	15-Oct-24	11-Feb-25
SUB-3430	Prepare & Submit Chemical Products Product Data	81	15-Oct-24	11-Feb-25
SUB-3440	Prepare & Submit Detail of Gag for the Safety Relief Valves	71	15-Oct-24	28-Jan-25
SUB-3450	Prepare & Submit Boiler Accessories Maintenance Data	71	15-Oct-24	28-Jan-25
SUB-3460	Prepare & Submit Breeching Chimney Connectors and Chimneys Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3470	Prepare & Submit Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	81	15-Oct-24	11-Feb-25
SUB-3480	Prepare & Submit Plate Heat Exchanger Maintenance Data	81	15-Oct-24	11-Feb-25
SUB-3490	Prepare & Submit Plate Heat Exchanger Product Data	81	15-Oct-24	11-Feb-25
SUB-3500	Prepare & Submit Coils Maintenance Data	81	15-Oct-24	11-Feb-25
SUB-3510	Prepare & Submit Coils Certifications	81	15-Oct-24	11-Feb-25
SUB-3520	Prepare & Submit Convectors Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3530	Prepare & Submit Convectors Product Data	81	15-Oct-24	11-Feb-25
SUB-3540	Prepare & Submit Fan Coils Units Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3550	Prepare & Submit Fan Coils Units Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-3560	Prepare & Submit Door Air Curtains Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3570	Prepare & Submit Door Air Curtains Product Data	81	15-Oct-24	11-Feb-25
SUB-3580	Prepare & Submit Centrifugal Fans Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3590	Prepare & Submit Centrifugal Fans Product Data	81	15-Oct-24	11-Feb-25
SUB-3600	Prepare & Submit Centrifugal Fans Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3610	Prepare & Submit Air Filters Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3620	Prepare & Submit Air Filters Product Data	81	15-Oct-24	11-Feb-25
SUB-3630	Prepare & Submit Air Filters Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3640	Prepare & Submit Duct Accessories Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3650	Prepare & Submit Damper Assemblies Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3660	Prepare & Submit Damper Assemblies Product Data	81	15-Oct-24	11-Feb-25
SUB-3670	Prepare & Submit Damper Assemblies Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3680	Prepare & Submit Variable Air Terminals Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3690	Prepare & Submit Variable Air Terminals Product Data	81	15-Oct-24	11-Feb-25
SUB-3700	Prepare & Submit Variable Air Terminals Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3710	Prepare & Submit AHU for Public Assemblies Sapces Shop Drawing	81	15-Oct-24	11-Feb-25

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-3720	Prepare & Submit AHU for Public Assemblies Sapces Product Data	81	15-Oct-24	11-Feb-25
SUB-3730	Prepare & Submit AHU for Public Assemblies Sapces Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3740	Prepare & Submit Control Systems Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3750	Prepare & Submit Truck Network Cable Schematic Diagram	81	15-Oct-24	11-Feb-25
SUB-3760	Prepare & Submit Lighting Control Devices Shop Drawing	71	15-Oct-24	28-Jan-25
SUB-3770	Prepare & Submit Lighting Control Devices Product Data	71	15-Oct-24	28-Jan-25
SUB-3780	Prepare & Submit Lighting Control Devices Warranty	71	15-Oct-24	28-Jan-25
SUB-3790	Prepare & Submit Surge Protective Devices Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3800	Prepare & Submit Surge Protective Devices Product Data	81	15-Oct-24	11-Feb-25
SUB-3810	Prepare & Submit Surge Protective Devices Warranty	81	15-Oct-24	11-Feb-25
SUB-3820	Prepare & Submit Service Entrance Equipment Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3830	Prepare & Submit Service Entrance Equipment Product Data	81	15-Oct-24	11-Feb-25
SUB-3840	Prepare & Submit Service Entrance Equipment Warranty	81	15-Oct-24	11-Feb-25
SUB-3850	Prepare & Submit Enclosed Switches Product Data	81	15-Oct-24	11-Feb-25
SUB-3860	Prepare & Submit Enclosed Switches Test Reports	81	15-Oct-24	11-Feb-25
SUB-3870	Prepare & Submit Motors, Motor Control Centers and Starters Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3880	Prepare & Submit Motors, Motor Control Centers and Starters Product Data	81	15-Oct-24	11-Feb-25
SUB-3890	Prepare & Submit Motors, Motor Control Centers and Starters Field Test Reports	81	15-Oct-24	11-Feb-25
SUB-3900	Prepare & Submit Lightning Protection Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3920	Prepare & Submit Lightning Protection Test Reports	81	15-Oct-24	11-Feb-25
SUB-3930	Prepare & Submit Fiber Optic Cabling system Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3940	Prepare & Submit Fiber Optic Cabling system Product Data	81	15-Oct-24	11-Feb-25
SUB-3950	Prepare & Submit Fiber Optic Cabling system Samples	81	15-Oct-24	11-Feb-25
SUB-3960	Prepare & Submit Sound, Intercome & Security System Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3970	Prepare & Submit Sound, Intercome & Security System Programming Code and Password for the System	81	15-Oct-24	11-Feb-25
SUB-3980	Prepare & Submit Sound, Intercome & Security System Warranty	81	15-Oct-24	11-Feb-25
SUB-3990	Prepare & Submit Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	81	15-Oct-24	11-Feb-25
SUB-4000	Prepare & Submit Projection and Interactive Whiteboard Systems Wiring diagram	81	15-Oct-24	11-Feb-25
SUB-4010	Prepare & Submit Self Corrective Clock System Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-4020	Prepare & Submit Self Corrective Clock System Product Data	81	15-Oct-24	11-Feb-25
SUB-4030	Prepare & Submit Self Corrective Clock System Field Test Reports	81	15-Oct-24	11-Feb-25
SUB-4040	Prepare & Submit Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	81	15-Oct-24	11-Feb-25
SUB-4060	Prepare & Submit Steel Stairs Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-4070	Prepare & Submit Steel Stairs Product Data	81	15-Oct-24	11-Feb-25
SUB-4080	Prepare & Submit Green School Submittal	81	15-Oct-24	11-Feb-25
APP-1000	Review & Approve Site Safety Plan	21	17-Oct-24	06-Nov-24
APP-1010	Review & Approve Foundation Product Data	21	22-Oct-24	11-Nov-24
APP-1020	Review & Approve Erosion Control and Sedimentation Plan	21	24-Oct-24	13-Nov-24
APP-1030	Review & Approve Existing Conditions Survey	21	29-Oct-24	18-Nov-24
APP-1040	Review & Approve Sustainable Materials	21	29-Oct-24	18-Nov-24
APP-1050	Review & Approve Site Furnishings Shop Drawings	21	05-Nov-24	25-Nov-24
APP-1060	Review & Approve Photo Submission - Temporary Fence	21	05-Nov-24	25-Nov-24
CON-8010	Coordination With CON-ED For Temporary Electrical Power	10	07-Nov-24	21-Nov-24
APP-1080	Review & Approve Electrical Equipment, Conduits, and Cables	21	13-Nov-24	03-Dec-24

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1090	Review & Approve Switch Gears Product Data	21	13-Nov-24	03-Dec-24
CON-8020	Scheduling With CON-ED For Temporary Electrical Power	7	22-Nov-24	03-Dec-24
APP-1100	Review & Approve Concrete Reinforcement	21	27-Nov-24	17-Dec-24
APP-1110	Review & Approve Concrete Shop Drawings	21	27-Nov-24	17-Dec-24
APP-1130	Review & Approve QCP	21	27-Nov-24	17-Dec-24
APP-1140	Review & Approve Concrete Mix Design	21	27-Nov-24	17-Dec-24
APP-1150	Review & Approve Ductile Iron Pipes	21	07-Dec-24	27-Dec-24
APP-1160	Review & Approve Thermometers	21	12-Dec-24	01-Jan-25
APP-1170	Review & Approve Pressure Gages	21	12-Dec-24	01-Jan-25
APP-1180	Review & Approve Floor Drains	21	12-Dec-24	01-Jan-25
APP-1190	Review & Approve Hangers & Supports	21	12-Dec-24	01-Jan-25
APP-1200	Review & Approve SSDS Geotextile	21	12-Dec-24	01-Jan-25
APP-1230	Review & Approve Initial Underground Coordination Drawings	21	27-Dec-24	16-Jan-25
APP-1240	Review & Approve Baseline Schedule	21	31-Dec-24	20-Jan-25
APP-1250	Review & Approve Split Heat Pump System - SUB	21	11-Jan-25	31-Jan-25
APP-1260	Review & Approve Submittal Schedule	21	11-Jan-25	31-Jan-25
APP-1270	Review & Approve Acosutical Ceiling Tiles	21	11-Jan-25	31-Jan-25
APP-1280	Review & Approve Mechanical Piping	21	11-Jan-25	31-Jan-25
APP-1290	Review & Approve Unit Cabinet Heaters	21	11-Jan-25	31-Jan-25
SUB-2270	Prepare & Submit Final Underground Coordination Drawings	37	17-Jan-25	11-Mar-25
APP-1210	Review & Approve Elevator Machine	21	29-Jan-25	18-Feb-25
APP-1120	Review & Approve Lighting Fixtures	21	29-Jan-25	18-Feb-25
APP-1780	Review & Approve Kitchen Equipment	21	29-Jan-25	18-Feb-25
APP-1310	Review & Approve Aluminum Projected Windows	21	29-Jan-25	18-Feb-25
APP-1220	Review & Approve Internet Protocol Digital Video Surveillance System using Digital Cameras	35	29-Jan-25	04-Mar-25
APP-1820	Review & Approve Chillers Product Data	21	29-Jan-25	18-Feb-25
APP-1300	Review & Approve Air Handling Units Product Data	21	29-Jan-25	18-Feb-25
APP-1830	Review & Approve Boilers	21	29-Jan-25	18-Feb-25
APP-1070	Review & Approve Emergency Generator System Product Data	21	29-Jan-25	18-Feb-25
APP-1920	Review & Approve Precast Architectural Concrete	21	29-Jan-25	18-Feb-25
APP-1930	Review & Approve Unit Masonry Product Data	21	29-Jan-25	18-Feb-25
APP-1950	Review & Approve Structure Steel Drawings	21	29-Jan-25	18-Feb-25
APP-2200	Review & Approve Emergency Generator System Accessories	21	29-Jan-25	18-Feb-25
APP-2340	Review & Approve Tree Protection Plan	21	29-Jan-25	18-Feb-25
APP-3440	Review & Approve Detail of Gag for the Safety Relief Valves	21	29-Jan-25	18-Feb-25
APP-3450	Review & Approve Boiler Accessories Maintenance Data	21	29-Jan-25	18-Feb-25
APP-3760	Review & Approve Lighting Control Devices Shop Drawing	21	29-Jan-25	18-Feb-25
APP-3770	Review & Approve Lighting Control Devices Product Data	21	29-Jan-25	18-Feb-25
APP-3780	Review & Approve Lighting Control Devices Warranty	21	29-Jan-25	18-Feb-25
APP-1320	Review & Approve Stationary Metal Wall Louvers	21	31-Jan-25	20-Feb-25
APP-1330	Review & Approve Initial 1st Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1340	Review & Approve Initial 2nd Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1350	Review & Approve Initial 3rd Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1360	Review & Approve Initial 4th Floor Coordination Drawings	21	04-Feb-25	24-Feb-25

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1370	Review & Approve Initial 5th Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1380	Review & Approve Fire & Jockey Pumps	21	12-Feb-25	04-Mar-25
APP-1390	Review & Approve Interior Signage Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1400	Review & Approve Ceramic Tiles Product Data	21	12-Feb-25	04-Mar-25
APP-1410	Review & Approve Door Hardware Submittal	21	12-Feb-25	04-Mar-25
APP-1420	Review & Approve Painting	21	12-Feb-25	04-Mar-25
APP-1430	Review & Approve Door & Frame Corners Samples	21	12-Feb-25	04-Mar-25
APP-1440	Review & Approve Roof Drains & Clean Outs	21	12-Feb-25	04-Mar-25
APP-1450	Review & Approve Flashing & Sheet Metal Shop Drawing	21	12-Feb-25	04-Mar-25
APP-1460	Review & Approve Roofing Membrane Product Data	21	12-Feb-25	04-Mar-25
APP-1470	Review & Approve Perimeter Foundation Insulation Product Data	21	12-Feb-25	04-Mar-25
APP-1480	Review & Approve Crystalline Waterproofing Product Data	21	12-Feb-25	04-Mar-25
APP-1490	Review & Approve Suspension Assembly Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1500	Review & Approve Certification of Material	21	12-Feb-25	04-Mar-25
APP-1510	Review & Approve Formwork Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1520	Review & Approve Planting Schedule	21	12-Feb-25	04-Mar-25
APP-1530	Review & Approve Playgroung Equipment Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1540	Review & Approve Catch Basin Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1550	Review & Approve Concrete Curbs & Pavements Shop Drawing	21	12-Feb-25	04-Mar-25
APP-1560	Review & Approve Steel Curb Facing Shop Drawing	21	12-Feb-25	04-Mar-25
APP-1570	Review & Approve Asphaltic Concrete Paving	21	12-Feb-25	04-Mar-25
APP-1580	Review & Approve Gas Vapor Barrier Submittal & Inspection Schedule	21	12-Feb-25	04-Mar-25
APP-1590	Review & Approve Training Outline & Schedule	21	12-Feb-25	04-Mar-25
APP-1600	Review & Approve Temporary Ventilation Plan	21	12-Feb-25	04-Mar-25
APP-1610	Review & Approve Construction Indoor Air Quality Management Plan	21	12-Feb-25	04-Mar-25
APP-1620	Review & Approve CWM Plan	21	12-Feb-25	04-Mar-25
APP-1630	Review & Approve Heating Plan	21	12-Feb-25	04-Mar-25
APP-1640	Review & Approve Sample Classroom Materials	21	12-Feb-25	04-Mar-25
APP-1650	Review & Approve Electrical Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1660	Review & Approve Plumbing Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1670	Review & Approve Sprinkler System Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1680	Review & Approve Gypsum Board	21	12-Feb-25	04-Mar-25
APP-1690	Review & Approve Floorings	21	12-Feb-25	04-Mar-25
APP-1700	Review & Approve Toilet Accessories	21	12-Feb-25	04-Mar-25
APP-1710	Review & Approve Millwork	21	12-Feb-25	04-Mar-25
APP-1720	Review & Approve Furniture	21	12-Feb-25	04-Mar-25
APP-1730	Review & Approve Mechanical Ducts	21	12-Feb-25	04-Mar-25
APP-1740	Review & Approve Plumbing Fixtures	21	12-Feb-25	04-Mar-25
APP-1750	Review & Approve Wood Doors	21	12-Feb-25	04-Mar-25
APP-1760	Review & Approve Fire Protection Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1770	Review & Approve Fire Detectors & Alarms	21	12-Feb-25	04-Mar-25
APP-1790	Review & Approve Signs	21	12-Feb-25	04-Mar-25
APP-1800	Review & Approve Telecommunication System Drawings	21	12-Feb-25	04-Mar-25
APP-1840	Review & Approve Gymnasium Equipment	21	12-Feb-25	04-Mar-25

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1850	Review & Approve Supplemental Comissioning Requirements	21	12-Feb-25	04-Mar-25
APP-1860	Review & Approve Record Documents	21	12-Feb-25	04-Mar-25
APP-1870	Review & Approve Environmental Site Assessment Reports	21	12-Feb-25	04-Mar-25
APP-1880	Review & Approve Selective Removals & Demoloition	21	12-Feb-25	04-Mar-25
APP-1890	Review & Approve Trench Drains Prodcut Data	21	12-Feb-25	04-Mar-25
APP-1900	Review & Approve Chain Link Fences & Gates Drawings	21	12-Feb-25	04-Mar-25
APP-1910	Review & Approve Outdoor Game Equipment	21	12-Feb-25	04-Mar-25
APP-1940	Review & Approve Cast Stone Product Data	21	12-Feb-25	04-Mar-25
APP-1960	Review & Approve Metal Deck Product Data	21	12-Feb-25	04-Mar-25
APP-1970	Review & Approve Prefabricated Expansion Joint Covers	21	12-Feb-25	04-Mar-25
APP-1980	Review & Approve Self Adhering Sheet Air Barriers	21	12-Feb-25	04-Mar-25
APP-1990	Review & Approve Metal Plate Wall Panels	21	12-Feb-25	04-Mar-25
APP-2000	Review & Approve Security Screens & Barriers	21	12-Feb-25	04-Mar-25
APP-2010	Review & Approve Wood Flooring	21	12-Feb-25	04-Mar-25
APP-2020	Review & Approve Visual Display Boards	21	12-Feb-25	04-Mar-25
APP-2030	Review & Approve Metal Lockers	21	12-Feb-25	04-Mar-25
APP-2040	Review & Approve Fire Extinguishers & Cabinets	21	12-Feb-25	04-Mar-25
APP-2050	Review & Approve Library Equipment	21	12-Feb-25	04-Mar-25
APP-2060	Review & Approve Platform Curtains & Auditorium Window Curtains	21	12-Feb-25	04-Mar-25
APP-2070	Review & Approve Waste Handling Equipment	21	12-Feb-25	04-Mar-25
APP-2080	Review & Approve Domestic Equipment	21	12-Feb-25	04-Mar-25
APP-2090	Review & Approve Laboratory Equipment	21	12-Feb-25	04-Mar-25
APP-2100	Review & Approve Manufactured Wood Casework	21	12-Feb-25	04-Mar-25
APP-2110	Review & Approve Concrete Floating Floor Assembly	21	12-Feb-25	04-Mar-25
APP-2120	Review & Approve Hydraulic Vertical Wheelchair Lifts	21	12-Feb-25	04-Mar-25
APP-2130	Review & Approve Switch & Panel Boards	21	12-Feb-25	04-Mar-25
APP-2140	Review & Approve Auditorium & Television Studio Dimming System Product Data	21	12-Feb-25	04-Mar-25
APP-2150	Review & Approve Overcurrent Protective Devices Data	21	12-Feb-25	04-Mar-25
APP-2160	Review & Approve Gas Pipes	21	12-Feb-25	04-Mar-25
APP-2170	Review & Approve Water Heaters	21	12-Feb-25	04-Mar-25
APP-2180	Review & Approve Pumping Apparatus & Tanks	21	12-Feb-25	04-Mar-25
APP-2190	Review & Approve HVAC Pumps	21	12-Feb-25	04-Mar-25
APP-2210	Review & Approve Fuel Storage Equipment	21	12-Feb-25	04-Mar-25
APP-2220	Review & Approve Natural Gas Leak Detection Equipment	21	12-Feb-25	04-Mar-25
APP-2240	Review & Approve Temperature Control System	21	12-Feb-25	04-Mar-25
APP-2250	Review & Approve Air Outlets & Inlets	21	12-Feb-25	04-Mar-25
APP-2360	Review & Approve Adjacent Property and Structures Protection & Monitoring Plan	21	12-Feb-25	04-Mar-25
APP-2370	Review & Approve Ornamenta Metal Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2920	Review & Approve Documentation of Proper Disposal	21	12-Feb-25	04-Mar-25
APP-2930	Review & Approve Ornamenta Metal Product Data	21	12-Feb-25	04-Mar-25
APP-2960	Review & Approve Coiling Doors, Grilles and Shutters Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2970	Review & Approve Coiling Doors, Grilles and ShuttersProduct Data	21	12-Feb-25	04-Mar-25
APP-2980	Review & Approve Aluminum Framed Entrances & Storefronts Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2990	Review & Approve Aluminum Framed Entrances & Storefronts Product Data	21	12-Feb-25	04-Mar-25

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
APP-3000	Review & Approve Thresholds, Weatherstripping and Seals Color Samples	21	12-Feb-25	04-Mar-25
APP-3010	Review & Approve Thresholds, Weatherstripping and Seals Product Data	21	12-Feb-25	04-Mar-25
APP-3020	Review & Approve Miscellaneous Glazing Samples	21	12-Feb-25	04-Mar-25
APP-3030	Review & Approve Miscellaneous Glazing Product Data	21	12-Feb-25	04-Mar-25
APP-3040	Review & Approve Fire Rated Glazing Samples	21	12-Feb-25	04-Mar-25
APP-3050	Review & Approve Fire Rated Glazing Product Data	21	12-Feb-25	04-Mar-25
APP-3060	Review & Approve Graffiti Resistant Coating Product Data	21	12-Feb-25	04-Mar-25
APP-3070	Review & Approve Special Coating Samples	21	12-Feb-25	04-Mar-25
APP-3080	Review & Approve Special Coating Product Data	21	12-Feb-25	04-Mar-25
APP-3090	Review & Approve Flagpole Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3100	Review & Approve Flagpole Product Data	21	12-Feb-25	04-Mar-25
APP-3110	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals	21	12-Feb-25	04-Mar-25
APP-3120	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	21	12-Feb-25	04-Mar-25
APP-3130	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	21	12-Feb-25	04-Mar-25
APP-3140	Review & Approve Wire Mesh Work Samples	21	12-Feb-25	04-Mar-25
APP-3150	Review & Approve Miscellaneous Glazing Shop drawings	21	12-Feb-25	04-Mar-25
APP-3160	Review & Approve Metal Storage Shelving Samples	21	12-Feb-25	04-Mar-25
APP-3170	Review & Approve Metal Storage Shelving Shop drawings	21	12-Feb-25	04-Mar-25
APP-3180	Review & Approve Mirrors Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3190	Review & Approve Mirrors Product Data	21	12-Feb-25	04-Mar-25
APP-3200	Review & Approve Mirrors Mastic Compatibility Test Reports & Certifications	21	12-Feb-25	04-Mar-25
APP-3210	Review & Approve Grab Bars Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3220	Review & Approve Grab Bars Product Data	21	12-Feb-25	04-Mar-25
APP-3230	Review & Approve Shop Equipment Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3240	Review & Approve Shop Equipment Product Data	21	12-Feb-25	04-Mar-25
APP-3250	Review & Approve Bleachers Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3260	Review & Approve Bleachers Product Data	21	12-Feb-25	04-Mar-25
APP-3270	Review & Approve Bleachers Manufacturer's Warranty	21	12-Feb-25	04-Mar-25
APP-3280	Review & Approve Valves Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3290	Review & Approve Valves Product Data	21	12-Feb-25	04-Mar-25
APP-3300	Review & Approve Certification of Tests	21	12-Feb-25	04-Mar-25
APP-3310	Review & Approve Domestic Water Sterilization Plan	21	12-Feb-25	04-Mar-25
APP-3320	Review & Approve Tags, Charts & Identifications Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3330	Review & Approve Tags, Charts & Identifications Product Data	21	12-Feb-25	04-Mar-25
APP-3340	Review & Approve Micselianeous Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3350	Review & Approve Valves (HVAC) Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3360	Review & Approve Valves (HVAC) Product Data	21	12-Feb-25	04-Mar-25
APP-3370	Review & Approve Piping Insulation Schedule Listing Items	21	12-Feb-25	04-Mar-25
APP-3380	Review & Approve chedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	21	12-Feb-25	04-Mar-25
APP-3390	Review & Approve chedules Showing Manfacturers's Product Number Duct Work Insulation	21	12-Feb-25	04-Mar-25
APP-3400	Review & Approve Hydronic Specialities Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3410	Review & Approve Hydronic Specialities Product Data	21	12-Feb-25	04-Mar-25
APP-3420	Review & Approve Water Treatment Firm	21	12-Feb-25	04-Mar-25
APP-3430	Review & Approve Chemical Products Product Data	21	12-Feb-25	04-Mar-25

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
APP-3460	Review & Approve Breeching Chimney Connectors and Chimneys Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3470	Review & Approve Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	21	12-Feb-25	04-Mar-25
APP-3480	Review & Approve Plate Heat Exchanger Maintenance Data	21	12-Feb-25	04-Mar-25
APP-3490	Review & Approve Plate Heat Exchanger Product Data	21	12-Feb-25	04-Mar-25
APP-3500	Review & Approve Coils Maintenance Data	21	12-Feb-25	04-Mar-25
APP-3510	Review & Approve Coils Certifications	21	12-Feb-25	04-Mar-25
APP-3520	Review & Approve Convectors Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3530	Review & Approve Convectors Product Data	21	12-Feb-25	04-Mar-25
APP-3540	Review & Approve Fan Coils Units Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3550	Review & Approve Fan Coils Units Shop Drawings	21	12-Feb-25	04-Mar-25
APP-3560	Review & Approve Door Air Curtains Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3570	Review & Approve Door Air Curtains Product Data	21	12-Feb-25	04-Mar-25
APP-3580	Review & Approve Centrifugal Fans Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3590	Review & Approve Centrifugal Fans Product Data	21	12-Feb-25	04-Mar-25
APP-3600	Review & Approve Centrifugal Fans Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3610	Review & Approve Air Filters Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3620	Review & Approve Air Filters Product Data	21	12-Feb-25	04-Mar-25
APP-3630	Review & Approve Air Filters Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3640	Review & Approve Duct Accessories Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3650	Review & Approve Damper Assemblies Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3660	Review & Approve Damper Assemblies Product Data	21	12-Feb-25	04-Mar-25
APP-3670	Review & Approve Damper Assemblies Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3680	Review & Approve Variable Air Terminals Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3690	Review & Approve Variable Air Terminals Product Data	21	12-Feb-25	04-Mar-25
APP-3700	Review & Approve Variable Air Terminals Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3710	Review & Approve AHU for Public Assemblies Sapces Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3720	Review & Approve AHU for Public Assemblies Sapces Product Data	21	12-Feb-25	04-Mar-25
APP-3730	Review & Approve AHU for Public Assemblies Sapces Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3740	Review & Approve Control Systems Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3750	Review & Approve Truck Network Cable Schematic Diagram	21	12-Feb-25	04-Mar-25
APP-3790	Review & Approve Surge Protective Devices Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3800	Review & Approve Surge Protective Devices Product Data	21	12-Feb-25	04-Mar-25
APP-3810	Review & Approve Surge Protective Devices Warranty	21	12-Feb-25	04-Mar-25
APP-3820	Review & Approve Service Entrance Equipment Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3830	Review & Approve Service Entrance Equipment Product Data	21	12-Feb-25	04-Mar-25
APP-3840	Review & Approve Service Entrance Equipment Warranty	21	12-Feb-25	04-Mar-25
APP-3850	Review & Approve Enclosed Switches Product Data	21	12-Feb-25	04-Mar-25
APP-3860	Review & Approve Enclosed Switches Test Reports	21	12-Feb-25	04-Mar-25
APP-3870	Review & Approve Motors, Motor Control Centers and Starters Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3880	Review & Approve Motors, Motor Control Centers and Starters Product Data	21	12-Feb-25	04-Mar-25
APP-3890	Review & Approve Motors, Motor Control Centers and Starters Field Test Reports	21	12-Feb-25	04-Mar-25
APP-3900	Review & Approve Lightning Protection Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3920	Review & Approve Lightning Protection Test Reports	21	12-Feb-25	04-Mar-25
APP-3930	Review & Approve Fiber Optic Cabling system Shop Drawing	21	12-Feb-25	04-Mar-25

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
APP-3940	Review & Approve Fiber Optic Cabling system Product Data	21	12-Feb-25	04-Mar-25
APP-3950	Review & Approve Fiber Optic Cabling system Samples	21	12-Feb-25	04-Mar-25
APP-3960	Review & Approve Sound, Intercome & Security System Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3970	Review & Approve Sound, Intercome & Security System Programming Code and Password for the System	21	12-Feb-25	04-Mar-25
APP-3980	Review & Approve Sound, Intercome & Security System warranty	21	12-Feb-25	04-Mar-25
APP-3990	Review & Approve Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	21	12-Feb-25	04-Mar-25
APP-4000	Review & Approve Projection and Interactive Whiteboard Systems Wiring diagram	21	12-Feb-25	04-Mar-25
APP-4010	Review & Approve Self Corrective Clock System Shop Drawing	21	12-Feb-25	04-Mar-25
APP-4020	Review & Approve Self Corrective Clock System Product Data	21	12-Feb-25	04-Mar-25
APP-4030	Review & Approve Self Corrective Clock System Field Test Reports	21	12-Feb-25	04-Mar-25
APP-4040	Review & Approve Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	21	12-Feb-25	04-Mar-25
APP-4060	Review & Approve Steel Stairs Shop Drawings	21	12-Feb-25	04-Mar-25
APP-4070	Review & Approve Steel Stairs Product Data	21	12-Feb-25	04-Mar-25
APP-4080	Review & Approve Green School Submittal	21	12-Feb-25	04-Mar-25
APP-2260	Review & Approve Product Substitutions	21	13-Feb-25	05-Mar-25
MIL-2572	Place Steel Mill Order	0	20-Feb-25	
SUB-2280	Prepare & Submit Final 1st Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2290	Prepare & Submit Final 2nd Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2300	Prepare & Submit Final 3rd Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2310	Prepare & Submit Final 4th Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2320	Prepare & Submit Final 5th Floor Coordination Drawings	49	25-Feb-25	02-May-25
MIL-2762	Green Schools Compliance Submission	0		04-Mar-25
SUB-1700	Prepare & Submit Roof Dunnage	81	05-Mar-25	27-Jun-25
APP-2270	Review & Approve Final Foundations Coordination Drawings	21	12-Mar-25	01-Apr-25
APP-2280	Review & Approve Final 1st Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2290	Review & Approve Final 2nd Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2300	Review & Approve Final 3rd Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2310	Review & Approve Final 4th Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2320	Review & Approve Final 5th Floor Coordination Drawings	21	03-May-25	23-May-25
MIL-1640	Provide Complete Set of Approved Coordination Drawings	0		23-May-25
SUB-2900	Prepare & Submit Excavated Material Disposal Plan	71	26-May-25	05-Sep-25
SUB-4050	Prepare & Submit Soil Sampling Plan	71	26-May-25	05-Sep-25
PRO-1590	Procure & Deliver Steel Columns	120	02-Jun-25	29-Sep-25
APP-1810	Review & Approve Roof Dunnage	21	28-Jun-25	18-Jul-25
PRO-1120	Procure & Deliver Erosion Control and Sedimentation Devices	25	05-Sep-25	29-Sep-25
APP-2900	Review & Approve Excavated Material Disposal Plan	21	06-Sep-25	26-Sep-25
APP-4050	Review & Approve Soil Sampling Plan	21	06-Sep-25	26-Sep-25
SUB-2910	Prepare & Submit Backfill & Resue Plan	20	08-Sep-25	03-Oct-25
PRE-2630	Obtain Builders Pavement Permit	10	16-Sep-25	29-Sep-25
PRE-2640	Obtain Excavation & Shoring Permit	10	16-Sep-25	29-Sep-25
PRE-2650	Obtain Permit to Enter (PTE) Amtrak	10	16-Sep-25	29-Sep-25
PRE-2660	Obtain NYPA Permit	10	16-Sep-25	29-Sep-25
PRE-2540	SCA Work Notification	7	23-Sep-25	29-Sep-25
PRE-1660	DOB Permit & Insurance	3	25-Sep-25	29-Sep-25

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
PRE-1460	Obtain Construction Fences Permit	3	25-Sep-25	29-Sep-25
PRE-2550	Obtain CCD1	3	25-Sep-25	29-Sep-25
PRE-2570	Obtain Sidewalk Shed Permits	3	25-Sep-25	29-Sep-25
MIL-2532	Submit Complete Permit Application	0		29-Sep-25
MIL-2832	Issuance of Excavation & Shoring Permit	0		29-Sep-25
MIL-2842	Issuance of Builders Pavement Permit	0		29-Sep-25
MIL-2852	Issuance of Permit to Enter (PTE)	0		29-Sep-25
MIL-2862	Issuance of NYPA Permit	0		29-Sep-25
MIL-2872	Issuance of Construction Fences Permit	0		29-Sep-25
MIL-2882	Issuance of Sidewalk Shed Permits	0		29-Sep-25
MIL-2892	Issuance of CCD1	0		29-Sep-25
MIL-2902	Issuance of DOB Permit & Insurance	0		29-Sep-25
MIL-1060	Mobilization Start	0	30-Sep-25	
PRO-1420	Procure & Deliver Painting	70	30-Sep-25	08-Dec-25
PRO-1410	Procure & Deliver Door Frames	70	30-Sep-25	08-Dec-25
PRO-1200	Procure & Deliver Elevator Machine	112	30-Sep-25	19-Jan-26
PRO-1150	Procure & Deliver Gypsum Board	150	30-Sep-25	26-Feb-26
PRO-1160	Procure & Deliver Floorings	80	30-Sep-25	18-Dec-25
PRO-1170	Procure & Deliver Acosutical Ceiling Tiles	120	30-Sep-25	27-Jan-26
PRO-1190	Procure & Deliver Toilet Accessories	100	30-Sep-25	07-Jan-26
PRO-1000	Procure & Deliver Kitchen Equipment	180	30-Sep-25	28-Mar-26
PRO-1140	Procure & Deliver Lighting Fixtures	60	30-Sep-25	28-Nov-25
PRO-1010	Procure & Deliver Furnitures	130	30-Sep-25	06-Feb-26
PRO-1020	Procure & Deliver Mechanical Piping	70	30-Sep-25	08-Dec-25
PRO-1030	Procure & Deliver Mechanical Ducts	70	30-Sep-25	08-Dec-25
PRO-1050	Procure & Deliver Electrical Equipment	130	30-Sep-25	06-Feb-26
PRO-1060	Procure & Deliver Plumbing Fixtures	100	30-Sep-25	07-Jan-26
PRO-1070	Procure & Deliver Wood Doors	50	30-Sep-25	18-Nov-25
PRO-1090	Procure & Deliver Fire Sprinklers	100	30-Sep-25	07-Jan-26
PRO-1110	Procure & Deliver Fire Detectors & Alarms	60	30-Sep-25	28-Nov-25
PRO-1210	Procure & Deliver Signs	70	30-Sep-25	08-Dec-25
PRO-1220	Procure & Deliver Windows & Storefronts	154	30-Sep-25	02-Mar-26
PRO-1250	Procure & Deliver Plumbing Pipes	60	30-Sep-25	28-Nov-25
PRO-1260	Procure & Deliver Electrical Wires & Conduits	130	30-Sep-25	06-Feb-26
PRO-1270	Procure & Deliver Mechanical Pumps	70	30-Sep-25	08-Dec-25
PRO-1280	Procure & Deliver Fire Protection Pumps	70	30-Sep-25	08-Dec-25
PRO-1290	Procure & Deliver Plumbing Pumps	250	30-Sep-25	06-Jun-26
PRO-1310	Procure & Deliver Telecommunication System	60	30-Sep-25	28-Nov-25
PRO-1330	Procure & Deliver Cameras	60	30-Sep-25	28-Nov-25
PRO-1360	Procure & Deliver Metal Panel Ceilings	120	30-Sep-25	27-Jan-26
PRO-1380	Procure & Deliver Roof Dunnage	100	30-Sep-25	07-Jan-26
PRO-1470	Procure & Deliver Cabinet Heaters	126	30-Sep-25	02-Feb-26
PRO-1480	Procure & Deliver Chillers	170	30-Sep-25	18-Mar-26
PRO-1490	Procure & Deliver Air Handling Units	250	30-Sep-25	06-Jun-26

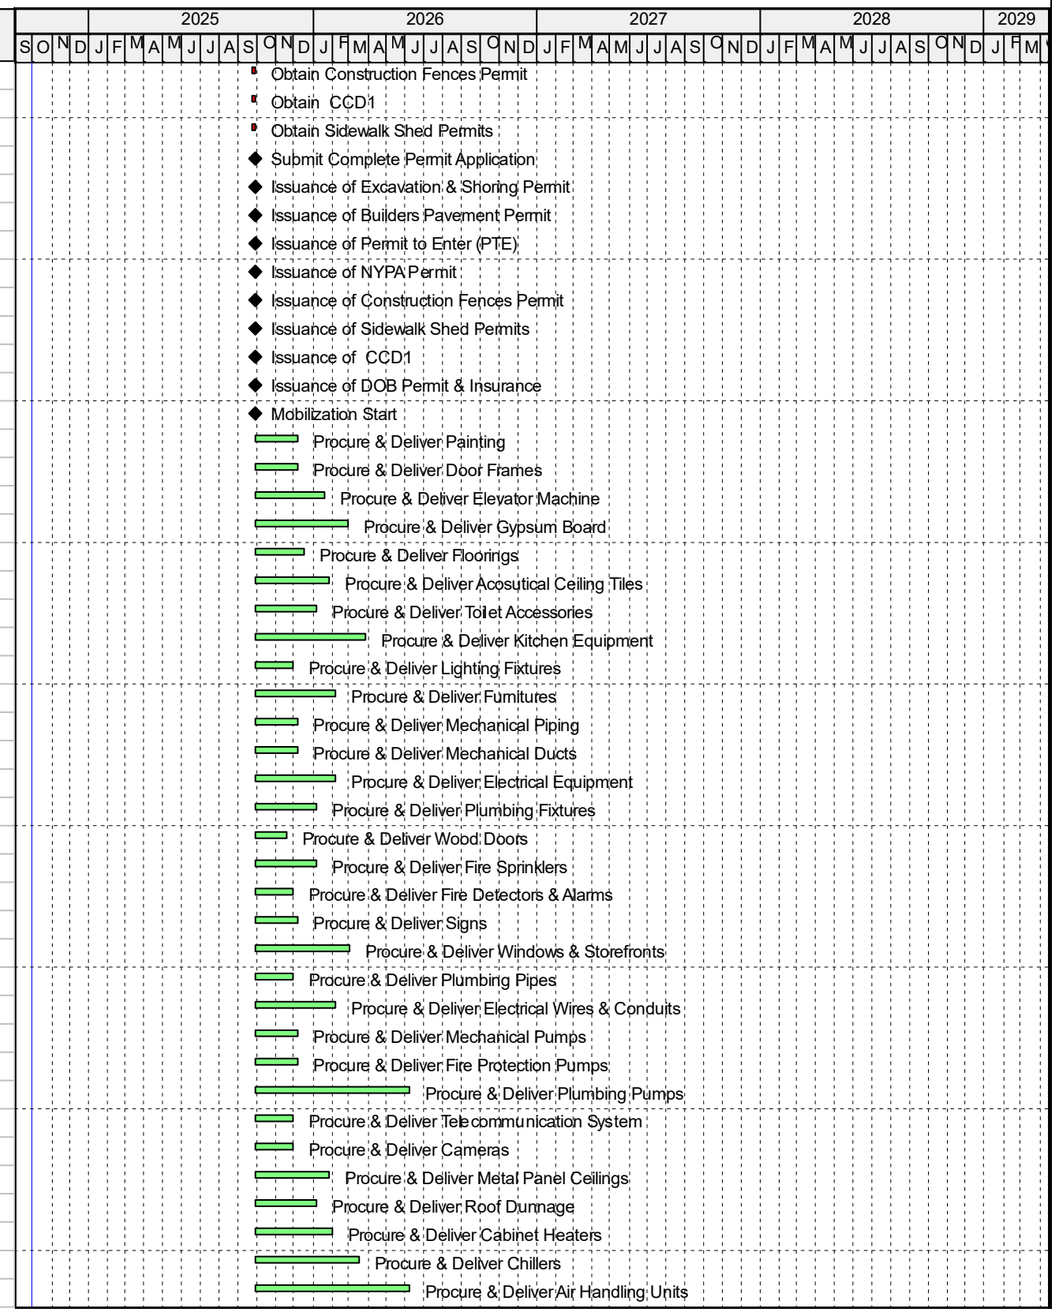

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
PRO-1500	Procure & Deliver Boilers	84	30-Sep-25	22-Dec-25
PRO-1510	Procure & Deliver Emergency Generator	290	30-Sep-25	16-Jul-26
PRO-1520	Procure & Deliver Switch Gears	250	30-Sep-25	06-Jun-26
PRO-1530	Procure & Deliver Hydraulic Vertical Wheelchair Lift	90	30-Sep-25	28-Dec-25
PRO-1560	Procure & Deliver Gymnasium Equipment	180	30-Sep-25	28-Mar-26
CON-8030	Procurement From CON-ED For Temporary Electrical Power	20	30-Sep-25	19-Oct-25
PRO-1570	Procure & Deliver Precast Sandwich Panels	112	30-Sep-25	19-Jan-26
PRO-1580	Procure & Deliver Metal Deck	70	30-Sep-25	08-Dec-25
PRO-1600	Procure & Deliver Trusses	60	30-Sep-25	28-Nov-25
PRO-1610	Procure & Deliver Prefabricated Expansion Joint Covers	60	30-Sep-25	28-Nov-25
PRO-1620	Procure & Deliver Security Screens & Barriers	60	30-Sep-25	28-Nov-25
PRO-1630	Procure & Deliver Wood Flooring	120	30-Sep-25	27-Jan-26
PRO-1640	Procure & Deliver Concrete Floating Floor Assembly	120	30-Sep-25	27-Jan-26
PRO-1660	Procure & Deliver Auditorium Television Studio Dimming System	90	30-Sep-25	28-Dec-25
MIL-1850	Construction Start	0	30-Sep-25	
PRO-2010	Procure & Deliver Steel Stairs Components	120	30-Sep-25	27-Jan-26
PRO-2020	Procure & Deliver Flagpole	60	30-Sep-25	28-Nov-25
PRO-2030	Procure & Deliver Bleachers	130	30-Sep-25	06-Feb-26
PRO-2040	Procure & Deliver VAV Units	170	30-Sep-25	18-Mar-26
PRO-2050	Procure & Deliver Furnitures (Owner Responsibility)	130	30-Sep-25	06-Feb-26
MIL-1710	Complete Mobilization	0		03-Oct-25
APP-2910	Review & Approve Backfill & Resue Plan	21	04-Oct-25	24-Oct-25
PRE-2610	Prepare & Submit FDNY Fuel Permit	10	06-Oct-25	20-Oct-25
CON-8040	CON-ED Work For Temporary Electrical Power	10	20-Oct-25	31-Oct-25
PRE-2620	Review & Approve FDNY Fuel Permit	21	21-Oct-25	10-Nov-25
I-1010	Concrete Cast-IN-Place Inspection	86	28-Oct-25	04-Mar-26
MIL-2582	Start Concrete Placement	0	28-Oct-25	
MIL-2812	Start Foundation	0	28-Oct-25	
MIL-2912	Start Concrete Cast In Place Inspection	0	28-Oct-25	
CON-8050	Available Temporary Electrical Power For Testing MEP Equipment	0		31-Oct-25
MIL-1810	Crane Mobilization-Steel Installation start	0	05-Dec-25	
I-1140	Structural Steel Inspection	58	05-Dec-25	02-Mar-26
PRO-1450	Procure & Deliver Playground Equipment	60	09-Dec-25	06-Feb-26
MIL-1120	Metal Decking Start	0	22-Dec-25	
I-1080	Standpipe System Inspection	111	29-Dec-25	05-Jun-26
MIL-2622	Deliveries of all owner-furnished equipment and/or materials	0		06-Feb-26
MIL-1140	Layout Start	0	23-Feb-26	
MIL-1150	Masonry Walls Start	0	23-Feb-26	
MIL-1180	MEP Risers Start	0	23-Feb-26	
MIL-1210	Duct Rough-ins Start	0	24-Feb-26	
MIL-1160	Top & Bottom Track Start	0	26-Feb-26	
I-1020	Masonry Inspection	32	02-Mar-26	14-Apr-26
I-1100	Fire-Resistant Penetrations And Joints Inspection	87	03-Mar-26	06-Jul-26
MIL-1830	Crane Mobilization-Precast Sandwich Panels Installation Start	0	05-Mar-26	

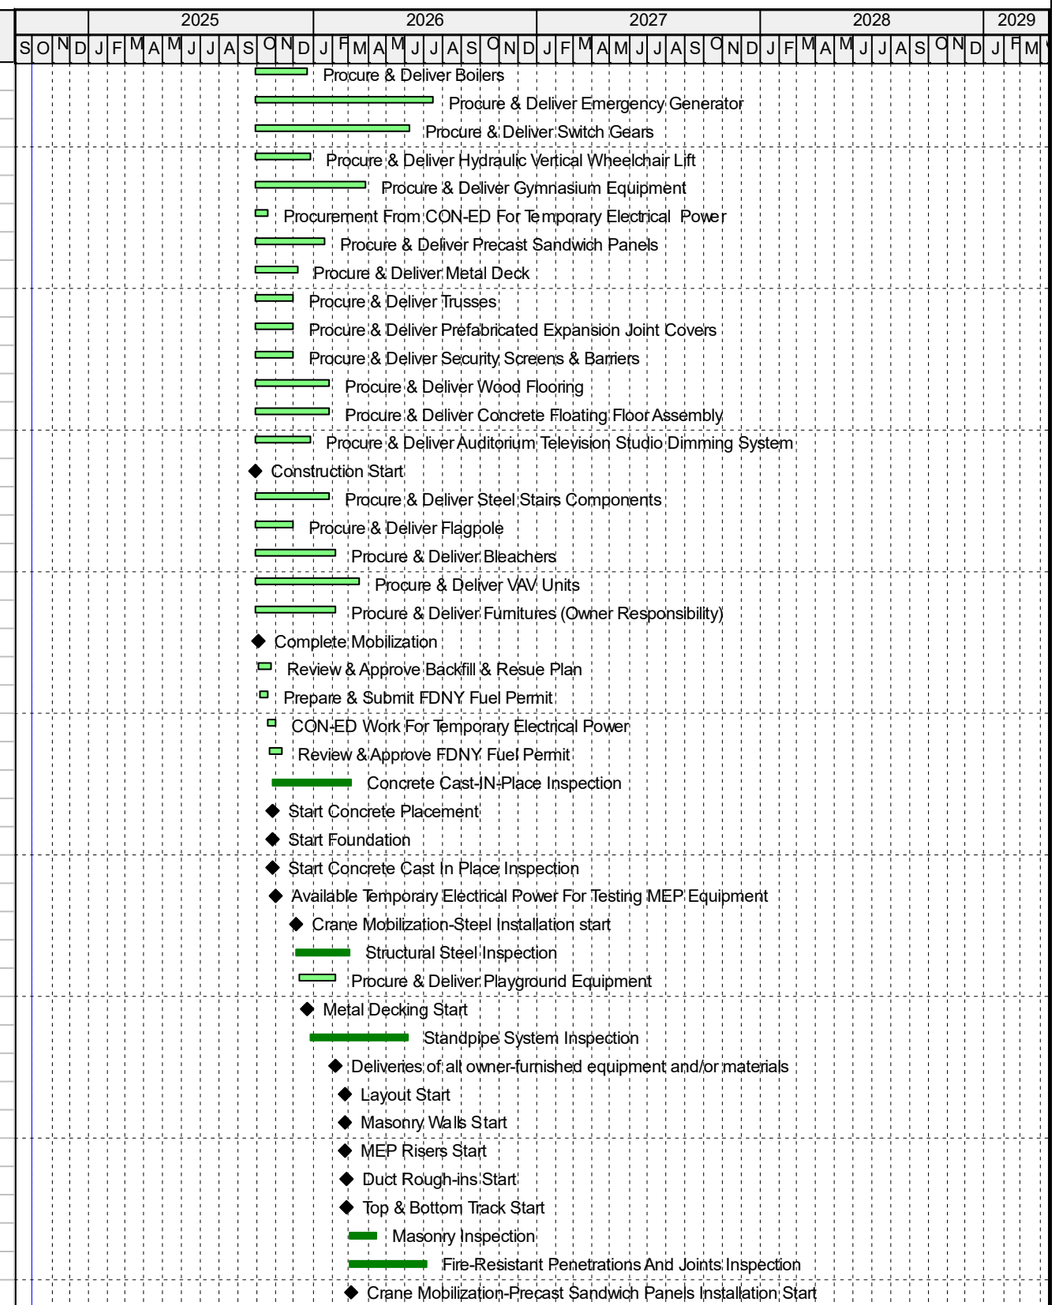

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
MIL-2932	Start Masonry Inspection	0	05-Mar-26	
MIL-1170	Finish Concrete Work	0		11-Mar-26
MIL-1820	Crane Mobilization-Steel Installation Finish	0		12-Mar-26
MIL-2612	Start Suspended Ceiling Grid	0	16-Mar-26	
MIL-1380	Crane Mobilization-Mechanical Subcontractor	78	17-Mar-26	07-Jul-26
I-1150	Concrete Precast Inspection	9	25-Mar-26	06-Apr-26
MIL-2922	Start Pre -Cast Concrete Inspection	0	25-Mar-26	
MIL-1840	Crane Mobilization-Precast Sandwich Panels Installation Finish	0		06-Apr-26
MIL-1230	5th Floor Roofing Start	0	07-Apr-26	
I-1120	Mechanical System Inspection	69	07-Apr-26	15-Jul-26
MIL-2602	Start Mechanical Distribution Lines	0	08-Apr-26	
MIL-1200	Main Roofing Start	0	09-Apr-26	
MIL-1270	Electrical Rough-ins Start	0	09-Apr-26	
MIL-1220	Layout Finish	0		09-Apr-26
MIL-2942	Start In-Wall Inspection	0	10-Apr-26	
MIL-1290	Duct Rough-ins Finish	0		14-Apr-26
MIL-1250	Top & Bottom Track Finish	0		15-Apr-26
CON-7970	Coordinate With CON-ED For Gas Service	7	16-Apr-26	24-Apr-26
MIL-2712	Start Low Voltage	0	16-Apr-26	
PRO-1990	Procure & Deliver Gas Meter Rig	60	25-Apr-26	23-Jun-26
MIL-1580	Window Installation Finish	0		28-Apr-26
MIL-1400	Start Site Work	0	29-Apr-26	
I-1040	Roofing Flood Testing Inspection	5	30-Apr-26	06-May-26
MIL-1300	Start Sprinkler Rough-ins	0	04-May-26	
MIL-1340	BLDG Tight	0		06-May-26
MIL-1350	Electrical Rough-ins Finish	0		06-May-26
MIL-1360	Start Mockup Room Work	0	07-May-26	
MIL-1430	Start Architecture Finishes	0	07-May-26	
MIL-1260	Plumbing Rough-ins Start	0	07-May-26	
MIL-1310	5th Floor Roofing Finish	0		13-May-26
MIL-1280	Main Roofing Finish	0		15-May-26
MIL-1410	Mockup Room Ready For Inspection	0		26-May-26
MIL-1420	Finish Mockup Room	0		26-May-26
MIL-1440	Start Gypsum Board	0	27-May-26	
I-1130	Fire Alarm Inspection	47	28-May-26	04-Aug-26
MIL-1320	Plumbing Rough-ins Finish	0		29-May-26
I-1110	Fuel-Oil Storage & Fuel Oil Piping Systems Inspection	9	01-Jun-26	11-Jun-26
MIL-2952	Finish Standpipe System Inspection	0		05-Jun-26
MIL-1460	Roof Top Units Installations Start	0	08-Jun-26	
MIL-1450	Start 1st Coat Painting	0	10-Jun-26	
MIL-2992	Finish Fuel-Oil Storage & Fuel Oil Piping Systems Inspection	0		11-Jun-26
CON-8060	CON-ED - Switchgear Inspection	4	15-Jun-26	18-Jun-26
CON-8070	CON-ED - Pull Power Cable to the Building	10	22-Jun-26	06-Jul-26
MIL-1330	Finish Sprinkler Rough-ins	0		22-Jun-26

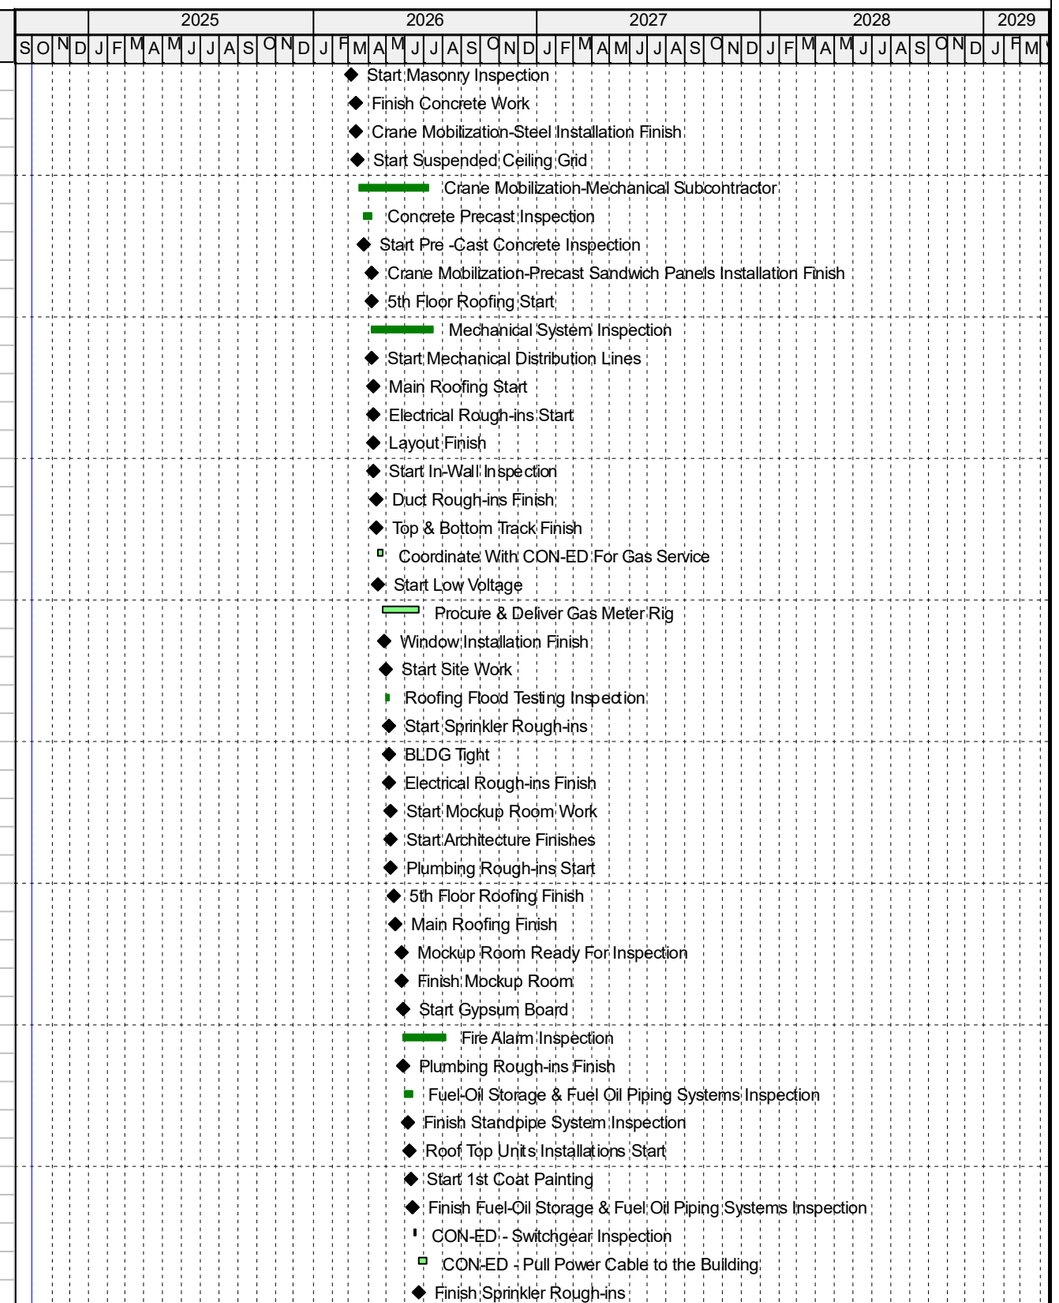

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
CON-7990	Gas Authorization	5	24-Jun-26	30-Jun-26
CON-8000	Pink Slip	5	01-Jul-26	08-Jul-26
CLO-1120	MDF & IDF Rooms Testing & Commissioning	12	06-Jul-26	21-Jul-26
MIL-2632	Finish HVAC	0		06-Jul-26
MIL-2982	Finish Fire-Resistant Penetrations And Joints Inspection	0		06-Jul-26
CLO-1010	HVAC Flush-Out	20	07-Jul-26	03-Aug-26
MIL-2732	Start Mechanical and Electrical System Commissioning	0	07-Jul-26	
CON-8080	CON-ED - Terminate Power Cables	10	07-Jul-26	20-Jul-26
PRO-2000	Procure & Deliver Key Cutting Machine	74	08-Jul-26	19-Sep-26
MIL-1480	Roof Top Units Installations Finish	0		14-Jul-26
MIL-2972	Finish Mechanical System Inspection	0		15-Jul-26
CLO-1140	SSDS System Testing & Commissioning	7	16-Jul-26	24-Jul-26
MIL-2562	Start Below Grade Plumbing and Other Utilities	0	16-Jul-26	
CON-8090	CON-ED - Energize to the Building	5	21-Jul-26	27-Jul-26
MIL-1600	MDF Work Finish	0		21-Jul-26*
MIL-1610	IDF Work Finish	0		21-Jul-26*
SUB-2330	Prepare & Submit Remedial Closure Report	3	27-Jul-26	29-Jul-26
MIL-2742	Permanent Power Available	0		27-Jul-26
MIL-2592	P&D - Connection to Roof Drains	0	28-Jul-26	
CLO-1240	Elevator Sump Pump Testing & Commissioning	21	28-Jul-26	25-Aug-26
CLO-1270	Water Heater Testing & Commissioning	21	28-Jul-26	25-Aug-26
CLO-1220	Emergency Generator Electric Load Test	3	29-Jul-26	31-Jul-26
APP-2330	Review & Approve Remedial Closure Report	21	30-Jul-26	19-Aug-26
PER-2640	Obtain Emergency Generator Permit	5	03-Aug-26	07-Aug-26
CLO-1250	Emergency Generator Testing & Commissioning	21	03-Aug-26	31-Aug-26
MIL-2692	Building HVAC Flush-out	0		03-Aug-26
CLO-1230	Air Handling Unit Testing & Commissioning	21	04-Aug-26	01-Sep-26
CLO-1190	Pre-Elevator Test Inspection	5	05-Aug-26	11-Aug-26
CLO-1290	Glycol System Testing & Commissioning	21	05-Aug-26	02-Sep-26
MIL-1680	Emergency Generator Final Sign-off	0		07-Aug-26
MIL-2642	Finish Fire Alarm Signoff	0		07-Aug-26
MIL-2962	Finish Fire Alarm Inspection	0		07-Aug-26
CLO-1020	Electrical System Testing & Commissioning	21	10-Aug-26	08-Sep-26
MIL-2802	Provision of Training Schedules (30 days prior to start of Training)	0	10-Aug-26	
CLO-1260	HVAC Split System Testing & Commissioning	21	10-Aug-26	08-Sep-26
CLO-1280	Fire Alarm Testing & Commissioning	21	10-Aug-26	08-Sep-26
MIL-2702	Finish Concrete Work	0		10-Aug-26
MIL-2822	Elevator Ready for Testing	0		11-Aug-26
CLO-1000	Elevator Testing & Commissioning	20	12-Aug-26	09-Sep-26
CLO-1160	Sprinkler/Domestic Booster Pumps Testing & Commissioning	14	20-Aug-26	09-Sep-26
CLO-1130	IPDVS System Testing & Commissioning	11	03-Sep-26	18-Sep-26
MIL-2662	Finishes and Ceiling Complete	0		04-Sep-26
CLO-1300	Provide Training	10	09-Sep-26	22-Sep-26
CLO-1170	Sprinkler/Domestic Booster Pumps Inspection	3	10-Sep-26	14-Sep-26

Full Schedule Layout Grouped by Location

Activity ID	Activity Name	Original Duration	Start	Finish
CLO-1200	Elevator DOB Inspection	5	10-Sep-26	16-Sep-26
CLO-1030	Pre-Final Clean-Out	5	11-Sep-26	17-Sep-26
CLO-1180	Sprinkler/Domestic Booster Pumps Sign-offs	0		14-Sep-26
CLO-1150	FDNY Inspection	12	15-Sep-26	30-Sep-26
PER-2650	Elevator Equipment Use Permit	10	17-Sep-26	30-Sep-26
CLO-1040	Pre-TCO Inspection	11	18-Sep-26	02-Oct-26
MIL-1620	IPDVS Work Finish	0		18-Sep-26*
MIL-2652	Finish Mechanical and Electrical System Commissioning	0		18-Sep-26
MIL-2772	Performance test for all mechanical equipment and low voltage systems	0		18-Sep-26
MIL-2792	Commissioning for all mechanical equipment and low voltage systems	0		18-Sep-26
MIL-1650	FDNY Inspection Finish	0		30-Sep-26
MIL-1670	Elevator Final Sign-off	0		30-Sep-26
CLO-1110	Pre-TCO Punchlist	10	05-Oct-26	19-Oct-26
MIL-1510	TCO	0		19-Oct-26*
CLO-1050	Pre-Substantial Punchlist	105	20-Oct-26	17-Apr-27
MIL-1550	Substantial Completion	0		17-Apr-27*
CLO-1060	Prepare & Submit O&M Manuals	30	19-Apr-27	01-Jun-27
MIL-2782	Submission of Operations and Maintenance Manuals	0		01-Jun-27
CLO-1070	Prepare & Submit As-Built Drawings	30	02-Jun-27	15-Jul-27
CLO-1080	Final Inspection	5	16-Jul-27	22-Jul-27
CLO-1090	Final Clean Out	10	23-Jul-27	05-Aug-27
CLO-1100	Demobilization	10	06-Aug-27	15-Aug-27
MIL-1560	Final Completion	0		15-Aug-27*

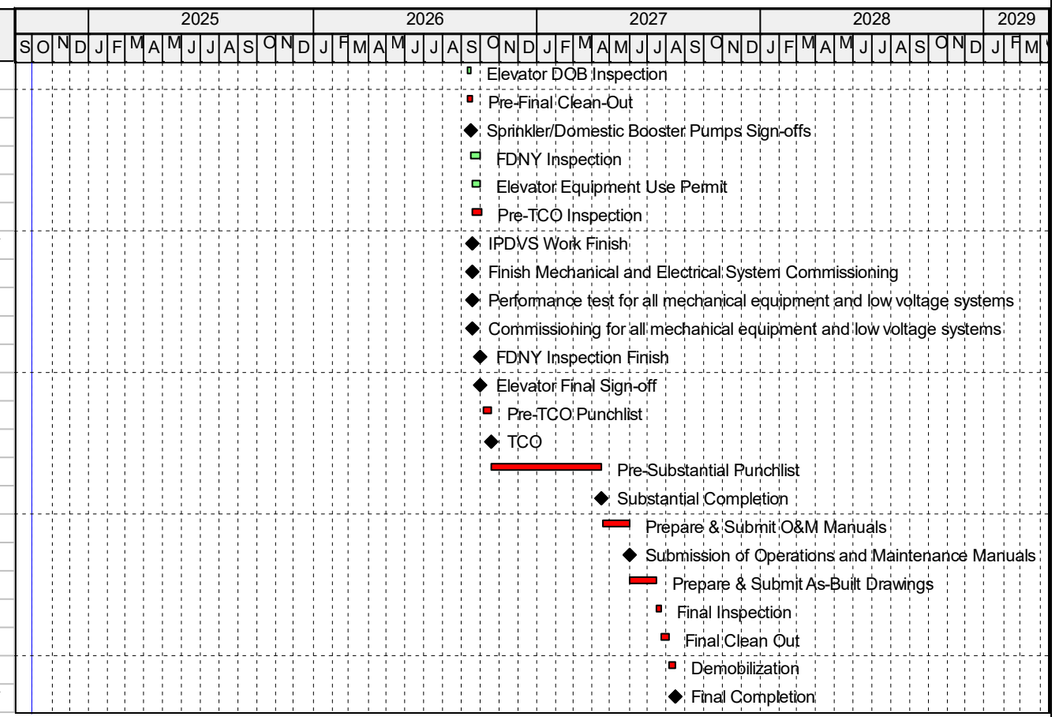

APPENDIX 4
Full Schedule Layout Grouped by AREA Code

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
Site Area		513	30-Sep-24	19-Oct-26
CON-99257	Subcontractor Buyout	10	30-Sep-24	11-Oct-24
MIL-1660	Start Security Guard Services (30 Days From NTP)	0	30-Oct-24	
CON-1000	Mobilization	4	30-Sep-25	03-Oct-25
CON-7740	Protection Of All Overhead & Underground Utilities	263	30-Sep-25	19-Oct-26
CON-9000	Protection & Restoration the adjacent Properties to Original Condition	263	30-Sep-25	19-Oct-26
CON-1080	Install Erosion Control Devices	2	06-Oct-25	07-Oct-25
CON-1010	Install Construction Signs	2	06-Oct-25	07-Oct-25
CON-1030	Install Construction Fences	2	06-Oct-25	07-Oct-25
CON-9120	Soli Sampling	2	06-Oct-25	07-Oct-25
CON-7750	Install Field Offices	5	08-Oct-25	15-Oct-25
CON-9140	Excavation	5	08-Oct-25	15-Oct-25
CON-3780	Install Traffic Control Devices - 54th Avenue Street	3	01-May-26	05-May-26
CON-3850	Remove Existing Steel Faced Curb - 54th Avenue Street	3	06-May-26	08-May-26
CON-3860	Remove Existing Asphalt - 54th Avenue Street	4	06-May-26	11-May-26
CON-3870	Install Traffic Control Devices - 2nd Street	5	06-May-26	12-May-26
CON-4040	Install Walls GWB-Mockup Room	3	07-May-26	11-May-26
CON-4270	Install Gypsum Board Ceiling -Mockup Room	3	07-May-26	11-May-26
CON-4380	Install Doors & Hardware-Mockup Room	3	11-May-26	13-May-26
CON-4260	Install Door Frames-Mockup Room	2	12-May-26	13-May-26
CON-3940	Remove Existing Electrical Manhole - 54th Avenue Street	4	12-May-26	15-May-26
CON-3900	Remove Existing Sidewalk - 2nd Street	5	13-May-26	19-May-26
CON-4480	Paint First coat -Mockup Room	2	14-May-26	15-May-26
CON-4640	Flooring Finishes-Mockup Room	2	18-May-26	19-May-26
CON-4080	Install 5' Wide Silva Cells Under Concrete Pavement Strip - 54th Avenue Street	4	18-May-26	21-May-26
CON-4750	Paint Second coat-Mockup Room	2	20-May-26	21-May-26
CON-3950	Install Pedestrian Ramps With Truncated Domes - 2nd Street	6	20-May-26	28-May-26
CON-4930	Install Furniture & Signs -Mockup Room	2	22-May-26	26-May-26
CON-4150	Pavement Replacement - 54th Avenue Street	4	22-May-26	28-May-26
CON-5000	Mockup Room Inspection & Punchlist	5	27-May-26	02-Jun-26
CON-4290	Install New Steel Faced Curb - 54th Avenue Street	4	29-May-26	03-Jun-26
CON-4300	Install Pedestrian Ramps With Truncated Domes - 54th Avenue Street	4	29-May-26	03-Jun-26
CON-4090	Remove Existing Steel Faced Curb - 2nd Street	6	29-May-26	05-Jun-26
CON-4400	Install 4" Concrete Sidewalk - 54th Avenue Street	5	04-Jun-26	10-Jun-26
CON-4410	Install 7" Concrete Sidewalk - 54th Avenue Street	5	04-Jun-26	10-Jun-26
CON-4160	Install New Steel Faced Curb - 2nd Street	6	08-Jun-26	15-Jun-26
CON-4170	Install 4" Concrete Sidewalk - 2nd Street	7	08-Jun-26	16-Jun-26
CON-4560	Install Pavement Marking - 54th Avenue Street	3	11-Jun-26	15-Jun-26
CON-4580	Remove Traffic Control Devices - 54th Avenue Street	3	16-Jun-26	18-Jun-26
CON-4310	Install 7" Concrete Sidewalk - 2nd Street	6	16-Jun-26	24-Jun-26
CON-4420	Remove Traffic Control Devices - 2nd Street	5	25-Jun-26	01-Jul-26
CON-4660	Excavation - Drainage Work - Building Perimeter	3	02-Jul-26	07-Jul-26
CON-4740	Install Flood Barrier Wall - Drainage Work - Building Perimeter	3	08-Jul-26	10-Jul-26
CON-4860	Install Drilled Caisson Supported Ventilation Structure - Drainage Work - Building Perimeter	3	13-Jul-26	15-Jul-26

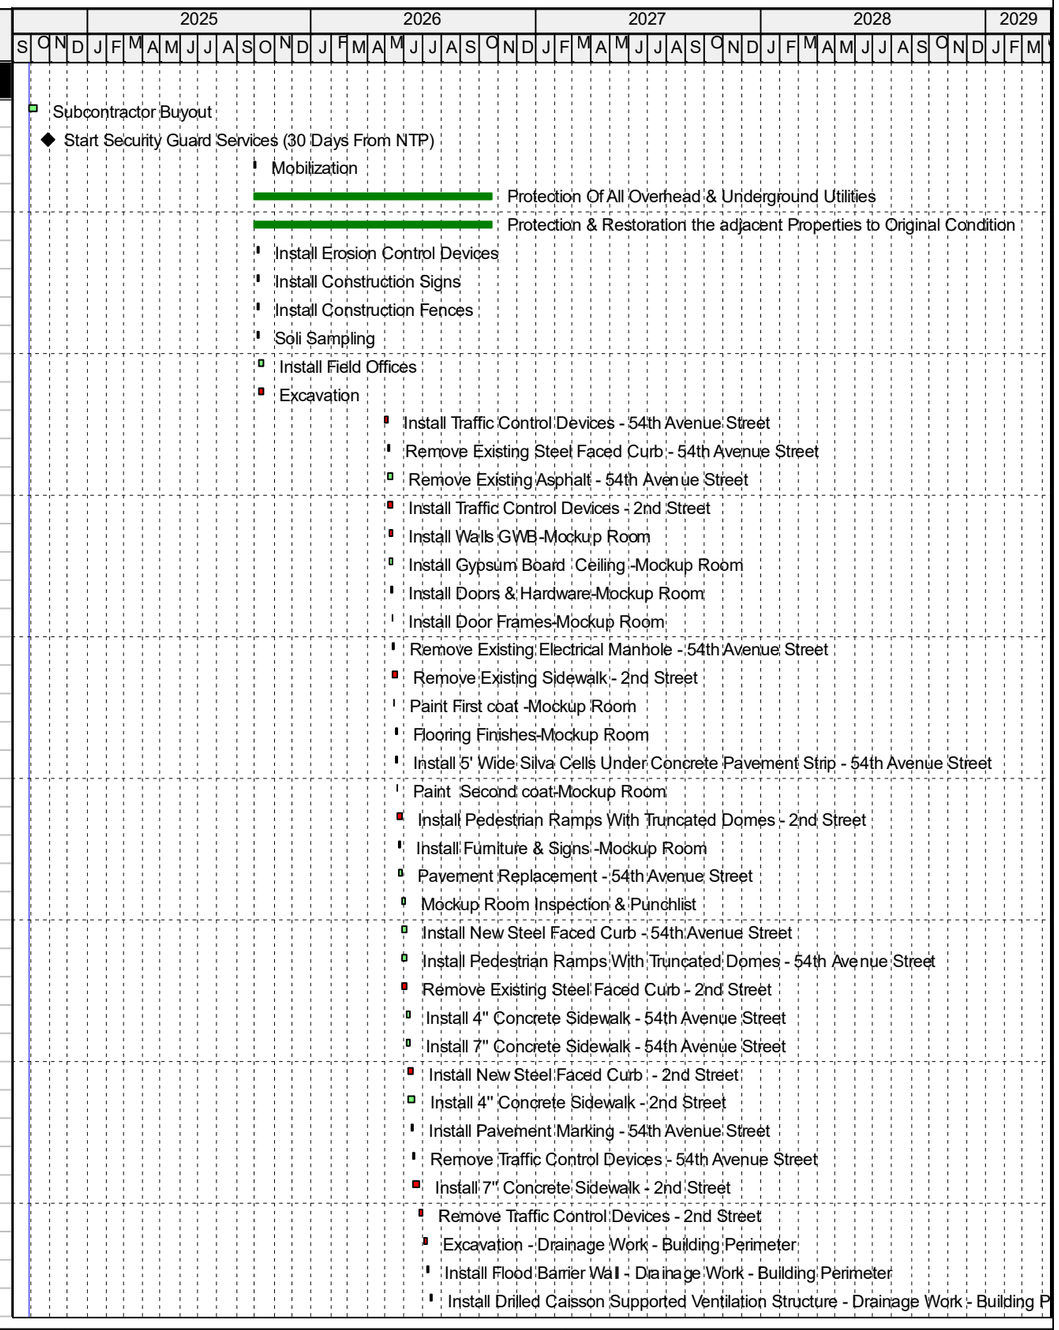

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
CON-4980	Install 4" & 6" & 10" & 12" DIP - Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-9170	Install 8" Combined Water Service (2nd Street)- Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-9180	Install 6" Fire Water Service (54th Avenue Street)- Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-5190	Install Catch Basin - Drainage Work - Building Perimeter	2	21-Jul-26	22-Jul-26
CON-5290	Install Storm Inlet With Hood & Storm Hood - Drainage Work - Building Perimeter	2	23-Jul-26	24-Jul-26
CON-5400	Install Trench Drain - Drainage Work - Building Perimeter	1	27-Jul-26	27-Jul-26
CON-9160	Excavate for Footings - Playground Area & Fences - Building Perimeter	2	28-Jul-26	29-Jul-26
CON-9010	Remove Steel Plate Protection over NYPA Easement - Playground Area & Fences - Building Perimeter	1	28-Jul-26	28-Jul-26
CON-9190	F/R/P Playground Equipment Footings - Playground Area & Fences - Building Perimeter	2	30-Jul-26	31-Jul-26
CON-5470	Install Flush Concrete Curb - Playground Area & Fences - Building Perimeter	3	03-Aug-26	05-Aug-26
CON-5420	Install Asphalt Pavement - Playground Area & Fences - Building Perimeter	2	04-Aug-26	05-Aug-26
CON-5600	Install Concrete Pavement Pedestrian Ramp With Painted Black Handrails - Playground Area & Fences - Building Perimeter	3	06-Aug-26	10-Aug-26
CON-5650	Install Playground Rubber Tile Safety Surface - Playground Area & Fences - Building Perimeter	3	11-Aug-26	13-Aug-26
CON-5800	Install Painted Asphalt Pavement & Painted Games On Asphalt Surface - Playground Area & Fences - Building Perimeter	3	14-Aug-26	18-Aug-26
CON-5850	Install Colored Athletic Wearing Surface Color - Playground Area & Fences - Building Perimeter	2	19-Aug-26	20-Aug-26
CON-5990	Install Playground Equipment - Playground Area & Fences - Building Perimeter	7	21-Aug-26	31-Aug-26
CON-6140	Install Basketball Hoop - Playground Area & Fences - Building Perimeter	1	01-Sep-26	01-Sep-26
CON-6190	Install Wrought Iron Fence Double Gate - Playground Area - Building Perimeter	3	02-Sep-26	04-Sep-26
CON-6270	Install Chain Link Fence - Playground Area & Fences - Building Perimeter	3	08-Sep-26	10-Sep-26
Building Area		231	16-Oct-25	17-Sep-26
CON-9898	Install Gas Permeable Aggregate -1st Floor	3	16-Oct-25	20-Oct-25
CON-98947	Install 4" slotted schedule 80 PVC Piping -1st Floor	3	16-Oct-25	20-Oct-25
CON-9888	Install Liquid Boot VI-20 Geomembrane -1st Floor	2	21-Oct-25	22-Oct-25
CON-1020	Install 60 Dry MILS Liquid Boot -1st Floor	3	23-Oct-25	27-Oct-25
CON-9777	Install Liquid Ultrashield G-1000 -1st Floor	2	24-Oct-25	27-Oct-25
CON-1040	F/R/P Concrete Walls & Beams -1st Floor	10	28-Oct-25	10-Nov-25
CON-1050	Install Underground Conduits & Wires -1st Floor	6	12-Nov-25	19-Nov-25
CON-1060	Backfilling & Compaction -1st Floor	6	12-Nov-25	19-Nov-25
CON-1070	F/R/P SOG -1st Floor	10	20-Nov-25	04-Dec-25
CON-4920	Install Floor Drains & Clean-outs -1st Floor	5	27-Nov-25	04-Dec-25
CON-99327	Install Lightning Protection System-1st Floor	2	03-Dec-25	04-Dec-25
CON-98787	Install Steel Columns -1st Floor	7	05-Dec-25	15-Dec-25
CON-1090	Install Trusses -1st Floor	3	16-Dec-25	18-Dec-25
CON-1100	Install Framing Beams -1st Floor	4	16-Dec-25	19-Dec-25
CON-3160	Install Floor Drains & Clean-outs -2nd Floor	5	19-Dec-25	26-Dec-25
CON-1110	Install Metal Deck Slab -2nd Floor	4	22-Dec-25	26-Dec-25
CON-1130	Install MEP Hangers & Sleeves- 2nd Floor	4	22-Dec-25	26-Dec-25
CON-1150	Install Steel Canopy Framing -2nd Floor	5	29-Dec-25	05-Jan-26
CON-1160	Hoist Material Design	10	29-Dec-25	12-Jan-26
CON-1170	Install Steel Columns -2nd Floor	3	29-Dec-25	31-Dec-25
CON-3270	Install Temporary Standpipe	9	29-Dec-25	09-Jan-26
CON-1190	Install Trusses -2nd Floor	4	02-Jan-26	07-Jan-26
CON-1200	Install Framing Beams -2nd Floor	5	02-Jan-26	08-Jan-26
CON-3320	Install Floor Drains & Clean-outs -3rd Floor	5	08-Jan-26	14-Jan-26

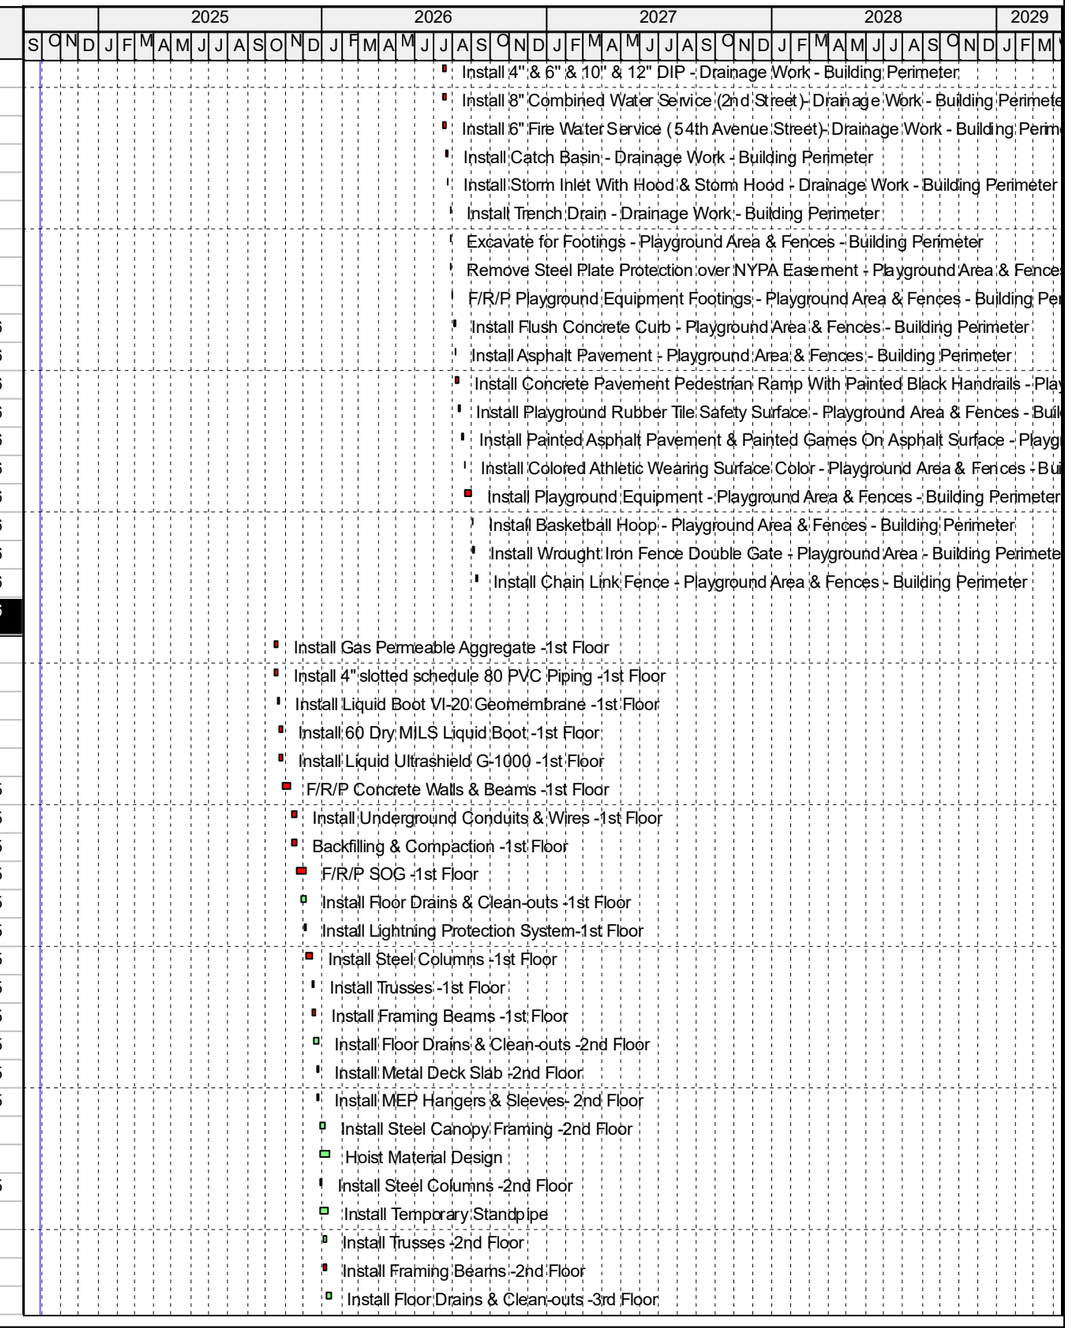

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1230	Install MEP Hangers & Sleeves-3rd Floor	4	09-Jan-26	14-Jan-26
CON-1210	Install Metal Deck Slab - 3rd Floor	4	09-Jan-26	14-Jan-26
CON-1250	Approval of Hoist Design	7	13-Jan-26	19-Jan-26
CON-1240	Install Steel Columns - 3rd Floor	4	15-Jan-26	21-Jan-26
CON-1280	Install Elevator Hoist Pad	5	20-Jan-26	26-Jan-26
CON-1260	Install Trusses - 3rd Floor	3	22-Jan-26	26-Jan-26
CON-1270	Install Framing Beams - 3rd Floor	5	22-Jan-26	28-Jan-26
CON-1320	Erect Material Hoist	5	27-Jan-26	02-Feb-26
CON-3530	Install Floor Drains & Clean-outs -4th Floor	5	28-Jan-26	03-Feb-26
CON-99277	Install Steel Stairs -1st Floor	7	28-Jan-26	05-Feb-26
CON-1310	Install MEP Hangers & Sleeves-4th Floor	4	29-Jan-26	03-Feb-26
CON-1290	Install Metal Deck Slab - 4th Floor	4	29-Jan-26	03-Feb-26
CON-1330	Install Steel Columns - 4th Floor	4	04-Feb-26	09-Feb-26
CON-99287	Install Steel Stairs -2nd Floor	3	06-Feb-26	10-Feb-26
CON-1360	Install Trusses - 4th Floor	3	10-Feb-26	12-Feb-26
CON-1370	Install Framing Beams - 4th Floor	5	10-Feb-26	17-Feb-26
CON-99297	Install Steel Stairs- 3rd Floor	4	11-Feb-26	17-Feb-26
CON-3610	Install Floor Drains & Clean-outs -5th Floor	5	13-Feb-26	20-Feb-26
CON-1400	Install MEP Hangers & Sleeves-5th Floor	4	17-Feb-26	20-Feb-26
CON-1380	Install Metal Deck Slab - 5th Floor	3	18-Feb-26	20-Feb-26
CON-1410	Install Duct Risers-2nd Floor	1	23-Feb-26	23-Feb-26
CON-1420	Layout -2nd Floor	3	23-Feb-26	25-Feb-26
CON-1430	Install Unit Masonry Mock-Up	1	23-Feb-26	23-Feb-26
CON-1440	Install Steel Columns - 5th Floor	3	23-Feb-26	25-Feb-26
CON-1460	F/R/P Piers - 5th Floor	5	23-Feb-26	27-Feb-26
CON-99307	Install Steel Stairs - 4th Floor	4	23-Feb-26	26-Feb-26
CON-1480	Rough-in Duct Work -2nd Floor	4	24-Feb-26	27-Feb-26
CON-1490	Install Duct Risers -3rd Floor	2	24-Feb-26	25-Feb-26
CON-1500	Install Mechanical Piping Risers-2nd Floor	2	24-Feb-26	25-Feb-26
CON-1510	Duct Leak Test -2nd Floor	2	24-Feb-26	25-Feb-26
CON-1470	Approve Unit Masonry Mock-Up	4	24-Feb-26	27-Feb-26
CON-1560	Install Duct Risers -4th Floor	2	26-Feb-26	27-Feb-26
CON-1520	Install Top & Bottom Track-2nd Floor	4	26-Feb-26	03-Mar-26
CON-1530	Layout -3rd Floor	3	26-Feb-26	02-Mar-26
CON-1770	Install Roof Drains & Clean outs -Roof Floor	5	26-Feb-26	04-Mar-26
CON-1580	Install Plumbing Risers -2nd Floor	2	26-Feb-26	27-Feb-26
CON-1590	Install Mechanical Piping Risers -3rd Floor	2	26-Feb-26	27-Feb-26
CON-1600	Duct Leak Test -3rd Floor	2	26-Feb-26	27-Feb-26
CON-1540	Install Trusses - 5th Floor	2	26-Feb-26	27-Feb-26
CON-1550	Install Framing Beams - 5th Floor	3	26-Feb-26	02-Mar-26
CON-1610	Install MEP Hangers & Sleeves-Roof Floor	4	27-Feb-26	04-Mar-26
CON-99317	Install Steel Stairs - 5th Floor	3	27-Feb-26	03-Mar-26
CON-1850	Rough-in Hot Water Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1860	Rough-in Hot Glycol Piping-2nd Floor	7	02-Mar-26	10-Mar-26

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1870	Rough-in Chilled Glycol Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1880	Rough-in Refrigerant Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1890	Rough-in Duct Work -3rd Floor	5	02-Mar-26	06-Mar-26
CON-1630	Install Duct Risers-5th Floor	2	02-Mar-26	03-Mar-26
CON-1570	Install CMU Walls -2nd Floor	3	02-Mar-26	04-Mar-26
CON-1680	Install Plumbing Risers -3rd Floor	2	02-Mar-26	03-Mar-26
CON-1690	Install Mechanical Piping Risers -4th Floor	2	02-Mar-26	03-Mar-26
CON-1700	Duct Leak Test -4th Floor	2	02-Mar-26	03-Mar-26
CON-1710	Install Power Risers-2nd Floor	2	02-Mar-26	03-Mar-26
CON-1740	Install SSDS Risers -SSDS System -2nd Floor	2	02-Mar-26	03-Mar-26
CON-1620	Install Dunnage - 5th Floor	8	02-Mar-26	11-Mar-26
CON-1670	Layout -4th Floor	3	03-Mar-26	05-Mar-26
CON-1720	Install Metal Deck Slab -Roof Floor	2	03-Mar-26	04-Mar-26
CON-1180	Spray Fireproofing - 1st Floor	5	03-Mar-26	09-Mar-26
CON-1640	Install Wall Steel Studs & Framing-2nd Floor	5	04-Mar-26	10-Mar-26
CON-1650	Install Top & Bottom Track-3rd Floor	4	04-Mar-26	09-Mar-26
CON-1780	Install Plumbing Risers -4th Floor	2	04-Mar-26	05-Mar-26
CON-1790	Install Mechanical Piping Risers-5th Floor	2	04-Mar-26	05-Mar-26
CON-1800	Install Low Voltage Risers-2nd Floor	2	04-Mar-26	05-Mar-26
CON-1810	Duct Leak Test -5th Floor	1	04-Mar-26	04-Mar-26
CON-1820	Install Power Risers-3rd Floor	2	04-Mar-26	05-Mar-26
CON-1840	Install SSDS Risers -SSDS System -3rd Floor	2	04-Mar-26	05-Mar-26
CON-1750	F/R/P Concrete Columns -Bulkhead	3	05-Mar-26	09-Mar-26
CON-1760	Install Dunnage-Roof Floor	8	05-Mar-26	16-Mar-26
CON-1660	Install CMU Walls -3rd Floor	3	05-Mar-26	09-Mar-26
CON-2070	Install Roof Drains & Clean outs - Mechanical Work - Roof Bulkhead	5	05-Mar-26	11-Mar-26
CON-99347	Install Lightning Protection System - Roof Floor	6	05-Mar-26	12-Mar-26
CON-1930	Layout -5th Floor	3	06-Mar-26	10-Mar-26
CON-1940	Install Plumbing Risers-5th Floor	1	06-Mar-26	06-Mar-26
CON-1950	Install Low Voltage Risers-3rd Floor	2	06-Mar-26	09-Mar-26
CON-1960	Install Power Risers-4th Floor	2	06-Mar-26	09-Mar-26
CON-1970	Install SSDS Risers -SSDS System -4th Floor	2	06-Mar-26	09-Mar-26
CON-2160	Rough-in Refrigerant Piping-3rd Floor	7	09-Mar-26	17-Mar-26
CON-2170	Rough-in Duct Work -4th Floor	5	09-Mar-26	13-Mar-26
CON-2000	Install SSDS Risers -SSDS System -5th Floor	1	09-Mar-26	09-Mar-26
CON-1980	F/R/P Bulkhead Slab -Bulkhead	2	10-Mar-26	11-Mar-26
CON-1900	Install Wall Steel Studs & Framing-3rd Floor	5	10-Mar-26	16-Mar-26
CON-1910	Install Top & Bottom Track-4th Floor	4	10-Mar-26	13-Mar-26
CON-1920	Install CMU Walls -4th Floor	3	10-Mar-26	12-Mar-26
CON-2040	Install Low Voltage Risers-4th Floor	2	10-Mar-26	11-Mar-26
CON-2050	Install Power Risers-5th Floor	3	10-Mar-26	12-Mar-26
CON-1220	Spray Fireproofing - 2nd Floor	5	10-Mar-26	16-Mar-26
CON-2130	Rough-in Hot Water Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-2140	Rough-in Hot Glycol Piping-3rd Floor	7	11-Mar-26	19-Mar-26

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2150	Rough-in Chilled Glycol Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-2180	Rough-in Power Conduits -2nd Floor	6	11-Mar-26	18-Mar-26
CON-2060	Install Hoist Beam-Bulkhead	1	12-Mar-26	12-Mar-26
CON-2190	Install Electric Unit Heater EUH - Mechanical Work - Roof Bulkhead	5	12-Mar-26	18-Mar-26
CON-2030	Install CMU Walls -5th Floor	3	13-Mar-26	17-Mar-26
CON-2100	Install Low Voltage Risers-5th Floor	3	13-Mar-26	17-Mar-26
CON-99337	Install Lightning Protection system -5th Floor	3	13-Mar-26	17-Mar-26
CON-2290	Rough-in Refrigerant Piping-4th Floor	7	16-Mar-26	24-Mar-26
CON-2300	Rough-in Duct Work-5th Floor	5	16-Mar-26	20-Mar-26
CON-2010	Install Wall Steel Studs & Framing-4th Floor	5	16-Mar-26	20-Mar-26
CON-2020	Install Top & Bottom Track-5th Floor	4	16-Mar-26	19-Mar-26
CON-2310	Install Ceiling Hangers & Supports-2nd Floor	4	16-Mar-26	19-Mar-26
CON-2120	Install Air Cooled Chiller CH-1 -Roof Floor	7	17-Mar-26	25-Mar-26
CON-1300	Spray Fireproofing - 3rd Floor	5	17-Mar-26	23-Mar-26
CON-3980	Install VAV Boxes & Sound Attenuator Devices-2nd Floor	5	19-Mar-26	25-Mar-26
CON-2320	Rough-in Power Conduits-3rd Floor	6	19-Mar-26	26-Mar-26
CON-2330	Rough-in Low-Voltage Conduits -2nd Floor	6	19-Mar-26	26-Mar-26
CON-2340	Power Wires Pulling -2nd Floor	6	19-Mar-26	26-Mar-26
CON-2230	Install Emergency Generator -Bulkhead	7	19-Mar-26	27-Mar-26
CON-2260	Rough-in Hot Water Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-2270	Rough-in Hot Glycol Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-2280	Rough-in Chilled Glycol Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-2390	Install Ceiling Hangers & Supports-3rd Floor	4	20-Mar-26	25-Mar-26
CON-2470	Rough-in Refrigerant Piping-5th Floor	7	23-Mar-26	31-Mar-26
CON-2200	Install Wall Steel Studs & Framing-5th Floor	5	23-Mar-26	27-Mar-26
CON-1390	Spray Fireproofing - 4th Floor	5	24-Mar-26	30-Mar-26
CON-4140	Install VAV Boxes & Sound Attenuator Devices-3rd Floor	5	26-Mar-26	01-Apr-26
CON-2550	Install Ceiling Hangers & Supports-4th Floor	4	26-Mar-26	31-Mar-26
CON-2350	Install Air Cooled Chiller CH-2 -Roof Floor	7	26-Mar-26	03-Apr-26
CON-2360	Install Smoke Purge Fan SPF - Mechanical Work - Roof Bulkhead	3	26-Mar-26	30-Mar-26
CON-2640	Install Grounding Bars - 3rd Floor IDF Room	5	27-Mar-26	02-Apr-26
CON-2480	Rough-in Power Conduits-4th Floor	6	27-Mar-26	03-Apr-26
CON-2490	Low Voltage Wires Pulling -2nd Floor	6	27-Mar-26	03-Apr-26
CON-2500	Rough-in Low-Voltage Conduits-3rd Floor	6	27-Mar-26	03-Apr-26
CON-2510	Power Wires Pulling-3rd Floor	6	27-Mar-26	03-Apr-26
CON-2520	Install Voice Rack - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2530	Install Data Rack - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2540	Install Ground Bus Bar - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2440	Rough-in Hot Water Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-2450	Rough-in Hot Glycol Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-2460	Rough-in Chilled Glycol Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-1730	Spray Fireproofing - 5th Floor	3	31-Mar-26	02-Apr-26
CON-2620	Install Ceiling Hangers & Supports-5th Floor	4	01-Apr-26	06-Apr-26
CON-4220	Install VAV Boxes & Sound Attenuator Devices-4th Floor	5	02-Apr-26	08-Apr-26

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2800	Install Data rack - 3rd Floor IDF Room	8	03-Apr-26	14-Apr-26
CON-2830	Install IPDVS Equipment Rack - 3rd Floor IDF Room	4	03-Apr-26	08-Apr-26
CON-2630	Rough-in Gas Risers -2nd Floor	4	06-Apr-26	09-Apr-26
CON-2810	Install Grounding Bars - 4th Floor IDF Room	5	06-Apr-26	10-Apr-26
CON-2650	Install Data Rack - 4th Floor IDF Room	7	06-Apr-26	14-Apr-26
CON-2660	Install Voice Rack - 4th Floor IDF Room	5	06-Apr-26	10-Apr-26
CON-2670	Install Wiring Devices -2nd Floor	7	06-Apr-26	14-Apr-26
CON-2680	Rough-in Power Conduits -5th Floor	6	06-Apr-26	13-Apr-26
CON-2690	Low Voltage Wires Pulling -3rd Floor	6	06-Apr-26	13-Apr-26
CON-2700	Rough-in Low-Voltage Conduits-4th Floor	6	06-Apr-26	13-Apr-26
CON-2710	Power Wires Pulling-4th Floor	6	06-Apr-26	13-Apr-26
CON-2900	Install Duct Risers-1st Floor	1	07-Apr-26	07-Apr-26
CON-2910	Layout -1st Floor	3	07-Apr-26	09-Apr-26
CON-2920	Pour Sloped Concrete Fill -5th Floor Roof	2	07-Apr-26	08-Apr-26
CON-3060	Install Mechanical Piping Risers-1st Floor	2	08-Apr-26	09-Apr-26
CON-3070	Duct Leak Test -1st Floor	1	08-Apr-26	08-Apr-26
CON-3120	Rough-in Duct Work -1st Floor	4	09-Apr-26	14-Apr-26
CON-4330	Install VAV Boxes & Sound Attenuator Devices-5th Floor	5	09-Apr-26	15-Apr-26
CON-3010	Pour Sloped Concrete Fill -Roof Floor	2	09-Apr-26	10-Apr-26
CON-3080	Install Top & Bottom Track -1st Floor	4	10-Apr-26	15-Apr-26
CON-3090	Install CMU Walls -1st Floor	3	10-Apr-26	14-Apr-26
CON-3140	Install Plumbing Risers -1st Floor	2	10-Apr-26	13-Apr-26
CON-2740	Rough-in Domestic Water Piping -2nd Floor	4	10-Apr-26	15-Apr-26
CON-2750	Rough-in Gas Risers-3rd Floor	4	10-Apr-26	15-Apr-26
CON-2760	Install IPDVS Equipment Rack - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2770	Install Ladder Rack Cable Tray - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2780	Install BACnet Data Cabinet - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2820	Install Cable Ladder - 4th Floor IDF Room	5	13-Apr-26	17-Apr-26
CON-3210	Install Fluid-Applied Protected Membrane Mock-Up	2	13-Apr-26	14-Apr-26
CON-2840	Install Main Sound Rack - 34th Floor IDF Room	5	13-Apr-26	17-Apr-26
CON-3230	Install SSDS Risers -SSDS System -1st Floor	2	14-Apr-26	15-Apr-26
CON-3260	Install Power Risers-1st Floor	2	14-Apr-26	15-Apr-26
CON-2950	Rough-in Low-Voltage Conduits-5th Floor	6	14-Apr-26	21-Apr-26
CON-2960	Power Wires Pulling-5th Floor	6	14-Apr-26	21-Apr-26
CON-3460	Rough-in Hot Water Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3470	Rough-in Hot Glycol Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3480	Rough-in Chilled Glycol Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3490	Rough-in Refrigerant Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3520	Install Ceiling Hangers & Supports -1st Floor	4	15-Apr-26	20-Apr-26
CON-3250	Install Voice Rack - 3rd Floor IDF Room	5	15-Apr-26	21-Apr-26
CON-2930	Install Wiring Devices -3rd Floor	7	15-Apr-26	23-Apr-26
CON-2940	Low Voltage Wires Pulling-4th Floor	6	15-Apr-26	22-Apr-26
CON-3300	Approve Fluid-Applied Protected Membrane Mock-Up	4	15-Apr-26	20-Apr-26
CON-3970	Install VAV Boxes & Sound Attenuator Devices- 1st Floor	5	16-Apr-26	22-Apr-26

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2850	Install Electric Unit Heaters -2nd Floor	5	16-Apr-26	22-Apr-26
CON-3240	Install Wall Steel Studs & Framing -1st Floor	5	16-Apr-26	22-Apr-26
CON-2870	Rough-in Sanitary & Vent Piping -2nd Floor	4	16-Apr-26	21-Apr-26
CON-2880	Rough-in Domestic Water Piping -3rd Floor	4	16-Apr-26	21-Apr-26
CON-2890	Rough-in Gas Risers -4th Floor	4	16-Apr-26	21-Apr-26
CON-3350	Install Low Voltage Risers-1st Floor	2	16-Apr-26	17-Apr-26
CON-9070	In-Wall Inspection-2nd Floor	2	16-Apr-26	17-Apr-26
CON-3110	Install IPDVS Equipment Rack - 4th Floor IDF Room	5	20-Apr-26	24-Apr-26
CON-3430	Install Hot Fluid Applied Membrane -Roof Floor	3	21-Apr-26	23-Apr-26
CON-3440	Install Hot Fluid Applied Membrane -5th Floor Roof	4	21-Apr-26	24-Apr-26
CON-3760	Rough-in Power Conduits -1st Floor	4	21-Apr-26	24-Apr-26
CON-3020	Rough-in Storm Piping -2nd Floor	4	22-Apr-26	27-Apr-26
CON-3030	Rough-in Sanitary & Vent Piping -3rd Floor	4	22-Apr-26	27-Apr-26
CON-3040	Rough-in Domestic Water Piping -4th Floor	4	22-Apr-26	27-Apr-26
CON-3050	Rough-in Gas Risers & Piping -5th Floor	4	22-Apr-26	27-Apr-26
CON-3550	Install Cable Ladder - 3rd Floor IDF Room	5	22-Apr-26	28-Apr-26
CON-3570	Install Main Sound Rack - 3rd Floor IDF Room	5	22-Apr-26	28-Apr-26
CON-9080	In-Wall Inspection -3rd Floor	2	22-Apr-26	23-Apr-26
CON-3130	Install Electric Unit Heaters -3rd Floor	5	23-Apr-26	29-Apr-26
CON-3290	Low Voltage Wires Pulling-5th Floor	6	23-Apr-26	30-Apr-26
CON-3150	Install Convector Heater CV - Mechanical Work - 2nd Floor	5	23-Apr-26	29-Apr-26
CON-4730	Rough-in Conduits & Wires - Electric Service Room	6	23-Apr-26	30-Apr-26
CON-3600	Install Drainage Panels- Roof Floor	3	24-Apr-26	28-Apr-26
CON-3280	Install Wiring Devices -4th Floor	7	24-Apr-26	04-May-26
CON-3580	Install 6" Thick Rigid Insulation -5th Floor Roof	3	27-Apr-26	29-Apr-26
CON-3910	Install Grounding System -1st Floor	5	27-Apr-26	01-May-26
CON-3920	Rough-in Low-Voltage Conduits-1st Floor	4	27-Apr-26	30-Apr-26
CON-3930	Power Wires Pulling-1st Floor	4	27-Apr-26	30-Apr-26
CON-3170	Rough-in Storm Piping -3rd Floor	4	28-Apr-26	01-May-26
CON-3180	Rough-in Sanitary & Vent Piping -4th Floor	4	28-Apr-26	01-May-26
CON-3190	Rough-in Domestic Water Piping -5th Floor	4	28-Apr-26	01-May-26
CON-3200	Plumbing Pressure Testing -2nd Floor	5	28-Apr-26	04-May-26
CON-9090	In-Wall Inspection -4th Floor	7	28-Apr-26	06-May-26
CON-3730	Install 6" Thick Rigid Insulation -Roof Floor	3	29-Apr-26	01-May-26
CON-3740	Install Ground Bus Bar - 1st Floor MDF Room	6	29-Apr-26	06-May-26
CON-3420	Install Electric Unit Heaters -4th Floor	5	30-Apr-26	06-May-26
CON-3700	Install Drainage -5th Floor Roof	3	30-Apr-26	04-May-26
CON-3710	Roof Flood Test -5th Floor Roof	4	30-Apr-26	05-May-26
CON-3450	Install Air Conditioning Unit AC - Mechanical Work - 2nd Floor	4	30-Apr-26	05-May-26
CON-4180	Low Voltage Wires Pulling -1st Floor	4	01-May-26	06-May-26
CON-4960	F/R/P Concrete Pad - Electric Service Room	6	01-May-26	08-May-26
CON-3310	Install 4" Standpipe -2nd Floor	4	04-May-26	07-May-26
CON-3330	Rough-in Storm Piping -4th Floor	4	04-May-26	07-May-26
CON-3340	Rough-in Sanitary & Vent Piping -5th Floor	4	04-May-26	07-May-26

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3840	Roof Flood Test -Roof Floor	3	04-May-26	06-May-26
CON-3400	Install Hot Water Circulation Pump -5th Floor	5	04-May-26	08-May-26
CON-3410	Install Electric Hot Water Heater (EWH-1) -5th Floor	5	04-May-26	08-May-26
CON-9100	In-Wall Inspections -5th Floor	7	04-May-26	12-May-26
CON-3660	Install Wiring Devices -5th Floor	8	05-May-26	14-May-26
CON-3360	Plumbing Pressure Testing -3rd Floor	5	05-May-26	11-May-26
CON-3820	Install Filter Fabric -5th Floor Roof	3	06-May-26	08-May-26
CON-3640	Install Electric Unit Heaters -5th Floor	3	07-May-26	11-May-26
CON-4020	Install Filter Fabric -Roof Floor	3	07-May-26	11-May-26
CON-4460	Rough-in Gas Risers -1st Floor	4	07-May-26	12-May-26
CON-4110	Install Voice Rack - 1st Floor MDF Room	6	07-May-26	14-May-26
CON-4050	Plumbing Piping Insulation -2nd Floor	5	07-May-26	13-May-26
CON-4070	Install Duct Insulation -2nd Floor	8	07-May-26	18-May-26
MIL-1760	Start Elevator Work	0	07-May-26	
CON-4500	Install SSDS Control Panel -1st Floor	5	07-May-26	13-May-26
CON-99357	Install CMU Wall for Shaft -Elevator Machine Room	10	07-May-26	20-May-26
CON-3500	Rough-in Main Sprinkler Piping -2nd Floor	5	08-May-26	14-May-26
CON-3510	Install 4" Standpipe -3rd Floor	4	08-May-26	13-May-26
CON-3540	Rough-in Storm Piping -5th Floor	4	08-May-26	13-May-26
CON-3960	Install Concrete Pavers -5th Floor Roof	3	11-May-26	13-May-26
CON-5180	Install Service Switchboard "SS-A"- Electric Service Room	5	11-May-26	15-May-26
CON-3560	Plumbing Pressure Testing -4th Floor	5	12-May-26	18-May-26
CON-4210	Install Concrete Pavers -Roof Floor	4	12-May-26	15-May-26
CON-4590	Rough-in Domestic Water Piping-1st Floor	4	13-May-26	18-May-26
CON-3650	Install 4" Standpipe -4th Floor	4	14-May-26	19-May-26
CON-3590	Plumbing Pressure Testing -5th Floor	5	14-May-26	20-May-26
CON-4190	Plumbing Piping Insulation -3rd Floor	5	14-May-26	20-May-26
CON-3670	Rough-in Branch Sprinkler Piping -2nd Floor	5	15-May-26	21-May-26
CON-3680	Rough-in Sprinkler Heads -2nd Floor	5	15-May-26	21-May-26
CON-3720	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -2nd Floor	5	15-May-26	21-May-26
CON-3690	Rough-in Main Sprinkler Piping-3rd Floor	5	15-May-26	21-May-26
CON-4510	Install Sound Rack - 1st Floor MDF Room	6	15-May-26	22-May-26
CON-4120	Install Project Connect Cabinet - 1st Floor MDF Room	8	15-May-26	27-May-26
CON-4470	Install Wiring Devices -1st Floor	7	15-May-26	26-May-26
CON-5510	Install Leak Detector - Electric Service Room	3	18-May-26	20-May-26
CON-4690	Rough-in Sanitary & Vent Piping -1st Floor	4	19-May-26	22-May-26
CON-4320	Install Duct Insulation -3rd Floor	8	19-May-26	29-May-26
CON-9110	In-Wall Inspection -1st Floor	2	19-May-26	20-May-26
CON-3770	Install 4" Standpipe -5th Floor	4	20-May-26	26-May-26
CON-4390	Plumbing Piping Insulation -4th Floor	5	21-May-26	28-May-26
CON-5610	Install Sprinkler Booster Pump - Electric Service Room	4	21-May-26	27-May-26
CON-99167	Install Elevator Guide Rails -Elevator Machine Room	8	21-May-26	02-Jun-26
CON-3790	Rough-in Branch Sprinkler Piping -3rd Floor	5	22-May-26	29-May-26
CON-3800	Rough-in Sprinkler Heads -3rd Floor	5	22-May-26	29-May-26

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3880	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-3rd Floor	5	22-May-26	29-May-26
CON-3810	Rough-in Main Sprinkler Piping-4th Floor	5	22-May-26	29-May-26
CON-3830	Sprinklers Air Testing-2nd Floor	5	22-May-26	29-May-26
CON-4760	Rough-in Storm Piping -1st Floor	4	26-May-26	29-May-26
CON-4520	Install Data Rack - 1st Floor MDF Room	6	26-May-26	02-Jun-26
CON-3890	Install 4" Standpipe -Roof	4	27-May-26	01-Jun-26
CON-4030	Install Gypsum Board Walls-2nd Floor	5	27-May-26	02-Jun-26
CON-4200	Tape Gypsum Board -2nd Floor	4	28-May-26	02-Jun-26
CON-5640	Install Fire Alarm Normal ATS - Electric Service Room	4	28-May-26	02-Jun-26
CON-4530	Plumbing Piping Insulation -5th Floor	5	29-May-26	04-Jun-26
CON-4890	F/R/P Concrete Pads -Fuel Oil Room	2	01-Jun-26	02-Jun-26
CON-4900	Rough-in Fuel Oil Piping -Fuel Oil Room	3	01-Jun-26	03-Jun-26
CON-3990	Rough-in Branch Sprinkler Piping -4th Floor	5	01-Jun-26	05-Jun-26
CON-4000	Rough-in Sprinkler Heads -4th Floor	5	01-Jun-26	05-Jun-26
CON-4100	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-4th Floor	5	01-Jun-26	05-Jun-26
CON-4010	Rough-in Main Sprinkler Piping -5th Floor	5	01-Jun-26	05-Jun-26
CON-4060	Sprinklers Air Testing-3rd Floor	5	01-Jun-26	05-Jun-26
CON-4570	Install Duct Insulation -4th Floor	8	01-Jun-26	10-Jun-26
CON-1120	Install Firestopping Mock-Up	2	01-Jun-26	02-Jun-26
CON-4940	Install Duplex Domestic Water Booster Pump System (BP-1&BP-2) -1st Floor	8	01-Jun-26	10-Jun-26
CON-4950	Install Duplex Ejector Pump System (EJ-1&EJ-2) -1st Floor	8	01-Jun-26	10-Jun-26
CON-4910	Install 4" Standpipe -1st Floor	4	02-Jun-26	05-Jun-26
CON-4990	Install Fuel Oil Storage Tank (FOT-1) - Fuel Oil Room	3	03-Jun-26	05-Jun-26
CON-4350	Install Ceramic Wall Tiles at Corridor-2nd Floor	7	03-Jun-26	11-Jun-26
CON-4360	Install Gypsum Board Walls-3rd Floor	5	03-Jun-26	09-Jun-26
CON-4370	Install Gypsum Board Ceiling -2nd Floor	6	03-Jun-26	10-Jun-26
CON-2090	Install Elevator Controller #1 -Elevator Machine Room	10	03-Jun-26	16-Jun-26
CON-1140	Approve Firestopping Mock-Up	2	03-Jun-26	04-Jun-26
CON-4550	Install UPS- 1st Floor MDF Room	9	03-Jun-26	15-Jun-26
CON-4130	Install BACnet Data Cabinet- 1st Floor MDF Room	9	03-Jun-26	15-Jun-26
CON-5780	Install Motorized Fire/Smoke Damper & Control Panel - Electric Service Room	5	03-Jun-26	09-Jun-26
CON-5790	Install Main Grounding Bus Bar - Electric Service Room	4	03-Jun-26	08-Jun-26
CON-5020	Rough-in Fuel Oil Fill Piping -Fuel Oil Room	3	04-Jun-26	08-Jun-26
CON-4540	Tape Gypsum Board -3rd Floor	4	04-Jun-26	09-Jun-26
CON-4700	Install Firestopping-2nd Floor	3	05-Jun-26	09-Jun-26
MIL-1750	Start Firestopping	0	05-Jun-26	
CON-2250	Install Air Handling Unit AHU-1 -Roof Floor	5	08-Jun-26	12-Jun-26
CON-5160	Install Fuel Oil Transfer Duplex Pump (FOP-1 & 2) -1st Floor	4	08-Jun-26	11-Jun-26
CON-5030	Rough-in Main Sprinkler Piping -1st Floor	5	08-Jun-26	12-Jun-26
CON-4230	Rough-in Branch Sprinkler Piping -5th Floor	5	08-Jun-26	12-Jun-26
CON-4240	Rough-in Sprinkler Heads -5th Floor	5	08-Jun-26	12-Jun-26
CON-4340	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -5th Floor	5	08-Jun-26	12-Jun-26
CON-4250	Rough-in Main Sprinkler Piping -Roof	5	08-Jun-26	12-Jun-26
CON-4280	Sprinklers Air Testing-4th Floor	5	08-Jun-26	12-Jun-26

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
CON-9130	Install Switch Gear - Electric Service Room	5	08-Jun-26	12-Jun-26
CON-5200	Rough-in Fuel Oil Vent Piping -Fuel Oil Room	4	09-Jun-26	12-Jun-26
CON-4620	Install Gypsum Board Walls-4th Floor	5	10-Jun-26	16-Jun-26
CON-4850	Install Firestopping-3rd Floor	4	10-Jun-26	15-Jun-26
CON-5840	Install Electric Unit Heater EUH-6 - Electric Service Room	4	10-Jun-26	15-Jun-26
CON-4630	Install Gypsum Board Ceiling-3rd Floor	6	11-Jun-26	18-Jun-26
CON-4830	Install First Coat Painting-2nd Floor	5	11-Jun-26	17-Jun-26
CON-5050	Plumbing Pressure Testing -1st Floor	5	11-Jun-26	17-Jun-26
CON-4710	Install Duct Insulation -5th Floor	8	11-Jun-26	23-Jun-26
CON-4720	Tape Gypsum Board -4th Floor	4	11-Jun-26	16-Jun-26
CON-4610	Install Ceramic Wall Tiles at Corridor-3rd Floor	7	12-Jun-26	23-Jun-26
CON-2430	Install Air Handling Unit AHU-2 -Roof Floor	5	15-Jun-26	22-Jun-26
CON-5230	Rough-in Branch Sprinkler Piping -1st Floor	5	15-Jun-26	22-Jun-26
CON-5240	Rough-in Sprinkler Heads -1st Floor	5	15-Jun-26	22-Jun-26
CON-4430	Rough-in Branch Sprinkler Piping -Roof	5	15-Jun-26	22-Jun-26
CON-4440	Rough-in Sprinkler Heads -Roof	5	15-Jun-26	22-Jun-26
CON-4490	Sprinklers Air Testing-5th Floor	5	15-Jun-26	22-Jun-26
CON-5010	Install Firestopping-4th Floor	4	16-Jun-26	22-Jun-26
CON-4780	Install IPDVS Equipment Rack - 1st Floor MDF Room	6	16-Jun-26	24-Jun-26
CON-4810	Install Gypsum Board Walls-5th Floor	5	17-Jun-26	24-Jun-26
CON-2370	Install Elevator Controller #2 -Elevator Machine Room	10	17-Jun-26	01-Jul-26
CON-5120	Install Door Frames & Doors-2nd Floor	5	18-Jun-26	25-Jun-26
CON-5130	Install Lighting Fixtures -2nd Floor	5	18-Jun-26	25-Jun-26
CON-5210	Plumbing Piping Insulation -1st Floor	5	18-Jun-26	25-Jun-26
CON-4970	Tape Gypsum Board -5th Floor	4	18-Jun-26	24-Jun-26
CON-98797	Install Intrusion System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-98847	Install Auxiliary System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-98897	Install Sound Clock System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-4820	Install Gypsum Board Ceiling-4th Floor	6	22-Jun-26	29-Jun-26
CON-5110	Install First Coat Painting-3rd Floor	5	22-Jun-26	26-Jun-26
CON-2560	Install Air Handling Unit AHU-3 -Roof Floor	5	23-Jun-26	29-Jun-26
CON-5270	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -1st Floor	5	23-Jun-26	29-Jun-26
CON-5220	Install Firestopping-5th Floor	4	23-Jun-26	26-Jun-26
CON-4650	Install 3 Way Roof Manifold -Roof	5	23-Jun-26	29-Jun-26
CON-4800	Install Ceramic Wall Tiles at Corridor-4th Floor	7	24-Jun-26	02-Jul-26
CON-4840	Install Duct Insulation -1st Floor	8	24-Jun-26	06-Jul-26
CON-4790	Install Ladder Rack Cable Tray- 1st Floor MDF Room	6	25-Jun-26	02-Jul-26
CON-4450	Install Gypsum Board Walls-1st Floor	6	26-Jun-26	06-Jul-26
CON-5360	Install Flooring Tiles-2nd Floor	5	26-Jun-26	02-Jul-26
CON-5310	Install Fire alarm Sensors and Devises -2nd Floor	5	26-Jun-26	02-Jul-26
CON-5340	Install First Coat Painting-4th Floor	5	29-Jun-26	06-Jul-26
CON-5350	Install Door Frames & Doors-3rd Floor	5	29-Jun-26	06-Jul-26
CON-5370	Install Lighting Fixtures -3rd Floor	6	29-Jun-26	07-Jul-26
CON-98807	Install Intrusion System Components-3rd Floor	6	29-Jun-26	07-Jul-26

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
CON-98857	Install Auxiliary System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-98907	Install Sound Clock System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-2720	Install Air Handling Unit AHU-4 -Roof Floor	5	30-Jun-26	07-Jul-26
CON-5100	Install Gypsum Board Ceiling-5th Floor	6	30-Jun-26	08-Jul-26
CON-5410	Sprinklers Air Testing-1st Floor	5	30-Jun-26	07-Jul-26
CON-4600	Tape Gypsum Board -1st Floor	4	30-Jun-26	06-Jul-26
CON-5390	Install Firestopping-1st Floor	4	30-Jun-26	06-Jul-26
CON-2580	Install Power Panels -Elevator Machine Room	7	02-Jul-26	13-Jul-26
CON-5080	Install Ceramic Wall Tiles at Corridor-5th Floor	7	06-Jul-26	14-Jul-26
CON-5560	Install Final Coat Painting-2nd Floor	6	06-Jul-26	13-Jul-26
CON-5570	Install Plumbing Fixtures -2nd Floor	7	06-Jul-26	14-Jul-26
CON-4770	Install PBX - 1st Floor MDF Room	8	06-Jul-26	15-Jul-26
CON-5140	Install IPDVS Devices -2nd Floor	9	06-Jul-26	16-Jul-26
CON-4670	Install Exhaust Fans -1st Floor	5	07-Jul-26	13-Jul-26
CON-4680	Install Ceramic Wall Tiles at Corridor -1st Floor	7	07-Jul-26	15-Jul-26
CON-5540	Install Door Frames & Doors-4th Floor	5	07-Jul-26	13-Jul-26
CON-5550	Install Flooring Tiles-3rd Floor	5	07-Jul-26	13-Jul-26
CON-2860	Install Fume Hood Exhaust -Roof Floor	3	08-Jul-26	10-Jul-26
CON-5480	Install Gypsum Board Ceiling -1st Floor	6	08-Jul-26	15-Jul-26
CON-5580	Install Lighting Fixtures -4th Floor	6	08-Jul-26	15-Jul-26
CON-5500	Install Fire alarm Sensors and Devises -3rd Floor	8	08-Jul-26	17-Jul-26
CON-5770	Install Air Cooled Condensing Unit ACCU - Mechanical Work - 5th Floor	5	08-Jul-26	14-Jul-26
CON-98817	Install Intrusion System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-98867	Install Auxiliary System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-98917	Install Sound Clock System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-5530	Install First Coat Painting -5th Floor	5	09-Jul-26	15-Jul-26
CON-3000	Install Smoke Purge Fan -Roof Floor	3	13-Jul-26	15-Jul-26
CON-4870	Install Cabinet Unit Heaters With Fan CUH-1st Floor	3	14-Jul-26	16-Jul-26
CON-5090	Install Acoustical Ceiling Tiles-2nd Floor	5	14-Jul-26	20-Jul-26
CON-5690	Install Flooring Tiles-4th Floor	5	14-Jul-26	20-Jul-26
CON-5700	Install Final Coat Painting-3rd Floor	6	14-Jul-26	21-Jul-26
CON-5710	Install Furniture & Milling Work (Contractor Provided & Installed) -2nd Floor	5	14-Jul-26	20-Jul-26
CON-2790	Rough-in Conduits & Wires-Elevator Machine Room	6	14-Jul-26	21-Jul-26
CON-5760	Install Wood Floating Floor System -Gymnatorium	10	14-Jul-26	27-Jul-26
CON-4880	Install Motorized Fire/Smoke Damper FSD - Mechanical Work - 1st Floor	7	14-Jul-26	22-Jul-26
CON-9030	Install Furniture & Milling Work (Owner Provided & Installed) -2nd Floor	5	14-Jul-26	20-Jul-26
CON-99157	Install Elevator Sump Pump -Elevator Machine Room	10	14-Jul-26	27-Jul-26
CON-99247	Install Laboratory Equipment -3rd Floor	4	14-Jul-26	17-Jul-26
CON-5730	Install Plumbing Fixtures -3rd Floor	7	15-Jul-26	23-Jul-26
CON-5960	F/R/P Concert Pad -Boiler Room	3	15-Jul-26	17-Jul-26
CON-5680	Install Door Frames & Doors -5th Floor	5	16-Jul-26	22-Jul-26
CON-5720	Install First Coat Painting-1st Floor	5	16-Jul-26	22-Jul-26
CON-5740	Install Lighting Fixtures -5th Floor	6	16-Jul-26	23-Jul-26
CON-98827	Install Intrusion System Components -5th Floor	6	16-Jul-26	23-Jul-26

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
CON-98877	Install Auxiliary System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-98927	Install Sound Clock System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-5060	Install Hot Glycol / Hot Water Cabinet Heater (CUH) -3rd Floor	4	17-Jul-26	22-Jul-26
CON-5070	Install Electric Unit Heaters -1st Floor	7	17-Jul-26	27-Jul-26
CON-3750	Install Emergency Generator- Roof Floor	4	17-Jul-26	22-Jul-26
CON-5440	Install IPDVS Devices -3rd Floor	9	17-Jul-26	29-Jul-26
CON-6000	Rough-in Conduits & Wires-Boiler Room	3	20-Jul-26	22-Jul-26
CON-5660	Install Fire alarm Sensors and Devises -4th Floor	7	20-Jul-26	28-Jul-26
CON-5820	Install Signages-2nd Floor	5	21-Jul-26	27-Jul-26
CON-5330	Install Acoustical Ceiling Tiles-3rd Floor	5	22-Jul-26	28-Jul-26
CON-5900	Install Final Coat Painting-4th Floor	6	22-Jul-26	29-Jul-26
CON-5910	Install Furniture & Milling Work (Contractor Provided & Installed) -3rd Floor	5	22-Jul-26	28-Jul-26
CON-3100	Install Elevator Cabinet (1) -Elevator Machine Room	10	22-Jul-26	04-Aug-26
CON-3620	Install Elevator Cabinet (2) -Elevator Machine Room	10	22-Jul-26	04-Aug-26
CON-9040	Install Furniture & Milling Work (Owner Provided & Installed) -3rd Floor	5	22-Jul-26	28-Jul-26
CON-6050	Install Boiler B-1-Boiler Room	5	23-Jul-26	29-Jul-26
CON-5260	Install Cabinet Unit Heater With Fan CUH -4th Floor	4	23-Jul-26	28-Jul-26
CON-5860	Install Sprinkler Booster Pump (SBP-1) -1st Floor	10	23-Jul-26	05-Aug-26
CON-5870	Install Metal Panel Ceiling & Metal Geometric Ceiling -1st Floor	5	23-Jul-26	29-Jul-26
CON-5890	Install Flooring Tiles -5th Floor	5	23-Jul-26	29-Jul-26
CON-5920	Install Door Frames & Doors-1st Floor	5	23-Jul-26	29-Jul-26
CON-5380	Install Generator Connections -Roof Floor	4	23-Jul-26	28-Jul-26
CON-5150	Install Air Conditioning Unit AC - Mechanical Work - 1st Floor	4	23-Jul-26	28-Jul-26
CON-5280	Install Convector Heater CV - Mechanical Work - 3rd Floor	4	23-Jul-26	28-Jul-26
CON-5930	Install Plumbing Fixtures -4th Floor	7	24-Jul-26	03-Aug-26
CON-5940	Install Lighting Fixtures -1st Floor	7	24-Jul-26	03-Aug-26
CON-98937	Install Sound Clock System Components-1st Floor	3	24-Jul-26	28-Jul-26
CON-5300	Install Grease Interceptors - 1st Floor	5	28-Jul-26	03-Aug-26
CON-5810	Install Wall Pads - Gymnatorium	4	28-Jul-26	31-Jul-26
CON-5430	Install Hot Glycol / Hot Water Cabinet Heater (CUH) -5th Floor	4	29-Jul-26	03-Aug-26
CON-6030	Install Signages-3rd Floor	5	29-Jul-26	04-Aug-26
CON-5830	Install Fire alarm Sensors and Devises -5th Floor	5	29-Jul-26	04-Aug-26
CON-5320	Install Door Curtains DC - Mechanical Work - 1st Floor	7	29-Jul-26	06-Aug-26
CON-5450	Install Air Conditioning Unit AC - Mechanical Work - 3rd Floor	4	29-Jul-26	03-Aug-26
CON-5460	Install Convector Heater CV - Mechanical Work - 4th Floor	3	29-Jul-26	31-Jul-26
CON-98887	Install Auxiliary System Components-1st Floor	4	29-Jul-26	03-Aug-26
CON-6110	Install Boiler B-2-Boiler Room	5	30-Jul-26	05-Aug-26
CON-6120	Install Air Separator Units (AS-1 , AS-2 & AS-3)	2	30-Jul-26	31-Jul-26
CON-6130	Install Boiler Condensate ACID Neutralization Tubes -Boiler Room	2	30-Jul-26	31-Jul-26
CON-5520	Install Acoustical Ceiling Tiles-4th Floor	5	30-Jul-26	05-Aug-26
CON-6070	Install Furniture & Milling Work (Contractor Provided & Installed) -4th Floor	5	30-Jul-26	05-Aug-26
CON-6080	Install Flooring Tiles-1st Floor	5	30-Jul-26	05-Aug-26
CON-5750	Install IPDVS Devices -4th Floor	9	30-Jul-26	11-Aug-26
CON-9050	Install Furniture & Milling Work (Owner Provided & Installed) -4th Floor	5	30-Jul-26	05-Aug-26

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
CON-99267	Install Rolling Doors-1st Floor	3	30-Jul-26	03-Aug-26
CON-6200	Install Expansion Tanks (ET-1 , ET-2 & ET-3)	2	03-Aug-26	04-Aug-26
CON-6210	Install Glycol Make-up Units (GF-1 & GF-2 & GF-3)	2	03-Aug-26	04-Aug-26
CON-6220	Install Reduced Pressure Zone (RPZ) Devices -Boiler Room	2	03-Aug-26	04-Aug-26
CON-5970	Install Retractable Basketball Goal Assembly -Gymnatorium	3	03-Aug-26	05-Aug-26
CON-6090	Install Plumbing Fixtures -5th Floor	7	04-Aug-26	12-Aug-26
CON-5620	Install Air Conditioning Unit AC - Mechanical Work - 4th Floor	4	04-Aug-26	07-Aug-26
CON-5590	Install Exhaust Fan EF - Mechanical Work - 5th Floor	4	04-Aug-26	07-Aug-26
CON-98837	Install Intrusion System Components-1st Floor	4	04-Aug-26	07-Aug-26
CON-5950	Install Fire alarm Sensors and Devises -1st Floor	3	05-Aug-26	07-Aug-26
CON-6260	Install Heat Exchanger -Boiler Room	2	06-Aug-26	07-Aug-26
CON-6100	Install Jockey Pump (JP-1) -1st Floor	10	06-Aug-26	19-Aug-26
CON-5670	Install Acoustical Ceiling Tiles-5th Floor	5	06-Aug-26	12-Aug-26
CON-6160	Install Signages-4th Floor	5	06-Aug-26	12-Aug-26
CON-6180	Install Plumbing Fixtures-1st Floor	5	06-Aug-26	12-Aug-26
CON-6020	Install 8"Acoustic Block Painted-Gymnatorium	7	06-Aug-26	14-Aug-26
CON-5490	Install Convector Heater CV - Mechanical Work - 1st Floor	7	07-Aug-26	17-Aug-26
CON-6290	Install Hot Glycol Units Heaters (UH-5-1, UH-5-2)	2	10-Aug-26	11-Aug-26
CON-5630	Install Convector Heater CV - Mechanical Work - 5th Floor	3	10-Aug-26	12-Aug-26
CON-6330	Install Heat Pump Electric Hot Water Heater (HPWH#1&2)-Boiler Room	2	12-Aug-26	13-Aug-26
CON-6010	Install IPDVS Devices -5th Floor	9	12-Aug-26	24-Aug-26
CON-99217	Install Bleachers -Gymnatorium	3	12-Aug-26	14-Aug-26
CON-6060	Install Final Coat Painting -5th Floor	6	13-Aug-26	20-Aug-26
CON-6340	Install Exhaust Fans -Boiler Room	2	14-Aug-26	17-Aug-26
CON-6350	Install Primary Hot Water Pump (GHWP 1 to 3) -Boiler Room	2	14-Aug-26	17-Aug-26
CON-6360	Install Primary Chilled Water Pump (GCHWP-1&2)-Boiler Room	2	14-Aug-26	17-Aug-26
CON-6230	Install Gym Equipment -Gymnatorium -Gymnatorium	6	17-Aug-26	24-Aug-26
CON-6240	Install Fine Tube Radiator FTR - Gymnatorium	5	17-Aug-26	21-Aug-26
CON-6250	Install Hydraulic Vertical Wheelchair Lift -Gymnatorium	8	17-Aug-26	26-Aug-26
CON-6400	Install Secondary Hot Water Pump(HWP-1&2)-Boiler Room	2	18-Aug-26	19-Aug-26
CON-6410	Install Electric Unit Heater (EUH-3) - Boiler Room	2	18-Aug-26	19-Aug-26
CON-6420	Install Branch Panels (BRPP) -Boiler Room	2	18-Aug-26	19-Aug-26
CON-6150	Install Furniture & Milling Work (Contractor Provided & Installed) -5th Floor	4	21-Aug-26	26-Aug-26
CON-6170	Install Final Coat Painting-1st Floor	6	21-Aug-26	28-Aug-26
CON-9060	Install Furniture & Milling Work (Owner Provided & Installed) -5th Floor	4	21-Aug-26	26-Aug-26
CON-6040	Install IPDVS Devices -1st Floor	7	25-Aug-26	02-Sep-26
CON-9150	Install LED Theatrical Lighting -Gymnatorium	4	25-Aug-26	28-Aug-26
CON-6280	Install Signages- 5th Floor	5	27-Aug-26	02-Sep-26
CON-6390	Install Auditorium Television Studio Dimming System -Gymnatorium	7	27-Aug-26	04-Sep-26
CON-5880	Install Acoustical Ceiling Tiles -1st Floor	5	31-Aug-26	04-Sep-26
CON-6300	Install Furniture & Milling Work (Contractor Provided & Installed) -1st Floor	4	31-Aug-26	03-Sep-26
CON-6310	Install Security Screens & Barriers-1st Floor	3	31-Aug-26	02-Sep-26
CON-6320	Install Cafeteria Equipment-1st Floor	4	31-Aug-26	03-Sep-26
CON-9020	Install Furniture & Milling Work (Owner Provided & Installed) -1st Floor	3	31-Aug-26	02-Sep-26

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
CON-6370	Install Signages-1st Floor	4	04-Sep-26	10-Sep-26
CON-6380	Install Food Service Equipment-1st Floor	5	04-Sep-26	11-Sep-26
CON-5040	Dismantle Hoist	2	10-Sep-26	11-Sep-26
CON-5170	Demolish Hoist Pad	2	14-Sep-26	15-Sep-26
CON-5250	Hoist In-Fill	2	16-Sep-26	17-Sep-26
Elevation Area		89	29-Dec-25	05-May-26
CON-8390	Install Sidewalk Sheds -South Elevation	4	29-Dec-25	02-Jan-26
CON-8400	Install Sidewalk Sheds -East Elevation	4	29-Dec-25	02-Jan-26
MIL-1720	Start Sidewalk Bridge Installations	0	29-Dec-25	
CON-1830	Install Insulated Precast Concrete Sandwich Panel - Mock Up	2	05-Mar-26	06-Mar-26
CON-1990	Approve Insulated Precast Concrete Sandwich Panel - Mock Up	2	09-Mar-26	10-Mar-26
CON-2110	Install & Windows Mock-Up	3	11-Mar-26	13-Mar-26
CON-2210	Approve Windows Mock-Up	2	16-Mar-26	17-Mar-26
CON-2220	Install Storefront System Mock-Up	3	18-Mar-26	20-Mar-26
CON-2240	Approve Storefront System Mock-Up	2	23-Mar-26	24-Mar-26
CON-2380	Install Insulated Precast Concrete Sandwich Panel - West Elevation	3	25-Mar-26	27-Mar-26
CON-2420	Install Insulated Precast Concrete Sandwich Panel - South Elevation	5	25-Mar-26	31-Mar-26
CON-2400	Install Windows -West Elevation	5	30-Mar-26	03-Apr-26
CON-2410	Install Storefront System-West Elevation	5	30-Mar-26	03-Apr-26
MIL-1740	Start Windows	0	30-Mar-26	
CON-2590	Install Windows - South Elevation	10	01-Apr-26	14-Apr-26
CON-2600	Install Storefront System- South Elevation	10	01-Apr-26	14-Apr-26
CON-2610	Install Insulated Precast Concrete Sandwich Panel - East Elevation	4	01-Apr-26	06-Apr-26
CON-2730	Install Insulated Precast Concrete Sandwich Panel - North Elevation	4	01-Apr-26	06-Apr-26
CON-2570	Field Testing of Windows (5%)	5	06-Apr-26	10-Apr-26
CON-2970	Field Testing of Windows (50%)	5	15-Apr-26	21-Apr-26
CON-2980	Install Windows - East Elevation	8	15-Apr-26	24-Apr-26
CON-2990	Install Storefront System- East Elevation	8	15-Apr-26	24-Apr-26
CON-3380	Install Windows -North Elevation	10	15-Apr-26	28-Apr-26
CON-3390	Install Storefront System-North Elevation	10	15-Apr-26	28-Apr-26
CON-99237	Install Flag Pole - South Elevation	10	15-Apr-26	28-Apr-26
CON-3370	Field Testing of Windows (90%)	5	27-Apr-26	01-May-26
CON-3220	Dismantle Sidewalk Sheds- South Elevation	2	29-Apr-26	30-Apr-26
CON-3630	Dismantle Sidewalk Sheds- East Elevation	2	04-May-26	05-May-26
MIL-1730	Sidewalk Sheds Dismantle Complete	0		05-May-26
No P026453 - AREA		699	30-Sep-24	15-Aug-27
MIL-1000	NTP	0	30-Sep-24	
MIL-1030	Project Duration(From NTP till TCO)	750	30-Sep-24	19-Oct-26
MIL-1040	Project Duration(From NTP till Substantial Completion)	930	30-Sep-24	17-Apr-27
PRE-2590	Meeting With SCA to Review The Permit Requirements	14	30-Sep-24	18-Oct-24
PRE-2600	Prepare & Submit Permit Waiver Requests to SCA Chief Project Officer	5	30-Sep-24	04-Oct-24
MIL-1770	Project Duration(From NTP till Final Completion)	1050	30-Sep-24	15-Aug-27
MIL-2522	Site Access	365	30-Sep-24	29-Sep-25
CON-7960	Obtain Gas Meter Layout From CON-ED	5	07-Oct-24	11-Oct-24

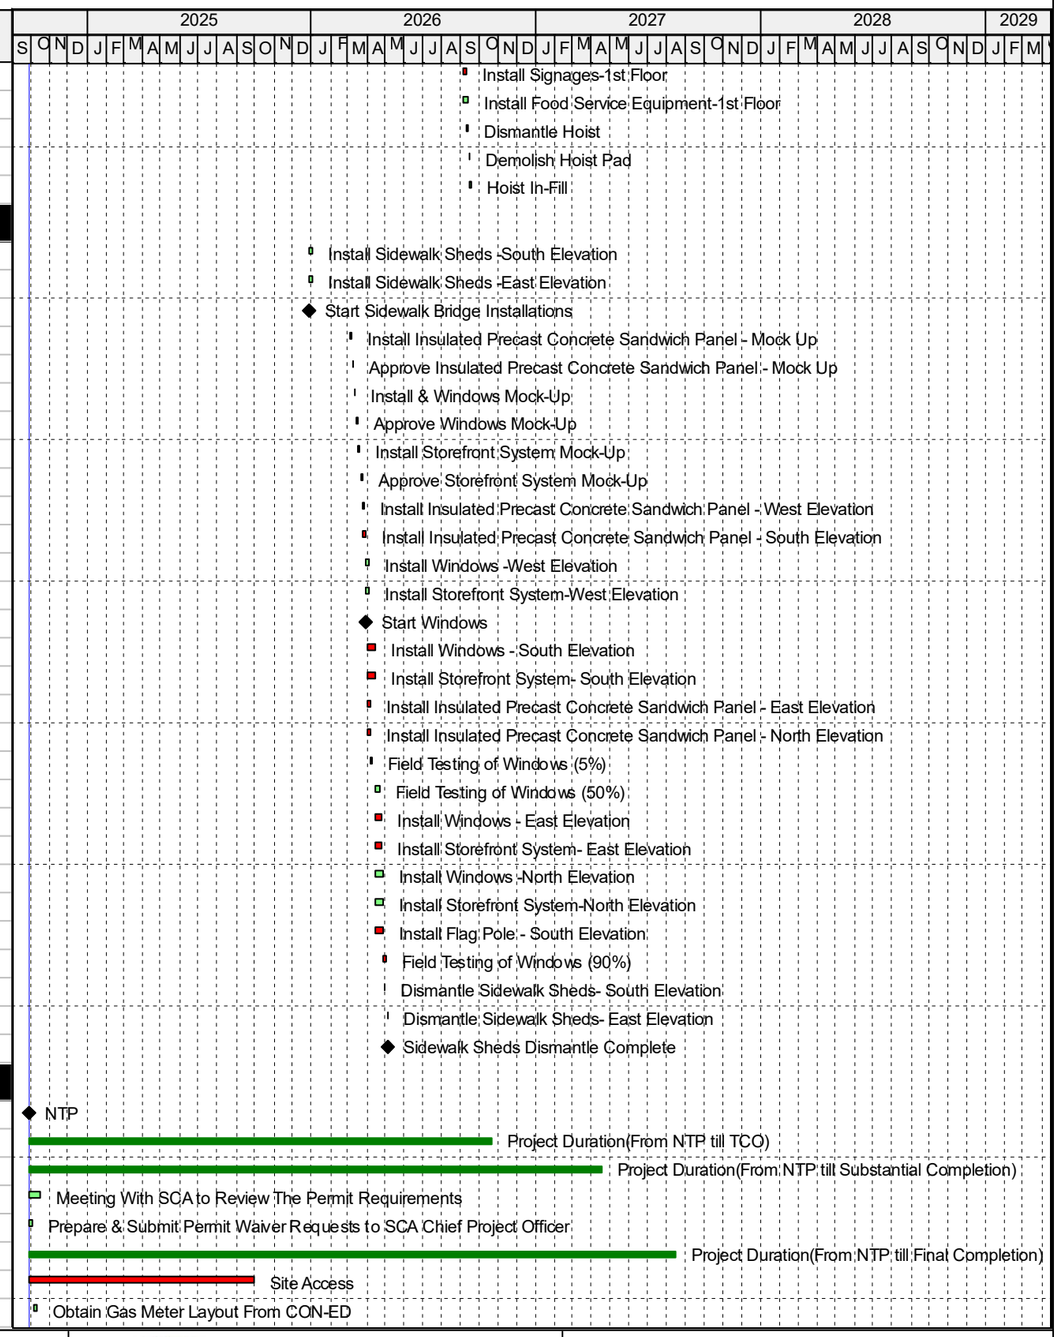

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
MIL-2542	Complete Subcontractor 'Buyout'	0		11-Oct-24
SUB-1000	Prepare & Submit Split Heat Pump System - SUB	60	15-Oct-24	10-Jan-25
SUB-1010	Prepare & Submit Thermometers	40	15-Oct-24	11-Dec-24
SUB-1020	Prepare & Submit Pressure Gages	40	15-Oct-24	11-Dec-24
SUB-1030	Prepare & Submit Floor Drains	40	15-Oct-24	11-Dec-24
SUB-1040	Prepare & Submit Hangers & Supports	40	15-Oct-24	11-Dec-24
SUB-1050	Prepare & Submit Fire & Jockey Pumps	81	15-Oct-24	11-Feb-25
SUB-1060	Prepare & Submit Interior Signage Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1070	Prepare & Submit Ceramic Tiles Product Data	81	15-Oct-24	11-Feb-25
SUB-1080	Prepare & Submit Door Hardware Submittal	81	15-Oct-24	11-Feb-25
SUB-1090	Prepare & Submit Painting	81	15-Oct-24	11-Feb-25
SUB-1100	Prepare & Submit Door & Frame Corners Samples	81	15-Oct-24	11-Feb-25
SUB-1110	Prepare & Submit Roof Drains & Clean Outs	81	15-Oct-24	11-Feb-25
SUB-1120	Prepare & Submit Flashing & Sheet Metal Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-1130	Prepare & Submit Roofing Membrane Product Data	81	15-Oct-24	11-Feb-25
SUB-1140	Prepare & Submit Perimeter Foundation Insulation Product Data	81	15-Oct-24	11-Feb-25
SUB-1150	Prepare & Submit Crystalline Waterproofing Product Data	81	15-Oct-24	11-Feb-25
SUB-1160	Prepare & Submit Suspension Assembly Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1170	Prepare & Submit Certification of Material	81	15-Oct-24	11-Feb-25
SUB-1180	Prepare & Submit Concrete Reinforcement	30	15-Oct-24	26-Nov-24
SUB-1190	Prepare & Submit Formwork Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1200	Prepare & Submit Planting Schedule	81	15-Oct-24	11-Feb-25
SUB-1210	Prepare & Submit Site Furnishings Shop Drawings	15	15-Oct-24	04-Nov-24
SUB-1220	Prepare & Submit Playgroung Equipment Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1230	Prepare & Submit Ductile Iron Pipes	37	15-Oct-24	06-Dec-24
SUB-1240	Prepare & Submit Catch Basin Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1250	Prepare & Submit Concrete Curbs & Pavements Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-1260	Prepare & Submit Steel Curb Facing Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-1270	Prepare & Submit Asphaltic Concrete Paving	81	15-Oct-24	11-Feb-25
SUB-1280	Prepare & Submit SSDS Geotextile	40	15-Oct-24	11-Dec-24
SUB-1290	Prepare & Submit Gas Vapor Barrier Submittal & Inspection Schedule	81	15-Oct-24	11-Feb-25
SUB-1300	Prepare & Submit Existing Conditions Survey	10	15-Oct-24	28-Oct-24
SUB-1310	Prepare & Submit Training Outline & Schedule	81	15-Oct-24	11-Feb-25
SUB-1320	Prepare & Submit Product Substitutions	82	15-Oct-24	12-Feb-25
SUB-1330	Prepare & Submit Temporary Ventilation Plan	81	15-Oct-24	11-Feb-25
SUB-1340	Prepare & Submit Construction Indoor Air Quality Management Plan	81	15-Oct-24	11-Feb-25
SUB-1350	Prepare & Submit Site Safety Plan	2	15-Oct-24	16-Oct-24
SUB-1360	Prepare & Submit CWM Plan	81	15-Oct-24	11-Feb-25
SUB-1370	Prepare & Submit Photo Submission - Temporary Fence	15	15-Oct-24	04-Nov-24
SUB-1380	Prepare & Submit Heating Plan	81	15-Oct-24	11-Feb-25
SUB-1390	Prepare & Submit Sample Classroom Materials	81	15-Oct-24	11-Feb-25
SUB-1400	Prepare & Submit Sustainable Materials	10	15-Oct-24	28-Oct-24
SUB-1410	Prepare & Submit Submittal Schedule	60	15-Oct-24	10-Jan-25
SUB-1420	Prepare & Submit Electrical Shop Drawings	81	15-Oct-24	11-Feb-25

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1430	Prepare & Submit Plumbing Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1440	Prepare & Submit Sprinkler System Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1450	Prepare & Submit Concrete Shop Drawings	30	15-Oct-24	26-Nov-24
SUB-1460	Prepare & Submit Elevator Machine	71	15-Oct-24	28-Jan-25
SUB-1470	Prepare & Submit Gypsum Board	81	15-Oct-24	11-Feb-25
SUB-1480	Prepare & Submit Floorings	81	15-Oct-24	11-Feb-25
SUB-1490	Prepare & Submit Acosutical Ceiling Tiles	60	15-Oct-24	10-Jan-25
SUB-1500	Prepare & Submit Toilet Accessories	81	15-Oct-24	11-Feb-25
SUB-1510	Prepare & Submit Millwork	81	15-Oct-24	11-Feb-25
SUB-1520	Prepare & Submit Lighting Fixtures	71	15-Oct-24	28-Jan-25
SUB-1530	Prepare & Submit Furniture	81	15-Oct-24	11-Feb-25
SUB-1540	Prepare & Submit Mechanical Ducts	81	15-Oct-24	11-Feb-25
SUB-1550	Prepare & Submit Mechanical Piping	60	15-Oct-24	10-Jan-25
SUB-1560	Prepare & Submit Erosion Control and Sedimentation Plan	7	15-Oct-24	23-Oct-24
SUB-1570	Prepare & Submit QCP	30	15-Oct-24	26-Nov-24
SUB-1580	Prepare & Submit Concrete Mix Design	30	15-Oct-24	26-Nov-24
SUB-1590	Prepare & Submit Electrical Equipment, Conduits, and Cables	20	15-Oct-24	12-Nov-24
SUB-1600	Prepare & Submit Plumbing Fixtures	81	15-Oct-24	11-Feb-25
SUB-1610	Prepare & Submit Baseline Schedule	52	15-Oct-24	30-Dec-24
SUB-1620	Prepare & Submit Wood Doors	81	15-Oct-24	11-Feb-25
SUB-1630	Prepare & Submit Fire Protection Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1640	Prepare & Submit Fire Detectors & Alarms	81	15-Oct-24	11-Feb-25
SUB-1650	Prepare & Submit Kitchen Equipment	71	15-Oct-24	28-Jan-25
SUB-1660	Prepare & Submit Signs	81	15-Oct-24	11-Feb-25
SUB-1670	Prepare & Submit Aluminum Projected Windows	71	15-Oct-24	28-Jan-25
SUB-1680	Prepare & Submit Telecommunication System Drawings	81	15-Oct-24	11-Feb-25
SUB-1690	Prepare & Submit Internet Protocol Digital Video Surveillance System using Digital Cameras	71	15-Oct-24	28-Jan-25
SUB-1710	Prepare & Submit Chillers Product Data	71	15-Oct-24	28-Jan-25
SUB-1720	Prepare & Submit Air Handling Units Product Data	71	15-Oct-24	28-Jan-25
SUB-1730	Prepare & Submit Boilers	71	15-Oct-24	28-Jan-25
SUB-1740	Prepare & Submit Emergency Generator System Product Data	71	15-Oct-24	28-Jan-25
SUB-1750	Prepare & Submit Switch Gears Product Data	20	15-Oct-24	12-Nov-24
SUB-1760	Prepare & Submit Unit Cabinet Heaters	60	15-Oct-24	10-Jan-25
SUB-1770	Prepare & Submit Gymnasium Equipment	81	15-Oct-24	11-Feb-25
SUB-1780	Prepare & Submit Initial Underground Coordination Drawings	50	15-Oct-24	26-Dec-24
SUB-1790	Prepare & Submit Initial 1st Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1800	Prepare & Submit Initial 2nd Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1810	Prepare & Submit Initial 3rd Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1820	Prepare & Submit Initial 4th Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1830	Prepare & Submit Initial 5th Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1840	Prepare & Submit Supplemental Comissioning Requirements	81	15-Oct-24	11-Feb-25
SUB-1850	Prepare & Submit Record Documents	81	15-Oct-24	11-Feb-25
SUB-1860	Prepare & Submit Environmental Site Assessment Reports	81	15-Oct-24	11-Feb-25
SUB-1870	Prepare & Submit Selective Removals & Demoloition	81	15-Oct-24	11-Feb-25

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1880	Prepare & Submit Foundation Product Data	5	15-Oct-24	21-Oct-24
SUB-1890	Prepare & Submit Trench Drains Product Data	81	15-Oct-24	11-Feb-25
SUB-1900	Prepare & Submit Chain Link Fences & Gates Drawings	81	15-Oct-24	11-Feb-25
SUB-1910	Prepare & Submit Outdoor Game Equipment	81	15-Oct-24	11-Feb-25
SUB-1920	Prepare & Submit Precast Architectural Concrete	71	15-Oct-24	28-Jan-25
SUB-1930	Prepare & Submit Unit Masonry Product Data	71	15-Oct-24	28-Jan-25
SUB-1940	Prepare & Submit Cast Stone Product Data	81	15-Oct-24	11-Feb-25
SUB-1950	Prepare & Submit Structure Steel Drawings	71	15-Oct-24	28-Jan-25
SUB-1960	Prepare & Submit Metal Deck Product Data	81	15-Oct-24	11-Feb-25
SUB-1970	Prepare & Submit Prefabricated Expansion Joint Covers	81	15-Oct-24	11-Feb-25
SUB-1980	Prepare & Submit Self Adhering Sheet Air Barriers	81	15-Oct-24	11-Feb-25
SUB-1990	Prepare & Submit Metal Plate Wall Panels	81	15-Oct-24	11-Feb-25
SUB-2000	Prepare & Submit Security Screens & Barriers	81	15-Oct-24	11-Feb-25
SUB-2010	Prepare & Submit Wood Flooring	81	15-Oct-24	11-Feb-25
SUB-2020	Prepare & Submit Visual Display Boards	81	15-Oct-24	11-Feb-25
SUB-2030	Prepare & Submit Metal Lockers	81	15-Oct-24	11-Feb-25
SUB-2040	Prepare & Submit Fire Extinguishers & Cabinets	81	15-Oct-24	11-Feb-25
SUB-2050	Prepare & Submit Stationary Metal Wall Louvers	73	15-Oct-24	30-Jan-25
SUB-2060	Prepare & Submit Library Equipment	81	15-Oct-24	11-Feb-25
SUB-2070	Prepare & Submit Platform Curtains & Auditorium Window Curtains	81	15-Oct-24	11-Feb-25
SUB-2080	Prepare & Submit Waste Handling Equipment	81	15-Oct-24	11-Feb-25
SUB-2090	Prepare & Submit Domestic Equipment	81	15-Oct-24	11-Feb-25
SUB-2100	Prepare & Submit Laboratory Equipment	81	15-Oct-24	11-Feb-25
SUB-2110	Prepare & Submit Manufactured Wood Casework	81	15-Oct-24	11-Feb-25
SUB-2120	Prepare & Submit Concrete Floating Floor Assembly	81	15-Oct-24	11-Feb-25
SUB-2130	Prepare & Submit Hydraulic Vertical Wheelchair Lifts	81	15-Oct-24	11-Feb-25
SUB-2140	Prepare & Submit Switch & Panel Boards	81	15-Oct-24	11-Feb-25
SUB-2150	Prepare & Submit Auditorium & Television Studio Dimming System Product Data	81	15-Oct-24	11-Feb-25
SUB-2160	Prepare & Submit Overcurrent Protective Devices Data	81	15-Oct-24	11-Feb-25
SUB-2170	Prepare & Submit Gas Pipes	81	15-Oct-24	11-Feb-25
SUB-2180	Prepare & Submit Water Heaters	81	15-Oct-24	11-Feb-25
SUB-2190	Prepare & Submit Pumping Apparatus & Tanks	81	15-Oct-24	11-Feb-25
SUB-2200	Prepare & Submit HVAC Pumps	81	15-Oct-24	11-Feb-25
SUB-2210	Prepare & Submit Emergency Generator System Accessories	71	15-Oct-24	28-Jan-25
SUB-2220	Prepare & Submit Fuel Storage Equipment	81	15-Oct-24	11-Feb-25
SUB-2230	Prepare & Submit Natural Gas Leak Detection Equipment	81	15-Oct-24	11-Feb-25
SUB-2250	Prepare & Submit Temperature Control System	81	15-Oct-24	11-Feb-25
SUB-2260	Prepare & Submit Air Outlets & Inlets	81	15-Oct-24	11-Feb-25
SUB-2340	Prepare & Submit Tree Protection Plan	71	15-Oct-24	28-Jan-25
SUB-2360	Prepare & Submit Adjacent Property and Structures Protection & Monitoring Plan	81	15-Oct-24	11-Feb-25
SUB-2370	Prepare & Submit Ornamenta Metal Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2920	Prepare & Submit Documentation of Proper Disposal	81	15-Oct-24	11-Feb-25
SUB-2930	Prepare & Submit Ornamenta Metal Product Data	81	15-Oct-24	11-Feb-25
SUB-2960	Prepare & Submit Coiling Doors, Grilles and Shutters Shop Drawings	81	15-Oct-24	11-Feb-25

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-2970	Prepare & Submit Coiling Doors, Grilles and Shutters Product Data	81	15-Oct-24	11-Feb-25
SUB-2980	Prepare & Submit Aluminum Framed Entrances & Storefronts Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2990	Prepare & Submit Aluminum Framed Entrances & Storefronts Product Data	81	15-Oct-24	11-Feb-25
SUB-3000	Prepare & Submit Thresholds, Weatherstripping and Seals Color Samples	81	15-Oct-24	11-Feb-25
SUB-3010	Prepare & Submit Thresholds, Weatherstripping and Seals Product Data	81	15-Oct-24	11-Feb-25
SUB-3020	Prepare & Submit Miscellaneous Glazing Samples	81	15-Oct-24	11-Feb-25
SUB-3030	Prepare & Submit Miscellaneous Glazing Product Data	81	15-Oct-24	11-Feb-25
SUB-3040	Prepare & Submit Fire Rated Glazing Samples	81	15-Oct-24	11-Feb-25
SUB-3050	Prepare & Submit Fire Rated Glazing Product Data	81	15-Oct-24	11-Feb-25
SUB-3060	Prepare & Submit Graffiti Resistant Coating Product Data	81	15-Oct-24	11-Feb-25
SUB-3070	Prepare & Submit Special Coating Samples	81	15-Oct-24	11-Feb-25
SUB-3080	Prepare & Submit Special Coating Product Data	81	15-Oct-24	11-Feb-25
SUB-3090	Prepare & Submit Flagpole Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3100	Prepare & Submit Flagpole Product Data	81	15-Oct-24	11-Feb-25
SUB-3110	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals	81	15-Oct-24	11-Feb-25
SUB-3120	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-3130	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	81	15-Oct-24	11-Feb-25
SUB-3140	Prepare & Submit Wire Mesh Work Samples	81	15-Oct-24	11-Feb-25
SUB-3150	Prepare & Submit Wire Mesh Work Shop drawings	81	15-Oct-24	11-Feb-25
SUB-3160	Prepare & Submit Metal Storage Shelving Samples	81	15-Oct-24	11-Feb-25
SUB-3170	Prepare & Submit Metal Storage Shelving Shop drawings	81	15-Oct-24	11-Feb-25
SUB-3180	Prepare & Submit Mirrors Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3190	Prepare & Submit Mirrors Product Data	81	15-Oct-24	11-Feb-25
SUB-3200	Prepare & Submit Mirrors Mastic Compatibility Test Reports & Certifications	81	15-Oct-24	11-Feb-25
SUB-3210	Prepare & Submit Grab Bars Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3220	Prepare & Submit Grab Bars Product Data	81	15-Oct-24	11-Feb-25
SUB-3230	Prepare & Submit Shop Equipment Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3240	Prepare & Submit Shop Equipment Product Data	81	15-Oct-24	11-Feb-25
SUB-3250	Prepare & Submit Bleachers Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3260	Prepare & Submit Bleachers Product Data	81	15-Oct-24	11-Feb-25
SUB-3270	Prepare & Submit Bleachers Manufacturer's Warranty	81	15-Oct-24	11-Feb-25
SUB-3280	Prepare & Submit Valves Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3290	Prepare & Submit Valves Product Data	81	15-Oct-24	11-Feb-25
SUB-3300	Prepare & Submit Certification of Tests	81	15-Oct-24	11-Feb-25
SUB-3310	Prepare & Submit Domestic Water Sterilization Plan	81	15-Oct-24	11-Feb-25
SUB-3320	Prepare & Submit Tags, Charts & Identifications Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3330	Prepare & Submit Tags, Charts & Identifications Product Data	81	15-Oct-24	11-Feb-25
SUB-3340	Prepare & Submit Micselianeous Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3350	Prepare & Submit Valves (HVAC) Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3360	Prepare & Submit Valves (HVAC) Product Data	81	15-Oct-24	11-Feb-25
SUB-3370	Prepare & Submit Piping Insulation Schedule Listing Items	81	15-Oct-24	11-Feb-25
SUB-3380	Prepare & Submit Schedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	81	15-Oct-24	11-Feb-25
SUB-3390	Prepare & Submit Schedules Showing Manfacturers's Product Number Duct Work Insulation	81	15-Oct-24	11-Feb-25
SUB-3400	Prepare & Submit Hydronic Specialities Shop Drawing	81	15-Oct-24	11-Feb-25

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-3410	Prepare & Submit Hydronic Specialities Product Data	81	15-Oct-24	11-Feb-25
SUB-3420	Prepare & Submit Water Treatment Firm	81	15-Oct-24	11-Feb-25
SUB-3430	Prepare & Submit Chemical Products Product Data	81	15-Oct-24	11-Feb-25
SUB-3440	Prepare & Submit Detail of Gag for the Safety Relief Valves	71	15-Oct-24	28-Jan-25
SUB-3450	Prepare & Submit Boiler Accessories Maintenance Data	71	15-Oct-24	28-Jan-25
SUB-3460	Prepare & Submit Breeching Chimney Connectors and Chimneys Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3470	Prepare & Submit Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	81	15-Oct-24	11-Feb-25
SUB-3480	Prepare & Submit Plate Heat Exchanger Maintenance Data	81	15-Oct-24	11-Feb-25
SUB-3490	Prepare & Submit Plate Heat Exchanger Product Data	81	15-Oct-24	11-Feb-25
SUB-3500	Prepare & Submit Coils Maintenance Data	81	15-Oct-24	11-Feb-25
SUB-3510	Prepare & Submit Coils Certifications	81	15-Oct-24	11-Feb-25
SUB-3520	Prepare & Submit Convectors Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3530	Prepare & Submit Convectors Product Data	81	15-Oct-24	11-Feb-25
SUB-3540	Prepare & Submit Fan Coils Units Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3550	Prepare & Submit Fan Coils Units Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-3560	Prepare & Submit Door Air Curtains Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3570	Prepare & Submit Door Air Curtains Product Data	81	15-Oct-24	11-Feb-25
SUB-3580	Prepare & Submit Centrifugal Fans Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3590	Prepare & Submit Centrifugal Fans Product Data	81	15-Oct-24	11-Feb-25
SUB-3600	Prepare & Submit Centrifugal Fans Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3610	Prepare & Submit Air Filters Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3620	Prepare & Submit Air Filters Product Data	81	15-Oct-24	11-Feb-25
SUB-3630	Prepare & Submit Air Filters Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3640	Prepare & Submit Duct Accessories Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3650	Prepare & Submit Damper Assemblies Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3660	Prepare & Submit Damper Assemblies Product Data	81	15-Oct-24	11-Feb-25
SUB-3670	Prepare & Submit Damper Assemblies Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3680	Prepare & Submit Variable Air Terminals Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3690	Prepare & Submit Variable Air Terminals Product Data	81	15-Oct-24	11-Feb-25
SUB-3700	Prepare & Submit Variable Air Terminals Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3710	Prepare & Submit AHU for Public Assemblies Sapces Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3720	Prepare & Submit AHU for Public Assemblies Sapces Product Data	81	15-Oct-24	11-Feb-25
SUB-3730	Prepare & Submit AHU for Public Assemblies Sapces Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3740	Prepare & Submit Control Systems Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3750	Prepare & Submit Truck Network Cable Schematic Diagram	81	15-Oct-24	11-Feb-25
SUB-3760	Prepare & Submit Lighting Control Devices Shop Drawing	71	15-Oct-24	28-Jan-25
SUB-3770	Prepare & Submit Lighting Control Devices Product Data	71	15-Oct-24	28-Jan-25
SUB-3780	Prepare & Submit Lighting Control Devices Warranty	71	15-Oct-24	28-Jan-25
SUB-3790	Prepare & Submit Surge Protective Devices Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3800	Prepare & Submit Surge Protective Devices Product Data	81	15-Oct-24	11-Feb-25
SUB-3810	Prepare & Submit Surge Protective Devices Warranty	81	15-Oct-24	11-Feb-25
SUB-3820	Prepare & Submit Service Entrance Equipment Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3830	Prepare & Submit Service Entrance Equipment Product Data	81	15-Oct-24	11-Feb-25
SUB-3840	Prepare & Submit Service Entrance Equipment Warranty	81	15-Oct-24	11-Feb-25

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-3850	Prepare & Submit Enclosed Switches Product Data	81	15-Oct-24	11-Feb-25
SUB-3860	Prepare & Submit Enclosed Switches Test Reports	81	15-Oct-24	11-Feb-25
SUB-3870	Prepare & Submit Motors, Motor Control Centers and Starters Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3880	Prepare & Submit Motors, Motor Control Centers and Starters Product Data	81	15-Oct-24	11-Feb-25
SUB-3890	Prepare & Submit Motors, Motor Control Centers and Starters Field Test Reports	81	15-Oct-24	11-Feb-25
SUB-3900	Prepare & Submit Lightning Protection Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3920	Prepare & Submit Lightning Protection Test Reports	81	15-Oct-24	11-Feb-25
SUB-3930	Prepare & Submit Fiber Optic Cabling system Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3940	Prepare & Submit Fiber Optic Cabling system Product Data	81	15-Oct-24	11-Feb-25
SUB-3950	Prepare & Submit Fiber Optic Cabling system Samples	81	15-Oct-24	11-Feb-25
SUB-3960	Prepare & Submit Sound, Intercome & Security System Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3970	Prepare & Submit Sound, Intercome & Security System Programming Code and Password for the System	81	15-Oct-24	11-Feb-25
SUB-3980	Prepare & Submit Sound, Intercome & Security System Warranty	81	15-Oct-24	11-Feb-25
SUB-3990	Prepare & Submit Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	81	15-Oct-24	11-Feb-25
SUB-4000	Prepare & Submit Projection and Interactive Whiteboard Systems Wiring diagram	81	15-Oct-24	11-Feb-25
SUB-4010	Prepare & Submit Self Corrective Clock System Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-4020	Prepare & Submit Self Corrective Clock System Product Data	81	15-Oct-24	11-Feb-25
SUB-4030	Prepare & Submit Self Corrective Clock System Field Test Reports	81	15-Oct-24	11-Feb-25
SUB-4040	Prepare & Submit Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	81	15-Oct-24	11-Feb-25
SUB-4060	Prepare & Submit Steel Stairs Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-4070	Prepare & Submit Steel Stairs Product Data	81	15-Oct-24	11-Feb-25
SUB-4080	Prepare & Submit Green School Submittal	81	15-Oct-24	11-Feb-25
APP-1000	Review & Approve Site Safety Plan	21	17-Oct-24	06-Nov-24
APP-1010	Review & Approve Foundation Product Data	21	22-Oct-24	11-Nov-24
APP-1020	Review & Approve Erosion Control and Sedimentation Plan	21	24-Oct-24	13-Nov-24
APP-1030	Review & Approve Existing Conditions Survey	21	29-Oct-24	18-Nov-24
APP-1040	Review & Approve Sustainable Materials	21	29-Oct-24	18-Nov-24
APP-1050	Review & Approve Site Furnishings Shop Drawings	21	05-Nov-24	25-Nov-24
APP-1060	Review & Approve Photo Submission - Temporary Fence	21	05-Nov-24	25-Nov-24
CON-8010	Coordination With CON-ED For Temporary Electrical Power	10	07-Nov-24	21-Nov-24
APP-1080	Review & Approve Electrical Equipment, Conduits, and Cables	21	13-Nov-24	03-Dec-24
APP-1090	Review & Approve Switch Gears Product Data	21	13-Nov-24	03-Dec-24
CON-8020	Scheduling With CON-ED For Temporary Electrical Power	7	22-Nov-24	03-Dec-24
APP-1100	Review & Approve Concrete Reinforcement	21	27-Nov-24	17-Dec-24
APP-1110	Review & Approve Concrete Shop Drawings	21	27-Nov-24	17-Dec-24
APP-1130	Review & Approve QCP	21	27-Nov-24	17-Dec-24
APP-1140	Review & Approve Concrete Mix Design	21	27-Nov-24	17-Dec-24
APP-1150	Review & Approve Ductile Iron Pipes	21	07-Dec-24	27-Dec-24
APP-1160	Review & Approve Thermometers	21	12-Dec-24	01-Jan-25
APP-1170	Review & Approve Pressure Gages	21	12-Dec-24	01-Jan-25
APP-1180	Review & Approve Floor Drains	21	12-Dec-24	01-Jan-25
APP-1190	Review & Approve Hangers & Supports	21	12-Dec-24	01-Jan-25
APP-1200	Review & Approve SSDS Geotextile	21	12-Dec-24	01-Jan-25
APP-1230	Review & Approve Initial Underground Coordination Drawings	21	27-Dec-24	16-Jan-25

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1240	Review & Approve Baseline Schedule	21	31-Dec-24	20-Jan-25
APP-1250	Review & Approve Split Heat Pump System - SUB	21	11-Jan-25	31-Jan-25
APP-1260	Review & Approve Submittal Schedule	21	11-Jan-25	31-Jan-25
APP-1270	Review & Approve Acosutical Ceiling Tiles	21	11-Jan-25	31-Jan-25
APP-1280	Review & Approve Mechanical Piping	21	11-Jan-25	31-Jan-25
APP-1290	Review & Approve Unit Cabinet Heaters	21	11-Jan-25	31-Jan-25
SUB-2270	Prepare & Submit Final Underground Coordination Drawings	37	17-Jan-25	11-Mar-25
APP-1210	Review & Approve Elevator Machine	21	29-Jan-25	18-Feb-25
APP-1120	Review & Approve Lighting Fixtures	21	29-Jan-25	18-Feb-25
APP-1780	Review & Approve Kitchen Equipment	21	29-Jan-25	18-Feb-25
APP-1310	Review & Approve Aluminum Projected Windows	21	29-Jan-25	18-Feb-25
APP-1220	Review & Approve Internet Protocol Digital Video Surveillance System using Digital Cameras	35	29-Jan-25	04-Mar-25
APP-1820	Review & Approve Chillers Product Data	21	29-Jan-25	18-Feb-25
APP-1300	Review & Approve Air Handling Units Product Data	21	29-Jan-25	18-Feb-25
APP-1830	Review & Approve Boilers	21	29-Jan-25	18-Feb-25
APP-1070	Review & Approve Emergency Generator System Product Data	21	29-Jan-25	18-Feb-25
APP-1920	Review & Approve Precast Architectural Concrete	21	29-Jan-25	18-Feb-25
APP-1930	Review & Approve Unit Masonry Product Data	21	29-Jan-25	18-Feb-25
APP-1950	Review & Approve Structure Steel Drawings	21	29-Jan-25	18-Feb-25
APP-2200	Review & Approve Emergency Generator System Accessories	21	29-Jan-25	18-Feb-25
APP-2340	Review & Approve Tree Protection Plan	21	29-Jan-25	18-Feb-25
APP-3440	Review & Approve Detail of Gag for the Safety Relief Valves	21	29-Jan-25	18-Feb-25
APP-3450	Review & Approve Boiler Accessories Maintenance Data	21	29-Jan-25	18-Feb-25
APP-3760	Review & Approve Lighting Control Devices Shop Drawing	21	29-Jan-25	18-Feb-25
APP-3770	Review & Approve Lighting Control Devices Product Data	21	29-Jan-25	18-Feb-25
APP-3780	Review & Approve Lighting Control Devices Warranty	21	29-Jan-25	18-Feb-25
APP-1320	Review & Approve Stationary Metal Wall Louvers	21	31-Jan-25	20-Feb-25
APP-1330	Review & Approve Initial 1st Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1340	Review & Approve Initial 2nd Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1350	Review & Approve Initial 3rd Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1360	Review & Approve Initial 4th Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1370	Review & Approve Initial 5th Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1380	Review & Approve Fire & Jockey Pumps	21	12-Feb-25	04-Mar-25
APP-1390	Review & Approve Interior Signage Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1400	Review & Approve Ceramic Tiles Product Data	21	12-Feb-25	04-Mar-25
APP-1410	Review & Approve Door Hardware Submittal	21	12-Feb-25	04-Mar-25
APP-1420	Review & Approve Painting	21	12-Feb-25	04-Mar-25
APP-1430	Review & Approve Door & Frame Corners Samples	21	12-Feb-25	04-Mar-25
APP-1440	Review & Approve Roof Drains & Clean Outs	21	12-Feb-25	04-Mar-25
APP-1450	Review & Approve Flashing & Sheet Metal Shop Drawing	21	12-Feb-25	04-Mar-25
APP-1460	Review & Approve Roofing Membrane Product Data	21	12-Feb-25	04-Mar-25
APP-1470	Review & Approve Perimeter Foundation Insulation Product Data	21	12-Feb-25	04-Mar-25
APP-1480	Review & Approve Crystalline Waterproofing Product Data	21	12-Feb-25	04-Mar-25
APP-1490	Review & Approve Suspension Assembly Shop Drawings	21	12-Feb-25	04-Mar-25

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1500	Review & Approve Certification of Material	21	12-Feb-25	04-Mar-25
APP-1510	Review & Approve Formwork Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1520	Review & Approve Planting Schedule	21	12-Feb-25	04-Mar-25
APP-1530	Review & Approve Playgroung Equipment Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1540	Review & Approve Catch Basin Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1550	Review & Approve Concrete Curbs & Pavements Shop Drawing	21	12-Feb-25	04-Mar-25
APP-1560	Review & Approve Steel Curb Facing Shop Drawing	21	12-Feb-25	04-Mar-25
APP-1570	Review & Approve Asphaltic Concrete Paving	21	12-Feb-25	04-Mar-25
APP-1580	Review & Approve Gas Vapor Barrier Submittal & Inspection Schedule	21	12-Feb-25	04-Mar-25
APP-1590	Review & Approve Training Outline & Schedule	21	12-Feb-25	04-Mar-25
APP-1600	Review & Approve Temporary Ventilation Plan	21	12-Feb-25	04-Mar-25
APP-1610	Review & Approve Construction Indoor Air Quality Management Plan	21	12-Feb-25	04-Mar-25
APP-1620	Review & Approve CWM Plan	21	12-Feb-25	04-Mar-25
APP-1630	Review & Approve Heating Plan	21	12-Feb-25	04-Mar-25
APP-1640	Review & Approve Sample Classroom Materials	21	12-Feb-25	04-Mar-25
APP-1650	Review & Approve Electrical Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1660	Review & Approve Plumbing Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1670	Review & Approve Sprinkler System Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1680	Review & Approve Gypsum Board	21	12-Feb-25	04-Mar-25
APP-1690	Review & Approve Floorings	21	12-Feb-25	04-Mar-25
APP-1700	Review & Approve Toilet Accessories	21	12-Feb-25	04-Mar-25
APP-1710	Review & Approve Millwork	21	12-Feb-25	04-Mar-25
APP-1720	Review & Approve Furniture	21	12-Feb-25	04-Mar-25
APP-1730	Review & Approve Mechanical Ducts	21	12-Feb-25	04-Mar-25
APP-1740	Review & Approve Plumbing Fixtures	21	12-Feb-25	04-Mar-25
APP-1750	Review & Approve Wood Doors	21	12-Feb-25	04-Mar-25
APP-1760	Review & Approve Fire Protection Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1770	Review & Approve Fire Detectors & Alarms	21	12-Feb-25	04-Mar-25
APP-1790	Review & Approve Signs	21	12-Feb-25	04-Mar-25
APP-1800	Review & Approve Telecommunication System Drawings	21	12-Feb-25	04-Mar-25
APP-1840	Review & Approve Gymnasium Equipment	21	12-Feb-25	04-Mar-25
APP-1850	Review & Approve Supplemental Comissioning Requirements	21	12-Feb-25	04-Mar-25
APP-1860	Review & Approve Record Documents	21	12-Feb-25	04-Mar-25
APP-1870	Review & Approve Environmental Site Assessment Reports	21	12-Feb-25	04-Mar-25
APP-1880	Review & Approve Selective Removals & Demoloition	21	12-Feb-25	04-Mar-25
APP-1890	Review & Approve Trench Drains Prodcut Data	21	12-Feb-25	04-Mar-25
APP-1900	Review & Approve Chain Link Fences & Gates Drawings	21	12-Feb-25	04-Mar-25
APP-1910	Review & Approve Outdoor Game Equipment	21	12-Feb-25	04-Mar-25
APP-1940	Review & Approve Cast Stone Product Data	21	12-Feb-25	04-Mar-25
APP-1960	Review & Approve Metal Deck Product Data	21	12-Feb-25	04-Mar-25
APP-1970	Review & Approve Prefabricated Expansion Joint Covers	21	12-Feb-25	04-Mar-25
APP-1980	Review & Approve Self Adhering Sheet Air Barriers	21	12-Feb-25	04-Mar-25
APP-1990	Review & Approve Metal Plate Wall Panels	21	12-Feb-25	04-Mar-25
APP-2000	Review & Approve Security Screens & Barriers	21	12-Feb-25	04-Mar-25

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
APP-2010	Review & Approve Wood Flooring	21	12-Feb-25	04-Mar-25
APP-2020	Review & Approve Visual Display Boards	21	12-Feb-25	04-Mar-25
APP-2030	Review & Approve Metal Lockers	21	12-Feb-25	04-Mar-25
APP-2040	Review & Approve Fire Extinguishers & Cabinets	21	12-Feb-25	04-Mar-25
APP-2050	Review & Approve Library Equipment	21	12-Feb-25	04-Mar-25
APP-2060	Review & Approve Platform Curtains & Auditorium Window Curtains	21	12-Feb-25	04-Mar-25
APP-2070	Review & Approve Waste Handling Equipment	21	12-Feb-25	04-Mar-25
APP-2080	Review & Approve Domestic Equipment	21	12-Feb-25	04-Mar-25
APP-2090	Review & Approve Laboratory Equipment	21	12-Feb-25	04-Mar-25
APP-2100	Review & Approve Manufactured Wood Casework	21	12-Feb-25	04-Mar-25
APP-2110	Review & Approve Concrete Floating Floor Assembly	21	12-Feb-25	04-Mar-25
APP-2120	Review & Approve Hydraulic Vertical Wheelchair Lifts	21	12-Feb-25	04-Mar-25
APP-2130	Review & Approve Switch & Panel Boards	21	12-Feb-25	04-Mar-25
APP-2140	Review & Approve Auditorium & Television Studio Dimming System Product Data	21	12-Feb-25	04-Mar-25
APP-2150	Review & Approve Overcurrent Protective Devices Data	21	12-Feb-25	04-Mar-25
APP-2160	Review & Approve Gas Pipes	21	12-Feb-25	04-Mar-25
APP-2170	Review & Approve Water Heaters	21	12-Feb-25	04-Mar-25
APP-2180	Review & Approve Pumping Apparatus & Tanks	21	12-Feb-25	04-Mar-25
APP-2190	Review & Approve HVAC Pumps	21	12-Feb-25	04-Mar-25
APP-2210	Review & Approve Fuel Storage Equipment	21	12-Feb-25	04-Mar-25
APP-2220	Review & Approve Natural Gas Leak Detection Equipment	21	12-Feb-25	04-Mar-25
APP-2240	Review & Approve Temperature Control System	21	12-Feb-25	04-Mar-25
APP-2250	Review & Approve Air Outlets & Inlets	21	12-Feb-25	04-Mar-25
APP-2360	Review & Approve Adjacent Property and Structures Protection & Monitoring Plan	21	12-Feb-25	04-Mar-25
APP-2370	Review & Approve Ornamenta Metal Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2920	Review & Approve Documentation of Proper Disposal	21	12-Feb-25	04-Mar-25
APP-2930	Review & Approve Ornamenta Metal Product Data	21	12-Feb-25	04-Mar-25
APP-2960	Review & Approve Coiling Doors, Grilles and Shutters Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2970	Review & Approve Coiling Doors, Grilles and ShuttersProduct Data	21	12-Feb-25	04-Mar-25
APP-2980	Review & Approve Aluminum Framed Entrances & Storefronts Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2990	Review & Approve Aluminum Framed Entrances & Storefronts Product Data	21	12-Feb-25	04-Mar-25
APP-3000	Review & Approve Thresholds, Weatherstripping and Seals Color Samples	21	12-Feb-25	04-Mar-25
APP-3010	Review & Approve Thresholds, Weatherstripping and Seals Product Data	21	12-Feb-25	04-Mar-25
APP-3020	Review & Approve Miscellaneous Glazing Samples	21	12-Feb-25	04-Mar-25
APP-3030	Review & Approve Miscellaneous Glazing Product Data	21	12-Feb-25	04-Mar-25
APP-3040	Review & Approve Fire Rated Glazing Samples	21	12-Feb-25	04-Mar-25
APP-3050	Review & Approve Fire Rated Glazing Product Data	21	12-Feb-25	04-Mar-25
APP-3060	Review & Approve Graffiti Resistant Coating Product Data	21	12-Feb-25	04-Mar-25
APP-3070	Review & Approve Special Coating Samples	21	12-Feb-25	04-Mar-25
APP-3080	Review & Approve Special Coating Product Data	21	12-Feb-25	04-Mar-25
APP-3090	Review & Approve Flagpole Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3100	Review & Approve Flagpole Product Data	21	12-Feb-25	04-Mar-25
APP-3110	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals	21	12-Feb-25	04-Mar-25
APP-3120	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	21	12-Feb-25	04-Mar-25

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
APP-3130	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	21	12-Feb-25	04-Mar-25
APP-3140	Review & Approve Wire Mesh Work Samples	21	12-Feb-25	04-Mar-25
APP-3150	Review & Approve Miscellaneous Glazing Shop drawings	21	12-Feb-25	04-Mar-25
APP-3160	Review & Approve Metal Storage Shelving Samples	21	12-Feb-25	04-Mar-25
APP-3170	Review & Approve Metal Storage Shelving Shop drawings	21	12-Feb-25	04-Mar-25
APP-3180	Review & Approve Mirrors Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3190	Review & Approve Mirrors Product Data	21	12-Feb-25	04-Mar-25
APP-3200	Review & Approve Mirrors Mastic Compatibility Test Reports & Certifications	21	12-Feb-25	04-Mar-25
APP-3210	Review & Approve Grab Bars Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3220	Review & Approve Grab Bars Product Data	21	12-Feb-25	04-Mar-25
APP-3230	Review & Approve Shop Equipment Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3240	Review & Approve Shop Equipment Product Data	21	12-Feb-25	04-Mar-25
APP-3250	Review & Approve Bleachers Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3260	Review & Approve Bleachers Product Data	21	12-Feb-25	04-Mar-25
APP-3270	Review & Approve Bleachers Manufacturer's Warranty	21	12-Feb-25	04-Mar-25
APP-3280	Review & Approve Valves Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3290	Review & Approve Valves Product Data	21	12-Feb-25	04-Mar-25
APP-3300	Review & Approve Certification of Tests	21	12-Feb-25	04-Mar-25
APP-3310	Review & Approve Domestic Water Sterilization Plan	21	12-Feb-25	04-Mar-25
APP-3320	Review & Approve Tags, Charts & Identifications Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3330	Review & Approve Tags, Charts & Identifications Product Data	21	12-Feb-25	04-Mar-25
APP-3340	Review & Approve Micselianeous Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3350	Review & Approve Valves (HVAC) Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3360	Review & Approve Valves (HVAC) Product Data	21	12-Feb-25	04-Mar-25
APP-3370	Review & Approve Piping Insulation Schedule Listing Items	21	12-Feb-25	04-Mar-25
APP-3380	Review & Approve chedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	21	12-Feb-25	04-Mar-25
APP-3390	Review & Approve chedules Showing Manfacturers's Product Number Duct Work Insulation	21	12-Feb-25	04-Mar-25
APP-3400	Review & Approve Hydronic Specialities Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3410	Review & Approve Hydronic Specialities Product Data	21	12-Feb-25	04-Mar-25
APP-3420	Review & Approve Water Treatment Firm	21	12-Feb-25	04-Mar-25
APP-3430	Review & Approve Chemical Products Product Data	21	12-Feb-25	04-Mar-25
APP-3460	Review & Approve Breeching Chimney Connectors and Chimneys Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3470	Review & Approve Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	21	12-Feb-25	04-Mar-25
APP-3480	Review & Approve Plate Heat Exchanger Maintenance Data	21	12-Feb-25	04-Mar-25
APP-3490	Review & Approve Plate Heat Exchanger Product Data	21	12-Feb-25	04-Mar-25
APP-3500	Review & Approve Coils Maintenance Data	21	12-Feb-25	04-Mar-25
APP-3510	Review & Approve Coils Certifications	21	12-Feb-25	04-Mar-25
APP-3520	Review & Approve Convectors Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3530	Review & Approve Convectors Product Data	21	12-Feb-25	04-Mar-25
APP-3540	Review & Approve Fan Coils Units Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3550	Review & Approve Fan Coils Units Shop Drawings	21	12-Feb-25	04-Mar-25
APP-3560	Review & Approve Door Air Curtains Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3570	Review & Approve Door Air Curtains Product Data	21	12-Feb-25	04-Mar-25
APP-3580	Review & Approve Centrifugal Fans Shop Drawing	21	12-Feb-25	04-Mar-25

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
APP-3590	Review & Approve Centrifugal Fans Product Data	21	12-Feb-25	04-Mar-25
APP-3600	Review & Approve Centrifugal Fans Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3610	Review & Approve Air Filters Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3620	Review & Approve Air Filters Product Data	21	12-Feb-25	04-Mar-25
APP-3630	Review & Approve Air Filters Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3640	Review & Approve Duct Accessories Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3650	Review & Approve Damper Assemblies Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3660	Review & Approve Damper Assemblies Product Data	21	12-Feb-25	04-Mar-25
APP-3670	Review & Approve Damper Assemblies Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3680	Review & Approve Variable Air Terminals Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3690	Review & Approve Variable Air Terminals Product Data	21	12-Feb-25	04-Mar-25
APP-3700	Review & Approve Variable Air Terminals Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3710	Review & Approve AHU for Public Assemblies Sapces Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3720	Review & Approve AHU for Public Assemblies Sapces Product Data	21	12-Feb-25	04-Mar-25
APP-3730	Review & Approve AHU for Public Assemblies Sapces Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3740	Review & Approve Control Systems Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3750	Review & Approve Truck Network Cable Schematic Diagram	21	12-Feb-25	04-Mar-25
APP-3790	Review & Approve Surge Protective Devices Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3800	Review & Approve Surge Protective Devices Product Data	21	12-Feb-25	04-Mar-25
APP-3810	Review & Approve Surge Protective Devices Warranty	21	12-Feb-25	04-Mar-25
APP-3820	Review & Approve Service Entrance Equipment Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3830	Review & Approve Service Entrance Equipment Product Data	21	12-Feb-25	04-Mar-25
APP-3840	Review & Approve Service Entrance Equipment Warranty	21	12-Feb-25	04-Mar-25
APP-3850	Review & Approve Enclosed Switches Product Data	21	12-Feb-25	04-Mar-25
APP-3860	Review & Approve Enclosed Switches Test Reports	21	12-Feb-25	04-Mar-25
APP-3870	Review & Approve Motors, Motor Control Centers and Starters Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3880	Review & Approve Motors, Motor Control Centers and Starters Product Data	21	12-Feb-25	04-Mar-25
APP-3890	Review & Approve Motors, Motor Control Centers and Starters Field Test Reports	21	12-Feb-25	04-Mar-25
APP-3900	Review & Approve Lightning Protection Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3920	Review & Approve Lightning Protection Test Reports	21	12-Feb-25	04-Mar-25
APP-3930	Review & Approve Fiber Optic Cabling system Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3940	Review & Approve Fiber Optic Cabling system Product Data	21	12-Feb-25	04-Mar-25
APP-3950	Review & Approve Fiber Optic Cabling system Samples	21	12-Feb-25	04-Mar-25
APP-3960	Review & Approve Sound, Intercome & Security System Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3970	Review & Approve Sound, Intercome & Security System Programming Code and Password for the System	21	12-Feb-25	04-Mar-25
APP-3980	Review & Approve Sound, Intercome & Security System warranty	21	12-Feb-25	04-Mar-25
APP-3990	Review & Approve Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	21	12-Feb-25	04-Mar-25
APP-4000	Review & Approve Projection and Interactive Whiteboard Systems Wiring diagram	21	12-Feb-25	04-Mar-25
APP-4010	Review & Approve Self Corrective Clock System Shop Drawing	21	12-Feb-25	04-Mar-25
APP-4020	Review & Approve Self Corrective Clock System Product Data	21	12-Feb-25	04-Mar-25
APP-4030	Review & Approve Self Corrective Clock System Field Test Reports	21	12-Feb-25	04-Mar-25
APP-4040	Review & Approve Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	21	12-Feb-25	04-Mar-25
APP-4060	Review & Approve Steel Stairs Shop Drawings	21	12-Feb-25	04-Mar-25
APP-4070	Review & Approve Steel Stairs Product Data	21	12-Feb-25	04-Mar-25

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
APP-4080	Review & Approve Green School Submittal	21	12-Feb-25	04-Mar-25
APP-2260	Review & Approve Product Substitutions	21	13-Feb-25	05-Mar-25
MIL-2572	Place Steel Mill Order	0	20-Feb-25	
SUB-2280	Prepare & Submit Final 1st Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2290	Prepare & Submit Final 2nd Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2300	Prepare & Submit Final 3rd Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2310	Prepare & Submit Final 4th Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2320	Prepare & Submit Final 5th Floor Coordination Drawings	49	25-Feb-25	02-May-25
MIL-2762	Green Schools Compliance Submission	0		04-Mar-25
SUB-1700	Prepare & Submit Roof Dunnage	81	05-Mar-25	27-Jun-25
APP-2270	Review & Approve Final Foundations Coordination Drawings	21	12-Mar-25	01-Apr-25
APP-2280	Review & Approve Final 1st Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2290	Review & Approve Final 2nd Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2300	Review & Approve Final 3rd Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2310	Review & Approve Final 4th Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2320	Review & Approve Final 5th Floor Coordination Drawings	21	03-May-25	23-May-25
MIL-1640	Provide Complete Set of Approved Coordination Drawings	0		23-May-25
SUB-2900	Prepare & Submit Excavated Material Disposal Plan	71	26-May-25	05-Sep-25
SUB-4050	Prepare & Submit Soil Sampling Plan	71	26-May-25	05-Sep-25
PRO-1590	Procure & Deliver Steel Columns	120	02-Jun-25	29-Sep-25
APP-1810	Review & Approve Roof Dunnage	21	28-Jun-25	18-Jul-25
PRO-1120	Procure & Deliver Erosion Control and Sedimentation Devices	25	05-Sep-25	29-Sep-25
APP-2900	Review & Approve Excavated Material Disposal Plan	21	06-Sep-25	26-Sep-25
APP-4050	Review & Approve Soil Sampling Plan	21	06-Sep-25	26-Sep-25
SUB-2910	Prepare & Submit Backfill & Resue Plan	20	08-Sep-25	03-Oct-25
PRE-2630	Obtain Builders Pavement Permit	10	16-Sep-25	29-Sep-25
PRE-2640	Obtain Excavation & Shoring Permit	10	16-Sep-25	29-Sep-25
PRE-2650	Obtain Permit to Enter (PTE) Amtrak	10	16-Sep-25	29-Sep-25
PRE-2660	Obtain NYPA Permit	10	16-Sep-25	29-Sep-25
PRE-2540	SCA Work Notification	7	23-Sep-25	29-Sep-25
PRE-1660	DOB Permit & Insurance	3	25-Sep-25	29-Sep-25
PRE-1460	Obtain Construction Fences Permit	3	25-Sep-25	29-Sep-25
PRE-2550	Obtain CCD1	3	25-Sep-25	29-Sep-25
PRE-2570	Obtain Sidewalk Shed Permits	3	25-Sep-25	29-Sep-25
MIL-2532	Submit Complete Permit Application	0		29-Sep-25
MIL-2832	Issuance of Excavation & Shoring Permit	0		29-Sep-25
MIL-2842	Issuance of Builders Pavement Permit	0		29-Sep-25
MIL-2852	Issuance of Permit to Enter (PTE)	0		29-Sep-25
MIL-2862	Issuance of NYPA Permit	0		29-Sep-25
MIL-2872	Issuance of Construction Fences Permit	0		29-Sep-25
MIL-2882	Issuance of Sidewalk Shed Permits	0		29-Sep-25
MIL-2892	Issuance of CCD1	0		29-Sep-25
MIL-2902	Issuance of DOB Permit & Insurance	0		29-Sep-25
MIL-1060	Mobilization Start	0	30-Sep-25	

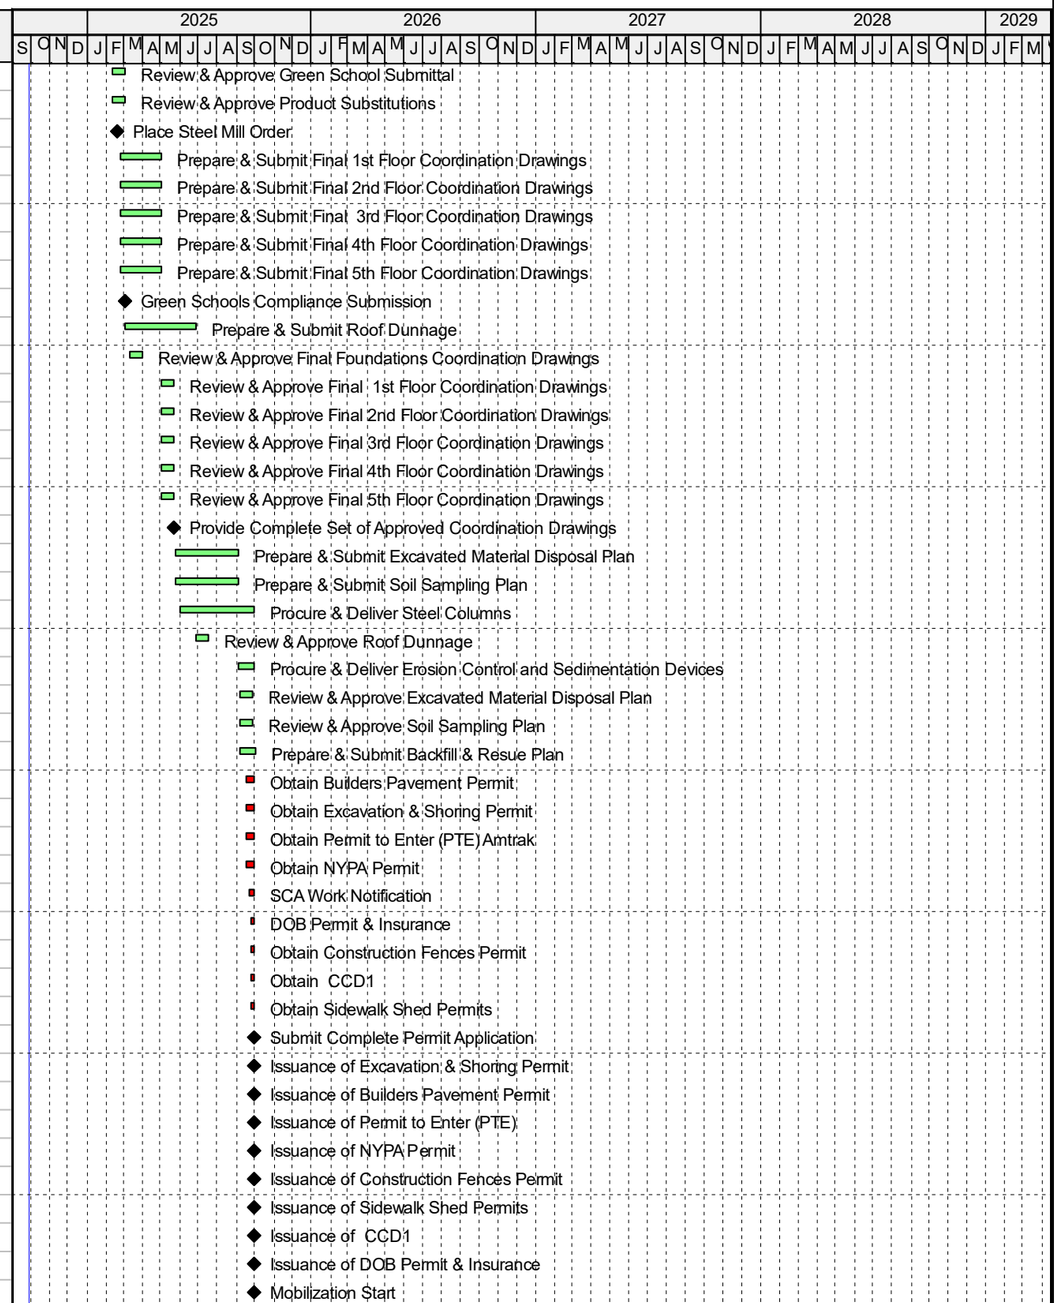

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
PRO-1420	Procure & Deliver Painting	70	30-Sep-25	08-Dec-25
PRO-1410	Procure & Deliver Door Frames	70	30-Sep-25	08-Dec-25
PRO-1200	Procure & Deliver Elevator Machine	112	30-Sep-25	19-Jan-26
PRO-1150	Procure & Deliver Gypsum Board	150	30-Sep-25	26-Feb-26
PRO-1160	Procure & Deliver Floorings	80	30-Sep-25	18-Dec-25
PRO-1170	Procure & Deliver Acosutical Ceiling Tiles	120	30-Sep-25	27-Jan-26
PRO-1190	Procure & Deliver Toilet Accessories	100	30-Sep-25	07-Jan-26
PRO-1000	Procure & Deliver Kitchen Equipment	180	30-Sep-25	28-Mar-26
PRO-1140	Procure & Deliver Lighting Fixtures	60	30-Sep-25	28-Nov-25
PRO-1010	Procure & Deliver Fumitures	130	30-Sep-25	06-Feb-26
PRO-1020	Procure & Deliver Mechanical Piping	70	30-Sep-25	08-Dec-25
PRO-1030	Procure & Deliver Mechanical Ducts	70	30-Sep-25	08-Dec-25
PRO-1050	Procure & Deliver Electrical Equipment	130	30-Sep-25	06-Feb-26
PRO-1060	Procure & Deliver Plumbing Fixtures	100	30-Sep-25	07-Jan-26
PRO-1070	Procure & Deliver Wood Doors	50	30-Sep-25	18-Nov-25
PRO-1090	Procure & Deliver Fire Sprinklers	100	30-Sep-25	07-Jan-26
PRO-1110	Procure & Deliver Fire Detectors & Alarms	60	30-Sep-25	28-Nov-25
PRO-1210	Procure & Deliver Signs	70	30-Sep-25	08-Dec-25
PRO-1220	Procure & Deliver Windows & Storefronts	154	30-Sep-25	02-Mar-26
PRO-1250	Procure & Deliver Plumbing Pipes	60	30-Sep-25	28-Nov-25
PRO-1260	Procure & Deliver Electrical Wires & Conduits	130	30-Sep-25	06-Feb-26
PRO-1270	Procure & Deliver Mechanical Pumps	70	30-Sep-25	08-Dec-25
PRO-1280	Procure & Deliver Fire Protection Pumps	70	30-Sep-25	08-Dec-25
PRO-1290	Procure & Deliver Plumbing Pumps	250	30-Sep-25	06-Jun-26
PRO-1310	Procure & Deliver Telecommunication System	60	30-Sep-25	28-Nov-25
PRO-1330	Procure & Deliver Cameras	60	30-Sep-25	28-Nov-25
PRO-1360	Procure & Deliver Metal Panel Ceilings	120	30-Sep-25	27-Jan-26
PRO-1380	Procure & Deliver Roof Dunnage	100	30-Sep-25	07-Jan-26
PRO-1470	Procure & Deliver Cabinet Heaters	126	30-Sep-25	02-Feb-26
PRO-1480	Procure & Deliver Chillers	170	30-Sep-25	18-Mar-26
PRO-1490	Procure & Deliver Air Handling Units	250	30-Sep-25	06-Jun-26
PRO-1500	Procure & Deliver Boilers	84	30-Sep-25	22-Dec-25
PRO-1510	Procure & Deliver Emergency Generator	290	30-Sep-25	16-Jul-26
PRO-1520	Procure & Deliver Switch Gears	250	30-Sep-25	06-Jun-26
PRO-1530	Procure & Deliver Hydraulic Vertical Wheelchair Lift	90	30-Sep-25	28-Dec-25
PRO-1560	Procure & Deliver Gymnasium Equipment	180	30-Sep-25	28-Mar-26
CON-8030	Procurement From CON-ED For Temporary Electrical Power	20	30-Sep-25	19-Oct-25
PRO-1570	Procure & Deliver Precast Sandwich Panels	112	30-Sep-25	19-Jan-26
PRO-1580	Procure & Deliver Metal Deck	70	30-Sep-25	08-Dec-25
PRO-1600	Procure & Deliver Trusses	60	30-Sep-25	28-Nov-25
PRO-1610	Procure & Deliver Prefabricated Expansion Joint Covers	60	30-Sep-25	28-Nov-25
PRO-1620	Procure & Deliver Security Screens & Barriers	60	30-Sep-25	28-Nov-25
PRO-1630	Procure & Deliver Wood Flooring	120	30-Sep-25	27-Jan-26
PRO-1640	Procure & Deliver Concrete Floating Floor Assembly	120	30-Sep-25	27-Jan-26

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

New Building PS/IS 341Q - Baseline Schedule Rev 01

NAVILLUS BUILDING THE WORLD AROUND YOU

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By : M.K

Date	**Revision**	**Checked**	**Approved**
21-Mar-25	00	A.R	

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
PRO-1660	Procure & Deliver Auditorium Television Studio Dimming System	90	30-Sep-25	28-Dec-25
MIL-1850	Construction Start	0	30-Sep-25	
PRO-2010	Procure & Deliver Steel Stairs Components	120	30-Sep-25	27-Jan-26
PRO-2020	Procure & Deliver Flagpole	60	30-Sep-25	28-Nov-25
PRO-2030	Procure & Deliver Bleachers	130	30-Sep-25	06-Feb-26
PRO-2040	Procure & Deliver VAV Units	170	30-Sep-25	18-Mar-26
PRO-2050	Procure & Deliver Furnitures (Owner Responsibility)	130	30-Sep-25	06-Feb-26
MIL-1710	Complete Mobilization	0		03-Oct-25
APP-2910	Review & Approve Backfill & Resue Plan	21	04-Oct-25	24-Oct-25
PRE-2610	Prepare & Submit FDNY Fuel Permit	10	06-Oct-25	20-Oct-25
CON-8040	CON-ED Work For Temporary Electrical Power	10	20-Oct-25	31-Oct-25
PRE-2620	Review & Approve FDNY Fuel Permit	21	21-Oct-25	10-Nov-25
I-1010	Concrete Cast-IN-Place Inspection	86	28-Oct-25	04-Mar-26
MIL-2582	Start Concrete Placement	0	28-Oct-25	
MIL-2812	Start Foundation	0	28-Oct-25	
MIL-2912	Start Concrete Cast In Place Inspection	0	28-Oct-25	
CON-8050	Available Temporary Electrical Power For Testing MEP Equipment	0		31-Oct-25
MIL-1810	Crane Mobilization-Steel Installation start	0	05-Dec-25	
I-1140	Structural Steel Inspection	58	05-Dec-25	02-Mar-26
PRO-1450	Procure & Deliver Playground Equipment	60	09-Dec-25	06-Feb-26
MIL-1120	Metal Decking Start	0	22-Dec-25	
I-1080	Standpipe System Inspection	111	29-Dec-25	05-Jun-26
MIL-2622	Deliveries of all owner-furnished equipment and/or materials	0		06-Feb-26
MIL-1140	Layout Start	0	23-Feb-26	
MIL-1150	Masonry Walls Start	0	23-Feb-26	
MIL-1180	MEP Risers Start	0	23-Feb-26	
MIL-1210	Duct Rough-ins Start	0	24-Feb-26	
MIL-1160	Top & Bottom Track Start	0	26-Feb-26	
I-1020	Masonry Inspection	32	02-Mar-26	14-Apr-26
I-1100	Fire-Resistant Penetrations And Joints Inspection	87	03-Mar-26	06-Jul-26
MIL-1830	Crane Mobilization-Precast Sandwich Panels Installation Start	0	05-Mar-26	
MIL-2932	Start Masonry Inspection	0	05-Mar-26	
MIL-1170	Finish Concrete Work	0		11-Mar-26
MIL-1820	Crane Mobilization-Steel Installation Finish	0		12-Mar-26
MIL-2612	Start Suspended Ceiling Grid	0	16-Mar-26	
MIL-1380	Crane Mobilization-Mechanical Subcontractor	78	17-Mar-26	07-Jul-26
I-1150	Concrete Precast Inspection	9	25-Mar-26	06-Apr-26
MIL-2922	Start Pre -Cast Concrete Inspection	0	25-Mar-26	
MIL-1840	Crane Mobilization-Precast Sandwich Panels Installation Finish	0		06-Apr-26
MIL-1230	5th Floor Roofing Start	0	07-Apr-26	
I-1120	Mechanical System Inspection	69	07-Apr-26	15-Jul-26
MIL-2602	Start Mechanical Distribution Lines	0	08-Apr-26	
MIL-1200	Main Roofing Start	0	09-Apr-26	
MIL-1270	Electrical Rough-ins Start	0	09-Apr-26	

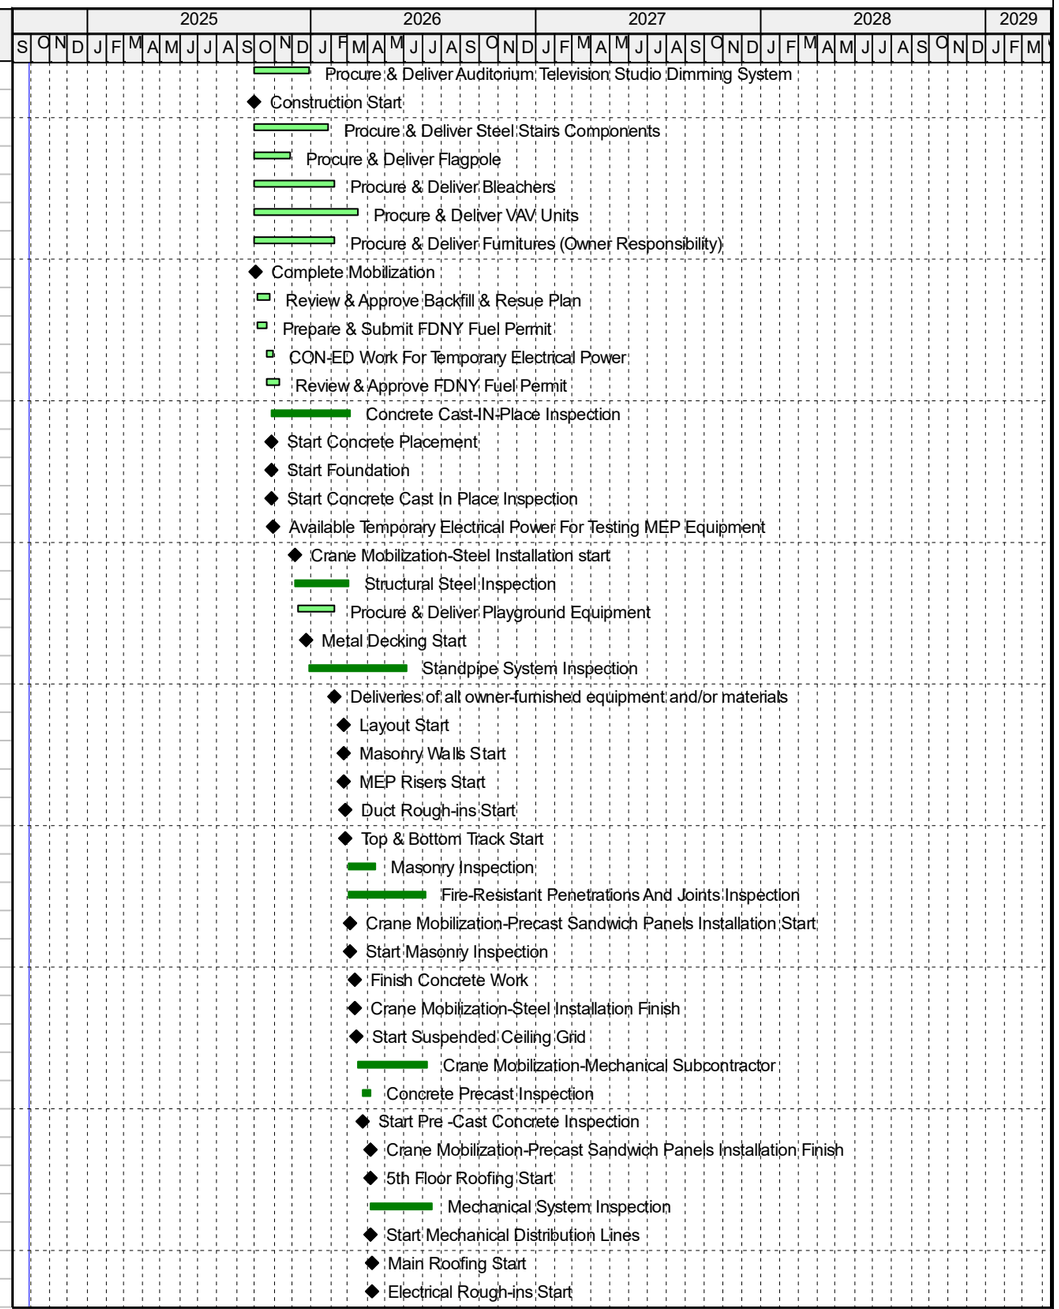

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
MIL-1220	Layout Finish	0		09-Apr-26
MIL-2942	Start In-Wall Inspection	0	10-Apr-26	
MIL-1290	Duct Rough-ins Finish	0		14-Apr-26
MIL-1250	Top & Bottom Track Finish	0		15-Apr-26
CON-7970	Coordinate With CON-ED For Gas Service	7	16-Apr-26	24-Apr-26
MIL-2712	Start Low Voltage	0	16-Apr-26	
PRO-1990	Procure & Deliver Gas Meter Rig	60	25-Apr-26	23-Jun-26
MIL-1580	Window Installation Finish	0		28-Apr-26
MIL-1400	Start Site Work	0	29-Apr-26	
I-1040	Roofing Flood Testing Inspection	5	30-Apr-26	06-May-26
MIL-1300	Start Sprinkler Rough-ins	0	04-May-26	
MIL-1340	BLDG Tight	0		06-May-26
MIL-1350	Electrical Rough-ins Finish	0		06-May-26
MIL-1360	Start Mockup Room Work	0	07-May-26	
MIL-1430	Start Architecture Finishes	0	07-May-26	
MIL-1260	Plumbing Rough-ins Start	0	07-May-26	
MIL-1310	5th Floor Roofing Finish	0		13-May-26
MIL-1280	Main Roofing Finish	0		15-May-26
MIL-1410	Mockup Room Ready For Inspection	0		26-May-26
MIL-1420	Finish Mockup Room	0		26-May-26
MIL-1440	Start Gypsum Board	0	27-May-26	
I-1130	Fire Alarm Inspection	47	28-May-26	04-Aug-26
MIL-1320	Plumbing Rough-ins Finish	0		29-May-26
I-1110	Fuel-Oil Storage & Fuel Oil Piping Systems Inspection	9	01-Jun-26	11-Jun-26
MIL-2952	Finish Standpipe System Inspection	0		05-Jun-26
MIL-1460	Roof Top Units Installations Start	0	08-Jun-26	
MIL-1450	Start 1st Coat Painting	0	10-Jun-26	
MIL-2992	Finish Fuel-Oil Storage & Fuel Oil Piping Systems Inspection	0		11-Jun-26
CON-8060	CON-ED - Switchgear Inspection	4	15-Jun-26	18-Jun-26
CON-8070	CON-ED - Pull Power Cable to the Building	10	22-Jun-26	06-Jul-26
MIL-1330	Finish Sprinkler Rough-ins	0		22-Jun-26
CON-7990	Gas Authorization	5	24-Jun-26	30-Jun-26
CON-8000	Pink Slip	5	01-Jul-26	08-Jul-26
CLO-1120	MDF & IDF Rooms Testing & Commissioning	12	06-Jul-26	21-Jul-26
MIL-2632	Finish HVAC	0		06-Jul-26
MIL-2982	Finish Fire-Resistant Penetrations And Joints Inspection	0		06-Jul-26
CLO-1010	HVAC Flush-Out	20	07-Jul-26	03-Aug-26
MIL-2732	Start Mechanical and Electrical System Commissioning	0	07-Jul-26	
CON-8080	CON-ED - Terminate Power Cables	10	07-Jul-26	20-Jul-26
PRO-2000	Procure & Deliver Key Cutting Machine	74	08-Jul-26	19-Sep-26
MIL-1480	Roof Top Units Installations Finish	0		14-Jul-26
MIL-2972	Finish Mechanical System Inspection	0		15-Jul-26
CLO-1140	SSDS System Testing & Commissioning	7	16-Jul-26	24-Jul-26
MIL-2562	Start Below Grade Plumbing and Other Utilities	0	16-Jul-26	

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
CON-8090	CON-ED - Energize to the Building	5	21-Jul-26	27-Jul-26
MIL-1600	MDF Work Finish	0		21-Jul-26*
MIL-1610	IDF Work Finish	0		21-Jul-26*
SUB-2330	Prepare & Submit Remedial Closure Report	3	27-Jul-26	29-Jul-26
MIL-2742	Permanent Power Available	0		27-Jul-26
MIL-2592	P&D - Connection to Roof Drains	0	28-Jul-26	
CLO-1240	Elevator Sump Pump Testing & Commissioning	21	28-Jul-26	25-Aug-26
CLO-1270	Water Heater Testing & Commissioning	21	28-Jul-26	25-Aug-26
CLO-1220	Emergency Generator Electric Load Test	3	29-Jul-26	31-Jul-26
APP-2330	Review & Approve Remedial Closure Report	21	30-Jul-26	19-Aug-26
PER-2640	Obtain Emergency Generator Permit	5	03-Aug-26	07-Aug-26
CLO-1250	Emergency Generator Testing & Commissioning	21	03-Aug-26	31-Aug-26
MIL-2692	Building HVAC Flush-out	0		03-Aug-26
CLO-1230	Air Handling Unit Testing & Commissioning	21	04-Aug-26	01-Sep-26
CLO-1190	Pre-Elevator Test Inspection	5	05-Aug-26	11-Aug-26
CLO-1290	Glycol System Testing & Commissioning	21	05-Aug-26	02-Sep-26
MIL-1680	Emergency Generator Final Sign-off	0		07-Aug-26
MIL-2642	Finish Fire Alarm Signoff	0		07-Aug-26
MIL-2962	Finish Fire Alarm Inspection	0		07-Aug-26
CLO-1020	Electrical System Testing & Commissioning	21	10-Aug-26	08-Sep-26
MIL-2802	Provision of Training Schedules (30 days prior to start of Training)	0	10-Aug-26	
CLO-1260	HVAC Split System Testing & Commissioning	21	10-Aug-26	08-Sep-26
CLO-1280	Fire Alarm Testing & Commissioning	21	10-Aug-26	08-Sep-26
MIL-2702	Finish Concrete Work	0		10-Aug-26
MIL-2822	Elevator Ready for Testing	0		11-Aug-26
CLO-1000	Elevator Testing & Commissioning	20	12-Aug-26	09-Sep-26
CLO-1160	Sprinkler/Domestic Booster Pumps Testing & Commissioning	14	20-Aug-26	09-Sep-26
MIL-2672	Finish Painting	0		28-Aug-26
CLO-1130	IPDVS System Testing & Commissioning	11	03-Sep-26	18-Sep-26
MIL-2722	Start Kitchen	0	04-Sep-26	
MIL-2662	Finishes and Ceiling Complete	0		04-Sep-26
CLO-1300	Provide Training	10	09-Sep-26	22-Sep-26
CLO-1170	Sprinkler/Domestic Booster Pumps Inspection	3	10-Sep-26	14-Sep-26
CLO-1200	Elevator DOB Inspection	5	10-Sep-26	16-Sep-26
MIL-1470	Finish Site Work	0		10-Sep-26
CLO-1030	Pre-Final Clean-Out	5	11-Sep-26	17-Sep-26
CLO-1180	Sprinkler/Domestic Booster Pumps Sign-offs	0		14-Sep-26
CLO-1150	FDNY Inspection	12	15-Sep-26	30-Sep-26
PER-2650	Elevator Equipment Use Permit	10	17-Sep-26	30-Sep-26
CLO-1040	Pre-TCO Inspection	11	18-Sep-26	02-Oct-26
MIL-1620	IPDVS Work Finish	0		18-Sep-26*
MIL-2652	Finish Mechanical and Electrical System Commissioning	0		18-Sep-26
MIL-2772	Performance test for all mechanical equipment and low voltage systems	0		18-Sep-26
MIL-2792	Commissioning for all mechanical equipment and low voltage systems	0		18-Sep-26

Full Schedule Layout Grouped by Area

Activity ID	Activity Name	Original Duration	Start	Finish
MIL-1650	FDNY Inspection Finish	0		30-Sep-26
MIL-1670	Elevator Final Sign-off	0		30-Sep-26
CLO-1110	Pre-TCO Punchlist	10	05-Oct-26	19-Oct-26
MIL-1510	TCO	0		19-Oct-26*
CLO-1050	Pre-Substantial Punchlist	105	20-Oct-26	17-Apr-27
MIL-1550	Substantial Completion	0		17-Apr-27*
CLO-1060	Prepare & Submit O&M Manuals	30	19-Apr-27	01-Jun-27
MIL-2782	Submission of Operations and Maintenance Manuals	0		01-Jun-27
CLO-1070	Prepare & Submit As-Built Drawings	30	02-Jun-27	15-Jul-27
CLO-1080	Final Inspection	5	16-Jul-27	22-Jul-27
CLO-1090	Final Clean Out	10	23-Jul-27	05-Aug-27
CLO-1100	Demobilization	10	06-Aug-27	15-Aug-27
MIL-1560	Final Completion	0		15-Aug-27*

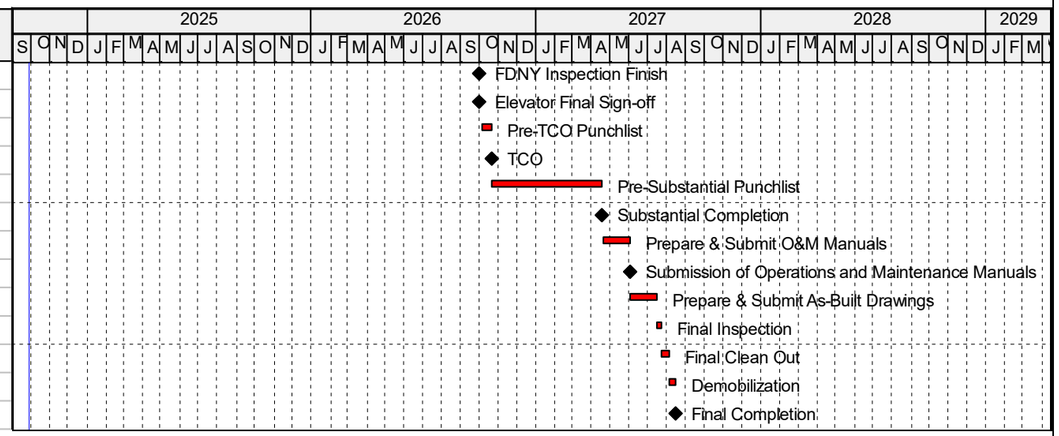

APPENDIX 5
Full Schedule Layout Grouped by PHAS Code

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
Preconstruction		699	30-Sep-24	15-Aug-27
Milestones		699	30-Sep-24	15-Aug-27
Major Milestones		699	30-Sep-24	15-Aug-27
MIL-1000	NTP	0	30-Sep-24	
MIL-1030	Project Duration(From NTP till TCO)	750	30-Sep-24	19-Oct-26
MIL-1040	Project Duration(From NTP till Substantial Completion)	930	30-Sep-24	17-Apr-27
MIL-1770	Project Duration(From NTP till Final Completion)	1050	30-Sep-24	15-Aug-27
MIL-2522	Site Access	365	30-Sep-24	29-Sep-25
MIL-1850	Construction Start	0	30-Sep-25	
MIL-1600	MDF Work Finish	0		21-Jul-26*
MIL-1610	IDF Work Finish	0		21-Jul-26*
MIL-1620	IPDVS Work Finish	0		18-Sep-26*
MIL-1510	TCO	0		19-Oct-26*
MIL-1550	Substantial Completion	0		17-Apr-27*
MIL-1560	Final Completion	0		15-Aug-27*
Contract Milestones		638	11-Oct-24	01-Jun-27
MIL-2542	Complete Subcontractor 'Buyout'	0		11-Oct-24
MIL-2572	Place Steel Mill Order	0	20-Feb-25	
MIL-2762	Green Schools Compliance Submission	0		04-Mar-25
MIL-1640	Provide Complete Set of Approved Coordination Drawings	0		23-May-25
MIL-2532	Submit Complete Permit Application	0		29-Sep-25
MIL-2832	Issuance of Excavation & Shoring Permit	0		29-Sep-25
MIL-2842	Issuance of Builders Pavement Permit	0		29-Sep-25
MIL-2852	Issuance of Permit to Enter (PTE)	0		29-Sep-25
MIL-2862	Issuance of NYPA Permit	0		29-Sep-25
MIL-2872	Issuance of Construction Fences Permit	0		29-Sep-25
MIL-2882	Issuance of Sidewalk Shed Permits	0		29-Sep-25
MIL-2892	Issuance of CCD1	0		29-Sep-25
MIL-2902	Issuance of DOB Permit & Insurance	0		29-Sep-25
MIL-1060	Mobilization Start	0	30-Sep-25	
MIL-1710	Complete Mobilization	0		03-Oct-25
MIL-2582	Start Concrete Placement	0	28-Oct-25	
MIL-2812	Start Foundation	0	28-Oct-25	
MIL-2912	Start Concrete Cast In Place Inspection	0	28-Oct-25	
MIL-1810	Crane Mobilization-Steel Installation start	0	05-Dec-25	
MIL-1120	Metal Decking Start	0	22-Dec-25	
MIL-2622	Deliveries of all owner-furnished equipment and/or materials	0		06-Feb-26
MIL-1140	Layout Start	0	23-Feb-26	
MIL-1150	Masonry Walls Start	0	23-Feb-26	
MIL-1180	MEP Risers Start	0	23-Feb-26	
MIL-1210	Duct Rough-ins Start	0	24-Feb-26	
MIL-1160	Top & Bottom Track Start	0	26-Feb-26	
MIL-1830	Crane Mobilization-Precast Sandwich Panels Installation Start	0	05-Mar-26	
MIL-2932	Start Masonry Inspection	0	05-Mar-26	

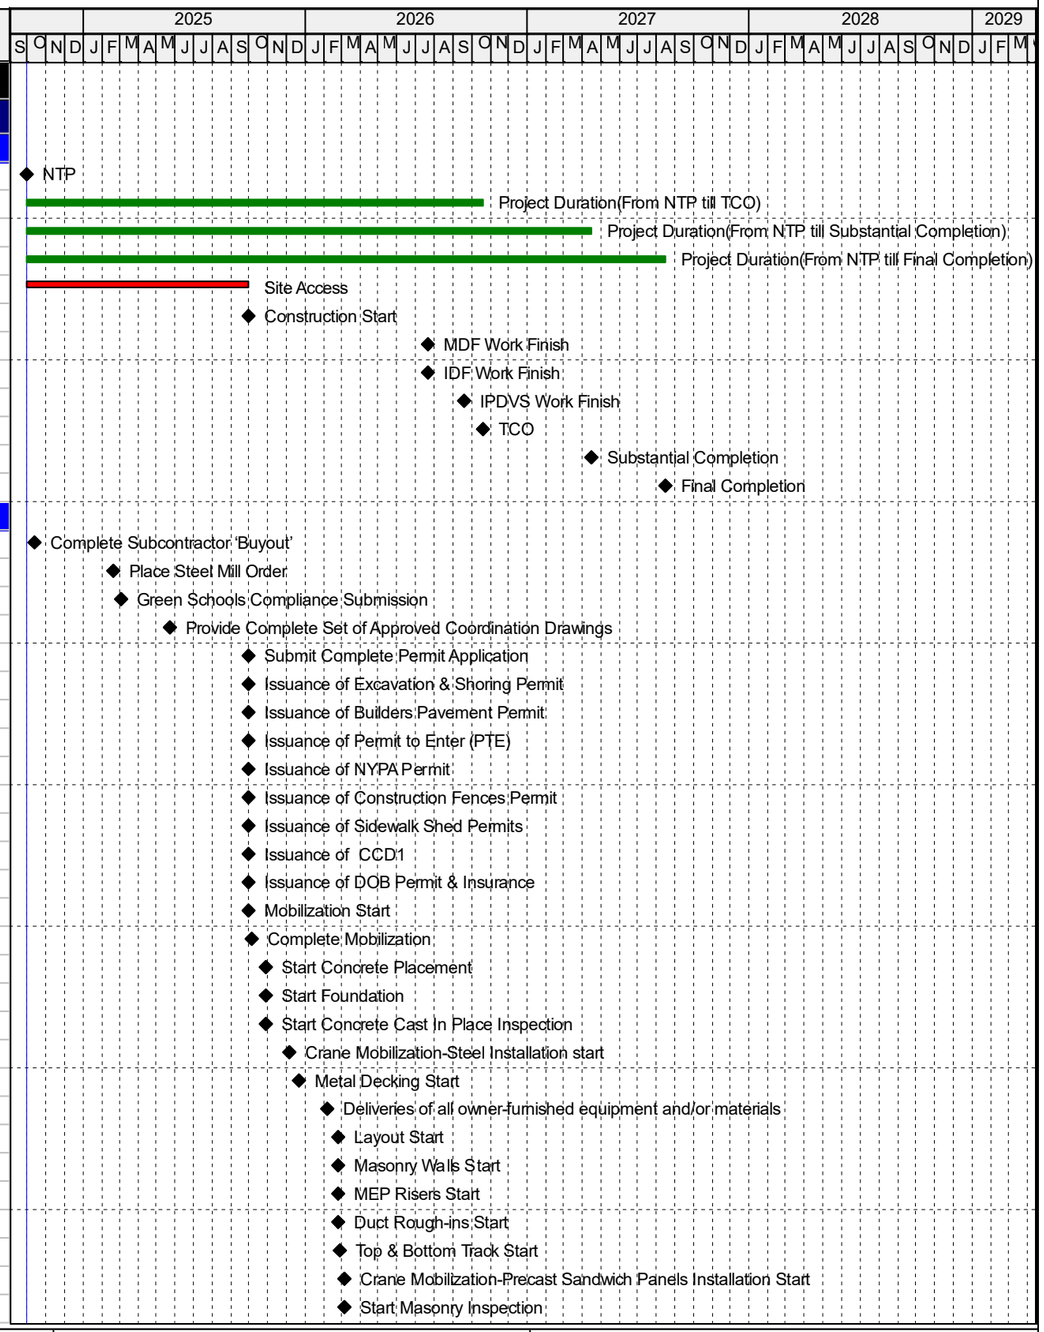

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

PROJECS
ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
MIL-1170	Finish Concrete Work	0		11-Mar-26
MIL-1820	Crane Mobilization-Steel Installation Finish	0		12-Mar-26
MIL-2612	Start Suspended Ceiling Grid	0	16-Mar-26	
MIL-1380	Crane Mobilization-Mechanical Subcontractor	78	17-Mar-26	07-Jul-26
MIL-2922	Start Pre -Cast Concrete Inspection	0	25-Mar-26	
MIL-1840	Crane Mobilization-Precast Sandwich Panels Installation Finish	0		06-Apr-26
MIL-1230	5th Floor Roofing Start	0	07-Apr-26	
MIL-2602	Start Mechanical Distribution Lines	0	08-Apr-26	
MIL-1200	Main Roofing Start	0	09-Apr-26	
MIL-1270	Electrical Rough-ins Start	0	09-Apr-26	
MIL-1220	Layout Finish	0		09-Apr-26
MIL-2942	Start In-Wall Inspection	0	10-Apr-26	
MIL-1290	Duct Rough-ins Finish	0		14-Apr-26
MIL-1250	Top & Bottom Track Finish	0		15-Apr-26
MIL-2712	Start Low Voltage	0	16-Apr-26	
MIL-1580	Window Installation Finish	0		28-Apr-26
MIL-1400	Start Site Work	0	29-Apr-26	
MIL-1300	Start Sprinkler Rough-ins	0	04-May-26	
MIL-1340	BLDG Tight	0		06-May-26
MIL-1350	Electrical Rough-ins Finish	0		06-May-26
MIL-1360	Start Mockup Room Work	0	07-May-26	
MIL-1430	Start Architecture Finishes	0	07-May-26	
MIL-1260	Plumbing Rough-ins Start	0	07-May-26	
MIL-1310	5th Floor Roofing Finish	0		13-May-26
MIL-1280	Main Roofing Finish	0		15-May-26
MIL-1410	Mockup Room Ready For Inspection	0		26-May-26
MIL-1420	Finish Mockup Room	0		26-May-26
MIL-1440	Start Gypsum Board	0	27-May-26	
MIL-1320	Plumbing Rough-ins Finish	0		29-May-26
MIL-2952	Finish Standpipe System Inspection	0		05-Jun-26
MIL-1460	Roof Top Units Installations Start	0	08-Jun-26	
MIL-1450	Start 1st Coat Painting	0	10-Jun-26	
MIL-1330	Finish Sprinkler Rough-ins	0		22-Jun-26
MIL-2632	Finish HVAC	0		06-Jul-26
MIL-2982	Finish Fire-Resistant Penetrations And Joints Inspection	0		06-Jul-26
MIL-2732	Start Mechanical and Electrical System Commissioning	0	07-Jul-26	
MIL-1480	Roof Top Units Installations Finish	0		14-Jul-26
MIL-2972	Finish Mechanical System Inspection	0		15-Jul-26
MIL-2562	Start Below Grade Plumbing and Other Utilities	0	16-Jul-26	
MIL-2742	Permanent Power Available	0		27-Jul-26
MIL-2592	P&D - Connection to Roof Drains	0	28-Jul-26	
MIL-2692	Building HVAC Flush-out	0		03-Aug-26
MIL-2642	Finish Fire Alarm Signoff	0		07-Aug-26
MIL-2962	Finish Fire Alarm Inspection	0		07-Aug-26

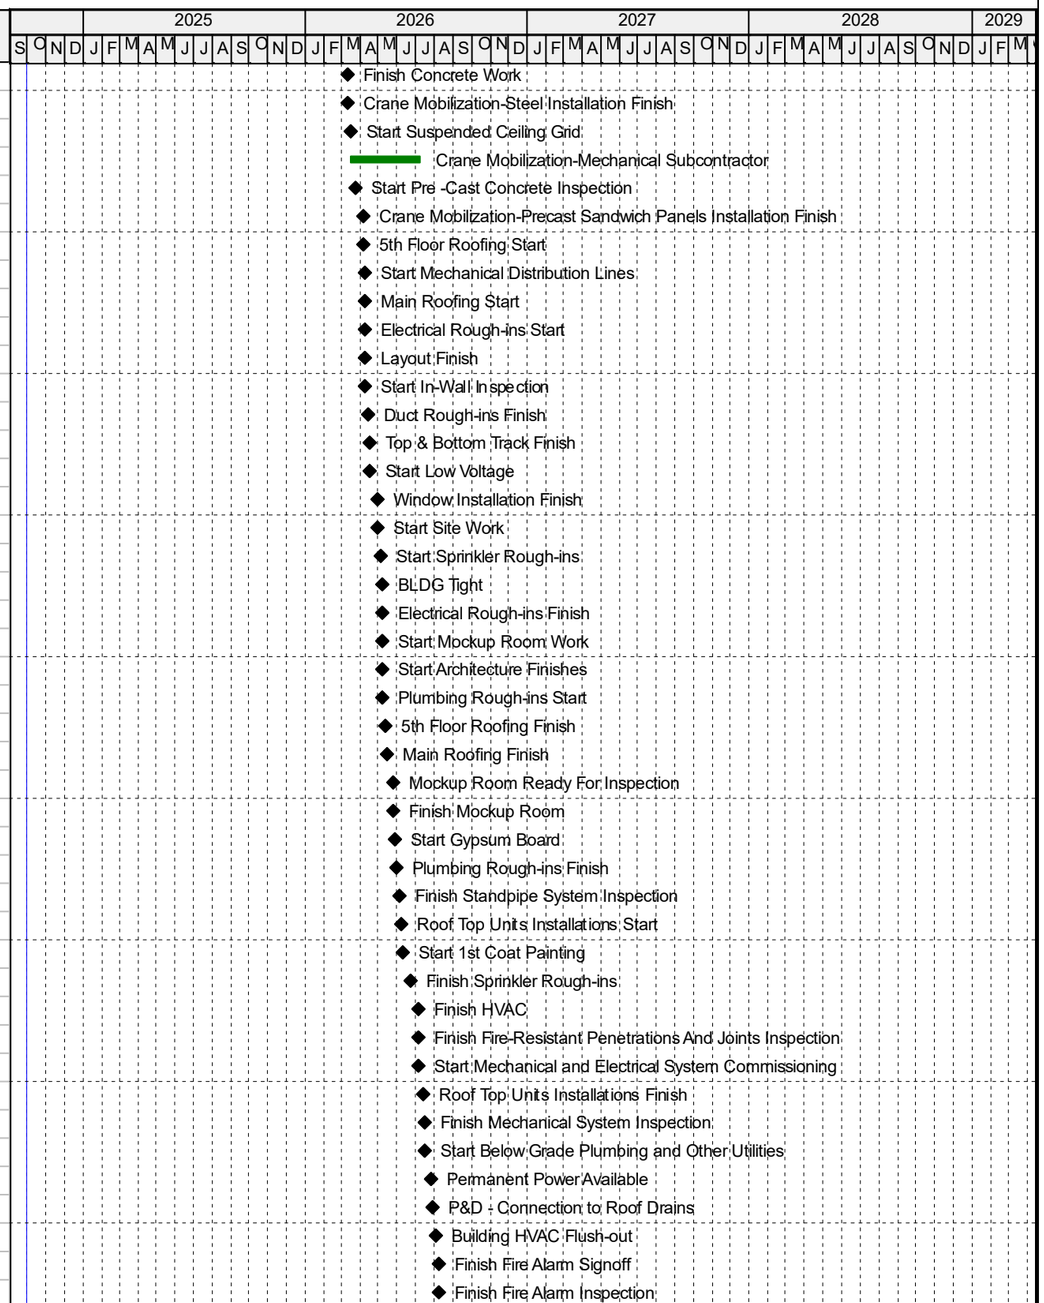

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

PROJECS
ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
MIL-2802	Provision of Training Schedules (30 days prior to start of Training)	0	10-Aug-26	
MIL-2702	Finish Concrete Work	0		10-Aug-26
MIL-2822	Elevator Ready for Testing	0		11-Aug-26
MIL-2672	Finish Painting	0		28-Aug-26
MIL-2722	Start Kitchen	0	04-Sep-26	
MIL-2662	Finishes and Ceiling Complete	0		04-Sep-26
MIL-1470	Finish Site Work	0		10-Sep-26
MIL-2652	Finish Mechanical and Electrical System Commissioning	0		18-Sep-26
MIL-2772	Performance test for all mechanical equipment and low voltage systems	0		18-Sep-26
MIL-2792	Commissioning for all mechanical equipment and low voltage systems	0		18-Sep-26
MIL-2782	Submission of Operations and Maintenance Manuals	0		01-Jun-27
Permits		279	30-Sep-24	10-Nov-25
PRE-2590	Meeting With SCA to Review The Permit Requirements	14	30-Sep-24	18-Oct-24
PRE-2600	Prepare & Submit Permit Waiver Requests to SCA Chief Project Officer	5	30-Sep-24	04-Oct-24
PRE-2630	Obtain Builders Pavement Permit	10	16-Sep-25	29-Sep-25
PRE-2640	Obtain Excavation & Shoring Permit	10	16-Sep-25	29-Sep-25
PRE-2650	Obtain Permit to Enter (PTE) Amtrak	10	16-Sep-25	29-Sep-25
PRE-2660	Obtain NYPA Permit	10	16-Sep-25	29-Sep-25
PRE-2540	SCA Work Notification	7	23-Sep-25	29-Sep-25
PRE-1660	DOB Permit & Insurance	3	25-Sep-25	29-Sep-25
PRE-1460	Obtain Construction Fences Permit	3	25-Sep-25	29-Sep-25
PRE-2550	Obtain CCD1	3	25-Sep-25	29-Sep-25
PRE-2570	Obtain Sidewalk Shed Permits	3	25-Sep-25	29-Sep-25
PRE-2610	Prepare & Submit FDNY Fuel Permit	10	06-Oct-25	20-Oct-25
PRE-2620	Review & Approve FDNY Fuel Permit	21	21-Oct-25	10-Nov-25
Mobilization		513	30-Sep-24	19-Oct-26
CON-99257	Subcontractor Buyout	10	30-Sep-24	11-Oct-24
MIL-1660	Start Security Guard Services (30 Days From NTP)	0	30-Oct-24	
CON-1000	Mobilization	4	30-Sep-25	03-Oct-25
CON-7740	Protection Of All Overhead & Underground Utilities	263	30-Sep-25	19-Oct-26
CON-9000	Protection & Restoration the adjacent Properties to Original Condition	263	30-Sep-25	19-Oct-26
CON-1080	Install Erosion Control Devices	2	06-Oct-25	07-Oct-25
CON-1010	Install Construction Signs	2	06-Oct-25	07-Oct-25
CON-1030	Install Construction Fences	2	06-Oct-25	07-Oct-25
CON-9120	Soli Sampling	2	06-Oct-25	07-Oct-25
CON-7750	Install Field Offices	5	08-Oct-25	15-Oct-25
CON-9140	Excavation	5	08-Oct-25	15-Oct-25
CON-8390	Install Sidewalk Sheds -South Elevation	4	29-Dec-25	02-Jan-26
CON-8400	Install Sidewalk Sheds -East Elevation	4	29-Dec-25	02-Jan-26
MIL-1720	Start Sidewalk Bridge Installations	0	29-Dec-25	
Utilities Coordination		450	07-Oct-24	27-Jul-26
Gas Coordination		437	07-Oct-24	08-Jul-26
CON-7960	Obtain Gas Meter Layout From CON-ED	5	07-Oct-24	11-Oct-24
CON-7970	Coordinate With CON-ED For Gas Service	7	16-Apr-26	24-Apr-26

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
CON-7990	Gas Authorization	5	24-Jun-26	30-Jun-26
CON-8000	Pink Slip	5	01-Jul-26	08-Jul-26
Temporary Power Coordination		428	07-Nov-24	27-Jul-26
CON-8010	Coordination With CON-ED For Temporary Electrical Power	10	07-Nov-24	21-Nov-24
CON-8020	Scheduling With CON-ED For Temporary Electrical Power	7	22-Nov-24	03-Dec-24
CON-8030	Procurement From CON-ED For Temporary Electrical Power	20	30-Sep-25	19-Oct-25
CON-8040	CON-ED Work For Temporary Electrical Power	10	20-Oct-25	31-Oct-25
CON-8050	Available Temporary Electrical Power For Testing MEP Equipment	0		31-Oct-25
CON-8060	CON-ED - Switchgear Inspection	4	15-Jun-26	18-Jun-26
CON-8070	CON-ED - Pull Power Cable to the Building	10	22-Jun-26	06-Jul-26
CON-8080	CON-ED - Terminate Power Cables	10	07-Jul-26	20-Jul-26
CON-8090	CON-ED - Energize to the Building	5	21-Jul-26	27-Jul-26
Procurement		483	15-Oct-24	19-Sep-26
Submittals & Approvals		462	15-Oct-24	19-Aug-26
Division 01 - General Requirements		153	15-Oct-24	23-May-25
Spec Section S01300 - Submittals		153	15-Oct-24	23-May-25
SUB-1410	Prepare & Submit Submittal Schedule	60	15-Oct-24	10-Jan-25
SUB-1780	Prepare & Submit Initial Underground Coordination Drawings	50	15-Oct-24	26-Dec-24
SUB-1790	Prepare & Submit Initial 1st Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1800	Prepare & Submit Initial 2nd Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1810	Prepare & Submit Initial 3rd Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1820	Prepare & Submit Initial 4th Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1830	Prepare & Submit Initial 5th Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
APP-1230	Review & Approve Initial Underground Coordination Drawings	21	27-Dec-24	16-Jan-25
APP-1260	Review & Approve Submittal Schedule	21	11-Jan-25	31-Jan-25
SUB-2270	Prepare & Submit Final Underground Coordination Drawings	37	17-Jan-25	11-Mar-25
APP-1330	Review & Approve Initial 1st Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1340	Review & Approve Initial 2nd Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1350	Review & Approve Initial 3rd Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1360	Review & Approve Initial 4th Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1370	Review & Approve Initial 5th Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
SUB-2280	Prepare & Submit Final 1st Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2290	Prepare & Submit Final 2nd Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2300	Prepare & Submit Final 3rd Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2310	Prepare & Submit Final 4th Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2320	Prepare & Submit Final 5th Floor Coordination Drawings	49	25-Feb-25	02-May-25
APP-2270	Review & Approve Final Foundations Coordination Drawings	21	12-Mar-25	01-Apr-25
APP-2280	Review & Approve Final 1st Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2290	Review & Approve Final 2nd Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2300	Review & Approve Final 3rd Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2310	Review & Approve Final 4th Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2320	Review & Approve Final 5th Floor Coordination Drawings	21	03-May-25	23-May-25
Spec Section S01311 - Progress Schedule		65	15-Oct-24	20-Jan-25
SUB-1610	Prepare & Submit Baseline Schedule	52	15-Oct-24	30-Dec-24

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1240	Review & Approve Baseline Schedule	21	31-Dec-24	20-Jan-25
Spec Section S01352 - Sustainability Requirements		24	15-Oct-24	18-Nov-24
SUB-1400	Prepare & Submit Sustainable Materials	10	15-Oct-24	28-Oct-24
APP-1040	Review & Approve Sustainable Materials	21	29-Oct-24	18-Nov-24
Spec Section S01400 - Quality Control		44	15-Oct-24	17-Dec-24
SUB-1570	Prepare & Submit QCP	30	15-Oct-24	26-Nov-24
APP-1130	Review & Approve QCP	21	27-Nov-24	17-Dec-24
Spec Section S01426 - Sample Classroom		95	15-Oct-24	04-Mar-25
SUB-1390	Prepare & Submit Sample Classroom Materials	81	15-Oct-24	11-Feb-25
APP-1640	Review & Approve Sample Classroom Materials	21	12-Feb-25	04-Mar-25
Spec Section S01500 - Temporary Facilities and Controls		95	15-Oct-24	04-Mar-25
SUB-1370	Prepare & Submit Photo Submission - Temporary Fence	15	15-Oct-24	04-Nov-24
SUB-1380	Prepare & Submit Heating Plan	81	15-Oct-24	11-Feb-25
SUB-2340	Prepare & Submit Tree Protection Plan	71	15-Oct-24	28-Jan-25
APP-1060	Review & Approve Photo Submission - Temporary Fence	21	05-Nov-24	25-Nov-24
APP-2340	Review & Approve Tree Protection Plan	21	29-Jan-25	18-Feb-25
APP-1630	Review & Approve Heating Plan	21	12-Feb-25	04-Mar-25
Spec Section S01524 - Construction Waste Management		95	15-Oct-24	04-Mar-25
SUB-1360	Prepare & Submit CWM Plan	81	15-Oct-24	11-Feb-25
APP-1620	Review & Approve CWM Plan	21	12-Feb-25	04-Mar-25
Spec Section S01535 - Safety Program		17	15-Oct-24	06-Nov-24
SUB-1350	Prepare & Submit Site Safety Plan	2	15-Oct-24	16-Oct-24
APP-1000	Review & Approve Site Safety Plan	21	17-Oct-24	06-Nov-24
Spec Section S01550 - Indoor Air Quality (IAQ) Requirements		95	15-Oct-24	04-Mar-25
SUB-1340	Prepare & Submit Construction Indoor Air Quality Management Plan	81	15-Oct-24	11-Feb-25
APP-1610	Review & Approve Construction Indoor Air Quality Management Plan	21	12-Feb-25	04-Mar-25
Spec Section S01560 - Installation Sequence of Finish Materials		95	15-Oct-24	04-Mar-25
SUB-1330	Prepare & Submit Temporary Ventilation Plan	81	15-Oct-24	11-Feb-25
APP-1600	Review & Approve Temporary Ventilation Plan	21	12-Feb-25	04-Mar-25
Spec Section S01630 - Product Substitutions		96	15-Oct-24	05-Mar-25
SUB-1320	Prepare & Submit Product Substitutions	82	15-Oct-24	12-Feb-25
APP-2260	Review & Approve Product Substitutions	21	13-Feb-25	05-Mar-25
Spec Section S01650 - Facility Start-Up, Demonstration, and Training		95	15-Oct-24	04-Mar-25
SUB-1310	Prepare & Submit Training Outline & Schedule	81	15-Oct-24	11-Feb-25
APP-1590	Review & Approve Training Outline & Schedule	21	12-Feb-25	04-Mar-25
Spec Section S01660 - Supplemental Comissioning Requirements		95	15-Oct-24	04-Mar-25
SUB-1840	Prepare & Submit Supplemental Comissioning Requirements	81	15-Oct-24	11-Feb-25
APP-1850	Review & Approve Supplemental Comissioning Requirements	21	12-Feb-25	04-Mar-25
Spec Section S01720 - Record Documents		95	15-Oct-24	04-Mar-25
SUB-1850	Prepare & Submit Record Documents	81	15-Oct-24	11-Feb-25
APP-1860	Review & Approve Record Documents	21	12-Feb-25	04-Mar-25
Division 02 - Site Work		462	15-Oct-24	19-Aug-26
Spec Section 02010 - Environmental Site Assessment Reports		95	15-Oct-24	04-Mar-25
SUB-1860	Prepare & Submit Environmental Site Assessment Reports	81	15-Oct-24	11-Feb-25

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1870	Review & Approve Environmental Site Assessment Reports	21	12-Feb-25	04-Mar-25
Spec Section 02070 - Selective Removals & Demoloition		95	15-Oct-24	04-Mar-25
SUB-1870	Prepare & Submit Selective Removals & Demoloition	81	15-Oct-24	11-Feb-25
SUB-3900	Prepare & Submit Lightning Protection Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3920	Prepare & Submit Lightning Protection Test Reports	81	15-Oct-24	11-Feb-25
APP-1880	Review & Approve Selective Removals & Demoloition	21	12-Feb-25	04-Mar-25
APP-3900	Review & Approve Lightning Protection Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3920	Review & Approve Lightning Protection Test Reports	21	12-Feb-25	04-Mar-25
Spec Section 02090 - Environmental Management Of Excavated Material And Fill/Backfil		258	15-Oct-24	24-Oct-25
SUB-2920	Prepare & Submit Documentation of Proper Disposal	81	15-Oct-24	11-Feb-25
APP-2920	Review & Approve Documentation of Proper Disposal	21	12-Feb-25	04-Mar-25
SUB-2900	Prepare & Submit Excavated Material Disposal Plan	71	26-May-25	05-Sep-25
SUB-4050	Prepare & Submit Soil Sampling Plan	71	26-May-25	05-Sep-25
APP-2900	Review & Approve Excavated Material Disposal Plan	21	06-Sep-25	26-Sep-25
APP-4050	Review & Approve Soil Sampling Plan	21	06-Sep-25	26-Sep-25
SUB-2910	Prepare & Submit Backfill & Resue Plan	20	08-Sep-25	03-Oct-25
APP-2910	Review & Approve Backfill & Resue Plan	21	04-Oct-25	24-Oct-25
Spec Section 02100 - Site Preparation		24	15-Oct-24	18-Nov-24
SUB-1300	Prepare & Submit Existing Conditions Survey	10	15-Oct-24	28-Oct-24
APP-1030	Review & Approve Existing Conditions Survey	21	29-Oct-24	18-Nov-24
Spec Section 02200 - Earthwork		21	15-Oct-24	13-Nov-24
SUB-1560	Prepare & Submit Erosion Control and Sedimentation Plan	7	15-Oct-24	23-Oct-24
APP-1020	Review & Approve Erosion Control and Sedimentation Plan	21	24-Oct-24	13-Nov-24
Spec Section 02220 - Gas Vapor Barrier (Fluid Applied)		95	15-Oct-24	04-Mar-25
SUB-1290	Prepare & Submit Gas Vapor Barrier Submittal & Inspection Schedule	81	15-Oct-24	11-Feb-25
APP-1580	Review & Approve Gas Vapor Barrier Submittal & Inspection Schedule	21	12-Feb-25	04-Mar-25
Spec Section 02221 - Sub-Slab Depressurization System		462	15-Oct-24	19-Aug-26
SUB-1280	Prepare & Submit SSDS Geotextile	40	15-Oct-24	11-Dec-24
APP-1200	Review & Approve SSDS Geotextile	21	12-Dec-24	01-Jan-25
SUB-2330	Prepare & Submit Remedial Closure Report	3	27-Jul-26	29-Jul-26
APP-2330	Review & Approve Remedial Closure Report	21	30-Jul-26	19-Aug-26
Spec Section 02250 - Foundation & Other Change Adjustements		19	15-Oct-24	11-Nov-24
SUB-1880	Prepare & Submit Foundation Product Data	5	15-Oct-24	21-Oct-24
APP-1010	Review & Approve Foundation Product Data	21	22-Oct-24	11-Nov-24
Spec Section 02511 - Asphaltic Concrete Paving		95	15-Oct-24	04-Mar-25
SUB-1270	Prepare & Submit Asphaltic Concrete Paving	81	15-Oct-24	11-Feb-25
APP-1570	Review & Approve Asphaltic Concrete Paving	21	12-Feb-25	04-Mar-25
Spec Section 02513 - Sidewalk and Street Paving		95	15-Oct-24	04-Mar-25
SUB-1260	Prepare & Submit Steel Curb Facing Shop Drawing	81	15-Oct-24	11-Feb-25
APP-1560	Review & Approve Steel Curb Facing Shop Drawing	21	12-Feb-25	04-Mar-25
Spec Section 02521 - Concrete Curbs and Pavements		95	15-Oct-24	04-Mar-25
SUB-1250	Prepare & Submit Concrete Curbs & Pavements Shop Drawing	81	15-Oct-24	11-Feb-25
APP-1550	Review & Approve Concrete Curbs & Pavements Shop Drawing	21	12-Feb-25	04-Mar-25
Spec Section 02260 - Excavation Support And Monitoring		95	15-Oct-24	04-Mar-25

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-2360	Prepare & Submit Adjacent Property and Structures Protection & Monitoring Plan	81	15-Oct-24	11-Feb-25
APP-2360	Review & Approve Adjacent Property and Structures Protection & Monitoring Plan	21	12-Feb-25	04-Mar-25
Spec Section 02721 - Trench Drains		95	15-Oct-24	04-Mar-25
SUB-1890	Prepare & Submit Trench Drains Product Data	81	15-Oct-24	11-Feb-25
APP-1890	Review & Approve Trench Drains Prodcut Data	21	12-Feb-25	04-Mar-25
Spec Section 02722 - PC Basins, Detention Basins, and Manholes		95	15-Oct-24	04-Mar-25
SUB-1240	Prepare & Submit Catch Basin Shop Drawings	81	15-Oct-24	11-Feb-25
APP-1540	Review & Approve Catch Basin Shop Drawings	21	12-Feb-25	04-Mar-25
Spec Section 02723 - Storm Drainage Systems		51	15-Oct-24	27-Dec-24
SUB-1230	Prepare & Submit Ductile Iron Pipes	37	15-Oct-24	06-Dec-24
APP-1150	Review & Approve Ductile Iron Pipes	21	07-Dec-24	27-Dec-24
Spec Section 02860 - Early Childhood Playground Equipment		95	15-Oct-24	04-Mar-25
SUB-1220	Prepare & Submit Playgroung Equipment Shop Drawings	81	15-Oct-24	11-Feb-25
APP-1530	Review & Approve Playgroung Equipment Shop Drawings	21	12-Feb-25	04-Mar-25
Spec Section 02862 - Outdoor Game Equipment		95	15-Oct-24	04-Mar-25
SUB-1910	Prepare & Submit Outdoor Game Equipment	81	15-Oct-24	11-Feb-25
APP-1910	Review & Approve Outdoor Game Equipment	21	12-Feb-25	04-Mar-25
Spec Section 02870 - Site Furnishings		29	15-Oct-24	25-Nov-24
SUB-1210	Prepare & Submit Site Furnishings Shop Drawings	15	15-Oct-24	04-Nov-24
APP-1050	Review & Approve Site Furnishings Shop Drawings	21	05-Nov-24	25-Nov-24
Spec Section 02900 - Landscaping		95	15-Oct-24	04-Mar-25
SUB-1200	Prepare & Submit Planting Schedule	81	15-Oct-24	11-Feb-25
APP-1520	Review & Approve Planting Schedule	21	12-Feb-25	04-Mar-25
Division 03 - Concrete		95	15-Oct-24	04-Mar-25
Spec Section 03100 - Concrete Formwork		95	15-Oct-24	04-Mar-25
SUB-1190	Prepare & Submit Formwork Shop Drawings	81	15-Oct-24	11-Feb-25
APP-1510	Review & Approve Formwork Shop Drawings	21	12-Feb-25	04-Mar-25
Spec Section 03200 - Concrete Reinforcement		44	15-Oct-24	17-Dec-24
SUB-1180	Prepare & Submit Concrete Reinforcement	30	15-Oct-24	26-Nov-24
APP-1100	Review & Approve Concrete Reinforcement	21	27-Nov-24	17-Dec-24
Spec Section 03300 - Cast in Place Concrete		44	15-Oct-24	17-Dec-24
SUB-1450	Prepare & Submit Concrete Shop Drawings	30	15-Oct-24	26-Nov-24
SUB-1580	Prepare & Submit Concrete Mix Design	30	15-Oct-24	26-Nov-24
APP-1110	Review & Approve Concrete Shop Drawings	21	27-Nov-24	17-Dec-24
APP-1140	Review & Approve Concrete Mix Design	21	27-Nov-24	17-Dec-24
Spec Section 03450 - Precast Architectural Concrete		86	15-Oct-24	18-Feb-25
SUB-1920	Prepare & Submit Precast Architectural Concrete	71	15-Oct-24	28-Jan-25
APP-1920	Review & Approve Precast Architectural Concrete	21	29-Jan-25	18-Feb-25
Spec Section 03542 - Cement Based Self Leveling Underlayment		95	15-Oct-24	04-Mar-25
SUB-1170	Prepare & Submit Certification of Material	81	15-Oct-24	11-Feb-25
APP-1500	Review & Approve Certification of Material	21	12-Feb-25	04-Mar-25
Division 04 - Masonry		95	15-Oct-24	04-Mar-25
Spec Section 04200 - Unit Masonry		86	15-Oct-24	18-Feb-25
SUB-1930	Prepare & Submit Unit Masonry Product Data	71	15-Oct-24	28-Jan-25

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1930	Review & Approve Unit Masonry Product Data	21	29-Jan-25	18-Feb-25
Spec Section 04435 - Cast Stone		95	15-Oct-24	04-Mar-25
SUB-1940	Prepare & Submit Cast Stone Product Data	81	15-Oct-24	11-Feb-25
APP-1940	Review & Approve Cast Stone Product Data	21	12-Feb-25	04-Mar-25
Division 05 - Metals		190	15-Oct-24	18-Jul-25
Spec Section 05120 - Structural Steel		86	15-Oct-24	18-Feb-25
SUB-1950	Prepare & Submit Structure Steel Drawings	71	15-Oct-24	28-Jan-25
APP-1950	Review & Approve Structure Steel Drawings	21	29-Jan-25	18-Feb-25
Spec Section 05170 - Support System for Suspended Ceilings		95	15-Oct-24	04-Mar-25
SUB-1160	Prepare & Submit Suspension Assembly Shop Drawings	81	15-Oct-24	11-Feb-25
APP-1490	Review & Approve Suspension Assembly Shop Drawings	21	12-Feb-25	04-Mar-25
Spec Section 05300 - Metal Deck		95	15-Oct-24	04-Mar-25
SUB-1960	Prepare & Submit Metal Deck Product Data	81	15-Oct-24	11-Feb-25
APP-1960	Review & Approve Metal Deck Product Data	21	12-Feb-25	04-Mar-25
Spec Section 05500 - Metal Fabrications		190	15-Oct-24	18-Jul-25
SUB-1900	Prepare & Submit Chain Link Fences & Gates Drawings	81	15-Oct-24	11-Feb-25
APP-1900	Review & Approve Chain Link Fences & Gates Drawings	21	12-Feb-25	04-Mar-25
SUB-1700	Prepare & Submit Roof Dunnage	81	05-Mar-25	27-Jun-25
APP-1810	Review & Approve Roof Dunnage	21	28-Jun-25	18-Jul-25
Spec Section 05700 - Ornamental Metal		95	15-Oct-24	04-Mar-25
SUB-2370	Prepare & Submit Ornamenta Metal Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2930	Prepare & Submit Ornamenta Metal Product Data	81	15-Oct-24	11-Feb-25
APP-2370	Review & Approve Ornamenta Metal Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2930	Review & Approve Ornamenta Metal Product Data	21	12-Feb-25	04-Mar-25
Spec Section 05710 - Steel Stairs		95	15-Oct-24	04-Mar-25
SUB-4060	Prepare & Submit Steel Stairs Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-4070	Prepare & Submit Steel Stairs Product Data	81	15-Oct-24	11-Feb-25
APP-4060	Review & Approve Steel Stairs Shop Drawings	21	12-Feb-25	04-Mar-25
APP-4070	Review & Approve Steel Stairs Product Data	21	12-Feb-25	04-Mar-25
Spec Section 05810 - Prefabricated Expansion Joint Covers		95	15-Oct-24	04-Mar-25
SUB-1970	Prepare & Submit Prefabricated Expansion Joint Covers	81	15-Oct-24	11-Feb-25
APP-1970	Review & Approve Prefabricated Expansion Joint Covers	21	12-Feb-25	04-Mar-25
Division 06 - Wood & Plastics		95	15-Oct-24	04-Mar-25
Spec Section 06200 - Finish Carpentry		95	15-Oct-24	04-Mar-25
SUB-1530	Prepare & Submit Furniture	81	15-Oct-24	11-Feb-25
APP-1720	Review & Approve Furniture	21	12-Feb-25	04-Mar-25
Spec Section 06410 - Custom Casework		95	15-Oct-24	04-Mar-25
SUB-1510	Prepare & Submit Millwork	81	15-Oct-24	11-Feb-25
APP-1710	Review & Approve Millwork	21	12-Feb-25	04-Mar-25
Division 07 - Thermal & Moisture Protection		95	15-Oct-24	04-Mar-25
Spec Section 07147 - Crystalline Waterproofing		95	15-Oct-24	04-Mar-25
SUB-1150	Prepare & Submit Crystalline Waterproofing Product Data	81	15-Oct-24	11-Feb-25
APP-1480	Review & Approve Crystalline Waterproofing Product Data	21	12-Feb-25	04-Mar-25
Spec Section 07211 - Perimeter Foundation Insulation		95	15-Oct-24	04-Mar-25

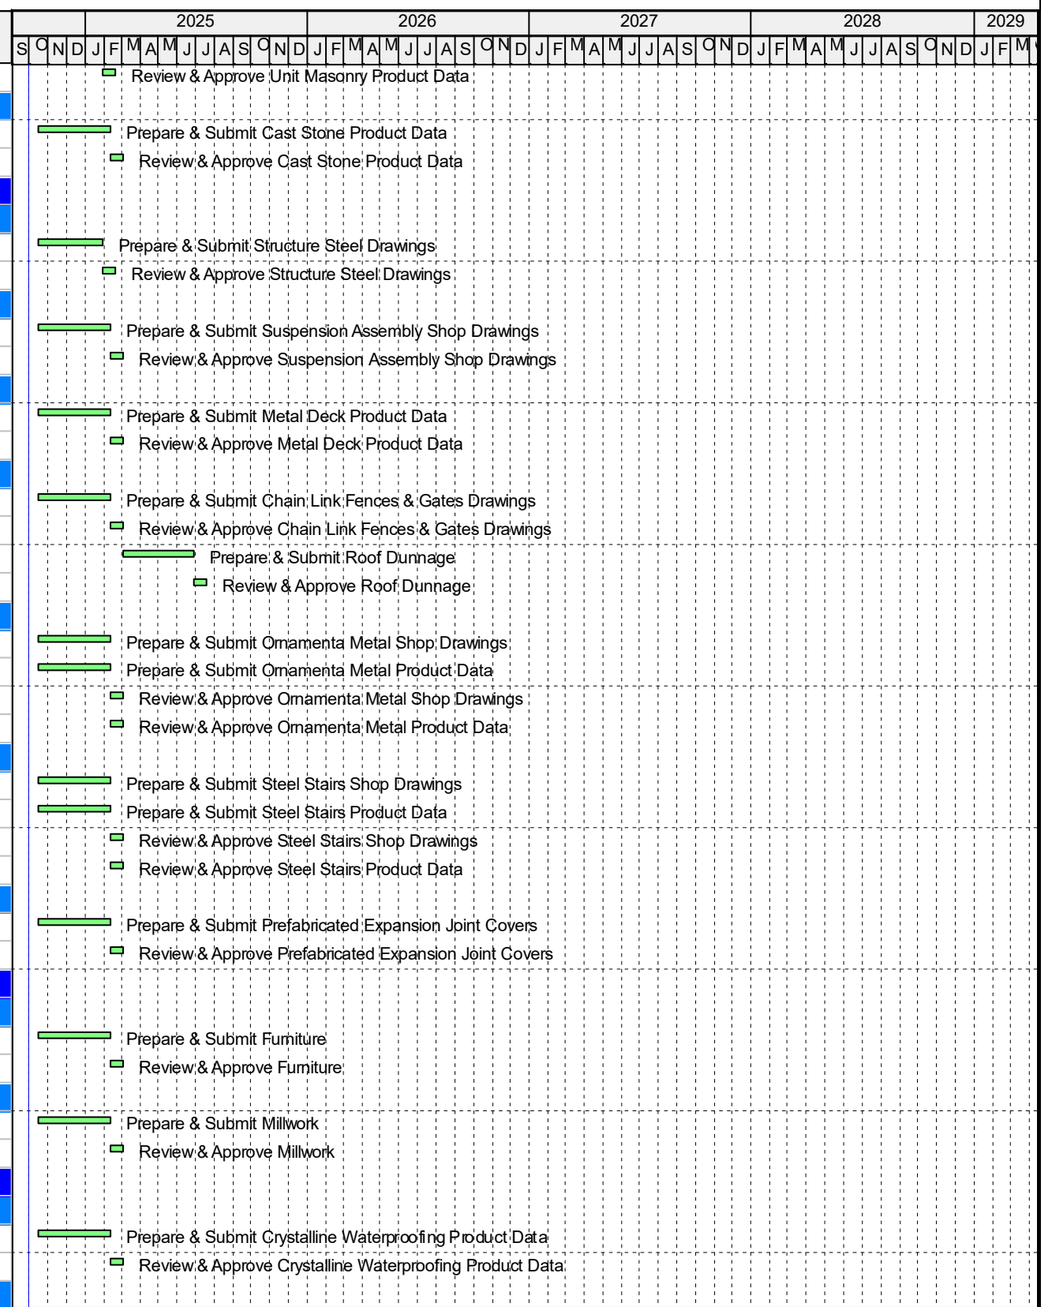

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1140	Prepare & Submit Perimeter Foundation Insulation Product Data	81	15-Oct-24	11-Feb-25
APP-1470	Review & Approve Perimeter Foundation Insulation Product Data	21	12-Feb-25	04-Mar-25
Spec Section 07271 - Self Adhering Sheet Air Barriers		95	15-Oct-24	04-Mar-25
SUB-1980	Prepare & Submit Self Adhering Sheet Air Barriers	81	15-Oct-24	11-Feb-25
APP-1980	Review & Approve Self Adhering Sheet Air Barriers	21	12-Feb-25	04-Mar-25
Spec Section 07414 - Metal Plate Wall Panels		95	15-Oct-24	04-Mar-25
SUB-1990	Prepare & Submit Metal Plate Wall Panels	81	15-Oct-24	11-Feb-25
SUB-4080	Prepare & Submit Green School Submittal	81	15-Oct-24	11-Feb-25
APP-1990	Review & Approve Metal Plate Wall Panels	21	12-Feb-25	04-Mar-25
APP-4080	Review & Approve Green School Submittal	21	12-Feb-25	04-Mar-25
Spec Section 07560 - Fluid Applied Protected Membrane Roofing		95	15-Oct-24	04-Mar-25
SUB-1130	Prepare & Submit Roofing Membrane Product Data	81	15-Oct-24	11-Feb-25
APP-1460	Review & Approve Roofing Membrane Product Data	21	12-Feb-25	04-Mar-25
Spec Section 07600 - Flashing and Sheet Metal		95	15-Oct-24	04-Mar-25
SUB-1120	Prepare & Submit Flashing & Sheet Metal Shop Drawing	81	15-Oct-24	11-Feb-25
APP-1450	Review & Approve Flashing & Sheet Metal Shop Drawing	21	12-Feb-25	04-Mar-25
Spec Section 07720 - Roof Accessories		95	15-Oct-24	04-Mar-25
SUB-1110	Prepare & Submit Roof Drains & Clean Outs	81	15-Oct-24	11-Feb-25
APP-1440	Review & Approve Roof Drains & Clean Outs	21	12-Feb-25	04-Mar-25
Division 08 - Doors & Windows		95	15-Oct-24	04-Mar-25
Spec Section 08110 - Steel Doors and Frames		95	15-Oct-24	04-Mar-25
SUB-1100	Prepare & Submit Door & Frame Corners Samples	81	15-Oct-24	11-Feb-25
APP-1430	Review & Approve Door & Frame Corners Samples	21	12-Feb-25	04-Mar-25
Spec Section 08210 - Wood Doors		95	15-Oct-24	04-Mar-25
SUB-1620	Prepare & Submit Wood Doors	81	15-Oct-24	11-Feb-25
APP-1750	Review & Approve Wood Doors	21	12-Feb-25	04-Mar-25
Spec Section - 08330 Coiling Doors, Grilles And Shutters		95	15-Oct-24	04-Mar-25
SUB-2960	Prepare & Submit Coiling Doors, Grilles and Shutters Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2970	Prepare & Submit Coiling Doors, Grilles and Shutters Product Data	81	15-Oct-24	11-Feb-25
APP-2960	Review & Approve Coiling Doors, Grilles and Shutters Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2970	Review & Approve Coiling Doors, Grilles and ShuttersProduct Data	21	12-Feb-25	04-Mar-25
Spec Section - 08411 Aluminum Framed Entrances And Storefronts		95	15-Oct-24	04-Mar-25
SUB-2980	Prepare & Submit Aluminum Framed Entrances & Storefronts Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2990	Prepare & Submit Aluminum Framed Entrances & Storefronts Product Data	81	15-Oct-24	11-Feb-25
APP-2980	Review & Approve Aluminum Framed Entrances & Storefronts Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2990	Review & Approve Aluminum Framed Entrances & Storefronts Product Data	21	12-Feb-25	04-Mar-25
Spec Section - 08521 Fire Rated Glazing Systems		95	15-Oct-24	04-Mar-25
SUB-3040	Prepare & Submit Fire Rated Glazing Samples	81	15-Oct-24	11-Feb-25
SUB-3050	Prepare & Submit Fire Rated Glazing Product Data	81	15-Oct-24	11-Feb-25
APP-3040	Review & Approve Fire Rated Glazing Samples	21	12-Feb-25	04-Mar-25
APP-3050	Review & Approve Fire Rated Glazing Product Data	21	12-Feb-25	04-Mar-25
Spec Section 08524 - Aluminum Windows & Entrances		86	15-Oct-24	18-Feb-25
SUB-1670	Prepare & Submit Aluminum Projected Windows	71	15-Oct-24	28-Jan-25
APP-1310	Review & Approve Aluminum Projected Windows	21	29-Jan-25	18-Feb-25

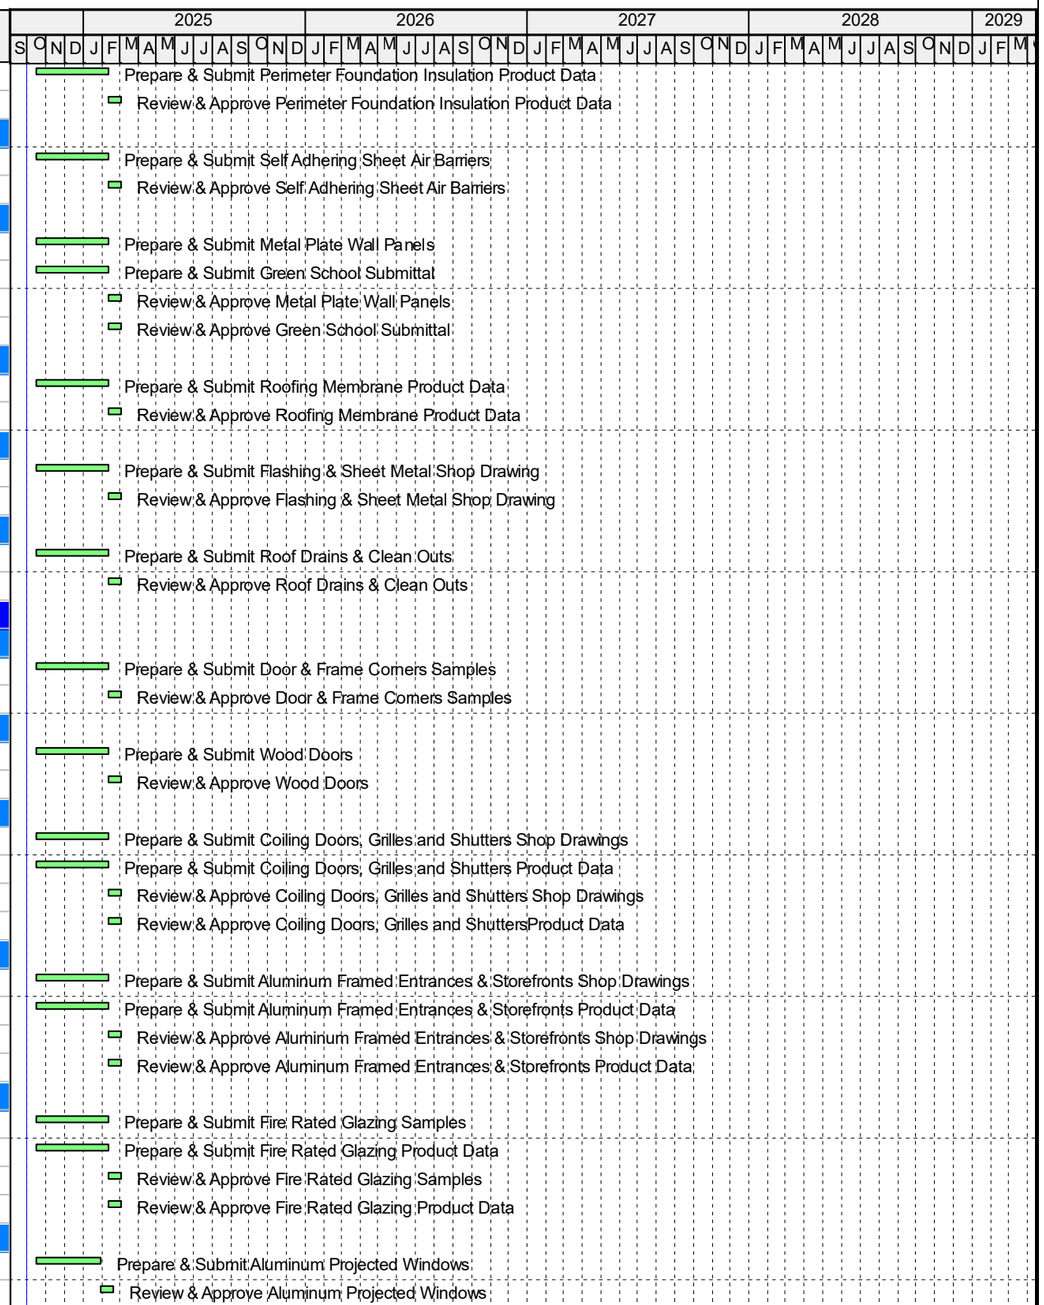

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
Spec Section 08662 - Security Screens & Barriers		95	15-Oct-24	04-Mar-25
SUB-2000	Prepare & Submit Security Screens & Barriers	81	15-Oct-24	11-Feb-25
APP-2000	Review & Approve Security Screens & Barriers	21	12-Feb-25	04-Mar-25
Spec Section 08710 - Finish Hardware		95	15-Oct-24	04-Mar-25
SUB-1080	Prepare & Submit Door Hardware Submittal	81	15-Oct-24	11-Feb-25
APP-1410	Review & Approve Door Hardware Submittal	21	12-Feb-25	04-Mar-25
Spec Section - 08730 Thresholds, Weatherstripping And Seals		95	15-Oct-24	04-Mar-25
SUB-3000	Prepare & Submit Thresholds, Weatherstripping and Seals Color Samples	81	15-Oct-24	11-Feb-25
SUB-3010	Prepare & Submit Thresholds, Weatherstripping and Seals Product Data	81	15-Oct-24	11-Feb-25
APP-3000	Review & Approve Thresholds, Weatherstripping and Seals Color Samples	21	12-Feb-25	04-Mar-25
APP-3010	Review & Approve Thresholds, Weatherstripping and Seals Product Data	21	12-Feb-25	04-Mar-25
Spec Section - 08800 Miscellaneous Glazing		95	15-Oct-24	04-Mar-25
SUB-3020	Prepare & Submit Miscellaneous Glazing Samples	81	15-Oct-24	11-Feb-25
SUB-3030	Prepare & Submit Miscellaneous Glazing Product Data	81	15-Oct-24	11-Feb-25
APP-3020	Review & Approve Miscellaneous Glazing Samples	21	12-Feb-25	04-Mar-25
APP-3030	Review & Approve Miscellaneous Glazing Product Data	21	12-Feb-25	04-Mar-25
Division 09 - Finishes		95	15-Oct-24	04-Mar-25
Spec Section 09260 - Gypsum Board Assemblies		95	15-Oct-24	04-Mar-25
SUB-1470	Prepare & Submit Gypsum Board	81	15-Oct-24	11-Feb-25
APP-1680	Review & Approve Gypsum Board	21	12-Feb-25	04-Mar-25
Spec Section 09310 - Ceramic Tiles		95	15-Oct-24	04-Mar-25
SUB-1070	Prepare & Submit Ceramic Tiles Product Data	81	15-Oct-24	11-Feb-25
APP-1400	Review & Approve Ceramic Tiles Product Data	21	12-Feb-25	04-Mar-25
Spec Section 09510 - Acoustical Ceilings		74	15-Oct-24	31-Jan-25
SUB-1490	Prepare & Submit Acoustical Ceiling Tiles	60	15-Oct-24	10-Jan-25
APP-1270	Review & Approve Acoustical Ceiling Tiles	21	11-Jan-25	31-Jan-25
Spec Section 09650 - Resilient Flooring		95	15-Oct-24	04-Mar-25
SUB-1480	Prepare & Submit Floorings	81	15-Oct-24	11-Feb-25
APP-1690	Review & Approve Floorings	21	12-Feb-25	04-Mar-25
Spec Section 09590 - Wood Flooring		95	15-Oct-24	04-Mar-25
SUB-2010	Prepare & Submit Wood Flooring	81	15-Oct-24	11-Feb-25
APP-2010	Review & Approve Wood Flooring	21	12-Feb-25	04-Mar-25
Spec Section - 09800 Special Coatings		95	15-Oct-24	04-Mar-25
SUB-3070	Prepare & Submit Special Coating Samples	81	15-Oct-24	11-Feb-25
SUB-3080	Prepare & Submit Special Coating Product Data	81	15-Oct-24	11-Feb-25
APP-3070	Review & Approve Special Coating Samples	21	12-Feb-25	04-Mar-25
APP-3080	Review & Approve Special Coating Product Data	21	12-Feb-25	04-Mar-25
Spec Section - 09860 Grafiti Resistant Coatings		95	15-Oct-24	04-Mar-25
SUB-3060	Prepare & Submit Graffiti Resistant Coating Product Data	81	15-Oct-24	11-Feb-25
APP-3060	Review & Approve Graffiti Resistant Coating Product Data	21	12-Feb-25	04-Mar-25
Spec Section 09900 - Painting		95	15-Oct-24	04-Mar-25
SUB-1090	Prepare & Submit Painting	81	15-Oct-24	11-Feb-25
APP-1420	Review & Approve Painting	21	12-Feb-25	04-Mar-25
Division 10 - Specialties		95	15-Oct-24	04-Mar-25

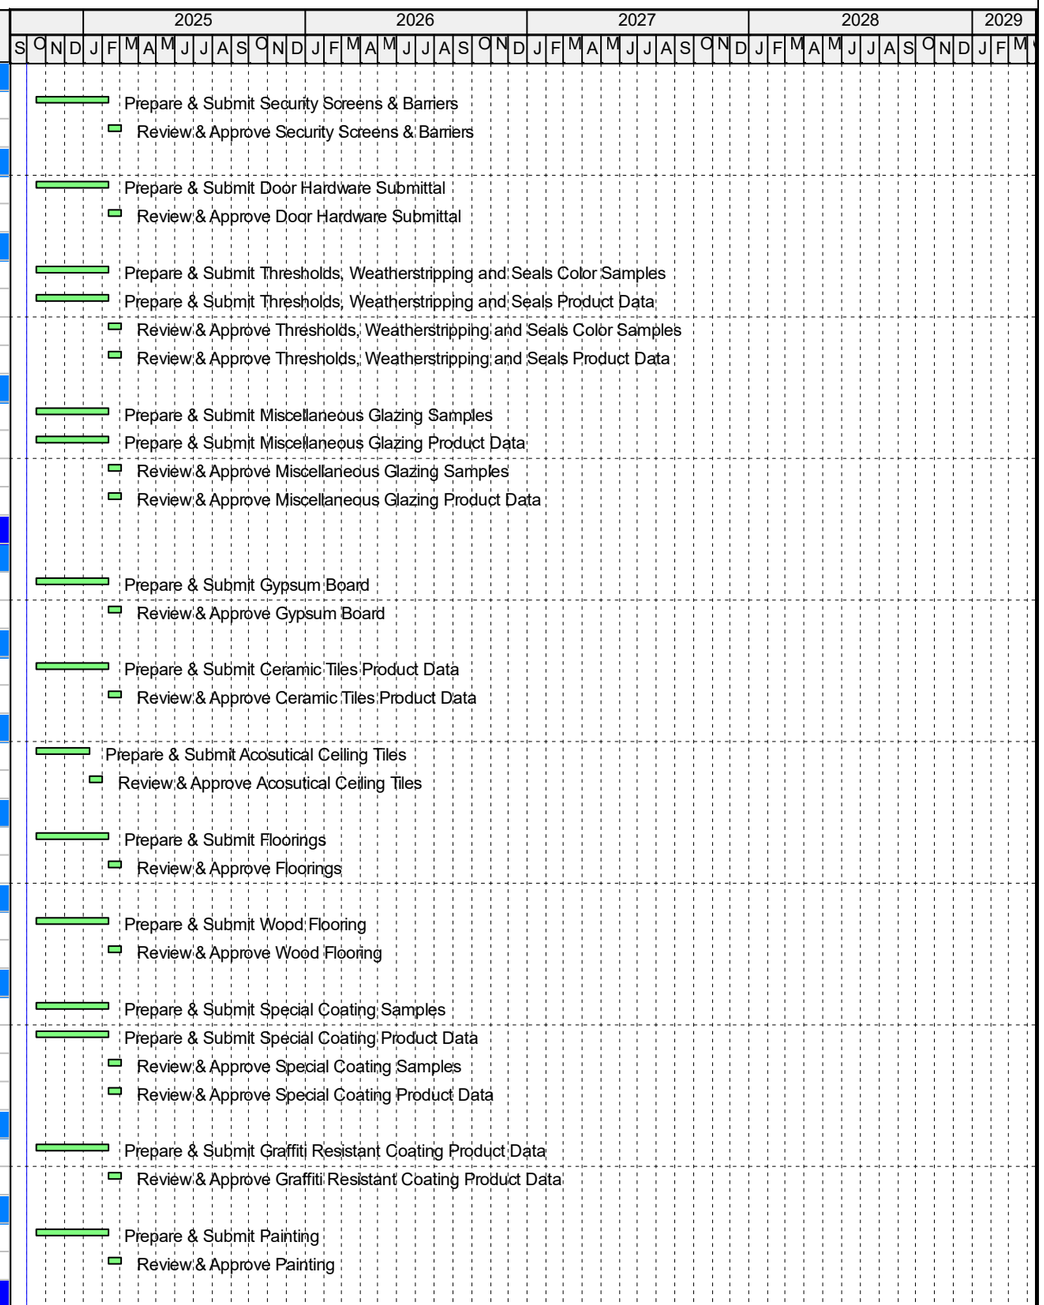

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
Spec Section 10100 - Visual Display Boards		95	15-Oct-24	04-Mar-25
SUB-2020	Prepare & Submit Visual Display Boards	81	15-Oct-24	11-Feb-25
APP-2020	Review & Approve Visual Display Boards	21	12-Feb-25	04-Mar-25
Spec Section - 10350 Flagpole		95	15-Oct-24	04-Mar-25
SUB-3090	Prepare & Submit Flagpole Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3100	Prepare & Submit Flagpole Product Data	81	15-Oct-24	11-Feb-25
APP-3090	Review & Approve Flagpole Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3100	Review & Approve Flagpole Product Data	21	12-Feb-25	04-Mar-25
Spec Section 10400 - Identification Devices		95	15-Oct-24	04-Mar-25
SUB-1060	Prepare & Submit Interior Signage Shop Drawings	81	15-Oct-24	11-Feb-25
APP-1390	Review & Approve Interior Signage Shop Drawings	21	12-Feb-25	04-Mar-25
Spec Section - 10415 Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases		95	15-Oct-24	04-Mar-25
SUB-3110	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals	81	15-Oct-24	11-Feb-25
SUB-3120	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-3130	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	81	15-Oct-24	11-Feb-25
APP-3110	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals	21	12-Feb-25	04-Mar-25
APP-3120	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	21	12-Feb-25	04-Mar-25
APP-3130	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	21	12-Feb-25	04-Mar-25
Spec Section 10505 - Metal Lockers		95	15-Oct-24	04-Mar-25
SUB-2030	Prepare & Submit Metal Lockers	81	15-Oct-24	11-Feb-25
APP-2030	Review & Approve Metal Lockers	21	12-Feb-25	04-Mar-25
Spec Section 10522 - Fire Extinguishers & Cabinets		95	15-Oct-24	04-Mar-25
SUB-2040	Prepare & Submit Fire Extinguishers & Cabinets	81	15-Oct-24	11-Feb-25
APP-2040	Review & Approve Fire Extinguishers & Cabinets	21	12-Feb-25	04-Mar-25
Spec Section - 10605 Wire Mesh Work		95	15-Oct-24	04-Mar-25
SUB-3140	Prepare & Submit Wire Mesh Work Samples	81	15-Oct-24	11-Feb-25
SUB-3150	Prepare & Submit Wire Mesh Work Shop drawings	81	15-Oct-24	11-Feb-25
APP-3140	Review & Approve Wire Mesh Work Samples	21	12-Feb-25	04-Mar-25
APP-3150	Review & Approve Miscellaneous Glazing Shop drawings	21	12-Feb-25	04-Mar-25
Spec Section - 10675 Metal Storage Shelving		95	15-Oct-24	04-Mar-25
SUB-3160	Prepare & Submit Metal Storage Shelving Samples	81	15-Oct-24	11-Feb-25
SUB-3170	Prepare & Submit Metal Storage Shelving Shop drawings	81	15-Oct-24	11-Feb-25
APP-3160	Review & Approve Metal Storage Shelving Samples	21	12-Feb-25	04-Mar-25
APP-3170	Review & Approve Metal Storage Shelving Shop drawings	21	12-Feb-25	04-Mar-25
Spec Section 10720 - Window Guards		87	15-Oct-24	20-Feb-25
SUB-2050	Prepare & Submit Stationary Metal Wall Louvers	73	15-Oct-24	30-Jan-25
APP-1320	Review & Approve Stationary Metal Wall Louvers	21	31-Jan-25	20-Feb-25
Spec Section 10810 - Toilet & Bath Accessories		95	15-Oct-24	04-Mar-25
SUB-1500	Prepare & Submit Toilet Accessories	81	15-Oct-24	11-Feb-25
APP-1700	Review & Approve Toilet Accessories	21	12-Feb-25	04-Mar-25
Spec Section - 10830 Mirrors		95	15-Oct-24	04-Mar-25
SUB-3180	Prepare & Submit Mirrors Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3190	Prepare & Submit Mirrors Product Data	81	15-Oct-24	11-Feb-25
SUB-3200	Prepare & Submit Mirrors Mastic Compatibility Test Reports & Certifications	81	15-Oct-24	11-Feb-25

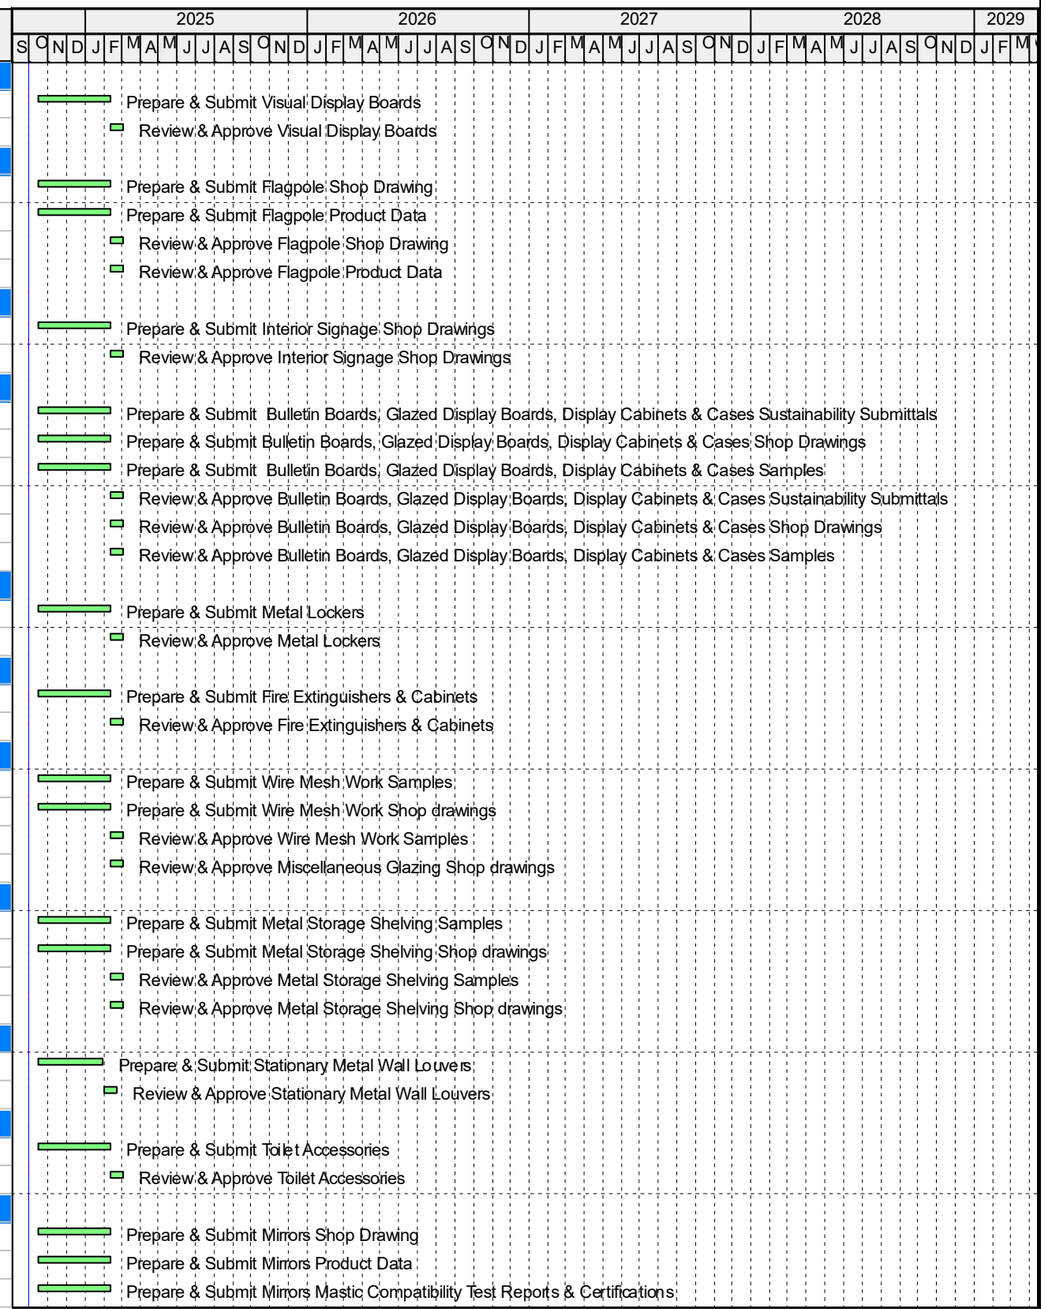

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
APP-3180	Review & Approve Mirrors Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3190	Review & Approve Mirrors Product Data	21	12-Feb-25	04-Mar-25
APP-3200	Review & Approve Mirrors Mastic Compatibility Test Reports & Certifications	21	12-Feb-25	04-Mar-25
Spec Section - 10840 Grab Bars		95	15-Oct-24	04-Mar-25
SUB-3210	Prepare & Submit Grab Bars Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3220	Prepare & Submit Grab Bars Product Data	81	15-Oct-24	11-Feb-25
APP-3210	Review & Approve Grab Bars Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3220	Review & Approve Grab Bars Product Data	21	12-Feb-25	04-Mar-25
Division 11 - Equipment		95	15-Oct-24	04-Mar-25
Spec Section 11050 - Library Equipment		95	15-Oct-24	04-Mar-25
SUB-2060	Prepare & Submit Library Equipment	81	15-Oct-24	11-Feb-25
APP-2050	Review & Approve Library Equipment	21	12-Feb-25	04-Mar-25
Spec Section 11061 - Platform Curtains & Auditorium Window Curtains		95	15-Oct-24	04-Mar-25
SUB-2070	Prepare & Submit Platform Curtains & Auditorium Window Curtains	81	15-Oct-24	11-Feb-25
APP-2060	Review & Approve Platform Curtains & Auditorium Window Curtains	21	12-Feb-25	04-Mar-25
Spec Section 11172 - Waste Handling Equipment		95	15-Oct-24	04-Mar-25
SUB-2080	Prepare & Submit Waste Handling Equipment	81	15-Oct-24	11-Feb-25
APP-2070	Review & Approve Waste Handling Equipment	21	12-Feb-25	04-Mar-25
Spec Section 11400 - Food Service Equipment		86	15-Oct-24	18-Feb-25
SUB-1650	Prepare & Submit Kitchen Equipment	71	15-Oct-24	28-Jan-25
APP-1780	Review & Approve Kitchen Equipment	21	29-Jan-25	18-Feb-25
Spec Section 11450 - Domestic Type Equipment		95	15-Oct-24	04-Mar-25
SUB-2090	Prepare & Submit Domestic Equipment	81	15-Oct-24	11-Feb-25
APP-2080	Review & Approve Domestic Equipment	21	12-Feb-25	04-Mar-25
Spec Section 11480 - Gymnasium Equipment		95	15-Oct-24	04-Mar-25
SUB-1770	Prepare & Submit Gymnasium Equipment	81	15-Oct-24	11-Feb-25
APP-1840	Review & Approve Gymnasium Equipment	21	12-Feb-25	04-Mar-25
Spec Section - 11500 Shop Equipment		95	15-Oct-24	04-Mar-25
SUB-3230	Prepare & Submit Shop Equipment Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3240	Prepare & Submit Shop Equipment Product Data	81	15-Oct-24	11-Feb-25
APP-3230	Review & Approve Shop Equipment Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3240	Review & Approve Shop Equipment Product Data	21	12-Feb-25	04-Mar-25
Spec Section 11600 - Laboratory Equipement		95	15-Oct-24	04-Mar-25
SUB-2100	Prepare & Submit Laboratory Equipment	81	15-Oct-24	11-Feb-25
APP-2090	Review & Approve Laboratory Equipment	21	12-Feb-25	04-Mar-25
Division 12 - Furnishings		95	15-Oct-24	04-Mar-25
Spec Section 12302 - Manufactured Wood Casework		95	15-Oct-24	04-Mar-25
SUB-2110	Prepare & Submit Manufactured Wood Casework	81	15-Oct-24	11-Feb-25
APP-2100	Review & Approve Manufactured Wood Casework	21	12-Feb-25	04-Mar-25
Spec Section - 12761 Bleachers		95	15-Oct-24	04-Mar-25
SUB-3250	Prepare & Submit Bleachers Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3260	Prepare & Submit Bleachers Product Data	81	15-Oct-24	11-Feb-25
SUB-3270	Prepare & Submit Bleachers Manufacturer's Warranty	81	15-Oct-24	11-Feb-25
APP-3250	Review & Approve Bleachers Shop Drawing	21	12-Feb-25	04-Mar-25

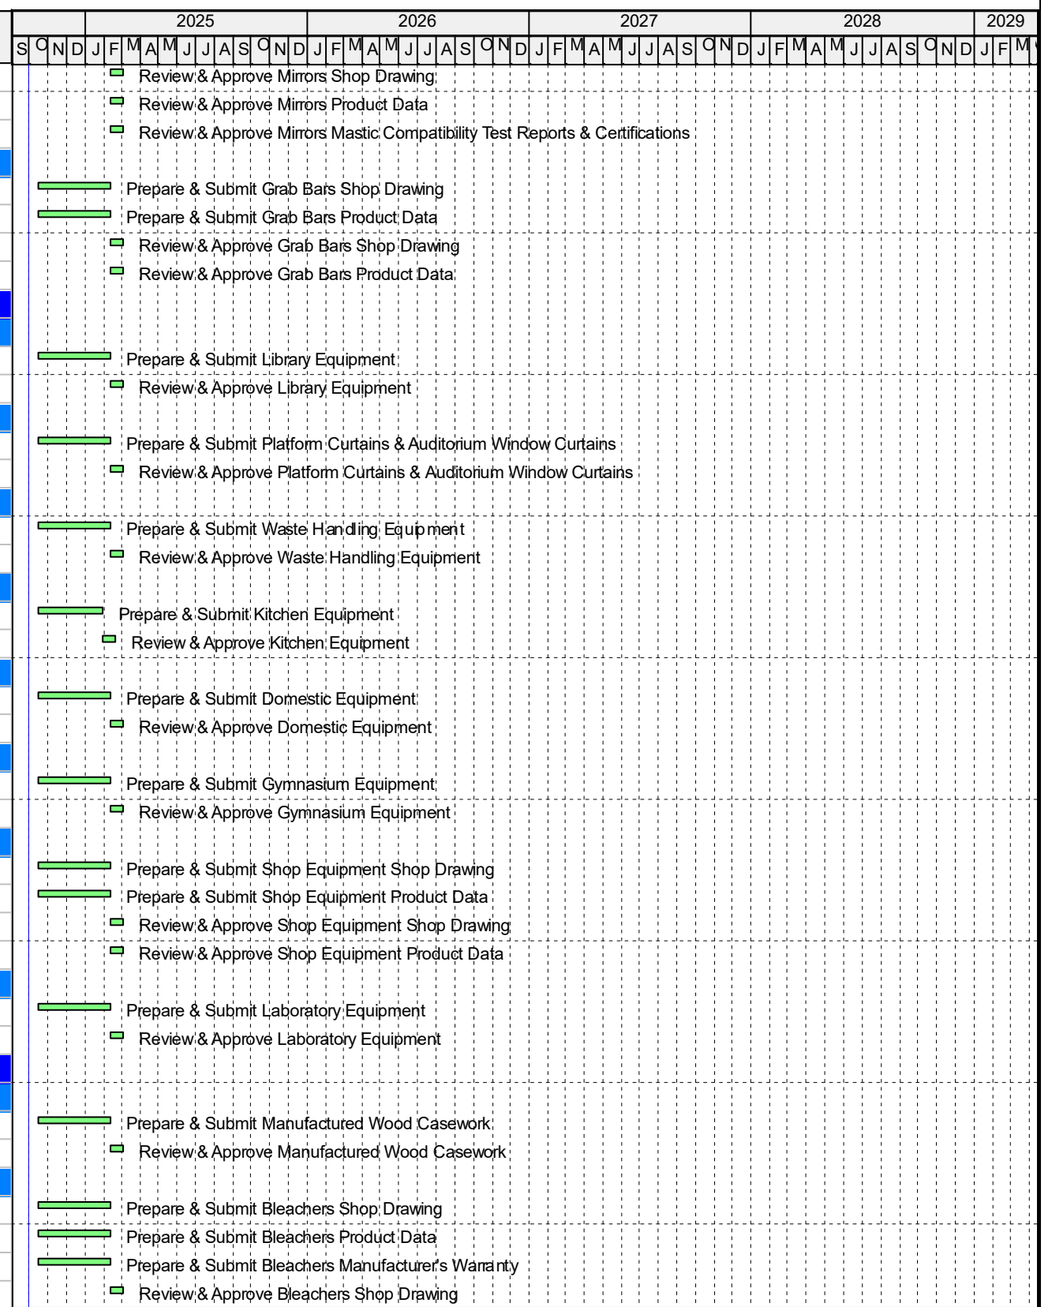

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
APP-3260	Review & Approve Bleachers Product Data	21	12-Feb-25	04-Mar-25
APP-3270	Review & Approve Bleachers Manufacturer's Warranty	21	12-Feb-25	04-Mar-25
Division 13 - Special Construction		95	15-Oct-24	04-Mar-25
Spec Section 13487 - Concrete Floating Floor Assembly		95	15-Oct-24	04-Mar-25
SUB-2120	Prepare & Submit Concrete Floating Floor Assembly	81	15-Oct-24	11-Feb-25
APP-2110	Review & Approve Concrete Floating Floor Assembly	21	12-Feb-25	04-Mar-25
Division 14 - Conveying Systems		95	15-Oct-24	04-Mar-25
Spec Section 14211 - Geared Traction Passenger Elevators		86	15-Oct-24	18-Feb-25
SUB-1460	Prepare & Submit Elevator Machine	71	15-Oct-24	28-Jan-25
APP-1210	Review & Approve Elevator Machine	21	29-Jan-25	18-Feb-25
Spec Section 14420 - Hydraulic Vertical Wheelchair Lifts		95	15-Oct-24	04-Mar-25
SUB-2130	Prepare & Submit Hydraulic Vertical Wheelchair Lifts	81	15-Oct-24	11-Feb-25
APP-2120	Review & Approve Hydraulic Vertical Wheelchair Lifts	21	12-Feb-25	04-Mar-25
Division 15A - Fire Protection		95	15-Oct-24	04-Mar-25
Spec Section 15330 - Sprinkler System		95	15-Oct-24	04-Mar-25
SUB-1440	Prepare & Submit Sprinkler System Shop Drawings	81	15-Oct-24	11-Feb-25
APP-1670	Review & Approve Sprinkler System Shop Drawings	21	12-Feb-25	04-Mar-25
Spec Section 15333 - Fire Pumps - Sprinkler Booster Pumps		95	15-Oct-24	04-Mar-25
SUB-1050	Prepare & Submit Fire & Jockey Pumps	81	15-Oct-24	11-Feb-25
SUB-1630	Prepare & Submit Fire Protection Shop Drawings	81	15-Oct-24	11-Feb-25
APP-1380	Review & Approve Fire & Jockey Pumps	21	12-Feb-25	04-Mar-25
APP-1760	Review & Approve Fire Protection Shop Drawings	21	12-Feb-25	04-Mar-25
Division 15B - Plumbing		95	15-Oct-24	04-Mar-25
Spec Section 15410 - Plumbing Piping		95	15-Oct-24	04-Mar-25
SUB-1430	Prepare & Submit Plumbing Shop Drawings	81	15-Oct-24	11-Feb-25
APP-1660	Review & Approve Plumbing Shop Drawings	21	12-Feb-25	04-Mar-25
Spec Section 15411 - Hangers and Supports		53	15-Oct-24	01-Jan-25
SUB-1040	Prepare & Submit Hangers & Supports	40	15-Oct-24	11-Dec-24
APP-1190	Review & Approve Hangers & Supports	21	12-Dec-24	01-Jan-25
Spec Section - 15412 Valves		95	15-Oct-24	04-Mar-25
SUB-3280	Prepare & Submit Valves Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3290	Prepare & Submit Valves Product Data	81	15-Oct-24	11-Feb-25
APP-3280	Review & Approve Valves Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3290	Review & Approve Valves Product Data	21	12-Feb-25	04-Mar-25
Spec Section - 15414 Tests		95	15-Oct-24	04-Mar-25
SUB-3300	Prepare & Submit Certification of Tests	81	15-Oct-24	11-Feb-25
SUB-3310	Prepare & Submit Domestic Water Sterilization Plan	81	15-Oct-24	11-Feb-25
APP-3300	Review & Approve Certification of Tests	21	12-Feb-25	04-Mar-25
APP-3310	Review & Approve Domestic Water Sterilization Plan	21	12-Feb-25	04-Mar-25
Spec Section 15415 - Drainage		53	15-Oct-24	01-Jan-25
SUB-1030	Prepare & Submit Floor Drains	40	15-Oct-24	11-Dec-24
APP-1180	Review & Approve Floor Drains	21	12-Dec-24	01-Jan-25
Spec Section 15416 - Gas Piping System		95	15-Oct-24	04-Mar-25
SUB-2170	Prepare & Submit Gas Pipes	81	15-Oct-24	11-Feb-25

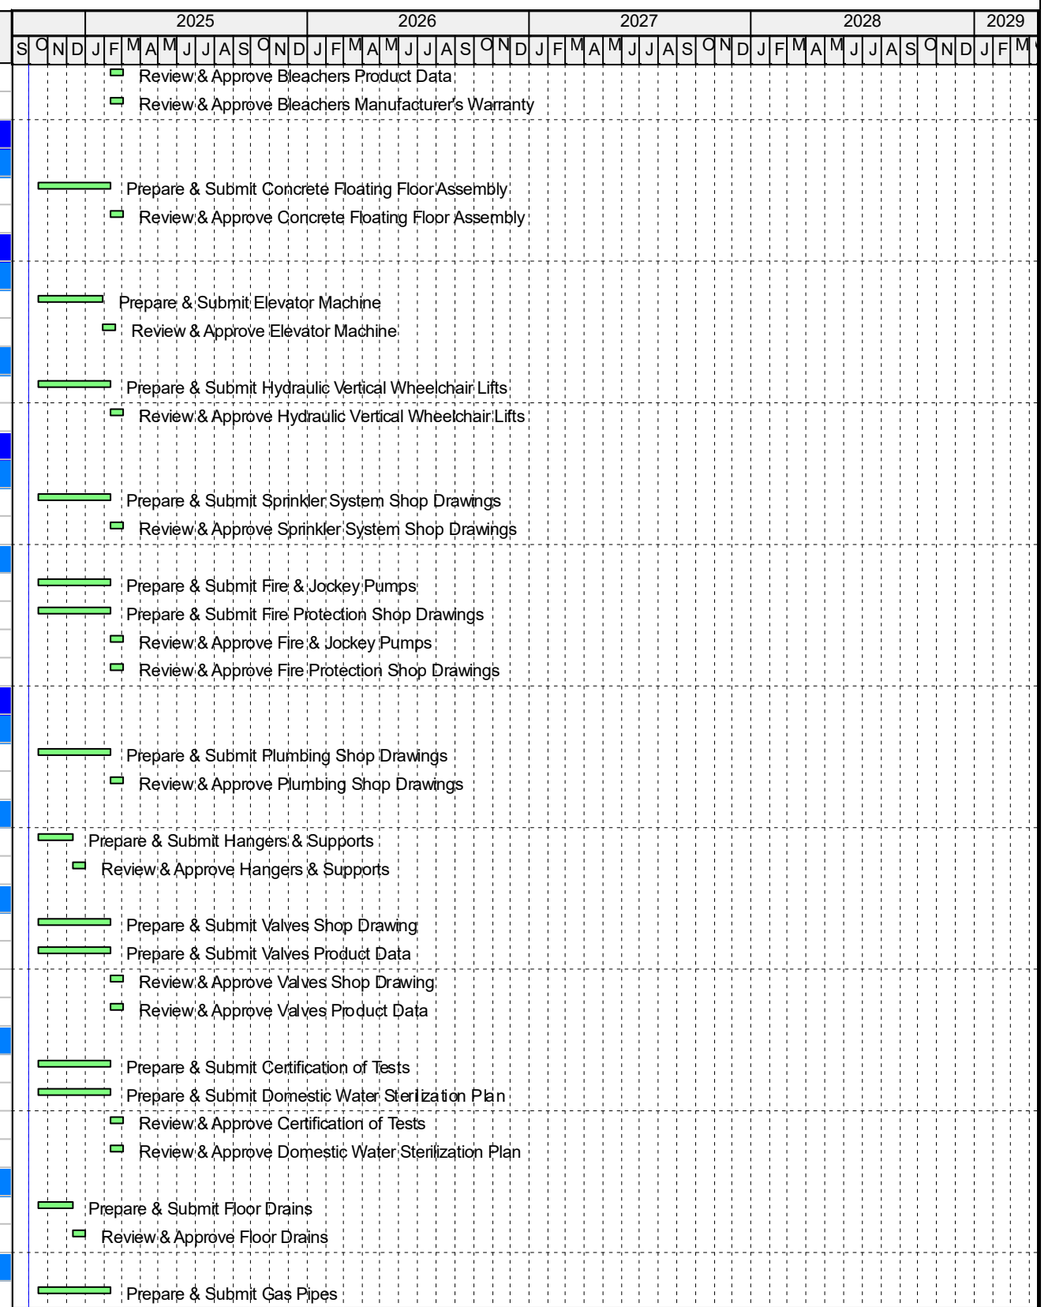

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
APP-2160	Review & Approve Gas Pipes	21	12-Feb-25	04-Mar-25
Spec Section 15417 - Cold Water Supply		53	15-Oct-24	01-Jan-25
SUB-1020	Prepare & Submit Pressure Gages	40	15-Oct-24	11-Dec-24
APP-1170	Review & Approve Pressure Gages	21	12-Dec-24	01-Jan-25
Spec Section 15418 - Hot Water Supply		53	15-Oct-24	01-Jan-25
SUB-1010	Prepare & Submit Thermometers	40	15-Oct-24	11-Dec-24
APP-1160	Review & Approve Thermometers	21	12-Dec-24	01-Jan-25
Spec Section - 15431 Tags, Charts, And Identification		95	15-Oct-24	04-Mar-25
SUB-3320	Prepare & Submit Tags, Charts & Identifications Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3330	Prepare & Submit Tags, Charts & Identifications Product Data	81	15-Oct-24	11-Feb-25
APP-3320	Review & Approve Tags, Charts & Identifications Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3330	Review & Approve Tags, Charts & Identifications Product Data	21	12-Feb-25	04-Mar-25
Spec Section - 15432 Miscellaneous		95	15-Oct-24	04-Mar-25
SUB-3340	Prepare & Submit Micselianeous Shop Drawing	81	15-Oct-24	11-Feb-25
APP-3340	Review & Approve Micselianeous Shop Drawing	21	12-Feb-25	04-Mar-25
Spec Section 15440 - Plumbing Fixtures		95	15-Oct-24	04-Mar-25
SUB-1600	Prepare & Submit Plumbing Fixtures	81	15-Oct-24	11-Feb-25
APP-1740	Review & Approve Plumbing Fixtures	21	12-Feb-25	04-Mar-25
Spec Section 15451 - Water Heaters		95	15-Oct-24	04-Mar-25
SUB-2180	Prepare & Submit Water Heaters	81	15-Oct-24	11-Feb-25
APP-2170	Review & Approve Water Heaters	21	12-Feb-25	04-Mar-25
Spec Section 15453 - Pumping Apparatus & Tanks		95	15-Oct-24	04-Mar-25
SUB-2190	Prepare & Submit Pumping Apparatus & Tanks	81	15-Oct-24	11-Feb-25
APP-2180	Review & Approve Pumping Apparatus & Tanks	21	12-Feb-25	04-Mar-25
Division 15C - Mechanical		95	15-Oct-24	04-Mar-25
Spec Section 15510 - HVAC Piping		74	15-Oct-24	31-Jan-25
SUB-1550	Prepare & Submit Mechanical Piping	60	15-Oct-24	10-Jan-25
APP-1280	Review & Approve Mechanical Piping	21	11-Jan-25	31-Jan-25
Spec Section - 15511 Valves (Hvac)		95	15-Oct-24	04-Mar-25
SUB-3350	Prepare & Submit Valves (HVAC) Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3360	Prepare & Submit Valves (HVAC) Product Data	81	15-Oct-24	11-Feb-25
APP-3350	Review & Approve Valves (HVAC) Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3360	Review & Approve Valves (HVAC) Product Data	21	12-Feb-25	04-Mar-25
Spec Section - 15512 Piping Insulation (Hvac)		95	15-Oct-24	04-Mar-25
SUB-3370	Prepare & Submit Piping Insulation Schedule Listing Items	81	15-Oct-24	11-Feb-25
APP-3370	Review & Approve Piping Insulation Schedule Listing Items	21	12-Feb-25	04-Mar-25
Spec Section - 15513 Equipment Insulation (Hvac)		95	15-Oct-24	04-Mar-25
SUB-3380	Prepare & Submit Schedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	81	15-Oct-24	11-Feb-25
APP-3380	Review & Approve chedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	21	12-Feb-25	04-Mar-25
Spec Section - 15514 Ductwork Insulation		95	15-Oct-24	04-Mar-25
SUB-3390	Prepare & Submit Schedules Showing Manfacturers's Product Number Duct Work Insulation	81	15-Oct-24	11-Feb-25
APP-3390	Review & Approve chedules Showing Manfacturers's Product Number Duct Work Insulation	21	12-Feb-25	04-Mar-25
Spec Section - 15515 Hydronic Specialties		95	15-Oct-24	04-Mar-25
SUB-3400	Prepare & Submit Hydronic Specialities Shop Drawing	81	15-Oct-24	11-Feb-25

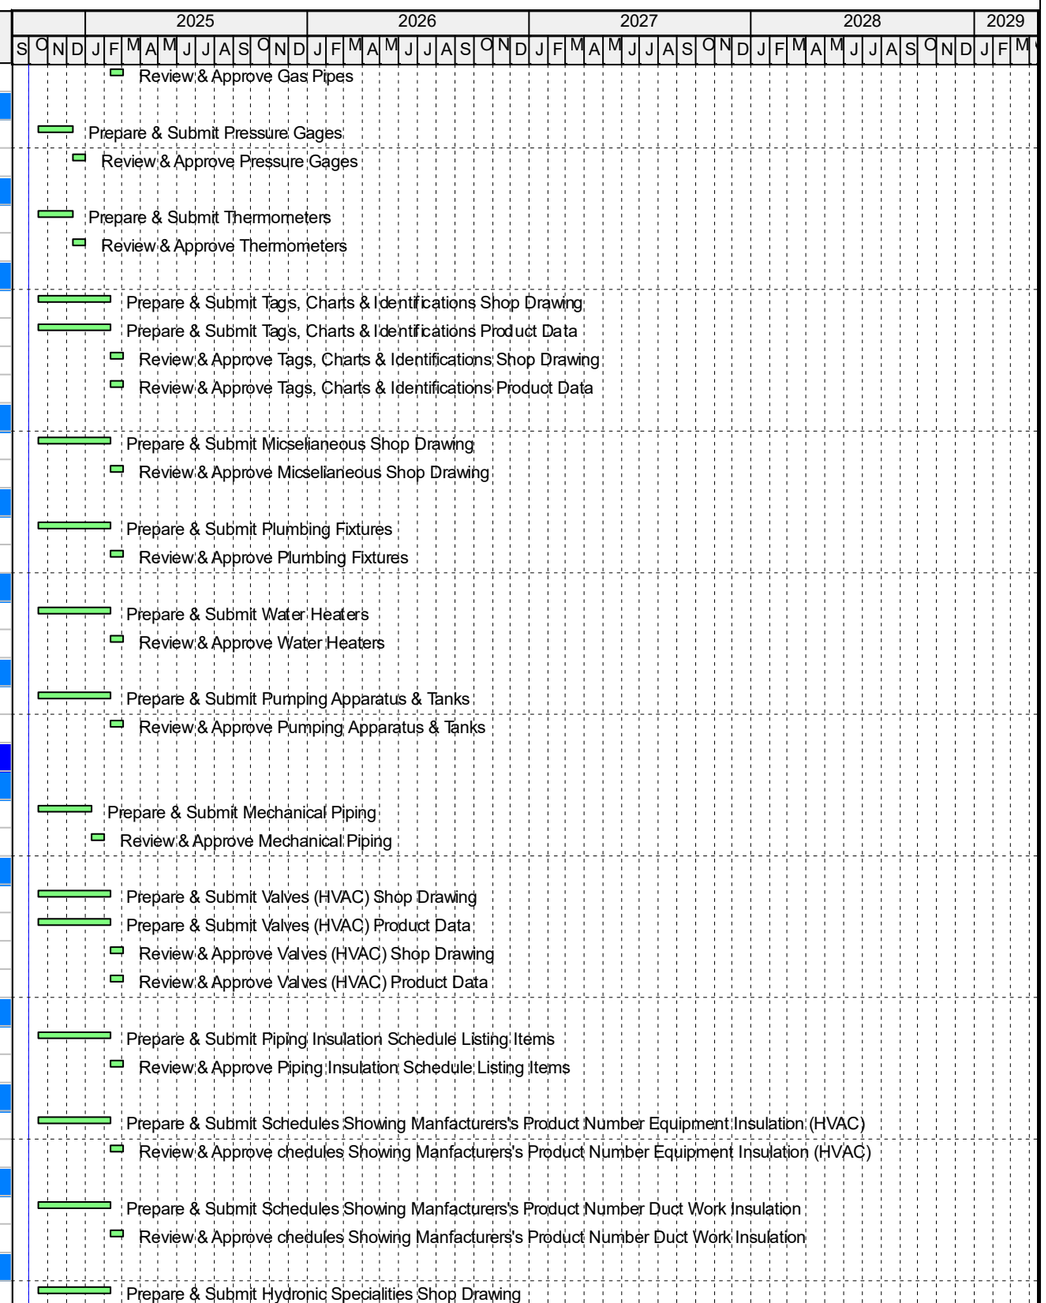

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

New Building PS/IS 341Q - Baseline Schedule Rev 01

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-3410	Prepare & Submit Hydronic Specialities Product Data	81	15-Oct-24	11-Feb-25
APP-3400	Review & Approve Hydronic Specialities Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3410	Review & Approve Hydronic Specialities Product Data	21	12-Feb-25	04-Mar-25
Spec Section - 15517 Water Treatment For Hydronic Systems		95	15-Oct-24	04-Mar-25
SUB-3420	Prepare & Submit Water Treatment Firm	81	15-Oct-24	11-Feb-25
SUB-3430	Prepare & Submit Chemical Products Product Data	81	15-Oct-24	11-Feb-25
APP-3420	Review & Approve Water Treatment Firm	21	12-Feb-25	04-Mar-25
APP-3430	Review & Approve Chemical Products Product Data	21	12-Feb-25	04-Mar-25
Spec Section 15660 - Packaged Modular Outdoor Chillers		86	15-Oct-24	18-Feb-25
SUB-1710	Prepare & Submit Chillers Product Data	71	15-Oct-24	28-Jan-25
APP-1820	Review & Approve Chillers Product Data	21	29-Jan-25	18-Feb-25
Spec Section 15565 - Hot Water Condensing Boilers		86	15-Oct-24	18-Feb-25
SUB-1730	Prepare & Submit Boilers	71	15-Oct-24	28-Jan-25
APP-1830	Review & Approve Boilers	21	29-Jan-25	18-Feb-25
Spec Section - 15570 Boiler Accessories		86	15-Oct-24	18-Feb-25
SUB-3440	Prepare & Submit Detail of Gag for the Safety Relief Valves	71	15-Oct-24	28-Jan-25
SUB-3450	Prepare & Submit Boiler Accessories Maintenance Data	71	15-Oct-24	28-Jan-25
APP-3440	Review & Approve Detail of Gag for the Safety Relief Valves	21	29-Jan-25	18-Feb-25
APP-3450	Review & Approve Boiler Accessories Maintenance Data	21	29-Jan-25	18-Feb-25
Spec Section - 15575 Breeching Chimney Connectors And Chimneys		95	15-Oct-24	04-Mar-25
SUB-3460	Prepare & Submit Breeching Chimney Connectors and Chimneys Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3470	Prepare & Submit Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	81	15-Oct-24	11-Feb-25
APP-3460	Review & Approve Breeching Chimney Connectors and Chimneys Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3470	Review & Approve Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	21	12-Feb-25	04-Mar-25
Spec Section - 15670 Plate Heat Exchangers		95	15-Oct-24	04-Mar-25
SUB-3480	Prepare & Submit Plate Heat Exchanger Maintenance Data	81	15-Oct-24	11-Feb-25
SUB-3490	Prepare & Submit Plate Heat Exchanger Product Data	81	15-Oct-24	11-Feb-25
APP-3480	Review & Approve Plate Heat Exchanger Maintenance Data	21	12-Feb-25	04-Mar-25
APP-3490	Review & Approve Plate Heat Exchanger Product Data	21	12-Feb-25	04-Mar-25
Spec Section 15783 - Split Heat Pump System		74	15-Oct-24	31-Jan-25
SUB-1000	Prepare & Submit Split Heat Pump System - SUB	60	15-Oct-24	10-Jan-25
APP-1250	Review & Approve Split Heat Pump System - SUB	21	11-Jan-25	31-Jan-25
Spec Section - 15792 Coils		95	15-Oct-24	04-Mar-25
SUB-3500	Prepare & Submit Coils Maintenance Data	81	15-Oct-24	11-Feb-25
SUB-3510	Prepare & Submit Coils Certifications	81	15-Oct-24	11-Feb-25
APP-3500	Review & Approve Coils Maintenance Data	21	12-Feb-25	04-Mar-25
APP-3510	Review & Approve Coils Certifications	21	12-Feb-25	04-Mar-25
Spec Section - 15835 Convectors		95	15-Oct-24	04-Mar-25
SUB-3520	Prepare & Submit Convectors Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3530	Prepare & Submit Convectors Product Data	81	15-Oct-24	11-Feb-25
APP-3520	Review & Approve Convectors Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3530	Review & Approve Convectors Product Data	21	12-Feb-25	04-Mar-25
Spec Section 15836 - Unit Heaters Cabinet Heaters		74	15-Oct-24	31-Jan-25
SUB-1760	Prepare & Submit Unit Cabinet Heaters	60	15-Oct-24	10-Jan-25

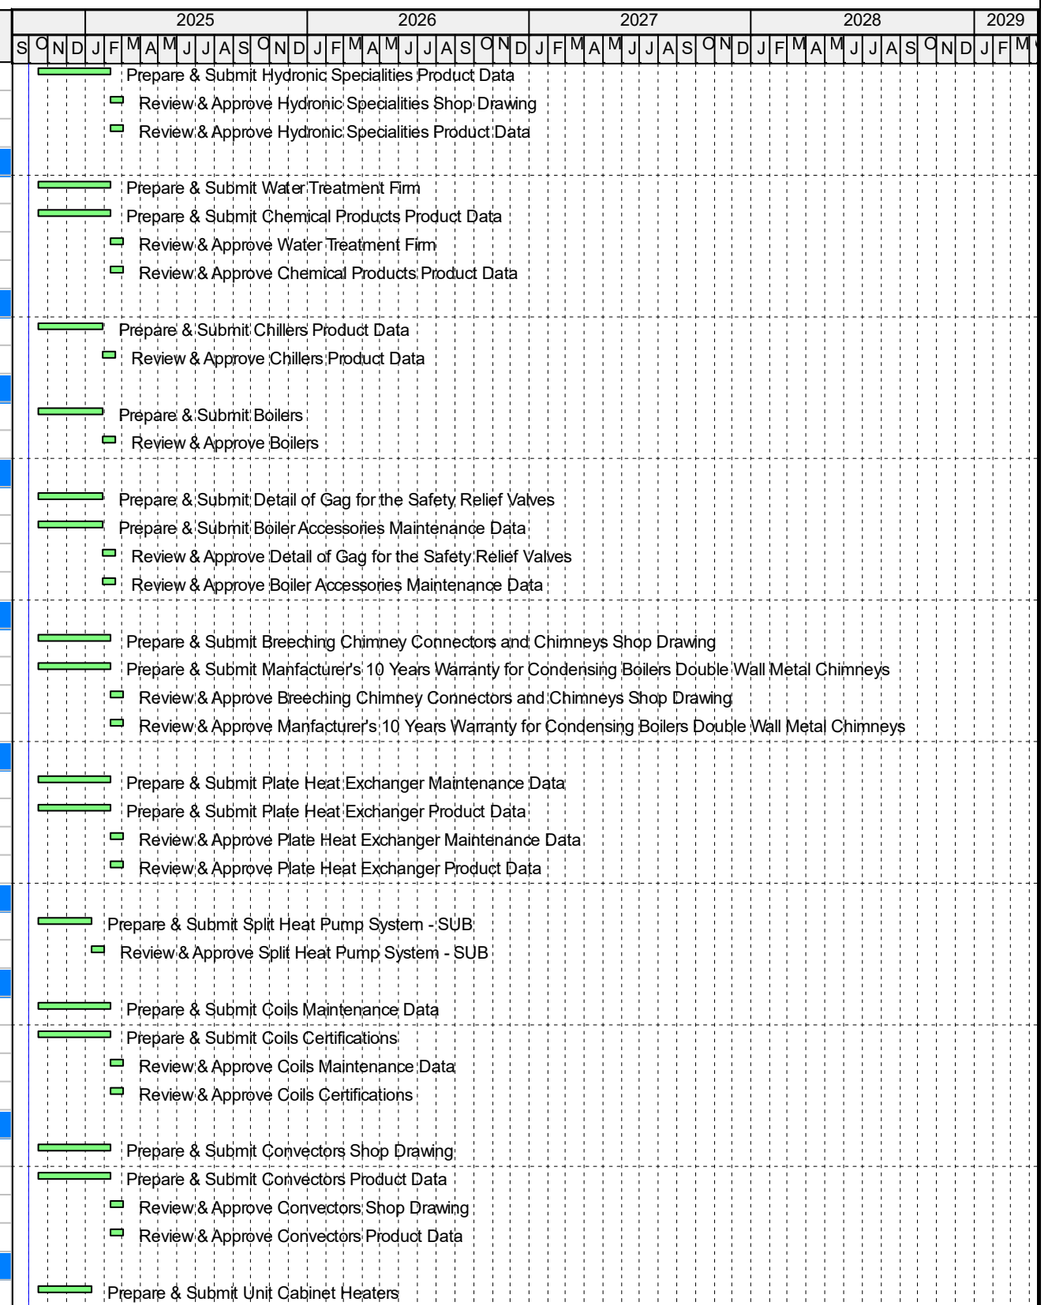

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1290	Review & Approve Unit Cabinet Heaters	21	11-Jan-25	31-Jan-25
Spec Section - 15838 Fan Coil Units		95	15-Oct-24	04-Mar-25
SUB-3540	Prepare & Submit Fan Coils Units Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3550	Prepare & Submit Fan Coils Units Shop Drawings	81	15-Oct-24	11-Feb-25
APP-3540	Review & Approve Fan Coils Units Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3550	Review & Approve Fan Coils Units Shop Drawings	21	12-Feb-25	04-Mar-25
Spec Section - 15839 Door Air Curtains		95	15-Oct-24	04-Mar-25
SUB-3560	Prepare & Submit Door Air Curtains Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3570	Prepare & Submit Door Air Curtains Product Data	81	15-Oct-24	11-Feb-25
APP-3560	Review & Approve Door Air Curtains Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3570	Review & Approve Door Air Curtains Product Data	21	12-Feb-25	04-Mar-25
Spec Section 15852 - Air Handling Units		86	15-Oct-24	18-Feb-25
SUB-1720	Prepare & Submit Air Handling Units Product Data	71	15-Oct-24	28-Jan-25
APP-1300	Review & Approve Air Handling Units Product Data	21	29-Jan-25	18-Feb-25
Spec Section - 15860 Centrifugal Fans		95	15-Oct-24	04-Mar-25
SUB-3580	Prepare & Submit Centrifugal Fans Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3590	Prepare & Submit Centrifugal Fans Product Data	81	15-Oct-24	11-Feb-25
SUB-3600	Prepare & Submit Centrifugal Fans Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
APP-3580	Review & Approve Centrifugal Fans Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3590	Review & Approve Centrifugal Fans Product Data	21	12-Feb-25	04-Mar-25
APP-3600	Review & Approve Centrifugal Fans Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
Spec Section - 15885 Air Filters		95	15-Oct-24	04-Mar-25
SUB-3610	Prepare & Submit Air Filters Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3620	Prepare & Submit Air Filters Product Data	81	15-Oct-24	11-Feb-25
SUB-3630	Prepare & Submit Air Filters Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
APP-3610	Review & Approve Air Filters Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3620	Review & Approve Air Filters Product Data	21	12-Feb-25	04-Mar-25
APP-3630	Review & Approve Air Filters Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
Spec Section 15891 - Metal Ductwork		95	15-Oct-24	04-Mar-25
SUB-1540	Prepare & Submit Mechanical Ducts	81	15-Oct-24	11-Feb-25
APP-1730	Review & Approve Mechanical Ducts	21	12-Feb-25	04-Mar-25
Spec Section 15540 - HVAC Pumps		95	15-Oct-24	04-Mar-25
SUB-2200	Prepare & Submit HVAC Pumps	81	15-Oct-24	11-Feb-25
APP-2190	Review & Approve HVAC Pumps	21	12-Feb-25	04-Mar-25
Spec Section 15590 - Emergency Generator System Accessories		86	15-Oct-24	18-Feb-25
SUB-2210	Prepare & Submit Emergency Generator System Accessories	71	15-Oct-24	28-Jan-25
APP-2200	Review & Approve Emergency Generator System Accessories	21	29-Jan-25	18-Feb-25
Spec Section - 15910 Duct Accessories		95	15-Oct-24	04-Mar-25
SUB-3640	Prepare & Submit Duct Accessories Shop Drawing	81	15-Oct-24	11-Feb-25
APP-3640	Review & Approve Duct Accessories Shop Drawing	21	12-Feb-25	04-Mar-25
Spec Section - 15915 Damper Assemblies		95	15-Oct-24	04-Mar-25
SUB-3650	Prepare & Submit Damper Assemblies Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3660	Prepare & Submit Damper Assemblies Product Data	81	15-Oct-24	11-Feb-25
SUB-3670	Prepare & Submit Damper Assemblies Maintenance Data & Materials	81	15-Oct-24	11-Feb-25

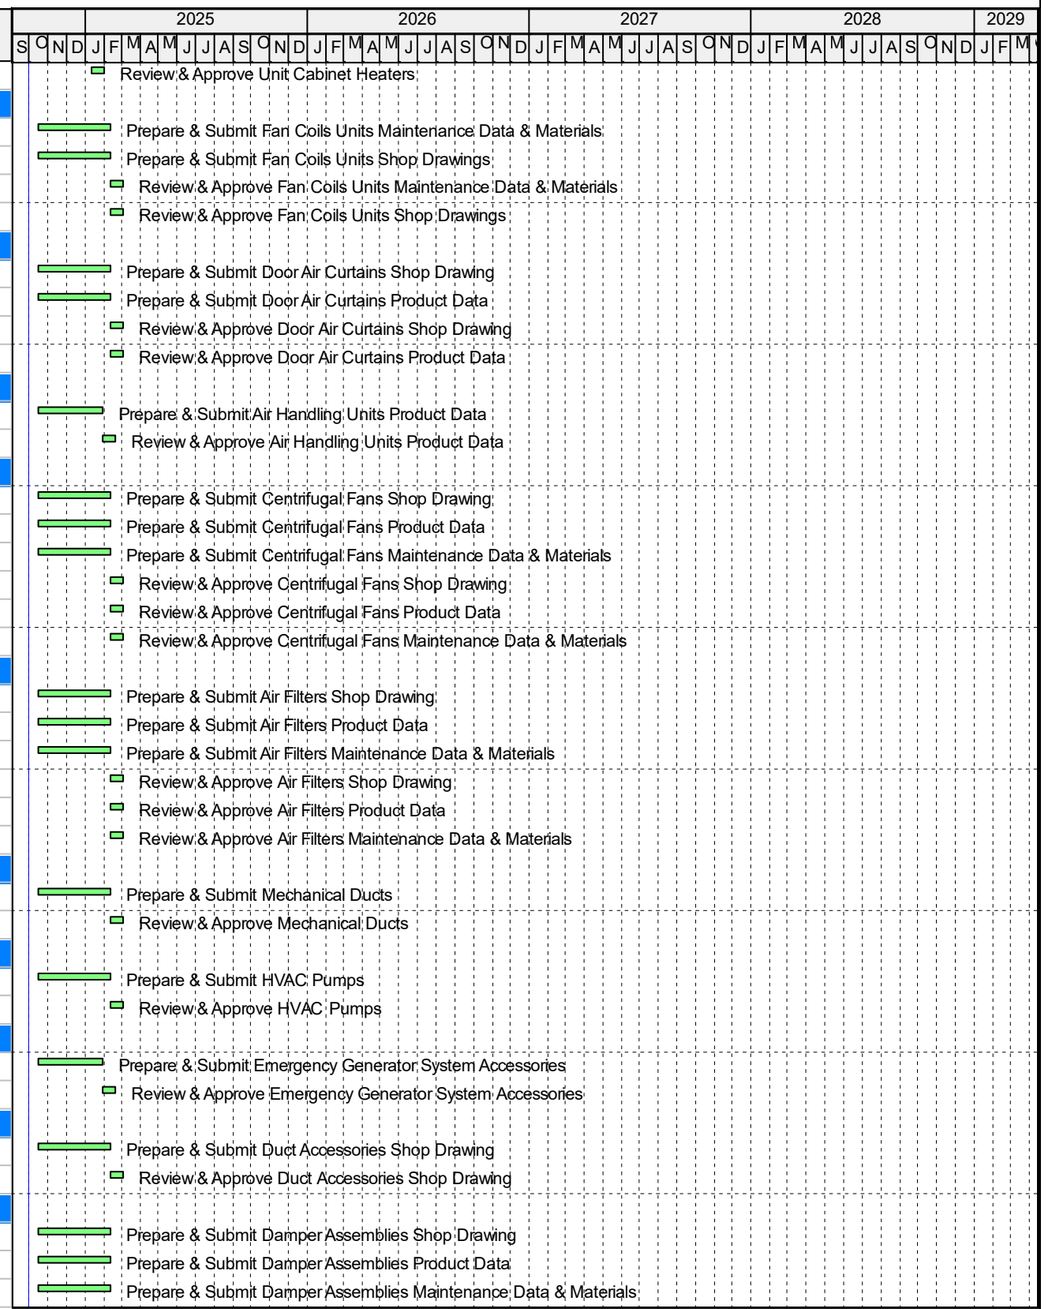

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
APP-3650	Review & Approve Damper Assemblies Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3660	Review & Approve Damper Assemblies Product Data	21	12-Feb-25	04-Mar-25
APP-3670	Review & Approve Damper Assemblies Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
Spec Section - 15930 Variable Air Terminals		95	15-Oct-24	04-Mar-25
SUB-3680	Prepare & Submit Variable Air Terminals Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3690	Prepare & Submit Variable Air Terminals Product Data	81	15-Oct-24	11-Feb-25
SUB-3700	Prepare & Submit Variable Air Terminals Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
APP-3680	Review & Approve Variable Air Terminals Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3690	Review & Approve Variable Air Terminals Product Data	21	12-Feb-25	04-Mar-25
APP-3700	Review & Approve Variable Air Terminals Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
Spec Section - 15935 Air Handling Units For Public Assembly Spaces		95	15-Oct-24	04-Mar-25
SUB-3710	Prepare & Submit AHU for Public Assemblies Sapces Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3720	Prepare & Submit AHU for Public Assemblies Sapces Product Data	81	15-Oct-24	11-Feb-25
SUB-3730	Prepare & Submit AHU for Public Assemblies Sapces Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
APP-3710	Review & Approve AHU for Public Assemblies Sapces Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3720	Review & Approve AHU for Public Assemblies Sapces Product Data	21	12-Feb-25	04-Mar-25
APP-3730	Review & Approve AHU for Public Assemblies Sapces Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
Spec Section 15940 - Air Outlets & Inlets		95	15-Oct-24	04-Mar-25
SUB-2260	Prepare & Submit Air Outlets & Inlets	81	15-Oct-24	11-Feb-25
APP-2250	Review & Approve Air Outlets & Inlets	21	12-Feb-25	04-Mar-25
Spec Section 15970 - Temperature Control System		95	15-Oct-24	04-Mar-25
SUB-2250	Prepare & Submit Temperature Control System	81	15-Oct-24	11-Feb-25
APP-2240	Review & Approve Temperature Control System	21	12-Feb-25	04-Mar-25
Spec Section - 15973 Facility Management Systems Integration		95	15-Oct-24	04-Mar-25
SUB-3740	Prepare & Submit Control Systems Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3750	Prepare & Submit Truck Network Cable Schematic Diagram	81	15-Oct-24	11-Feb-25
APP-3740	Review & Approve Control Systems Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3750	Review & Approve Truck Network Cable Schematic Diagram	21	12-Feb-25	04-Mar-25
Spec Section 15594 - Fuel Storage Equipment		95	15-Oct-24	04-Mar-25
SUB-2220	Prepare & Submit Fuel Storage Equipment	81	15-Oct-24	11-Feb-25
APP-2210	Review & Approve Fuel Storage Equipment	21	12-Feb-25	04-Mar-25
Spec Section 15596 - Natural Gas Leak Detection Equipment		95	15-Oct-24	04-Mar-25
SUB-2230	Prepare & Submit Natural Gas Leak Detection Equipment	81	15-Oct-24	11-Feb-25
APP-2220	Review & Approve Natural Gas Leak Detection Equipment	21	12-Feb-25	04-Mar-25
Division 16 - Electrical		95	15-Oct-24	04-Mar-25
Spec Section 16010 - Gen Provisions for Elec Work		95	15-Oct-24	04-Mar-25
SUB-1420	Prepare & Submit Electrical Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1590	Prepare & Submit Electrical Equipment, Conduits, and Cables	20	15-Oct-24	12-Nov-24
SUB-1750	Prepare & Submit Switch Gears Product Data	20	15-Oct-24	12-Nov-24
APP-1080	Review & Approve Electrical Equipment, Conduits, and Cables	21	13-Nov-24	03-Dec-24
APP-1090	Review & Approve Switch Gears Product Data	21	13-Nov-24	03-Dec-24
APP-1650	Review & Approve Electrical Shop Drawings	21	12-Feb-25	04-Mar-25
Spec Section 16120 - Wiring Systems		95	15-Oct-24	04-Mar-25
SUB-1680	Prepare & Submit Telecommunication System Drawings	81	15-Oct-24	11-Feb-25

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1800	Review & Approve Telecommunication System Drawings	21	12-Feb-25	04-Mar-25
Spec Section - 16145 Lighting Control Devices		86	15-Oct-24	18-Feb-25
SUB-3760	Prepare & Submit Lighting Control Devices Shop Drawing	71	15-Oct-24	28-Jan-25
SUB-3770	Prepare & Submit Lighting Control Devices Product Data	71	15-Oct-24	28-Jan-25
SUB-3780	Prepare & Submit Lighting Control Devices Warranty	71	15-Oct-24	28-Jan-25
APP-3760	Review & Approve Lighting Control Devices Shop Drawing	21	29-Jan-25	18-Feb-25
APP-3770	Review & Approve Lighting Control Devices Product Data	21	29-Jan-25	18-Feb-25
APP-3780	Review & Approve Lighting Control Devices Warranty	21	29-Jan-25	18-Feb-25
Spec Section 16231- Emergency Generator System		86	15-Oct-24	18-Feb-25
SUB-1740	Prepare & Submit Emergency Generator System Product Data	71	15-Oct-24	28-Jan-25
APP-1070	Review & Approve Emergency Generator System Product Data	21	29-Jan-25	18-Feb-25
Spec Section - 16289 Surge Protective Devices		95	15-Oct-24	04-Mar-25
SUB-3790	Prepare & Submit Surge Protective Devices Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3800	Prepare & Submit Surge Protective Devices Product Data	81	15-Oct-24	11-Feb-25
SUB-3810	Prepare & Submit Surge Protective Devices Warranty	81	15-Oct-24	11-Feb-25
APP-3790	Review & Approve Surge Protective Devices Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3800	Review & Approve Surge Protective Devices Product Data	21	12-Feb-25	04-Mar-25
APP-3810	Review & Approve Surge Protective Devices Warranty	21	12-Feb-25	04-Mar-25
Spec Section - 16420 Service Entrance Equipment		95	15-Oct-24	04-Mar-25
SUB-3820	Prepare & Submit Service Entrance Equipment Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3830	Prepare & Submit Service Entrance Equipment Product Data	81	15-Oct-24	11-Feb-25
SUB-3840	Prepare & Submit Service Entrance Equipment Warranty	81	15-Oct-24	11-Feb-25
APP-3820	Review & Approve Service Entrance Equipment Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3830	Review & Approve Service Entrance Equipment Product Data	21	12-Feb-25	04-Mar-25
APP-3840	Review & Approve Service Entrance Equipment Warranty	21	12-Feb-25	04-Mar-25
Spec Section 16425 - Switch Boards & Panel Boards		95	15-Oct-24	04-Mar-25
SUB-2140	Prepare & Submit Switch & Panel Boards	81	15-Oct-24	11-Feb-25
APP-2130	Review & Approve Switch & Panel Boards	21	12-Feb-25	04-Mar-25
Spec Section - 16441 Enclosed Switches		95	15-Oct-24	04-Mar-25
SUB-3850	Prepare & Submit Enclosed Switches Product Data	81	15-Oct-24	11-Feb-25
SUB-3860	Prepare & Submit Enclosed Switches Test Reports	81	15-Oct-24	11-Feb-25
APP-3850	Review & Approve Enclosed Switches Product Data	21	12-Feb-25	04-Mar-25
APP-3860	Review & Approve Enclosed Switches Test Reports	21	12-Feb-25	04-Mar-25
Spec Section 16471 - Auditorium & Television Studio Dimming System		95	15-Oct-24	04-Mar-25
SUB-2150	Prepare & Submit Auditorium & Television Studio Dimming System Product Data	81	15-Oct-24	11-Feb-25
APP-2140	Review & Approve Auditorium & Television Studio Dimming System Product Data	21	12-Feb-25	04-Mar-25
Spec Section 16475 - Overcurrent Protective Devices		95	15-Oct-24	04-Mar-25
SUB-2160	Prepare & Submit Overcurrent Protective Devices Data	81	15-Oct-24	11-Feb-25
APP-2150	Review & Approve Overcurrent Protective Devices Data	21	12-Feb-25	04-Mar-25
Spec Section - 16480 Motors, Motor Control Centers, Starters And Control Equipment		95	15-Oct-24	04-Mar-25
SUB-3870	Prepare & Submit Motors, Motor Control Centers and Starters Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3880	Prepare & Submit Motors, Motor Control Centers and Starters Product Data	81	15-Oct-24	11-Feb-25
SUB-3890	Prepare & Submit Motors, Motor Control Centers and Starters Field Test Reports	81	15-Oct-24	11-Feb-25
APP-3870	Review & Approve Motors, Motor Control Centers and Starters Shop Drawing	21	12-Feb-25	04-Mar-25

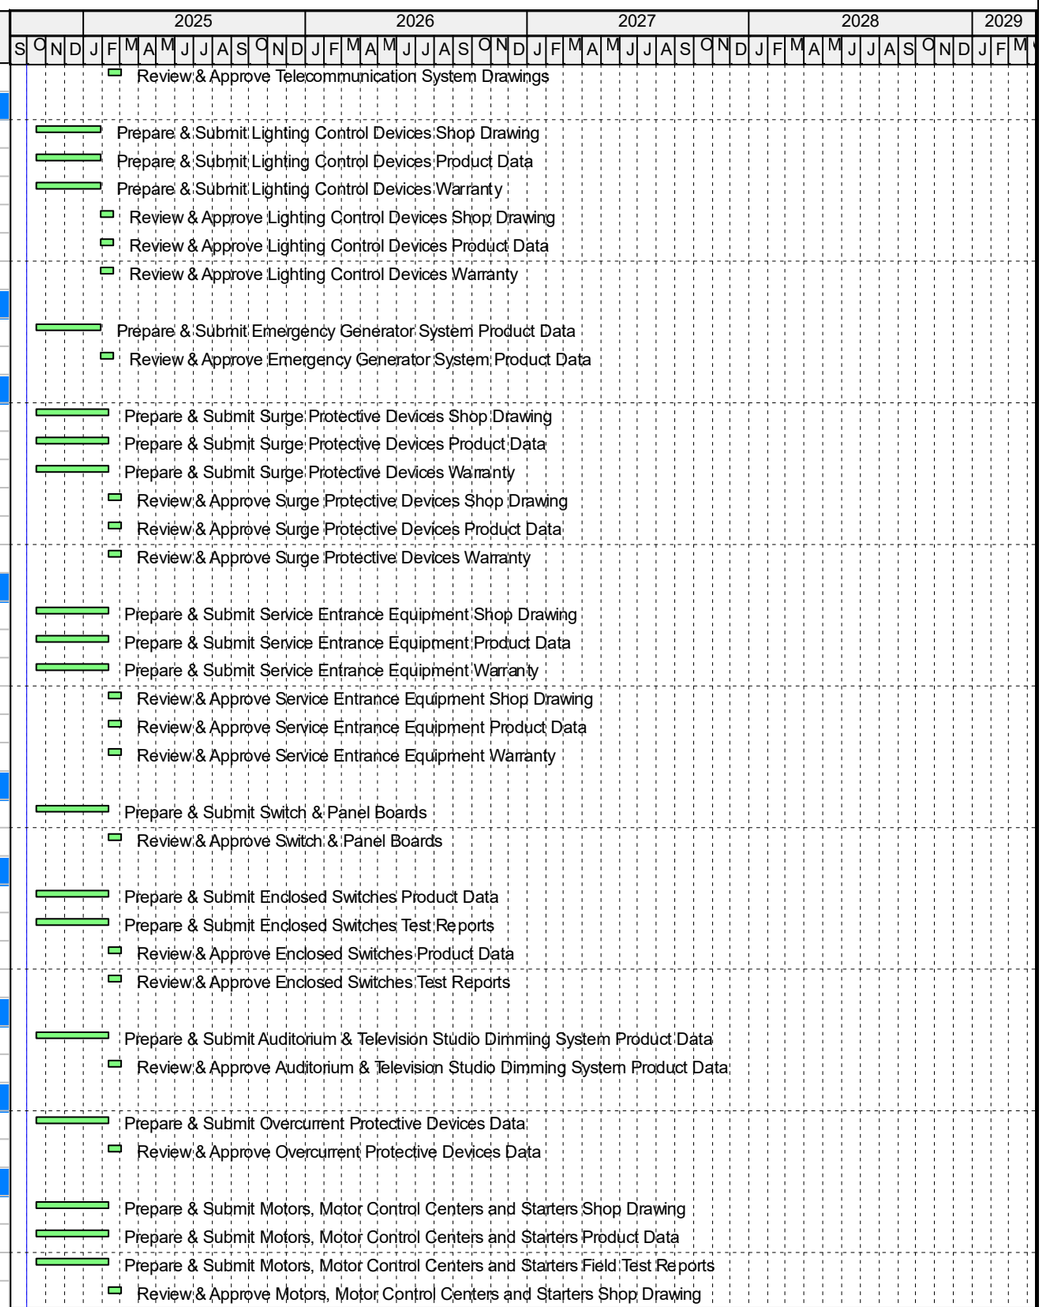

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
APP-3880	Review & Approve Motors, Motor Control Centers and Starters Product Data	21	12-Feb-25	04-Mar-25
APP-3890	Review & Approve Motors, Motor Control Centers and Starters Field Test Reports	21	12-Feb-25	04-Mar-25
Spec Section 16502 - Interior Lighting Fixtures		86	15-Oct-24	18-Feb-25
SUB-1520	Prepare & Submit Lighting Fixtures	71	15-Oct-24	28-Jan-25
APP-1120	Review & Approve Lighting Fixtures	21	29-Jan-25	18-Feb-25
Spec Section 16520 - Illuminated Exit Sign		95	15-Oct-24	04-Mar-25
SUB-1660	Prepare & Submit Signs	81	15-Oct-24	11-Feb-25
APP-1790	Review & Approve Signs	21	12-Feb-25	04-Mar-25
Spec Section 16720 - Fire Detection Alarm System with COC		95	15-Oct-24	04-Mar-25
SUB-1640	Prepare & Submit Fire Detectors & Alarms	81	15-Oct-24	11-Feb-25
APP-1770	Review & Approve Fire Detectors & Alarms	21	12-Feb-25	04-Mar-25
Spec Section - 16728 Fiber Optic Cabling System		95	15-Oct-24	04-Mar-25
SUB-3930	Prepare & Submit Fiber Optic Cabling system Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3940	Prepare & Submit Fiber Optic Cabling system Product Data	81	15-Oct-24	11-Feb-25
SUB-3950	Prepare & Submit Fiber Optic Cabling system Samples	81	15-Oct-24	11-Feb-25
APP-3930	Review & Approve Fiber Optic Cabling system Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3940	Review & Approve Fiber Optic Cabling system Product Data	21	12-Feb-25	04-Mar-25
APP-3950	Review & Approve Fiber Optic Cabling system Samples	21	12-Feb-25	04-Mar-25
Spec Section - 16770 Sound, Intercom & Teacher Activated Security System		95	15-Oct-24	04-Mar-25
SUB-3960	Prepare & Submit Sound, Intercome & Security System Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3970	Prepare & Submit Sound, Intercome & Security System Programming Code and Password for the System	81	15-Oct-24	11-Feb-25
SUB-3980	Prepare & Submit Sound, Intercome & Security System Warranty	81	15-Oct-24	11-Feb-25
APP-3960	Review & Approve Sound, Intercome & Security System Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3970	Review & Approve Sound, Intercome & Security System Programming Code and Password for the System	21	12-Feb-25	04-Mar-25
APP-3980	Review & Approve Sound, Intercome & Security System warranty	21	12-Feb-25	04-Mar-25
Spec Section - 16771 Projection And Interactive Whiteboard Systems		95	15-Oct-24	04-Mar-25
SUB-3990	Prepare & Submit Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	81	15-Oct-24	11-Feb-25
SUB-4000	Prepare & Submit Projection and Interactive Whiteboard Systems Wiring diagram	81	15-Oct-24	11-Feb-25
APP-3990	Review & Approve Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	21	12-Feb-25	04-Mar-25
APP-4000	Review & Approve Projection and Interactive Whiteboard Systems Wiring diagram	21	12-Feb-25	04-Mar-25
Spec Section 16785 - Internet Protocol Digital Video Surveillance System using Digital Cameras		95	15-Oct-24	04-Mar-25
SUB-1690	Prepare & Submit Internet Protocol Digital Video Surveillance System using Digital Cameras	71	15-Oct-24	28-Jan-25
APP-1220	Review & Approve Internet Protocol Digital Video Surveillance System using Digital Cameras	35	29-Jan-25	04-Mar-25
Spec Section - 16791 Self-Corrective Clock System		95	15-Oct-24	04-Mar-25
SUB-4010	Prepare & Submit Self Corrective Clock System Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-4020	Prepare & Submit Self Corrective Clock System Product Data	81	15-Oct-24	11-Feb-25
SUB-4030	Prepare & Submit Self Corrective Clock System Field Test Reports	81	15-Oct-24	11-Feb-25
APP-4010	Review & Approve Self Corrective Clock System Shop Drawing	21	12-Feb-25	04-Mar-25
APP-4020	Review & Approve Self Corrective Clock System Product Data	21	12-Feb-25	04-Mar-25
APP-4030	Review & Approve Self Corrective Clock System Field Test Reports	21	12-Feb-25	04-Mar-25
Spec Section - 16855 Heat Trace Cable System		95	15-Oct-24	04-Mar-25
SUB-4040	Prepare & Submit Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	81	15-Oct-24	11-Feb-25
APP-4040	Review & Approve Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	21	12-Feb-25	04-Mar-25
Fabrication & Delivery		475	02-Jun-25	19-Sep-26

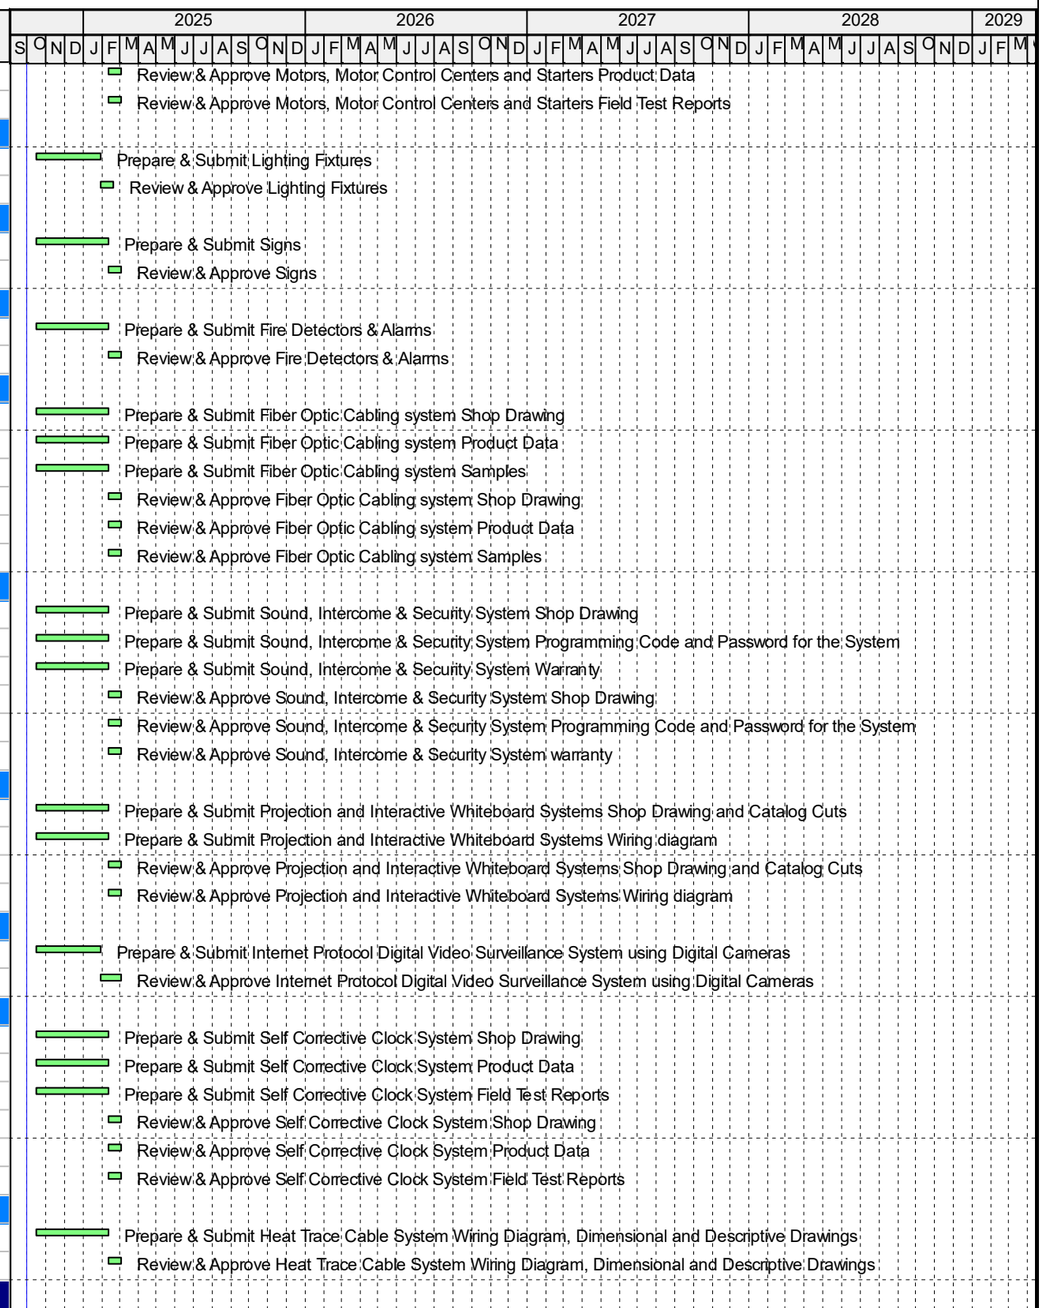

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
PRO-1590	Procure & Deliver Steel Columns	120	02-Jun-25	29-Sep-25
PRO-1120	Procure & Deliver Erosion Control and Sedimentation Devices	25	05-Sep-25	29-Sep-25
PRO-1420	Procure & Deliver Painting	70	30-Sep-25	08-Dec-25
PRO-1410	Procure & Deliver Door Frames	70	30-Sep-25	08-Dec-25
PRO-1200	Procure & Deliver Elevator Machine	112	30-Sep-25	19-Jan-26
PRO-1150	Procure & Deliver Gypsum Board	150	30-Sep-25	26-Feb-26
PRO-1160	Procure & Deliver Floorings	80	30-Sep-25	18-Dec-25
PRO-1170	Procure & Deliver Acosutical Ceiling Tiles	120	30-Sep-25	27-Jan-26
PRO-1190	Procure & Deliver Toilet Accessories	100	30-Sep-25	07-Jan-26
PRO-1000	Procure & Deliver Kitchen Equipment	180	30-Sep-25	28-Mar-26
PRO-1140	Procure & Deliver Lighting Fixtures	60	30-Sep-25	28-Nov-25
PRO-1010	Procure & Deliver Furnitures	130	30-Sep-25	06-Feb-26
PRO-1020	Procure & Deliver Mechanical Piping	70	30-Sep-25	08-Dec-25
PRO-1030	Procure & Deliver Mechanical Ducts	70	30-Sep-25	08-Dec-25
PRO-1050	Procure & Deliver Electrical Equipment	130	30-Sep-25	06-Feb-26
PRO-1060	Procure & Deliver Plumbing Fixtures	100	30-Sep-25	07-Jan-26
PRO-1070	Procure & Deliver Wood Doors	50	30-Sep-25	18-Nov-25
PRO-1090	Procure & Deliver Fire Sprinklers	100	30-Sep-25	07-Jan-26
PRO-1110	Procure & Deliver Fire Detectors & Alarms	60	30-Sep-25	28-Nov-25
PRO-1210	Procure & Deliver Signs	70	30-Sep-25	08-Dec-25
PRO-1220	Procure & Deliver Windows & Storefronts	154	30-Sep-25	02-Mar-26
PRO-1250	Procure & Deliver Plumbing Pipes	60	30-Sep-25	28-Nov-25
PRO-1260	Procure & Deliver Electrical Wires & Conduits	130	30-Sep-25	06-Feb-26
PRO-1270	Procure & Deliver Mechanical Pumps	70	30-Sep-25	08-Dec-25
PRO-1280	Procure & Deliver Fire Protection Pumps	70	30-Sep-25	08-Dec-25
PRO-1290	Procure & Deliver Plumbing Pumps	250	30-Sep-25	06-Jun-26
PRO-1310	Procure & Deliver Telecommunication System	60	30-Sep-25	28-Nov-25
PRO-1330	Procure & Deliver Cameras	60	30-Sep-25	28-Nov-25
PRO-1360	Procure & Deliver Metal Panel Ceilings	120	30-Sep-25	27-Jan-26
PRO-1380	Procure & Deliver Roof Dunnage	100	30-Sep-25	07-Jan-26
PRO-1470	Procure & Deliver Cabinet Heaters	126	30-Sep-25	02-Feb-26
PRO-1480	Procure & Deliver Chillers	170	30-Sep-25	18-Mar-26
PRO-1490	Procure & Deliver Air Handling Units	250	30-Sep-25	06-Jun-26
PRO-1500	Procure & Deliver Boilers	84	30-Sep-25	22-Dec-25
PRO-1510	Procure & Deliver Emergency Generator	290	30-Sep-25	16-Jul-26
PRO-1520	Procure & Deliver Switch Gears	250	30-Sep-25	06-Jun-26
PRO-1530	Procure & Deliver Hydraulic Vertical Wheelchair Lift	90	30-Sep-25	28-Dec-25
PRO-1560	Procure & Deliver Gymnasium Equipment	180	30-Sep-25	28-Mar-26
PRO-1570	Procure & Deliver Precast Sandwich Panels	112	30-Sep-25	19-Jan-26
PRO-1580	Procure & Deliver Metal Deck	70	30-Sep-25	08-Dec-25
PRO-1600	Procure & Deliver Trusses	60	30-Sep-25	28-Nov-25
PRO-1610	Procure & Deliver Prefabricated Expansion Joint Covers	60	30-Sep-25	28-Nov-25
PRO-1620	Procure & Deliver Security Screens & Barriers	60	30-Sep-25	28-Nov-25
PRO-1630	Procure & Deliver Wood Flooring	120	30-Sep-25	27-Jan-26

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
PRO-1640	Procure & Deliver Concrete Floating Floor Assembly	120	30-Sep-25	27-Jan-26
PRO-1660	Procure & Deliver Auditorium Television Studio Dimming System	90	30-Sep-25	28-Dec-25
PRO-2010	Procure & Deliver Steel Stairs Components	120	30-Sep-25	27-Jan-26
PRO-2020	Procure & Deliver Flagpole	60	30-Sep-25	28-Nov-25
PRO-2030	Procure & Deliver Bleachers	130	30-Sep-25	06-Feb-26
PRO-2040	Procure & Deliver VAV Units	170	30-Sep-25	18-Mar-26
PRO-2050	Procure & Deliver Furnitures (Owner Responsibility)	130	30-Sep-25	06-Feb-26
PRO-1450	Procure & Deliver Playground Equipment	60	09-Dec-25	06-Feb-26
PRO-1990	Procure & Deliver Gas Meter Rig	60	25-Apr-26	23-Jun-26
PRO-2000	Procure & Deliver Key Cutting Machine	74	08-Jul-26	19-Sep-26
Construction		231	16-Oct-25	17-Sep-26
First Floor		227	16-Oct-25	11-Sep-26
SSDS		8	16-Oct-25	27-Oct-25
CON-9898	Install Gas Permeable Aggregate -1st Floor	3	16-Oct-25	20-Oct-25
CON-98947	Install 4" slotted schedule 80 PVC Piping -1st Floor	3	16-Oct-25	20-Oct-25
CON-9888	Install Liquid Boot VI-20 Geomembrane -1st Floor	2	21-Oct-25	22-Oct-25
CON-1020	Install 60 Dry MILS Liquid Boot -1st Floor	3	23-Oct-25	27-Oct-25
CON-9777	Install Liquid Ultrashield G-1000 -1st Floor	2	24-Oct-25	27-Oct-25
Structure-1st Floor		89	28-Oct-25	09-Mar-26
CON-1040	F/R/P Concrete Walls & Beams -1st Floor	10	28-Oct-25	10-Nov-25
CON-1050	Install Underground Conduits & Wires -1st Floor	6	12-Nov-25	19-Nov-25
CON-1060	Backfilling & Compaction -1st Floor	6	12-Nov-25	19-Nov-25
CON-1070	F/R/P SOG -1st Floor	10	20-Nov-25	04-Dec-25
CON-98787	Install Steel Columns -1st Floor	7	05-Dec-25	15-Dec-25
CON-1090	Install Trusses -1st Floor	3	16-Dec-25	18-Dec-25
CON-1100	Install Framing Beams -1st Floor	4	16-Dec-25	19-Dec-25
CON-99277	Install Steel Stairs -1st Floor	7	28-Jan-26	05-Feb-26
CON-1180	Spray Fireproofing - 1st Floor	5	03-Mar-26	09-Mar-26
Mechanical-1st Floor		164	22-Dec-25	17-Aug-26
HVAC Rough-ins		134	22-Dec-25	06-Jul-26
CON-1130	Install MEP Hangers & Sleeves- 2nd Floor	4	22-Dec-25	26-Dec-25
CON-2900	Install Duct Risers-1st Floor	1	07-Apr-26	07-Apr-26
CON-3060	Install Mechanical Piping Risers-1st Floor	2	08-Apr-26	09-Apr-26
CON-3070	Duct Leak Test -1st Floor	1	08-Apr-26	08-Apr-26
CON-3120	Rough-in Duct Work -1st Floor	4	09-Apr-26	14-Apr-26
CON-3460	Rough-in Hot Water Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3470	Rough-in Hot Glycol Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3480	Rough-in Chilled Glycol Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3490	Rough-in Refrigerant Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3970	Install VAV Boxes & Sound Attenuator Devices- 1st Floor	5	16-Apr-26	22-Apr-26
CON-4840	Install Duct Insulation -1st Floor	8	24-Jun-26	06-Jul-26
Mechanical Equipment		30	07-Jul-26	17-Aug-26
CON-4670	Install Exhaust Fans -1st Floor	5	07-Jul-26	13-Jul-26
CON-4870	Install Cabinet Unit Heaters With Fan CUH-1st Floor	3	14-Jul-26	16-Jul-26

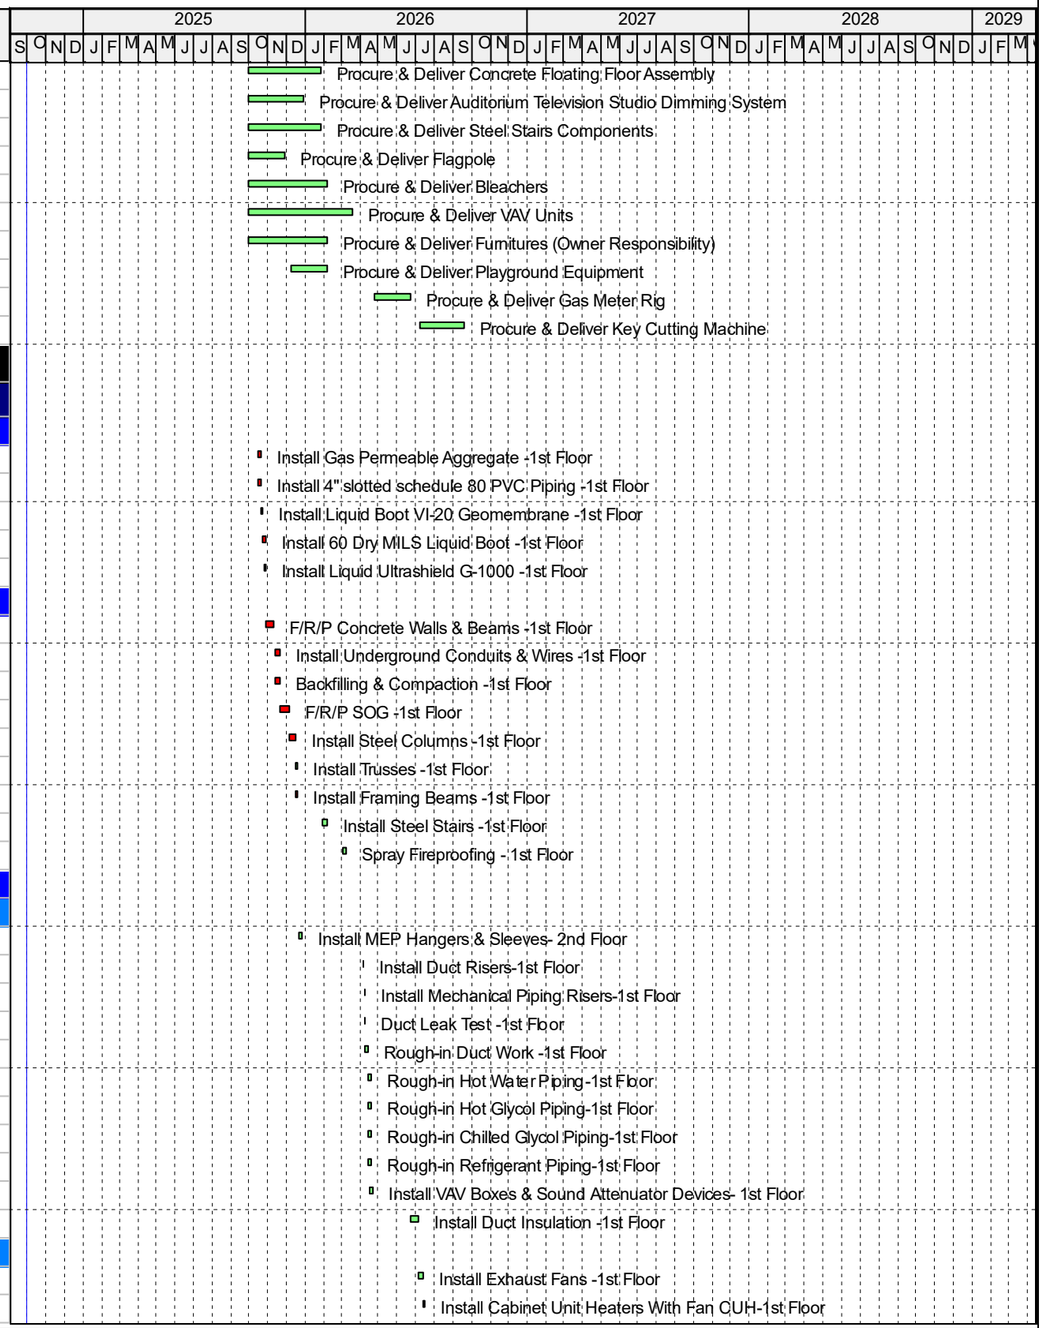

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
CON-4880	Install Motorized Fire/Smoke Damper FSD - Mechanical Work - 1st Floor	7	14-Jul-26	22-Jul-26
CON-5070	Install Electric Unit Heaters -1st Floor	7	17-Jul-26	27-Jul-26
CON-5150	Install Air Conditioning Unit AC - Mechanical Work - 1st Floor	4	23-Jul-26	28-Jul-26
CON-5320	Install Door Curtains DC - Mechanical Work - 1st Floor	7	29-Jul-26	06-Aug-26
CON-5490	Install Convector Heater CV - Mechanical Work - 1st Floor	7	07-Aug-26	17-Aug-26
Plumbing-1st Floor		177	27-Nov-25	12-Aug-26
CON-4920	Install Floor Drains & Clean-outs -1st Floor	5	27-Nov-25	04-Dec-25
CON-3140	Install Plumbing Risers -1st Floor	2	10-Apr-26	13-Apr-26
CON-3230	Install SSDS Risers -SSDS System -1st Floor	2	14-Apr-26	15-Apr-26
CON-4460	Rough-in Gas Risers -1st Floor	4	07-May-26	12-May-26
CON-4590	Rough-in Domestic Water Piping-1st Floor	4	13-May-26	18-May-26
CON-4690	Rough-in Sanitary & Vent Piping -1st Floor	4	19-May-26	22-May-26
CON-4760	Rough-in Storm Piping -1st Floor	4	26-May-26	29-May-26
CON-4940	Install Duplex Domestic Water Booster Pump System (BP-1&BP-2) -1st Floor	8	01-Jun-26	10-Jun-26
CON-4950	Install Duplex Ejector Pump System (EJ-1&EJ-2) -1st Floor	8	01-Jun-26	10-Jun-26
CON-5050	Plumbing Pressure Testing -1st Floor	5	11-Jun-26	17-Jun-26
CON-5210	Plumbing Piping Insulation -1st Floor	5	18-Jun-26	25-Jun-26
CON-5300	Install Grease Interceptors - 1st Floor	5	28-Jul-26	03-Aug-26
CON-6180	Install Plumbing Fixtures-1st Floor	5	06-Aug-26	12-Aug-26
Fire Protection-1st Floor		55	02-Jun-26	19-Aug-26
CON-4910	Install 4" Standpipe -1st Floor	4	02-Jun-26	05-Jun-26
CON-5030	Rough-in Main Sprinkler Piping -1st Floor	5	08-Jun-26	12-Jun-26
CON-5230	Rough-in Branch Sprinkler Piping -1st Floor	5	15-Jun-26	22-Jun-26
CON-5240	Rough-in Sprinkler Heads -1st Floor	5	15-Jun-26	22-Jun-26
CON-5270	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -1st Floor	5	23-Jun-26	29-Jun-26
CON-5410	Sprinklers Air Testing-1st Floor	5	30-Jun-26	07-Jul-26
CON-5860	Install Sprinkler Booster Pump (SBP-1) -1st Floor	10	23-Jul-26	05-Aug-26
CON-6100	Install Jockey Pump (JP-1) -1st Floor	10	06-Aug-26	19-Aug-26
Electrical-1st Floor		189	03-Dec-25	02-Sep-26
CON-99327	Install Lightning Protection System-1st Floor	2	03-Dec-25	04-Dec-25
CON-3260	Install Power Risers-1st Floor	2	14-Apr-26	15-Apr-26
CON-3350	Install Low Voltage Risers-1st Floor	2	16-Apr-26	17-Apr-26
CON-3760	Rough-in Power Conduits -1st Floor	4	21-Apr-26	24-Apr-26
CON-3910	Install Grounding System -1st Floor	5	27-Apr-26	01-May-26
CON-3920	Rough-in Low-Voltage Conduits-1st Floor	4	27-Apr-26	30-Apr-26
CON-3930	Power Wires Pulling-1st Floor	4	27-Apr-26	30-Apr-26
CON-4180	Low Voltage Wires Pulling -1st Floor	4	01-May-26	06-May-26
CON-4500	Install SSDS Control Panel -1st Floor	5	07-May-26	13-May-26
CON-4470	Install Wiring Devices -1st Floor	7	15-May-26	26-May-26
CON-5940	Install Lighting Fixtures -1st Floor	7	24-Jul-26	03-Aug-26
CON-5950	Install Fire alarm Sensors and Devises -1st Floor	3	05-Aug-26	07-Aug-26
CON-6040	Install IPDVS Devices -1st Floor	7	25-Aug-26	02-Sep-26
Architecture-1st Floor		141	23-Feb-26	11-Sep-26
Interior Walls		100	23-Feb-26	15-Jul-26

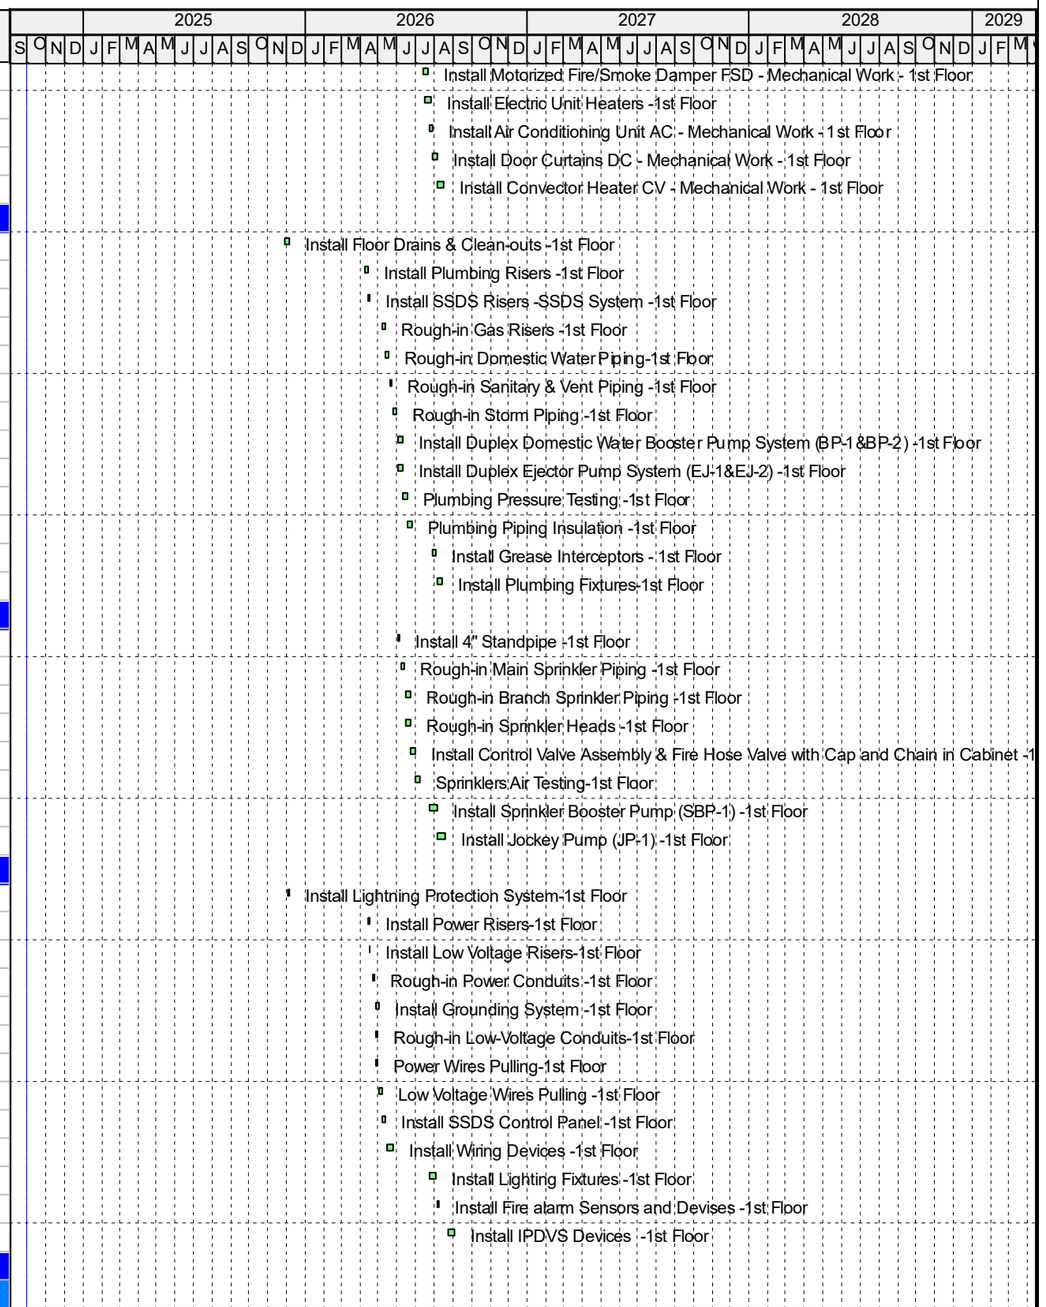

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1430	Install Unit Masonry Mock-Up	1	23-Feb-26	23-Feb-26
CON-1470	Approve Unit Masonry Mock-Up	4	24-Feb-26	27-Feb-26
CON-2910	Layout -1st Floor	3	07-Apr-26	09-Apr-26
CON-3080	Install Top & Bottom Track -1st Floor	4	10-Apr-26	15-Apr-26
CON-3090	Install CMU Walls -1st Floor	3	10-Apr-26	14-Apr-26
CON-3240	Install Wall Steel Studs & Framing -1st Floor	5	16-Apr-26	22-Apr-26
CON-9110	In-Wall Inspection -1st Floor	2	19-May-26	20-May-26
CON-1120	Install Firestopping Mock-Up	2	01-Jun-26	02-Jun-26
CON-1140	Approve Firestopping Mock-Up	2	03-Jun-26	04-Jun-26
MIL-1750	Start Firestopping	0	05-Jun-26	
CON-4450	Install Gypsum Board Walls-1st Floor	6	26-Jun-26	06-Jul-26
CON-4600	Tape Gypsum Board -1st Floor	4	30-Jun-26	06-Jul-26
CON-5390	Install Firestopping-1st Floor	4	30-Jun-26	06-Jul-26
CON-4680	Install Ceramic Wall Tiles at Corridor -1st Floor	7	07-Jul-26	15-Jul-26
Ceiling		100	15-Apr-26	04-Sep-26
CON-3520	Install Ceiling Hangers & Supports -1st Floor	4	15-Apr-26	20-Apr-26
CON-5480	Install Gypsum Board Ceiling -1st Floor	6	08-Jul-26	15-Jul-26
CON-5870	Install Metal Panel Ceiling & Metal Geometric Ceiling -1st Floor	5	23-Jul-26	29-Jul-26
CON-5880	Install Acoustical Ceiling Tiles -1st Floor	5	31-Aug-26	04-Sep-26
Finishes		41	16-Jul-26	11-Sep-26
CON-5720	Install First Coat Painting-1st Floor	5	16-Jul-26	22-Jul-26
CON-5920	Install Door Frames & Doors-1st Floor	5	23-Jul-26	29-Jul-26
CON-98937	Install Sound Clock System Components-1st Floor	3	24-Jul-26	28-Jul-26
CON-98887	Install Auxiliary System Components-1st Floor	4	29-Jul-26	03-Aug-26
CON-6080	Install Flooring Tiles-1st Floor	5	30-Jul-26	05-Aug-26
CON-99267	Install Rolling Doors-1st Floor	3	30-Jul-26	03-Aug-26
CON-98837	Install Intrusion System Components-1st Floor	4	04-Aug-26	07-Aug-26
CON-6170	Install Final Coat Painting-1st Floor	6	21-Aug-26	28-Aug-26
CON-6300	Install Furniture & Milling Work (Contractor Provided & Installed) -1st Floor	4	31-Aug-26	03-Sep-26
CON-6310	Install Security Screens & Barriers-1st Floor	3	31-Aug-26	02-Sep-26
CON-6320	Install Cafeteria Equipment-1st Floor	4	31-Aug-26	03-Sep-26
CON-9020	Install Furniture & Milling Work (Owner Provided & Installed) -1st Floor	3	31-Aug-26	02-Sep-26
CON-6370	Install Signages-1st Floor	4	04-Sep-26	10-Sep-26
CON-6380	Install Food Service Equipment-1st Floor	5	04-Sep-26	11-Sep-26
Second Floor		150	19-Dec-25	27-Jul-26
Structure-2nd Floor		57	22-Dec-25	16-Mar-26
CON-1110	Install Metal Deck Slab -2nd Floor	4	22-Dec-25	26-Dec-25
CON-1150	Install Steel Canopy Framing -2nd Floor	5	29-Dec-25	05-Jan-26
CON-1170	Install Steel Columns -2nd Floor	3	29-Dec-25	31-Dec-25
CON-1190	Install Trusses -2nd Floor	4	02-Jan-26	07-Jan-26
CON-1200	Install Framing Beams -2nd Floor	5	02-Jan-26	08-Jan-26
CON-99287	Install Steel Stairs -2nd Floor	3	06-Feb-26	10-Feb-26
CON-1220	Spray Fireproofing - 2nd Floor	5	10-Mar-26	16-Mar-26
Mechanical-2nd Floor		90	09-Jan-26	18-May-26

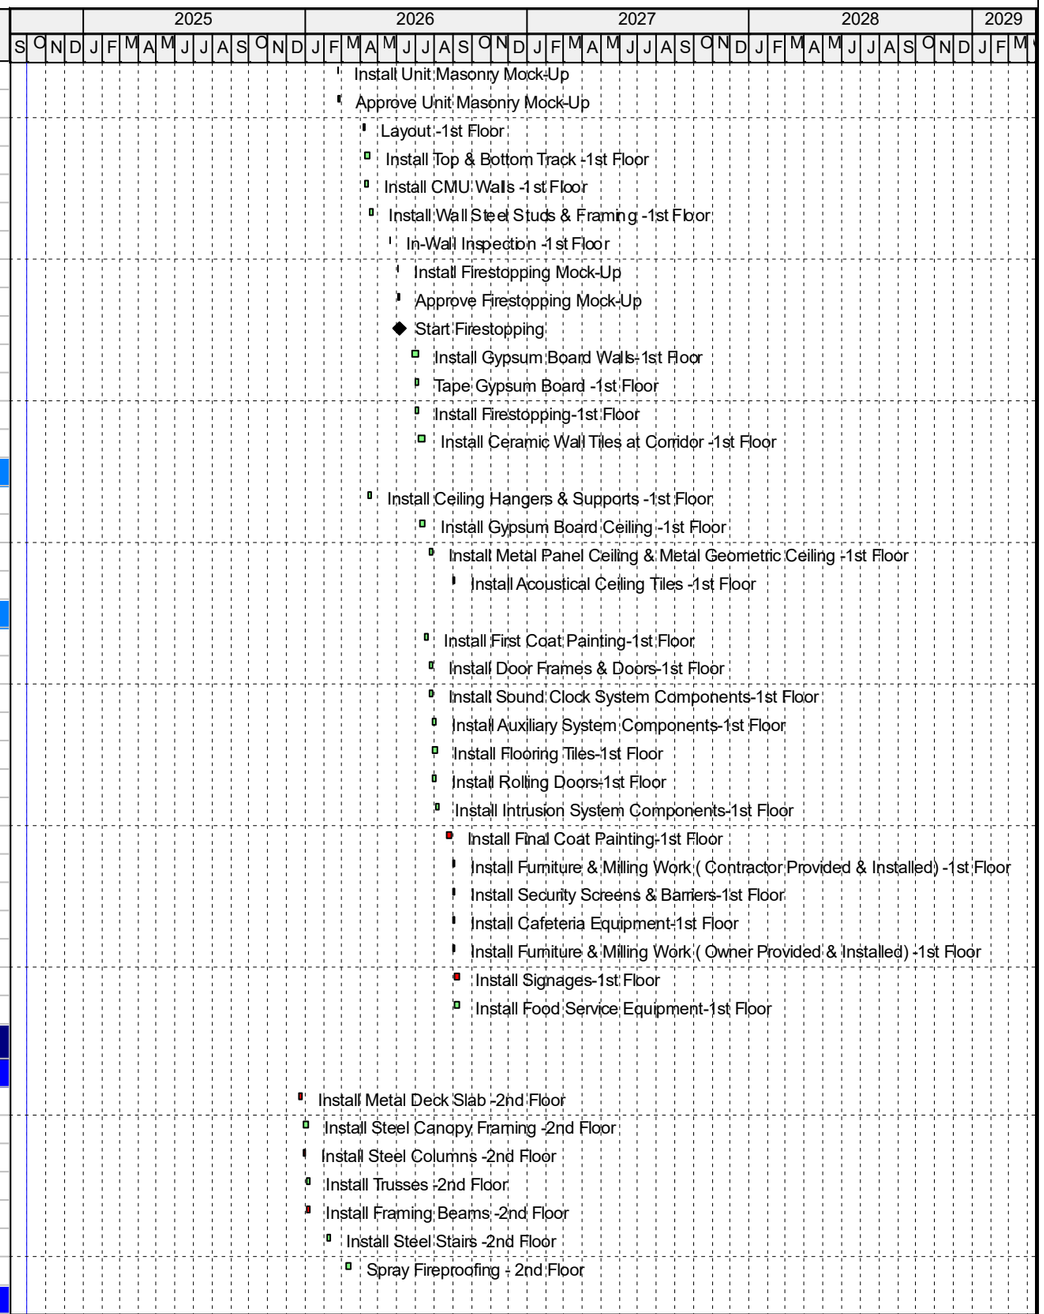

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
HVAC Rough-ins		90	09-Jan-26	18-May-26
CON-1230	Install MEP Hangers & Sleeves-3rd Floor	4	09-Jan-26	14-Jan-26
CON-1410	Install Duct Risers-2nd Floor	1	23-Feb-26	23-Feb-26
CON-1480	Rough-in Duct Work -2nd Floor	4	24-Feb-26	27-Feb-26
CON-1500	Install Mechanical Piping Risers-2nd Floor	2	24-Feb-26	25-Feb-26
CON-1510	Duct Leak Test -2nd Floor	2	24-Feb-26	25-Feb-26
CON-1850	Rough-in Hot Water Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1860	Rough-in Hot Glycol Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1870	Rough-in Chilled Glycol Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1880	Rough-in Refrigerant Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-3980	Install VAV Boxes & Sound Attenuator Devices-2nd Floor	5	19-Mar-26	25-Mar-26
CON-4070	Install Duct Insulation -2nd Floor	8	07-May-26	18-May-26
Mechanical Equipment		14	16-Apr-26	05-May-26
CON-2850	Install Electric Unit Heaters -2nd Floor	5	16-Apr-26	22-Apr-26
CON-3150	Install Convector Heater CV - Mechanical Work - 2nd Floor	5	23-Apr-26	29-Apr-26
CON-3450	Install Air Conditioning Unit AC - Mechanical Work - 2nd Floor	4	30-Apr-26	05-May-26
Plumbing-2nd Floor		141	19-Dec-25	14-Jul-26
CON-3160	Install Floor Drains & Clean-outs -2nd Floor	5	19-Dec-25	26-Dec-25
CON-1580	Install Plumbing Risers -2nd Floor	2	26-Feb-26	27-Feb-26
CON-1740	Install SSDS Risers -SSDS System -2nd Floor	2	02-Mar-26	03-Mar-26
CON-2630	Rough-in Gas Risers -2nd Floor	4	06-Apr-26	09-Apr-26
CON-2740	Rough-in Domestic Water Piping -2nd Floor	4	10-Apr-26	15-Apr-26
CON-2870	Rough-in Sanitary & Vent Piping -2nd Floor	4	16-Apr-26	21-Apr-26
CON-3020	Rough-in Storm Piping -2nd Floor	4	22-Apr-26	27-Apr-26
CON-3200	Plumbing Pressure Testing -2nd Floor	5	28-Apr-26	04-May-26
CON-4050	Plumbing Piping Insulation -2nd Floor	5	07-May-26	13-May-26
CON-5570	Install Plumbing Fixtures -2nd Floor	7	06-Jul-26	14-Jul-26
Fire Protection-2nd Floor		106	29-Dec-25	29-May-26
CON-3270	Install Temporary Standpipe	9	29-Dec-25	09-Jan-26
CON-3310	Install 4" Standpipe -2nd Floor	4	04-May-26	07-May-26
CON-3500	Rough-in Main Sprinkler Piping -2nd Floor	5	08-May-26	14-May-26
CON-3670	Rough-in Branch Sprinkler Piping -2nd Floor	5	15-May-26	21-May-26
CON-3680	Rough-in Sprinkler Heads -2nd Floor	5	15-May-26	21-May-26
CON-3720	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -2nd Floor	5	15-May-26	21-May-26
CON-3830	Sprinklers Air Testing-2nd Floor	5	22-May-26	29-May-26
Electrical-2nd Floor		96	02-Mar-26	16-Jul-26
CON-1710	Install Power Risers-2nd Floor	2	02-Mar-26	03-Mar-26
CON-1800	Install Low Voltage Risers-2nd Floor	2	04-Mar-26	05-Mar-26
CON-2180	Rough-in Power Conduits -2nd Floor	6	11-Mar-26	18-Mar-26
CON-2330	Rough-in Low-Voltage Conduits -2nd Floor	6	19-Mar-26	26-Mar-26
CON-2340	Power Wires Pulling -2nd Floor	6	19-Mar-26	26-Mar-26
CON-2490	Low Voltage Wires Pulling -2nd Floor	6	27-Mar-26	03-Apr-26
CON-2520	Install Voice Rack - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2530	Install Data Rack - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26

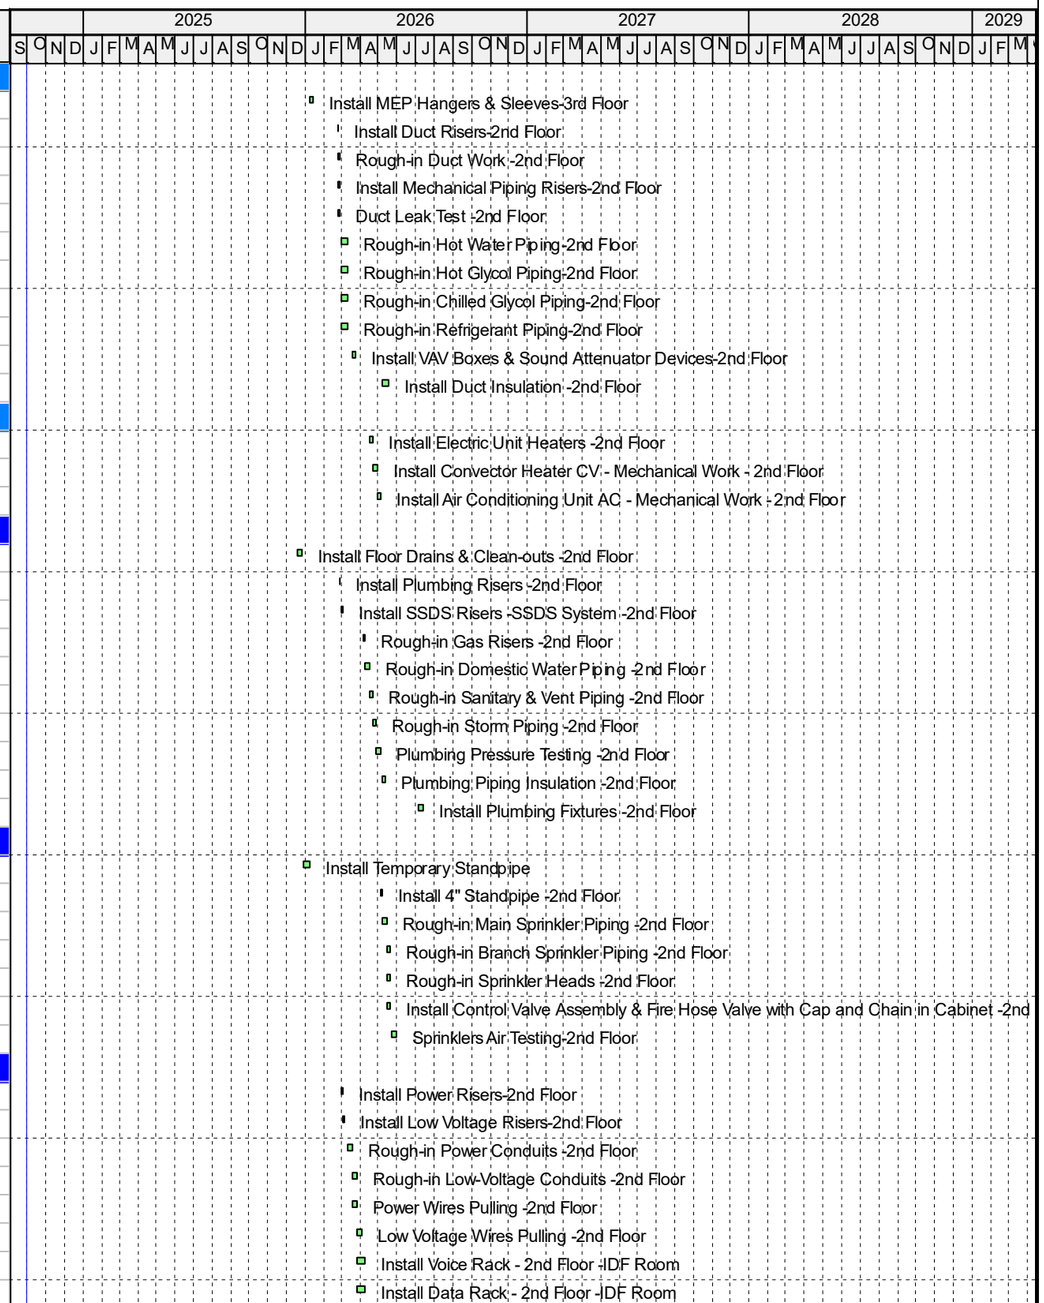

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2540	Install Ground Bus Bar - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2670	Install Wiring Devices -2nd Floor	7	06-Apr-26	14-Apr-26
CON-2760	Install IPDVS Equipment Rack - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2770	Install Ladder Rack Cable Tray - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2780	Install BACnet Data Cabinet - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-5130	Install Lighting Fixtures -2nd Floor	5	18-Jun-26	25-Jun-26
CON-5310	Install Fire alarm Sensors and Devises -2nd Floor	5	26-Jun-26	02-Jul-26
CON-5140	Install IPDVS Devices -2nd Floor	9	06-Jul-26	16-Jul-26
Architecture-2nd Floor		108	23-Feb-26	27-Jul-26
Interior Walls		78	23-Feb-26	11-Jun-26
CON-1420	Layout -2nd Floor	3	23-Feb-26	25-Feb-26
CON-1520	Install Top & Bottom Track-2nd Floor	4	26-Feb-26	03-Mar-26
CON-1570	Install CMU Walls -2nd Floor	3	02-Mar-26	04-Mar-26
CON-1640	Install Wall Steel Studs & Framing-2nd Floor	5	04-Mar-26	10-Mar-26
CON-9070	In-Wall Inspection-2nd Floor	2	16-Apr-26	17-Apr-26
CON-4030	Install Gypsum Board Walls-2nd Floor	5	27-May-26	02-Jun-26
CON-4200	Tape Gypsum Board -2nd Floor	4	28-May-26	02-Jun-26
CON-4350	Install Ceramic Wall Tiles at Corridor-2nd Floor	7	03-Jun-26	11-Jun-26
CON-4700	Install Firestopping-2nd Floor	3	05-Jun-26	09-Jun-26
Ceiling		88	16-Mar-26	20-Jul-26
CON-2310	Install Ceiling Hangers & Supports-2nd Floor	4	16-Mar-26	19-Mar-26
CON-4370	Install Gypsum Board Ceiling -2nd Floor	6	03-Jun-26	10-Jun-26
CON-5090	Install Acoustical Ceiling Tiles-2nd Floor	5	14-Jul-26	20-Jul-26
Finishes		31	11-Jun-26	27-Jul-26
CON-4830	Install First Coat Painting-2nd Floor	5	11-Jun-26	17-Jun-26
CON-5120	Install Door Frames & Doors-2nd Floor	5	18-Jun-26	25-Jun-26
CON-98797	Install Intrusion System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-98847	Install Auxiliary System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-98897	Install Sound Clock System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-5360	Install Flooring Tiles-2nd Floor	5	26-Jun-26	02-Jul-26
CON-5560	Install Final Coat Painting-2nd Floor	6	06-Jul-26	13-Jul-26
CON-5710	Install Furniture & Milling Work (Contractor Provided & Installed) -2nd Floor	5	14-Jul-26	20-Jul-26
CON-9030	Install Furniture & Milling Work (Owner Provided & Installed) -2nd Floor	5	14-Jul-26	20-Jul-26
CON-5820	Install Signages-2nd Floor	5	21-Jul-26	27-Jul-26
Third Floor		144	08-Jan-26	04-Aug-26
Structure-3rd Floor		50	09-Jan-26	23-Mar-26
CON-1210	Install Metal Deck Slab - 3rd Floor	4	09-Jan-26	14-Jan-26
CON-1240	Install Steel Columns - 3rd Floor	4	15-Jan-26	21-Jan-26
CON-1260	Install Trusses - 3rd Floor	3	22-Jan-26	26-Jan-26
CON-1270	Install Framing Beams - 3rd Floor	5	22-Jan-26	28-Jan-26
CON-99297	Install Steel Stairs- 3rd Floor	4	11-Feb-26	17-Feb-26
CON-1300	Spray Fireproofing - 3rd Floor	5	17-Mar-26	23-Mar-26
Mechanical-3rd Floor		129	29-Jan-26	03-Aug-26
HVAC Rough-ins		85	29-Jan-26	29-May-26

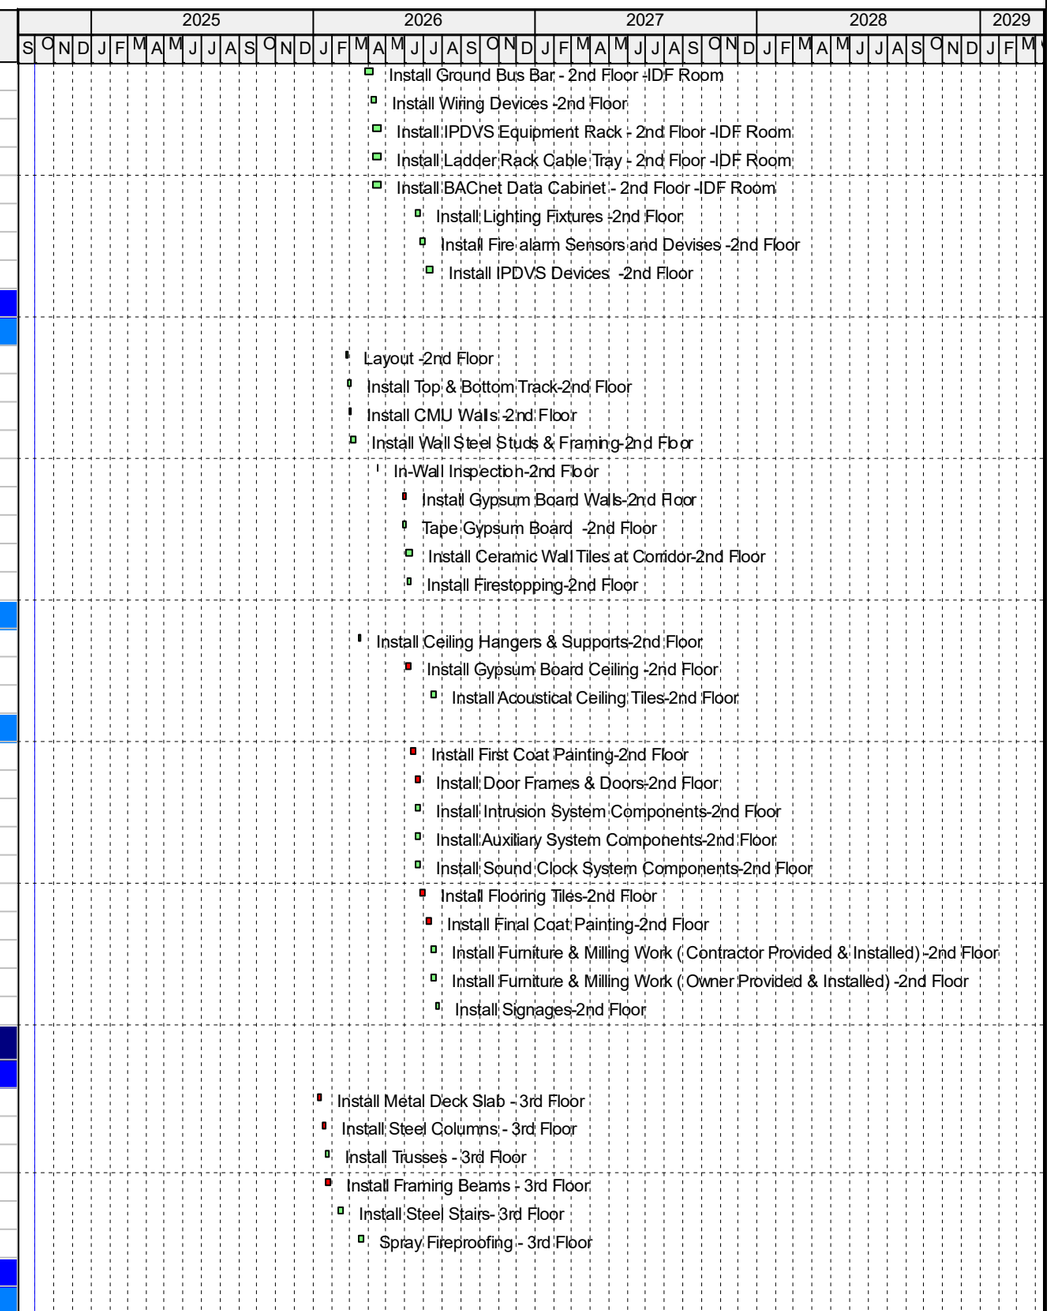

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1310	Install MEP Hangers & Sleeves-4th Floor	4	29-Jan-26	03-Feb-26
CON-1490	Install Duct Risers -3rd Floor	2	24-Feb-26	25-Feb-26
CON-1590	Install Mechanical Piping Risers -3rd Floor	2	26-Feb-26	27-Feb-26
CON-1600	Duct Leak Test -3rd Floor	2	26-Feb-26	27-Feb-26
CON-1890	Rough-in Duct Work -3rd Floor	5	02-Mar-26	06-Mar-26
CON-2160	Rough-in Refrigerant Piping-3rd Floor	7	09-Mar-26	17-Mar-26
CON-2130	Rough-in Hot Water Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-2140	Rough-in Hot Glycol Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-2150	Rough-in Chilled Glycol Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-4140	Install VAV Boxes & Sound Attenuator Devices-3rd Floor	5	26-Mar-26	01-Apr-26
CON-4320	Install Duct Insulation -3rd Floor	8	19-May-26	29-May-26
Mechanical Equipment		70	23-Apr-26	03-Aug-26
CON-3130	Install Electric Unit Heaters -3rd Floor	5	23-Apr-26	29-Apr-26
CON-5060	Install Hot Glycol / Hot Water Cabinet Heater (CUH)-3rd Floor	4	17-Jul-26	22-Jul-26
CON-5280	Install Convector Heater CV - Mechanical Work - 3rd Floor	4	23-Jul-26	28-Jul-26
CON-5450	Install Air Conditioning Unit AC - Mechanical Work - 3rd Floor	4	29-Jul-26	03-Aug-26
Plumbing-3rd Floor		136	08-Jan-26	23-Jul-26
CON-3320	Install Floor Drains & Clean-outs -3rd Floor	5	08-Jan-26	14-Jan-26
CON-1680	Install Plumbing Risers -3rd Floor	2	02-Mar-26	03-Mar-26
CON-1840	Install SSDS Risers -SSDS System -3rd Floor	2	04-Mar-26	05-Mar-26
CON-2750	Rough-in Gas Risers-3rd Floor	4	10-Apr-26	15-Apr-26
CON-2880	Rough-in Domestic Water Piping -3rd Floor	4	16-Apr-26	21-Apr-26
CON-3030	Rough-in Sanitary & Vent Piping -3rd Floor	4	22-Apr-26	27-Apr-26
CON-3170	Rough-in Storm Piping -3rd Floor	4	28-Apr-26	01-May-26
CON-3360	Plumbing Pressure Testing -3rd Floor	5	05-May-26	11-May-26
CON-4190	Plumbing Piping Insulation -3rd Floor	5	14-May-26	20-May-26
CON-5730	Install Plumbing Fixtures -3rd Floor	7	15-Jul-26	23-Jul-26
Fire Protection-3rd Floor		20	08-May-26	05-Jun-26
CON-3510	Install 4" Standpipe -3rd Floor	4	08-May-26	13-May-26
CON-3690	Rough-in Main Sprinkler Piping-3rd Floor	5	15-May-26	21-May-26
CON-3790	Rough-in Branch Sprinkler Piping -3rd Floor	5	22-May-26	29-May-26
CON-3800	Rough-in Sprinkler Heads -3rd Floor	5	22-May-26	29-May-26
CON-3880	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-3rd Floor	5	22-May-26	29-May-26
CON-4060	Sprinklers Air Testing-3rd Floor	5	01-Jun-26	05-Jun-26
Electrical-3rd Floor		103	04-Mar-26	29-Jul-26
CON-1820	Install Power Risers-3rd Floor	2	04-Mar-26	05-Mar-26
CON-1950	Install Low Voltage Risers-3rd Floor	2	06-Mar-26	09-Mar-26
CON-2320	Rough-in Power Conduits-3rd Floor	6	19-Mar-26	26-Mar-26
CON-2640	Install Grounding Bars - 3rd Floor IDF Room	5	27-Mar-26	02-Apr-26
CON-2500	Rough-in Low-Voltage Conduits-3rd Floor	6	27-Mar-26	03-Apr-26
CON-2510	Power Wires Pulling-3rd Floor	6	27-Mar-26	03-Apr-26
CON-2800	Install Data rack - 3rd Floor IDF Room	8	03-Apr-26	14-Apr-26
CON-2830	Install IPDVS Equipment Rack - 3rd Floor IDF Room	4	03-Apr-26	08-Apr-26
CON-2690	Low Voltage Wires Pulling -3rd Floor	6	06-Apr-26	13-Apr-26

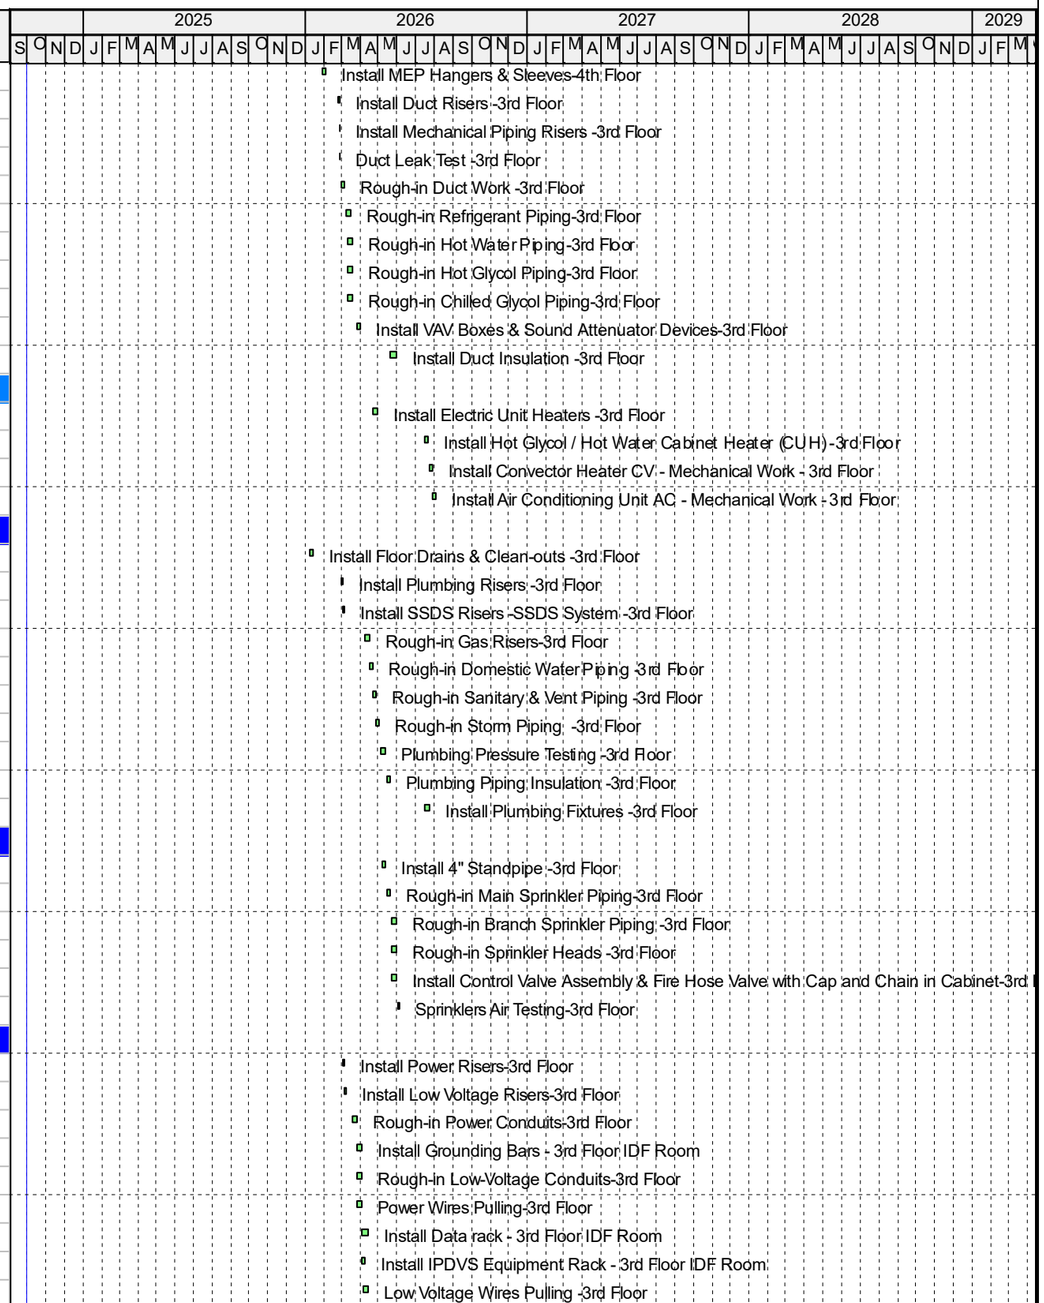

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3250	Install Voice Rack - 3rd Floor IDF Room	5	15-Apr-26	21-Apr-26
CON-2930	Install Wiring Devices -3rd Floor	7	15-Apr-26	23-Apr-26
CON-3550	Install Cable Ladder - 3rd Floor IDF Room	5	22-Apr-26	28-Apr-26
CON-3570	Install Main Sound Rack - 3rd Floor IDF Room	5	22-Apr-26	28-Apr-26
CON-5370	Install Lighting Fixtures -3rd Floor	6	29-Jun-26	07-Jul-26
CON-5500	Install Fire alarm Sensors and Devises -3rd Floor	8	08-Jul-26	17-Jul-26
CON-5440	Install IPDVS Devices -3rd Floor	9	17-Jul-26	29-Jul-26
Architecture-3rd Floor		111	26-Feb-26	04-Aug-26
Interior Walls		82	26-Feb-26	23-Jun-26
CON-1530	Layout -3rd Floor	3	26-Feb-26	02-Mar-26
CON-1650	Install Top & Bottom Track-3rd Floor	4	04-Mar-26	09-Mar-26
CON-1660	Install CMU Walls -3rd Floor	3	05-Mar-26	09-Mar-26
CON-1900	Install Wall Steel Studs & Framing-3rd Floor	5	10-Mar-26	16-Mar-26
CON-9080	In-Wall Inspection -3rd Floor	2	22-Apr-26	23-Apr-26
CON-4360	Install Gypsum Board Walls-3rd Floor	5	03-Jun-26	09-Jun-26
CON-4540	Tape Gypsum Board -3rd Floor	4	04-Jun-26	09-Jun-26
CON-4850	Install Firestopping-3rd Floor	4	10-Jun-26	15-Jun-26
CON-4610	Install Ceramic Wall Tiles at Corridor-3rd Floor	7	12-Jun-26	23-Jun-26
Ceiling		90	20-Mar-26	28-Jul-26
CON-2390	Install Ceiling Hangers & Supports-3rd Floor	4	20-Mar-26	25-Mar-26
CON-4630	Install Gypsum Board Ceiling-3rd Floor	6	11-Jun-26	18-Jun-26
CON-5330	Install Acoustical Ceiling Tiles-3rd Floor	5	22-Jul-26	28-Jul-26
Finishes		31	22-Jun-26	04-Aug-26
CON-5110	Install First Coat Painting-3rd Floor	5	22-Jun-26	26-Jun-26
CON-5350	Install Door Frames & Doors-3rd Floor	5	29-Jun-26	06-Jul-26
CON-98807	Install Intrusion System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-98857	Install Auxiliary System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-98907	Install Sound Clock System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-5550	Install Flooring Tiles-3rd Floor	5	07-Jul-26	13-Jul-26
CON-5700	Install Final Coat Painting-3rd Floor	6	14-Jul-26	21-Jul-26
CON-99247	Install Laboratory Equipment -3rd Floor	4	14-Jul-26	17-Jul-26
CON-5910	Install Furniture & Milling Work (Contractor Provided & Installed) -3rd Floor	5	22-Jul-26	28-Jul-26
CON-9040	Install Furniture & Milling Work (Owner Provided & Installed) -3rd Floor	5	22-Jul-26	28-Jul-26
CON-6030	Install Signages-3rd Floor	5	29-Jul-26	04-Aug-26
Fourth Floor		182	29-Dec-25	17-Sep-26
Structure-4th Floor		42	29-Jan-26	30-Mar-26
CON-1290	Install Metal Deck Slab - 4th Floor	4	29-Jan-26	03-Feb-26
CON-1330	Install Steel Columns - 4th Floor	4	04-Feb-26	09-Feb-26
CON-1360	Install Trusses - 4th Floor	3	10-Feb-26	12-Feb-26
CON-1370	Install Framing Beams - 4th Floor	5	10-Feb-26	17-Feb-26
CON-99307	Install Steel Stairs - 4th Floor	4	23-Feb-26	26-Feb-26
CON-1390	Spray Fireproofing - 4th Floor	5	24-Mar-26	30-Mar-26
Material Hoist		182	29-Dec-25	17-Sep-26
CON-1160	Hoist Material Design	10	29-Dec-25	12-Jan-26

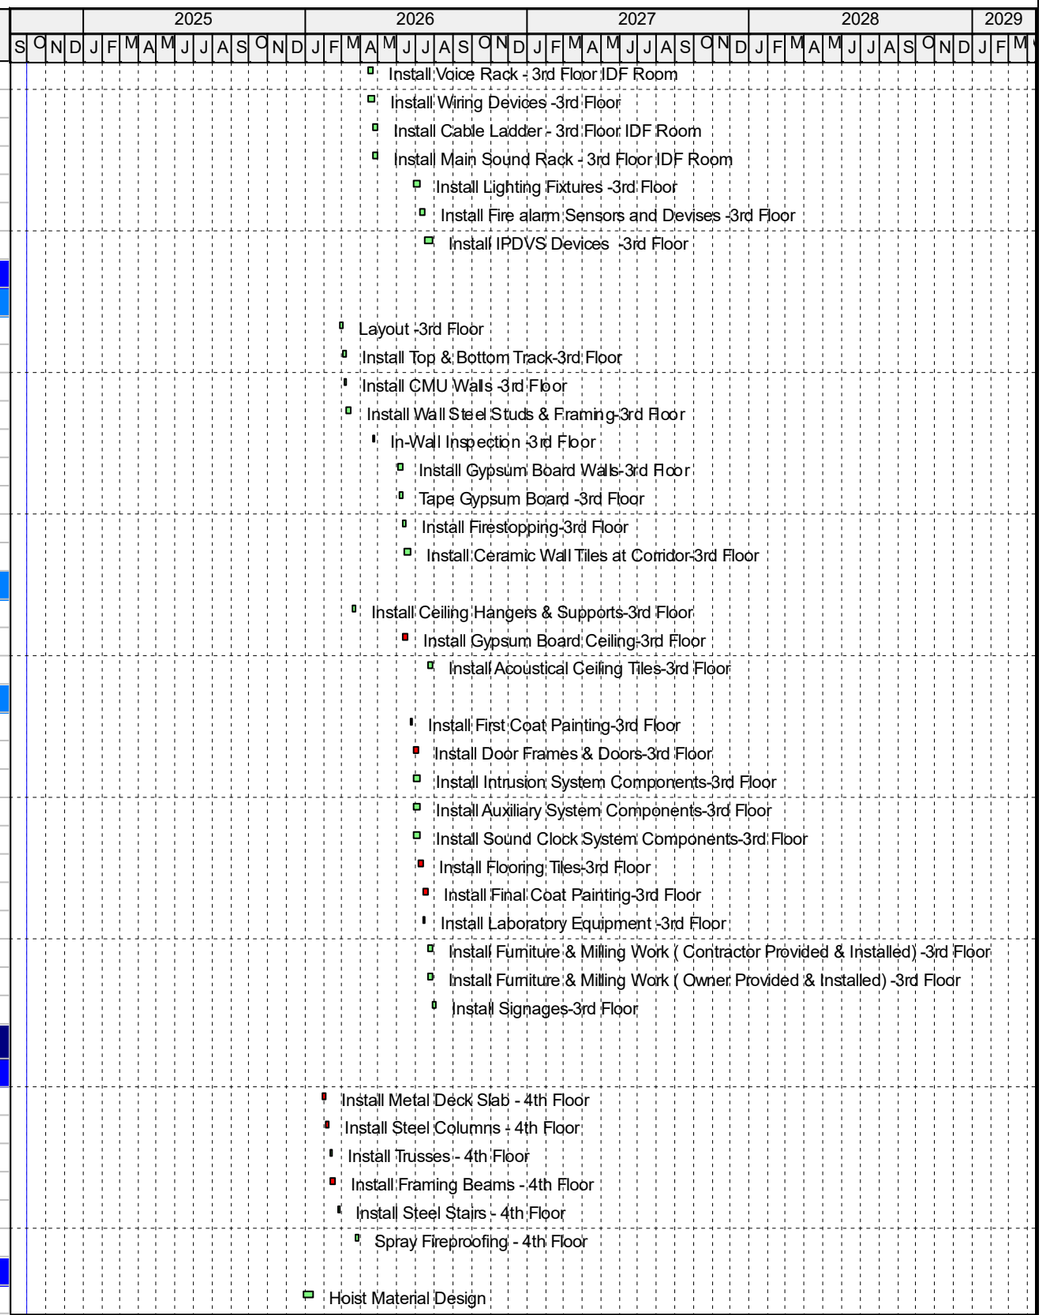

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1250	Approval of Hoist Design	7	13-Jan-26	19-Jan-26
CON-1280	Install Elevator Hoist Pad	5	20-Jan-26	26-Jan-26
CON-1320	Erect Material Hoist	5	27-Jan-26	02-Feb-26
CON-5040	Dismantle Hoist	2	10-Sep-26	11-Sep-26
CON-5170	Demolish Hoist Pad	2	14-Sep-26	15-Sep-26
CON-5250	Hoist In-Fill	2	16-Sep-26	17-Sep-26
Mechanical-4th Floor		121	17-Feb-26	07-Aug-26
HVAC Rough-ins		81	17-Feb-26	10-Jun-26
CON-1400	Install MEP Hangers & Sleeves-5th Floor	4	17-Feb-26	20-Feb-26
CON-1560	Install Duct Risers -4th Floor	2	26-Feb-26	27-Feb-26
CON-1690	Install Mechanical Piping Risers -4th Floor	2	02-Mar-26	03-Mar-26
CON-1700	Duct Leak Test -4th Floor	2	02-Mar-26	03-Mar-26
CON-2170	Rough-in Duct Work -4th Floor	5	09-Mar-26	13-Mar-26
CON-2290	Rough-in Refrigerant Piping-4th Floor	7	16-Mar-26	24-Mar-26
CON-2260	Rough-in Hot Water Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-2270	Rough-in Hot Glycol Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-2280	Rough-in Chilled Glycol Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-4220	Install VAV Boxes & Sound Attenuator Devices-4th Floor	5	02-Apr-26	08-Apr-26
CON-4570	Install Duct Insulation -4th Floor	8	01-Jun-26	10-Jun-26
Mechanical Equipment		69	30-Apr-26	07-Aug-26
CON-3420	Install Electric Unit Heaters -4th Floor	5	30-Apr-26	06-May-26
CON-5260	Install Cabinet Unit Heater With Fan CUH -4th Floor	4	23-Jul-26	28-Jul-26
CON-5460	Install Convector Heater CV - Mechanical Work - 4th Floor	3	29-Jul-26	31-Jul-26
CON-5620	Install Air Conditioning Unit AC - Mechanical Work - 4th Floor	4	04-Aug-26	07-Aug-26
Plumbing-4th Floor		130	28-Jan-26	03-Aug-26
CON-3530	Install Floor Drains & Clean-outs -4th Floor	5	28-Jan-26	03-Feb-26
CON-1780	Install Plumbing Risers -4th Floor	2	04-Mar-26	05-Mar-26
CON-1970	Install SSDS Risers -SSDS System -4th Floor	2	06-Mar-26	09-Mar-26
CON-2890	Rough-in Gas Risers -4th Floor	4	16-Apr-26	21-Apr-26
CON-3040	Rough-in Domestic Water Piping -4th Floor	4	22-Apr-26	27-Apr-26
CON-3180	Rough-in Sanitary & Vent Piping -4th Floor	4	28-Apr-26	01-May-26
CON-3330	Rough-in Storm Piping -4th Floor	4	04-May-26	07-May-26
CON-3560	Plumbing Pressure Testing -4th Floor	5	12-May-26	18-May-26
CON-4390	Plumbing Piping Insulation -4th Floor	5	21-May-26	28-May-26
CON-5930	Install Plumbing Fixtures -4th Floor	7	24-Jul-26	03-Aug-26
Fire Protection-4th Floor		21	14-May-26	12-Jun-26
CON-3650	Install 4" Standpipe -4th Floor	4	14-May-26	19-May-26
CON-3810	Rough-in Main Sprinkler Piping-4th Floor	5	22-May-26	29-May-26
CON-3990	Rough-in Branch Sprinkler Piping -4th Floor	5	01-Jun-26	05-Jun-26
CON-4000	Rough-in Sprinkler Heads -4th Floor	5	01-Jun-26	05-Jun-26
CON-4100	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-4th Floor	5	01-Jun-26	05-Jun-26
CON-4280	Sprinklers Air Testing-4th Floor	5	08-Jun-26	12-Jun-26
Electrical-4th Floor		110	06-Mar-26	11-Aug-26
CON-1960	Install Power Risers-4th Floor	2	06-Mar-26	09-Mar-26

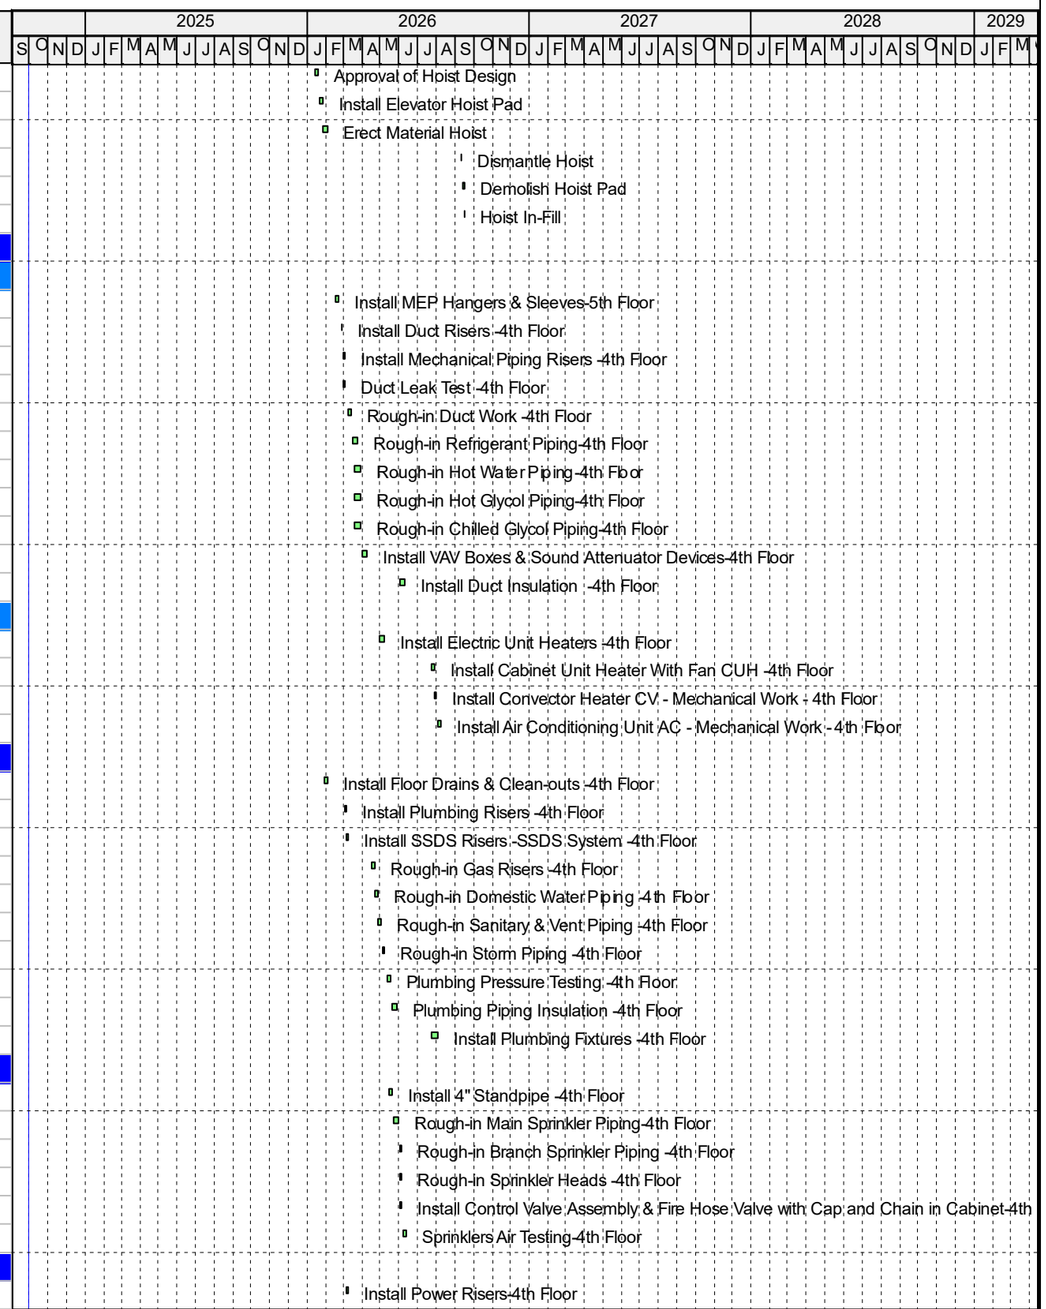

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2040	Install Low Voltage Risers-4th Floor	2	10-Mar-26	11-Mar-26
CON-2480	Rough-in Power Conduits-4th Floor	6	27-Mar-26	03-Apr-26
CON-2810	Install Grounding Bars - 4th Floor IDF Room	5	06-Apr-26	10-Apr-26
CON-2650	Install Data Rack - 4th Floor IDF Room	7	06-Apr-26	14-Apr-26
CON-2660	Install Voice Rack - 4th Floor IDF Room	5	06-Apr-26	10-Apr-26
CON-2700	Rough-in Low-Voltage Conduits-4th Floor	6	06-Apr-26	13-Apr-26
CON-2710	Power Wires Pulling-4th Floor	6	06-Apr-26	13-Apr-26
CON-2820	Install Cable Ladder - 4th Floor IDF Room	5	13-Apr-26	17-Apr-26
CON-2840	Install Main Sound Rack - 34th Floor IDF Room	5	13-Apr-26	17-Apr-26
CON-2940	Low Voltage Wires Pulling-4th Floor	6	15-Apr-26	22-Apr-26
CON-3110	Install IPDVS Equipment Rack - 4th Floor IDF Room	5	20-Apr-26	24-Apr-26
CON-3280	Install Wiring Devices -4th Floor	7	24-Apr-26	04-May-26
CON-5580	Install Lighting Fixtures -4th Floor	6	08-Jul-26	15-Jul-26
CON-5660	Install Fire alarm Sensors and Devises -4th Floor	7	20-Jul-26	28-Jul-26
CON-5750	Install IPDVS Devices -4th Floor	9	30-Jul-26	11-Aug-26
Architecture-4th Floor		114	03-Mar-26	12-Aug-26
Interior Walls		86	03-Mar-26	02-Jul-26
CON-1670	Layout -4th Floor	3	03-Mar-26	05-Mar-26
CON-1910	Install Top & Bottom Track-4th Floor	4	10-Mar-26	13-Mar-26
CON-1920	Install CMU Walls -4th Floor	3	10-Mar-26	12-Mar-26
CON-2010	Install Wall Steel Studs & Framing-4th Floor	5	16-Mar-26	20-Mar-26
CON-9090	In-Wall Inspection -4th Floor	7	28-Apr-26	06-May-26
CON-4620	Install Gypsum Board Walls-4th Floor	5	10-Jun-26	16-Jun-26
CON-4720	Tape Gypsum Board -4th Floor	4	11-Jun-26	16-Jun-26
CON-5010	Install Firestopping-4th Floor	4	16-Jun-26	22-Jun-26
CON-4800	Install Ceramic Wall Tiles at Corridor-4th Floor	7	24-Jun-26	02-Jul-26
Ceiling		92	26-Mar-26	05-Aug-26
CON-2550	Install Ceiling Hangers & Supports-4th Floor	4	26-Mar-26	31-Mar-26
CON-4820	Install Gypsum Board Ceiling-4th Floor	6	22-Jun-26	29-Jun-26
CON-5520	Install Acoustical Ceiling Tiles-4th Floor	5	30-Jul-26	05-Aug-26
Finishes		32	29-Jun-26	12-Aug-26
CON-5340	Install First Coat Painting-4th Floor	5	29-Jun-26	06-Jul-26
CON-5540	Install Door Frames & Doors-4th Floor	5	07-Jul-26	13-Jul-26
CON-98817	Install Intrusion System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-98867	Install Auxiliary System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-98917	Install Sound Clock System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-5690	Install Flooring Tiles-4th Floor	5	14-Jul-26	20-Jul-26
CON-5900	Install Final Coat Painting-4th Floor	6	22-Jul-26	29-Jul-26
CON-6070	Install Furniture & Milling Work (Contractor Provided & Installed) -4th Floor	5	30-Jul-26	05-Aug-26
CON-9050	Install Furniture & Milling Work (Owner Provided & Installed) -4th Floor	5	30-Jul-26	05-Aug-26
CON-6160	Install Signages-4th Floor	5	06-Aug-26	12-Aug-26
Fifth Floor		140	13-Feb-26	02-Sep-26
Structure-5th Floor		32	18-Feb-26	02-Apr-26
CON-1380	Install Metal Deck Slab - 5th Floor	3	18-Feb-26	20-Feb-26

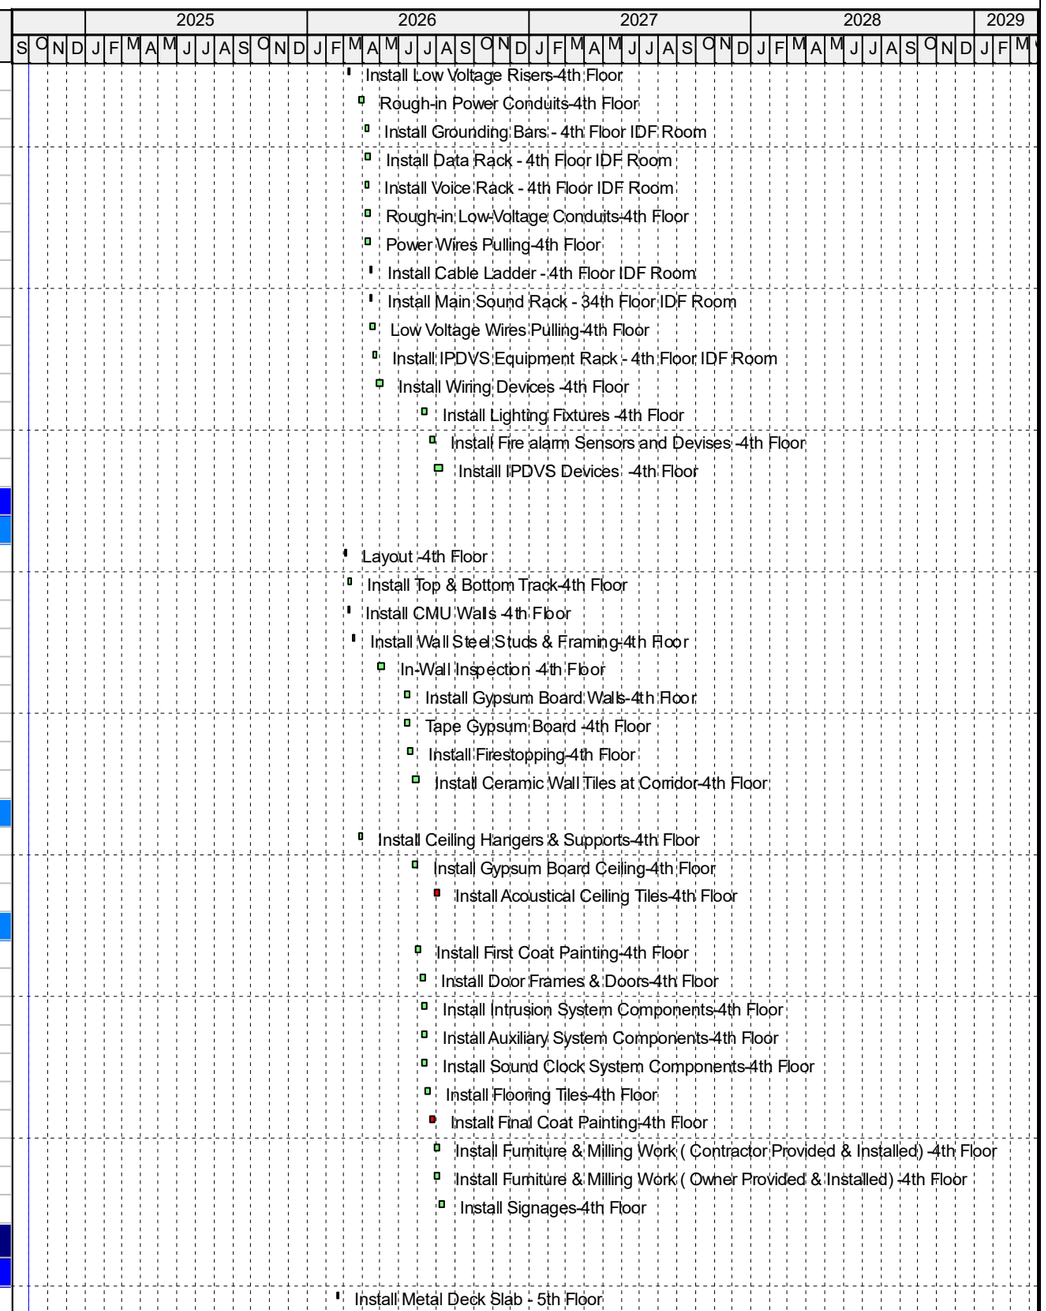

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1440	Install Steel Columns - 5th Floor	3	23-Feb-26	25-Feb-26
CON-1460	F/R/P Piers - 5th Floor	5	23-Feb-26	27-Feb-26
CON-1540	Install Trusses - 5th Floor	2	26-Feb-26	27-Feb-26
CON-1550	Install Framing Beams - 5th Floor	3	26-Feb-26	02-Mar-26
CON-99317	Install Steel Stairs - 5th Floor	3	27-Feb-26	03-Mar-26
CON-1730	Spray Fireproofing - 5th Floor	3	31-Mar-26	02-Apr-26
Mechanical-5th Floor		116	27-Feb-26	12-Aug-26
HVAC Rough-ins		81	27-Feb-26	23-Jun-26
CON-1610	Install MEP Hangers & Sleeves-Roof Floor	4	27-Feb-26	04-Mar-26
CON-1630	Install Duct Risers-5th Floor	2	02-Mar-26	03-Mar-26
CON-1790	Install Mechanical Piping Risers-5th Floor	2	04-Mar-26	05-Mar-26
CON-1810	Duct Leak Test -5th Floor	1	04-Mar-26	04-Mar-26
CON-2300	Rough-in Duct Work-5th Floor	5	16-Mar-26	20-Mar-26
CON-2470	Rough-in Refrigerant Piping-5th Floor	7	23-Mar-26	31-Mar-26
CON-2440	Rough-in Hot Water Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-2450	Rough-in Hot Glycol Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-2460	Rough-in Chilled Glycol Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-4330	Install VAV Boxes & Sound Attenuator Devices-5th Floor	5	09-Apr-26	15-Apr-26
CON-4710	Install Duct Insulation -5th Floor	8	11-Jun-26	23-Jun-26
Mechanical Equipment		67	07-May-26	12-Aug-26
CON-3640	Install Electric Unit Heaters -5th Floor	3	07-May-26	11-May-26
CON-5770	Install Air Cooled Condensing Unit ACCU - Mechanical Work - 5th Floor	5	08-Jul-26	14-Jul-26
CON-5430	Install Hot Glycol / Hot Water Cabinet Heater (CUH)-5th Floor	4	29-Jul-26	03-Aug-26
CON-5590	Install Exhaust Fan EF - Mechanical Work - 5th Floor	4	04-Aug-26	07-Aug-26
CON-5630	Install Convector Heater CV - Mechanical Work - 5th Floor	3	10-Aug-26	12-Aug-26
Plumbing-5th Floor		125	13-Feb-26	12-Aug-26
CON-3610	Install Floor Drains & Clean-outs -5th Floor	5	13-Feb-26	20-Feb-26
CON-1940	Install Plumbing Risers-5th Floor	1	06-Mar-26	06-Mar-26
CON-2000	Install SSDS Risers -SSDS System -5th Floor	1	09-Mar-26	09-Mar-26
CON-3050	Rough-in Gas Risers & Piping -5th Floor	4	22-Apr-26	27-Apr-26
CON-3190	Rough-in Domestic Water Piping -5th Floor	4	28-Apr-26	01-May-26
CON-3340	Rough-in Sanitary & Vent Piping -5th Floor	4	04-May-26	07-May-26
CON-3400	Install Hot Water Circulation Pump -5th Floor	5	04-May-26	08-May-26
CON-3410	Install Electric Hot Water Heater (EWH-1) -5th Floor	5	04-May-26	08-May-26
CON-3540	Rough-in Storm Piping -5th Floor	4	08-May-26	13-May-26
CON-3590	Plumbing Pressure Testing -5th Floor	5	14-May-26	20-May-26
CON-4530	Plumbing Piping Insulation -5th Floor	5	29-May-26	04-Jun-26
CON-6090	Install Plumbing Fixtures -5th Floor	7	04-Aug-26	12-Aug-26
Fire Protection-5th Floor		22	20-May-26	22-Jun-26
CON-3770	Install 4" Standpipe -5th Floor	4	20-May-26	26-May-26
CON-4010	Rough-in Main Sprinkler Piping -5th Floor	5	01-Jun-26	05-Jun-26
CON-4230	Rough-in Branch Sprinkler Piping -5th Floor	5	08-Jun-26	12-Jun-26
CON-4240	Rough-in Sprinkler Heads -5th Floor	5	08-Jun-26	12-Jun-26
CON-4340	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -5th Floor	5	08-Jun-26	12-Jun-26

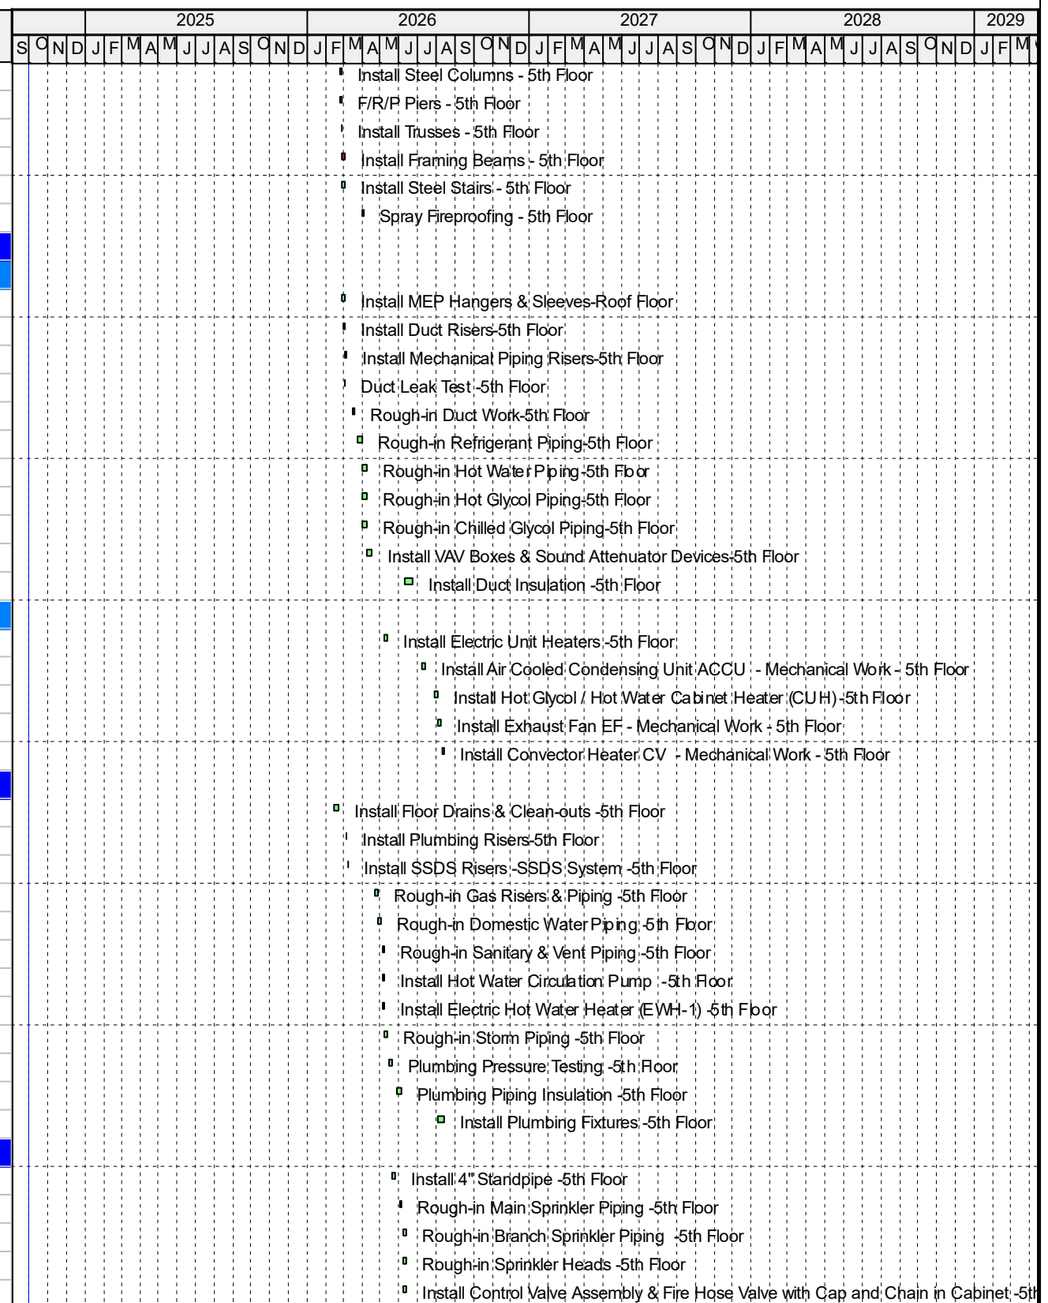

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
CON-4490	Sprinklers Air Testing-5th Floor	5	15-Jun-26	22-Jun-26
Electrical-5th Floor		117	10-Mar-26	24-Aug-26
CON-2050	Install Power Risers-5th Floor	3	10-Mar-26	12-Mar-26
CON-2100	Install Low Voltage Risers-5th Floor	3	13-Mar-26	17-Mar-26
CON-99337	Install Lightning Protection system -5th Floor	3	13-Mar-26	17-Mar-26
CON-2680	Rough-in Power Conduits -5th Floor	6	06-Apr-26	13-Apr-26
CON-2950	Rough-in Low-Voltage Conduits-5th Floor	6	14-Apr-26	21-Apr-26
CON-2960	Power Wires Pulling-5th Floor	6	14-Apr-26	21-Apr-26
CON-3290	Low Voltage Wires Pulling-5th Floor	6	23-Apr-26	30-Apr-26
CON-3660	Install Wiring Devices -5th Floor	8	05-May-26	14-May-26
CON-5740	Install Lighting Fixtures -5th Floor	6	16-Jul-26	23-Jul-26
CON-5830	Install Fire alarm Sensors and Devises -5th Floor	5	29-Jul-26	04-Aug-26
CON-6010	Install IPDVS Devices -5th Floor	9	12-Aug-26	24-Aug-26
Architecture-5th Floor		126	06-Mar-26	02-Sep-26
Interior Walls		90	06-Mar-26	14-Jul-26
CON-1930	Layout -5th Floor	3	06-Mar-26	10-Mar-26
CON-2030	Install CMU Walls -5th Floor	3	13-Mar-26	17-Mar-26
CON-2020	Install Top & Bottom Track-5th Floor	4	16-Mar-26	19-Mar-26
CON-2200	Install Wall Steel Studs & Framing-5th Floor	5	23-Mar-26	27-Mar-26
CON-9100	In-Wall Inspections -5th Floor	7	04-May-26	12-May-26
CON-4810	Install Gypsum Board Walls-5th Floor	5	17-Jun-26	24-Jun-26
CON-4970	Tape Gypsum Board -5th Floor	4	18-Jun-26	24-Jun-26
CON-5220	Install Firestopping-5th Floor	4	23-Jun-26	26-Jun-26
CON-5080	Install Ceramic Wall Tiles at Corridor-5th Floor	7	06-Jul-26	14-Jul-26
Ceiling		93	01-Apr-26	12-Aug-26
CON-2620	Install Ceiling Hangers & Supports-5th Floor	4	01-Apr-26	06-Apr-26
CON-5100	Install Gypsum Board Ceiling-5th Floor	6	30-Jun-26	08-Jul-26
CON-5670	Install Acoustical Ceiling Tiles-5th Floor	5	06-Aug-26	12-Aug-26
Finishes		40	09-Jul-26	02-Sep-26
CON-5530	Install First Coat Painting -5th Floor	5	09-Jul-26	15-Jul-26
CON-5680	Install Door Frames & Doors -5th Floor	5	16-Jul-26	22-Jul-26
CON-98827	Install Intrusion System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-98877	Install Auxiliary System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-98927	Install Sound Clock System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-5890	Install Flooring Tiles -5th Floor	5	23-Jul-26	29-Jul-26
CON-6060	Install Final Coat Painting -5th Floor	6	13-Aug-26	20-Aug-26
CON-6150	Install Furniture & Milling Work (Contractor Provided & Installed) -5th Floor	4	21-Aug-26	26-Aug-26
CON-9060	Install Furniture & Milling Work (Owner Provided & Installed) -5th Floor	4	21-Aug-26	26-Aug-26
CON-6280	Install Signages- 5th Floor	5	27-Aug-26	02-Sep-26
Roof Floor		106	26-Feb-26	28-Jul-26
Structure -Roof		11	02-Mar-26	16-Mar-26
CON-1620	Install Dunnage - 5th Floor	8	02-Mar-26	11-Mar-26
CON-1720	Install Metal Deck Slab -Roof Floor	2	03-Mar-26	04-Mar-26
CON-1760	Install Dunnage-Roof Floor	8	05-Mar-26	16-Mar-26

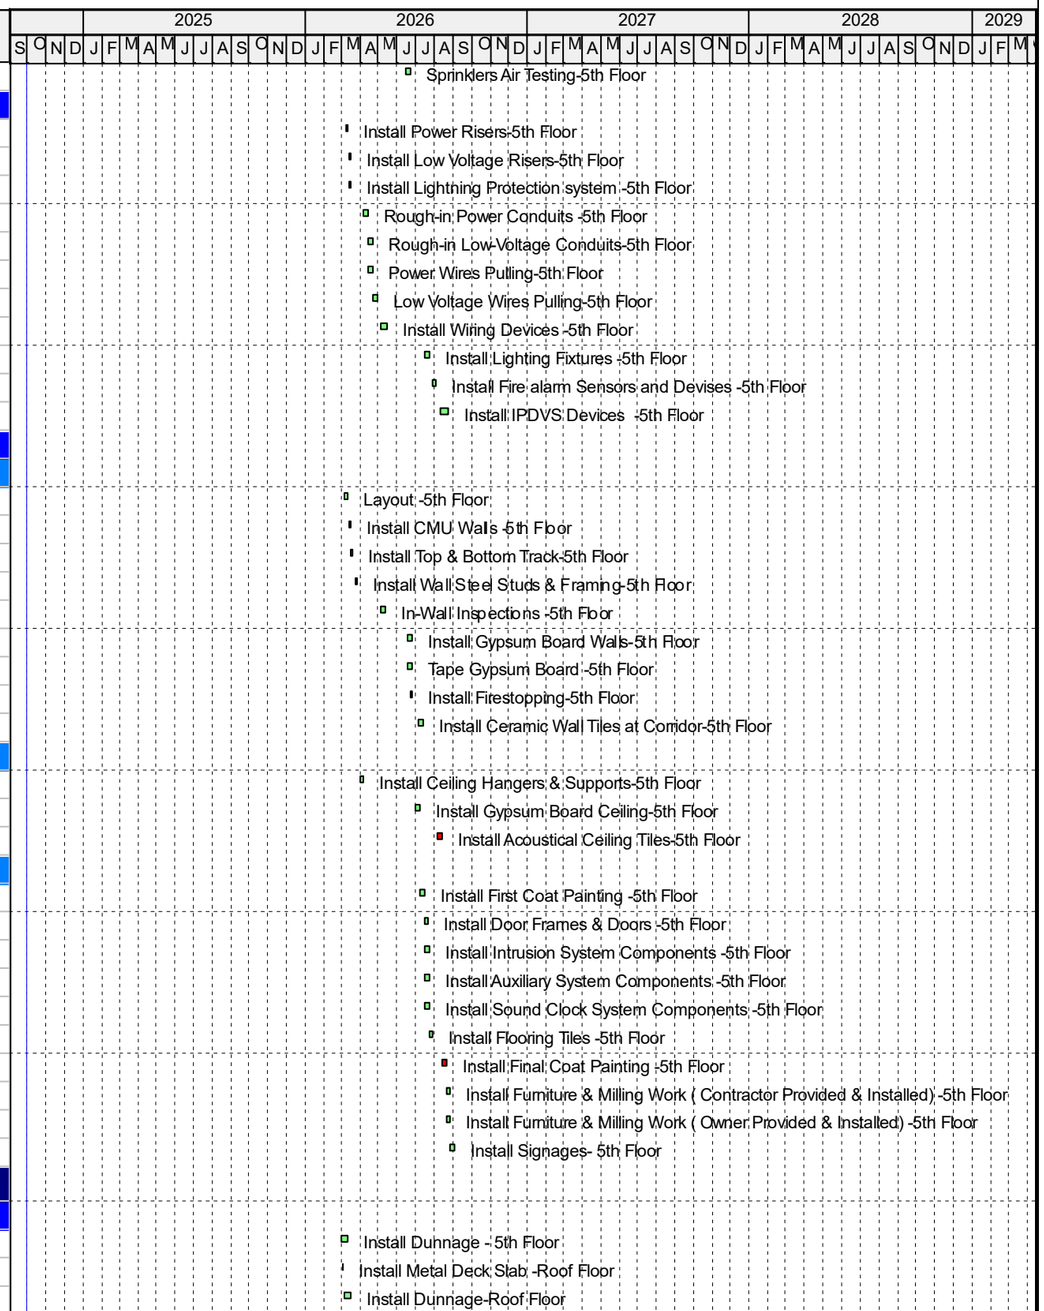

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
Mechanical -Roof		97	26-Feb-26	15-Jul-26
CON-1770	Install Roof Drains & Clean outs -Roof Floor	5	26-Feb-26	04-Mar-26
CON-2250	Install Air Handling Unit AHU-1 -Roof Floor	5	08-Jun-26	12-Jun-26
CON-2560	Install Air Handling Unit AHU-3 -Roof Floor	5	23-Jun-26	29-Jun-26
CON-2720	Install Air Handling Unit AHU-4 -Roof Floor	5	30-Jun-26	07-Jul-26
CON-2860	Install Fume Hood Exhaust -Roof Floor	3	08-Jul-26	10-Jul-26
CON-3000	Install Smoke Purge Fan -Roof Floor	3	13-Jul-26	15-Jul-26
Electrical -Roof		101	05-Mar-26	28-Jul-26
CON-99347	Install Lightning Protection System - Roof Floor	6	05-Mar-26	12-Mar-26
CON-3750	Install Emergency Generator- Roof Floor	4	17-Jul-26	22-Jul-26
CON-5380	Install Generator Connections -Roof Floor	4	23-Jul-26	28-Jul-26
Fire Protection -Roof		23	27-May-26	29-Jun-26
CON-3890	Install 4" Standpipe -Roof	4	27-May-26	01-Jun-26
CON-4250	Rough-in Main Sprinkler Piping -Roof	5	08-Jun-26	12-Jun-26
CON-4430	Rough-in Branch Sprinkler Piping -Roof	5	15-Jun-26	22-Jun-26
CON-4440	Rough-in Sprinkler Heads -Roof	5	15-Jun-26	22-Jun-26
CON-4650	Install 3 Way Roof Manifold -Roof	5	23-Jun-26	29-Jun-26
Bulkhead		76	05-Mar-26	22-Jun-26
Structure -Bulkhead		6	05-Mar-26	12-Mar-26
CON-1750	F/R/P Concrete Columns -Bulkhead	3	05-Mar-26	09-Mar-26
CON-1980	F/R/P Bulkhead Slab -Bulkhead	2	10-Mar-26	11-Mar-26
CON-2060	Install Hoist Beam-Bulkhead	1	12-Mar-26	12-Mar-26
Mechanical -Bulkhead		76	05-Mar-26	22-Jun-26
CON-2070	Install Roof Drains & Clean outs - Mechanical Work - Roof Bulkhead	5	05-Mar-26	11-Mar-26
CON-2190	Install Electric Unit Heater EUH - Mechanical Work - Roof Bulkhead	5	12-Mar-26	18-Mar-26
CON-2120	Install Air Cooled Chiller CH-1 -Roof Floor	7	17-Mar-26	25-Mar-26
CON-2230	Install Emergency Generator -Bulkhead	7	19-Mar-26	27-Mar-26
CON-2350	Install Air Cooled Chiller CH-2 -Roof Floor	7	26-Mar-26	03-Apr-26
CON-2360	Install Smoke Purge Fan SPF - Mechanical Work - Roof Bulkhead	3	26-Mar-26	30-Mar-26
CON-2430	Install Air Handling Unit AHU-2 -Roof Floor	5	15-Jun-26	22-Jun-26
Elevations		44	05-Mar-26	05-May-26
West Elevation		27	05-Mar-26	10-Apr-26
CON-1830	Install Insulated Precast Concrete Sandwich Panel - Mock Up	2	05-Mar-26	06-Mar-26
CON-1990	Approve Insulated Precast Concrete Sandwich Panel - Mock Up	2	09-Mar-26	10-Mar-26
CON-2110	Install & Windows Mock-Up	3	11-Mar-26	13-Mar-26
CON-2210	Approve Windows Mock-Up	2	16-Mar-26	17-Mar-26
CON-2220	Install Storefront System Mock-Up	3	18-Mar-26	20-Mar-26
CON-2240	Approve Storefront System Mock-Up	2	23-Mar-26	24-Mar-26
CON-2380	Install Insulated Precast Concrete Sandwich Panel - West Elevation	3	25-Mar-26	27-Mar-26
CON-2400	Install Windows -West Elevation	5	30-Mar-26	03-Apr-26
CON-2410	Install Storefront System-West Elevation	5	30-Mar-26	03-Apr-26
MIL-1740	Start Windows	0	30-Mar-26	
CON-2570	Field Testing of Windows (5%)	5	06-Apr-26	10-Apr-26
South Elevation		27	25-Mar-26	30-Apr-26

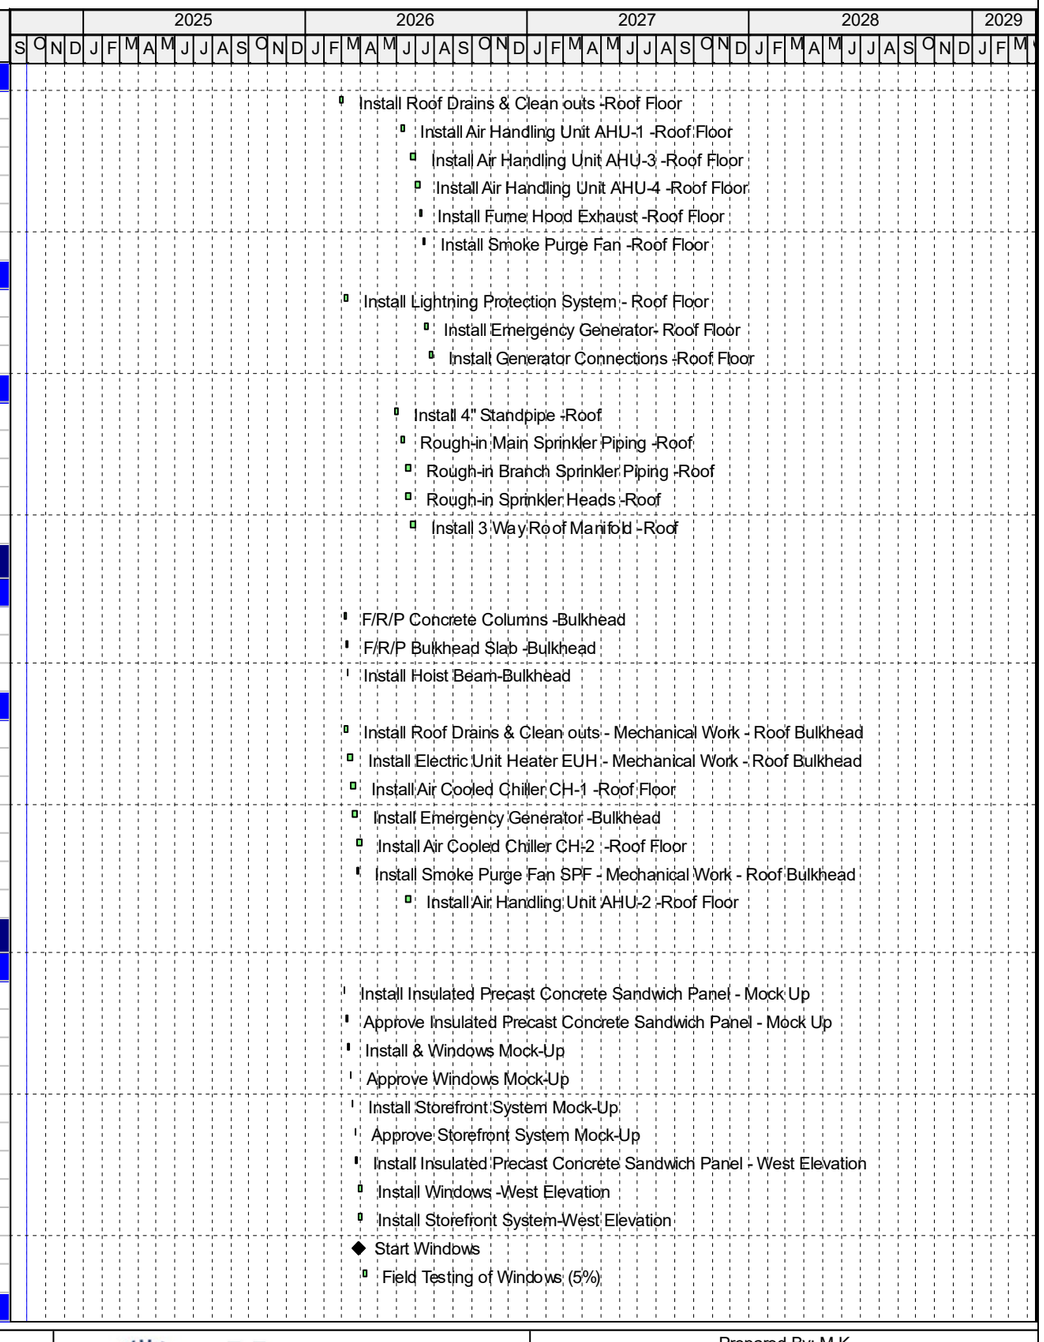

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2420	Install Insulated Precast Concrete Sandwich Panel - South Elevation	5	25-Mar-26	31-Mar-26
CON-2590	Install Windows - South Elevation	10	01-Apr-26	14-Apr-26
CON-2600	Install Storefront System- South Elevation	10	01-Apr-26	14-Apr-26
CON-2970	Field Testing of Windows (50%)	5	15-Apr-26	21-Apr-26
CON-99237	Install Flag Pole - South Elevation	10	15-Apr-26	28-Apr-26
CON-3220	Dismantle Sidewalk Sheds- South Elevation	2	29-Apr-26	30-Apr-26
East Elevation		25	01-Apr-26	05-May-26
CON-2610	Install Insulated Precast Concrete Sandwich Panel - East Elevation	4	01-Apr-26	06-Apr-26
CON-2980	Install Windows - East Elevation	8	15-Apr-26	24-Apr-26
CON-2990	Install Storefront System- East Elevation	8	15-Apr-26	24-Apr-26
CON-3370	Field Testing of Windows (90%)	5	27-Apr-26	01-May-26
CON-3630	Dismantle Sidewalk Sheds- East Elevation	2	04-May-26	05-May-26
North Elevation		25	01-Apr-26	05-May-26
CON-2730	Install Insulated Precast Concrete Sandwich Panel - North Elevation	4	01-Apr-26	06-Apr-26
CON-3380	Install Windows -North Elevation	10	15-Apr-26	28-Apr-26
CON-3390	Install Storefront System-North Elevation	10	15-Apr-26	28-Apr-26
MIL-1730	Sidewalk Sheds Dismantle Complete	0		05-May-26
Roofing		29	07-Apr-26	15-May-26
5th Floor		27	07-Apr-26	13-May-26
CON-2920	Pour Sloped Concrete Fill -5th Floor Roof	2	07-Apr-26	08-Apr-26
CON-3210	Install Fluid-Applied Protected Membrane Mock-Up	2	13-Apr-26	14-Apr-26
CON-3300	Approve Fluid-Applied Protected Membrane Mock-Up	4	15-Apr-26	20-Apr-26
CON-3440	Install Hot Fluid Applied Membrane -5th Floor Roof	4	21-Apr-26	24-Apr-26
CON-3580	Install 6" Thick Rigid Insulation -5th Floor Roof	3	27-Apr-26	29-Apr-26
CON-3700	Install Drainage -5th Floor Roof	3	30-Apr-26	04-May-26
CON-3710	Roof Flood Test -5th Floor Roof	4	30-Apr-26	05-May-26
CON-3820	Install Filter Fabric -5th Floor Roof	3	06-May-26	08-May-26
CON-3960	Install Concrete Pavers -5th Floor Roof	3	11-May-26	13-May-26
Main Roof		27	09-Apr-26	15-May-26
CON-3010	Pour Sloped Concrete Fill -Roof Floor	2	09-Apr-26	10-Apr-26
CON-3430	Install Hot Fluid Applied Membrane -Roof Floor	3	21-Apr-26	23-Apr-26
CON-3600	Install Drainage Panels- Roof Floor	3	24-Apr-26	28-Apr-26
CON-3730	Install 6" Thick Rigid Insulation -Roof Floor	3	29-Apr-26	01-May-26
CON-3840	Roof Flood Test -Roof Floor	3	04-May-26	06-May-26
CON-4020	Install Filter Fabric -Roof Floor	3	07-May-26	11-May-26
CON-4210	Install Concrete Pavers -Roof Floor	4	12-May-26	15-May-26
Special Rooms		94	23-Apr-26	04-Sep-26
Fuel Oil Room-1st Floor		10	01-Jun-26	12-Jun-26
CON-4890	F/R/P Concrete Pads -Fuel Oil Room	2	01-Jun-26	02-Jun-26
CON-4900	Rough-in Fuel Oil Piping -Fuel Oil Room	3	01-Jun-26	03-Jun-26
CON-4990	Install Fuel Oil Storage Tank (FOT-1) - Fuel Oil Room	3	03-Jun-26	05-Jun-26
CON-5020	Rough-in Fuel Oil Fill Piping -Fuel Oil Room	3	04-Jun-26	08-Jun-26
CON-5160	Install Fuel Oil Transfer Duplex Pump (FOP-1 & 2) -1st Floor	4	08-Jun-26	11-Jun-26
CON-5200	Rough-in Fuel Oil Vent Piping -Fuel Oil Room	4	09-Jun-26	12-Jun-26

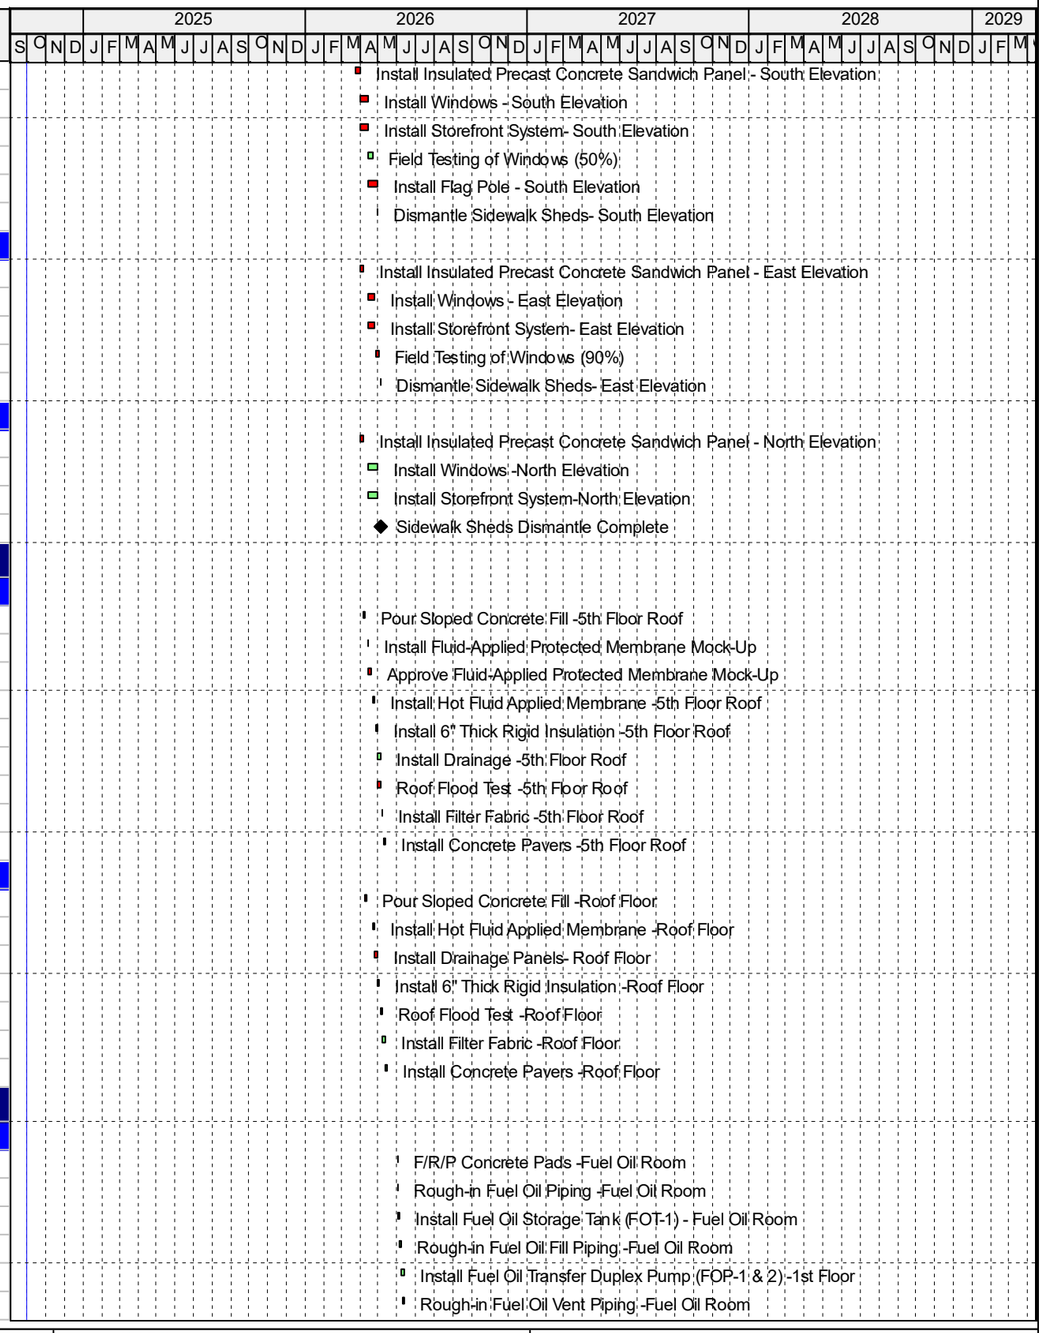

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
Electrical Service Room -1st Floor		37	23-Apr-26	15-Jun-26
CON-4730	Rough-in Conduits & Wires - Electric Service Room	6	23-Apr-26	30-Apr-26
CON-4960	F/R/P Concrete Pad - Electric Service Room	6	01-May-26	08-May-26
CON-5180	Install Service Switchboard "SS-A"- Electric Service Room	5	11-May-26	15-May-26
CON-5510	Install Leak Detector - Electric Service Room	3	18-May-26	20-May-26
CON-5610	Install Sprinkler Booster Pump - Electric Service Room	4	21-May-26	27-May-26
CON-5640	Install Fire Alarm Normal ATS - Electric Service Room	4	28-May-26	02-Jun-26
CON-5780	Install Motorized Fire/Smoke Damper & Control Panel - Electric Service Room	5	03-Jun-26	09-Jun-26
CON-5790	Install Main Grounding Bus Bar - Electric Service Room	4	03-Jun-26	08-Jun-26
CON-9130	Install Switch Gear - Electric Service Room	5	08-Jun-26	12-Jun-26
CON-5840	Install Electric Unit Heater EUH-6 - Electric Service Room	4	10-Jun-26	15-Jun-26
MDF Room 127A -1st Floor		53	29-Apr-26	15-Jul-26
CON-3740	Install Ground Bus Bar - 1st Floor MDF Room	6	29-Apr-26	06-May-26
CON-4110	Install Voice Rack - 1st Floor MDF Room	6	07-May-26	14-May-26
CON-4510	Install Sound Rack - 1st Floor MDF Room	6	15-May-26	22-May-26
CON-4120	Install Project Connect Cabinet - 1st Floor MDF Room	8	15-May-26	27-May-26
CON-4520	Install Data Rack - 1st Floor MDF Room	6	26-May-26	02-Jun-26
CON-4550	Install UPS- 1st Floor MDF Room	9	03-Jun-26	15-Jun-26
CON-4130	Install BACnet Data Cabinet- 1st Floor MDF Room	9	03-Jun-26	15-Jun-26
CON-4780	Install IPDVS Equipment Rack - 1st Floor MDF Room	6	16-Jun-26	24-Jun-26
CON-4790	Install Ladder Rack Cable Tray- 1st Floor MDF Room	6	25-Jun-26	02-Jul-26
CON-4770	Install PBX - 1st Floor MDF Room	8	06-Jul-26	15-Jul-26
Gymatorium - 4th Floor		39	14-Jul-26	04-Sep-26
CON-5760	Install Wood Floating Floor System -Gymnatorium	10	14-Jul-26	27-Jul-26
CON-5810	Install Wall Pads - Gymnatorium	4	28-Jul-26	31-Jul-26
CON-5970	Install Retractable Basketball Goal Assembly -Gymnatorium	3	03-Aug-26	05-Aug-26
CON-6020	Install 8" Acoustic Block Painted-Gymnatorium	7	06-Aug-26	14-Aug-26
CON-99217	Install Bleachers -Gymnatorium	3	12-Aug-26	14-Aug-26
CON-6230	Install Gym Equipment -Gymnatorium -Gymnatorium	6	17-Aug-26	24-Aug-26
CON-6240	Install Fine Tube Radiator FTR - Gymnatorium	5	17-Aug-26	21-Aug-26
CON-6250	Install Hydraulic Vertical Wheelchair Lift -Gymnatorium	8	17-Aug-26	26-Aug-26
CON-9150	Install LED Theatrical Lighting -Gymnatorium	4	25-Aug-26	28-Aug-26
CON-6390	Install Auditorium Television Studio Dimming System -Gymnatorium	7	27-Aug-26	04-Sep-26
Boiler Room - 5th Floor		26	15-Jul-26	19-Aug-26
CON-5960	F/R/P Concert Pad -Boiler Room	3	15-Jul-26	17-Jul-26
CON-6000	Rough-in Conduits & Wires-Boiler Room	3	20-Jul-26	22-Jul-26
CON-6050	Install Boiler B-1-Boiler Room	5	23-Jul-26	29-Jul-26
CON-6110	Install Boiler B-2-Boiler Room	5	30-Jul-26	05-Aug-26
CON-6120	Install Air Separator Units (AS-1 , AS-2 & AS-3)	2	30-Jul-26	31-Jul-26
CON-6130	Install Boiler Condensate ACID Neutralization Tubes -Boiler Room	2	30-Jul-26	31-Jul-26
CON-6200	Install Expansion Tanks (ET-1 , ET-2 & ET-3)	2	03-Aug-26	04-Aug-26
CON-6210	Install Glycol Make-up Units (GF-1 & GF-2 & GF-3)	2	03-Aug-26	04-Aug-26
CON-6220	Install Reduced Pressure Zone (RPZ) Devices -Boiler Room	2	03-Aug-26	04-Aug-26
CON-6260	Install Heat Exchanger -Boiler Room	2	06-Aug-26	07-Aug-26

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
CON-6290	Install Hot Glycol Units Heaters (UH-5-1, UH-5-2)	2	10-Aug-26	11-Aug-26
CON-6330	Install Heat Pump Electric Hot Water Heater (HPWH#1&2)-Boiler Room	2	12-Aug-26	13-Aug-26
CON-6340	Install Exhaust Fans -Boiler Room	2	14-Aug-26	17-Aug-26
CON-6350	Install Primary Hot Water Pump (GHWP 1 to 3) -Boiler Room	2	14-Aug-26	17-Aug-26
CON-6360	Install Primary Chilled Water Pump (GCHWP-1&2)-Boiler Room	2	14-Aug-26	17-Aug-26
CON-6400	Install Secondary Hot Water Pump(HWP-1&2)-Boiler Room	2	18-Aug-26	19-Aug-26
CON-6410	Install Electric Unit Heater (EUH-3) - Boiler Room	2	18-Aug-26	19-Aug-26
CON-6420	Install Branch Panels (BRPP) -Boiler Room	2	18-Aug-26	19-Aug-26
Elevator Machine Room -Roof Floor		61	07-May-26	04-Aug-26
MIL-1760	Start Elevator Work	0	07-May-26	
CON-99357	Install CMU Wall for Shaft -Elevator Machine Room	10	07-May-26	20-May-26
CON-99167	Install Elevator Guide Rails -Elevator Machine Room	8	21-May-26	02-Jun-26
CON-2090	Install Elevator Controller #1 -Elevator Machine Room	10	03-Jun-26	16-Jun-26
CON-2370	Install Elevator Controller #2 -Elevator Machine Room	10	17-Jun-26	01-Jul-26
CON-2580	Install Power Panels -Elevator Machine Room	7	02-Jul-26	13-Jul-26
CON-2790	Rough-in Conduits & Wires-Elevator Machine Room	6	14-Jul-26	21-Jul-26
CON-99157	Install Elevator Sump Pump -Elevator Machine Room	10	14-Jul-26	27-Jul-26
CON-3100	Install Elevator Cabinet (1) -Elevator Machine Room	10	22-Jul-26	04-Aug-26
CON-3620	Install Elevator Cabinet (2) -Elevator Machine Room	10	22-Jul-26	04-Aug-26
Mockup Room		18	07-May-26	02-Jun-26
CON-4040	Install Walls GWB-Mockup Room	3	07-May-26	11-May-26
CON-4270	Install Gypsum Board Ceiling -Mockup Room	3	07-May-26	11-May-26
CON-4380	Install Doors & Hardware-Mockup Room	3	11-May-26	13-May-26
CON-4260	Install Door Frames-Mockup Room	2	12-May-26	13-May-26
CON-4480	Paint First coat -Mockup Room	2	14-May-26	15-May-26
CON-4640	Flooring Finishes-Mockup Room	2	18-May-26	19-May-26
CON-4750	Paint Second coat-Mockup Room	2	20-May-26	21-May-26
CON-4930	Install Furniture & Signs -Mockup Room	2	22-May-26	26-May-26
CON-5000	Mockup Room Inspection & Punchlist	5	27-May-26	02-Jun-26
Site Work		91	01-May-26	10-Sep-26
54th Avenue Street		34	01-May-26	18-Jun-26
CON-3780	Install Traffic Control Devices - 54th Avenue Street	3	01-May-26	05-May-26
CON-3850	Remove Existing Steel Faced Curb - 54th Avenue Street	3	06-May-26	08-May-26
CON-3860	Remove Existing Asphalt - 54th Avenue Street	4	06-May-26	11-May-26
CON-3940	Remove Existing Electrical Manhole - 54th Avenue Street	4	12-May-26	15-May-26
CON-4080	Install 5' Wide Silva Cells Under Concrete Pavement Strip - 54th Avenue Street	4	18-May-26	21-May-26
CON-4150	Pavement Replacement - 54th Avenue Street	4	22-May-26	28-May-26
CON-4290	Install New Steel Faced Curb - 54th Avenue Street	4	29-May-26	03-Jun-26
CON-4300	Install Pedestrian Ramps With Truncated Domes - 54th Avenue Street	4	29-May-26	03-Jun-26
CON-4400	Install 4" Concrete Sidewalk - 54th Avenue Street	5	04-Jun-26	10-Jun-26
CON-4410	Install 7" Concrete Sidewalk - 54th Avenue Street	5	04-Jun-26	10-Jun-26
CON-4560	Install Pavement Marking - 54th Avenue Street	3	11-Jun-26	15-Jun-26
CON-4580	Remove Traffic Control Devices - 54th Avenue Street	3	16-Jun-26	18-Jun-26
2ND Street		39	06-May-26	01-Jul-26

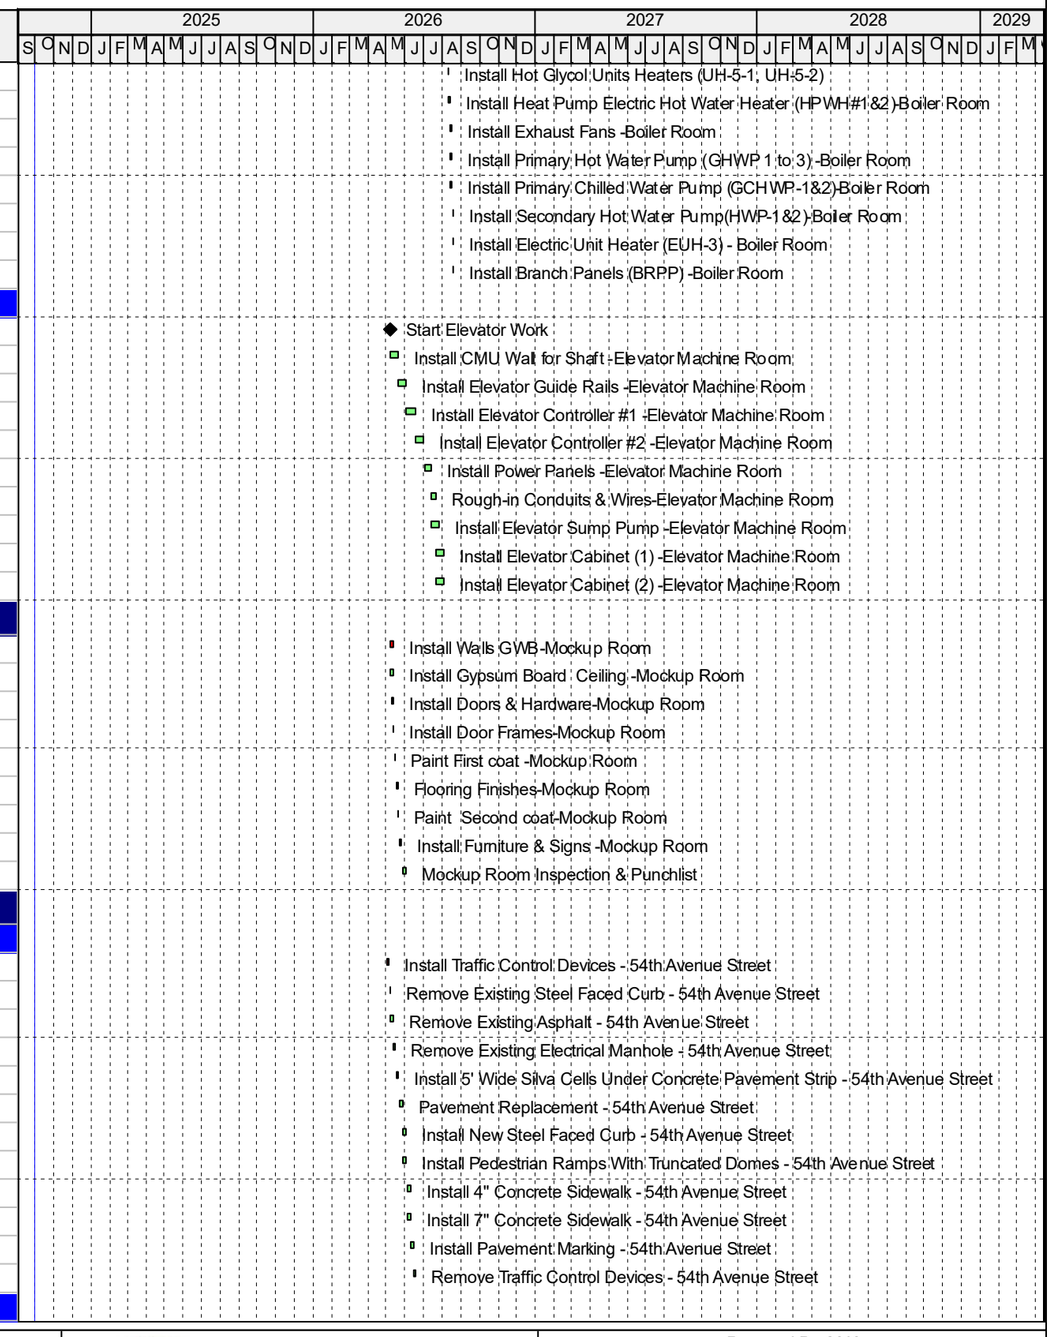

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3870	Install Traffic Control Devices - 2nd Street	5	06-May-26	12-May-26
CON-3900	Remove Existing Sidewalk - 2nd Street	5	13-May-26	19-May-26
CON-3950	Install Pedestrian Ramps With Truncated Domes - 2nd Street	6	20-May-26	28-May-26
CON-4090	Remove Existing Steel Faced Curb - 2nd Street	6	29-May-26	05-Jun-26
CON-4160	Install New Steel Faced Curb - 2nd Street	6	08-Jun-26	15-Jun-26
CON-4170	Install 4" Concrete Sidewalk - 2nd Street	7	08-Jun-26	16-Jun-26
CON-4310	Install 7" Concrete Sidewalk - 2nd Street	6	16-Jun-26	24-Jun-26
CON-4420	Remove Traffic Control Devices - 2nd Street	5	25-Jun-26	01-Jul-26
Perimeter of New Building		49	02-Jul-26	10-Sep-26
CON-4660	Excavation - Drainage Work - Building Perimeter	3	02-Jul-26	07-Jul-26
CON-4740	Install Flood Barrier Wall - Drainage Work - Building Perimeter	3	08-Jul-26	10-Jul-26
CON-4860	Install Drilled Caisson Supported Ventilation Structure - Drainage Work - Building Perimeter	3	13-Jul-26	15-Jul-26
CON-4980	Install 4" & 6" & 10" & 12" DIP - Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-9170	Install 8" Combined Water Service (2nd Street)- Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-9180	Install 6" Fire Water Service (54th Avenue Street)- Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-5190	Install Catch Basin - Drainage Work - Building Perimeter	2	21-Jul-26	22-Jul-26
CON-5290	Install Storm Inlet With Hood & Storm Hood - Drainage Work - Building Perimeter	2	23-Jul-26	24-Jul-26
CON-5400	Install Trench Drain - Drainage Work - Building Perimeter	1	27-Jul-26	27-Jul-26
CON-9160	Excavate for Footings - Playground Area & Fences - Building Perimeter	2	28-Jul-26	29-Jul-26
CON-9010	Remove Steel Plate Protection over NYPA Easement - Playground Area & Fences - Building Perimeter	1	28-Jul-26	28-Jul-26
CON-9190	F/R/P Playground Equipment Footings - Playground Area & Fences - Building Perimeter	2	30-Jul-26	31-Jul-26
CON-5470	Install Flush Concrete Curb - Playground Area & Fences - Building Perimeter	3	03-Aug-26	05-Aug-26
CON-5420	Install Asphalt Pavement - Playground Area & Fences - Building Perimeter	2	04-Aug-26	05-Aug-26
CON-5600	Install Concrete Pavement Pedestrian Ramp With Painted Black Handrails - Playground Area & Fences - Building Perimeter	3	06-Aug-26	10-Aug-26
CON-5650	Install Playground Rubber Tile Safety Surface - Playground Area & Fences - Building Perimeter	3	11-Aug-26	13-Aug-26
CON-5800	Install Painted Asphalt Pavement & Painted Games On Asphalt Surface - Playground Area & Fences - Building Perimeter	3	14-Aug-26	18-Aug-26
CON-5850	Install Colored Athletic Wearing Surface Color - Playground Area & Fences - Building Perimeter	2	19-Aug-26	20-Aug-26
CON-5990	Install Playground Equipment - Playground Area & Fences - Building Perimeter	7	21-Aug-26	31-Aug-26
CON-6140	Install Basketball Hoop - Playground Area & Fences - Building Perimeter	1	01-Sep-26	01-Sep-26
CON-6190	Install Wrought Iron Fence Double Gate - Playground Area - Building Perimeter	3	02-Sep-26	04-Sep-26
CON-6270	Install Chain Link Fence - Playground Area & Fences - Building Perimeter	3	08-Sep-26	10-Sep-26
Close-Outs		430	28-Oct-25	15-Aug-27
Inspections		192	28-Oct-25	04-Aug-26
I-1010	Concrete Cast-IN-Place Inspection	86	28-Oct-25	04-Mar-26
I-1140	Structural Steel Inspection	58	05-Dec-25	02-Mar-26
I-1080	Standpipe System Inspection	111	29-Dec-25	05-Jun-26
I-1020	Masonry Inspection	32	02-Mar-26	14-Apr-26
I-1100	Fire-Resistant Penetrations And Joints Inspection	87	03-Mar-26	06-Jul-26
I-1150	Concrete Precast Inspection	9	25-Mar-26	06-Apr-26
I-1120	Mechanical System Inspection	69	07-Apr-26	15-Jul-26
I-1040	Roofing Flood Testing Inspection	5	30-Apr-26	06-May-26
I-1130	Fire Alarm Inspection	47	28-May-26	04-Aug-26
I-1110	Fuel-Oil Storage & Fuel Oil Piping Systems Inspection	9	01-Jun-26	11-Jun-26
MIL-2992	Finish Fuel-Oil Storage & Fuel Oil Piping Systems Inspection	0		11-Jun-26

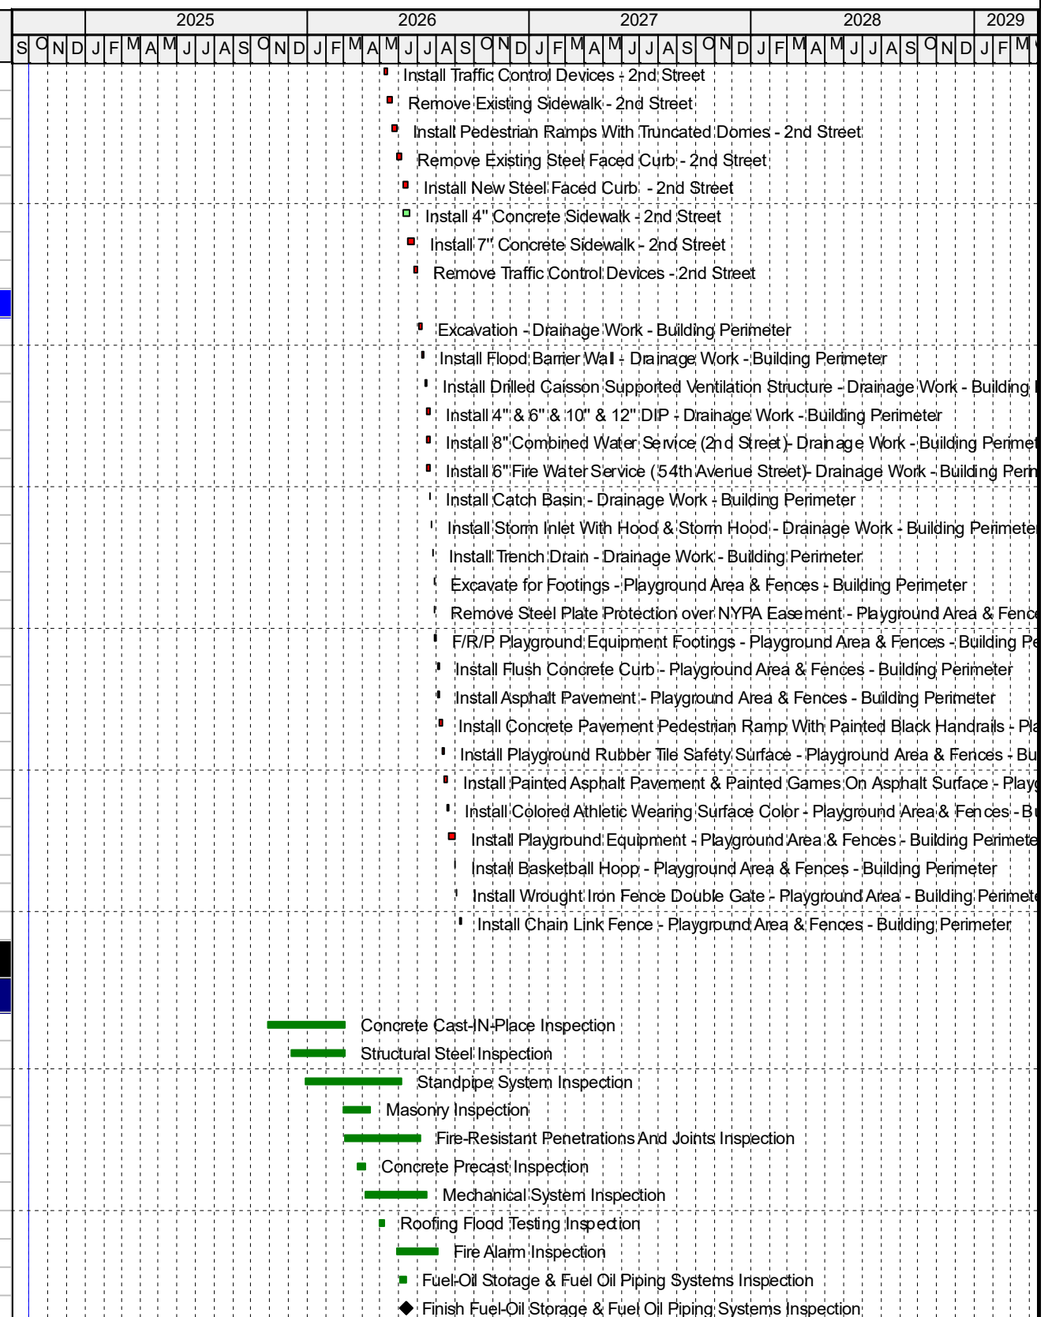

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

New Building PS/IS 341Q - Baseline Schedule Rev 01

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AA	

Full Schedule Layout Grouped by Phase

Activity ID	Activity Name	Original Duration	Start	Finish
Testing		62	06-Jul-26	30-Sep-26
CLO-1120	MDF & IDF Rooms Testing & Commissioning	12	06-Jul-26	21-Jul-26
CLO-1010	HVAC Flush-Out	20	07-Jul-26	03-Aug-26
CLO-1140	SSDS System Testing & Commissioning	7	16-Jul-26	24-Jul-26
CLO-1240	Elevator Sump Pump Testing & Commissioning	21	28-Jul-26	25-Aug-26
CLO-1270	Water Heater Testing & Commissioning	21	28-Jul-26	25-Aug-26
CLO-1220	Emergency Generator Electric Load Test	3	29-Jul-26	31-Jul-26
PER-2640	Obtain Emergency Generator Permit	5	03-Aug-26	07-Aug-26
CLO-1250	Emergency Generator Testing & Commissioning	21	03-Aug-26	31-Aug-26
CLO-1230	Air Handling Unit Testing & Commissioning	21	04-Aug-26	01-Sep-26
CLO-1190	Pre-Elevator Test Inspection	5	05-Aug-26	11-Aug-26
CLO-1290	Glycol System Testing & Commissioning	21	05-Aug-26	02-Sep-26
MIL-1680	Emergency Generator Final Sign-off	0		07-Aug-26
CLO-1020	Electrical System Testing & Commissioning	21	10-Aug-26	08-Sep-26
CLO-1260	HVAC Split System Testing & Commissioning	21	10-Aug-26	08-Sep-26
CLO-1280	Fire Alarm Testing & Commissioning	21	10-Aug-26	08-Sep-26
CLO-1000	Elevator Testing & Commissioning	20	12-Aug-26	09-Sep-26
CLO-1160	Sprinkler/Domestic Booster Pumps Testing & Commissioning	14	20-Aug-26	09-Sep-26
CLO-1130	IPDVS System Testing & Commissioning	11	03-Sep-26	18-Sep-26
CLO-1170	Sprinkler/Domestic Booster Pumps Inspection	3	10-Sep-26	14-Sep-26
CLO-1200	Elevator DOB Inspection	5	10-Sep-26	16-Sep-26
CLO-1180	Sprinkler/Domestic Booster Pumps Sign-offs	0		14-Sep-26
CLO-1150	FDNY Inspection	12	15-Sep-26	30-Sep-26
PER-2650	Elevator Equipment Use Permit	10	17-Sep-26	30-Sep-26
MIL-1650	FDNY Inspection Finish	0		30-Sep-26
MIL-1670	Elevator Final Sign-off	0		30-Sep-26
TCO		214	09-Sep-26	15-Aug-27
CLO-1300	Provide Training	10	09-Sep-26	22-Sep-26
CLO-1030	Pre-Final Clean-Out	5	11-Sep-26	17-Sep-26
CLO-1040	Pre-TCO Inspection	11	18-Sep-26	02-Oct-26
CLO-1110	Pre-TCO Punchlist	10	05-Oct-26	19-Oct-26
CLO-1050	Pre-Substantial Punchlist	105	20-Oct-26	17-Apr-27
CLO-1060	Prepare & Submit O&M Manuals	30	19-Apr-27	01-Jun-27
CLO-1070	Prepare & Submit As-Built Drawings	30	02-Jun-27	15-Jul-27
CLO-1080	Final Inspection	5	16-Jul-27	22-Jul-27
CLO-1090	Final Clean Out	10	23-Jul-27	05-Aug-27
CLO-1100	Demobilization	10	06-Aug-27	15-Aug-27

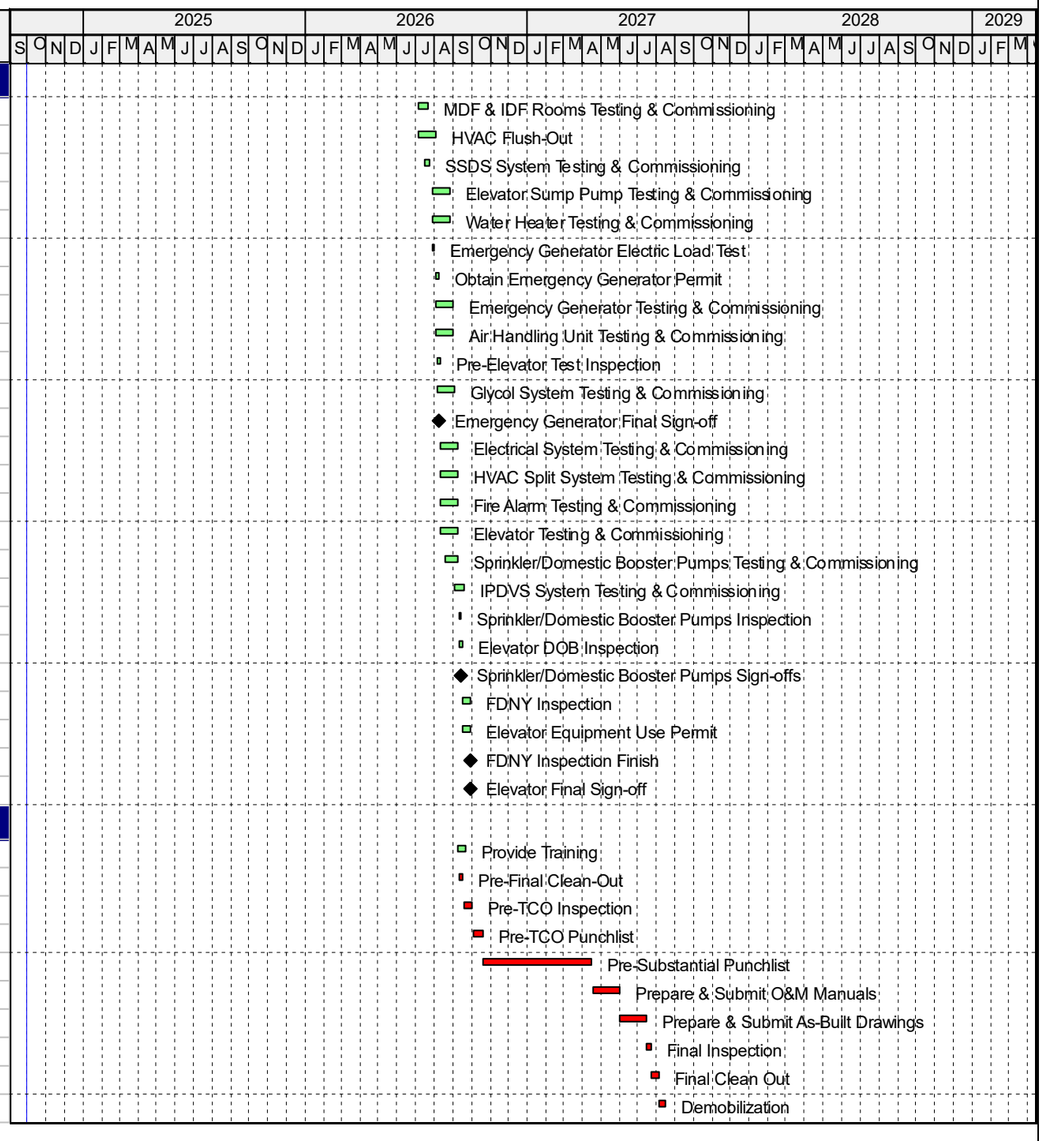

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

New Building PS/IS 341Q - Baseline Schedule Rev 01

NAVILLUS BUILDING THE WORLD AROUND YOU

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AA	

APPENDIX 6
Full Schedule Layout Grouped by Subcontractors Trades Code

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
General		699	30-Sep-24	15-Aug-27
MIL-1000	NTP	0	30-Sep-24	
MIL-1030	Project Duration(From NTP till TCO)	750	30-Sep-24	19-Oct-26
MIL-1040	Project Duration(From NTP till Substantial Completion)	930	30-Sep-24	17-Apr-27
MIL-1770	Project Duration(From NTP till Final Completion)	1050	30-Sep-24	15-Aug-27
MIL-2542	Complete Subcontractor 'Buyout'	0		11-Oct-24
MIL-2572	Place Steel Mill Order	0	20-Feb-25	
MIL-2762	Green Schools Compliance Submission	0		04-Mar-25
MIL-2532	Submit Complete Permit Application	0		29-Sep-25
MIL-2832	Issuance of Excavation & Shoring Permit	0		29-Sep-25
MIL-2842	Issuance of Builders Pavement Permit	0		29-Sep-25
MIL-2852	Issuance of Permit to Enter (PTE)	0		29-Sep-25
MIL-2862	Issuance of NYPA Permit	0		29-Sep-25
MIL-2872	Issuance of Construction Fences Permit	0		29-Sep-25
MIL-2882	Issuance of Sidewalk Shed Permits	0		29-Sep-25
MIL-2892	Issuance of CCD1	0		29-Sep-25
MIL-2902	Issuance of DOB Permit & Insurance	0		29-Sep-25
MIL-1850	Construction Start	0	30-Sep-25	
I-1010	Concrete Cast-IN-Place Inspection	86	28-Oct-25	04-Mar-26
MIL-2582	Start Concrete Placement	0	28-Oct-25	
MIL-2812	Start Foundation	0	28-Oct-25	
MIL-2912	Start Concrete Cast In Place Inspection	0	28-Oct-25	
I-1140	Structural Steel Inspection	58	05-Dec-25	02-Mar-26
I-1080	Standpipe System Inspection	111	29-Dec-25	05-Jun-26
MIL-2622	Deliveries of all owner-furnished equipment and/or materials	0		06-Feb-26
I-1020	Masonry Inspection	32	02-Mar-26	14-Apr-26
I-1100	Fire-Resistant Penetrations And Joints Inspection	87	03-Mar-26	06-Jul-26
MIL-1820	Crane Mobilization-Steel Installation Finish	0		12-Mar-26
MIL-2612	Start Suspended Ceiling Grid	0	16-Mar-26	
MIL-1380	Crane Mobilization-Mechanical Subcontractor	78	17-Mar-26	07-Jul-26
I-1150	Concrete Precast Inspection	9	25-Mar-26	06-Apr-26
MIL-2922	Start Pre -Cast Concrete Inspection	0	25-Mar-26	
I-1120	Mechanical System Inspection	69	07-Apr-26	15-Jul-26
MIL-2602	Start Mechanical Distribution Lines	0	08-Apr-26	
MIL-2712	Start Low Voltage	0	16-Apr-26	
I-1040	Roofing Flood Testing Inspection	5	30-Apr-26	06-May-26
I-1130	Fire Alarm Inspection	47	28-May-26	04-Aug-26
I-1110	Fuel-Oil Storage & Fuel Oil Piping Systems Inspection	9	01-Jun-26	11-Jun-26
MIL-2992	Finish Fuel-Oil Storage & Fuel Oil Piping Systems Inspection	0		11-Jun-26
MIL-2632	Finish HVAC	0		06-Jul-26
MIL-2982	Finish Fire-Resistant Penetrations And Joints Inspection	0		06-Jul-26
MIL-2732	Start Mechanical and Electrical System Commissioning	0	07-Jul-26	
MIL-2562	Start Below Grade Plumbing and Other Utilities	0	16-Jul-26	
MIL-2742	Permanent Power Available	0		27-Jul-26

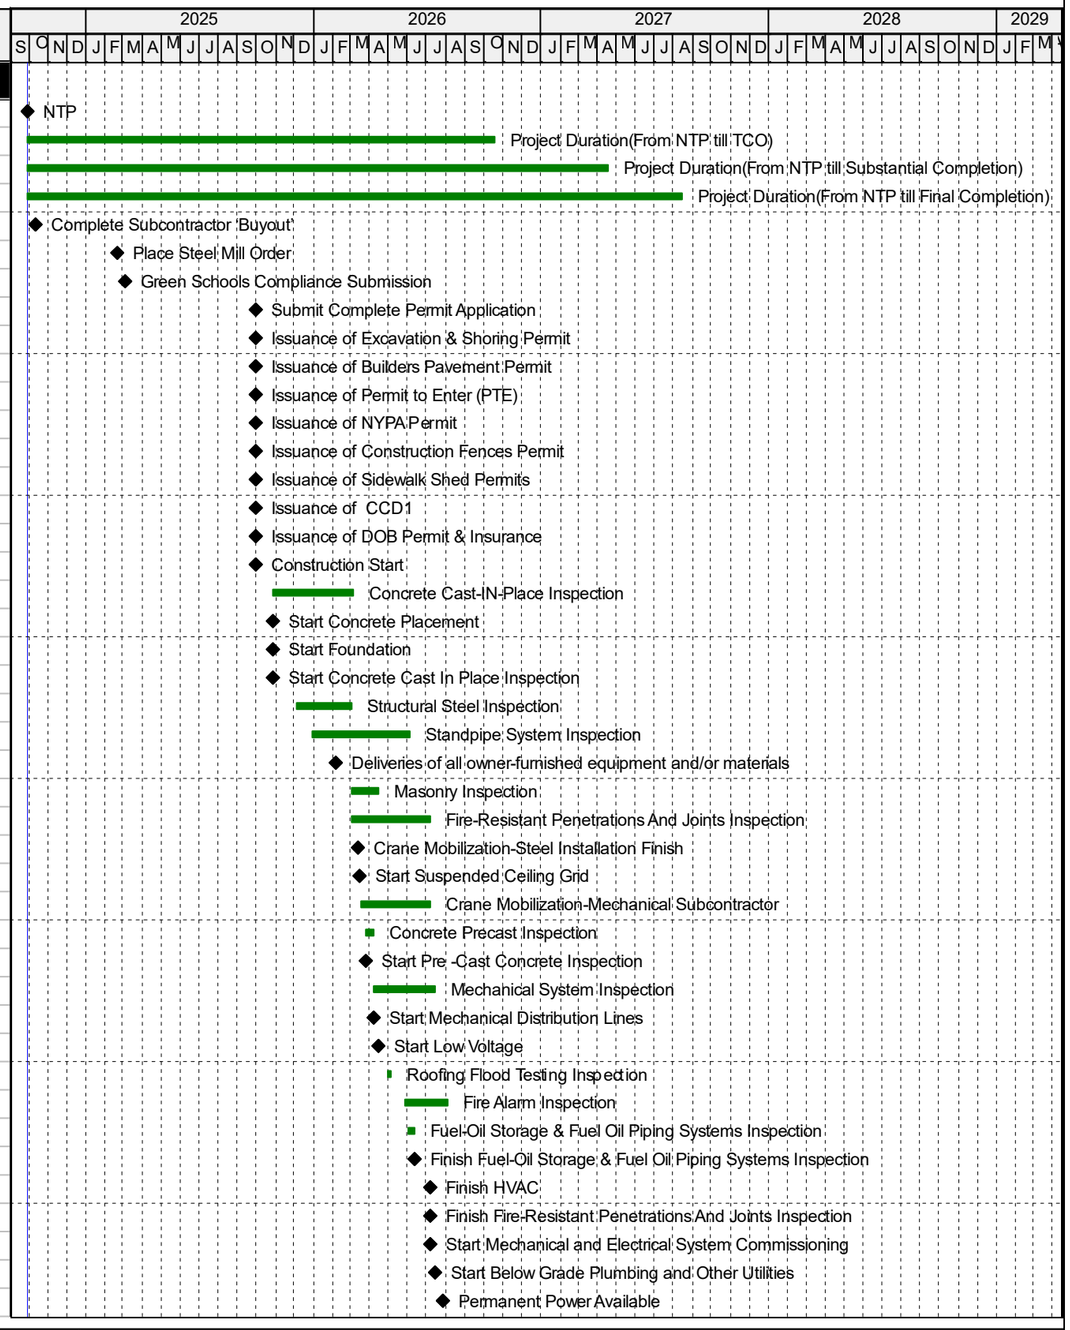

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
MIL-2592	P&D - Connection to Roof Drains	0	28-Jul-26	
MIL-2692	Building HVAC Flush-out	0		03-Aug-26
MIL-2642	Finish Fire Alarm Signoff	0		07-Aug-26
MIL-2962	Finish Fire Alarm Inspection	0		07-Aug-26
MIL-2802	Provision of Training Schedules (30 days prior to start of Training)	0	10-Aug-26	
MIL-2702	Finish Concrete Work	0		10-Aug-26
MIL-2822	Elevator Ready for Testing	0		11-Aug-26
MIL-2672	Finish Painting	0		28-Aug-26
MIL-2722	Start Kitchen	0	04-Sep-26	
MIL-2662	Finishes and Ceiling Complete	0		04-Sep-26
MIL-1470	Finish Site Work	0		10-Sep-26
MIL-2652	Finish Mechanical and Electrical System Commissioning	0		18-Sep-26
MIL-2772	Performance test for all mechanical equipment and low voltage systems	0		18-Sep-26
MIL-2792	Commissioning for all mechanical equipment and low voltage systems	0		18-Sep-26
MIL-2782	Submission of Operations and Maintenance Manuals	0		01-Jun-27
Preconstruction		501	30-Sep-24	30-Sep-26
Submittals		447	15-Oct-24	29-Jul-26
SUB-1000	Prepare & Submit Split Heat Pump System - SUB	60	15-Oct-24	10-Jan-25
SUB-1010	Prepare & Submit Thermometers	40	15-Oct-24	11-Dec-24
SUB-1020	Prepare & Submit Pressure Gages	40	15-Oct-24	11-Dec-24
SUB-1030	Prepare & Submit Floor Drains	40	15-Oct-24	11-Dec-24
SUB-1040	Prepare & Submit Hangers & Supports	40	15-Oct-24	11-Dec-24
SUB-1050	Prepare & Submit Fire & Jockey Pumps	81	15-Oct-24	11-Feb-25
SUB-1060	Prepare & Submit Interior Signage Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1070	Prepare & Submit Ceramic Tiles Product Data	81	15-Oct-24	11-Feb-25
SUB-1080	Prepare & Submit Door Hardware Submittal	81	15-Oct-24	11-Feb-25
SUB-1090	Prepare & Submit Painting	81	15-Oct-24	11-Feb-25
SUB-1100	Prepare & Submit Door & Frame Corners Samples	81	15-Oct-24	11-Feb-25
SUB-1110	Prepare & Submit Roof Drains & Clean Outs	81	15-Oct-24	11-Feb-25
SUB-1120	Prepare & Submit Flashing & Sheet Metal Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-1130	Prepare & Submit Roofing Membrane Product Data	81	15-Oct-24	11-Feb-25
SUB-1140	Prepare & Submit Perimeter Foundation Insulation Product Data	81	15-Oct-24	11-Feb-25
SUB-1150	Prepare & Submit Crystalline Waterproofing Product Data	81	15-Oct-24	11-Feb-25
SUB-1160	Prepare & Submit Suspension Assembly Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1170	Prepare & Submit Certification of Material	81	15-Oct-24	11-Feb-25
SUB-1180	Prepare & Submit Concrete Reinforcement	30	15-Oct-24	26-Nov-24
SUB-1190	Prepare & Submit Formwork Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1200	Prepare & Submit Planting Schedule	81	15-Oct-24	11-Feb-25
SUB-1210	Prepare & Submit Site Furnishings Shop Drawings	15	15-Oct-24	04-Nov-24
SUB-1220	Prepare & Submit Playgroung Equipment Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1230	Prepare & Submit Ductile Iron Pipes	37	15-Oct-24	06-Dec-24
SUB-1240	Prepare & Submit Catch Basin Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1250	Prepare & Submit Concrete Curbs & Pavements Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-1260	Prepare & Submit Steel Curb Facing Shop Drawing	81	15-Oct-24	11-Feb-25

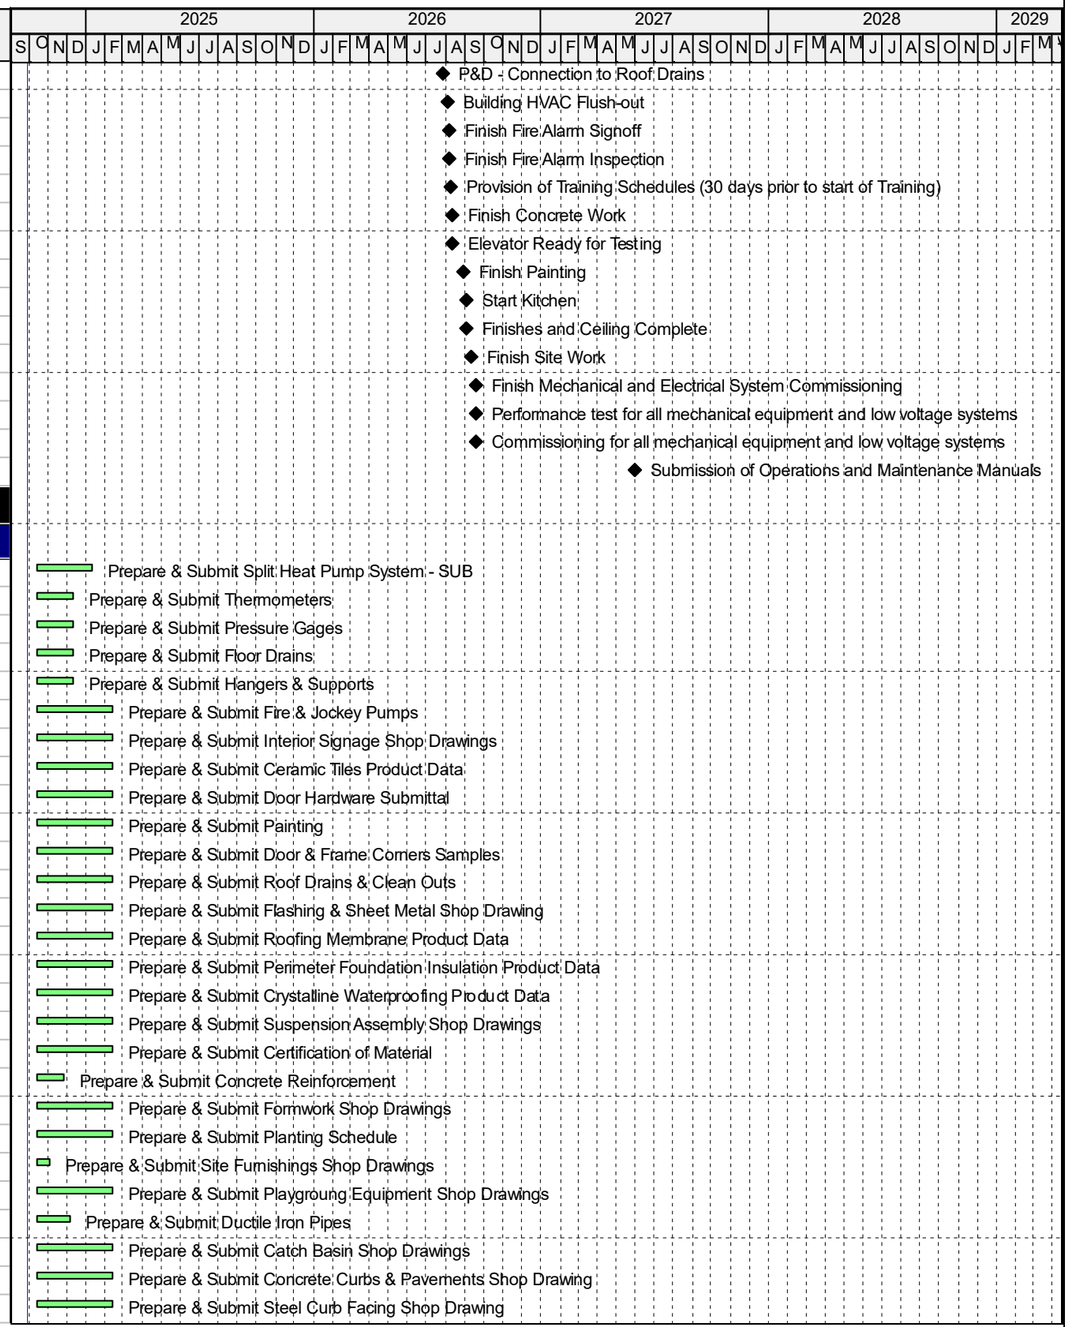

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1270	Prepare & Submit Asphaltic Concrete Paving	81	15-Oct-24	11-Feb-25
SUB-1280	Prepare & Submit SSDS Geotextile	40	15-Oct-24	11-Dec-24
SUB-1290	Prepare & Submit Gas Vapor Barrier Submittal & Inspection Schedule	81	15-Oct-24	11-Feb-25
SUB-1300	Prepare & Submit Existing Conditions Survey	10	15-Oct-24	28-Oct-24
SUB-1310	Prepare & Submit Training Outline & Schedule	81	15-Oct-24	11-Feb-25
SUB-1320	Prepare & Submit Product Substitutions	82	15-Oct-24	12-Feb-25
SUB-1330	Prepare & Submit Temporary Ventilation Plan	81	15-Oct-24	11-Feb-25
SUB-1340	Prepare & Submit Construction Indoor Air Quality Management Plan	81	15-Oct-24	11-Feb-25
SUB-1350	Prepare & Submit Site Safety Plan	2	15-Oct-24	16-Oct-24
SUB-1360	Prepare & Submit CWM Plan	81	15-Oct-24	11-Feb-25
SUB-1370	Prepare & Submit Photo Submission - Temporary Fence	15	15-Oct-24	04-Nov-24
SUB-1380	Prepare & Submit Heating Plan	81	15-Oct-24	11-Feb-25
SUB-1390	Prepare & Submit Sample Classroom Materials	81	15-Oct-24	11-Feb-25
SUB-1400	Prepare & Submit Sustainable Materials	10	15-Oct-24	28-Oct-24
SUB-1410	Prepare & Submit Submittal Schedule	60	15-Oct-24	10-Jan-25
SUB-1420	Prepare & Submit Electrical Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1430	Prepare & Submit Plumbing Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1440	Prepare & Submit Sprinkler System Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1450	Prepare & Submit Concrete Shop Drawings	30	15-Oct-24	26-Nov-24
SUB-1460	Prepare & Submit Elevator Machine	71	15-Oct-24	28-Jan-25
SUB-1470	Prepare & Submit Gypsum Board	81	15-Oct-24	11-Feb-25
SUB-1480	Prepare & Submit Floorings	81	15-Oct-24	11-Feb-25
SUB-1490	Prepare & Submit Acosutical Ceiling Tiles	60	15-Oct-24	10-Jan-25
SUB-1500	Prepare & Submit Toilet Accessories	81	15-Oct-24	11-Feb-25
SUB-1510	Prepare & Submit Millwork	81	15-Oct-24	11-Feb-25
SUB-1520	Prepare & Submit Lighting Fixtures	71	15-Oct-24	28-Jan-25
SUB-1530	Prepare & Submit Furniture	81	15-Oct-24	11-Feb-25
SUB-1540	Prepare & Submit Mechanical Ducts	81	15-Oct-24	11-Feb-25
SUB-1550	Prepare & Submit Mechanical Piping	60	15-Oct-24	10-Jan-25
SUB-1560	Prepare & Submit Erosion Control and Sedimentation Plan	7	15-Oct-24	23-Oct-24
SUB-1570	Prepare & Submit QCP	30	15-Oct-24	26-Nov-24
SUB-1580	Prepare & Submit Concrete Mix Design	30	15-Oct-24	26-Nov-24
SUB-1590	Prepare & Submit Electrical Equipment, Conduits, and Cables	20	15-Oct-24	12-Nov-24
SUB-1600	Prepare & Submit Plumbing Fixtures	81	15-Oct-24	11-Feb-25
SUB-1610	Prepare & Submit Baseline Schedule	52	15-Oct-24	30-Dec-24
SUB-1620	Prepare & Submit Wood Doors	81	15-Oct-24	11-Feb-25
SUB-1630	Prepare & Submit Fire Protection Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1640	Prepare & Submit Fire Detectors & Alarms	81	15-Oct-24	11-Feb-25
SUB-1650	Prepare & Submit Kitchen Equipment	71	15-Oct-24	28-Jan-25
SUB-1660	Prepare & Submit Signs	81	15-Oct-24	11-Feb-25
SUB-1670	Prepare & Submit Aluminum Projected Windows	71	15-Oct-24	28-Jan-25
SUB-1680	Prepare & Submit Telecommunication System Drawings	81	15-Oct-24	11-Feb-25
SUB-1690	Prepare & Submit Internet Protocol Digital Video Surveillance System using Digital Cameras	71	15-Oct-24	28-Jan-25
SUB-1710	Prepare & Submit Chillers Product Data	71	15-Oct-24	28-Jan-25

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1720	Prepare & Submit Air Handling Units Product Data	71	15-Oct-24	28-Jan-25
SUB-1730	Prepare & Submit Boilers	71	15-Oct-24	28-Jan-25
SUB-1740	Prepare & Submit Emergency Generator System Product Data	71	15-Oct-24	28-Jan-25
SUB-1750	Prepare & Submit Switch Gears Product Data	20	15-Oct-24	12-Nov-24
SUB-1760	Prepare & Submit Unit Cabinet Heaters	60	15-Oct-24	10-Jan-25
SUB-1770	Prepare & Submit Gymnasium Equipment	81	15-Oct-24	11-Feb-25
SUB-1780	Prepare & Submit Initial Underground Coordination Drawings	50	15-Oct-24	26-Dec-24
SUB-1790	Prepare & Submit Initial 1st Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1800	Prepare & Submit Initial 2nd Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1810	Prepare & Submit Initial 3rd Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1820	Prepare & Submit Initial 4th Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1830	Prepare & Submit Initial 5th Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1840	Prepare & Submit Supplemental Comissioning Requirements	81	15-Oct-24	11-Feb-25
SUB-1850	Prepare & Submit Record Documents	81	15-Oct-24	11-Feb-25
SUB-1860	Prepare & Submit Environmental Site Assessment Reports	81	15-Oct-24	11-Feb-25
SUB-1870	Prepare & Submit Selective Removals & Demoloition	81	15-Oct-24	11-Feb-25
SUB-1880	Prepare & Submit Foundation Product Data	5	15-Oct-24	21-Oct-24
SUB-1890	Prepare & Submit Trench Drains Product Data	81	15-Oct-24	11-Feb-25
SUB-1900	Prepare & Submit Chain Link Fences & Gates Drawings	81	15-Oct-24	11-Feb-25
SUB-1910	Prepare & Submit Outdoor Game Equipment	81	15-Oct-24	11-Feb-25
SUB-1920	Prepare & Submit Precast Architectural Concrete	71	15-Oct-24	28-Jan-25
SUB-1930	Prepare & Submit Unit Masonry Product Data	71	15-Oct-24	28-Jan-25
SUB-1940	Prepare & Submit Cast Stone Product Data	81	15-Oct-24	11-Feb-25
SUB-1950	Prepare & Submit Structure Steel Drawings	71	15-Oct-24	28-Jan-25
SUB-1960	Prepare & Submit Metal Deck Product Data	81	15-Oct-24	11-Feb-25
SUB-1970	Prepare & Submit Prefabricated Expansion Joint Covers	81	15-Oct-24	11-Feb-25
SUB-1980	Prepare & Submit Self Adhering Sheet Air Barriers	81	15-Oct-24	11-Feb-25
SUB-1990	Prepare & Submit Metal Plate Wall Panels	81	15-Oct-24	11-Feb-25
SUB-2000	Prepare & Submit Security Screens & Barriers	81	15-Oct-24	11-Feb-25
SUB-2010	Prepare & Submit Wood Flooring	81	15-Oct-24	11-Feb-25
SUB-2020	Prepare & Submit Visual Display Boards	81	15-Oct-24	11-Feb-25
SUB-2030	Prepare & Submit Metal Lockers	81	15-Oct-24	11-Feb-25
SUB-2040	Prepare & Submit Fire Extinguishers & Cabinets	81	15-Oct-24	11-Feb-25
SUB-2050	Prepare & Submit Stationary Metal Wall Louvers	73	15-Oct-24	30-Jan-25
SUB-2060	Prepare & Submit Library Equipment	81	15-Oct-24	11-Feb-25
SUB-2070	Prepare & Submit Platform Curtains & Auditorium Window Curtains	81	15-Oct-24	11-Feb-25
SUB-2080	Prepare & Submit Waste Handling Equipment	81	15-Oct-24	11-Feb-25
SUB-2090	Prepare & Submit Domestic Equipment	81	15-Oct-24	11-Feb-25
SUB-2100	Prepare & Submit Laboratory Equipment	81	15-Oct-24	11-Feb-25
SUB-2110	Prepare & Submit Manufactured Wood Casework	81	15-Oct-24	11-Feb-25
SUB-2120	Prepare & Submit Concrete Floating Floor Assembly	81	15-Oct-24	11-Feb-25
SUB-2130	Prepare & Submit Hydraulic Vertical Wheelchair Lifts	81	15-Oct-24	11-Feb-25
SUB-2140	Prepare & Submit Switch & Panel Boards	81	15-Oct-24	11-Feb-25
SUB-2150	Prepare & Submit Auditorium & Television Studio Dimming System Product Data	81	15-Oct-24	11-Feb-25

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-2160	Prepare & Submit Overcurrent Protective Devices Data	81	15-Oct-24	11-Feb-25
SUB-2170	Prepare & Submit Gas Pipes	81	15-Oct-24	11-Feb-25
SUB-2180	Prepare & Submit Water Heaters	81	15-Oct-24	11-Feb-25
SUB-2190	Prepare & Submit Pumping Apparatus & Tanks	81	15-Oct-24	11-Feb-25
SUB-2200	Prepare & Submit HVAC Pumps	81	15-Oct-24	11-Feb-25
SUB-2210	Prepare & Submit Emergency Generator System Accessories	71	15-Oct-24	28-Jan-25
SUB-2220	Prepare & Submit Fuel Storage Equipment	81	15-Oct-24	11-Feb-25
SUB-2230	Prepare & Submit Natural Gas Leak Detection Equipment	81	15-Oct-24	11-Feb-25
SUB-2250	Prepare & Submit Temperature Control System	81	15-Oct-24	11-Feb-25
SUB-2260	Prepare & Submit Air Outlets & Inlets	81	15-Oct-24	11-Feb-25
SUB-2340	Prepare & Submit Tree Protection Plan	71	15-Oct-24	28-Jan-25
SUB-2360	Prepare & Submit Adjacent Property and Structures Protection & Monitoring Plan	81	15-Oct-24	11-Feb-25
SUB-2370	Prepare & Submit Ornamenta Metal Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2920	Prepare & Submit Documentation of Proper Disposal	81	15-Oct-24	11-Feb-25
SUB-2930	Prepare & Submit Ornamenta Metal Product Data	81	15-Oct-24	11-Feb-25
SUB-2960	Prepare & Submit Coiling Doors, Grilles and Shutters Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2970	Prepare & Submit Coiling Doors, Grilles and Shutters Product Data	81	15-Oct-24	11-Feb-25
SUB-2980	Prepare & Submit Aluminum Framed Entrances & Storefronts Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2990	Prepare & Submit Aluminum Framed Entrances & Storefronts Product Data	81	15-Oct-24	11-Feb-25
SUB-3000	Prepare & Submit Thresholds, Weatherstripping and Seals Color Samples	81	15-Oct-24	11-Feb-25
SUB-3010	Prepare & Submit Thresholds, Weatherstripping and Seals Product Data	81	15-Oct-24	11-Feb-25
SUB-3020	Prepare & Submit Miscellaneous Glazing Samples	81	15-Oct-24	11-Feb-25
SUB-3030	Prepare & Submit Miscellaneous Glazing Product Data	81	15-Oct-24	11-Feb-25
SUB-3040	Prepare & Submit Fire Rated Glazing Samples	81	15-Oct-24	11-Feb-25
SUB-3050	Prepare & Submit Fire Rated Glazing Product Data	81	15-Oct-24	11-Feb-25
SUB-3060	Prepare & Submit Graffiti Resistant Coating Product Data	81	15-Oct-24	11-Feb-25
SUB-3070	Prepare & Submit Special Coating Samples	81	15-Oct-24	11-Feb-25
SUB-3080	Prepare & Submit Special Coating Product Data	81	15-Oct-24	11-Feb-25
SUB-3090	Prepare & Submit Flagpole Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3100	Prepare & Submit Flagpole Product Data	81	15-Oct-24	11-Feb-25
SUB-3110	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals	81	15-Oct-24	11-Feb-25
SUB-3120	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-3130	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	81	15-Oct-24	11-Feb-25
SUB-3140	Prepare & Submit Wire Mesh Work Samples	81	15-Oct-24	11-Feb-25
SUB-3150	Prepare & Submit Wire Mesh Work Shop drawings	81	15-Oct-24	11-Feb-25
SUB-3160	Prepare & Submit Metal Storage Shelving Samples	81	15-Oct-24	11-Feb-25
SUB-3170	Prepare & Submit Metal Storage Shelving Shop drawings	81	15-Oct-24	11-Feb-25
SUB-3180	Prepare & Submit Mirrors Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3190	Prepare & Submit Mirrors Product Data	81	15-Oct-24	11-Feb-25
SUB-3200	Prepare & Submit Mirrors Mastic Compatibility Test Reports & Certifications	81	15-Oct-24	11-Feb-25
SUB-3210	Prepare & Submit Grab Bars Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3220	Prepare & Submit Grab Bars Product Data	81	15-Oct-24	11-Feb-25
SUB-3230	Prepare & Submit Shop Equipment Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3240	Prepare & Submit Shop Equipment Product Data	81	15-Oct-24	11-Feb-25

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-3250	Prepare & Submit Bleachers Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3260	Prepare & Submit Bleachers Product Data	81	15-Oct-24	11-Feb-25
SUB-3270	Prepare & Submit Bleachers Manufacturer's Warranty	81	15-Oct-24	11-Feb-25
SUB-3280	Prepare & Submit Valves Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3290	Prepare & Submit Valves Product Data	81	15-Oct-24	11-Feb-25
SUB-3300	Prepare & Submit Certification of Tests	81	15-Oct-24	11-Feb-25
SUB-3310	Prepare & Submit Domestic Water Sterilization Plan	81	15-Oct-24	11-Feb-25
SUB-3320	Prepare & Submit Tags, Charts & Identifications Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3330	Prepare & Submit Tags, Charts & Identifications Product Data	81	15-Oct-24	11-Feb-25
SUB-3340	Prepare & Submit Micselianeous Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3350	Prepare & Submit Valves (HVAC) Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3360	Prepare & Submit Valves (HVAC) Product Data	81	15-Oct-24	11-Feb-25
SUB-3370	Prepare & Submit Piping Insulation Schedule Listing Items	81	15-Oct-24	11-Feb-25
SUB-3380	Prepare & Submit Schedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	81	15-Oct-24	11-Feb-25
SUB-3390	Prepare & Submit Schedules Showing Manfacturers's Product Number Duct Work Insulation	81	15-Oct-24	11-Feb-25
SUB-3400	Prepare & Submit Hydronic Specialities Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3410	Prepare & Submit Hydronic Specialities Product Data	81	15-Oct-24	11-Feb-25
SUB-3420	Prepare & Submit Water Treatment Firm	81	15-Oct-24	11-Feb-25
SUB-3430	Prepare & Submit Chemical Products Product Data	81	15-Oct-24	11-Feb-25
SUB-3440	Prepare & Submit Detail of Gag for the Safety Relief Valves	71	15-Oct-24	28-Jan-25
SUB-3450	Prepare & Submit Boiler Accessories Maintenance Data	71	15-Oct-24	28-Jan-25
SUB-3460	Prepare & Submit Breeching Chimney Connectors and Chimneys Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3470	Prepare & Submit Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	81	15-Oct-24	11-Feb-25
SUB-3480	Prepare & Submit Plate Heat Exchanger Maintenance Data	81	15-Oct-24	11-Feb-25
SUB-3490	Prepare & Submit Plate Heat Exchanger Product Data	81	15-Oct-24	11-Feb-25
SUB-3500	Prepare & Submit Coils Maintenance Data	81	15-Oct-24	11-Feb-25
SUB-3510	Prepare & Submit Coils Certifications	81	15-Oct-24	11-Feb-25
SUB-3520	Prepare & Submit Convectors Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3530	Prepare & Submit Convectors Product Data	81	15-Oct-24	11-Feb-25
SUB-3540	Prepare & Submit Fan Coils Units Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3550	Prepare & Submit Fan Coils Units Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-3560	Prepare & Submit Door Air Curtains Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3570	Prepare & Submit Door Air Curtains Product Data	81	15-Oct-24	11-Feb-25
SUB-3580	Prepare & Submit Centrifugal Fans Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3590	Prepare & Submit Centrifugal Fans Product Data	81	15-Oct-24	11-Feb-25
SUB-3600	Prepare & Submit Centrifugal Fans Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3610	Prepare & Submit Air Filters Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3620	Prepare & Submit Air Filters Product Data	81	15-Oct-24	11-Feb-25
SUB-3630	Prepare & Submit Air Filters Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3640	Prepare & Submit Duct Accessories Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3650	Prepare & Submit Damper Assemblies Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3660	Prepare & Submit Damper Assemblies Product Data	81	15-Oct-24	11-Feb-25
SUB-3670	Prepare & Submit Damper Assemblies Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3680	Prepare & Submit Variable Air Terminals Shop Drawing	81	15-Oct-24	11-Feb-25

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-3690	Prepare & Submit Variable Air Terminals Product Data	81	15-Oct-24	11-Feb-25
SUB-3700	Prepare & Submit Variable Air Terminals Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3710	Prepare & Submit AHU for Public Assemblies Sapces Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3720	Prepare & Submit AHU for Public Assemblies Sapces Product Data	81	15-Oct-24	11-Feb-25
SUB-3730	Prepare & Submit AHU for Public Assemblies Sapces Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3740	Prepare & Submit Control Systems Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3750	Prepare & Submit Truck Network Cable Schematic Diagram	81	15-Oct-24	11-Feb-25
SUB-3760	Prepare & Submit Lighting Control Devices Shop Drawing	71	15-Oct-24	28-Jan-25
SUB-3770	Prepare & Submit Lighting Control Devices Product Data	71	15-Oct-24	28-Jan-25
SUB-3780	Prepare & Submit Lighting Control Devices Warranty	71	15-Oct-24	28-Jan-25
SUB-3790	Prepare & Submit Surge Protective Devices Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3800	Prepare & Submit Surge Protective Devices Product Data	81	15-Oct-24	11-Feb-25
SUB-3810	Prepare & Submit Surge Protective Devices Warranty	81	15-Oct-24	11-Feb-25
SUB-3820	Prepare & Submit Service Entrance Equipment Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3830	Prepare & Submit Service Entrance Equipment Product Data	81	15-Oct-24	11-Feb-25
SUB-3840	Prepare & Submit Service Entrance Equipment Warranty	81	15-Oct-24	11-Feb-25
SUB-3850	Prepare & Submit Enclosed Switches Product Data	81	15-Oct-24	11-Feb-25
SUB-3860	Prepare & Submit Enclosed Switches Test Reports	81	15-Oct-24	11-Feb-25
SUB-3870	Prepare & Submit Motors, Motor Control Centers and Starters Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3880	Prepare & Submit Motors, Motor Control Centers and Starters Product Data	81	15-Oct-24	11-Feb-25
SUB-3890	Prepare & Submit Motors, Motor Control Centers and Starters Field Test Reports	81	15-Oct-24	11-Feb-25
SUB-3900	Prepare & Submit Lightning Protection Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3920	Prepare & Submit Lightning Protection Test Reports	81	15-Oct-24	11-Feb-25
SUB-3930	Prepare & Submit Fiber Optic Cabling system Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3940	Prepare & Submit Fiber Optic Cabling system Product Data	81	15-Oct-24	11-Feb-25
SUB-3950	Prepare & Submit Fiber Optic Cabling system Samples	81	15-Oct-24	11-Feb-25
SUB-3960	Prepare & Submit Sound, Intercome & Security System Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3970	Prepare & Submit Sound, Intercome & Security System Programming Code and Password for the System	81	15-Oct-24	11-Feb-25
SUB-3980	Prepare & Submit Sound, Intercome & Security System Warranty	81	15-Oct-24	11-Feb-25
SUB-3990	Prepare & Submit Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	81	15-Oct-24	11-Feb-25
SUB-4000	Prepare & Submit Projection and Interactive Whiteboard Systems Wiring diagram	81	15-Oct-24	11-Feb-25
SUB-4010	Prepare & Submit Self Corrective Clock System Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-4020	Prepare & Submit Self Corrective Clock System Product Data	81	15-Oct-24	11-Feb-25
SUB-4030	Prepare & Submit Self Corrective Clock System Field Test Reports	81	15-Oct-24	11-Feb-25
SUB-4040	Prepare & Submit Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	81	15-Oct-24	11-Feb-25
SUB-4060	Prepare & Submit Steel Stairs Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-4070	Prepare & Submit Steel Stairs Product Data	81	15-Oct-24	11-Feb-25
SUB-4080	Prepare & Submit Green School Submittal	81	15-Oct-24	11-Feb-25
SUB-2270	Prepare & Submit Final Underground Coordination Drawings	37	17-Jan-25	11-Mar-25
SUB-2280	Prepare & Submit Final 1st Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2290	Prepare & Submit Final 2nd Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2300	Prepare & Submit Final 3rd Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2310	Prepare & Submit Final 4th Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2320	Prepare & Submit Final 5th Floor Coordination Drawings	49	25-Feb-25	02-May-25

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1700	Prepare & Submit Roof Dunnage	81	05-Mar-25	27-Jun-25
SUB-2900	Prepare & Submit Excavated Material Disposal Plan	71	26-May-25	05-Sep-25
SUB-4050	Prepare & Submit Soil Sampling Plan	71	26-May-25	05-Sep-25
SUB-2910	Prepare & Submit Backfill & Resue Plan	20	08-Sep-25	03-Oct-25
PRE-2550	Obtain CCD1	3	25-Sep-25	29-Sep-25
SUB-2330	Prepare & Submit Remedial Closure Report	3	27-Jul-26	29-Jul-26
Approvals		460	17-Oct-24	19-Aug-26
APP-1000	Review & Approve Site Safety Plan	21	17-Oct-24	06-Nov-24
APP-1010	Review & Approve Foundation Product Data	21	22-Oct-24	11-Nov-24
APP-1020	Review & Approve Erosion Control and Sedimentation Plan	21	24-Oct-24	13-Nov-24
APP-1030	Review & Approve Existing Conditions Survey	21	29-Oct-24	18-Nov-24
APP-1040	Review & Approve Sustainable Materials	21	29-Oct-24	18-Nov-24
APP-1050	Review & Approve Site Furnishings Shop Drawings	21	05-Nov-24	25-Nov-24
APP-1060	Review & Approve Photo Submission - Temporary Fence	21	05-Nov-24	25-Nov-24
APP-1080	Review & Approve Electrical Equipment, Conduits, and Cables	21	13-Nov-24	03-Dec-24
APP-1090	Review & Approve Switch Gears Product Data	21	13-Nov-24	03-Dec-24
APP-1100	Review & Approve Concrete Reinforcement	21	27-Nov-24	17-Dec-24
APP-1110	Review & Approve Concrete Shop Drawings	21	27-Nov-24	17-Dec-24
APP-1130	Review & Approve QCP	21	27-Nov-24	17-Dec-24
APP-1140	Review & Approve Concrete Mix Design	21	27-Nov-24	17-Dec-24
APP-1150	Review & Approve Ductile Iron Pipes	21	07-Dec-24	27-Dec-24
APP-1160	Review & Approve Thermometers	21	12-Dec-24	01-Jan-25
APP-1170	Review & Approve Pressure Gages	21	12-Dec-24	01-Jan-25
APP-1180	Review & Approve Floor Drains	21	12-Dec-24	01-Jan-25
APP-1190	Review & Approve Hangers & Supports	21	12-Dec-24	01-Jan-25
APP-1200	Review & Approve SSDS Geotextile	21	12-Dec-24	01-Jan-25
APP-1230	Review & Approve Initial Underground Coordination Drawings	21	27-Dec-24	16-Jan-25
APP-1240	Review & Approve Baseline Schedule	21	31-Dec-24	20-Jan-25
APP-1250	Review & Approve Split Heat Pump System - SUB	21	11-Jan-25	31-Jan-25
APP-1260	Review & Approve Submittal Schedule	21	11-Jan-25	31-Jan-25
APP-1270	Review & Approve Acosutical Ceiling Tiles	21	11-Jan-25	31-Jan-25
APP-1280	Review & Approve Mechanical Piping	21	11-Jan-25	31-Jan-25
APP-1290	Review & Approve Unit Cabinet Heaters	21	11-Jan-25	31-Jan-25
APP-1210	Review & Approve Elevator Machine	21	29-Jan-25	18-Feb-25
APP-1120	Review & Approve Lighting Fixtures	21	29-Jan-25	18-Feb-25
APP-1780	Review & Approve Kitchen Equipment	21	29-Jan-25	18-Feb-25
APP-1310	Review & Approve Aluminum Projected Windows	21	29-Jan-25	18-Feb-25
APP-1220	Review & Approve Internet Protocol Digital Video Surveillance System using Digital Cameras	35	29-Jan-25	04-Mar-25
APP-1820	Review & Approve Chillers Product Data	21	29-Jan-25	18-Feb-25
APP-1300	Review & Approve Air Handling Units Product Data	21	29-Jan-25	18-Feb-25
APP-1830	Review & Approve Boilers	21	29-Jan-25	18-Feb-25
APP-1070	Review & Approve Emergency Generator System Product Data	21	29-Jan-25	18-Feb-25
APP-1920	Review & Approve Precast Architectural Concrete	21	29-Jan-25	18-Feb-25
APP-1930	Review & Approve Unit Masonry Product Data	21	29-Jan-25	18-Feb-25

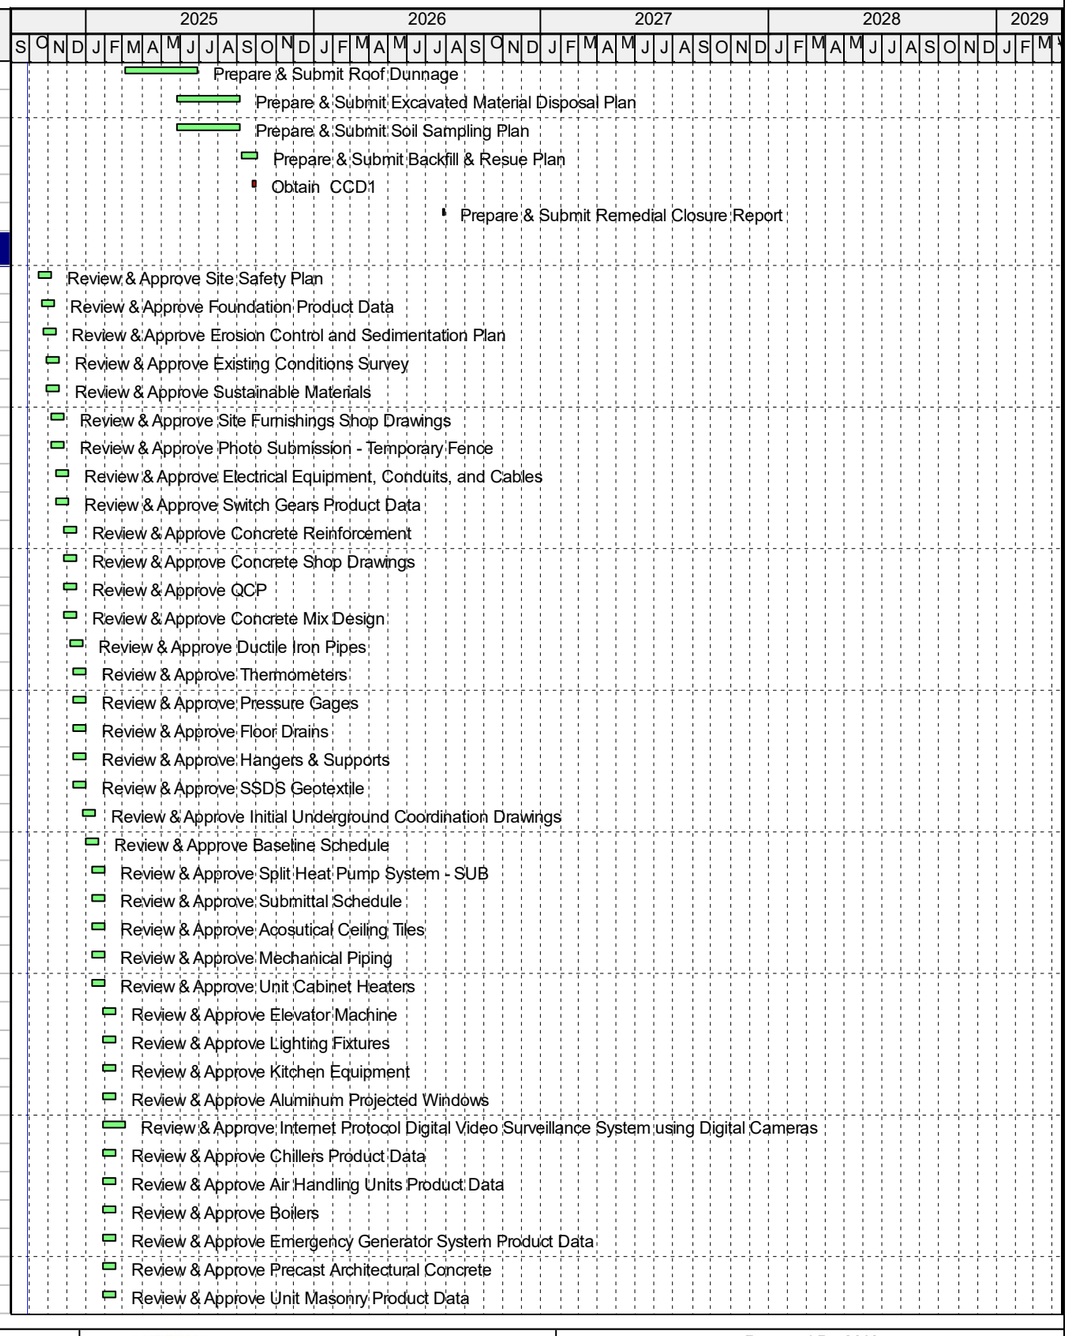

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1950	Review & Approve Structure Steel Drawings	21	29-Jan-25	18-Feb-25
APP-2200	Review & Approve Emergency Generator System Accessories	21	29-Jan-25	18-Feb-25
APP-2340	Review & Approve Tree Protection Plan	21	29-Jan-25	18-Feb-25
APP-3440	Review & Approve Detail of Gag for the Safety Relief Valves	21	29-Jan-25	18-Feb-25
APP-3450	Review & Approve Boiler Accessories Maintenance Data	21	29-Jan-25	18-Feb-25
APP-3760	Review & Approve Lighting Control Devices Shop Drawing	21	29-Jan-25	18-Feb-25
APP-3770	Review & Approve Lighting Control Devices Product Data	21	29-Jan-25	18-Feb-25
APP-3780	Review & Approve Lighting Control Devices Warranty	21	29-Jan-25	18-Feb-25
APP-1320	Review & Approve Stationary Metal Wall Louvers	21	31-Jan-25	20-Feb-25
APP-1330	Review & Approve Initial 1st Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1340	Review & Approve Initial 2nd Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1350	Review & Approve Initial 3rd Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1360	Review & Approve Initial 4th Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1370	Review & Approve Initial 5th Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1380	Review & Approve Fire & Jockey Pumps	21	12-Feb-25	04-Mar-25
APP-1390	Review & Approve Interior Signage Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1400	Review & Approve Ceramic Tiles Product Data	21	12-Feb-25	04-Mar-25
APP-1410	Review & Approve Door Hardware Submittal	21	12-Feb-25	04-Mar-25
APP-1420	Review & Approve Painting	21	12-Feb-25	04-Mar-25
APP-1430	Review & Approve Door & Frame Corners Samples	21	12-Feb-25	04-Mar-25
APP-1440	Review & Approve Roof Drains & Clean Outs	21	12-Feb-25	04-Mar-25
APP-1450	Review & Approve Flashing & Sheet Metal Shop Drawing	21	12-Feb-25	04-Mar-25
APP-1460	Review & Approve Roofing Membrane Product Data	21	12-Feb-25	04-Mar-25
APP-1470	Review & Approve Perimeter Foundation Insulation Product Data	21	12-Feb-25	04-Mar-25
APP-1480	Review & Approve Crystalline Waterproofing Product Data	21	12-Feb-25	04-Mar-25
APP-1490	Review & Approve Suspension Assembly Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1500	Review & Approve Certification of Material	21	12-Feb-25	04-Mar-25
APP-1510	Review & Approve Formwork Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1520	Review & Approve Planting Schedule	21	12-Feb-25	04-Mar-25
APP-1530	Review & Approve Playgroung Equipment Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1540	Review & Approve Catch Basin Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1550	Review & Approve Concrete Curbs & Pavements Shop Drawing	21	12-Feb-25	04-Mar-25
APP-1560	Review & Approve Steel Curb Facing Shop Drawing	21	12-Feb-25	04-Mar-25
APP-1570	Review & Approve Asphaltic Concrete Paving	21	12-Feb-25	04-Mar-25
APP-1580	Review & Approve Gas Vapor Barrier Submittal & Inspection Schedule	21	12-Feb-25	04-Mar-25
APP-1590	Review & Approve Training Outline & Schedule	21	12-Feb-25	04-Mar-25
APP-1600	Review & Approve Temporary Ventilation Plan	21	12-Feb-25	04-Mar-25
APP-1610	Review & Approve Construction Indoor Air Quality Management Plan	21	12-Feb-25	04-Mar-25
APP-1620	Review & Approve CWM Plan	21	12-Feb-25	04-Mar-25
APP-1630	Review & Approve Heating Plan	21	12-Feb-25	04-Mar-25
APP-1640	Review & Approve Sample Classroom Materials	21	12-Feb-25	04-Mar-25
APP-1650	Review & Approve Electrical Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1660	Review & Approve Plumbing Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1670	Review & Approve Sprinkler System Shop Drawings	21	12-Feb-25	04-Mar-25

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1680	Review & Approve Gypsum Board	21	12-Feb-25	04-Mar-25
APP-1690	Review & Approve Floorings	21	12-Feb-25	04-Mar-25
APP-1700	Review & Approve Toilet Accessories	21	12-Feb-25	04-Mar-25
APP-1710	Review & Approve Millwork	21	12-Feb-25	04-Mar-25
APP-1720	Review & Approve Furniture	21	12-Feb-25	04-Mar-25
APP-1730	Review & Approve Mechanical Ducts	21	12-Feb-25	04-Mar-25
APP-1740	Review & Approve Plumbing Fixtures	21	12-Feb-25	04-Mar-25
APP-1750	Review & Approve Wood Doors	21	12-Feb-25	04-Mar-25
APP-1760	Review & Approve Fire Protection Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1770	Review & Approve Fire Detectors & Alarms	21	12-Feb-25	04-Mar-25
APP-1790	Review & Approve Signs	21	12-Feb-25	04-Mar-25
APP-1800	Review & Approve Telecommunication System Drawings	21	12-Feb-25	04-Mar-25
APP-1840	Review & Approve Gymnasium Equipment	21	12-Feb-25	04-Mar-25
APP-1850	Review & Approve Supplemental Comissioning Requirements	21	12-Feb-25	04-Mar-25
APP-1860	Review & Approve Record Documents	21	12-Feb-25	04-Mar-25
APP-1870	Review & Approve Environmental Site Assessment Reports	21	12-Feb-25	04-Mar-25
APP-1880	Review & Approve Selective Removals & Demoloition	21	12-Feb-25	04-Mar-25
APP-1890	Review & Approve Trench Drains Prodcut Data	21	12-Feb-25	04-Mar-25
APP-1900	Review & Approve Chain Link Fences & Gates Drawings	21	12-Feb-25	04-Mar-25
APP-1910	Review & Approve Outdoor Game Equipment	21	12-Feb-25	04-Mar-25
APP-1940	Review & Approve Cast Stone Product Data	21	12-Feb-25	04-Mar-25
APP-1960	Review & Approve Metal Deck Product Data	21	12-Feb-25	04-Mar-25
APP-1970	Review & Approve Prefabricated Expansion Joint Covers	21	12-Feb-25	04-Mar-25
APP-1980	Review & Approve Self Adhering Sheet Air Barriers	21	12-Feb-25	04-Mar-25
APP-1990	Review & Approve Metal Plate Wall Panels	21	12-Feb-25	04-Mar-25
APP-2000	Review & Approve Security Screens & Barriers	21	12-Feb-25	04-Mar-25
APP-2010	Review & Approve Wood Flooring	21	12-Feb-25	04-Mar-25
APP-2020	Review & Approve Visual Display Boards	21	12-Feb-25	04-Mar-25
APP-2030	Review & Approve Metal Lockers	21	12-Feb-25	04-Mar-25
APP-2040	Review & Approve Fire Extinguishers & Cabinets	21	12-Feb-25	04-Mar-25
APP-2050	Review & Approve Library Equipment	21	12-Feb-25	04-Mar-25
APP-2060	Review & Approve Platform Curtains & Auditorium Window Curtains	21	12-Feb-25	04-Mar-25
APP-2070	Review & Approve Waste Handling Equipment	21	12-Feb-25	04-Mar-25
APP-2080	Review & Approve Domestic Equipment	21	12-Feb-25	04-Mar-25
APP-2090	Review & Approve Laboratory Equipment	21	12-Feb-25	04-Mar-25
APP-2100	Review & Approve Manufactured Wood Casework	21	12-Feb-25	04-Mar-25
APP-2110	Review & Approve Concrete Floating Floor Assembly	21	12-Feb-25	04-Mar-25
APP-2120	Review & Approve Hydraulic Vertical Wheelchair Lifts	21	12-Feb-25	04-Mar-25
APP-2130	Review & Approve Switch & Panel Boards	21	12-Feb-25	04-Mar-25
APP-2140	Review & Approve Auditorium & Television Studio Dimming System Product Data	21	12-Feb-25	04-Mar-25
APP-2150	Review & Approve Overcurrent Protective Devices Data	21	12-Feb-25	04-Mar-25
APP-2160	Review & Approve Gas Pipes	21	12-Feb-25	04-Mar-25
APP-2170	Review & Approve Water Heaters	21	12-Feb-25	04-Mar-25
APP-2180	Review & Approve Pumping Apparatus & Tanks	21	12-Feb-25	04-Mar-25

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
APP-2190	Review & Approve HVAC Pumps	21	12-Feb-25	04-Mar-25
APP-2210	Review & Approve Fuel Storage Equipment	21	12-Feb-25	04-Mar-25
APP-2220	Review & Approve Natural Gas Leak Detection Equipment	21	12-Feb-25	04-Mar-25
APP-2240	Review & Approve Temperature Control System	21	12-Feb-25	04-Mar-25
APP-2250	Review & Approve Air Outlets & Inlets	21	12-Feb-25	04-Mar-25
APP-2360	Review & Approve Adjacent Property and Structures Protection & Monitoring Plan	21	12-Feb-25	04-Mar-25
APP-2370	Review & Approve Ornamenta Metal Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2920	Review & Approve Documentation of Proper Disposal	21	12-Feb-25	04-Mar-25
APP-2930	Review & Approve Ornamenta Metal Product Data	21	12-Feb-25	04-Mar-25
APP-2960	Review & Approve Coiling Doors, Grilles and Shutters Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2970	Review & Approve Coiling Doors, Grilles and ShuttersProduct Data	21	12-Feb-25	04-Mar-25
APP-2980	Review & Approve Aluminum Framed Entrances & Storefronts Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2990	Review & Approve Aluminum Framed Entrances & Storefronts Product Data	21	12-Feb-25	04-Mar-25
APP-3000	Review & Approve Thresholds, Weatherstripping and Seals Color Samples	21	12-Feb-25	04-Mar-25
APP-3010	Review & Approve Thresholds, Weatherstripping and Seals Product Data	21	12-Feb-25	04-Mar-25
APP-3020	Review & Approve Miscellaneous Glazing Samples	21	12-Feb-25	04-Mar-25
APP-3030	Review & Approve Miscellaneous Glazing Product Data	21	12-Feb-25	04-Mar-25
APP-3040	Review & Approve Fire Rated Glazing Samples	21	12-Feb-25	04-Mar-25
APP-3050	Review & Approve Fire Rated Glazing Product Data	21	12-Feb-25	04-Mar-25
APP-3060	Review & Approve Graffiti Resistant Coating Product Data	21	12-Feb-25	04-Mar-25
APP-3070	Review & Approve Special Coating Samples	21	12-Feb-25	04-Mar-25
APP-3080	Review & Approve Special Coating Product Data	21	12-Feb-25	04-Mar-25
APP-3090	Review & Approve Flagpole Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3100	Review & Approve Flagpole Product Data	21	12-Feb-25	04-Mar-25
APP-3110	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals	21	12-Feb-25	04-Mar-25
APP-3120	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	21	12-Feb-25	04-Mar-25
APP-3130	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	21	12-Feb-25	04-Mar-25
APP-3140	Review & Approve Wire Mesh Work Samples	21	12-Feb-25	04-Mar-25
APP-3150	Review & Approve Miscellaneous Glazing Shop drawings	21	12-Feb-25	04-Mar-25
APP-3160	Review & Approve Metal Storage Shelving Samples	21	12-Feb-25	04-Mar-25
APP-3170	Review & Approve Metal Storage Shelving Shop drawings	21	12-Feb-25	04-Mar-25
APP-3180	Review & Approve Mirrors Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3190	Review & Approve Mirrors Product Data	21	12-Feb-25	04-Mar-25
APP-3200	Review & Approve Mirrors Mastic Compatibility Test Reports & Certifications	21	12-Feb-25	04-Mar-25
APP-3210	Review & Approve Grab Bars Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3220	Review & Approve Grab Bars Product Data	21	12-Feb-25	04-Mar-25
APP-3230	Review & Approve Shop Equipment Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3240	Review & Approve Shop Equipment Product Data	21	12-Feb-25	04-Mar-25
APP-3250	Review & Approve Bleachers Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3260	Review & Approve Bleachers Product Data	21	12-Feb-25	04-Mar-25
APP-3270	Review & Approve Bleachers Manufacturer's Warranty	21	12-Feb-25	04-Mar-25
APP-3280	Review & Approve Valves Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3290	Review & Approve Valves Product Data	21	12-Feb-25	04-Mar-25
APP-3300	Review & Approve Certification of Tests	21	12-Feb-25	04-Mar-25

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
APP-3310	Review & Approve Domestic Water Sterilization Plan	21	12-Feb-25	04-Mar-25
APP-3320	Review & Approve Tags, Charts & Identifications Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3330	Review & Approve Tags, Charts & Identifications Product Data	21	12-Feb-25	04-Mar-25
APP-3340	Review & Approve Micselianeous Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3350	Review & Approve Valves (HVAC) Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3360	Review & Approve Valves (HVAC) Product Data	21	12-Feb-25	04-Mar-25
APP-3370	Review & Approve Piping Insulation Schedule Listing Items	21	12-Feb-25	04-Mar-25
APP-3380	Review & Approve chedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	21	12-Feb-25	04-Mar-25
APP-3390	Review & Approve chedules Showing Manfacturers's Product Number Duct Work Insulation	21	12-Feb-25	04-Mar-25
APP-3400	Review & Approve Hydronic Specialities Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3410	Review & Approve Hydronic Specialities Product Data	21	12-Feb-25	04-Mar-25
APP-3420	Review & Approve Water Treatment Firm	21	12-Feb-25	04-Mar-25
APP-3430	Review & Approve Chemical Products Product Data	21	12-Feb-25	04-Mar-25
APP-3460	Review & Approve Breeching Chimney Connectors and Chimneys Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3470	Review & Approve Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	21	12-Feb-25	04-Mar-25
APP-3480	Review & Approve Plate Heat Exchanger Maintenance Data	21	12-Feb-25	04-Mar-25
APP-3490	Review & Approve Plate Heat Exchanger Product Data	21	12-Feb-25	04-Mar-25
APP-3500	Review & Approve Coils Maintenance Data	21	12-Feb-25	04-Mar-25
APP-3510	Review & Approve Coils Certifications	21	12-Feb-25	04-Mar-25
APP-3520	Review & Approve Convectors Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3530	Review & Approve Convectors Product Data	21	12-Feb-25	04-Mar-25
APP-3540	Review & Approve Fan Coils Units Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3550	Review & Approve Fan Coils Units Shop Drawings	21	12-Feb-25	04-Mar-25
APP-3560	Review & Approve Door Air Curtains Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3570	Review & Approve Door Air Curtains Product Data	21	12-Feb-25	04-Mar-25
APP-3580	Review & Approve Centrifugal Fans Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3590	Review & Approve Centrifugal Fans Product Data	21	12-Feb-25	04-Mar-25
APP-3600	Review & Approve Centrifugal Fans Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3610	Review & Approve Air Filters Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3620	Review & Approve Air Filters Product Data	21	12-Feb-25	04-Mar-25
APP-3630	Review & Approve Air Filters Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3640	Review & Approve Duct Accessories Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3650	Review & Approve Damper Assemblies Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3660	Review & Approve Damper Assemblies Product Data	21	12-Feb-25	04-Mar-25
APP-3670	Review & Approve Damper Assemblies Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3680	Review & Approve Variable Air Terminals Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3690	Review & Approve Variable Air Terminals Product Data	21	12-Feb-25	04-Mar-25
APP-3700	Review & Approve Variable Air Terminals Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3710	Review & Approve AHU for Public Assemblies Sapces Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3720	Review & Approve AHU for Public Assemblies Sapces Product Data	21	12-Feb-25	04-Mar-25
APP-3730	Review & Approve AHU for Public Assemblies Sapces Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3740	Review & Approve Control Systems Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3750	Review & Approve Truck Network Cable Schematic Diagram	21	12-Feb-25	04-Mar-25
APP-3790	Review & Approve Surge Protective Devices Shop Drawing	21	12-Feb-25	04-Mar-25

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
APP-3800	Review & Approve Surge Protective Devices Product Data	21	12-Feb-25	04-Mar-25
APP-3810	Review & Approve Surge Protective Devices Warranty	21	12-Feb-25	04-Mar-25
APP-3820	Review & Approve Service Entrance Equipment Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3830	Review & Approve Service Entrance Equipment Product Data	21	12-Feb-25	04-Mar-25
APP-3840	Review & Approve Service Entrance Equipment Warranty	21	12-Feb-25	04-Mar-25
APP-3850	Review & Approve Enclosed Switches Product Data	21	12-Feb-25	04-Mar-25
APP-3860	Review & Approve Enclosed Switches Test Reports	21	12-Feb-25	04-Mar-25
APP-3870	Review & Approve Motors, Motor Control Centers and Starters Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3880	Review & Approve Motors, Motor Control Centers and Starters Product Data	21	12-Feb-25	04-Mar-25
APP-3890	Review & Approve Motors, Motor Control Centers and Starters Field Test Reports	21	12-Feb-25	04-Mar-25
APP-3900	Review & Approve Lightning Protection Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3920	Review & Approve Lightning Protection Test Reports	21	12-Feb-25	04-Mar-25
APP-3930	Review & Approve Fiber Optic Cabling system Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3940	Review & Approve Fiber Optic Cabling system Product Data	21	12-Feb-25	04-Mar-25
APP-3950	Review & Approve Fiber Optic Cabling system Samples	21	12-Feb-25	04-Mar-25
APP-3960	Review & Approve Sound, Intercome & Security System Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3970	Review & Approve Sound, Intercome & Security System Programming Code and Password for the System	21	12-Feb-25	04-Mar-25
APP-3980	Review & Approve Sound, Intercome & Security System warranty	21	12-Feb-25	04-Mar-25
APP-3990	Review & Approve Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	21	12-Feb-25	04-Mar-25
APP-4000	Review & Approve Projection and Interactive Whiteboard Systems Wiring diagram	21	12-Feb-25	04-Mar-25
APP-4010	Review & Approve Self Corrective Clock System Shop Drawing	21	12-Feb-25	04-Mar-25
APP-4020	Review & Approve Self Corrective Clock System Product Data	21	12-Feb-25	04-Mar-25
APP-4030	Review & Approve Self Corrective Clock System Field Test Reports	21	12-Feb-25	04-Mar-25
APP-4040	Review & Approve Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	21	12-Feb-25	04-Mar-25
APP-4060	Review & Approve Steel Stairs Shop Drawings	21	12-Feb-25	04-Mar-25
APP-4070	Review & Approve Steel Stairs Product Data	21	12-Feb-25	04-Mar-25
APP-4080	Review & Approve Green School Submittal	21	12-Feb-25	04-Mar-25
APP-2260	Review & Approve Product Substitutions	21	13-Feb-25	05-Mar-25
APP-2270	Review & Approve Final Foundations Coordination Drawings	21	12-Mar-25	01-Apr-25
APP-2280	Review & Approve Final 1st Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2290	Review & Approve Final 2nd Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2300	Review & Approve Final 3rd Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2310	Review & Approve Final 4th Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2320	Review & Approve Final 5th Floor Coordination Drawings	21	03-May-25	23-May-25
MIL-1640	Provide Complete Set of Approved Coordination Drawings	0		23-May-25
APP-1810	Review & Approve Roof Dunnage	21	28-Jun-25	18-Jul-25
APP-2900	Review & Approve Excavated Material Disposal Plan	21	06-Sep-25	26-Sep-25
APP-4050	Review & Approve Soil Sampling Plan	21	06-Sep-25	26-Sep-25
APP-2910	Review & Approve Backfill & Resue Plan	21	04-Oct-25	24-Oct-25
APP-2330	Review & Approve Remedial Closure Report	21	30-Jul-26	19-Aug-26
Permits		501	30-Sep-24	30-Sep-26
PRE-2590	Meeting With SCA to Review The Permit Requirements	14	30-Sep-24	18-Oct-24
PRE-2600	Prepare & Submit Permit Waiver Requests to SCA Chief Project Officer	5	30-Sep-24	04-Oct-24
PRE-2630	Obtain Builders Pavement Permit	10	16-Sep-25	29-Sep-25

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
PRE-2640	Obtain Excavation & Shoring Permit	10	16-Sep-25	29-Sep-25
PRE-2650	Obtain Permit to Enter (PTE) Amtrak	10	16-Sep-25	29-Sep-25
PRE-2660	Obtain NYPA Permit	10	16-Sep-25	29-Sep-25
PRE-2540	SCA Work Notification	7	23-Sep-25	29-Sep-25
PRE-1660	DOB Permit & Insurance	3	25-Sep-25	29-Sep-25
PRE-1460	Obtain Construction Fences Permit	3	25-Sep-25	29-Sep-25
PRE-2570	Obtain Sidewalk Shed Permits	3	25-Sep-25	29-Sep-25
PRE-2610	Prepare & Submit FDNY Fuel Permit	10	06-Oct-25	20-Oct-25
PRE-2620	Review & Approve FDNY Fuel Permit	21	21-Oct-25	10-Nov-25
PER-2640	Obtain Emergency Generator Permit	5	03-Aug-26	07-Aug-26
PER-2650	Elevator Equipment Use Permit	10	17-Sep-26	30-Sep-26
Procurements		475	02-Jun-25	19-Sep-26
PRO-1590	Procure & Deliver Steel Columns	120	02-Jun-25	29-Sep-25
PRO-1120	Procure & Deliver Erosion Control and Sedimentation Devices	25	05-Sep-25	29-Sep-25
PRO-1420	Procure & Deliver Painting	70	30-Sep-25	08-Dec-25
PRO-1410	Procure & Deliver Door Frames	70	30-Sep-25	08-Dec-25
PRO-1200	Procure & Deliver Elevator Machine	112	30-Sep-25	19-Jan-26
PRO-1150	Procure & Deliver Gypsum Board	150	30-Sep-25	26-Feb-26
PRO-1160	Procure & Deliver Floorings	80	30-Sep-25	18-Dec-25
PRO-1170	Procure & Deliver Acosutical Ceiling Tiles	120	30-Sep-25	27-Jan-26
PRO-1190	Procure & Deliver Toilet Accessories	100	30-Sep-25	07-Jan-26
PRO-1000	Procure & Deliver Kitchen Equipment	180	30-Sep-25	28-Mar-26
PRO-1140	Procure & Deliver Lighting Fixtures	60	30-Sep-25	28-Nov-25
PRO-1010	Procure & Deliver Furnitures	130	30-Sep-25	06-Feb-26
PRO-1020	Procure & Deliver Mechanical Piping	70	30-Sep-25	08-Dec-25
PRO-1030	Procure & Deliver Mechanical Ducts	70	30-Sep-25	08-Dec-25
PRO-1050	Procure & Deliver Electrical Equipment	130	30-Sep-25	06-Feb-26
PRO-1060	Procure & Deliver Plumbing Fixtures	100	30-Sep-25	07-Jan-26
PRO-1070	Procure & Deliver Wood Doors	50	30-Sep-25	18-Nov-25
PRO-1090	Procure & Deliver Fire Sprinklers	100	30-Sep-25	07-Jan-26
PRO-1110	Procure & Deliver Fire Detectors & Alarms	60	30-Sep-25	28-Nov-25
PRO-1210	Procure & Deliver Signs	70	30-Sep-25	08-Dec-25
PRO-1220	Procure & Deliver Windows & Storefronts	154	30-Sep-25	02-Mar-26
PRO-1250	Procure & Deliver Plumbing Pipes	60	30-Sep-25	28-Nov-25
PRO-1260	Procure & Deliver Electrical Wires & Conduits	130	30-Sep-25	06-Feb-26
PRO-1270	Procure & Deliver Mechanical Pumps	70	30-Sep-25	08-Dec-25
PRO-1280	Procure & Deliver Fire Protection Pumps	70	30-Sep-25	08-Dec-25
PRO-1290	Procure & Deliver Plumbing Pumps	250	30-Sep-25	06-Jun-26
PRO-1310	Procure & Deliver Telecommunication System	60	30-Sep-25	28-Nov-25
PRO-1330	Procure & Deliver Cameras	60	30-Sep-25	28-Nov-25
PRO-1360	Procure & Deliver Metal Panel Ceilings	120	30-Sep-25	27-Jan-26
PRO-1380	Procure & Deliver Roof Dunnage	100	30-Sep-25	07-Jan-26
PRO-1470	Procure & Deliver Cabinet Heaters	126	30-Sep-25	02-Feb-26
PRO-1480	Procure & Deliver Chillers	170	30-Sep-25	18-Mar-26

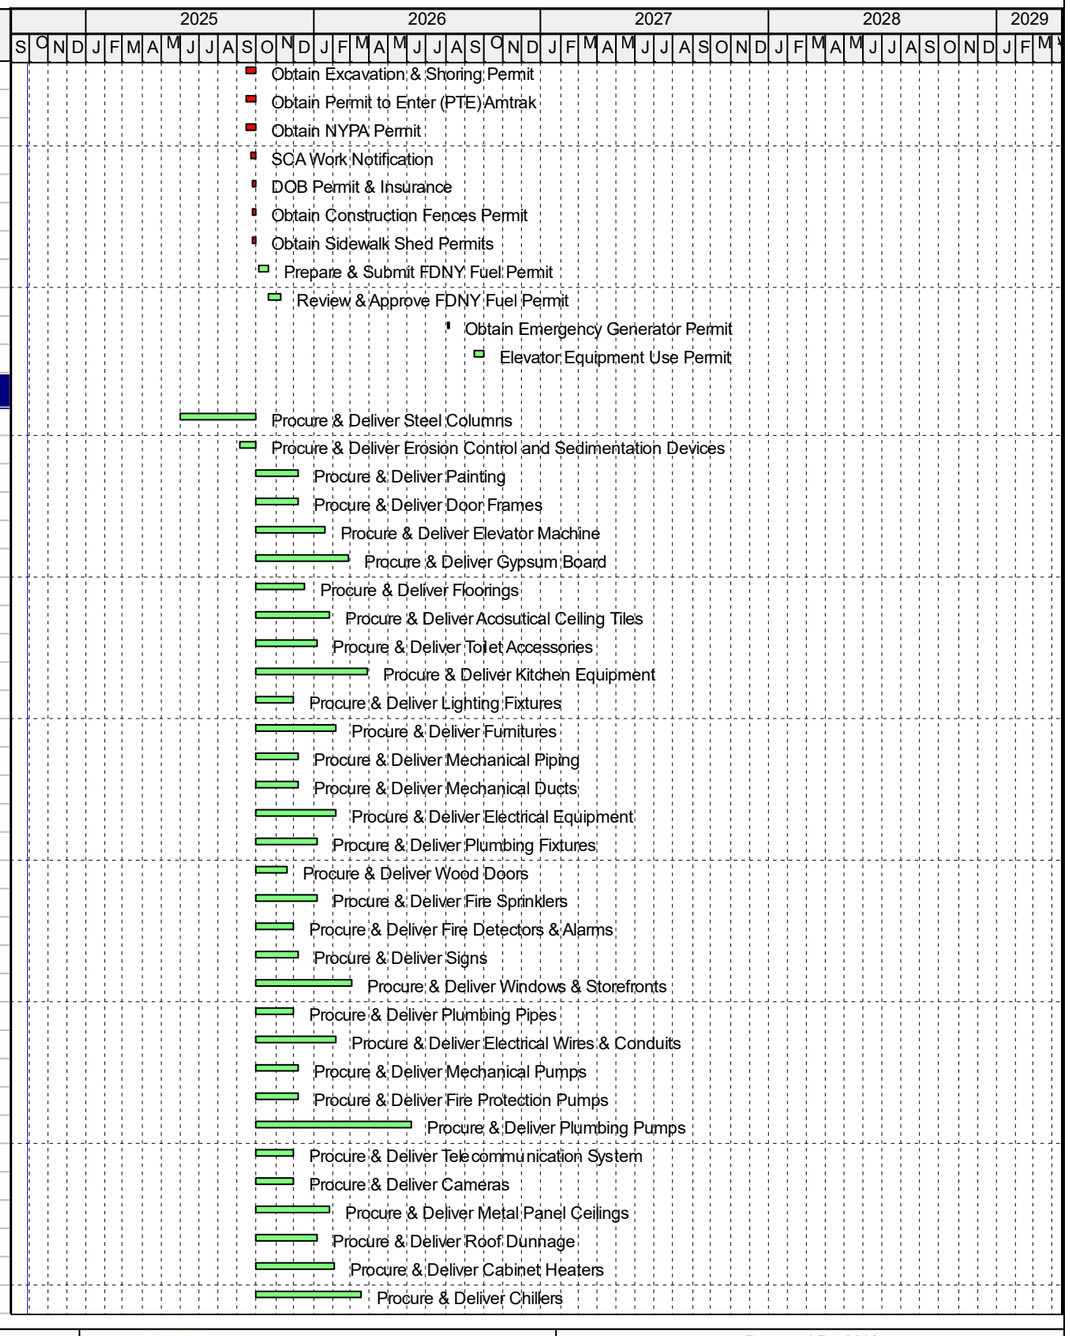

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
PRO-1490	Procure & Deliver Air Handling Units	250	30-Sep-25	06-Jun-26
PRO-1500	Procure & Deliver Boilers	84	30-Sep-25	22-Dec-25
PRO-1510	Procure & Deliver Emergency Generator	290	30-Sep-25	16-Jul-26
PRO-1520	Procure & Deliver Switch Gears	250	30-Sep-25	06-Jun-26
PRO-1530	Procure & Deliver Hydraulic Vertical Wheelchair Lift	90	30-Sep-25	28-Dec-25
PRO-1560	Procure & Deliver Gymnasium Equipment	180	30-Sep-25	28-Mar-26
PRO-1570	Procure & Deliver Precast Sandwich Panels	112	30-Sep-25	19-Jan-26
PRO-1580	Procure & Deliver Metal Deck	70	30-Sep-25	08-Dec-25
PRO-1600	Procure & Deliver Trusses	60	30-Sep-25	28-Nov-25
PRO-1610	Procure & Deliver Prefabricated Expansion Joint Covers	60	30-Sep-25	28-Nov-25
PRO-1620	Procure & Deliver Security Screens & Barriers	60	30-Sep-25	28-Nov-25
PRO-1630	Procure & Deliver Wood Flooring	120	30-Sep-25	27-Jan-26
PRO-1640	Procure & Deliver Concrete Floating Floor Assembly	120	30-Sep-25	27-Jan-26
PRO-1660	Procure & Deliver Auditorium Television Studio Dimming System	90	30-Sep-25	28-Dec-25
PRO-2010	Procure & Deliver Steel Stairs Components	120	30-Sep-25	27-Jan-26
PRO-2020	Procure & Deliver Flagpole	60	30-Sep-25	28-Nov-25
PRO-2030	Procure & Deliver Bleachers	130	30-Sep-25	06-Feb-26
PRO-2040	Procure & Deliver VAV Units	170	30-Sep-25	18-Mar-26
PRO-2050	Procure & Deliver Furnitures (Owner Responsibility)	130	30-Sep-25	06-Feb-26
PRO-1450	Procure & Deliver Playground Equipment	60	09-Dec-25	06-Feb-26
PRO-2000	Procure & Deliver Key Cutting Machine	74	08-Jul-26	19-Sep-26
Utilities Coordination		450	07-Oct-24	27-Jul-26
CON-7960	Obtain Gas Meter Layout From CON-ED	5	07-Oct-24	11-Oct-24
MIL-1660	Start Security Guard Services (30 Days From NTP)	0	30-Oct-24	
CON-8010	Coordination With CON-ED For Temporary Electrical Power	10	07-Nov-24	21-Nov-24
CON-8020	Scheduling With CON-ED For Temporary Electrical Power	7	22-Nov-24	03-Dec-24
CON-8030	Procurement From CON-ED For Temporary Electrical Power	20	30-Sep-25	19-Oct-25
CON-8040	CON-ED Work For Temporary Electrical Power	10	20-Oct-25	31-Oct-25
CON-8050	Available Temporary Electrical Power For Testing MEP Equipment	0		31-Oct-25
CON-7970	Coordinate With CON-ED For Gas Service	7	16-Apr-26	24-Apr-26
PRO-1990	Procure & Deliver Gas Meter Rig	60	25-Apr-26	23-Jun-26
CON-8060	CON-ED - Switchgear Inspection	4	15-Jun-26	18-Jun-26
CON-8070	CON-ED - Pull Power Cable to the Building	10	22-Jun-26	06-Jul-26
CON-7990	Gas Authorization	5	24-Jun-26	30-Jun-26
CON-8000	Pink Slip	5	01-Jul-26	08-Jul-26
CON-8080	CON-ED - Terminate Power Cables	10	07-Jul-26	20-Jul-26
CON-8090	CON-ED - Energize to the Building	5	21-Jul-26	27-Jul-26
Preliminary		513	30-Sep-24	19-Oct-26
MIL-2522	Site Access	365	30-Sep-24	29-Sep-25
CON-99257	Subcontractor Buyout	10	30-Sep-24	11-Oct-24
CON-1000	Mobilization	4	30-Sep-25	03-Oct-25
MIL-1060	Mobilization Start	0	30-Sep-25	
CON-7740	Protection Of All Overhead & Underground Utilities	263	30-Sep-25	19-Oct-26
CON-9000	Protection & Restoration the adjacent Properties to Original Condition	263	30-Sep-25	19-Oct-26

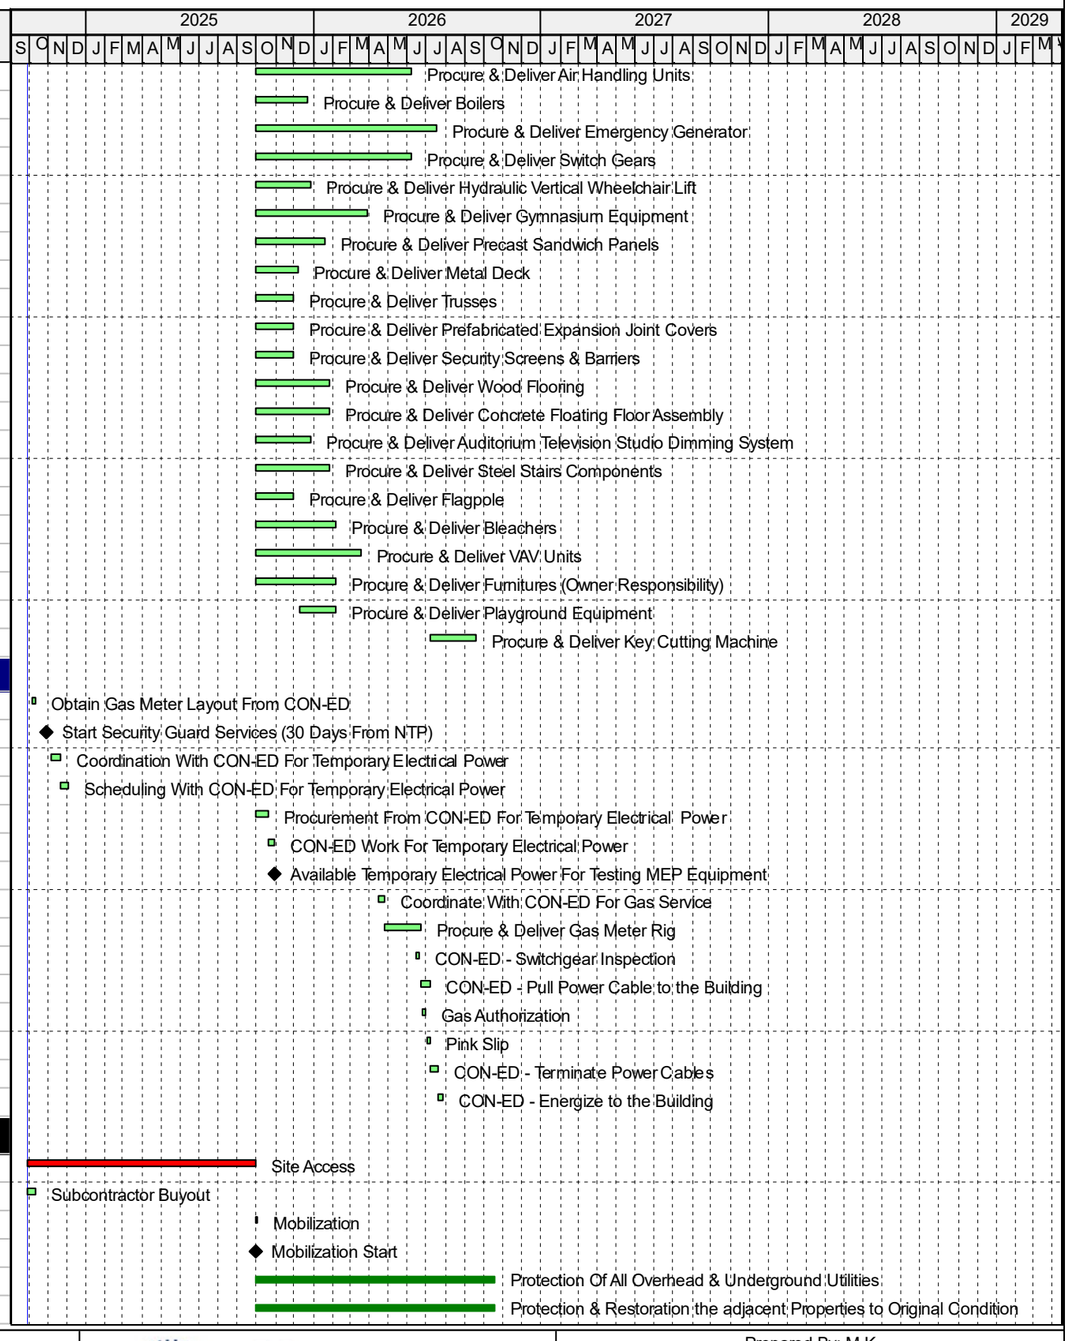

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
MIL-1710	Complete Mobilization	0		03-Oct-25
CON-1080	Install Erosion Control Devices	2	06-Oct-25	07-Oct-25
CON-1010	Install Construction Signs	2	06-Oct-25	07-Oct-25
CON-1030	Install Construction Fences	2	06-Oct-25	07-Oct-25
CON-9120	Soli Sampling	2	06-Oct-25	07-Oct-25
CON-7750	Install Field Offices	5	08-Oct-25	15-Oct-25
CON-9140	Excavation	5	08-Oct-25	15-Oct-25
CON-8390	Install Sidewalk Sheds -South Elevation	4	29-Dec-25	02-Jan-26
CON-8400	Install Sidewalk Sheds -East Elevation	4	29-Dec-25	02-Jan-26
MIL-1720	Start Sidewalk Bridge Installations	0	29-Dec-25	
SSDS System		144	16-Oct-25	13-May-26
CON-9898	Install Gas Permeable Aggregate -1st Floor	3	16-Oct-25	20-Oct-25
CON-98947	Install 4" slotted schedule 80 PVC Piping -1st Floor	3	16-Oct-25	20-Oct-25
CON-9888	Install Liquid Boot VI-20 Geomembrane -1st Floor	2	21-Oct-25	22-Oct-25
CON-1020	Install 60 Dry MILS Liquid Boot -1st Floor	3	23-Oct-25	27-Oct-25
CON-9777	Install Liquid Ultrashield G-1000 -1st Floor	2	24-Oct-25	27-Oct-25
CON-1740	Install SSDS Risers -SSDS System -2nd Floor	2	02-Mar-26	03-Mar-26
CON-1840	Install SSDS Risers -SSDS System -3rd Floor	2	04-Mar-26	05-Mar-26
CON-1970	Install SSDS Risers -SSDS System -4th Floor	2	06-Mar-26	09-Mar-26
CON-2000	Install SSDS Risers -SSDS System -5th Floor	1	09-Mar-26	09-Mar-26
CON-3230	Install SSDS Risers -SSDS System -1st Floor	2	14-Apr-26	15-Apr-26
CON-4500	Install SSDS Control Panel -1st Floor	5	07-May-26	13-May-26
SOG		26	28-Oct-25	04-Dec-25
CON-1040	F/R/P Concrete Walls & Beams -1st Floor	10	28-Oct-25	10-Nov-25
CON-1050	Install Underground Conduits & Wires -1st Floor	6	12-Nov-25	19-Nov-25
CON-1060	Backfilling & Compaction -1st Floor	6	12-Nov-25	19-Nov-25
CON-1070	F/R/P SOG -1st Floor	10	20-Nov-25	04-Dec-25
Floor Drains		70	27-Nov-25	11-Mar-26
CON-4920	Install Floor Drains & Clean-outs -1st Floor	5	27-Nov-25	04-Dec-25
CON-3160	Install Floor Drains & Clean-outs -2nd Floor	5	19-Dec-25	26-Dec-25
CON-3320	Install Floor Drains & Clean-outs -3rd Floor	5	08-Jan-26	14-Jan-26
CON-3530	Install Floor Drains & Clean-outs -4th Floor	5	28-Jan-26	03-Feb-26
CON-3610	Install Floor Drains & Clean-outs -5th Floor	5	13-Feb-26	20-Feb-26
CON-1770	Install Roof Drains & Clean outs -Roof Floor	5	26-Feb-26	04-Mar-26
CON-2070	Install Roof Drains & Clean outs - Mechanical Work - Roof Bulkhead	5	05-Mar-26	11-Mar-26
Structural Steel Work		68	05-Dec-25	16-Mar-26
CON-98787	Install Steel Columns -1st Floor	7	05-Dec-25	15-Dec-25
MIL-1810	Crane Mobilization-Steel Installation start	0	05-Dec-25	
CON-1090	Install Trusses -1st Floor	3	16-Dec-25	18-Dec-25
CON-1100	Install Framing Beams -1st Floor	4	16-Dec-25	19-Dec-25
CON-1150	Install Steel Canopy Framing -2nd Floor	5	29-Dec-25	05-Jan-26
CON-1170	Install Steel Columns -2nd Floor	3	29-Dec-25	31-Dec-25
CON-1190	Install Trusses -2nd Floor	4	02-Jan-26	07-Jan-26

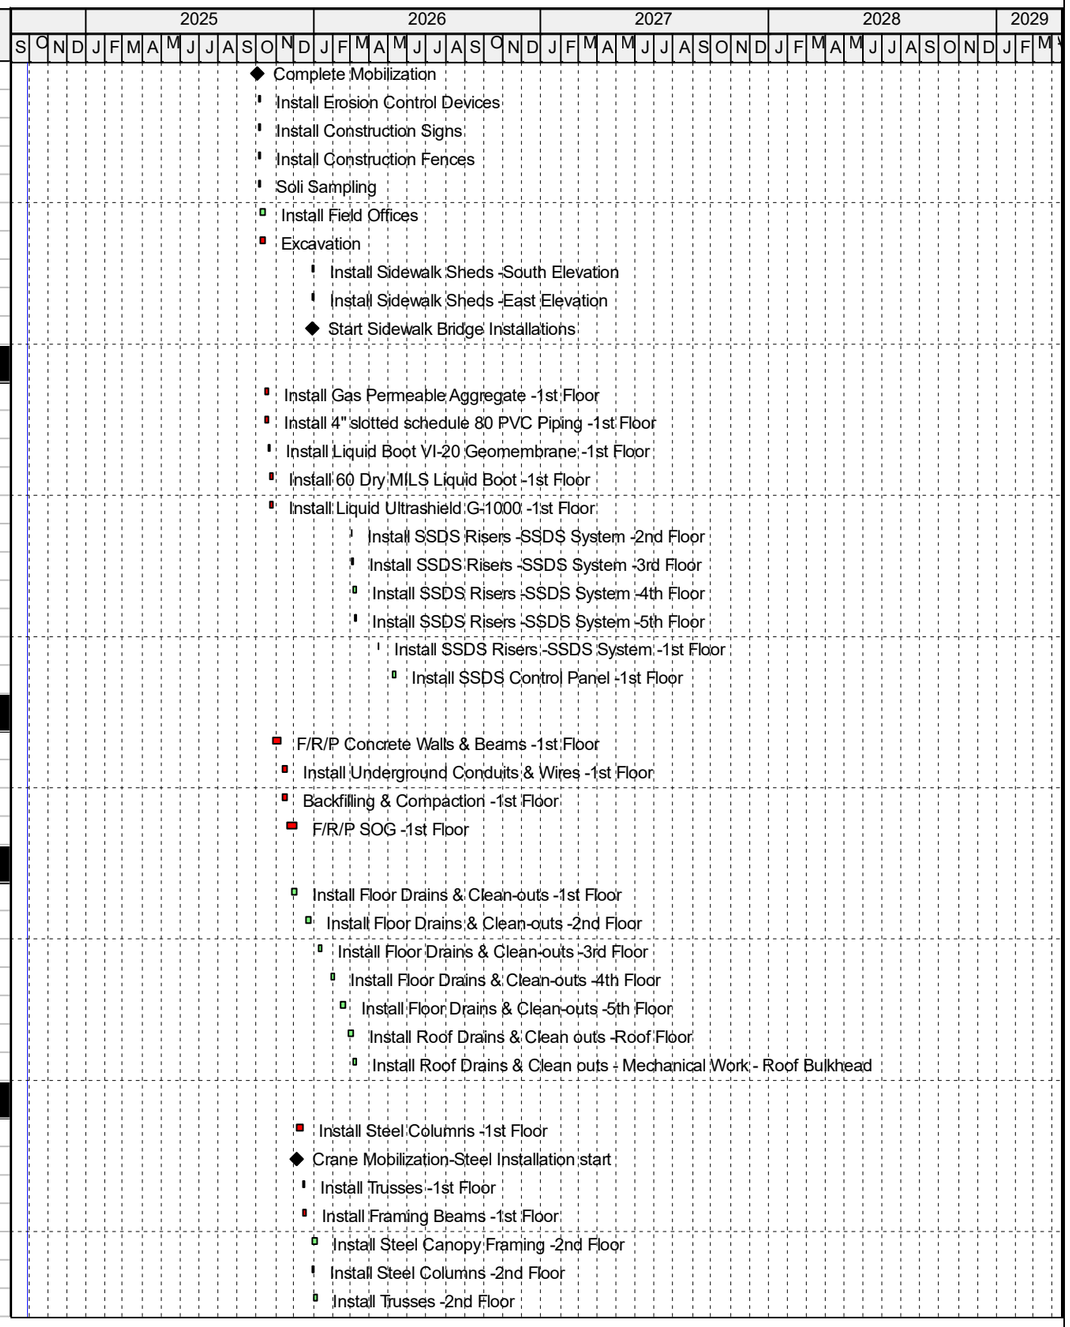

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1200	Install Framing Beams -2nd Floor	5	02-Jan-26	08-Jan-26
CON-1240	Install Steel Columns - 3rd Floor	4	15-Jan-26	21-Jan-26
CON-1260	Install Trusses - 3rd Floor	3	22-Jan-26	26-Jan-26
CON-1270	Install Framing Beams - 3rd Floor	5	22-Jan-26	28-Jan-26
CON-99277	Install Steel Stairs -1st Floor	7	28-Jan-26	05-Feb-26
CON-1330	Install Steel Columns - 4th Floor	4	04-Feb-26	09-Feb-26
CON-99287	Install Steel Stairs -2nd Floor	3	06-Feb-26	10-Feb-26
CON-1360	Install Trusses - 4th Floor	3	10-Feb-26	12-Feb-26
CON-1370	Install Framing Beams - 4th Floor	5	10-Feb-26	17-Feb-26
CON-99297	Install Steel Stairs- 3rd Floor	4	11-Feb-26	17-Feb-26
CON-1440	Install Steel Columns - 5th Floor	3	23-Feb-26	25-Feb-26
CON-1460	F/R/P Piers - 5th Floor	5	23-Feb-26	27-Feb-26
CON-99307	Install Steel Stairs - 4th Floor	4	23-Feb-26	26-Feb-26
CON-1540	Install Trusses - 5th Floor	2	26-Feb-26	27-Feb-26
CON-1550	Install Framing Beams - 5th Floor	3	26-Feb-26	02-Mar-26
CON-99317	Install Steel Stairs - 5th Floor	3	27-Feb-26	03-Mar-26
CON-1620	Install Dunnage - 5th Floor	8	02-Mar-26	11-Mar-26
CON-1750	F/R/P Concrete Columns -Bulkhead	3	05-Mar-26	09-Mar-26
CON-1760	Install Dunnage-Roof Floor	8	05-Mar-26	16-Mar-26
CON-2060	Install Hoist Beam-Bulkhead	1	12-Mar-26	12-Mar-26
Metal Deck Concrete Slabs		54	22-Dec-25	11-Mar-26
CON-1110	Install Metal Deck Slab -2nd Floor	4	22-Dec-25	26-Dec-25
MIL-1120	Metal Decking Start	0	22-Dec-25	
CON-1210	Install Metal Deck Slab - 3rd Floor	4	09-Jan-26	14-Jan-26
CON-1290	Install Metal Deck Slab - 4th Floor	4	29-Jan-26	03-Feb-26
CON-1380	Install Metal Deck Slab - 5th Floor	3	18-Feb-26	20-Feb-26
CON-1720	Install Metal Deck Slab -Roof Floor	2	03-Mar-26	04-Mar-26
CON-1980	F/R/P Bulkhead Slab -Bulkhead	2	10-Mar-26	11-Mar-26
MIL-1170	Finish Concrete Work	0		11-Mar-26
MEP Hangers		49	22-Dec-25	04-Mar-26
CON-1130	Install MEP Hangers & Sleeves- 2nd Floor	4	22-Dec-25	26-Dec-25
CON-1230	Install MEP Hangers & Sleeves-3rd Floor	4	09-Jan-26	14-Jan-26
CON-1310	Install MEP Hangers & Sleeves-4th Floor	4	29-Jan-26	03-Feb-26
CON-1400	Install MEP Hangers & Sleeves-5th Floor	4	17-Feb-26	20-Feb-26
CON-1610	Install MEP Hangers & Sleeves-Roof Floor	4	27-Feb-26	04-Mar-26
Fireproofing Spray		23	03-Mar-26	02-Apr-26
CON-1180	Spray Fireproofing - 1st Floor	5	03-Mar-26	09-Mar-26
CON-1220	Spray Fireproofing - 2nd Floor	5	10-Mar-26	16-Mar-26
CON-1300	Spray Fireproofing - 3rd Floor	5	17-Mar-26	23-Mar-26
CON-1390	Spray Fireproofing - 4th Floor	5	24-Mar-26	30-Mar-26
CON-1730	Spray Fireproofing - 5th Floor	3	31-Mar-26	02-Apr-26
Material Hoist		182	29-Dec-25	17-Sep-26
CON-1160	Hoist Material Design	10	29-Dec-25	12-Jan-26

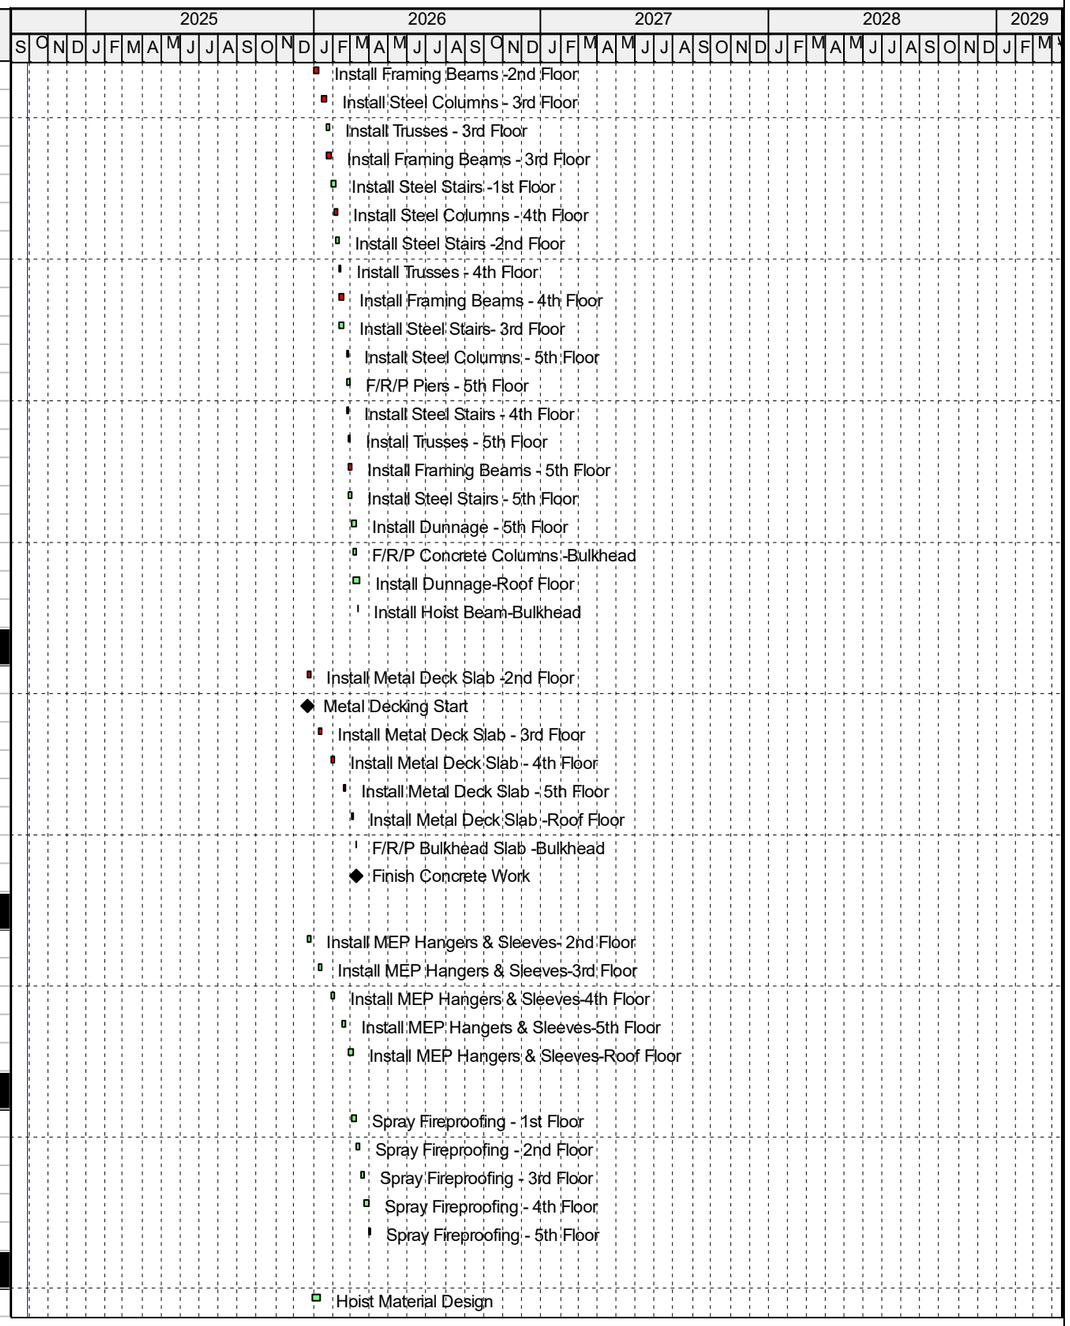

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1250	Approval of Hoist Design	7	13-Jan-26	19-Jan-26
CON-1280	Install Elevator Hoist Pad	5	20-Jan-26	26-Jan-26
CON-1320	Erect Material Hoist	5	27-Jan-26	02-Feb-26
CON-5040	Dismantle Hoist	2	10-Sep-26	11-Sep-26
CON-5170	Demolish Hoist Pad	2	14-Sep-26	15-Sep-26
CON-5250	Hoist In-Fill	2	16-Sep-26	17-Sep-26
Temporary Standpipe		9	29-Dec-25	09-Jan-26
CON-3270	Install Temporary Standpipe	9	29-Dec-25	09-Jan-26
Layout		34	23-Feb-26	09-Apr-26
CON-1420	Layout -2nd Floor	3	23-Feb-26	25-Feb-26
MIL-1140	Layout Start	0	23-Feb-26	
CON-1530	Layout -3rd Floor	3	26-Feb-26	02-Mar-26
CON-1670	Layout -4th Floor	3	03-Mar-26	05-Mar-26
CON-1930	Layout -5th Floor	3	06-Mar-26	10-Mar-26
CON-2910	Layout -1st Floor	3	07-Apr-26	09-Apr-26
MIL-1220	Layout Finish	0		09-Apr-26
Masonry		37	23-Feb-26	14-Apr-26
MIL-1150	Masonry Walls Start	0	23-Feb-26	
CON-1430	Install Unit Masonry Mock-Up	1	23-Feb-26	23-Feb-26
CON-1470	Approve Unit Masonry Mock-Up	4	24-Feb-26	27-Feb-26
CON-1570	Install CMU Walls -2nd Floor	3	02-Mar-26	04-Mar-26
CON-1660	Install CMU Walls -3rd Floor	3	05-Mar-26	09-Mar-26
MIL-2932	Start Masonry Inspection	0	05-Mar-26	
CON-1920	Install CMU Walls -4th Floor	3	10-Mar-26	12-Mar-26
CON-2030	Install CMU Walls -5th Floor	3	13-Mar-26	17-Mar-26
CON-3090	Install CMU Walls -1st Floor	3	10-Apr-26	14-Apr-26
MIL-2942	Start In-Wall Inspection	0	10-Apr-26	
Duct Risers		32	23-Feb-26	07-Apr-26
CON-1410	Install Duct Risers-2nd Floor	1	23-Feb-26	23-Feb-26
MIL-1180	MEP Risers Start	0	23-Feb-26	
CON-1490	Install Duct Risers -3rd Floor	2	24-Feb-26	25-Feb-26
CON-1560	Install Duct Risers -4th Floor	2	26-Feb-26	27-Feb-26
CON-1630	Install Duct Risers-5th Floor	2	02-Mar-26	03-Mar-26
CON-2900	Install Duct Risers-1st Floor	1	07-Apr-26	07-Apr-26
Mechanical Risers		33	24-Feb-26	09-Apr-26
CON-1500	Install Mechanical Piping Risers-2nd Floor	2	24-Feb-26	25-Feb-26
CON-1590	Install Mechanical Piping Risers -3rd Floor	2	26-Feb-26	27-Feb-26
CON-1690	Install Mechanical Piping Risers -4th Floor	2	02-Mar-26	03-Mar-26
CON-1790	Install Mechanical Piping Risers-5th Floor	2	04-Mar-26	05-Mar-26
CON-3060	Install Mechanical Piping Risers-1st Floor	2	08-Apr-26	09-Apr-26
Duct Leak Test		32	24-Feb-26	08-Apr-26
CON-1510	Duct Leak Test -2nd Floor	2	24-Feb-26	25-Feb-26

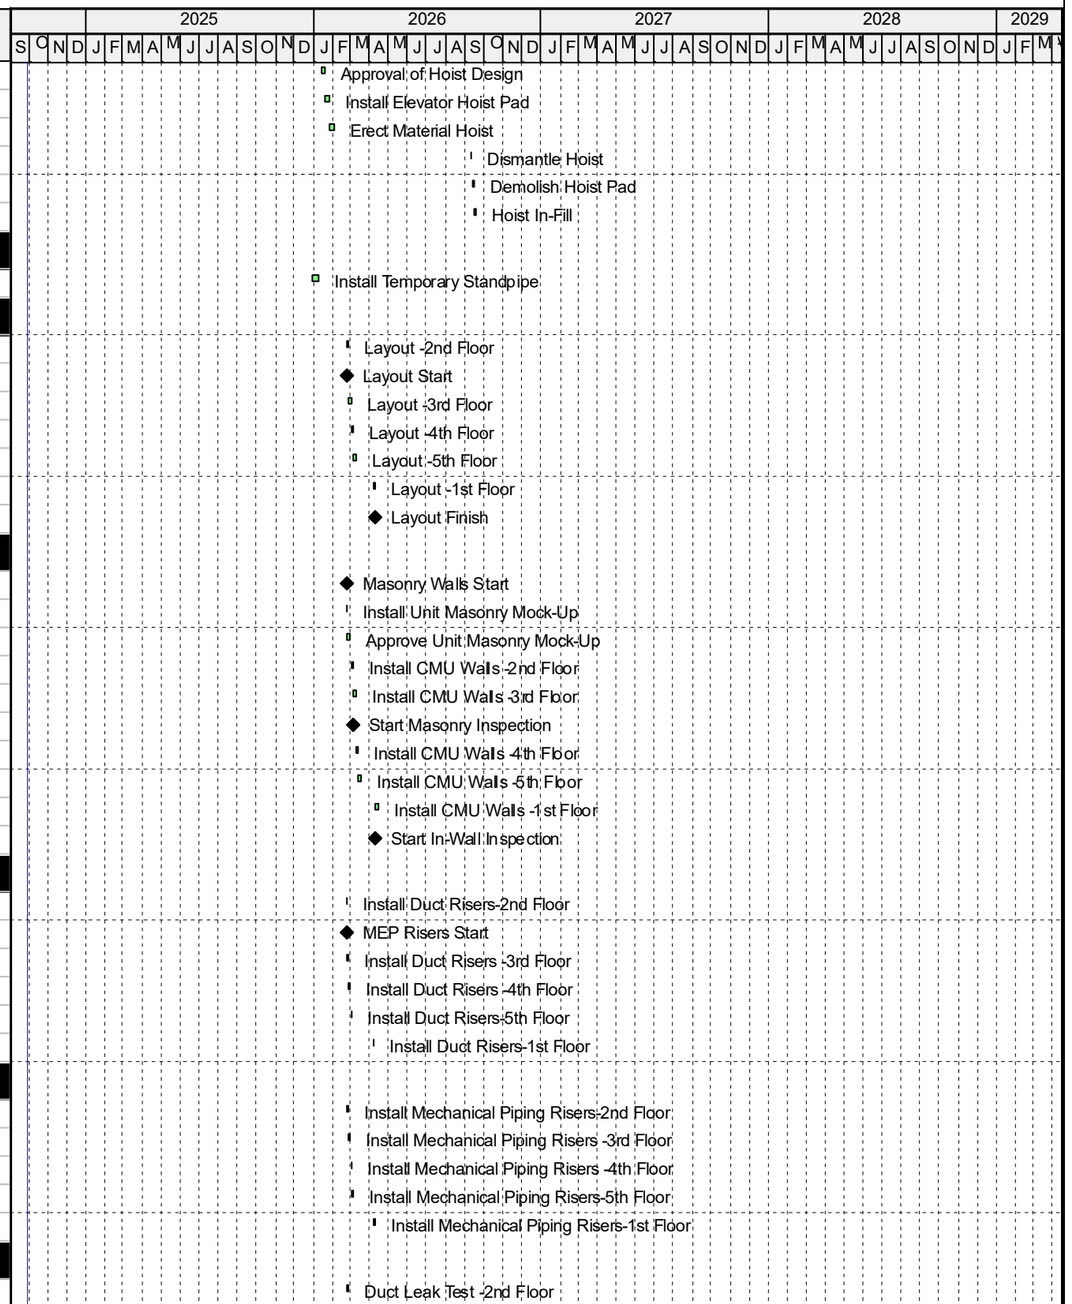

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1600	Duct Leak Test -3rd Floor	2	26-Feb-26	27-Feb-26
CON-1700	Duct Leak Test -4th Floor	2	02-Mar-26	03-Mar-26
CON-1810	Duct Leak Test -5th Floor	1	04-Mar-26	04-Mar-26
CON-3070	Duct Leak Test -1st Floor	1	08-Apr-26	08-Apr-26
Duct Rough-ins		36	24-Feb-26	14-Apr-26
CON-1480	Rough-in Duct Work -2nd Floor	4	24-Feb-26	27-Feb-26
MIL-1210	Duct Rough-ins Start	0	24-Feb-26	
CON-1890	Rough-in Duct Work -3rd Floor	5	02-Mar-26	06-Mar-26
CON-2170	Rough-in Duct Work -4th Floor	5	09-Mar-26	13-Mar-26
CON-2300	Rough-in Duct Work-5th Floor	5	16-Mar-26	20-Mar-26
CON-3120	Rough-in Duct Work -1st Floor	4	09-Apr-26	14-Apr-26
MIL-1290	Duct Rough-ins Finish	0		14-Apr-26
Top & Bottom Track		35	26-Feb-26	15-Apr-26
CON-1520	Install Top & Bottom Track-2nd Floor	4	26-Feb-26	03-Mar-26
MIL-1160	Top & Bottom Track Start	0	26-Feb-26	
CON-1650	Install Top & Bottom Track-3rd Floor	4	04-Mar-26	09-Mar-26
CON-1910	Install Top & Bottom Track-4th Floor	4	10-Mar-26	13-Mar-26
CON-2020	Install Top & Bottom Track-5th Floor	4	16-Mar-26	19-Mar-26
CON-3080	Install Top & Bottom Track -1st Floor	4	10-Apr-26	15-Apr-26
MIL-1250	Top & Bottom Track Finish	0		15-Apr-26
VAV Boxes & Sound Attenuator		25	19-Mar-26	22-Apr-26
CON-3980	Install VAV Boxes & Sound Attenuator Devices-2nd Floor	5	19-Mar-26	25-Mar-26
CON-4140	Install VAV Boxes & Sound Attenuator Devices-3rd Floor	5	26-Mar-26	01-Apr-26
CON-4220	Install VAV Boxes & Sound Attenuator Devices-4th Floor	5	02-Apr-26	08-Apr-26
CON-4330	Install VAV Boxes & Sound Attenuator Devices-5th Floor	5	09-Apr-26	15-Apr-26
CON-3970	Install VAV Boxes & Sound Attenuator Devices- 1st Floor	5	16-Apr-26	22-Apr-26
Plumbing Risers		33	26-Feb-26	13-Apr-26
CON-1580	Install Plumbing Risers -2nd Floor	2	26-Feb-26	27-Feb-26
CON-1680	Install Plumbing Risers -3rd Floor	2	02-Mar-26	03-Mar-26
CON-1780	Install Plumbing Risers -4th Floor	2	04-Mar-26	05-Mar-26
CON-1940	Install Plumbing Risers-5th Floor	1	06-Mar-26	06-Mar-26
CON-3140	Install Plumbing Risers -1st Floor	2	10-Apr-26	13-Apr-26
Interior Wall Framing		36	04-Mar-26	22-Apr-26
CON-1640	Install Wall Steel Studs & Framing-2nd Floor	5	04-Mar-26	10-Mar-26
CON-1900	Install Wall Steel Studs & Framing-3rd Floor	5	10-Mar-26	16-Mar-26
CON-2010	Install Wall Steel Studs & Framing-4th Floor	5	16-Mar-26	20-Mar-26
CON-2200	Install Wall Steel Studs & Framing-5th Floor	5	23-Mar-26	27-Mar-26
CON-3240	Install Wall Steel Studs & Framing -1st Floor	5	16-Apr-26	22-Apr-26
Electrical Risers		94	03-Dec-25	17-Apr-26
Power Risers		92	03-Dec-25	15-Apr-26
CON-99327	Install Lightning Protection System-1st Floor	2	03-Dec-25	04-Dec-25
CON-1710	Install Power Risers-2nd Floor	2	02-Mar-26	03-Mar-26

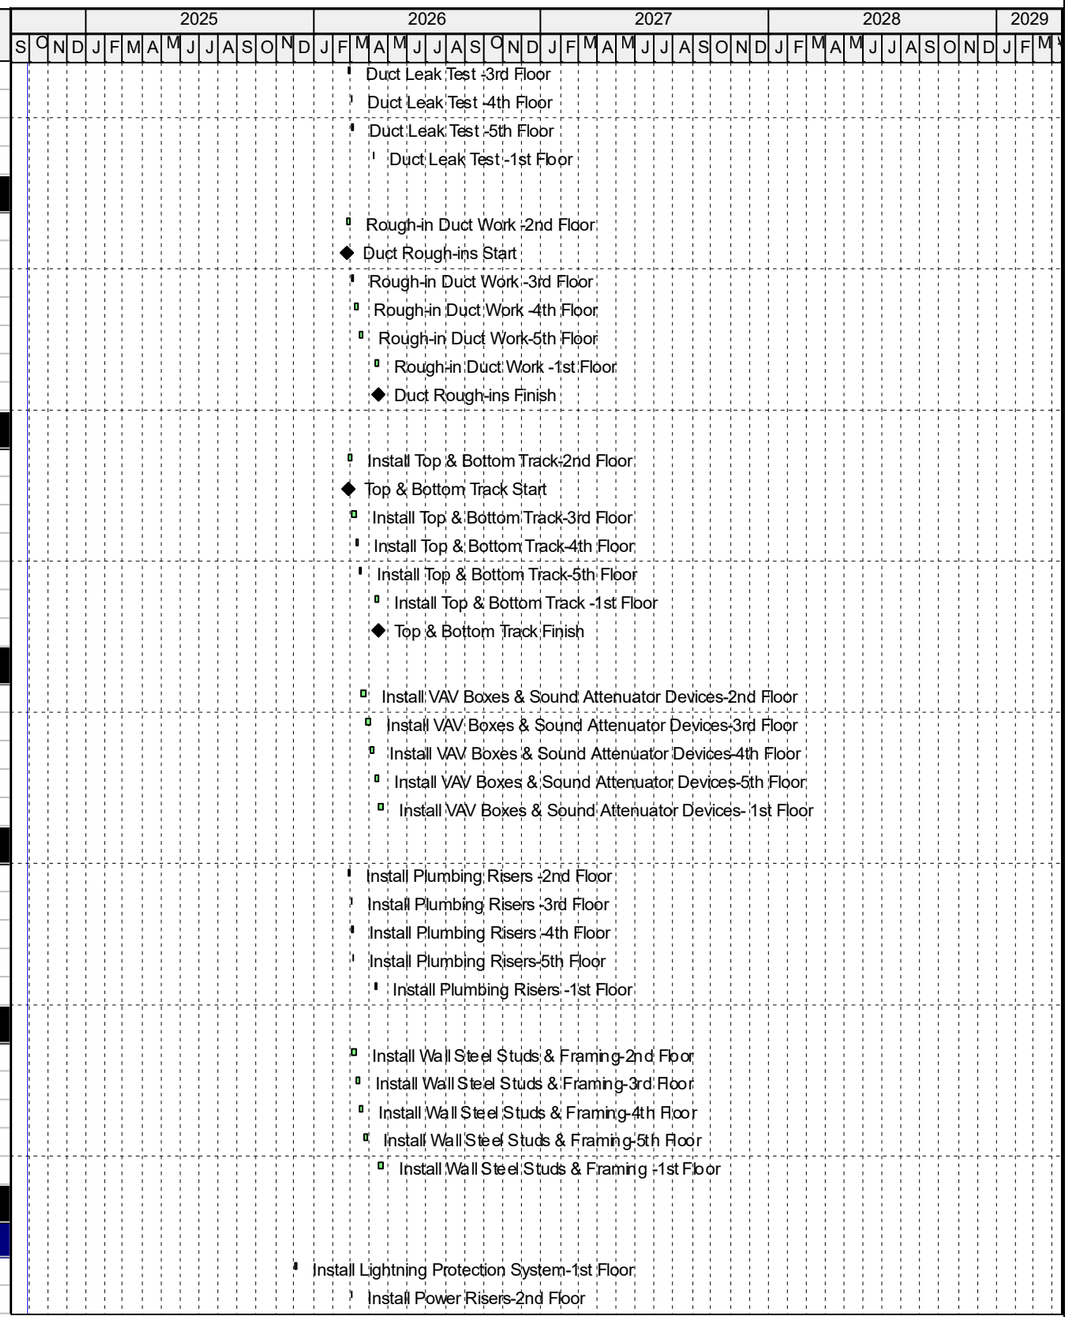

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1820	Install Power Risers-3rd Floor	2	04-Mar-26	05-Mar-26
CON-1960	Install Power Risers-4th Floor	2	06-Mar-26	09-Mar-26
CON-2050	Install Power Risers-5th Floor	3	10-Mar-26	12-Mar-26
CON-99337	Install Lightning Protection system -5th Floor	3	13-Mar-26	17-Mar-26
CON-3260	Install Power Risers-1st Floor	2	14-Apr-26	15-Apr-26
Low Voltage Risers		33	04-Mar-26	17-Apr-26
CON-1800	Install Low Voltage Risers-2nd Floor	2	04-Mar-26	05-Mar-26
CON-1950	Install Low Voltage Risers-3rd Floor	2	06-Mar-26	09-Mar-26
CON-2040	Install Low Voltage Risers-4th Floor	2	10-Mar-26	11-Mar-26
CON-2100	Install Low Voltage Risers-5th Floor	3	13-Mar-26	17-Mar-26
CON-3350	Install Low Voltage Risers-1st Floor	2	16-Apr-26	17-Apr-26
Mechanical Piping Rough-ins		36	02-Mar-26	20-Apr-26
Hot Water Piping		36	02-Mar-26	20-Apr-26
CON-1850	Rough-in Hot Water Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-2130	Rough-in Hot Water Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-2260	Rough-in Hot Water Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-2440	Rough-in Hot Water Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-3460	Rough-in Hot Water Piping-1st Floor	4	15-Apr-26	20-Apr-26
Chilled Glycol Piping		36	02-Mar-26	20-Apr-26
CON-1860	Rough-in Hot Glycol Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1870	Rough-in Chilled Glycol Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-2140	Rough-in Hot Glycol Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-2150	Rough-in Chilled Glycol Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-2270	Rough-in Hot Glycol Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-2280	Rough-in Chilled Glycol Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-2450	Rough-in Hot Glycol Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-2460	Rough-in Chilled Glycol Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-3470	Rough-in Hot Glycol Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3480	Rough-in Chilled Glycol Piping-1st Floor	4	15-Apr-26	20-Apr-26
Refrigerant Piping		36	02-Mar-26	20-Apr-26
CON-1880	Rough-in Refrigerant Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-2160	Rough-in Refrigerant Piping-3rd Floor	7	09-Mar-26	17-Mar-26
CON-2290	Rough-in Refrigerant Piping-4th Floor	7	16-Mar-26	24-Mar-26
CON-2470	Rough-in Refrigerant Piping-5th Floor	7	23-Mar-26	31-Mar-26
CON-3490	Rough-in Refrigerant Piping-1st Floor	4	15-Apr-26	20-Apr-26
Elevations		44	05-Mar-26	05-May-26
Elevations Mock-Up		14	05-Mar-26	24-Mar-26
CON-1830	Install Insulated Precast Concrete Sandwich Panel - Mock Up	2	05-Mar-26	06-Mar-26
MIL-1830	Crane Mobilization-Precast Sandwich Panels Installation Start	0	05-Mar-26	
CON-1990	Approve Insulated Precast Concrete Sandwich Panel - Mock Up	2	09-Mar-26	10-Mar-26
CON-2110	Install & Windows Mock-Up	3	11-Mar-26	13-Mar-26
CON-2210	Approve Windows Mock-Up	2	16-Mar-26	17-Mar-26

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2220	Install Storefront System Mock-Up	3	18-Mar-26	20-Mar-26
CON-2240	Approve Storefront System Mock-Up	2	23-Mar-26	24-Mar-26
Precast Sandwich Panel		30	25-Mar-26	05-May-26
CON-2380	Install Insulated Precast Concrete Sandwich Panel - West Elevation	3	25-Mar-26	27-Mar-26
CON-2420	Install Insulated Precast Concrete Sandwich Panel - South Elevation	5	25-Mar-26	31-Mar-26
CON-2610	Install Insulated Precast Concrete Sandwich Panel - East Elevation	4	01-Apr-26	06-Apr-26
CON-2730	Install Insulated Precast Concrete Sandwich Panel - North Elevation	4	01-Apr-26	06-Apr-26
MIL-1840	Crane Mobilization-Precast Sandwich Panels Installation Finish	0		06-Apr-26
CON-3220	Dismantle Sidewalk Sheds- South Elevation	2	29-Apr-26	30-Apr-26
CON-3630	Dismantle Sidewalk Sheds- East Elevation	2	04-May-26	05-May-26
MIL-1730	Sidewalk Sheds Dismantle Complete	0		05-May-26
Windows		25	30-Mar-26	01-May-26
CON-2400	Install Windows -West Elevation	5	30-Mar-26	03-Apr-26
CON-2410	Install Storefront System-West Elevation	5	30-Mar-26	03-Apr-26
MIL-1740	Start Windows	0	30-Mar-26	
CON-2590	Install Windows - South Elevation	10	01-Apr-26	14-Apr-26
CON-2600	Install Storefront System- South Elevation	10	01-Apr-26	14-Apr-26
CON-2570	Field Testing of Windows (5%)	5	06-Apr-26	10-Apr-26
CON-2970	Field Testing of Windows (50%)	5	15-Apr-26	21-Apr-26
CON-2980	Install Windows - East Elevation	8	15-Apr-26	24-Apr-26
CON-2990	Install Storefront System- East Elevation	8	15-Apr-26	24-Apr-26
CON-3380	Install Windows -North Elevation	10	15-Apr-26	28-Apr-26
CON-3390	Install Storefront System-North Elevation	10	15-Apr-26	28-Apr-26
CON-99237	Install Flag Pole - South Elevation	10	15-Apr-26	28-Apr-26
CON-3370	Field Testing of Windows (90%)	5	27-Apr-26	01-May-26
MIL-1580	Window Installation Finish	0		28-Apr-26
MEP Equipment		112	12-Mar-26	19-Aug-26
CON-2190	Install Electric Unit Heater EUH - Mechanical Work - Roof Bulkhead	5	12-Mar-26	18-Mar-26
CON-2230	Install Emergency Generator -Bulkhead	7	19-Mar-26	27-Mar-26
CON-2360	Install Smoke Purge Fan SPF - Mechanical Work - Roof Bulkhead	3	26-Mar-26	30-Mar-26
CON-2850	Install Electric Unit Heaters -2nd Floor	5	16-Apr-26	22-Apr-26
CON-3130	Install Electric Unit Heaters -3rd Floor	5	23-Apr-26	29-Apr-26
CON-3150	Install Convector Heater CV - Mechanical Work - 2nd Floor	5	23-Apr-26	29-Apr-26
CON-3420	Install Electric Unit Heaters -4th Floor	5	30-Apr-26	06-May-26
CON-3450	Install Air Conditioning Unit AC - Mechanical Work - 2nd Floor	4	30-Apr-26	05-May-26
CON-3640	Install Electric Unit Heaters -5th Floor	3	07-May-26	11-May-26
CON-4670	Install Exhaust Fans -1st Floor	5	07-Jul-26	13-Jul-26
CON-2860	Install Fume Hood Exhaust -Roof Floor	3	08-Jul-26	10-Jul-26
CON-3000	Install Smoke Purge Fan -Roof Floor	3	13-Jul-26	15-Jul-26
CON-4870	Install Cabinet Unit Heaters With Fan CUH-1st Floor	3	14-Jul-26	16-Jul-26
CON-4880	Install Motorized Fire/Smoke Damper FSD - Mechanical Work - 1st Floor	7	14-Jul-26	22-Jul-26
CON-5060	Install Hot Glycol / Hot Water Cabinet Heater (CUH) -3rd Floor	4	17-Jul-26	22-Jul-26
CON-5070	Install Electric Unit Heaters -1st Floor	7	17-Jul-26	27-Jul-26

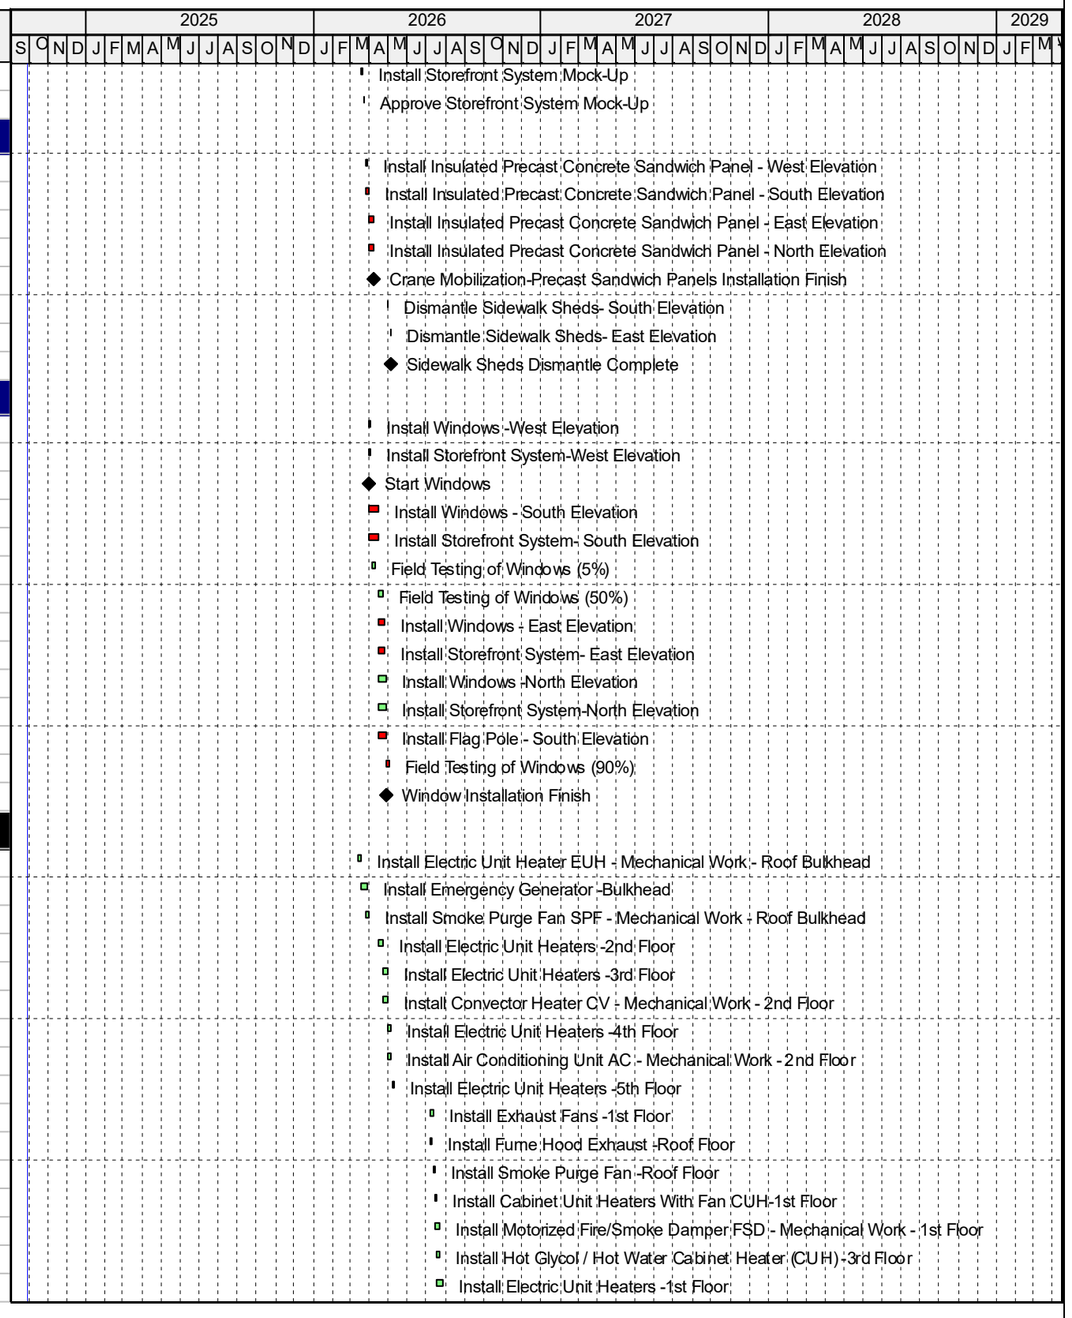

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-5260	Install Cabinet Unit Heater With Fan CUH -4th Floor	4	23-Jul-26	28-Jul-26
CON-5860	Install Sprinkler Booster Pump (SBP-1) -1st Floor	10	23-Jul-26	05-Aug-26
CON-5150	Install Air Conditioning Unit AC - Mechanical Work - 1st Floor	4	23-Jul-26	28-Jul-26
CON-5280	Install Convector Heater CV - Mechanical Work - 3rd Floor	4	23-Jul-26	28-Jul-26
CON-5300	Install Grease Interceptors - 1st Floor	5	28-Jul-26	03-Aug-26
CON-5430	Install Hot Glycol / Hot Water Cabinet Heater (CUH)-5th Floor	4	29-Jul-26	03-Aug-26
CON-5320	Install Door Curtains DC - Mechanical Work - 1st Floor	7	29-Jul-26	06-Aug-26
CON-5450	Install Air Conditioning Unit AC - Mechanical Work - 3rd Floor	4	29-Jul-26	03-Aug-26
CON-5460	Install Convector Heater CV - Mechanical Work - 4th Floor	3	29-Jul-26	31-Jul-26
CON-5620	Install Air Conditioning Unit AC - Mechanical Work - 4th Floor	4	04-Aug-26	07-Aug-26
CON-5590	Install Exhaust Fan EF - Mechanical Work - 5th Floor	4	04-Aug-26	07-Aug-26
CON-6100	Install Jockey Pump (JP-1) -1st Floor	10	06-Aug-26	19-Aug-26
CON-5490	Install Convector Heater CV - Mechanical Work - 1st Floor	7	07-Aug-26	17-Aug-26
CON-5630	Install Convector Heater CV - Mechanical Work - 5th Floor	3	10-Aug-26	12-Aug-26
Special Rooms		113	27-Mar-26	04-Sep-26
Elevator Machine Room-Roof Floor		61	07-May-26	04-Aug-26
MIL-1760	Start Elevator Work	0	07-May-26	
CON-99357	Install CMU Wall for Shaft -Elevator Machine Room	10	07-May-26	20-May-26
CON-99167	Install Elevator Guide Rails -Elevator Machine Room	8	21-May-26	02-Jun-26
CON-2090	Install Elevator Controller #1 -Elevator Machine Room	10	03-Jun-26	16-Jun-26
CON-2370	Install Elevator Controller #2 -Elevator Machine Room	10	17-Jun-26	01-Jul-26
CON-2580	Install Power Panels -Elevator Machine Room	7	02-Jul-26	13-Jul-26
CON-2790	Rough-in Conduits & Wires-Elevator Machine Room	6	14-Jul-26	21-Jul-26
CON-99157	Install Elevator Sump Pump -Elevator Machine Room	10	14-Jul-26	27-Jul-26
CON-3100	Install Elevator Cabinet (1) -Elevator Machine Room	10	22-Jul-26	04-Aug-26
CON-3620	Install Elevator Cabinet (2) -Elevator Machine Room	10	22-Jul-26	04-Aug-26
IDF ROOM		80	27-Mar-26	21-Jul-26
CON-2640	Install Grounding Bars - 3rd Floor IDF Room	5	27-Mar-26	02-Apr-26
CON-2520	Install Voice Rack - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2530	Install Data Rack - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2540	Install Ground Bus Bar - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2800	Install Data rack - 3rd Floor IDF Room	8	03-Apr-26	14-Apr-26
CON-2830	Install IPDVS Equipment Rack - 3rd Floor IDF Room	4	03-Apr-26	08-Apr-26
CON-2810	Install Grounding Bars - 4th Floor IDF Room	5	06-Apr-26	10-Apr-26
CON-2650	Install Data Rack - 4th Floor IDF Room	7	06-Apr-26	14-Apr-26
CON-2660	Install Voice Rack - 4th Floor IDF Room	5	06-Apr-26	10-Apr-26
CON-2760	Install IPDVS Equipment Rack - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2770	Install Ladder Rack Cable Tray - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2780	Install BACnet Data Cabinet - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2820	Install Cable Ladder - 4th Floor IDF Room	5	13-Apr-26	17-Apr-26
CON-2840	Install Main Sound Rack - 34th Floor IDF Room	5	13-Apr-26	17-Apr-26
CON-3250	Install Voice Rack - 3rd Floor IDF Room	5	15-Apr-26	21-Apr-26
CON-3110	Install IPDVS Equipment Rack - 4th Floor IDF Room	5	20-Apr-26	24-Apr-26

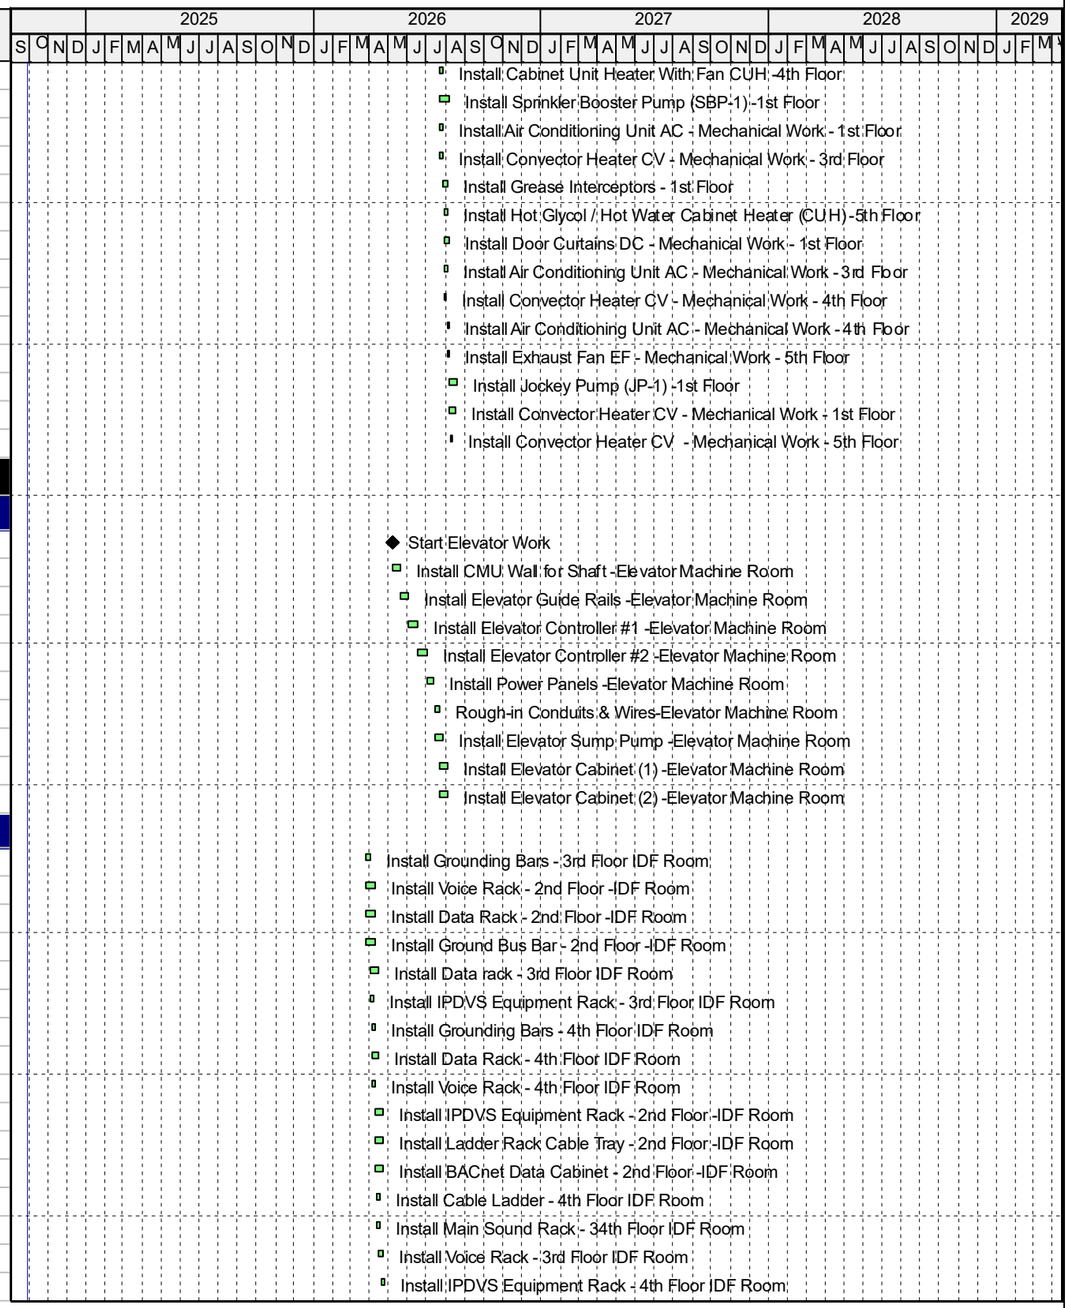

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3550	Install Cable Ladder - 3rd Floor IDF Room	5	22-Apr-26	28-Apr-26
CON-3570	Install Main Sound Rack - 3rd Floor IDF Room	5	22-Apr-26	28-Apr-26
MIL-1610	IDF Work Finish	0		21-Jul-26*
Boiler Room-5th Floor		26	15-Jul-26	19-Aug-26
CON-5960	F/R/P Concert Pad -Boiler Room	3	15-Jul-26	17-Jul-26
CON-6000	Rough-in Conduits & Wires-Boiler Room	3	20-Jul-26	22-Jul-26
CON-6050	Install Boiler B-1-Boiler Room	5	23-Jul-26	29-Jul-26
CON-6110	Install Boiler B-2-Boiler Room	5	30-Jul-26	05-Aug-26
CON-6120	Install Air Separator Units (AS-1 , AS-2 & AS-3)	2	30-Jul-26	31-Jul-26
CON-6130	Install Boiler Condensate ACID Neutralization Tubes -Boiler Room	2	30-Jul-26	31-Jul-26
CON-6200	Install Expansion Tanks (ET-1 , ET-2 & ET-3)	2	03-Aug-26	04-Aug-26
CON-6210	Install Glycol Make-up Units (GF-1 & GF-2 & GF-3)	2	03-Aug-26	04-Aug-26
CON-6220	Install Reduced Pressure Zone (RPZ) Devices -Boiler Room	2	03-Aug-26	04-Aug-26
CON-6260	Install Heat Exchanger -Boiler Room	2	06-Aug-26	07-Aug-26
CON-6290	Install Hot Glycol Units Heaters (UH-5-1, UH-5-2)	2	10-Aug-26	11-Aug-26
CON-6330	Install Heat Pump Electric Hot Water Heater (HPWH#1&2)-Boiler Room	2	12-Aug-26	13-Aug-26
CON-6340	Install Exhaust Fans -Boiler Room	2	14-Aug-26	17-Aug-26
CON-6350	Install Primary Hot Water Pump (GHWP 1 to 3) -Boiler Room	2	14-Aug-26	17-Aug-26
CON-6360	Install Primary Chilled Water Pump (GCHWP-1&2)-Boiler Room	2	14-Aug-26	17-Aug-26
CON-6400	Install Secondary Hot Water Pump(HWP-1&2)-Boiler Room	2	18-Aug-26	19-Aug-26
CON-6410	Install Electric Unit Heater (EUH-3) - Boiler Room	2	18-Aug-26	19-Aug-26
CON-6420	Install Branch Panels (BRPP) -Boiler Room	2	18-Aug-26	19-Aug-26
MDF Room -1st Floor		57	29-Apr-26	21-Jul-26
CON-3740	Install Ground Bus Bar - 1st Floor MDF Room	6	29-Apr-26	06-May-26
CON-4110	Install Voice Rack - 1st Floor MDF Room	6	07-May-26	14-May-26
CON-4510	Install Sound Rack - 1st Floor MDF Room	6	15-May-26	22-May-26
CON-4120	Install Project Connect Cabinet - 1st Floor MDF Room	8	15-May-26	27-May-26
CON-4520	Install Data Rack - 1st Floor MDF Room	6	26-May-26	02-Jun-26
CON-4550	Install UPS- 1st Floor MDF Room	9	03-Jun-26	15-Jun-26
CON-4130	Install BACnet Data Cabinet- 1st Floor MDF Room	9	03-Jun-26	15-Jun-26
CON-4780	Install IPDVS Equipment Rack - 1st Floor MDF Room	6	16-Jun-26	24-Jun-26
CON-4790	Install Ladder Rack Cable Tray- 1st Floor MDF Room	6	25-Jun-26	02-Jul-26
CON-4770	Install PBX - 1st Floor MDF Room	8	06-Jul-26	15-Jul-26
MIL-1600	MDF Work Finish	0		21-Jul-26*
Electrical Service Room-1st Floor		37	23-Apr-26	15-Jun-26
CON-4730	Rough-in Conduits & Wires - Electric Service Room	6	23-Apr-26	30-Apr-26
CON-4960	F/R/P Concrete Pad - Electric Service Room	6	01-May-26	08-May-26
CON-5180	Install Service Switchboard "SS-A"- Electric Service Room	5	11-May-26	15-May-26
CON-5510	Install Leak Detector - Electric Service Room	3	18-May-26	20-May-26
CON-5610	Install Sprinkler Booster Pump - Electric Service Room	4	21-May-26	27-May-26
CON-5640	Install Fire Alarm Normal ATS - Electric Service Room	4	28-May-26	02-Jun-26
CON-5780	Install Motorized Fire/Smoke Damper & Control Panel - Electric Service Room	5	03-Jun-26	09-Jun-26
CON-5790	Install Main Grounding Bus Bar - Electric Service Room	4	03-Jun-26	08-Jun-26
CON-9130	Install Switch Gear - Electric Service Room	5	08-Jun-26	12-Jun-26

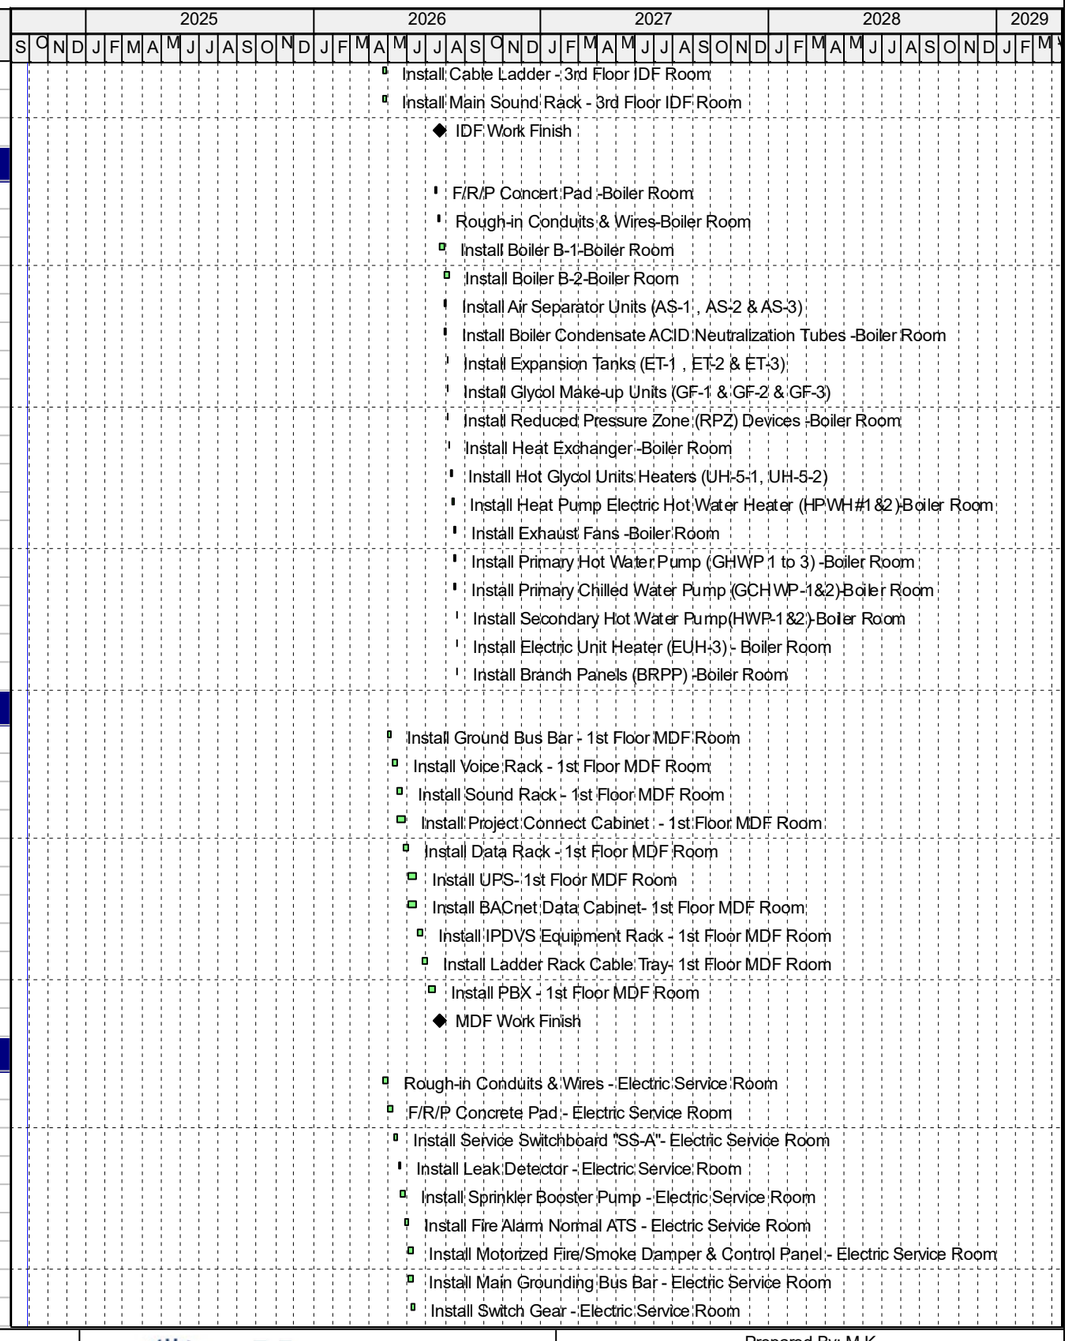

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-5840	Install Electric Unit Heater EUH-6 - Electric Service Room	4	10-Jun-26	15-Jun-26
Fuel Oil Room-1st Floor		10	01-Jun-26	12-Jun-26
CON-4890	F/R/P Concrete Pads -Fuel Oil Room	2	01-Jun-26	02-Jun-26
CON-4900	Rough-in Fuel Oil Piping -Fuel Oil Room	3	01-Jun-26	03-Jun-26
CON-4990	Install Fuel Oil Storage Tank (FOT-1) - Fuel Oil Room	3	03-Jun-26	05-Jun-26
CON-5020	Rough-in Fuel Oil Fill Piping -Fuel Oil Room	3	04-Jun-26	08-Jun-26
CON-5160	Install Fuel Oil Transfer Duplex Pump (FOP-1 & 2) -1st Floor	4	08-Jun-26	11-Jun-26
CON-5200	Rough-in Fuel Oil Vent Piping -Fuel Oil Room	4	09-Jun-26	12-Jun-26
Gymatorium -4th Floor		39	14-Jul-26	04-Sep-26
CON-5760	Install Wood Floating Floor System -Gymnatorium	10	14-Jul-26	27-Jul-26
CON-5810	Install Wall Pads - Gymnatorium	4	28-Jul-26	31-Jul-26
CON-5970	Install Retractable Basketball Goal Assembly -Gymnatorium	3	03-Aug-26	05-Aug-26
CON-6020	Install 8" Acoustic Block Painted-Gymnatorium	7	06-Aug-26	14-Aug-26
CON-99217	Install Bleachers -Gymnatorium	3	12-Aug-26	14-Aug-26
CON-6230	Install Gym Equipment -Gymnatorium -Gymnatorium	6	17-Aug-26	24-Aug-26
CON-6240	Install Fine Tube Radiator FTR - Gymnatorium	5	17-Aug-26	21-Aug-26
CON-6250	Install Hydraulic Vertical Wheelchair Lift -Gymnatorium	8	17-Aug-26	26-Aug-26
CON-9150	Install LED Theatrical Lighting -Gymnatorium	4	25-Aug-26	28-Aug-26
CON-6390	Install Auditorium Television Studio Dimming System -Gymnatorium	7	27-Aug-26	04-Sep-26
Electrical Rough-ins		41	11-Mar-26	06-May-26
Conduits Rough-ins		38	11-Mar-26	01-May-26
Power Conduits		38	11-Mar-26	01-May-26
CON-2180	Rough-in Power Conduits -2nd Floor	6	11-Mar-26	18-Mar-26
CON-2320	Rough-in Power Conduits-3rd Floor	6	19-Mar-26	26-Mar-26
CON-2480	Rough-in Power Conduits-4th Floor	6	27-Mar-26	03-Apr-26
CON-2680	Rough-in Power Conduits -5th Floor	6	06-Apr-26	13-Apr-26
MIL-1270	Electrical Rough-ins Start	0	09-Apr-26	
CON-3760	Rough-in Power Conduits -1st Floor	4	21-Apr-26	24-Apr-26
CON-3910	Install Grounding System -1st Floor	5	27-Apr-26	01-May-26
Low Voltage Conduits		31	19-Mar-26	30-Apr-26
CON-2330	Rough-in Low-Voltage Conduits -2nd Floor	6	19-Mar-26	26-Mar-26
CON-2500	Rough-in Low-Voltage Conduits-3rd Floor	6	27-Mar-26	03-Apr-26
CON-2700	Rough-in Low-Voltage Conduits-4th Floor	6	06-Apr-26	13-Apr-26
CON-2950	Rough-in Low-Voltage Conduits-5th Floor	6	14-Apr-26	21-Apr-26
CON-3920	Rough-in Low-Voltage Conduits-1st Floor	4	27-Apr-26	30-Apr-26
Wire Pulling		35	19-Mar-26	06-May-26
Power Wires		31	19-Mar-26	30-Apr-26
CON-2340	Power Wires Pulling -2nd Floor	6	19-Mar-26	26-Mar-26
CON-2510	Power Wires Pulling-3rd Floor	6	27-Mar-26	03-Apr-26
CON-2710	Power Wires Pulling-4th Floor	6	06-Apr-26	13-Apr-26
CON-2960	Power Wires Pulling-5th Floor	6	14-Apr-26	21-Apr-26
CON-3930	Power Wires Pulling-1st Floor	4	27-Apr-26	30-Apr-26
Low Voltage Wires		29	27-Mar-26	06-May-26

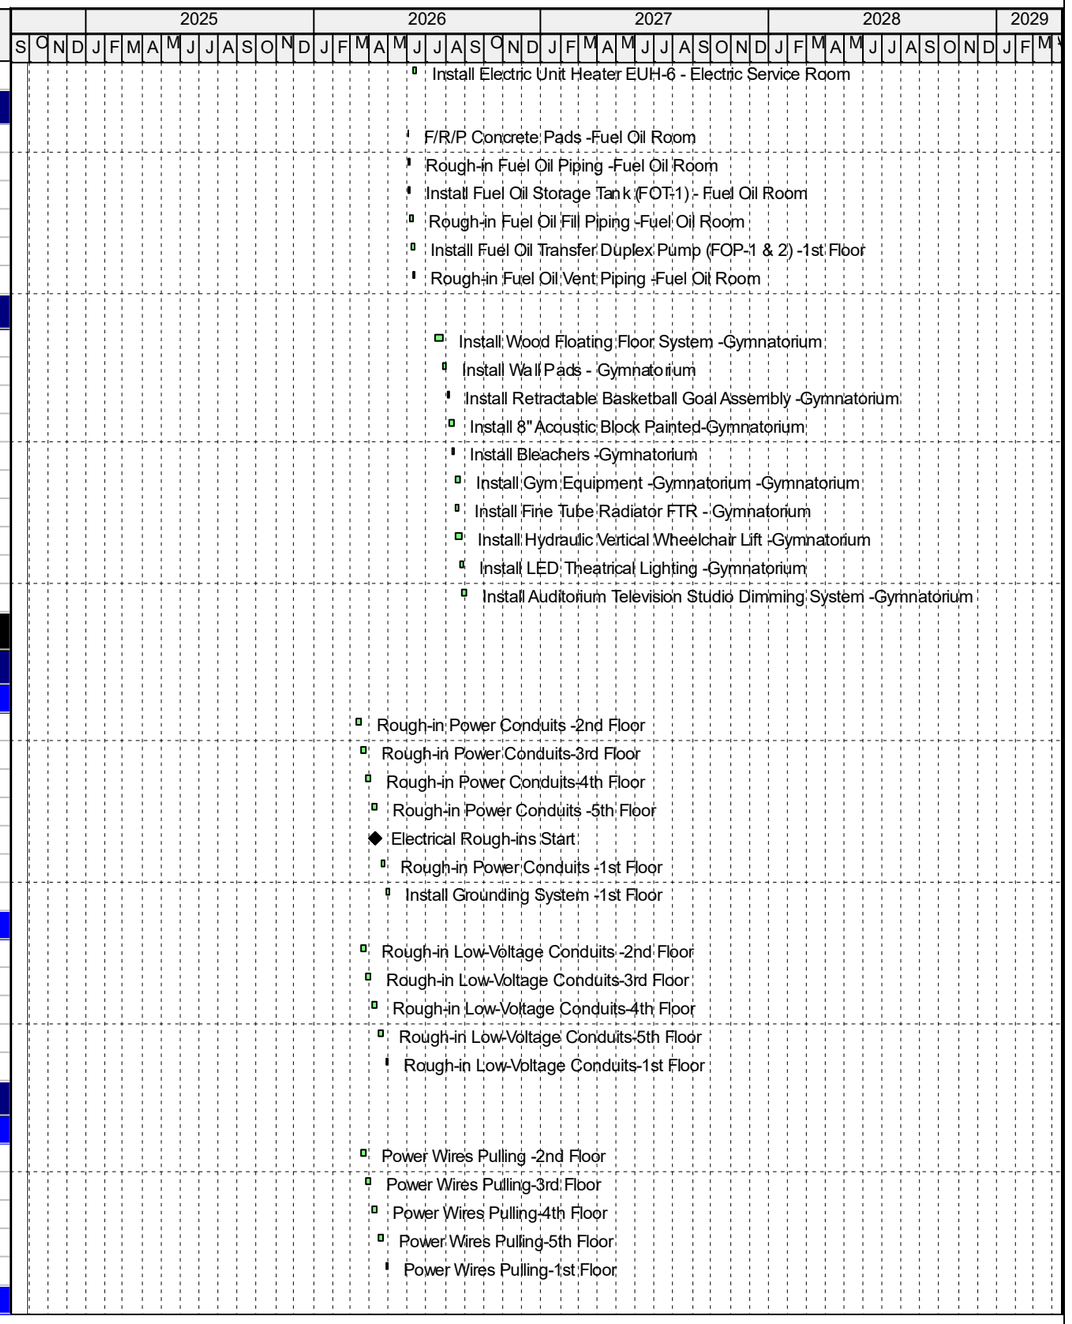

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2490	Low Voltage Wires Pulling -2nd Floor	6	27-Mar-26	03-Apr-26
CON-2690	Low Voltage Wires Pulling -3rd Floor	6	06-Apr-26	13-Apr-26
CON-2940	Low Voltage Wires Pulling-4th Floor	6	15-Apr-26	22-Apr-26
CON-3290	Low Voltage Wires Pulling-5th Floor	6	23-Apr-26	30-Apr-26
CON-4180	Low Voltage Wires Pulling -1st Floor	4	01-May-26	06-May-26
MIL-1350	Electrical Rough-ins Finish	0		06-May-26
Roof Top Units		84	17-Mar-26	15-Jul-26
CON-2120	Install Air Cooled Chiller CH-1 -Roof Floor	7	17-Mar-26	25-Mar-26
CON-2350	Install Air Cooled Chiller CH-2 -Roof Floor	7	26-Mar-26	03-Apr-26
CON-2250	Install Air Handling Unit AHU-1 -Roof Floor	5	08-Jun-26	12-Jun-26
MIL-1460	Roof Top Units Installations Start	0	08-Jun-26	
CON-2430	Install Air Handling Unit AHU-2 -Roof Floor	5	15-Jun-26	22-Jun-26
CON-2560	Install Air Handling Unit AHU-3 -Roof Floor	5	23-Jun-26	29-Jun-26
CON-2720	Install Air Handling Unit AHU-4 -Roof Floor	5	30-Jun-26	07-Jul-26
CON-5770	Install Air Cooled Condensing Unit ACCU - Mechanical Work - 5th Floor	5	08-Jul-26	14-Jul-26
MIL-1480	Roof Top Units Installations Finish	0		14-Jul-26
MIL-2972	Finish Mechanical System Inspection	0		15-Jul-26
Ceiling Framing		26	16-Mar-26	20-Apr-26
CON-2310	Install Ceiling Hangers & Supports-2nd Floor	4	16-Mar-26	19-Mar-26
CON-2390	Install Ceiling Hangers & Supports-3rd Floor	4	20-Mar-26	25-Mar-26
CON-2550	Install Ceiling Hangers & Supports-4th Floor	4	26-Mar-26	31-Mar-26
CON-2620	Install Ceiling Hangers & Supports-5th Floor	4	01-Apr-26	06-Apr-26
CON-3520	Install Ceiling Hangers & Supports -1st Floor	4	15-Apr-26	20-Apr-26
Roofing		29	07-Apr-26	15-May-26
5th Floor Roof		27	07-Apr-26	13-May-26
CON-2920	Pour Sloped Concrete Fill -5th Floor Roof	2	07-Apr-26	08-Apr-26
MIL-1230	5th Floor Roofing Start	0	07-Apr-26	
CON-3440	Install Hot Fluid Applied Membrane -5th Floor Roof	4	21-Apr-26	24-Apr-26
CON-3580	Install 6" Thick Rigid Insulation -5th Floor Roof	3	27-Apr-26	29-Apr-26
CON-3700	Install Drainage -5th Floor Roof	3	30-Apr-26	04-May-26
CON-3710	Roof Flood Test -5th Floor Roof	4	30-Apr-26	05-May-26
CON-3820	Install Filter Fabric -5th Floor Roof	3	06-May-26	08-May-26
CON-3960	Install Concrete Pavers -5th Floor Roof	3	11-May-26	13-May-26
MIL-1310	5th Floor Roofing Finish	0		13-May-26
Main Roof		27	09-Apr-26	15-May-26
CON-3010	Pour Sloped Concrete Fill -Roof Floor	2	09-Apr-26	10-Apr-26
MIL-1200	Main Roofing Start	0	09-Apr-26	
CON-3210	Install Fluid-Applied Protected Membrane Mock-Up	2	13-Apr-26	14-Apr-26
CON-3300	Approve Fluid-Applied Protected Membrane Mock-Up	4	15-Apr-26	20-Apr-26
CON-3430	Install Hot Fluid Applied Membrane -Roof Floor	3	21-Apr-26	23-Apr-26
CON-3600	Install Drainage Panels- Roof Floor	3	24-Apr-26	28-Apr-26
CON-3730	Install 6" Thick Rigid Insulation -Roof Floor	3	29-Apr-26	01-May-26
CON-3840	Roof Flood Test -Roof Floor	3	04-May-26	06-May-26

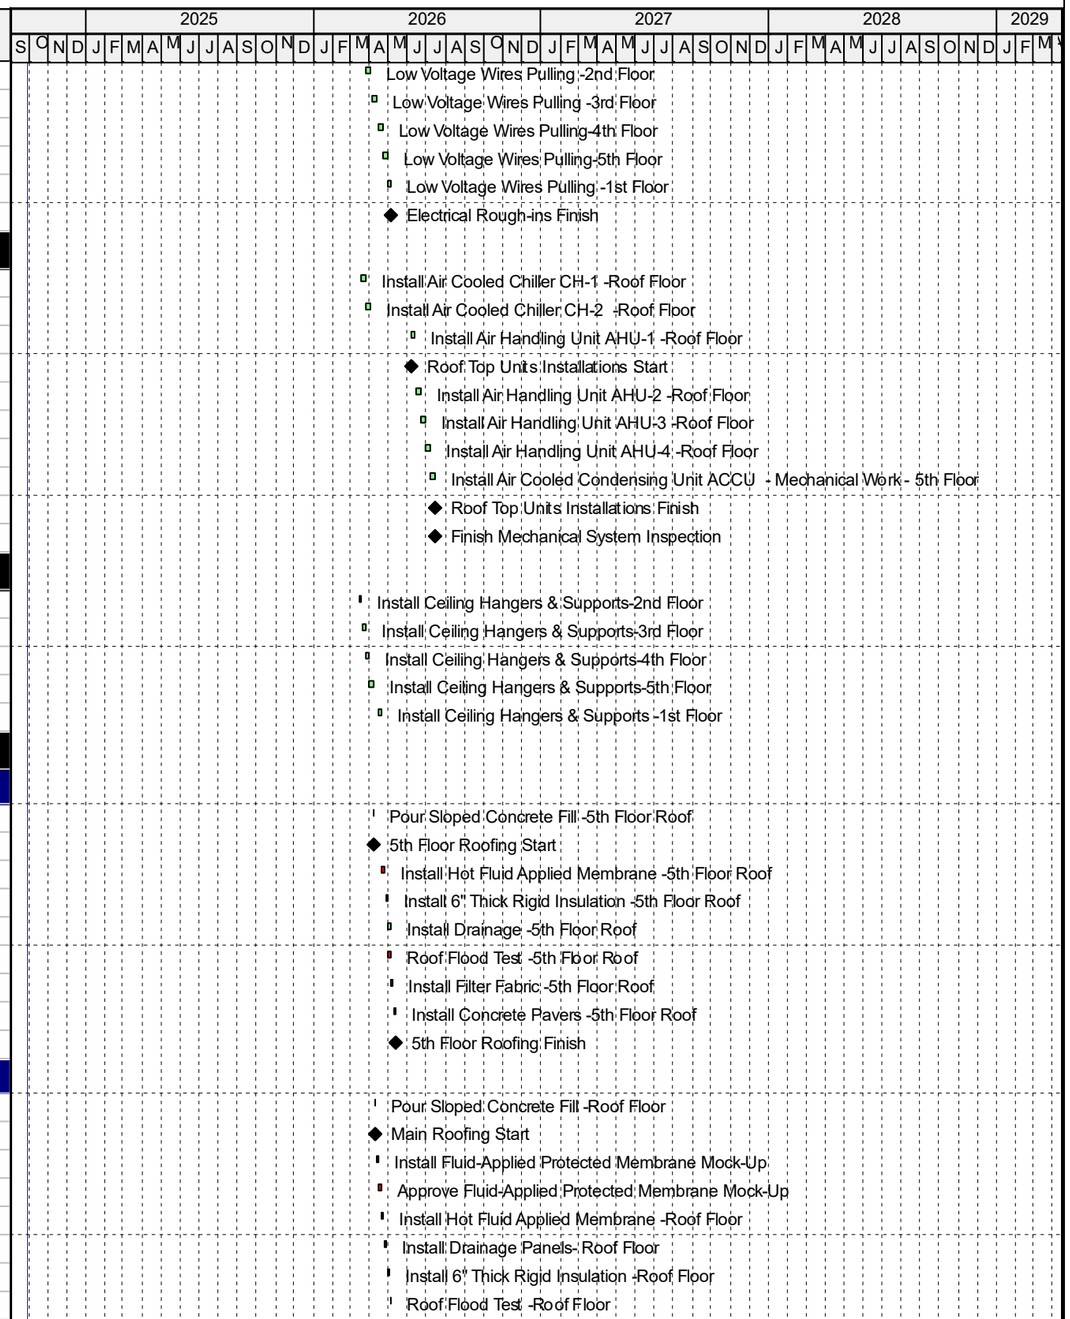

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
MIL-1340	BLDG Tight	0		06-May-26
CON-4020	Install Filter Fabric -Roof Floor	3	07-May-26	11-May-26
CON-4210	Install Concrete Pavers -Roof Floor	4	12-May-26	15-May-26
MIL-1280	Main Roofing Finish	0		15-May-26
Electrical Finishes		116	06-Apr-26	18-Sep-26
Wiring Devices		36	06-Apr-26	26-May-26
CON-2670	Install Wiring Devices -2nd Floor	7	06-Apr-26	14-Apr-26
CON-2930	Install Wiring Devices -3rd Floor	7	15-Apr-26	23-Apr-26
CON-3280	Install Wiring Devices -4th Floor	7	24-Apr-26	04-May-26
CON-3660	Install Wiring Devices -5th Floor	8	05-May-26	14-May-26
CON-4470	Install Wiring Devices -1st Floor	7	15-May-26	26-May-26
Lighting Fixtures		31	18-Jun-26	03-Aug-26
CON-5130	Install Lighting Fixtures -2nd Floor	5	18-Jun-26	25-Jun-26
CON-5370	Install Lighting Fixtures -3rd Floor	6	29-Jun-26	07-Jul-26
CON-5580	Install Lighting Fixtures -4th Floor	6	08-Jul-26	15-Jul-26
CON-5740	Install Lighting Fixtures -5th Floor	6	16-Jul-26	23-Jul-26
CON-5940	Install Lighting Fixtures -1st Floor	7	24-Jul-26	03-Aug-26
IPDVS Devices		54	06-Jul-26	18-Sep-26
CON-5140	Install IPDVS Devices -2nd Floor	9	06-Jul-26	16-Jul-26
CON-5440	Install IPDVS Devices -3rd Floor	9	17-Jul-26	29-Jul-26
CON-5750	Install IPDVS Devices -4th Floor	9	30-Jul-26	11-Aug-26
CON-6010	Install IPDVS Devices -5th Floor	9	12-Aug-26	24-Aug-26
CON-6040	Install IPDVS Devices -1st Floor	7	25-Aug-26	02-Sep-26
MIL-1620	IPDVS Work Finish	0		18-Sep-26*
Fire Alarm Sensors and Devices		30	26-Jun-26	07-Aug-26
CON-5310	Install Fire alarm Sensors and Devises -2nd Floor	5	26-Jun-26	02-Jul-26
CON-5500	Install Fire alarm Sensors and Devises -3rd Floor	8	08-Jul-26	17-Jul-26
CON-5660	Install Fire alarm Sensors and Devises -4th Floor	7	20-Jul-26	28-Jul-26
CON-5830	Install Fire alarm Sensors and Devises -5th Floor	5	29-Jul-26	04-Aug-26
CON-5950	Install Fire alarm Sensors and Devises -1st Floor	3	05-Aug-26	07-Aug-26
Plumbing Piping Rough-ins		57	06-Apr-26	25-Jun-26
Gas Piping		27	06-Apr-26	12-May-26
CON-2630	Rough-in Gas Risers -2nd Floor	4	06-Apr-26	09-Apr-26
CON-2750	Rough-in Gas Risers-3rd Floor	4	10-Apr-26	15-Apr-26
CON-2890	Rough-in Gas Risers -4th Floor	4	16-Apr-26	21-Apr-26
CON-3050	Rough-in Gas Risers & Piping -5th Floor	4	22-Apr-26	27-Apr-26
CON-4460	Rough-in Gas Risers -1st Floor	4	07-May-26	12-May-26
MIL-1260	Plumbing Rough-ins Start	0	07-May-26	
Water Piping		27	10-Apr-26	18-May-26
CON-2740	Rough-in Domestic Water Piping -2nd Floor	4	10-Apr-26	15-Apr-26
CON-2880	Rough-in Domestic Water Piping -3rd Floor	4	16-Apr-26	21-Apr-26
CON-3040	Rough-in Domestic Water Piping -4th Floor	4	22-Apr-26	27-Apr-26

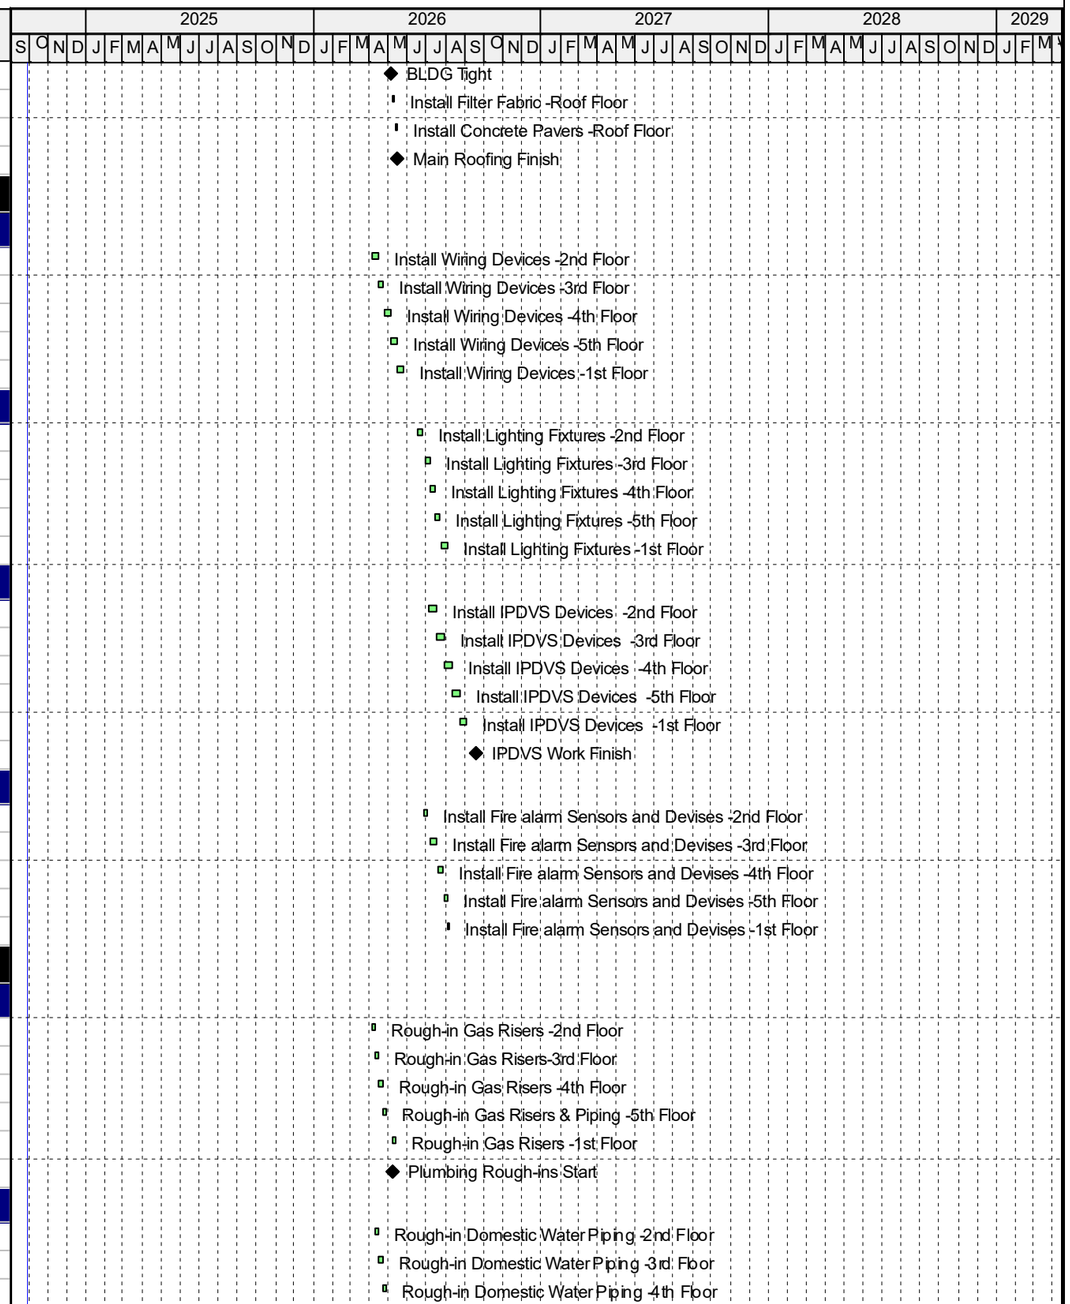

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3190	Rough-in Domestic Water Piping -5th Floor	4	28-Apr-26	01-May-26
CON-4590	Rough-in Domestic Water Piping-1st Floor	4	13-May-26	18-May-26
Sanitary Piping		27	16-Apr-26	22-May-26
CON-2870	Rough-in Sanitary & Vent Piping -2nd Floor	4	16-Apr-26	21-Apr-26
CON-3030	Rough-in Sanitary & Vent Piping -3rd Floor	4	22-Apr-26	27-Apr-26
CON-3180	Rough-in Sanitary & Vent Piping -4th Floor	4	28-Apr-26	01-May-26
CON-3340	Rough-in Sanitary & Vent Piping -5th Floor	4	04-May-26	07-May-26
CON-4690	Rough-in Sanitary & Vent Piping -1st Floor	4	19-May-26	22-May-26
Storm Piping		27	22-Apr-26	29-May-26
CON-3020	Rough-in Storm Piping -2nd Floor	4	22-Apr-26	27-Apr-26
CON-3170	Rough-in Storm Piping -3rd Floor	4	28-Apr-26	01-May-26
CON-3330	Rough-in Storm Piping -4th Floor	4	04-May-26	07-May-26
CON-3540	Rough-in Storm Piping -5th Floor	4	08-May-26	13-May-26
CON-4760	Rough-in Storm Piping -1st Floor	4	26-May-26	29-May-26
MIL-1320	Plumbing Rough-ins Finish	0		29-May-26
Plumbing Testing		36	28-Apr-26	17-Jun-26
CON-3200	Plumbing Pressure Testing -2nd Floor	5	28-Apr-26	04-May-26
CON-3400	Install Hot Water Circulation Pump -5th Floor	5	04-May-26	08-May-26
CON-3410	Install Electric Hot Water Heater (EWH-1) -5th Floor	5	04-May-26	08-May-26
CON-3360	Plumbing Pressure Testing -3rd Floor	5	05-May-26	11-May-26
CON-3560	Plumbing Pressure Testing -4th Floor	5	12-May-26	18-May-26
CON-3590	Plumbing Pressure Testing -5th Floor	5	14-May-26	20-May-26
CON-5050	Plumbing Pressure Testing -1st Floor	5	11-Jun-26	17-Jun-26
Plumbing Insulation		34	07-May-26	25-Jun-26
CON-4050	Plumbing Piping Insulation -2nd Floor	5	07-May-26	13-May-26
CON-4190	Plumbing Piping Insulation -3rd Floor	5	14-May-26	20-May-26
CON-4390	Plumbing Piping Insulation -4th Floor	5	21-May-26	28-May-26
CON-4530	Plumbing Piping Insulation -5th Floor	5	29-May-26	04-Jun-26
CON-5210	Plumbing Piping Insulation -1st Floor	5	18-Jun-26	25-Jun-26
Pumps		8	01-Jun-26	10-Jun-26
CON-4940	Install Duplex Domestic Water Booster Pump System (BP-1&BP-2) -1st Floor	8	01-Jun-26	10-Jun-26
CON-4950	Install Duplex Ejector Pump System (EJ-1&EJ-2) -1st Floor	8	01-Jun-26	10-Jun-26
Testing & Commesioning		62	06-Jul-26	30-Sep-26
CLO-1120	MDF & IDF Rooms Testing & Commissioning	12	06-Jul-26	21-Jul-26
CLO-1010	HVAC Flush-Out	20	07-Jul-26	03-Aug-26
CLO-1140	SSDS System Testing & Commissioning	7	16-Jul-26	24-Jul-26
CLO-1240	Elevator Sump Pump Testing & Commissioning	21	28-Jul-26	25-Aug-26
CLO-1270	Water Heater Testing & Commissioning	21	28-Jul-26	25-Aug-26
CLO-1220	Emergency Generator Electric Load Test	3	29-Jul-26	31-Jul-26
CLO-1250	Emergency Generator Testing & Commissioning	21	03-Aug-26	31-Aug-26
CLO-1230	Air Handling Unit Testing & Commissioning	21	04-Aug-26	01-Sep-26
CLO-1190	Pre-Elevator Test Inspection	5	05-Aug-26	11-Aug-26
CLO-1290	Glycol System Testing & Commissioning	21	05-Aug-26	02-Sep-26

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
MIL-1680	Emergency Generator Final Sign-off	0		07-Aug-26
CLO-1020	Electrical System Testing & Commissioning	21	10-Aug-26	08-Sep-26
CLO-1260	HVAC Split System Testing & Commissioning	21	10-Aug-26	08-Sep-26
CLO-1280	Fire Alarm Testing & Commissioning	21	10-Aug-26	08-Sep-26
CLO-1000	Elevator Testing & Commissioning	20	12-Aug-26	09-Sep-26
CLO-1160	Sprinkler/Domestic Booster Pumps Testing & Commissioning	14	20-Aug-26	09-Sep-26
CLO-1130	IPDVS System Testing & Commissioning	11	03-Sep-26	18-Sep-26
CLO-1170	Sprinkler/Domestic Booster Pumps Inspection	3	10-Sep-26	14-Sep-26
CLO-1200	Elevator DOB Inspection	5	10-Sep-26	16-Sep-26
CLO-1180	Sprinkler/Domestic Booster Pumps Sign-offs	0		14-Sep-26
CLO-1150	FDNY Inspection	12	15-Sep-26	30-Sep-26
MIL-1650	FDNY Inspection Finish	0		30-Sep-26
MIL-1670	Elevator Final Sign-off	0		30-Sep-26
Sprinkler Rough-ins		44	04-May-26	07-Jul-26
Stand Pipes		24	04-May-26	05-Jun-26
CON-3310	Install 4" Standpipe -2nd Floor	4	04-May-26	07-May-26
MIL-1300	Start Sprinkler Rough-ins	0	04-May-26	
CON-3510	Install 4" Standpipe -3rd Floor	4	08-May-26	13-May-26
CON-3650	Install 4" Standpipe -4th Floor	4	14-May-26	19-May-26
CON-3770	Install 4" Standpipe -5th Floor	4	20-May-26	26-May-26
CON-3890	Install 4" Standpipe -Roof	4	27-May-26	01-Jun-26
CON-4910	Install 4" Standpipe -1st Floor	4	02-Jun-26	05-Jun-26
MIL-2952	Finish Standpipe System Inspection	0		05-Jun-26
Main Sprinkler Pipes		25	08-May-26	12-Jun-26
CON-3500	Rough-in Main Sprinkler Piping -2nd Floor	5	08-May-26	14-May-26
CON-3690	Rough-in Main Sprinkler Piping-3rd Floor	5	15-May-26	21-May-26
CON-3810	Rough-in Main Sprinkler Piping-4th Floor	5	22-May-26	29-May-26
CON-4010	Rough-in Main Sprinkler Piping -5th Floor	5	01-Jun-26	05-Jun-26
CON-5030	Rough-in Main Sprinkler Piping -1st Floor	5	08-Jun-26	12-Jun-26
CON-4250	Rough-in Main Sprinkler Piping -Roof	5	08-Jun-26	12-Jun-26
Branch Sprinkler Pipes		25	15-May-26	22-Jun-26
CON-3670	Rough-in Branch Sprinkler Piping -2nd Floor	5	15-May-26	21-May-26
CON-3790	Rough-in Branch Sprinkler Piping -3rd Floor	5	22-May-26	29-May-26
CON-3990	Rough-in Branch Sprinkler Piping -4th Floor	5	01-Jun-26	05-Jun-26
CON-4230	Rough-in Branch Sprinkler Piping -5th Floor	5	08-Jun-26	12-Jun-26
CON-5230	Rough-in Branch Sprinkler Piping -1st Floor	5	15-Jun-26	22-Jun-26
CON-4430	Rough-in Branch Sprinkler Piping -Roof	5	15-Jun-26	22-Jun-26
Sprinkler Heads		30	15-May-26	29-Jun-26
CON-3680	Rough-in Sprinkler Heads -2nd Floor	5	15-May-26	21-May-26
CON-3800	Rough-in Sprinkler Heads -3rd Floor	5	22-May-26	29-May-26
CON-4000	Rough-in Sprinkler Heads -4th Floor	5	01-Jun-26	05-Jun-26
CON-4240	Rough-in Sprinkler Heads -5th Floor	5	08-Jun-26	12-Jun-26
CON-5240	Rough-in Sprinkler Heads -1st Floor	5	15-Jun-26	22-Jun-26

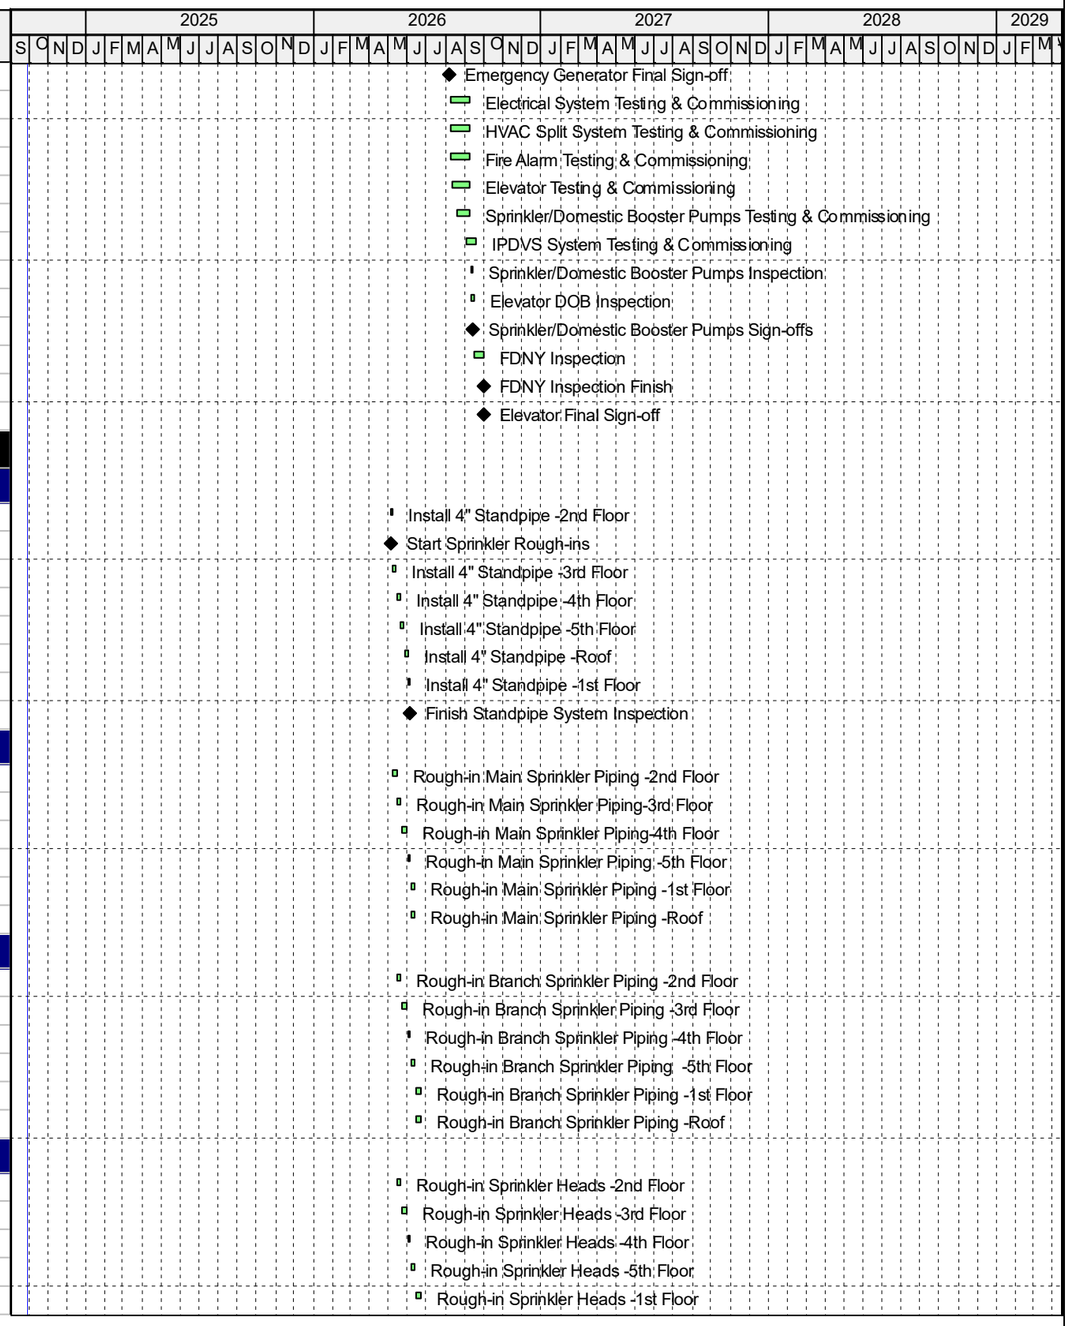

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-4440	Rough-in Sprinkler Heads -Roof	5	15-Jun-26	22-Jun-26
MIL-1330	Finish Sprinkler Rough-ins	0		22-Jun-26
CON-4650	Install 3 Way Roof Manifold -Roof	5	23-Jun-26	29-Jun-26
Control Valve Assembly		30	15-May-26	29-Jun-26
CON-3720	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -2nd Floor	5	15-May-26	21-May-26
CON-3880	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-3rd Floor	5	22-May-26	29-May-26
CON-4100	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-4th Floor	5	01-Jun-26	05-Jun-26
CON-4340	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -5th Floor	5	08-Jun-26	12-Jun-26
CON-5270	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -1st Floor	5	23-Jun-26	29-Jun-26
Air Testing		30	22-May-26	07-Jul-26
CON-3830	Sprinklers Air Testing-2nd Floor	5	22-May-26	29-May-26
CON-4060	Sprinklers Air Testing-3rd Floor	5	01-Jun-26	05-Jun-26
CON-4280	Sprinklers Air Testing-4th Floor	5	08-Jun-26	12-Jun-26
CON-4490	Sprinklers Air Testing-5th Floor	5	15-Jun-26	22-Jun-26
CON-5410	Sprinklers Air Testing-1st Floor	5	30-Jun-26	07-Jul-26
Site Work		93	29-Apr-26	10-Sep-26
Perimeter of New Building		49	02-Jul-26	10-Sep-26
CON-4660	Excavation - Drainage Work - Building Perimeter	3	02-Jul-26	07-Jul-26
CON-4740	Install Flood Barrier Wall - Drainage Work - Building Perimeter	3	08-Jul-26	10-Jul-26
CON-4860	Install Drilled Caisson Supported Ventilation Structure - Drainage Work - Building Perimeter	3	13-Jul-26	15-Jul-26
CON-4980	Install 4" & 6" & 10" & 12" DIP - Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-9170	Install 8" Combined Water Service (2nd Street)- Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-9180	Install 6" Fire Water Service (54th Avenue Street)- Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-5190	Install Catch Basin - Drainage Work - Building Perimeter	2	21-Jul-26	22-Jul-26
CON-5290	Install Storm Inlet With Hood & Storm Hood - Drainage Work - Building Perimeter	2	23-Jul-26	24-Jul-26
CON-5400	Install Trench Drain - Drainage Work - Building Perimeter	1	27-Jul-26	27-Jul-26
CON-9160	Excavate for Footings - Playground Area & Fences - Building Perimeter	2	28-Jul-26	29-Jul-26
CON-9010	Remove Steel Plate Protection over NYPA Easement - Playground Area & Fences - Building Perimeter	1	28-Jul-26	28-Jul-26
CON-9190	F/R/P Playground Equipment Footings - Playground Area & Fences - Building Perimeter	2	30-Jul-26	31-Jul-26
CON-5470	Install Flush Concrete Curb - Playground Area & Fences - Building Perimeter	3	03-Aug-26	05-Aug-26
CON-5420	Install Asphalt Pavement - Playground Area & Fences - Building Perimeter	2	04-Aug-26	05-Aug-26
CON-5600	Install Concrete Pavement Pedestrian Ramp With Painted Black Handrails - Playground Area & Fences - Building Perimeter	3	06-Aug-26	10-Aug-26
CON-5650	Install Playground Rubber Tile Safety Surface - Playground Area & Fences - Building Perimeter	3	11-Aug-26	13-Aug-26
CON-5800	Install Painted Asphalt Pavement & Painted Games On Asphalt Surface - Playground Area & Fences - Building Perimeter	3	14-Aug-26	18-Aug-26
CON-5850	Install Colored Athletic Wearing Surface Color - Playground Area & Fences - Building Perimeter	2	19-Aug-26	20-Aug-26
CON-5990	Install Playground Equipment - Playground Area & Fences - Building Perimeter	7	21-Aug-26	31-Aug-26
CON-6140	Install Basketball Hoop - Playground Area & Fences - Building Perimeter	1	01-Sep-26	01-Sep-26
CON-6190	Install Wrought Iron Fence Double Gate - Playground Area - Building Perimeter	3	02-Sep-26	04-Sep-26
CON-6270	Install Chain Link Fence - Playground Area & Fences - Building Perimeter	3	08-Sep-26	10-Sep-26
54th Avenue Street		36	29-Apr-26	18-Jun-26
MIL-1400	Start Site Work	0	29-Apr-26	
CON-3780	Install Traffic Control Devices - 54th Avenue Street	3	01-May-26	05-May-26
CON-3850	Remove Existing Steel Faced Curb - 54th Avenue Street	3	06-May-26	08-May-26

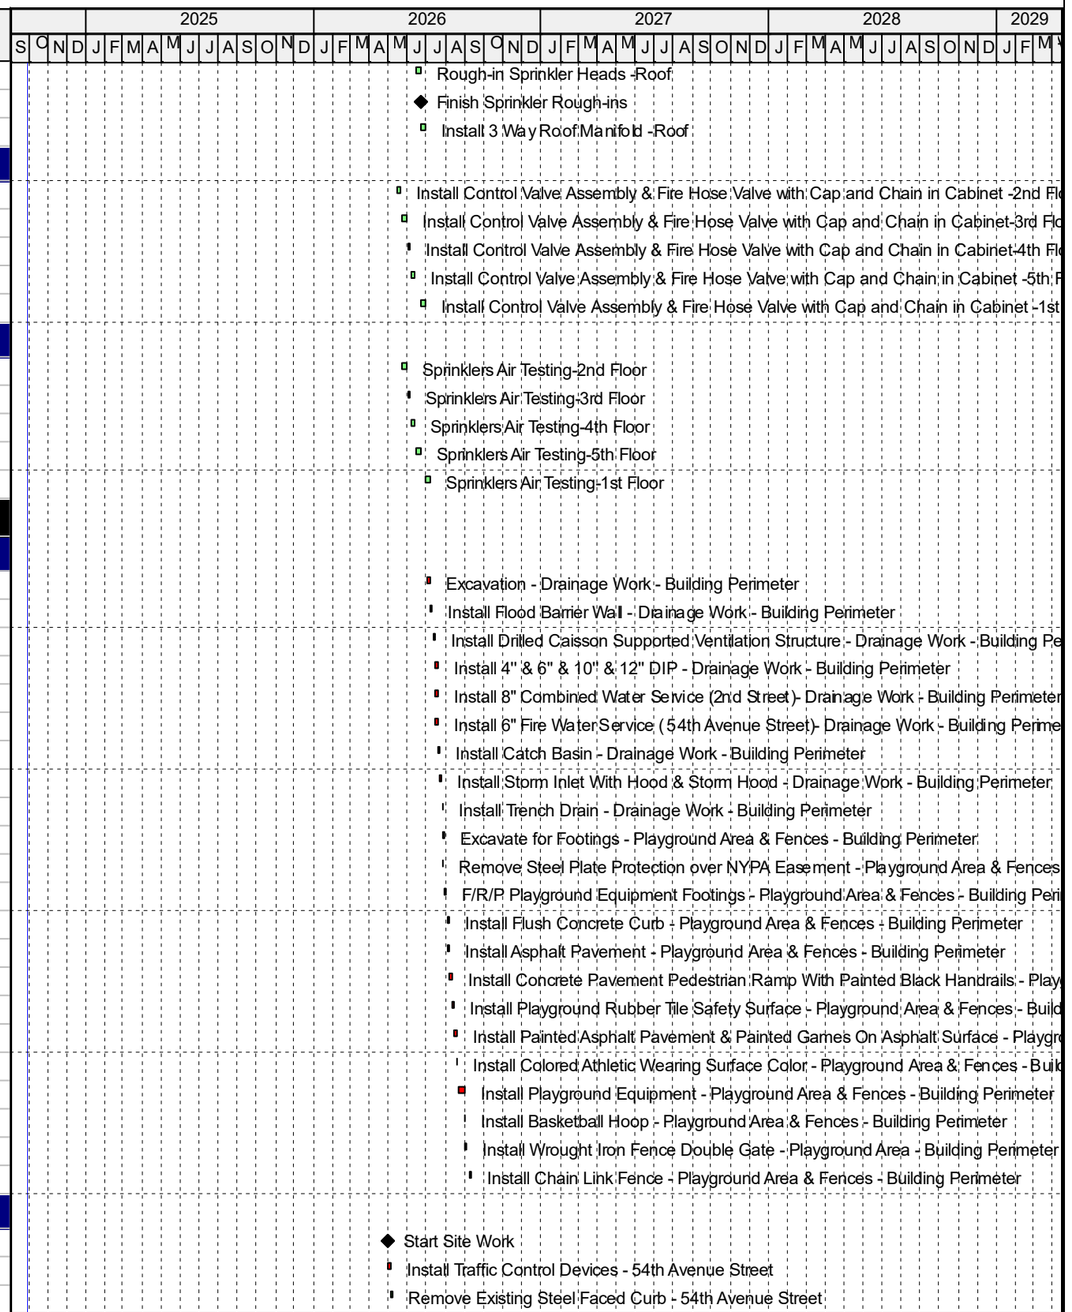

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3860	Remove Existing Asphalt - 54th Avenue Street	4	06-May-26	11-May-26
CON-3940	Remove Existing Electrical Manhole - 54th Avenue Street	4	12-May-26	15-May-26
CON-4080	Install 5' Wide Silva Cells Under Concrete Pavement Strip - 54th Avenue Street	4	18-May-26	21-May-26
CON-4150	Pavement Replacement - 54th Avenue Street	4	22-May-26	28-May-26
CON-4290	Install New Steel Faced Curb - 54th Avenue Street	4	29-May-26	03-Jun-26
CON-4300	Install Pedestrian Ramps With Truncated Domes - 54th Avenue Street	4	29-May-26	03-Jun-26
CON-4400	Install 4" Concrete Sidewalk - 54th Avenue Street	5	04-Jun-26	10-Jun-26
CON-4410	Install 7" Concrete Sidewalk - 54th Avenue Street	5	04-Jun-26	10-Jun-26
CON-4560	Install Pavement Marking - 54th Avenue Street	3	11-Jun-26	15-Jun-26
CON-4580	Remove Traffic Control Devices - 54th Avenue Street	3	16-Jun-26	18-Jun-26
2nd Street		39	06-May-26	01-Jul-26
CON-3870	Install Traffic Control Devices - 2nd Street	5	06-May-26	12-May-26
CON-3900	Remove Existing Sidewalk - 2nd Street	5	13-May-26	19-May-26
CON-3950	Install Pedestrian Ramps With Truncated Domes - 2nd Street	6	20-May-26	28-May-26
CON-4090	Remove Existing Steel Faced Curb - 2nd Street	6	29-May-26	05-Jun-26
CON-4160	Install New Steel Faced Curb - 2nd Street	6	08-Jun-26	15-Jun-26
CON-4170	Install 4" Concrete Sidewalk - 2nd Street	7	08-Jun-26	16-Jun-26
CON-4310	Install 7" Concrete Sidewalk - 2nd Street	6	16-Jun-26	24-Jun-26
CON-4420	Remove Traffic Control Devices - 2nd Street	5	25-Jun-26	01-Jul-26
Duct Insulations		40	07-May-26	06-Jul-26
CON-4070	Install Duct Insulation -2nd Floor	8	07-May-26	18-May-26
CON-4320	Install Duct Insulation -3rd Floor	8	19-May-26	29-May-26
CON-4570	Install Duct Insulation -4th Floor	8	01-Jun-26	10-Jun-26
CON-4710	Install Duct Insulation -5th Floor	8	11-Jun-26	23-Jun-26
CON-4840	Install Duct Insulation -1st Floor	8	24-Jun-26	06-Jul-26
Mockup Room		18	07-May-26	02-Jun-26
CON-4040	Install Walls GWB-Mockup Room	3	07-May-26	11-May-26
CON-4270	Install Gypsum Board Ceiling -Mockup Room	3	07-May-26	11-May-26
MIL-1360	Start Mockup Room Work	0	07-May-26	
MIL-1430	Start Architecture Finishes	0	07-May-26	
CON-4380	Install Doors & Hardware-Mockup Room	3	11-May-26	13-May-26
CON-4260	Install Door Frames-Mockup Room	2	12-May-26	13-May-26
CON-4480	Paint First coat -Mockup Room	2	14-May-26	15-May-26
CON-4640	Flooring Finishes-Mockup Room	2	18-May-26	19-May-26
CON-4750	Paint Second coat-Mockup Room	2	20-May-26	21-May-26
CON-4930	Install Furniture & Signs -Mockup Room	2	22-May-26	26-May-26
MIL-1410	Mockup Room Ready For Inspection	0		26-May-26
MIL-1420	Finish Mockup Room	0		26-May-26
CON-5000	Mockup Room Inspection & Punchlist	5	27-May-26	02-Jun-26
Emergency Generator		101	05-Mar-26	28-Jul-26
CON-99347	Install Lightning Protection System - Roof Floor	6	05-Mar-26	12-Mar-26
CON-3750	Install Emergency Generator- Roof Floor	4	17-Jul-26	22-Jul-26
CON-5380	Install Generator Connections -Roof Floor	4	23-Jul-26	28-Jul-26

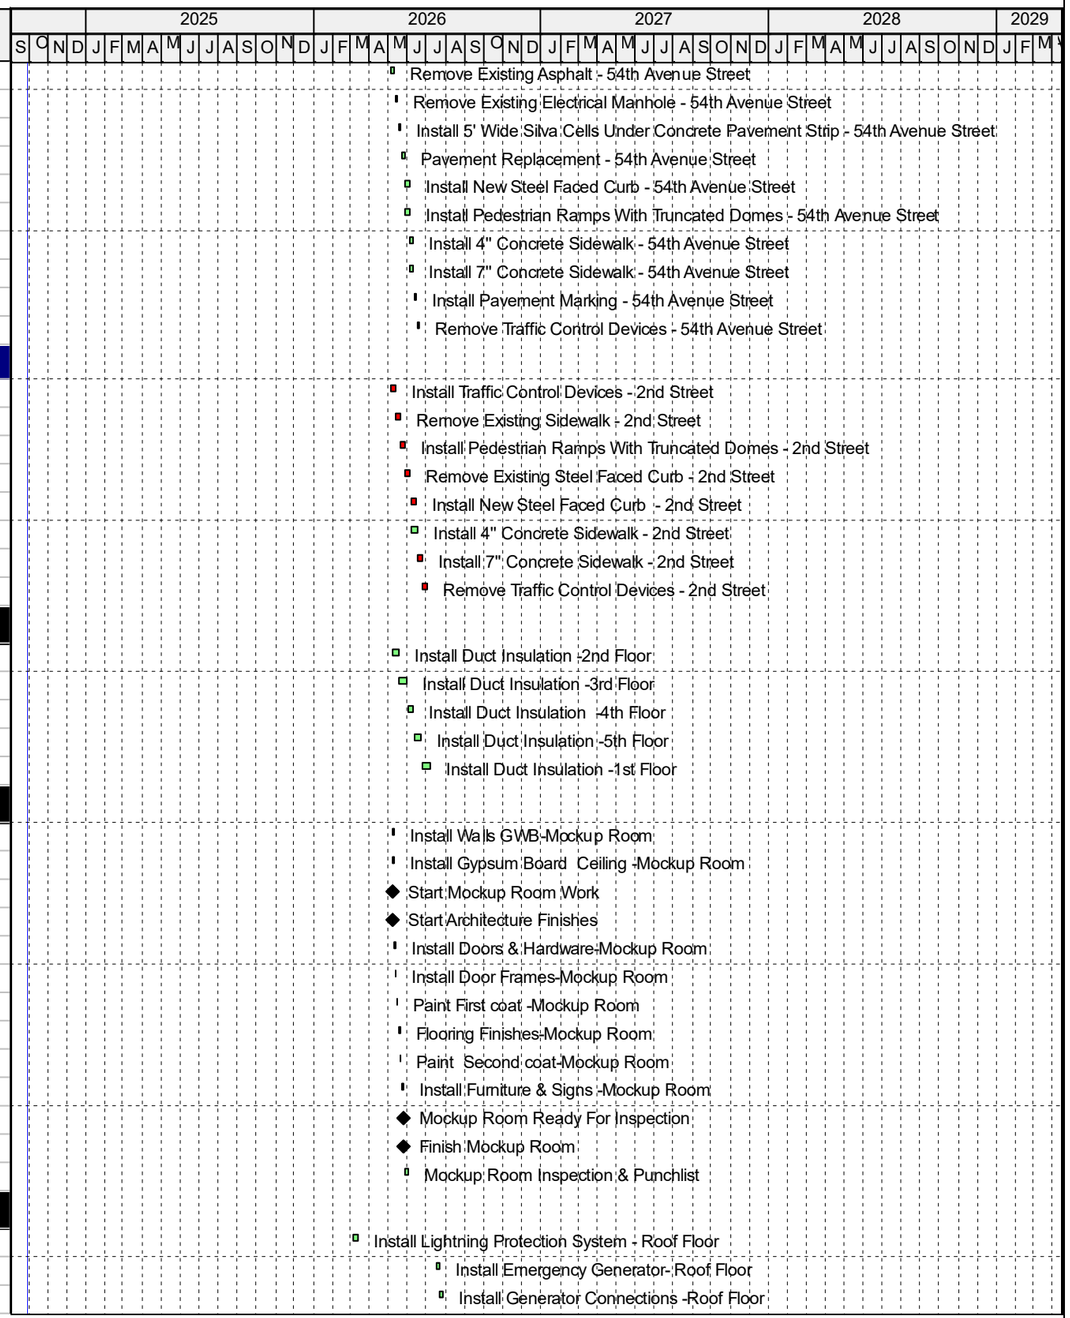

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
Gypsum Board Walls		55	16-Apr-26	06-Jul-26
CON-9070	In-Wall Inspection-2nd Floor	2	16-Apr-26	17-Apr-26
CON-9080	In-Wall Inspection -3rd Floor	2	22-Apr-26	23-Apr-26
CON-9090	In-Wall Inspection -4th Floor	7	28-Apr-26	06-May-26
CON-9100	In-Wall Inspections -5th Floor	7	04-May-26	12-May-26
CON-9110	In-Wall Inspection -1st Floor	2	19-May-26	20-May-26
CON-4030	Install Gypsum Board Walls-2nd Floor	5	27-May-26	02-Jun-26
MIL-1440	Start Gypsum Board	0	27-May-26	
CON-4200	Tape Gypsum Board -2nd Floor	4	28-May-26	02-Jun-26
CON-4360	Install Gypsum Board Walls-3rd Floor	5	03-Jun-26	09-Jun-26
CON-4540	Tape Gypsum Board -3rd Floor	4	04-Jun-26	09-Jun-26
CON-4620	Install Gypsum Board Walls-4th Floor	5	10-Jun-26	16-Jun-26
CON-4720	Tape Gypsum Board -4th Floor	4	11-Jun-26	16-Jun-26
CON-4810	Install Gypsum Board Walls-5th Floor	5	17-Jun-26	24-Jun-26
CON-4970	Tape Gypsum Board -5th Floor	4	18-Jun-26	24-Jun-26
CON-4450	Install Gypsum Board Walls-1st Floor	6	26-Jun-26	06-Jul-26
CON-4600	Tape Gypsum Board -1st Floor	4	30-Jun-26	06-Jul-26
Firestopping		24	01-Jun-26	06-Jul-26
CON-1120	Install Firestopping Mock-Up	2	01-Jun-26	02-Jun-26
CON-1140	Approve Firestopping Mock-Up	2	03-Jun-26	04-Jun-26
CON-4700	Install Firestopping-2nd Floor	3	05-Jun-26	09-Jun-26
MIL-1750	Start Firestopping	0	05-Jun-26	
CON-4850	Install Firestopping-3rd Floor	4	10-Jun-26	15-Jun-26
CON-5010	Install Firestopping-4th Floor	4	16-Jun-26	22-Jun-26
CON-5220	Install Firestopping-5th Floor	4	23-Jun-26	26-Jun-26
CON-5390	Install Firestopping-1st Floor	4	30-Jun-26	06-Jul-26
Gypsum Board Ceiling		29	03-Jun-26	15-Jul-26
CON-4370	Install Gypsum Board Ceiling -2nd Floor	6	03-Jun-26	10-Jun-26
CON-4630	Install Gypsum Board Ceiling-3rd Floor	6	11-Jun-26	18-Jun-26
CON-4820	Install Gypsum Board Ceiling-4th Floor	6	22-Jun-26	29-Jun-26
CON-5100	Install Gypsum Board Ceiling-5th Floor	6	30-Jun-26	08-Jul-26
CON-5480	Install Gypsum Board Ceiling -1st Floor	6	08-Jul-26	15-Jul-26
Wall Tiles		29	03-Jun-26	15-Jul-26
CON-4350	Install Ceramic Wall Tiles at Corridor-2nd Floor	7	03-Jun-26	11-Jun-26
CON-4610	Install Ceramic Wall Tiles at Corridor-3rd Floor	7	12-Jun-26	23-Jun-26
CON-4800	Install Ceramic Wall Tiles at Corridor-4th Floor	7	24-Jun-26	02-Jul-26
CON-5080	Install Ceramic Wall Tiles at Corridor-5th Floor	7	06-Jul-26	14-Jul-26
CON-4680	Install Ceramic Wall Tiles at Corridor -1st Floor	7	07-Jul-26	15-Jul-26
1st Coat Painting		29	10-Jun-26	22-Jul-26
MIL-1450	Start 1st Coat Painting	0	10-Jun-26	
CON-4830	Install First Coat Painting-2nd Floor	5	11-Jun-26	17-Jun-26
CON-5110	Install First Coat Painting-3rd Floor	5	22-Jun-26	26-Jun-26
CON-5340	Install First Coat Painting-4th Floor	5	29-Jun-26	06-Jul-26

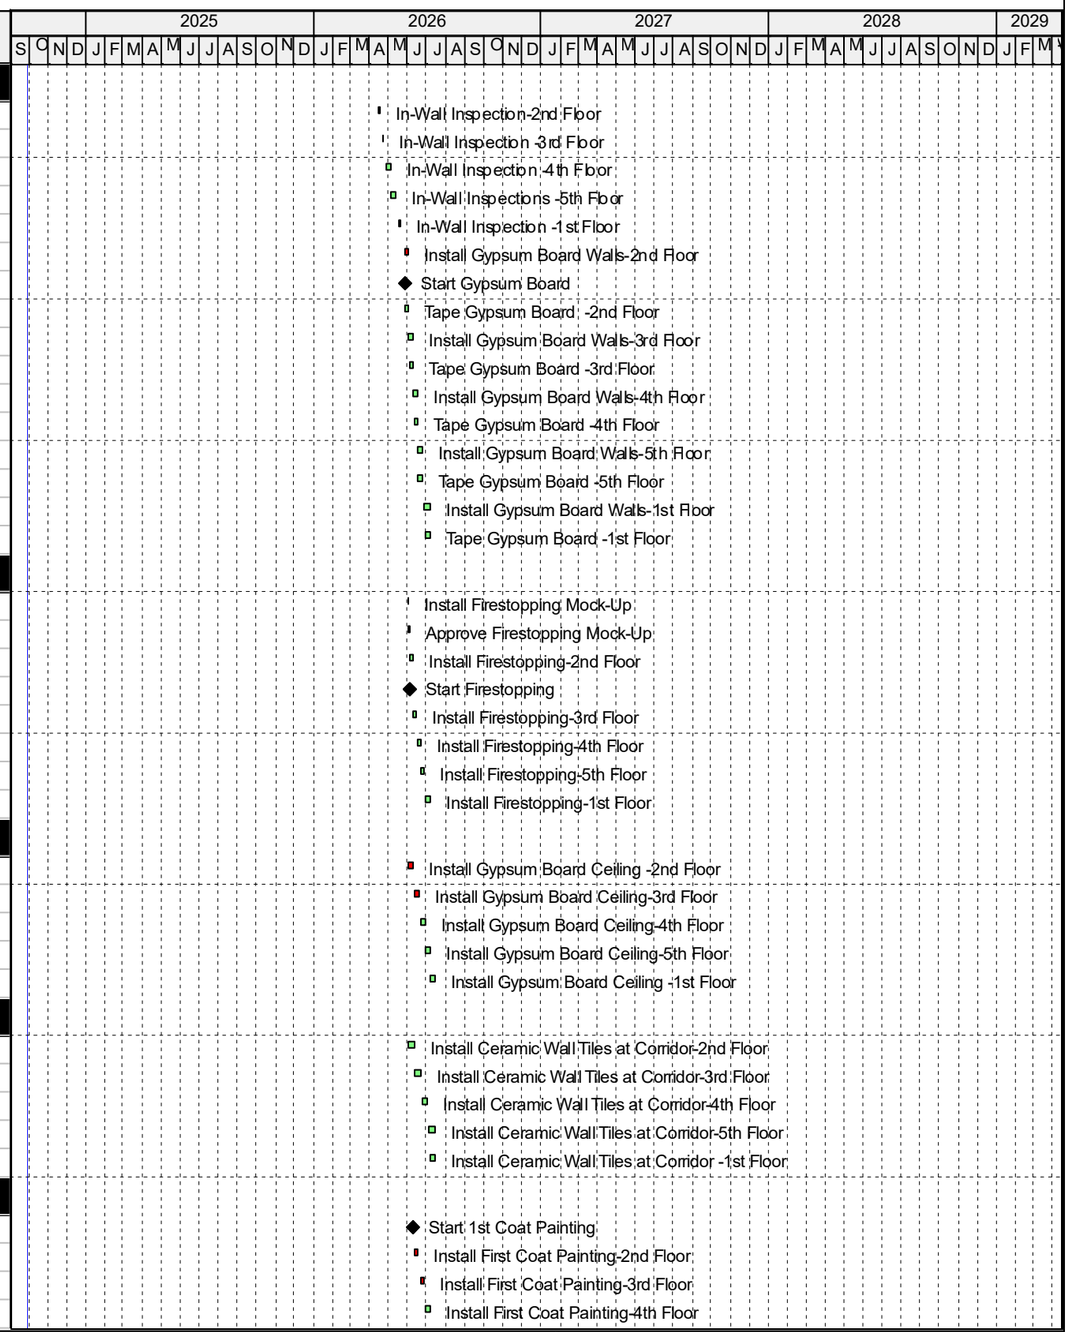

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-5530	Install First Coat Painting -5th Floor	5	09-Jul-26	15-Jul-26
CON-5720	Install First Coat Painting-1st Floor	5	16-Jul-26	22-Jul-26
Intrusion System		35	18-Jun-26	07-Aug-26
CON-98797	Install Intrusion System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-98807	Install Intrusion System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-98817	Install Intrusion System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-98827	Install Intrusion System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-98837	Install Intrusion System Components-1st Floor	4	04-Aug-26	07-Aug-26
Auxiliary System		31	18-Jun-26	03-Aug-26
CON-98847	Install Auxiliary System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-98857	Install Auxiliary System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-98867	Install Auxiliary System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-98877	Install Auxiliary System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-98887	Install Auxiliary System Components-1st Floor	4	29-Jul-26	03-Aug-26
Sound Clock System		27	18-Jun-26	28-Jul-26
CON-98897	Install Sound Clock System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-98907	Install Sound Clock System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-98917	Install Sound Clock System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-98927	Install Sound Clock System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-98937	Install Sound Clock System Components-1st Floor	3	24-Jul-26	28-Jul-26
Doors & Frames		31	18-Jun-26	03-Aug-26
CON-5120	Install Door Frames & Doors-2nd Floor	5	18-Jun-26	25-Jun-26
CON-5350	Install Door Frames & Doors-3rd Floor	5	29-Jun-26	06-Jul-26
CON-5540	Install Door Frames & Doors-4th Floor	5	07-Jul-26	13-Jul-26
CON-5680	Install Door Frames & Doors -5th Floor	5	16-Jul-26	22-Jul-26
CON-5920	Install Door Frames & Doors-1st Floor	5	23-Jul-26	29-Jul-26
CON-99267	Install Rolling Doors-1st Floor	3	30-Jul-26	03-Aug-26
Acoustical Ceiling Tiles		39	14-Jul-26	04-Sep-26
CON-5090	Install Acoustical Ceiling Tiles-2nd Floor	5	14-Jul-26	20-Jul-26
CON-5330	Install Acoustical Ceiling Tiles-3rd Floor	5	22-Jul-26	28-Jul-26
CON-5870	Install Metal Panel Ceiling & Metal Geometric Ceiling -1st Floor	5	23-Jul-26	29-Jul-26
CON-5520	Install Acoustical Ceiling Tiles-4th Floor	5	30-Jul-26	05-Aug-26
CON-5670	Install Acoustical Ceiling Tiles-5th Floor	5	06-Aug-26	12-Aug-26
CON-5880	Install Acoustical Ceiling Tiles -1st Floor	5	31-Aug-26	04-Sep-26
Flooring		28	26-Jun-26	05-Aug-26
CON-5360	Install Flooring Tiles-2nd Floor	5	26-Jun-26	02-Jul-26
CON-5550	Install Flooring Tiles-3rd Floor	5	07-Jul-26	13-Jul-26
CON-5690	Install Flooring Tiles-4th Floor	5	14-Jul-26	20-Jul-26
CON-5890	Install Flooring Tiles -5th Floor	5	23-Jul-26	29-Jul-26
CON-6080	Install Flooring Tiles-1st Floor	5	30-Jul-26	05-Aug-26
Plumbing Finishes		28	06-Jul-26	12-Aug-26
CON-5570	Install Plumbing Fixtures -2nd Floor	7	06-Jul-26	14-Jul-26

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-5730	Install Plumbing Fixtures -3rd Floor	7	15-Jul-26	23-Jul-26
CON-5930	Install Plumbing Fixtures -4th Floor	7	24-Jul-26	03-Aug-26
CON-6090	Install Plumbing Fixtures -5th Floor	7	04-Aug-26	12-Aug-26
CON-6180	Install Plumbing Fixtures-1st Floor	5	06-Aug-26	12-Aug-26
Final Coat Painting		40	06-Jul-26	28-Aug-26
CON-5560	Install Final Coat Painting-2nd Floor	6	06-Jul-26	13-Jul-26
CON-5700	Install Final Coat Painting-3rd Floor	6	14-Jul-26	21-Jul-26
CON-5900	Install Final Coat Painting-4th Floor	6	22-Jul-26	29-Jul-26
CON-6060	Install Final Coat Painting -5th Floor	6	13-Aug-26	20-Aug-26
CON-6170	Install Final Coat Painting-1st Floor	6	21-Aug-26	28-Aug-26
Furniture & Milling Work		43	14-Jul-26	11-Sep-26
CON-5710	Install Furniture & Milling Work (Contractor Provided & Installed) -2nd Floor	5	14-Jul-26	20-Jul-26
CON-9030	Install Furniture & Milling Work (Owner Provided & Installed) -2nd Floor	5	14-Jul-26	20-Jul-26
CON-99247	Install Laboratory Equipment -3rd Floor	4	14-Jul-26	17-Jul-26
CON-5910	Install Furniture & Milling Work (Contractor Provided & Installed) -3rd Floor	5	22-Jul-26	28-Jul-26
CON-9040	Install Furniture & Milling Work (Owner Provided & Installed) -3rd Floor	5	22-Jul-26	28-Jul-26
CON-6070	Install Furniture & Milling Work (Contractor Provided & Installed) -4th Floor	5	30-Jul-26	05-Aug-26
CON-9050	Install Furniture & Milling Work (Owner Provided & Installed) -4th Floor	5	30-Jul-26	05-Aug-26
CON-6150	Install Furniture & Milling Work (Contractor Provided & Installed) -5th Floor	4	21-Aug-26	26-Aug-26
CON-9060	Install Furniture & Milling Work (Owner Provided & Installed) -5th Floor	4	21-Aug-26	26-Aug-26
CON-6300	Install Furniture & Milling Work (Contractor Provided & Installed) -1st Floor	4	31-Aug-26	03-Sep-26
CON-6310	Install Security Screens & Barriers-1st Floor	3	31-Aug-26	02-Sep-26
CON-6320	Install Cafeteria Equipment-1st Floor	4	31-Aug-26	03-Sep-26
CON-9020	Install Furniture & Milling Work (Owner Provided & Installed) -1st Floor	3	31-Aug-26	02-Sep-26
CON-6380	Install Food Service Equipment-1st Floor	5	04-Sep-26	11-Sep-26
Signages		37	21-Jul-26	10-Sep-26
CON-5820	Install Signages-2nd Floor	5	21-Jul-26	27-Jul-26
CON-6030	Install Signages-3rd Floor	5	29-Jul-26	04-Aug-26
CON-6160	Install Signages-4th Floor	5	06-Aug-26	12-Aug-26
CON-6280	Install Signages- 5th Floor	5	27-Aug-26	02-Sep-26
CON-6370	Install Signages-1st Floor	4	04-Sep-26	10-Sep-26
Demobilization		214	09-Sep-26	15-Aug-27
CLO-1300	Provide Training	10	09-Sep-26	22-Sep-26
CLO-1030	Pre-Final Clean-Out	5	11-Sep-26	17-Sep-26
CLO-1040	Pre-TCO Inspection	11	18-Sep-26	02-Oct-26
CLO-1110	Pre-TCO Punchlist	10	05-Oct-26	19-Oct-26
MIL-1510	TCO	0		19-Oct-26*
CLO-1050	Pre-Substantial Punchlist	105	20-Oct-26	17-Apr-27
MIL-1550	Substantial Completion	0		17-Apr-27*
CLO-1060	Prepare & Submit O&M Manuals	30	19-Apr-27	01-Jun-27
CLO-1070	Prepare & Submit As-Built Drawings	30	02-Jun-27	15-Jul-27
CLO-1080	Final Inspection	5	16-Jul-27	22-Jul-27
CLO-1090	Final Clean Out	10	23-Jul-27	05-Aug-27

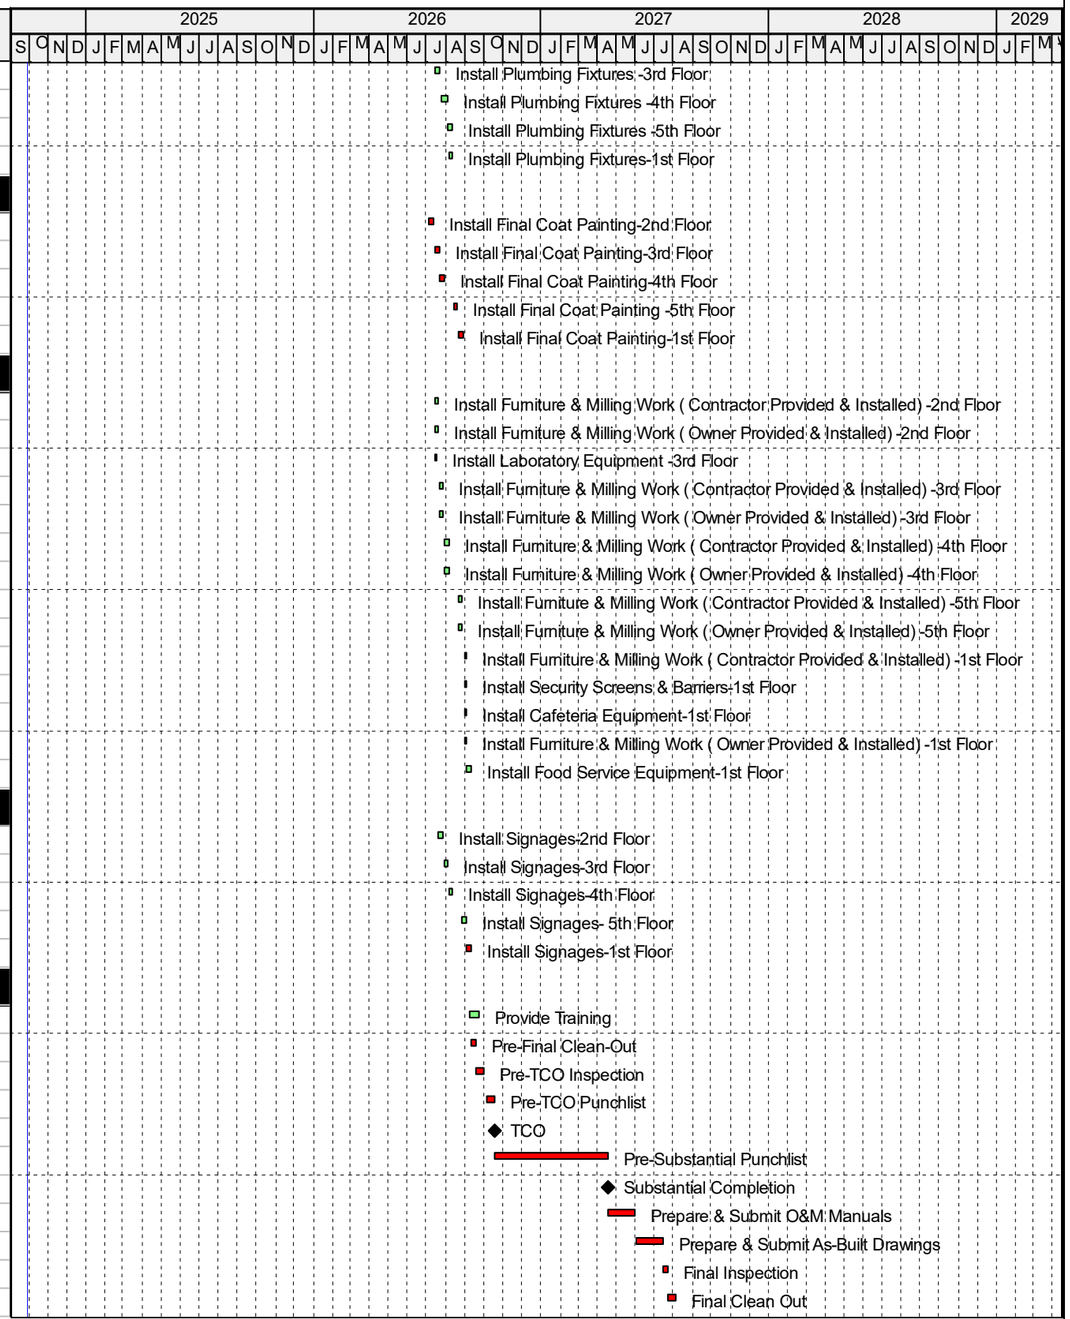

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Subcontractor Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CLO-1100	Demobilization	10	06-Aug-27	15-Aug-27
MIL-1560	Final Completion	0		15-Aug-27*



APPENDIX 7
Full Schedule Layout Grouped by Trades Code

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
DIV01-General Requirements		699	30-Sep-24	15-Aug-27
MIL-1000	NTP	0	30-Sep-24	
MIL-1030	Project Duration(From NTP till TCO)	750	30-Sep-24	19-Oct-26
MIL-1040	Project Duration(From NTP till Substantial Completion)	930	30-Sep-24	17-Apr-27
PRE-2590	Meeting With SCA to Review The Permit Requirements	14	30-Sep-24	18-Oct-24
PRE-2600	Prepare & Submit Permit Waiver Requests to SCA Chief Project Officer	5	30-Sep-24	04-Oct-24
MIL-1770	Project Duration(From NTP till Final Completion)	1050	30-Sep-24	15-Aug-27
MIL-2542	Complete Subcontractor 'Buyout'	0		11-Oct-24
SUB-1310	Prepare & Submit Training Outline & Schedule	81	15-Oct-24	11-Feb-25
SUB-1320	Prepare & Submit Product Substitutions	82	15-Oct-24	12-Feb-25
SUB-1330	Prepare & Submit Temporary Ventilation Plan	81	15-Oct-24	11-Feb-25
SUB-1340	Prepare & Submit Construction Indoor Air Quality Management Plan	81	15-Oct-24	11-Feb-25
SUB-1350	Prepare & Submit Site Safety Plan	2	15-Oct-24	16-Oct-24
SUB-1360	Prepare & Submit CWM Plan	81	15-Oct-24	11-Feb-25
SUB-1370	Prepare & Submit Photo Submission - Temporary Fence	15	15-Oct-24	04-Nov-24
SUB-1380	Prepare & Submit Heating Plan	81	15-Oct-24	11-Feb-25
SUB-1390	Prepare & Submit Sample Classroom Materials	81	15-Oct-24	11-Feb-25
SUB-1400	Prepare & Submit Sustainable Materials	10	15-Oct-24	28-Oct-24
SUB-1410	Prepare & Submit Submittal Schedule	60	15-Oct-24	10-Jan-25
SUB-1570	Prepare & Submit QCP	30	15-Oct-24	26-Nov-24
SUB-1610	Prepare & Submit Baseline Schedule	52	15-Oct-24	30-Dec-24
SUB-1780	Prepare & Submit Initial Underground Coordination Drawings	50	15-Oct-24	26-Dec-24
SUB-1790	Prepare & Submit Initial 1st Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1800	Prepare & Submit Initial 2nd Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1810	Prepare & Submit Initial 3rd Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1820	Prepare & Submit Initial 4th Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1830	Prepare & Submit Initial 5th Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1840	Prepare & Submit Supplemental Comissioning Requirements	81	15-Oct-24	11-Feb-25
SUB-1850	Prepare & Submit Record Documents	81	15-Oct-24	11-Feb-25
SUB-2340	Prepare & Submit Tree Protection Plan	71	15-Oct-24	28-Jan-25
APP-1000	Review & Approve Site Safety Plan	21	17-Oct-24	06-Nov-24
APP-1040	Review & Approve Sustainable Materials	21	29-Oct-24	18-Nov-24
MIL-1660	Start Security Guard Services (30 Days From NTP)	0	30-Oct-24	
APP-1060	Review & Approve Photo Submission - Temporary Fence	21	05-Nov-24	25-Nov-24
APP-1130	Review & Approve QCP	21	27-Nov-24	17-Dec-24
APP-1230	Review & Approve Initial Underground Coordination Drawings	21	27-Dec-24	16-Jan-25
APP-1240	Review & Approve Baseline Schedule	21	31-Dec-24	20-Jan-25
APP-1260	Review & Approve Submittal Schedule	21	11-Jan-25	31-Jan-25
SUB-2270	Prepare & Submit Final Underground Coordination Drawings	37	17-Jan-25	11-Mar-25
APP-2340	Review & Approve Tree Protection Plan	21	29-Jan-25	18-Feb-25
APP-1330	Review & Approve Initial 1st Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1340	Review & Approve Initial 2nd Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1350	Review & Approve Initial 3rd Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1360	Review & Approve Initial 4th Floor Coordination Drawings	21	04-Feb-25	24-Feb-25

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1370	Review & Approve Initial 5th Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1590	Review & Approve Training Outline & Schedule	21	12-Feb-25	04-Mar-25
APP-1600	Review & Approve Temporary Ventilation Plan	21	12-Feb-25	04-Mar-25
APP-1610	Review & Approve Construction Indoor Air Quality Management Plan	21	12-Feb-25	04-Mar-25
APP-1620	Review & Approve CWM Plan	21	12-Feb-25	04-Mar-25
APP-1630	Review & Approve Heating Plan	21	12-Feb-25	04-Mar-25
APP-1640	Review & Approve Sample Classroom Materials	21	12-Feb-25	04-Mar-25
APP-1850	Review & Approve Supplemental Comissioning Requirements	21	12-Feb-25	04-Mar-25
APP-1860	Review & Approve Record Documents	21	12-Feb-25	04-Mar-25
APP-2260	Review & Approve Product Substitutions	21	13-Feb-25	05-Mar-25
MIL-2572	Place Steel Mill Order	0	20-Feb-25	
SUB-2280	Prepare & Submit Final 1st Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2290	Prepare & Submit Final 2nd Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2300	Prepare & Submit Final 3rd Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2310	Prepare & Submit Final 4th Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2320	Prepare & Submit Final 5th Floor Coordination Drawings	49	25-Feb-25	02-May-25
MIL-2762	Green Schools Compliance Submission	0		04-Mar-25
APP-2270	Review & Approve Final Foundations Coordination Drawings	21	12-Mar-25	01-Apr-25
APP-2280	Review & Approve Final 1st Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2290	Review & Approve Final 2nd Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2300	Review & Approve Final 3rd Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2310	Review & Approve Final 4th Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2320	Review & Approve Final 5th Floor Coordination Drawings	21	03-May-25	23-May-25
MIL-1640	Provide Complete Set of Approved Coordination Drawings	0		23-May-25
PRE-2630	Obtain Builders Pavement Permit	10	16-Sep-25	29-Sep-25
PRE-2640	Obtain Excavation & Shoring Permit	10	16-Sep-25	29-Sep-25
PRE-2650	Obtain Permit to Enter (PTE) Amtrak	10	16-Sep-25	29-Sep-25
PRE-2660	Obtain NYPA Permit	10	16-Sep-25	29-Sep-25
PRE-2540	SCA Work Notification	7	23-Sep-25	29-Sep-25
PRE-1660	DOB Permit & Insurance	3	25-Sep-25	29-Sep-25
PRE-1460	Obtain Construction Fences Permit	3	25-Sep-25	29-Sep-25
PRE-2550	Obtain CCD1	3	25-Sep-25	29-Sep-25
PRE-2570	Obtain Sidewalk Shed Permits	3	25-Sep-25	29-Sep-25
MIL-2532	Submit Complete Permit Application	0		29-Sep-25
MIL-2832	Issuance of Excavation & Shoring Permit	0		29-Sep-25
MIL-2842	Issuance of Builders Pavement Permit	0		29-Sep-25
MIL-2852	Issuance of Permit to Enter (PTE)	0		29-Sep-25
MIL-2862	Issuance of NYPA Permit	0		29-Sep-25
MIL-2872	Issuance of Construction Fences Permit	0		29-Sep-25
MIL-2882	Issuance of Sidewalk Shed Permits	0		29-Sep-25
MIL-2892	Issuance of CCD1	0		29-Sep-25
MIL-2902	Issuance of DOB Permit & Insurance	0		29-Sep-25
PRE-2610	Prepare & Submit FDNY Fuel Permit	10	06-Oct-25	20-Oct-25
PRE-2620	Review & Approve FDNY Fuel Permit	21	21-Oct-25	10-Nov-25

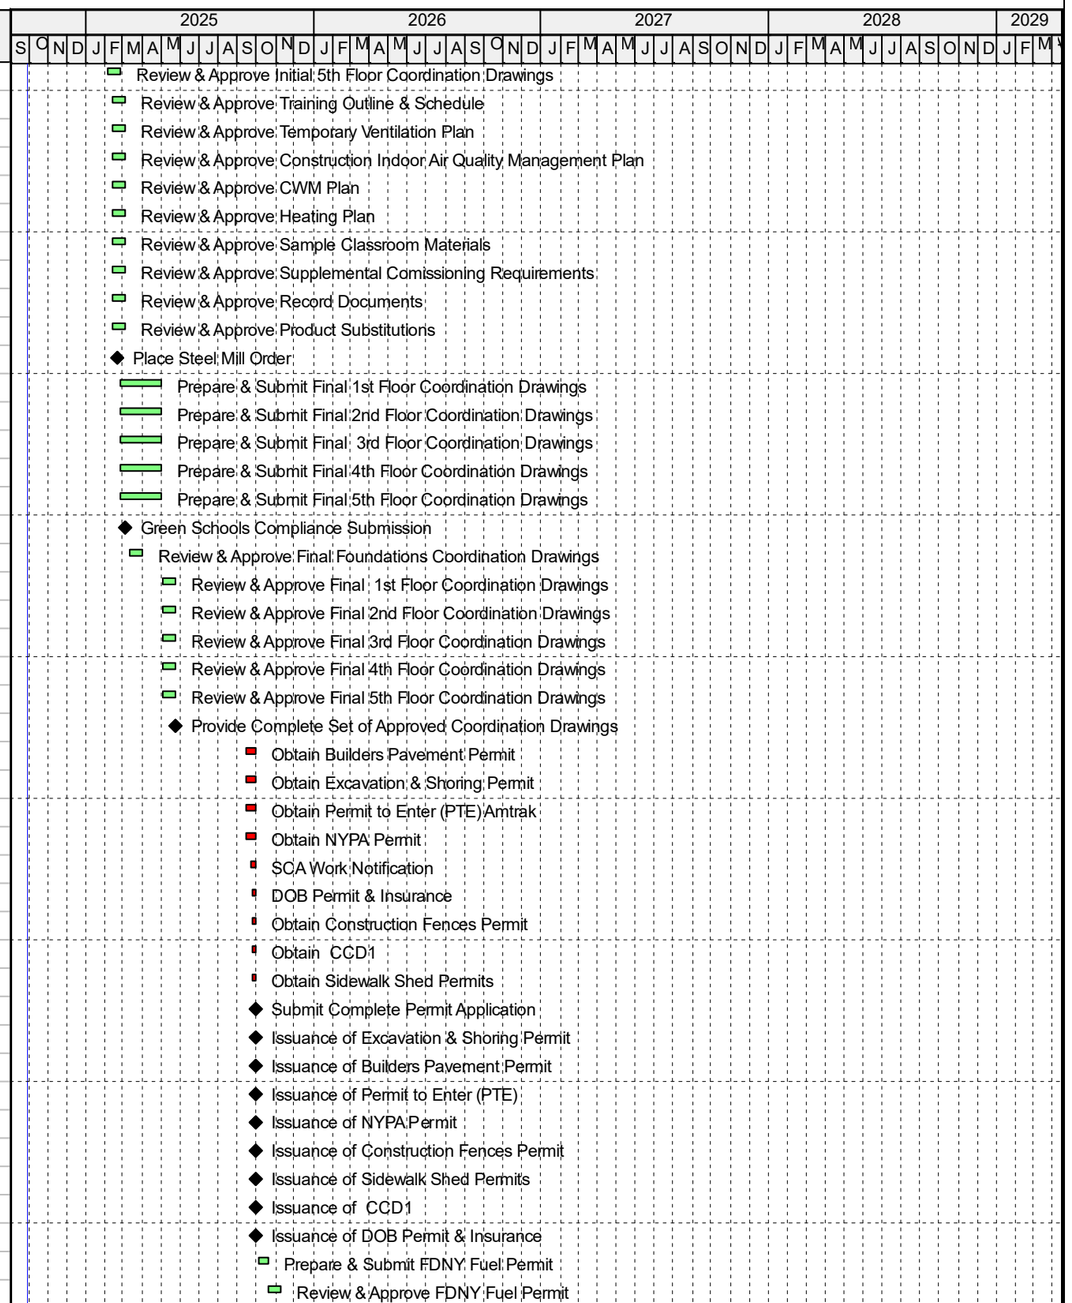

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
MIL-2582	Start Concrete Placement	0	28-Oct-25	
MIL-2812	Start Foundation	0	28-Oct-25	
MIL-2912	Start Concrete Cast In Place Inspection	0	28-Oct-25	
MIL-2622	Deliveries of all owner-furnished equipment and/or materials	0		06-Feb-26
MIL-2612	Start Suspended Ceiling Grid	0	16-Mar-26	
MIL-2922	Start Pre -Cast Concrete Inspection	0	25-Mar-26	
MIL-2602	Start Mechanical Distribution Lines	0	08-Apr-26	
MIL-2712	Start Low Voltage	0	16-Apr-26	
MIL-2632	Finish HVAC	0		06-Jul-26
MIL-2982	Finish Fire-Resistant Penetrations And Joints Inspection	0		06-Jul-26
MIL-2732	Start Mechanical and Electrical System Commissioning	0	07-Jul-26	
MIL-2562	Start Below Grade Plumbing and Other Utilities	0	16-Jul-26	
MIL-2742	Permanent Power Available	0		27-Jul-26
MIL-2592	P&D - Connection to Roof Drains	0	28-Jul-26	
MIL-2692	Building HVAC Flush-out	0		03-Aug-26
CLO-1190	Pre-Elevator Test Inspection	5	05-Aug-26	11-Aug-26
MIL-1680	Emergency Generator Final Sign-off	0		07-Aug-26
MIL-2642	Finish Fire Alarm Signoff	0		07-Aug-26
MIL-2962	Finish Fire Alarm Inspection	0		07-Aug-26
MIL-2802	Provision of Training Schedules (30 days prior to start of Training)	0	10-Aug-26	
MIL-2702	Finish Concrete Work	0		10-Aug-26
MIL-2822	Elevator Ready for Testing	0		11-Aug-26
MIL-2672	Finish Painting	0		28-Aug-26
CLO-1130	IPDVS System Testing & Commissioning	11	03-Sep-26	18-Sep-26
MIL-2722	Start Kitchen	0	04-Sep-26	
MIL-2662	Finishes and Ceiling Complete	0		04-Sep-26
CLO-1300	Provide Training	10	09-Sep-26	22-Sep-26
CLO-1200	Elevator DOB Inspection	5	10-Sep-26	16-Sep-26
CLO-1030	Pre-Final Clean-Out	5	11-Sep-26	17-Sep-26
CLO-1150	FDNY Inspection	12	15-Sep-26	30-Sep-26
PER-2650	Elevator Equipment Use Permit	10	17-Sep-26	30-Sep-26
CLO-1040	Pre-TCO Inspection	11	18-Sep-26	02-Oct-26
MIL-2652	Finish Mechanical and Electrical System Commissioning	0		18-Sep-26
MIL-2772	Performance test for all mechanical equipment and low voltage systems	0		18-Sep-26
MIL-2792	Commissioning for all mechanical equipment and low voltage systems	0		18-Sep-26
MIL-1650	FDNY Inspection Finish	0		30-Sep-26
MIL-1670	Elevator Final Sign-off	0		30-Sep-26
CLO-1110	Pre-TCO Punchlist	10	05-Oct-26	19-Oct-26
MIL-1510	TCO	0		19-Oct-26*
CLO-1050	Pre-Substantial Punchlist	105	20-Oct-26	17-Apr-27
MIL-1550	Substantial Completion	0		17-Apr-27*
CLO-1060	Prepare & Submit O&M Manuals	30	19-Apr-27	01-Jun-27
MIL-2782	Submission of Operations and Maintenance Manuals	0		01-Jun-27
CLO-1070	Prepare & Submit As-Built Drawings	30	02-Jun-27	15-Jul-27

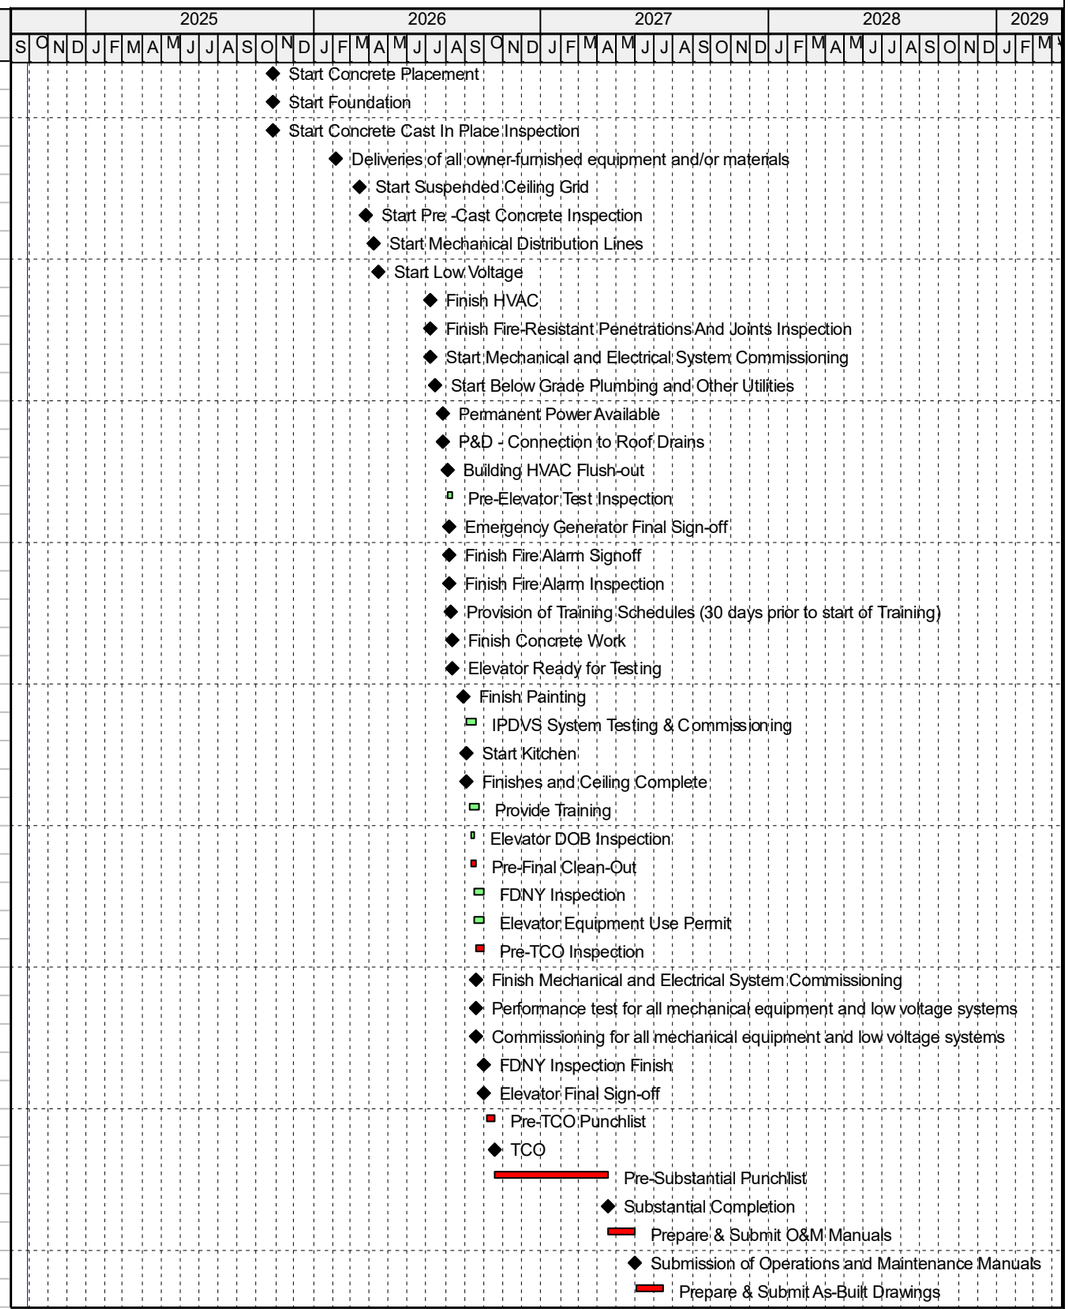

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

PROJECS
ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CLO-1080	Final Inspection	5	16-Jul-27	22-Jul-27
CLO-1090	Final Clean Out	10	23-Jul-27	05-Aug-27
CLO-1100	Demobilization	10	06-Aug-27	15-Aug-27
MIL-1560	Final Completion	0		15-Aug-27*
DIV02-Existing Conditions		513	30-Sep-24	19-Oct-26
MIL-2522	Site Access	365	30-Sep-24	29-Sep-25
CON-99257	Subcontractor Buyout	10	30-Sep-24	11-Oct-24
SUB-1200	Prepare & Submit Planting Schedule	81	15-Oct-24	11-Feb-25
SUB-1210	Prepare & Submit Site Furnishings Shop Drawings	15	15-Oct-24	04-Nov-24
SUB-1220	Prepare & Submit Playgroung Equipment Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1230	Prepare & Submit Ductile Iron Pipes	37	15-Oct-24	06-Dec-24
SUB-1240	Prepare & Submit Catch Basin Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1250	Prepare & Submit Concrete Curbs & Pavements Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-1260	Prepare & Submit Steel Curb Facing Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-1270	Prepare & Submit Asphaltic Concrete Paving	81	15-Oct-24	11-Feb-25
SUB-1280	Prepare & Submit SSDS Geotextile	40	15-Oct-24	11-Dec-24
SUB-1290	Prepare & Submit Gas Vapor Barrier Submittal & Inspection Schedule	81	15-Oct-24	11-Feb-25
SUB-1300	Prepare & Submit Existing Conditions Survey	10	15-Oct-24	28-Oct-24
SUB-1560	Prepare & Submit Erosion Control and Sedimentation Plan	7	15-Oct-24	23-Oct-24
SUB-1860	Prepare & Submit Environmental Site Assessment Reports	81	15-Oct-24	11-Feb-25
SUB-1870	Prepare & Submit Selective Removals & Demoloition	81	15-Oct-24	11-Feb-25
SUB-1880	Prepare & Submit Foundation Product Data	5	15-Oct-24	21-Oct-24
SUB-1890	Prepare & Submit Trench Drains Product Data	81	15-Oct-24	11-Feb-25
SUB-1900	Prepare & Submit Chain Link Fences & Gates Drawings	81	15-Oct-24	11-Feb-25
SUB-1910	Prepare & Submit Outdoor Game Equipment	81	15-Oct-24	11-Feb-25
SUB-2360	Prepare & Submit Adjacent Property and Structures Protection & Monitoring Plan	81	15-Oct-24	11-Feb-25
SUB-2920	Prepare & Submit Documentation of Proper Disposal	81	15-Oct-24	11-Feb-25
SUB-3230	Prepare & Submit Shop Equipment Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3240	Prepare & Submit Shop Equipment Product Data	81	15-Oct-24	11-Feb-25
SUB-3760	Prepare & Submit Lighting Control Devices Shop Drawing	71	15-Oct-24	28-Jan-25
SUB-3770	Prepare & Submit Lighting Control Devices Product Data	71	15-Oct-24	28-Jan-25
SUB-3780	Prepare & Submit Lighting Control Devices Warranty	71	15-Oct-24	28-Jan-25
SUB-3790	Prepare & Submit Surge Protective Devices Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3800	Prepare & Submit Surge Protective Devices Product Data	81	15-Oct-24	11-Feb-25
SUB-3810	Prepare & Submit Surge Protective Devices Warranty	81	15-Oct-24	11-Feb-25
SUB-3820	Prepare & Submit Service Entrance Equipment Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3830	Prepare & Submit Service Entrance Equipment Product Data	81	15-Oct-24	11-Feb-25
SUB-3840	Prepare & Submit Service Entrance Equipment Warranty	81	15-Oct-24	11-Feb-25
SUB-3850	Prepare & Submit Enclosed Switches Product Data	81	15-Oct-24	11-Feb-25
SUB-3860	Prepare & Submit Enclosed Switches Test Reports	81	15-Oct-24	11-Feb-25
SUB-3870	Prepare & Submit Motors, Motor Control Centers and Starters Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3880	Prepare & Submit Motors, Motor Control Centers and Starters Product Data	81	15-Oct-24	11-Feb-25
SUB-3890	Prepare & Submit Motors, Motor Control Centers and Starters Field Test Reports	81	15-Oct-24	11-Feb-25
SUB-3900	Prepare & Submit Lightning Protection Shop Drawing	81	15-Oct-24	11-Feb-25

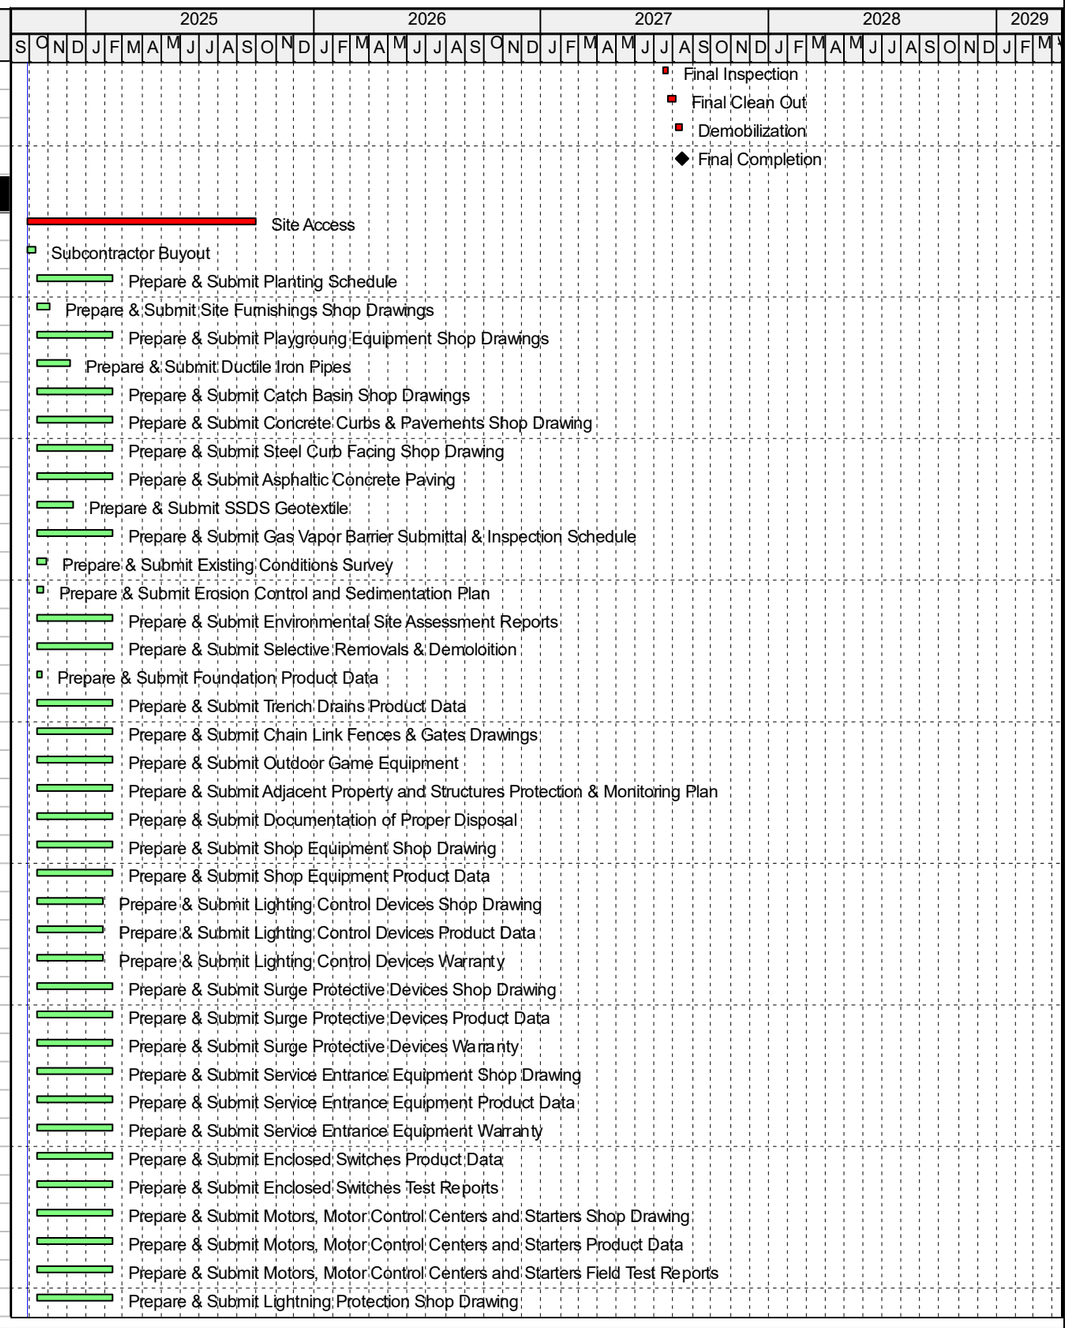

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-3920	Prepare & Submit Lightning Protection Test Reports	81	15-Oct-24	11-Feb-25
SUB-3930	Prepare & Submit Fiber Optic Cabling system Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3940	Prepare & Submit Fiber Optic Cabling system Product Data	81	15-Oct-24	11-Feb-25
SUB-3950	Prepare & Submit Fiber Optic Cabling system Samples	81	15-Oct-24	11-Feb-25
SUB-3960	Prepare & Submit Sound, Intercome & Security System Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3970	Prepare & Submit Sound, Intercome & Security System Programming Code and Password for the System	81	15-Oct-24	11-Feb-25
SUB-3980	Prepare & Submit Sound, Intercome & Security System Warranty	81	15-Oct-24	11-Feb-25
SUB-3990	Prepare & Submit Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	81	15-Oct-24	11-Feb-25
SUB-4000	Prepare & Submit Projection and Interactive Whiteboard Systems Wiring diagram	81	15-Oct-24	11-Feb-25
SUB-4010	Prepare & Submit Self Corrective Clock System Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-4020	Prepare & Submit Self Corrective Clock System Product Data	81	15-Oct-24	11-Feb-25
SUB-4030	Prepare & Submit Self Corrective Clock System Field Test Reports	81	15-Oct-24	11-Feb-25
SUB-4040	Prepare & Submit Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	81	15-Oct-24	11-Feb-25
APP-1010	Review & Approve Foundation Product Data	21	22-Oct-24	11-Nov-24
APP-1020	Review & Approve Erosion Control and Sedimentation Plan	21	24-Oct-24	13-Nov-24
APP-1030	Review & Approve Existing Conditions Survey	21	29-Oct-24	18-Nov-24
APP-1050	Review & Approve Site Furnishings Shop Drawings	21	05-Nov-24	25-Nov-24
APP-1150	Review & Approve Ductile Iron Pipes	21	07-Dec-24	27-Dec-24
APP-1200	Review & Approve SSDS Geotextile	21	12-Dec-24	01-Jan-25
APP-3760	Review & Approve Lighting Control Devices Shop Drawing	21	29-Jan-25	18-Feb-25
APP-3770	Review & Approve Lighting Control Devices Product Data	21	29-Jan-25	18-Feb-25
APP-3780	Review & Approve Lighting Control Devices Warranty	21	29-Jan-25	18-Feb-25
APP-1520	Review & Approve Planting Schedule	21	12-Feb-25	04-Mar-25
APP-1530	Review & Approve Playgroung Equipment Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1540	Review & Approve Catch Basin Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1550	Review & Approve Concrete Curbs & Pavements Shop Drawing	21	12-Feb-25	04-Mar-25
APP-1560	Review & Approve Steel Curb Facing Shop Drawing	21	12-Feb-25	04-Mar-25
APP-1570	Review & Approve Asphaltic Concrete Paving	21	12-Feb-25	04-Mar-25
APP-1580	Review & Approve Gas Vapor Barrier Submittal & Inspection Schedule	21	12-Feb-25	04-Mar-25
APP-1870	Review & Approve Environmental Site Assessment Reports	21	12-Feb-25	04-Mar-25
APP-1880	Review & Approve Selective Removals & Demoloition	21	12-Feb-25	04-Mar-25
APP-1890	Review & Approve Trench Drains Prodcut Data	21	12-Feb-25	04-Mar-25
APP-1900	Review & Approve Chain Link Fences & Gates Drawings	21	12-Feb-25	04-Mar-25
APP-1910	Review & Approve Outdoor Game Equipment	21	12-Feb-25	04-Mar-25
APP-2360	Review & Approve Adjacent Property and Structures Protection & Monitoring Plan	21	12-Feb-25	04-Mar-25
APP-2920	Review & Approve Documentation of Proper Disposal	21	12-Feb-25	04-Mar-25
APP-3230	Review & Approve Shop Equipment Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3240	Review & Approve Shop Equipment Product Data	21	12-Feb-25	04-Mar-25
APP-3790	Review & Approve Surge Protective Devices Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3800	Review & Approve Surge Protective Devices Product Data	21	12-Feb-25	04-Mar-25
APP-3810	Review & Approve Surge Protective Devices Warranty	21	12-Feb-25	04-Mar-25
APP-3820	Review & Approve Service Entrance Equipment Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3830	Review & Approve Service Entrance Equipment Product Data	21	12-Feb-25	04-Mar-25
APP-3840	Review & Approve Service Entrance Equipment Warranty	21	12-Feb-25	04-Mar-25

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
APP-3850	Review & Approve Enclosed Switches Product Data	21	12-Feb-25	04-Mar-25
APP-3860	Review & Approve Enclosed Switches Test Reports	21	12-Feb-25	04-Mar-25
APP-3870	Review & Approve Motors, Motor Control Centers and Starters Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3880	Review & Approve Motors, Motor Control Centers and Starters Product Data	21	12-Feb-25	04-Mar-25
APP-3890	Review & Approve Motors, Motor Control Centers and Starters Field Test Reports	21	12-Feb-25	04-Mar-25
APP-3900	Review & Approve Lightning Protection Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3920	Review & Approve Lightning Protection Test Reports	21	12-Feb-25	04-Mar-25
APP-3930	Review & Approve Fiber Optic Cabling system Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3940	Review & Approve Fiber Optic Cabling system Product Data	21	12-Feb-25	04-Mar-25
APP-3950	Review & Approve Fiber Optic Cabling system Samples	21	12-Feb-25	04-Mar-25
APP-3960	Review & Approve Sound, Intercome & Security System Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3970	Review & Approve Sound, Intercome & Security System Programming Code and Password for the System	21	12-Feb-25	04-Mar-25
APP-3980	Review & Approve Sound, Intercome & Security System warranty	21	12-Feb-25	04-Mar-25
APP-3990	Review & Approve Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	21	12-Feb-25	04-Mar-25
APP-4000	Review & Approve Projection and Interactive Whiteboard Systems Wiring diagram	21	12-Feb-25	04-Mar-25
APP-4010	Review & Approve Self Corrective Clock System Shop Drawing	21	12-Feb-25	04-Mar-25
APP-4020	Review & Approve Self Corrective Clock System Product Data	21	12-Feb-25	04-Mar-25
APP-4030	Review & Approve Self Corrective Clock System Field Test Reports	21	12-Feb-25	04-Mar-25
APP-4040	Review & Approve Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	21	12-Feb-25	04-Mar-25
SUB-2900	Prepare & Submit Excavated Material Disposal Plan	71	26-May-25	05-Sep-25
SUB-4050	Prepare & Submit Soil Sampling Plan	71	26-May-25	05-Sep-25
PRO-1120	Procure & Deliver Erosion Control and Sedimentation Devices	25	05-Sep-25	29-Sep-25
APP-2900	Review & Approve Excavated Material Disposal Plan	21	06-Sep-25	26-Sep-25
APP-4050	Review & Approve Soil Sampling Plan	21	06-Sep-25	26-Sep-25
SUB-2910	Prepare & Submit Backfill & Resue Plan	20	08-Sep-25	03-Oct-25
CON-1000	Mobilization	4	30-Sep-25	03-Oct-25
MIL-1060	Mobilization Start	0	30-Sep-25	
CON-7740	Protection Of All Overhead & Underground Utilities	263	30-Sep-25	19-Oct-26
CON-9000	Protection & Restoration the adjacent Properties to Original Condition	263	30-Sep-25	19-Oct-26
MIL-1710	Complete Mobilization	0		03-Oct-25
APP-2910	Review & Approve Backfill & Resue Plan	21	04-Oct-25	24-Oct-25
CON-1080	Install Erosion Control Devices	2	06-Oct-25	07-Oct-25
CON-1010	Install Construction Signs	2	06-Oct-25	07-Oct-25
CON-1030	Install Construction Fences	2	06-Oct-25	07-Oct-25
CON-9120	Soli Sampling	2	06-Oct-25	07-Oct-25
CON-7750	Install Field Offices	5	08-Oct-25	15-Oct-25
CON-9140	Excavation	5	08-Oct-25	15-Oct-25
CON-1060	Backfilling & Compaction -1st Floor	6	12-Nov-25	19-Nov-25
PRO-1450	Procure & Deliver Playground Equipment	60	09-Dec-25	06-Feb-26
MIL-1400	Start Site Work	0	29-Apr-26	
CON-3780	Install Traffic Control Devices - 54th Avenue Street	3	01-May-26	05-May-26
CON-3850	Remove Existing Steel Faced Curb - 54th Avenue Street	3	06-May-26	08-May-26
CON-3860	Remove Existing Asphalt - 54th Avenue Street	4	06-May-26	11-May-26
CON-3870	Install Traffic Control Devices - 2nd Street	5	06-May-26	12-May-26

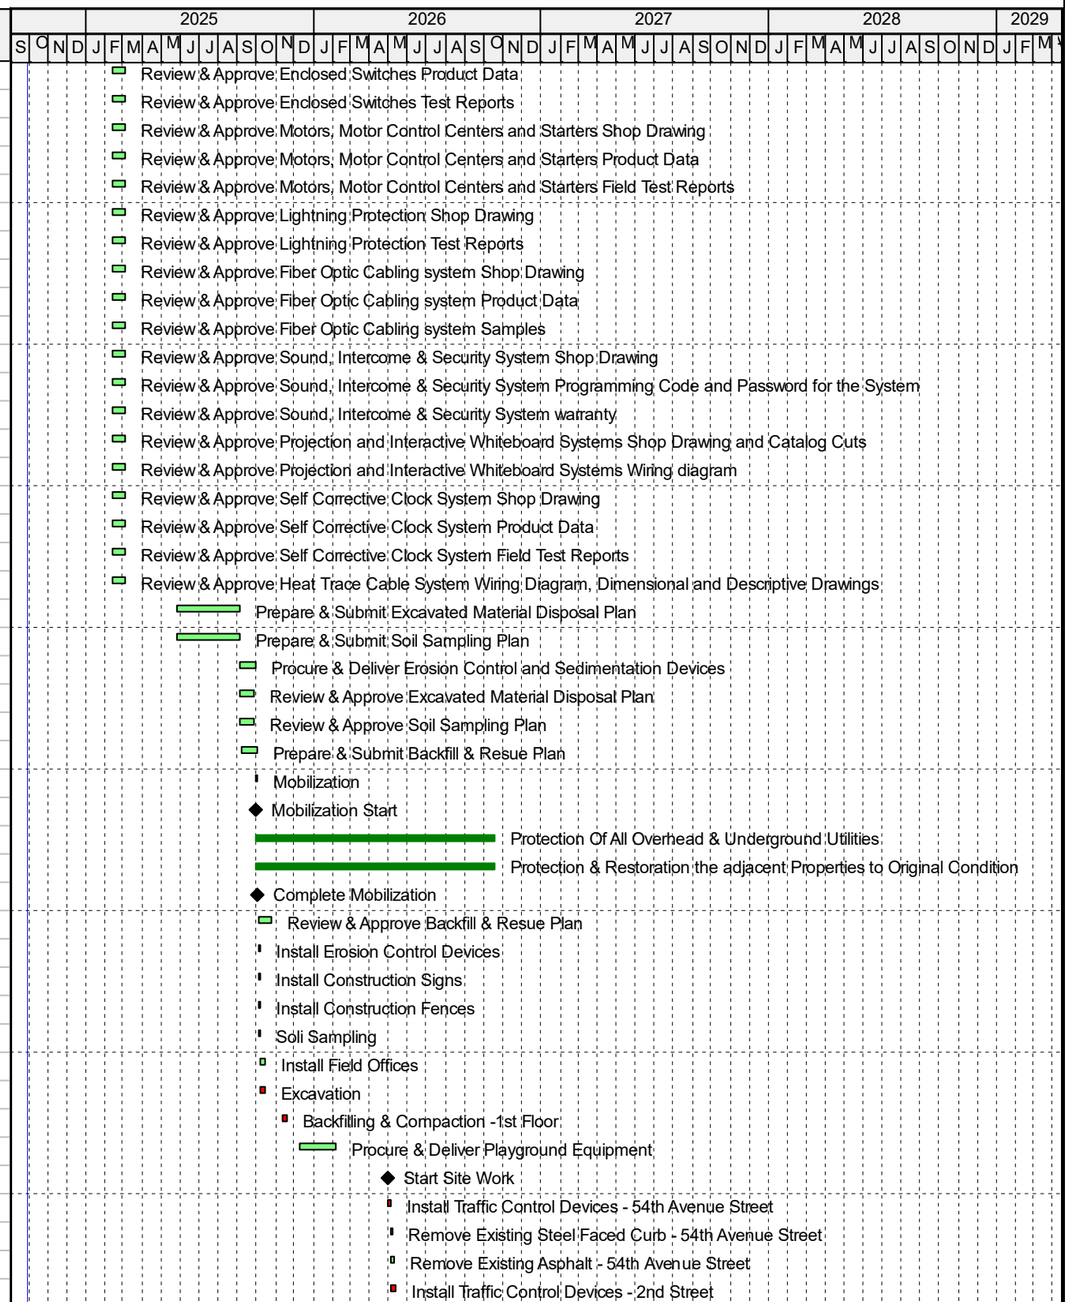

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

PROJECS
ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3940	Remove Existing Electrical Manhole - 54th Avenue Street	4	12-May-26	15-May-26
CON-3900	Remove Existing Sidewalk - 2nd Street	5	13-May-26	19-May-26
CON-4080	Install 5' Wide Silva Cells Under Concrete Pavement Strip - 54th Avenue Street	4	18-May-26	21-May-26
CON-3950	Install Pedestrian Ramps With Truncated Domes - 2nd Street	6	20-May-26	28-May-26
CON-4150	Pavement Replacement - 54th Avenue Street	4	22-May-26	28-May-26
CON-4290	Install New Steel Faced Curb - 54th Avenue Street	4	29-May-26	03-Jun-26
CON-4300	Install Pedestrian Ramps With Truncated Domes - 54th Avenue Street	4	29-May-26	03-Jun-26
CON-4090	Remove Existing Steel Faced Curb - 2nd Street	6	29-May-26	05-Jun-26
CON-4400	Install 4" Concrete Sidewalk - 54th Avenue Street	5	04-Jun-26	10-Jun-26
CON-4410	Install 7" Concrete Sidewalk - 54th Avenue Street	5	04-Jun-26	10-Jun-26
CON-4160	Install New Steel Faced Curb - 2nd Street	6	08-Jun-26	15-Jun-26
CON-4170	Install 4" Concrete Sidewalk - 2nd Street	7	08-Jun-26	16-Jun-26
CON-4560	Install Pavement Marking - 54th Avenue Street	3	11-Jun-26	15-Jun-26
CON-4580	Remove Traffic Control Devices - 54th Avenue Street	3	16-Jun-26	18-Jun-26
CON-4310	Install 7" Concrete Sidewalk - 2nd Street	6	16-Jun-26	24-Jun-26
CON-4420	Remove Traffic Control Devices - 2nd Street	5	25-Jun-26	01-Jul-26
CON-4660	Excavation - Drainage Work - Building Perimeter	3	02-Jul-26	07-Jul-26
CON-4740	Install Flood Barrier Wall - Drainage Work - Building Perimeter	3	08-Jul-26	10-Jul-26
CON-4860	Install Drilled Caisson Supported Ventilation Structure - Drainage Work - Building Perimeter	3	13-Jul-26	15-Jul-26
CON-4980	Install 4" & 6" & 10" & 12" DIP - Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-9170	Install 8" Combined Water Service (2nd Street)- Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-9180	Install 6" Fire Water Service (54th Avenue Street)- Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-5190	Install Catch Basin - Drainage Work - Building Perimeter	2	21-Jul-26	22-Jul-26
CON-5290	Install Storm Inlet With Hood & Storm Hood - Drainage Work - Building Perimeter	2	23-Jul-26	24-Jul-26
SUB-2330	Prepare & Submit Remedial Closure Report	3	27-Jul-26	29-Jul-26
CON-5400	Install Trench Drain - Drainage Work - Building Perimeter	1	27-Jul-26	27-Jul-26
CON-9160	Excavate for Footings - Playground Area & Fences - Building Perimeter	2	28-Jul-26	29-Jul-26
CON-9010	Remove Steel Plate Protection over NYPA Easement - Playground Area & Fences - Building Perimeter	1	28-Jul-26	28-Jul-26
APP-2330	Review & Approve Remedial Closure Report	21	30-Jul-26	19-Aug-26
CON-9190	F/R/P Playground Equipment Footings - Playground Area & Fences - Building Perimeter	2	30-Jul-26	31-Jul-26
CON-5470	Install Flush Concrete Curb - Playground Area & Fences - Building Perimeter	3	03-Aug-26	05-Aug-26
CON-5420	Install Asphalt Pavement - Playground Area & Fences - Building Perimeter	2	04-Aug-26	05-Aug-26
CON-5600	Install Concrete Pavement Pedestrian Ramp With Painted Black Handrails - Playground Area & Fences - Building Perimeter	3	06-Aug-26	10-Aug-26
CON-5650	Install Playground Rubber Tile Safety Surface - Playground Area & Fences - Building Perimeter	3	11-Aug-26	13-Aug-26
CON-5800	Install Painted Asphalt Pavement & Painted Games On Asphalt Surface - Playground Area & Fences - Building Perimeter	3	14-Aug-26	18-Aug-26
CON-5850	Install Colored Athletic Wearing Surface Color - Playground Area & Fences - Building Perimeter	2	19-Aug-26	20-Aug-26
CON-5990	Install Playground Equipment - Playground Area & Fences - Building Perimeter	7	21-Aug-26	31-Aug-26
CON-6140	Install Basketball Hoop - Playground Area & Fences - Building Perimeter	1	01-Sep-26	01-Sep-26
CON-6190	Install Wrought Iron Fence Double Gate - Playground Area - Building Perimeter	3	02-Sep-26	04-Sep-26
CON-6270	Install Chain Link Fence - Playground Area & Fences - Building Perimeter	3	08-Sep-26	10-Sep-26
MIL-1470	Finish Site Work	0		10-Sep-26
DIV03-Concrete		408	15-Oct-24	02-Jun-26
SUB-1170	Prepare & Submit Certification of Material	81	15-Oct-24	11-Feb-25
SUB-1180	Prepare & Submit Concrete Reinforcement	30	15-Oct-24	26-Nov-24

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1190	Prepare & Submit Formwork Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1450	Prepare & Submit Concrete Shop Drawings	30	15-Oct-24	26-Nov-24
SUB-1580	Prepare & Submit Concrete Mix Design	30	15-Oct-24	26-Nov-24
SUB-1920	Prepare & Submit Precast Architectural Concrete	71	15-Oct-24	28-Jan-25
APP-1100	Review & Approve Concrete Reinforcement	21	27-Nov-24	17-Dec-24
APP-1110	Review & Approve Concrete Shop Drawings	21	27-Nov-24	17-Dec-24
APP-1140	Review & Approve Concrete Mix Design	21	27-Nov-24	17-Dec-24
APP-1920	Review & Approve Precast Architectural Concrete	21	29-Jan-25	18-Feb-25
APP-1500	Review & Approve Certification of Material	21	12-Feb-25	04-Mar-25
APP-1510	Review & Approve Formwork Shop Drawings	21	12-Feb-25	04-Mar-25
CON-1040	F/R/P Concrete Walls & Beams -1st Floor	10	28-Oct-25	10-Nov-25
I-1010	Concrete Cast-IN-Place Inspection	86	28-Oct-25	04-Mar-26
CON-8050	Available Temporary Electrical Power For Testing MEP Equipment	0		31-Oct-25
CON-1070	F/R/P SOG -1st Floor	10	20-Nov-25	04-Dec-25
CON-1110	Install Metal Deck Slab -2nd Floor	4	22-Dec-25	26-Dec-25
MIL-1120	Metal Decking Start	0	22-Dec-25	
CON-1210	Install Metal Deck Slab - 3rd Floor	4	09-Jan-26	14-Jan-26
CON-1290	Install Metal Deck Slab - 4th Floor	4	29-Jan-26	03-Feb-26
CON-1380	Install Metal Deck Slab - 5th Floor	3	18-Feb-26	20-Feb-26
CON-1460	F/R/P Piers - 5th Floor	5	23-Feb-26	27-Feb-26
CON-1720	Install Metal Deck Slab -Roof Floor	2	03-Mar-26	04-Mar-26
CON-1830	Install Insulated Precast Concrete Sandwich Panel - Mock Up	2	05-Mar-26	06-Mar-26
CON-1990	Approve Insulated Precast Concrete Sandwich Panel - Mock Up	2	09-Mar-26	10-Mar-26
CON-1980	F/R/P Bulkhead Slab -Bulkhead	2	10-Mar-26	11-Mar-26
MIL-1170	Finish Concrete Work	0		11-Mar-26
CON-2380	Install Insulated Precast Concrete Sandwich Panel - West Elevation	3	25-Mar-26	27-Mar-26
CON-2420	Install Insulated Precast Concrete Sandwich Panel - South Elevation	5	25-Mar-26	31-Mar-26
I-1150	Concrete Precast Inspection	9	25-Mar-26	06-Apr-26
CON-2610	Install Insulated Precast Concrete Sandwich Panel - East Elevation	4	01-Apr-26	06-Apr-26
CON-2730	Install Insulated Precast Concrete Sandwich Panel - North Elevation	4	01-Apr-26	06-Apr-26
CON-2920	Pour Sloped Concrete Fill -5th Floor Roof	2	07-Apr-26	08-Apr-26
CON-3010	Pour Sloped Concrete Fill -Roof Floor	2	09-Apr-26	10-Apr-26
CON-4890	F/R/P Concrete Pads -Fuel Oil Room	2	01-Jun-26	02-Jun-26
DIV04-Masonry		374	15-Oct-24	14-Apr-26
SUB-1930	Prepare & Submit Unit Masonry Product Data	71	15-Oct-24	28-Jan-25
SUB-1940	Prepare & Submit Cast Stone Product Data	81	15-Oct-24	11-Feb-25
APP-1930	Review & Approve Unit Masonry Product Data	21	29-Jan-25	18-Feb-25
APP-1940	Review & Approve Cast Stone Product Data	21	12-Feb-25	04-Mar-25
MIL-1150	Masonry Walls Start	0	23-Feb-26	
CON-1430	Install Unit Masonry Mock-Up	1	23-Feb-26	23-Feb-26
CON-1470	Approve Unit Masonry Mock-Up	4	24-Feb-26	27-Feb-26
CON-1570	Install CMU Walls -2nd Floor	3	02-Mar-26	04-Mar-26
I-1020	Masonry Inspection	32	02-Mar-26	14-Apr-26
CON-1660	Install CMU Walls -3rd Floor	3	05-Mar-26	09-Mar-26

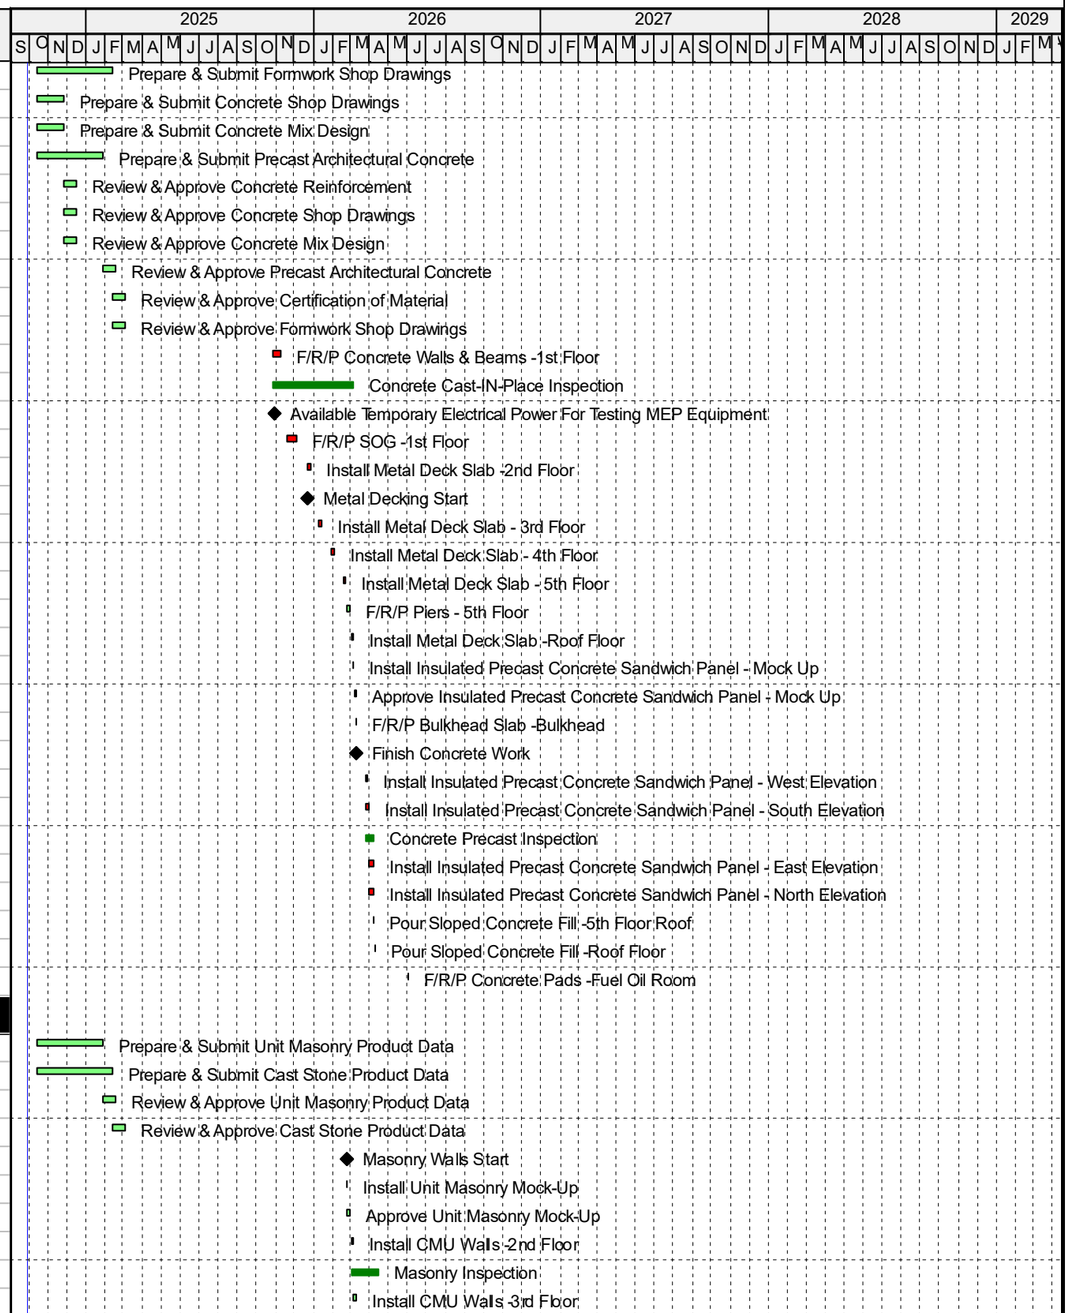

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
MIL-2932	Start Masonry Inspection	0	05-Mar-26	
CON-1920	Install CMU Walls -4th Floor	3	10-Mar-26	12-Mar-26
CON-2030	Install CMU Walls -5th Floor	3	13-Mar-26	17-Mar-26
CON-3090	Install CMU Walls -1st Floor	3	10-Apr-26	14-Apr-26
MIL-2942	Start In-Wall Inspection	0	10-Apr-26	
DIV05-Metals		380	15-Oct-24	22-Apr-26
SUB-1160	Prepare & Submit Suspension Assembly Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1950	Prepare & Submit Structure Steel Drawings	71	15-Oct-24	28-Jan-25
SUB-1960	Prepare & Submit Metal Deck Product Data	81	15-Oct-24	11-Feb-25
SUB-1970	Prepare & Submit Prefabricated Expansion Joint Covers	81	15-Oct-24	11-Feb-25
SUB-2370	Prepare & Submit Ornamenta Metal Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2930	Prepare & Submit Ornamenta Metal Product Data	81	15-Oct-24	11-Feb-25
SUB-4060	Prepare & Submit Steel Stairs Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-4070	Prepare & Submit Steel Stairs Product Data	81	15-Oct-24	11-Feb-25
APP-1950	Review & Approve Structure Steel Drawings	21	29-Jan-25	18-Feb-25
APP-1490	Review & Approve Suspension Assembly Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1960	Review & Approve Metal Deck Product Data	21	12-Feb-25	04-Mar-25
APP-1970	Review & Approve Prefabricated Expansion Joint Covers	21	12-Feb-25	04-Mar-25
APP-2370	Review & Approve Ornamenta Metal Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2930	Review & Approve Ornamenta Metal Product Data	21	12-Feb-25	04-Mar-25
APP-4060	Review & Approve Steel Stairs Shop Drawings	21	12-Feb-25	04-Mar-25
APP-4070	Review & Approve Steel Stairs Product Data	21	12-Feb-25	04-Mar-25
SUB-1700	Prepare & Submit Roof Dunnage	81	05-Mar-25	27-Jun-25
PRO-1590	Procure & Deliver Steel Columns	120	02-Jun-25	29-Sep-25
APP-1810	Review & Approve Roof Dunnage	21	28-Jun-25	18-Jul-25
PRO-1380	Procure & Deliver Roof Dunnage	100	30-Sep-25	07-Jan-26
PRO-1600	Procure & Deliver Trusses	60	30-Sep-25	28-Nov-25
PRO-2010	Procure & Deliver Steel Stairs Components	120	30-Sep-25	27-Jan-26
PRO-2020	Procure & Deliver Flagpole	60	30-Sep-25	28-Nov-25
CON-98787	Install Steel Columns -1st Floor	7	05-Dec-25	15-Dec-25
I-1140	Structural Steel Inspection	58	05-Dec-25	02-Mar-26
CON-1090	Install Trusses -1st Floor	3	16-Dec-25	18-Dec-25
CON-1100	Install Framing Beams -1st Floor	4	16-Dec-25	19-Dec-25
CON-1150	Install Steel Canopy Framing -2nd Floor	5	29-Dec-25	05-Jan-26
CON-1170	Install Steel Columns -2nd Floor	3	29-Dec-25	31-Dec-25
CON-1190	Install Trusses -2nd Floor	4	02-Jan-26	07-Jan-26
CON-1200	Install Framing Beams -2nd Floor	5	02-Jan-26	08-Jan-26
CON-1240	Install Steel Columns - 3rd Floor	4	15-Jan-26	21-Jan-26
CON-1260	Install Trusses - 3rd Floor	3	22-Jan-26	26-Jan-26
CON-1270	Install Framing Beams - 3rd Floor	5	22-Jan-26	28-Jan-26
CON-99277	Install Steel Stairs -1st Floor	7	28-Jan-26	05-Feb-26
CON-1330	Install Steel Columns - 4th Floor	4	04-Feb-26	09-Feb-26
CON-99287	Install Steel Stairs -2nd Floor	3	06-Feb-26	10-Feb-26
CON-1360	Install Trusses - 4th Floor	3	10-Feb-26	12-Feb-26

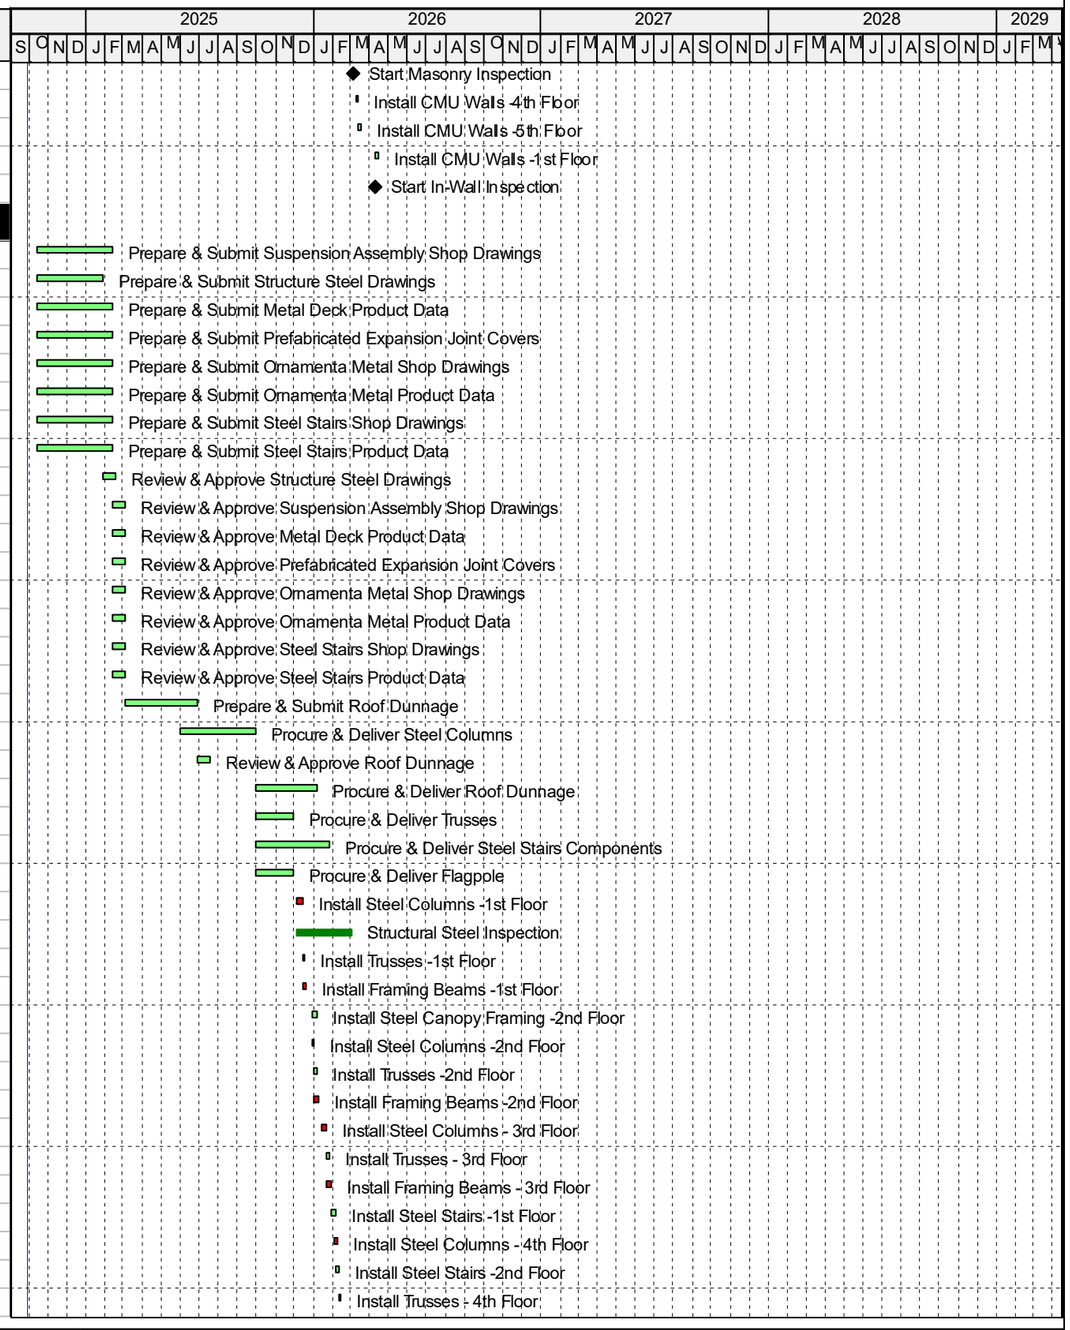

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1370	Install Framing Beams - 4th Floor	5	10-Feb-26	17-Feb-26
CON-99297	Install Steel Stairs- 3rd Floor	4	11-Feb-26	17-Feb-26
CON-1440	Install Steel Columns - 5th Floor	3	23-Feb-26	25-Feb-26
CON-99307	Install Steel Stairs - 4th Floor	4	23-Feb-26	26-Feb-26
CON-1540	Install Trusses - 5th Floor	2	26-Feb-26	27-Feb-26
CON-1550	Install Framing Beams - 5th Floor	3	26-Feb-26	02-Mar-26
CON-99317	Install Steel Stairs - 5th Floor	3	27-Feb-26	03-Mar-26
CON-1620	Install Dunnage - 5th Floor	8	02-Mar-26	11-Mar-26
CON-1640	Install Wall Steel Studs & Framing-2nd Floor	5	04-Mar-26	10-Mar-26
CON-1750	F/R/P Concrete Columns -Bulkhead	3	05-Mar-26	09-Mar-26
CON-1760	Install Dunnage-Roof Floor	8	05-Mar-26	16-Mar-26
CON-1900	Install Wall Steel Studs & Framing-3rd Floor	5	10-Mar-26	16-Mar-26
CON-2060	Install Hoist Beam-Bulkhead	1	12-Mar-26	12-Mar-26
CON-2010	Install Wall Steel Studs & Framing-4th Floor	5	16-Mar-26	20-Mar-26
CON-2310	Install Ceiling Hangers & Supports-2nd Floor	4	16-Mar-26	19-Mar-26
CON-2390	Install Ceiling Hangers & Supports-3rd Floor	4	20-Mar-26	25-Mar-26
CON-2200	Install Wall Steel Studs & Framing-5th Floor	5	23-Mar-26	27-Mar-26
CON-2550	Install Ceiling Hangers & Supports-4th Floor	4	26-Mar-26	31-Mar-26
CON-2620	Install Ceiling Hangers & Supports-5th Floor	4	01-Apr-26	06-Apr-26
CON-3520	Install Ceiling Hangers & Supports -1st Floor	4	15-Apr-26	20-Apr-26
CON-3240	Install Wall Steel Studs & Framing -1st Floor	5	16-Apr-26	22-Apr-26
DIV06-Wood & Plastics		328	15-Oct-24	06-Feb-26
SUB-1510	Prepare & Submit Millwork	81	15-Oct-24	11-Feb-25
SUB-1530	Prepare & Submit Furniture	81	15-Oct-24	11-Feb-25
APP-1710	Review & Approve Millwork	21	12-Feb-25	04-Mar-25
APP-1720	Review & Approve Furniture	21	12-Feb-25	04-Mar-25
PRO-1010	Procure & Deliver Furnitures	130	30-Sep-25	06-Feb-26
PRO-2050	Procure & Deliver Furnitures (Owner Responsibility)	130	30-Sep-25	06-Feb-26
DIV07-Thermal & Moisture Protection		430	15-Oct-24	06-Jul-26
SUB-1110	Prepare & Submit Roof Drains & Clean Outs	81	15-Oct-24	11-Feb-25
SUB-1120	Prepare & Submit Flashing & Sheet Metal Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-1130	Prepare & Submit Roofing Membrane Product Data	81	15-Oct-24	11-Feb-25
SUB-1140	Prepare & Submit Perimeter Foundation Insulation Product Data	81	15-Oct-24	11-Feb-25
SUB-1150	Prepare & Submit Crystalline Waterproofing Product Data	81	15-Oct-24	11-Feb-25
SUB-1980	Prepare & Submit Self Adhering Sheet Air Barriers	81	15-Oct-24	11-Feb-25
SUB-1990	Prepare & Submit Metal Plate Wall Panels	81	15-Oct-24	11-Feb-25
SUB-4080	Prepare & Submit Green School Submittal	81	15-Oct-24	11-Feb-25
APP-1440	Review & Approve Roof Drains & Clean Outs	21	12-Feb-25	04-Mar-25
APP-1450	Review & Approve Flashing & Sheet Metal Shop Drawing	21	12-Feb-25	04-Mar-25
APP-1460	Review & Approve Roofing Membrane Product Data	21	12-Feb-25	04-Mar-25
APP-1470	Review & Approve Perimeter Foundation Insulation Product Data	21	12-Feb-25	04-Mar-25
APP-1480	Review & Approve Crystalline Waterproofing Product Data	21	12-Feb-25	04-Mar-25
APP-1980	Review & Approve Self Adhering Sheet Air Barriers	21	12-Feb-25	04-Mar-25
APP-1990	Review & Approve Metal Plate Wall Panels	21	12-Feb-25	04-Mar-25

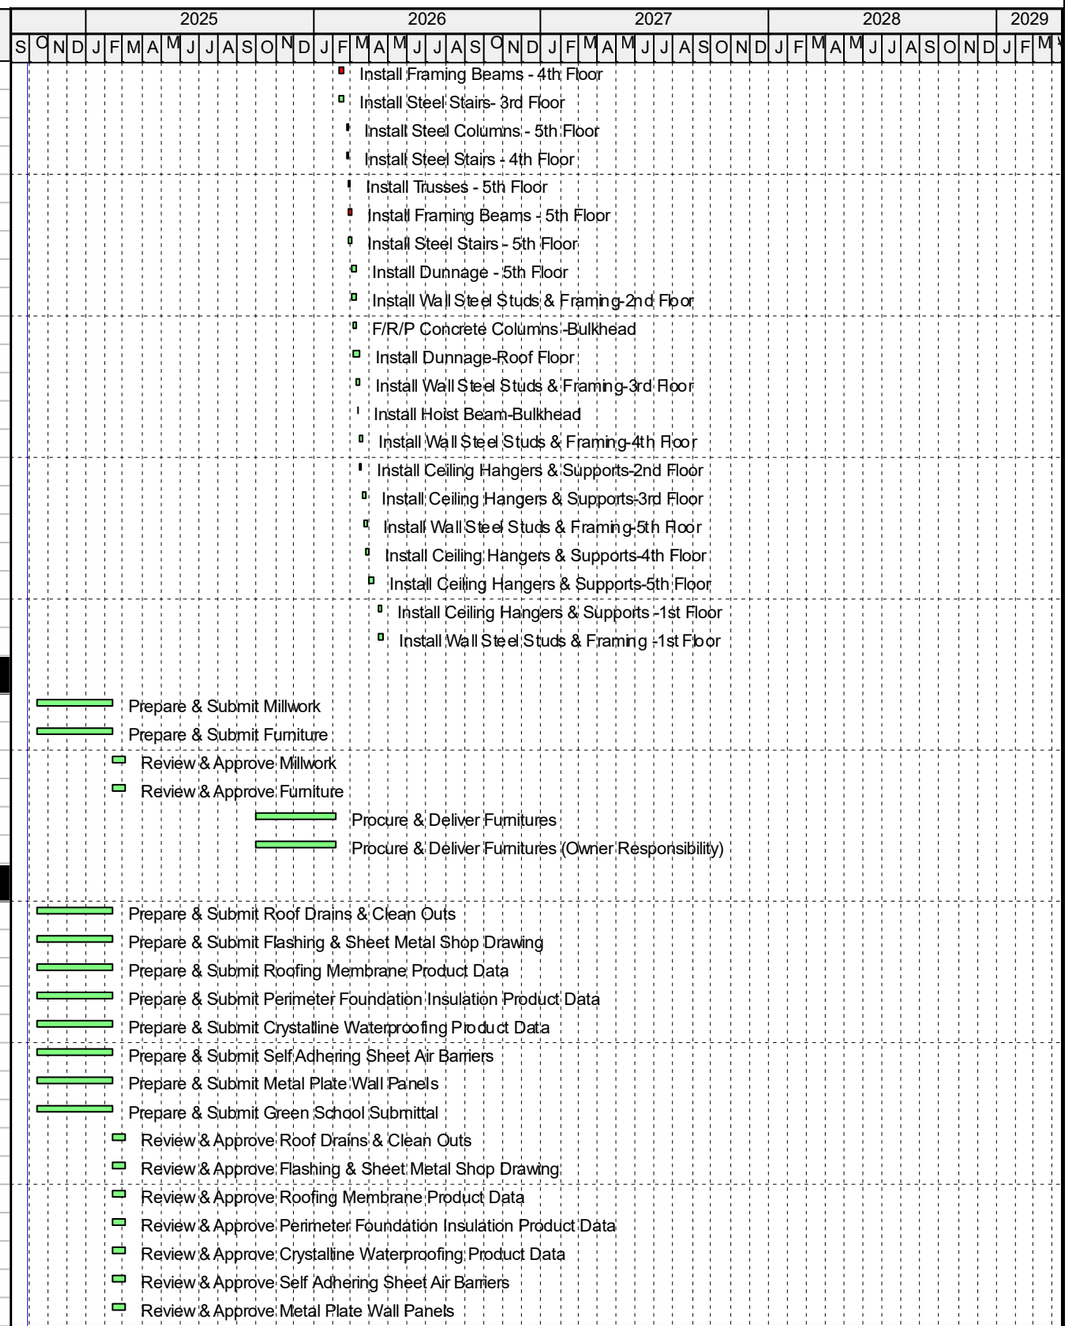

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
APP-4080	Review & Approve Green School Submittal	21	12-Feb-25	04-Mar-25
PRO-1530	Procure & Deliver Hydraulic Vertical Wheelchair Lift	90	30-Sep-25	28-Dec-25
PRO-1580	Procure & Deliver Metal Deck	70	30-Sep-25	08-Dec-25
PRO-1610	Procure & Deliver Prefabricated Expansion Joint Covers	60	30-Sep-25	28-Nov-25
PRO-1620	Procure & Deliver Security Screens & Barriers	60	30-Sep-25	28-Nov-25
PRO-1630	Procure & Deliver Wood Flooring	120	30-Sep-25	27-Jan-26
PRO-1640	Procure & Deliver Concrete Floating Floor Assembly	120	30-Sep-25	27-Jan-26
PRO-1660	Procure & Deliver Auditorium Television Studio Dimming System	90	30-Sep-25	28-Dec-25
CON-9898	Install Gas Permeable Aggregate -1st Floor	3	16-Oct-25	20-Oct-25
CON-98947	Install 4" slotted schedule 80 PVC Piping -1st Floor	3	16-Oct-25	20-Oct-25
CON-9888	Install Liquid Boot VI-20 Geomembrane -1st Floor	2	21-Oct-25	22-Oct-25
CON-1020	Install 60 Dry MILS Liquid Boot -1st Floor	3	23-Oct-25	27-Oct-25
CON-9777	Install Liquid Ultrashield G-1000 -1st Floor	2	24-Oct-25	27-Oct-25
CON-1180	Spray Fireproofing - 1st Floor	5	03-Mar-26	09-Mar-26
CON-1220	Spray Fireproofing - 2nd Floor	5	10-Mar-26	16-Mar-26
CON-1300	Spray Fireproofing - 3rd Floor	5	17-Mar-26	23-Mar-26
CON-1730	Spray Fireproofing - 5th Floor	3	31-Mar-26	02-Apr-26
MIL-1230	5th Floor Roofing Start	0	07-Apr-26	
MIL-1200	Main Roofing Start	0	09-Apr-26	
CON-3210	Install Fluid-Applied Protected Membrane Mock-Up	2	13-Apr-26	14-Apr-26
CON-3300	Approve Fluid-Applied Protected Membrane Mock-Up	4	15-Apr-26	20-Apr-26
CON-3430	Install Hot Fluid Applied Membrane -Roof Floor	3	21-Apr-26	23-Apr-26
CON-3440	Install Hot Fluid Applied Membrane -5th Floor Roof	4	21-Apr-26	24-Apr-26
CON-3600	Install Drainage Panels- Roof Floor	3	24-Apr-26	28-Apr-26
CON-3580	Install 6" Thick Rigid Insulation -5th Floor Roof	3	27-Apr-26	29-Apr-26
CON-3730	Install 6" Thick Rigid Insulation -Roof Floor	3	29-Apr-26	01-May-26
CON-3700	Install Drainage -5th Floor Roof	3	30-Apr-26	04-May-26
CON-3710	Roof Flood Test -5th Floor Roof	4	30-Apr-26	05-May-26
I-1040	Roofing Flood Testing Inspection	5	30-Apr-26	06-May-26
CON-3840	Roof Flood Test -Roof Floor	3	04-May-26	06-May-26
CON-3820	Install Filter Fabric -5th Floor Roof	3	06-May-26	08-May-26
CON-4020	Install Filter Fabric -Roof Floor	3	07-May-26	11-May-26
CON-3960	Install Concrete Pavers -5th Floor Roof	3	11-May-26	13-May-26
CON-4210	Install Concrete Pavers -Roof Floor	4	12-May-26	15-May-26
MIL-1310	5th Floor Roofing Finish	0		13-May-26
MIL-1280	Main Roofing Finish	0		15-May-26
CON-1120	Install Firestopping Mock-Up	2	01-Jun-26	02-Jun-26
CON-1140	Approve Firestopping Mock-Up	2	03-Jun-26	04-Jun-26
CON-4700	Install Firestopping-2nd Floor	3	05-Jun-26	09-Jun-26
MIL-1750	Start Firestopping	0	05-Jun-26	
CON-4850	Install Firestopping-3rd Floor	4	10-Jun-26	15-Jun-26
CON-5010	Install Firestopping-4th Floor	4	16-Jun-26	22-Jun-26
CON-5220	Install Firestopping-5th Floor	4	23-Jun-26	26-Jun-26
CON-5390	Install Firestopping-1st Floor	4	30-Jun-26	06-Jul-26

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

PROJECS
ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
DIV08-Doors & Windows		450	15-Oct-24	03-Aug-26
SUB-1080	Prepare & Submit Door Hardware Submittal	81	15-Oct-24	11-Feb-25
SUB-1100	Prepare & Submit Door & Frame Corners Samples	81	15-Oct-24	11-Feb-25
SUB-1620	Prepare & Submit Wood Doors	81	15-Oct-24	11-Feb-25
SUB-1670	Prepare & Submit Aluminum Projected Windows	71	15-Oct-24	28-Jan-25
SUB-2000	Prepare & Submit Security Screens & Barriers	81	15-Oct-24	11-Feb-25
SUB-2960	Prepare & Submit Coiling Doors, Grilles and Shutters Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2970	Prepare & Submit Coiling Doors, Grilles and Shutters Product Data	81	15-Oct-24	11-Feb-25
SUB-2980	Prepare & Submit Aluminum Framed Entrances & Storefronts Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2990	Prepare & Submit Aluminum Framed Entrances & Storefronts Product Data	81	15-Oct-24	11-Feb-25
SUB-3000	Prepare & Submit Thresholds, Weatherstripping and Seals Color Samples	81	15-Oct-24	11-Feb-25
SUB-3010	Prepare & Submit Thresholds, Weatherstripping and Seals Product Data	81	15-Oct-24	11-Feb-25
SUB-3020	Prepare & Submit Miscellaneous Glazing Samples	81	15-Oct-24	11-Feb-25
SUB-3030	Prepare & Submit Miscellaneous Glazing Product Data	81	15-Oct-24	11-Feb-25
SUB-3040	Prepare & Submit Fire Rated Glazing Samples	81	15-Oct-24	11-Feb-25
SUB-3050	Prepare & Submit Fire Rated Glazing Product Data	81	15-Oct-24	11-Feb-25
APP-1310	Review & Approve Aluminum Projected Windows	21	29-Jan-25	18-Feb-25
APP-1410	Review & Approve Door Hardware Submittal	21	12-Feb-25	04-Mar-25
APP-1430	Review & Approve Door & Frame Corners Samples	21	12-Feb-25	04-Mar-25
APP-1750	Review & Approve Wood Doors	21	12-Feb-25	04-Mar-25
APP-2000	Review & Approve Security Screens & Barriers	21	12-Feb-25	04-Mar-25
APP-2960	Review & Approve Coiling Doors, Grilles and Shutters Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2970	Review & Approve Coiling Doors, Grilles and ShuttersProduct Data	21	12-Feb-25	04-Mar-25
APP-2980	Review & Approve Aluminum Framed Entrances & Storefronts Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2990	Review & Approve Aluminum Framed Entrances & Storefronts Product Data	21	12-Feb-25	04-Mar-25
APP-3000	Review & Approve Thresholds, Weatherstripping and Seals Color Samples	21	12-Feb-25	04-Mar-25
APP-3010	Review & Approve Thresholds, Weatherstripping and Seals Product Data	21	12-Feb-25	04-Mar-25
APP-3020	Review & Approve Miscellaneous Glazing Samples	21	12-Feb-25	04-Mar-25
APP-3030	Review & Approve Miscellaneous Glazing Product Data	21	12-Feb-25	04-Mar-25
APP-3040	Review & Approve Fire Rated Glazing Samples	21	12-Feb-25	04-Mar-25
APP-3050	Review & Approve Fire Rated Glazing Product Data	21	12-Feb-25	04-Mar-25
PRO-1410	Procure & Deliver Door Frames	70	30-Sep-25	08-Dec-25
PRO-1070	Procure & Deliver Wood Doors	50	30-Sep-25	18-Nov-25
PRO-1220	Procure & Deliver Windows & Storefronts	154	30-Sep-25	02-Mar-26
CON-2110	Install & Windows Mock-Up	3	11-Mar-26	13-Mar-26
CON-2210	Approve Windows Mock-Up	2	16-Mar-26	17-Mar-26
CON-2220	Install Storefront System Mock-Up	3	18-Mar-26	20-Mar-26
CON-2240	Approve Storefront System Mock-Up	2	23-Mar-26	24-Mar-26
CON-2400	Install Windows -West Elevation	5	30-Mar-26	03-Apr-26
CON-2410	Install Storefront System-West Elevation	5	30-Mar-26	03-Apr-26
MIL-1740	Start Windows	0	30-Mar-26	
CON-2590	Install Windows - South Elevation	10	01-Apr-26	14-Apr-26
CON-2600	Install Storefront System- South Elevation	10	01-Apr-26	14-Apr-26
CON-2570	Field Testing of Windows (5%)	5	06-Apr-26	10-Apr-26

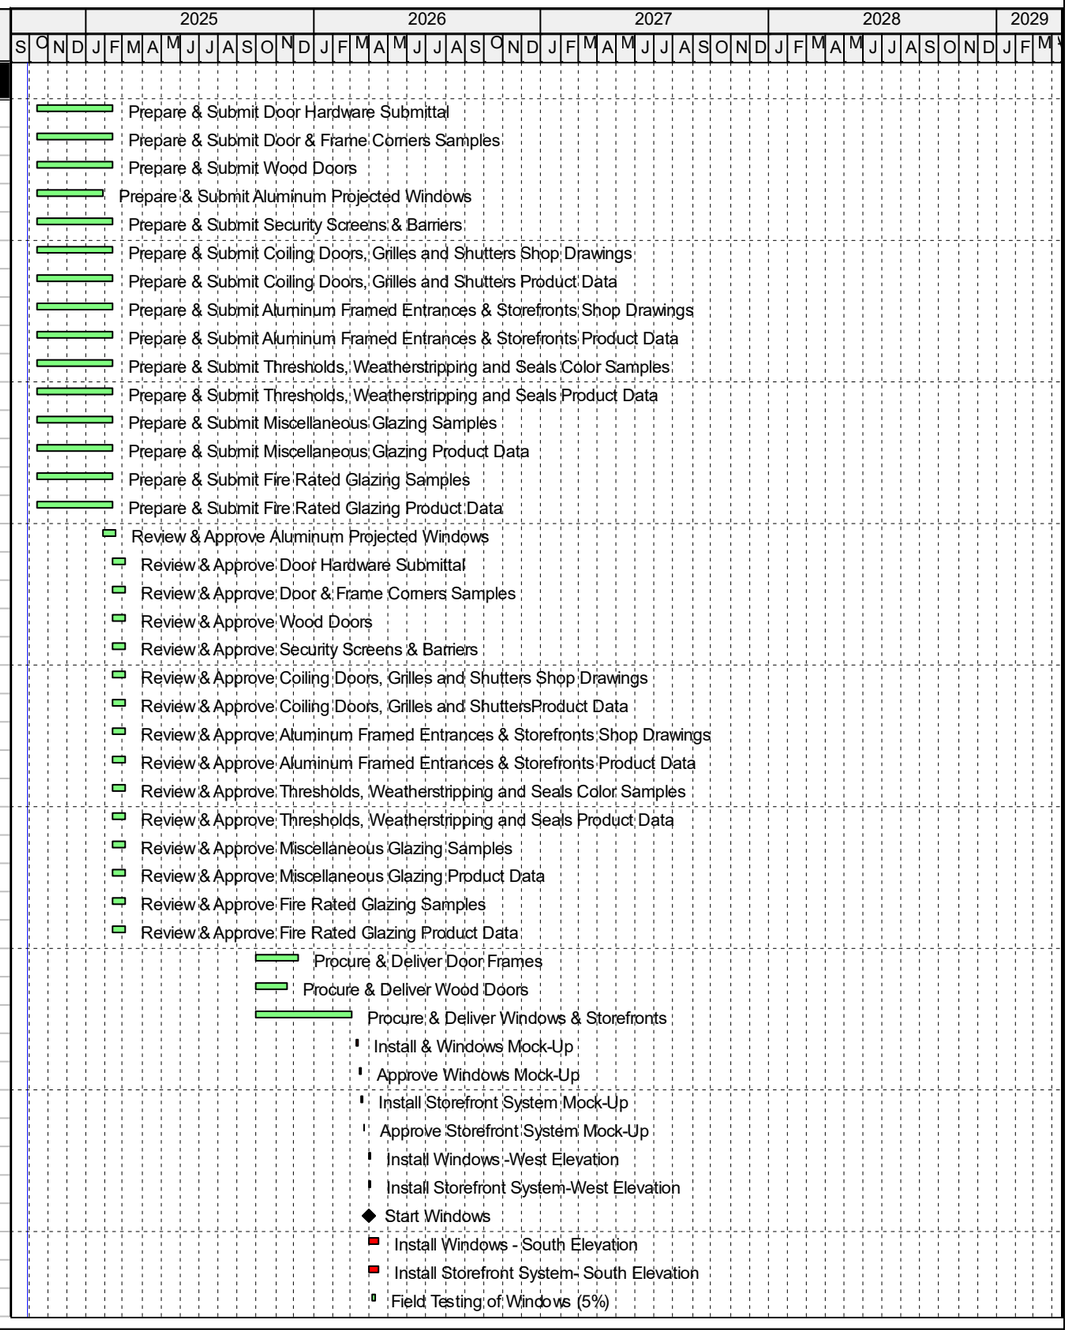

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2970	Field Testing of Windows (50%)	5	15-Apr-26	21-Apr-26
CON-2980	Install Windows - East Elevation	8	15-Apr-26	24-Apr-26
CON-2990	Install Storefront System- East Elevation	8	15-Apr-26	24-Apr-26
CON-3380	Install Windows -North Elevation	10	15-Apr-26	28-Apr-26
CON-3390	Install Storefront System-North Elevation	10	15-Apr-26	28-Apr-26
CON-3370	Field Testing of Windows (90%)	5	27-Apr-26	01-May-26
MIL-1580	Window Installation Finish	0		28-Apr-26
MIL-1340	BLDG Tight	0		06-May-26
CON-5120	Install Door Frames & Doors-2nd Floor	5	18-Jun-26	25-Jun-26
CON-5350	Install Door Frames & Doors-3rd Floor	5	29-Jun-26	06-Jul-26
CON-5540	Install Door Frames & Doors-4th Floor	5	07-Jul-26	13-Jul-26
CON-5680	Install Door Frames & Doors -5th Floor	5	16-Jul-26	22-Jul-26
CON-5920	Install Door Frames & Doors-1st Floor	5	23-Jul-26	29-Jul-26
CON-99267	Install Rolling Doors-1st Floor	3	30-Jul-26	03-Aug-26
DIV09-Finishes		478	15-Oct-24	11-Sep-26
SUB-1070	Prepare & Submit Ceramic Tiles Product Data	81	15-Oct-24	11-Feb-25
SUB-1090	Prepare & Submit Painting	81	15-Oct-24	11-Feb-25
SUB-1470	Prepare & Submit Gypsum Board	81	15-Oct-24	11-Feb-25
SUB-1480	Prepare & Submit Floorings	81	15-Oct-24	11-Feb-25
SUB-1490	Prepare & Submit Acosutical Ceiling Tiles	60	15-Oct-24	10-Jan-25
SUB-2010	Prepare & Submit Wood Flooring	81	15-Oct-24	11-Feb-25
SUB-3060	Prepare & Submit Graffiti Resistant Coating Product Data	81	15-Oct-24	11-Feb-25
SUB-3070	Prepare & Submit Special Coating Samples	81	15-Oct-24	11-Feb-25
SUB-3080	Prepare & Submit Special Coating Product Data	81	15-Oct-24	11-Feb-25
APP-1270	Review & Approve Acosutical Ceiling Tiles	21	11-Jan-25	31-Jan-25
APP-1400	Review & Approve Ceramic Tiles Product Data	21	12-Feb-25	04-Mar-25
APP-1420	Review & Approve Painting	21	12-Feb-25	04-Mar-25
APP-1680	Review & Approve Gypsum Board	21	12-Feb-25	04-Mar-25
APP-1690	Review & Approve Floorings	21	12-Feb-25	04-Mar-25
APP-2010	Review & Approve Wood Flooring	21	12-Feb-25	04-Mar-25
APP-3060	Review & Approve Graffiti Resistant Coating Product Data	21	12-Feb-25	04-Mar-25
APP-3070	Review & Approve Special Coating Samples	21	12-Feb-25	04-Mar-25
APP-3080	Review & Approve Special Coating Product Data	21	12-Feb-25	04-Mar-25
PRO-1420	Procure & Deliver Painting	70	30-Sep-25	08-Dec-25
PRO-1150	Procure & Deliver Gypsum Board	150	30-Sep-25	26-Feb-26
PRO-1160	Procure & Deliver Floorings	80	30-Sep-25	18-Dec-25
PRO-1170	Procure & Deliver Acosutical Ceiling Tiles	120	30-Sep-25	27-Jan-26
PRO-1360	Procure & Deliver Metal Panel Ceilings	120	30-Sep-25	27-Jan-26
CON-1420	Layout -2nd Floor	3	23-Feb-26	25-Feb-26
MIL-1140	Layout Start	0	23-Feb-26	
CON-1520	Install Top & Bottom Track-2nd Floor	4	26-Feb-26	03-Mar-26
CON-1530	Layout -3rd Floor	3	26-Feb-26	02-Mar-26
MIL-1160	Top & Bottom Track Start	0	26-Feb-26	
CON-1670	Layout -4th Floor	3	03-Mar-26	05-Mar-26

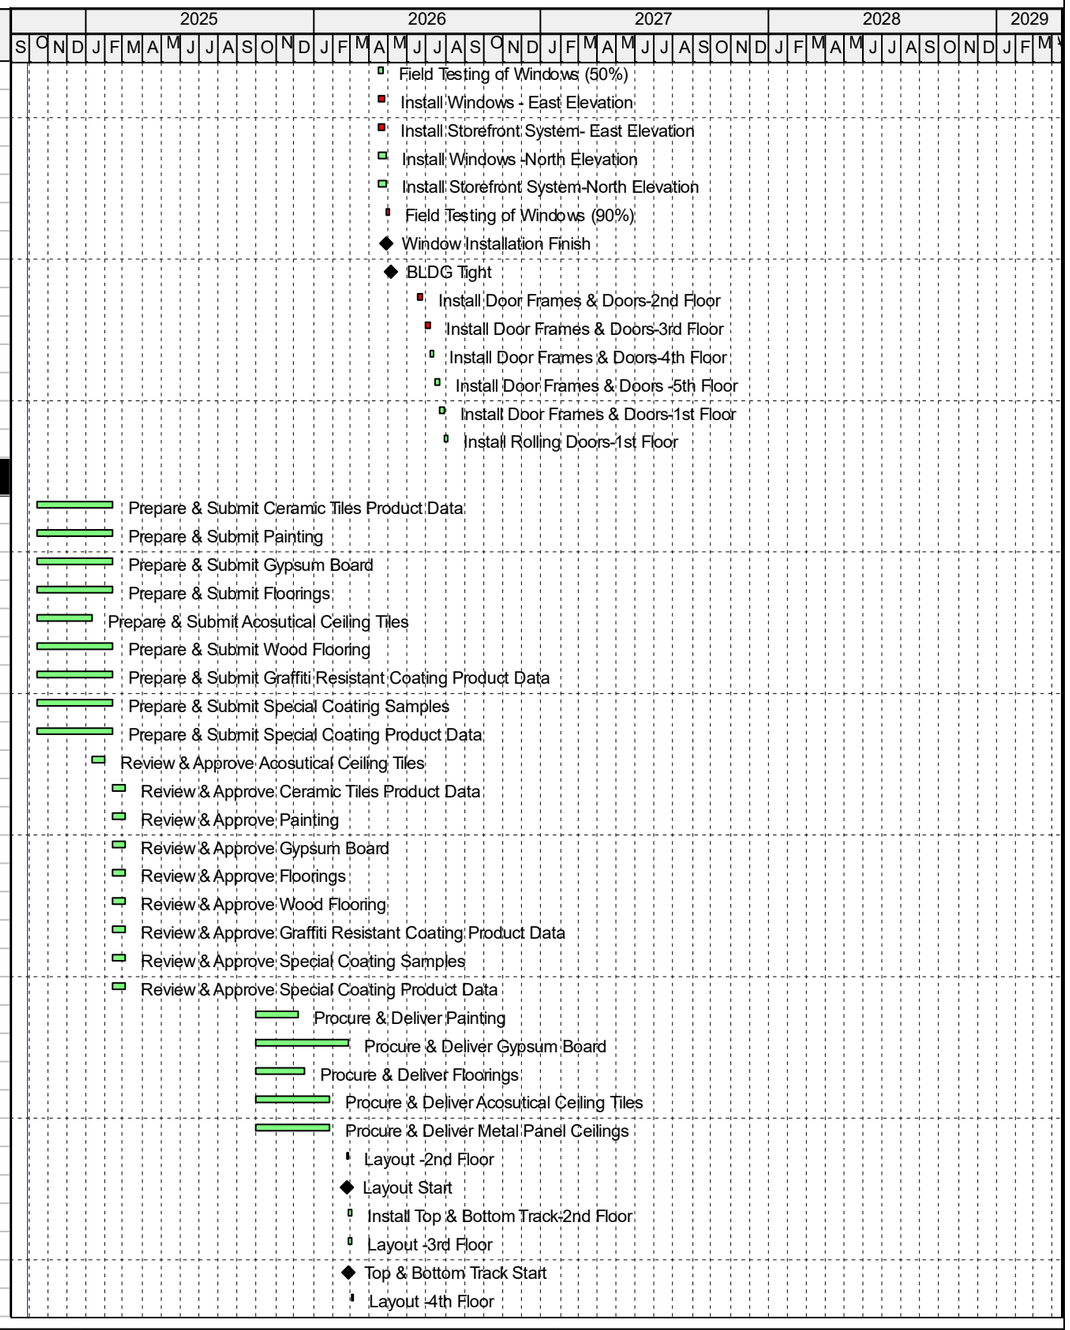

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1650	Install Top & Bottom Track-3rd Floor	4	04-Mar-26	09-Mar-26
CON-1930	Layout -5th Floor	3	06-Mar-26	10-Mar-26
CON-1910	Install Top & Bottom Track-4th Floor	4	10-Mar-26	13-Mar-26
CON-2020	Install Top & Bottom Track-5th Floor	4	16-Mar-26	19-Mar-26
CON-2910	Layout -1st Floor	3	07-Apr-26	09-Apr-26
MIL-1220	Layout Finish	0		09-Apr-26
CON-3080	Install Top & Bottom Track -1st Floor	4	10-Apr-26	15-Apr-26
MIL-1250	Top & Bottom Track Finish	0		15-Apr-26
CON-9070	In-Wall Inspection-2nd Floor	2	16-Apr-26	17-Apr-26
CON-9080	In-Wall Inspection -3rd Floor	2	22-Apr-26	23-Apr-26
CON-9090	In-Wall Inspection -4th Floor	7	28-Apr-26	06-May-26
CON-9100	In-Wall Inspections -5th Floor	7	04-May-26	12-May-26
CON-4040	Install Walls GWB-Mockup Room	3	07-May-26	11-May-26
CON-4270	Install Gypsum Board Ceiling -Mockup Room	3	07-May-26	11-May-26
MIL-1360	Start Mockup Room Work	0	07-May-26	
MIL-1430	Start Architecture Finishes	0	07-May-26	
CON-4380	Install Doors & Hardware-Mockup Room	3	11-May-26	13-May-26
CON-4260	Install Door Frames-Mockup Room	2	12-May-26	13-May-26
CON-4480	Paint First coat -Mockup Room	2	14-May-26	15-May-26
CON-4640	Flooring Finishes-Mockup Room	2	18-May-26	19-May-26
CON-9110	In-Wall Inspection -1st Floor	2	19-May-26	20-May-26
CON-4750	Paint Second coat-Mockup Room	2	20-May-26	21-May-26
CON-4930	Install Furniture & Signs -Mockup Room	2	22-May-26	26-May-26
MIL-1410	Mockup Room Ready For Inspection	0		26-May-26
MIL-1420	Finish Mockup Room	0		26-May-26
CON-4030	Install Gypsum Board Walls-2nd Floor	5	27-May-26	02-Jun-26
CON-5000	Mockup Room Inspection & Punchlist	5	27-May-26	02-Jun-26
MIL-1440	Start Gypsum Board	0	27-May-26	
CON-4200	Tape Gypsum Board -2nd Floor	4	28-May-26	02-Jun-26
CON-4350	Install Ceramic Wall Tiles at Corridor-2nd Floor	7	03-Jun-26	11-Jun-26
CON-4360	Install Gypsum Board Walls-3rd Floor	5	03-Jun-26	09-Jun-26
CON-4370	Install Gypsum Board Ceiling -2nd Floor	6	03-Jun-26	10-Jun-26
CON-4540	Tape Gypsum Board -3rd Floor	4	04-Jun-26	09-Jun-26
CON-4620	Install Gypsum Board Walls-4th Floor	5	10-Jun-26	16-Jun-26
MIL-1450	Start 1st Coat Painting	0	10-Jun-26	
CON-4630	Install Gypsum Board Ceiling-3rd Floor	6	11-Jun-26	18-Jun-26
CON-4830	Install First Coat Painting-2nd Floor	5	11-Jun-26	17-Jun-26
CON-4720	Tape Gypsum Board -4th Floor	4	11-Jun-26	16-Jun-26
CON-4610	Install Ceramic Wall Tiles at Corridor-3rd Floor	7	12-Jun-26	23-Jun-26
CON-4810	Install Gypsum Board Walls-5th Floor	5	17-Jun-26	24-Jun-26
CON-4970	Tape Gypsum Board -5th Floor	4	18-Jun-26	24-Jun-26
CON-98797	Install Intrusion System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-98847	Install Auxiliary System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-98897	Install Sound Clock System Components-2nd Floor	6	18-Jun-26	26-Jun-26

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-4820	Install Gypsum Board Ceiling-4th Floor	6	22-Jun-26	29-Jun-26
CON-5110	Install First Coat Painting-3rd Floor	5	22-Jun-26	26-Jun-26
CON-4800	Install Ceramic Wall Tiles at Corridor-4th Floor	7	24-Jun-26	02-Jul-26
CON-4450	Install Gypsum Board Walls-1st Floor	6	26-Jun-26	06-Jul-26
CON-5360	Install Flooring Tiles-2nd Floor	5	26-Jun-26	02-Jul-26
CON-5340	Install First Coat Painting-4th Floor	5	29-Jun-26	06-Jul-26
CON-98807	Install Intrusion System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-98857	Install Auxiliary System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-98907	Install Sound Clock System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-5100	Install Gypsum Board Ceiling-5th Floor	6	30-Jun-26	08-Jul-26
CON-4600	Tape Gypsum Board -1st Floor	4	30-Jun-26	06-Jul-26
CON-5080	Install Ceramic Wall Tiles at Corridor-5th Floor	7	06-Jul-26	14-Jul-26
CON-5560	Install Final Coat Painting-2nd Floor	6	06-Jul-26	13-Jul-26
CON-4680	Install Ceramic Wall Tiles at Corridor -1st Floor	7	07-Jul-26	15-Jul-26
CON-5550	Install Flooring Tiles-3rd Floor	5	07-Jul-26	13-Jul-26
CON-5480	Install Gypsum Board Ceiling -1st Floor	6	08-Jul-26	15-Jul-26
CON-98817	Install Intrusion System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-98867	Install Auxiliary System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-98917	Install Sound Clock System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-5530	Install First Coat Painting -5th Floor	5	09-Jul-26	15-Jul-26
CON-5090	Install Acoustical Ceiling Tiles-2nd Floor	5	14-Jul-26	20-Jul-26
CON-5690	Install Flooring Tiles-4th Floor	5	14-Jul-26	20-Jul-26
CON-5700	Install Final Coat Painting-3rd Floor	6	14-Jul-26	21-Jul-26
CON-5710	Install Furniture & Milling Work (Contractor Provided & Installed) -2nd Floor	5	14-Jul-26	20-Jul-26
CON-5760	Install Wood Floating Floor System -Gymnatorium	10	14-Jul-26	27-Jul-26
CON-9030	Install Furniture & Milling Work (Owner Provided & Installed) -2nd Floor	5	14-Jul-26	20-Jul-26
CON-99247	Install Laboratory Equipment -3rd Floor	4	14-Jul-26	17-Jul-26
CON-5720	Install First Coat Painting-1st Floor	5	16-Jul-26	22-Jul-26
CON-98827	Install Intrusion System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-98877	Install Auxiliary System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-98927	Install Sound Clock System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-5820	Install Signages-2nd Floor	5	21-Jul-26	27-Jul-26
CON-5330	Install Acoustical Ceiling Tiles-3rd Floor	5	22-Jul-26	28-Jul-26
CON-5900	Install Final Coat Painting-4th Floor	6	22-Jul-26	29-Jul-26
CON-5910	Install Furniture & Milling Work (Contractor Provided & Installed) -3rd Floor	5	22-Jul-26	28-Jul-26
CON-9040	Install Furniture & Milling Work (Owner Provided & Installed) -3rd Floor	5	22-Jul-26	28-Jul-26
CON-5870	Install Metal Panel Ceiling & Metal Geometric Ceiling -1st Floor	5	23-Jul-26	29-Jul-26
CON-5890	Install Flooring Tiles -5th Floor	5	23-Jul-26	29-Jul-26
CON-98937	Install Sound Clock System Components-1st Floor	3	24-Jul-26	28-Jul-26
CON-5810	Install Wall Pads - Gymnatorium	4	28-Jul-26	31-Jul-26
CON-6030	Install Signages-3rd Floor	5	29-Jul-26	04-Aug-26
CON-98887	Install Auxiliary System Components-1st Floor	4	29-Jul-26	03-Aug-26
CON-5520	Install Acoustical Ceiling Tiles-4th Floor	5	30-Jul-26	05-Aug-26
CON-6070	Install Furniture & Milling Work (Contractor Provided & Installed) -4th Floor	5	30-Jul-26	05-Aug-26

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-6080	Install Flooring Tiles-1st Floor	5	30-Jul-26	05-Aug-26
CON-9050	Install Furniture & Milling Work (Owner Provided & Installed) -4th Floor	5	30-Jul-26	05-Aug-26
CON-98837	Install Intrusion System Components-1st Floor	4	04-Aug-26	07-Aug-26
CON-5670	Install Acoustical Ceiling Tiles-5th Floor	5	06-Aug-26	12-Aug-26
CON-6160	Install Signages-4th Floor	5	06-Aug-26	12-Aug-26
CON-6060	Install Final Coat Painting -5th Floor	6	13-Aug-26	20-Aug-26
CON-6150	Install Furniture & Milling Work (Contractor Provided & Installed) -5th Floor	4	21-Aug-26	26-Aug-26
CON-6170	Install Final Coat Painting-1st Floor	6	21-Aug-26	28-Aug-26
CON-9060	Install Furniture & Milling Work (Owner Provided & Installed) -5th Floor	4	21-Aug-26	26-Aug-26
CON-6280	Install Signages- 5th Floor	5	27-Aug-26	02-Sep-26
CON-5880	Install Acoustical Ceiling Tiles -1st Floor	5	31-Aug-26	04-Sep-26
CON-6300	Install Furniture & Milling Work (Contractor Provided & Installed) -1st Floor	4	31-Aug-26	03-Sep-26
CON-6310	Install Security Screens & Barriers-1st Floor	3	31-Aug-26	02-Sep-26
CON-6320	Install Cafeteria Equipment-1st Floor	4	31-Aug-26	03-Sep-26
CON-9020	Install Furniture & Milling Work (Owner Provided & Installed) -1st Floor	3	31-Aug-26	02-Sep-26
CON-6370	Install Signages-1st Floor	4	04-Sep-26	10-Sep-26
CON-6380	Install Food Service Equipment-1st Floor	5	04-Sep-26	11-Sep-26
DIV10-Specialties		384	15-Oct-24	28-Apr-26
SUB-1060	Prepare & Submit Interior Signage Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1500	Prepare & Submit Toilet Accessories	81	15-Oct-24	11-Feb-25
SUB-2020	Prepare & Submit Visual Display Boards	81	15-Oct-24	11-Feb-25
SUB-2030	Prepare & Submit Metal Lockers	81	15-Oct-24	11-Feb-25
SUB-2040	Prepare & Submit Fire Extinguishers & Cabinets	81	15-Oct-24	11-Feb-25
SUB-2050	Prepare & Submit Stationary Metal Wall Louvers	73	15-Oct-24	30-Jan-25
SUB-3090	Prepare & Submit Flagpole Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3100	Prepare & Submit Flagpole Product Data	81	15-Oct-24	11-Feb-25
SUB-3110	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals	81	15-Oct-24	11-Feb-25
SUB-3120	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-3130	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	81	15-Oct-24	11-Feb-25
SUB-3140	Prepare & Submit Wire Mesh Work Samples	81	15-Oct-24	11-Feb-25
SUB-3150	Prepare & Submit Wire Mesh Work Shop drawings	81	15-Oct-24	11-Feb-25
SUB-3160	Prepare & Submit Metal Storage Shelving Samples	81	15-Oct-24	11-Feb-25
SUB-3170	Prepare & Submit Metal Storage Shelving Shop drawings	81	15-Oct-24	11-Feb-25
SUB-3180	Prepare & Submit Mirrors Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3190	Prepare & Submit Mirrors Product Data	81	15-Oct-24	11-Feb-25
SUB-3200	Prepare & Submit Mirrors Mastic Compatibility Test Reports & Certifications	81	15-Oct-24	11-Feb-25
SUB-3210	Prepare & Submit Grab Bars Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3220	Prepare & Submit Grab Bars Product Data	81	15-Oct-24	11-Feb-25
APP-1320	Review & Approve Stationary Metal Wall Louvers	21	31-Jan-25	20-Feb-25
APP-1390	Review & Approve Interior Signage Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1700	Review & Approve Toilet Accessories	21	12-Feb-25	04-Mar-25
APP-2020	Review & Approve Visual Display Boards	21	12-Feb-25	04-Mar-25
APP-2030	Review & Approve Metal Lockers	21	12-Feb-25	04-Mar-25
APP-2040	Review & Approve Fire Extinguishers & Cabinets	21	12-Feb-25	04-Mar-25

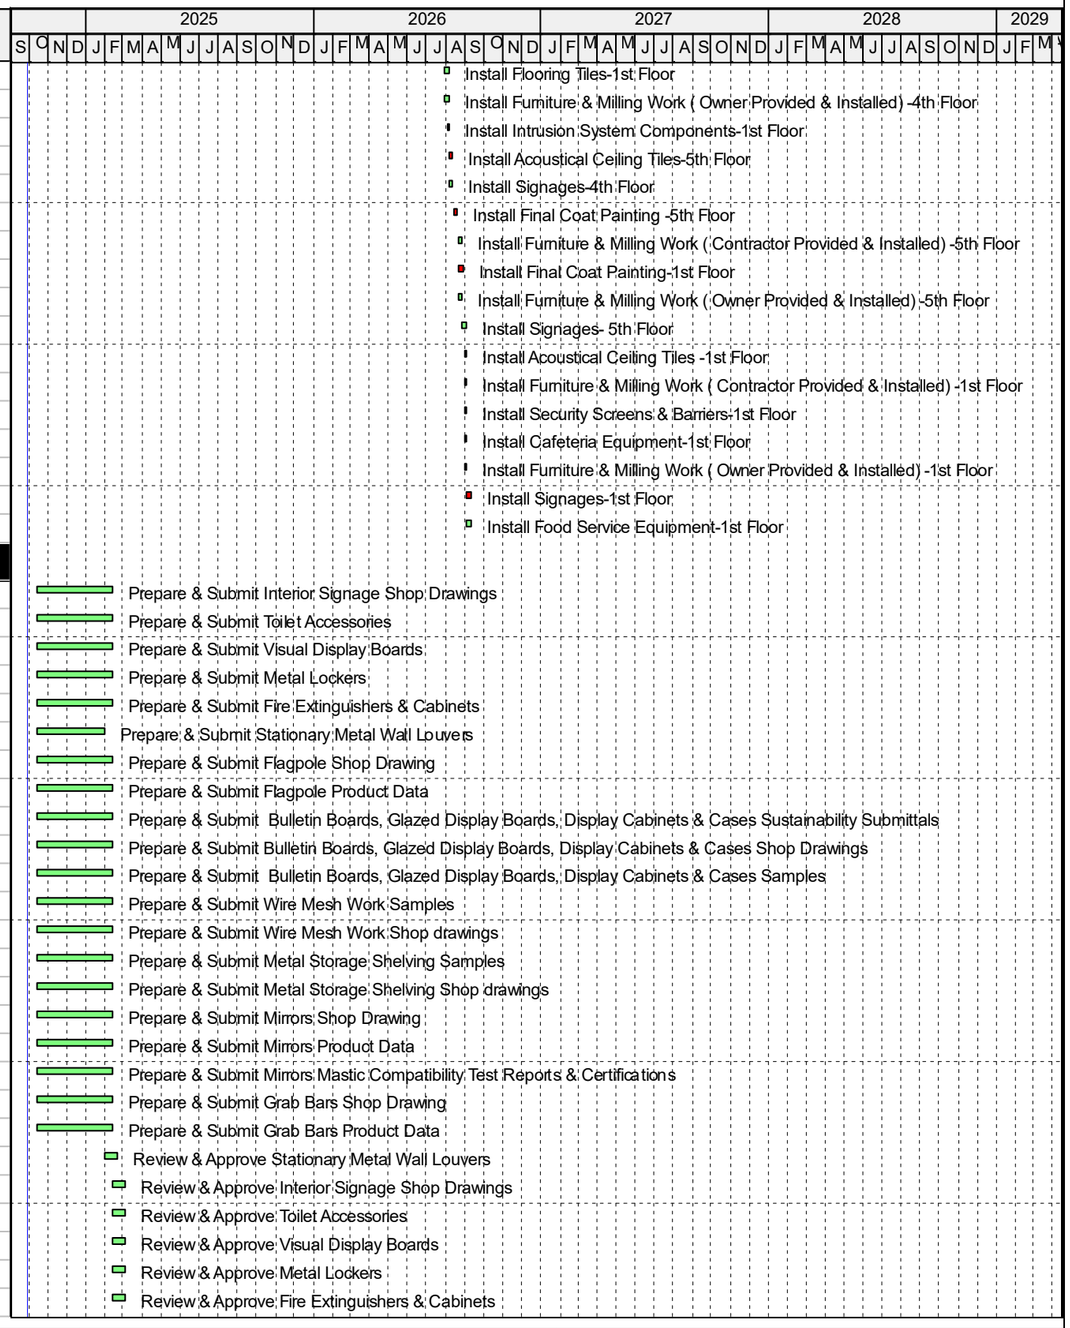

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
APP-3090	Review & Approve Flagpole Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3100	Review & Approve Flagpole Product Data	21	12-Feb-25	04-Mar-25
APP-3110	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals	21	12-Feb-25	04-Mar-25
APP-3120	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	21	12-Feb-25	04-Mar-25
APP-3130	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	21	12-Feb-25	04-Mar-25
APP-3140	Review & Approve Wire Mesh Work Samples	21	12-Feb-25	04-Mar-25
APP-3150	Review & Approve Miscellaneous Glazing Shop drawings	21	12-Feb-25	04-Mar-25
APP-3160	Review & Approve Metal Storage Shelving Samples	21	12-Feb-25	04-Mar-25
APP-3170	Review & Approve Metal Storage Shelving Shop drawings	21	12-Feb-25	04-Mar-25
APP-3180	Review & Approve Mirrors Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3190	Review & Approve Mirrors Product Data	21	12-Feb-25	04-Mar-25
APP-3200	Review & Approve Mirrors Mastic Compatibility Test Reports & Certifications	21	12-Feb-25	04-Mar-25
APP-3210	Review & Approve Grab Bars Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3220	Review & Approve Grab Bars Product Data	21	12-Feb-25	04-Mar-25
PRO-1190	Procure & Deliver Toilet Accessories	100	30-Sep-25	07-Jan-26
CON-99237	Install Flag Pole - South Elevation	10	15-Apr-26	28-Apr-26
DIV11-Equipment		475	15-Oct-24	08-Sep-26
SUB-1650	Prepare & Submit Kitchen Equipment	71	15-Oct-24	28-Jan-25
SUB-1770	Prepare & Submit Gymnasium Equipment	81	15-Oct-24	11-Feb-25
SUB-2060	Prepare & Submit Library Equipment	81	15-Oct-24	11-Feb-25
SUB-2070	Prepare & Submit Platform Curtains & Auditorium Window Curtains	81	15-Oct-24	11-Feb-25
SUB-2080	Prepare & Submit Waste Handling Equipment	81	15-Oct-24	11-Feb-25
SUB-2090	Prepare & Submit Domestic Equipment	81	15-Oct-24	11-Feb-25
SUB-2100	Prepare & Submit Laboratory Equipment	81	15-Oct-24	11-Feb-25
APP-1780	Review & Approve Kitchen Equipment	21	29-Jan-25	18-Feb-25
APP-1840	Review & Approve Gymnasium Equipment	21	12-Feb-25	04-Mar-25
APP-2050	Review & Approve Library Equipment	21	12-Feb-25	04-Mar-25
APP-2060	Review & Approve Platform Curtains & Auditorium Window Curtains	21	12-Feb-25	04-Mar-25
APP-2070	Review & Approve Waste Handling Equipment	21	12-Feb-25	04-Mar-25
APP-2080	Review & Approve Domestic Equipment	21	12-Feb-25	04-Mar-25
APP-2090	Review & Approve Laboratory Equipment	21	12-Feb-25	04-Mar-25
PRO-1000	Procure & Deliver Kitchen Equipment	180	30-Sep-25	28-Mar-26
PRO-1560	Procure & Deliver Gymnasium Equipment	180	30-Sep-25	28-Mar-26
CON-2190	Install Electric Unit Heater EUH - Mechanical Work - Roof Bulkhead	5	12-Mar-26	18-Mar-26
CON-2360	Install Smoke Purge Fan SPF - Mechanical Work - Roof Bulkhead	3	26-Mar-26	30-Mar-26
CON-2850	Install Electric Unit Heaters -2nd Floor	5	16-Apr-26	22-Apr-26
CON-3150	Install Convector Heater CV - Mechanical Work - 2nd Floor	5	23-Apr-26	29-Apr-26
CON-3450	Install Air Conditioning Unit AC - Mechanical Work - 2nd Floor	4	30-Apr-26	05-May-26
CON-5460	Install Convector Heater CV - Mechanical Work - 4th Floor	3	29-Jul-26	31-Jul-26
CON-5970	Install Retractable Basketball Goal Assembly -Gymnatorium	3	03-Aug-26	05-Aug-26
CON-5620	Install Air Conditioning Unit AC - Mechanical Work - 4th Floor	4	04-Aug-26	07-Aug-26
CLO-1230	Air Handling Unit Testing & Commissioning	21	04-Aug-26	01-Sep-26
CON-6020	Install 8" Acoustic Block Painted-Gymnatorium	7	06-Aug-26	14-Aug-26
CLO-1260	HVAC Split System Testing & Commissioning	21	10-Aug-26	08-Sep-26

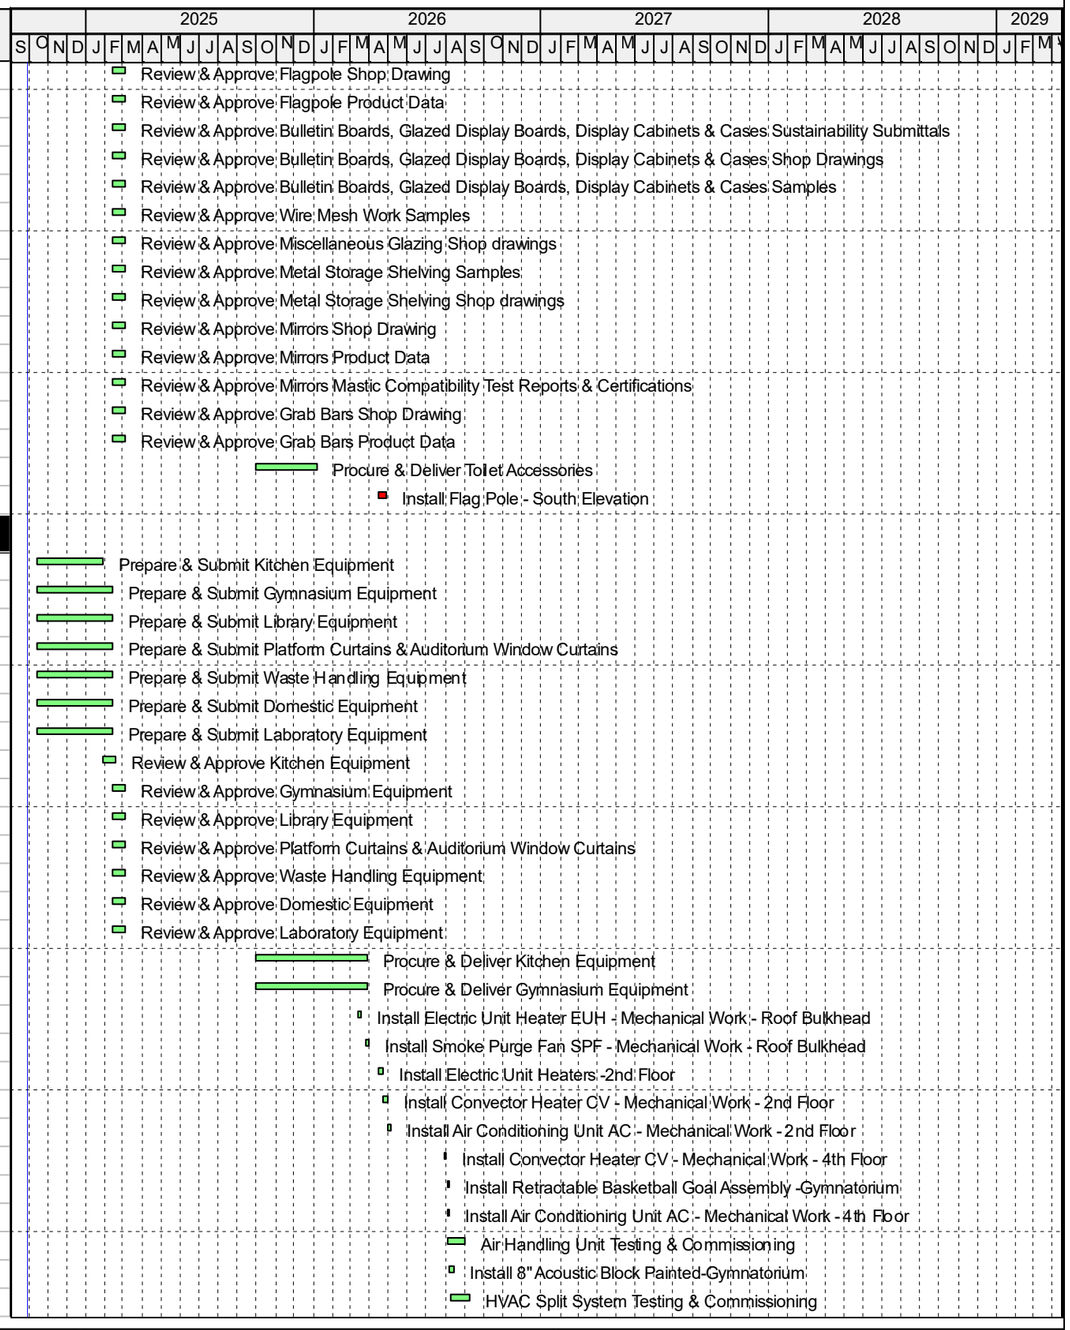

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-99217	Install Bleachers -Gymnatorium	3	12-Aug-26	14-Aug-26
CON-6230	Install Gym Equipment -Gymnatorium -Gymnatorium	6	17-Aug-26	24-Aug-26
CON-6240	Install Fine Tube Radiator FTR - Gymnatorium	5	17-Aug-26	21-Aug-26
CON-6250	Install Hydraulic Vertical Wheelchair Lift -Gymnatorium	8	17-Aug-26	26-Aug-26
CON-9150	Install LED Theatrical Lighting -Gymnatorium	4	25-Aug-26	28-Aug-26
CON-6390	Install Auditorium Television Studio Dimming System -Gymnatorium	7	27-Aug-26	04-Sep-26
DIV12-Furnishing		328	15-Oct-24	06-Feb-26
SUB-2110	Prepare & Submit Manufactured Wood Casework	81	15-Oct-24	11-Feb-25
SUB-3250	Prepare & Submit Bleachers Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3260	Prepare & Submit Bleachers Product Data	81	15-Oct-24	11-Feb-25
SUB-3270	Prepare & Submit Bleachers Manufacturer's Warranty	81	15-Oct-24	11-Feb-25
APP-2100	Review & Approve Manufactured Wood Casework	21	12-Feb-25	04-Mar-25
APP-3250	Review & Approve Bleachers Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3260	Review & Approve Bleachers Product Data	21	12-Feb-25	04-Mar-25
APP-3270	Review & Approve Bleachers Manufacturer's Warranty	21	12-Feb-25	04-Mar-25
PRO-2030	Procure & Deliver Bleachers	130	30-Sep-25	06-Feb-26
DIV13-Special Construction		95	15-Oct-24	04-Mar-25
SUB-2120	Prepare & Submit Concrete Floating Floor Assembly	81	15-Oct-24	11-Feb-25
APP-2110	Review & Approve Concrete Floating Floor Assembly	21	12-Feb-25	04-Mar-25
DIV14-Conveying Systems		482	15-Oct-24	17-Sep-26
SUB-1460	Prepare & Submit Elevator Machine	71	15-Oct-24	28-Jan-25
SUB-2130	Prepare & Submit Hydraulic Vertical Wheelchair Lifts	81	15-Oct-24	11-Feb-25
APP-1210	Review & Approve Elevator Machine	21	29-Jan-25	18-Feb-25
APP-2120	Review & Approve Hydraulic Vertical Wheelchair Lifts	21	12-Feb-25	04-Mar-25
PRO-1200	Procure & Deliver Elevator Machine	112	30-Sep-25	19-Jan-26
PRO-1570	Procure & Deliver Precast Sandwich Panels	112	30-Sep-25	19-Jan-26
CON-1160	Hoist Material Design	10	29-Dec-25	12-Jan-26
CON-8390	Install Sidewalk Sheds -South Elevation	4	29-Dec-25	02-Jan-26
CON-8400	Install Sidewalk Sheds -East Elevation	4	29-Dec-25	02-Jan-26
MIL-1720	Start Sidewalk Bridge Installations	0	29-Dec-25	
CON-1250	Approval of Hoist Design	7	13-Jan-26	19-Jan-26
CON-1280	Install Elevator Hoist Pad	5	20-Jan-26	26-Jan-26
CON-1320	Erect Material Hoist	5	27-Jan-26	02-Feb-26
CON-3220	Dismantle Sidewalk Sheds- South Elevation	2	29-Apr-26	30-Apr-26
CON-3630	Dismantle Sidewalk Sheds- East Elevation	2	04-May-26	05-May-26
MIL-1730	Sidewalk Sheds Dismantle Complete	0		05-May-26
MIL-1760	Start Elevator Work	0	07-May-26	
CON-99357	Install CMU Wall for Shaft -Elevator Machine Room	10	07-May-26	20-May-26
CON-99167	Install Elevator Guide Rails -Elevator Machine Room	8	21-May-26	02-Jun-26
CON-2090	Install Elevator Controller #1 -Elevator Machine Room	10	03-Jun-26	16-Jun-26
CON-2370	Install Elevator Controller #2 -Elevator Machine Room	10	17-Jun-26	01-Jul-26
CON-99157	Install Elevator Sump Pump -Elevator Machine Room	10	14-Jul-26	27-Jul-26
CON-3100	Install Elevator Cabinet (1) -Elevator Machine Room	10	22-Jul-26	04-Aug-26

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3620	Install Elevator Cabinet (2) -Elevator Machine Room	10	22-Jul-26	04-Aug-26
CON-5040	Dismantle Hoist	2	10-Sep-26	11-Sep-26
CON-5170	Demolish Hoist Pad	2	14-Sep-26	15-Sep-26
CON-5250	Hoist In-Fill	2	16-Sep-26	17-Sep-26
DIV 15A-Fire Protection		479	15-Oct-24	14-Sep-26
SUB-1050	Prepare & Submit Fire & Jockey Pumps	81	15-Oct-24	11-Feb-25
SUB-1440	Prepare & Submit Sprinkler System Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1630	Prepare & Submit Fire Protection Shop Drawings	81	15-Oct-24	11-Feb-25
APP-1380	Review & Approve Fire & Jockey Pumps	21	12-Feb-25	04-Mar-25
APP-1670	Review & Approve Sprinkler System Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1760	Review & Approve Fire Protection Shop Drawings	21	12-Feb-25	04-Mar-25
PRO-1090	Procure & Deliver Fire Sprinklers	100	30-Sep-25	07-Jan-26
PRO-1280	Procure & Deliver Fire Protection Pumps	70	30-Sep-25	08-Dec-25
CON-3270	Install Temporary Standpipe	9	29-Dec-25	09-Jan-26
I-1100	Fire-Resistant Penetrations And Joints Inspection	87	03-Mar-26	06-Jul-26
CON-1390	Spray Fireproofing - 4th Floor	5	24-Mar-26	30-Mar-26
CON-3310	Install 4" Standpipe -2nd Floor	4	04-May-26	07-May-26
MIL-1300	Start Sprinkler Rough-ins	0	04-May-26	
CON-3500	Rough-in Main Sprinkler Piping -2nd Floor	5	08-May-26	14-May-26
CON-3510	Install 4" Standpipe -3rd Floor	4	08-May-26	13-May-26
CON-3650	Install 4" Standpipe -4th Floor	4	14-May-26	19-May-26
CON-3670	Rough-in Branch Sprinkler Piping -2nd Floor	5	15-May-26	21-May-26
CON-3680	Rough-in Sprinkler Heads -2nd Floor	5	15-May-26	21-May-26
CON-3720	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -2nd Floor	5	15-May-26	21-May-26
CON-3690	Rough-in Main Sprinkler Piping-3rd Floor	5	15-May-26	21-May-26
CON-3770	Install 4" Standpipe -5th Floor	4	20-May-26	26-May-26
CON-3790	Rough-in Branch Sprinkler Piping -3rd Floor	5	22-May-26	29-May-26
CON-3800	Rough-in Sprinkler Heads -3rd Floor	5	22-May-26	29-May-26
CON-3880	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-3rd Floor	5	22-May-26	29-May-26
CON-3810	Rough-in Main Sprinkler Piping-4th Floor	5	22-May-26	29-May-26
CON-3830	Sprinklers Air Testing-2nd Floor	5	22-May-26	29-May-26
CON-3890	Install 4" Standpipe -Roof	4	27-May-26	01-Jun-26
I-1130	Fire Alarm Inspection	47	28-May-26	04-Aug-26
CON-3990	Rough-in Branch Sprinkler Piping -4th Floor	5	01-Jun-26	05-Jun-26
CON-4000	Rough-in Sprinkler Heads -4th Floor	5	01-Jun-26	05-Jun-26
CON-4100	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-4th Floor	5	01-Jun-26	05-Jun-26
CON-4010	Rough-in Main Sprinkler Piping -5th Floor	5	01-Jun-26	05-Jun-26
CON-4060	Sprinklers Air Testing-3rd Floor	5	01-Jun-26	05-Jun-26
I-1110	Fuel-Oil Storage & Fuel Oil Piping Systems Inspection	9	01-Jun-26	11-Jun-26
CON-4910	Install 4" Standpipe -1st Floor	4	02-Jun-26	05-Jun-26
MIL-2952	Finish Standpipe System Inspection	0		05-Jun-26
CON-5030	Rough-in Main Sprinkler Piping -1st Floor	5	08-Jun-26	12-Jun-26
CON-4230	Rough-in Branch Sprinkler Piping -5th Floor	5	08-Jun-26	12-Jun-26
CON-4240	Rough-in Sprinkler Heads -5th Floor	5	08-Jun-26	12-Jun-26

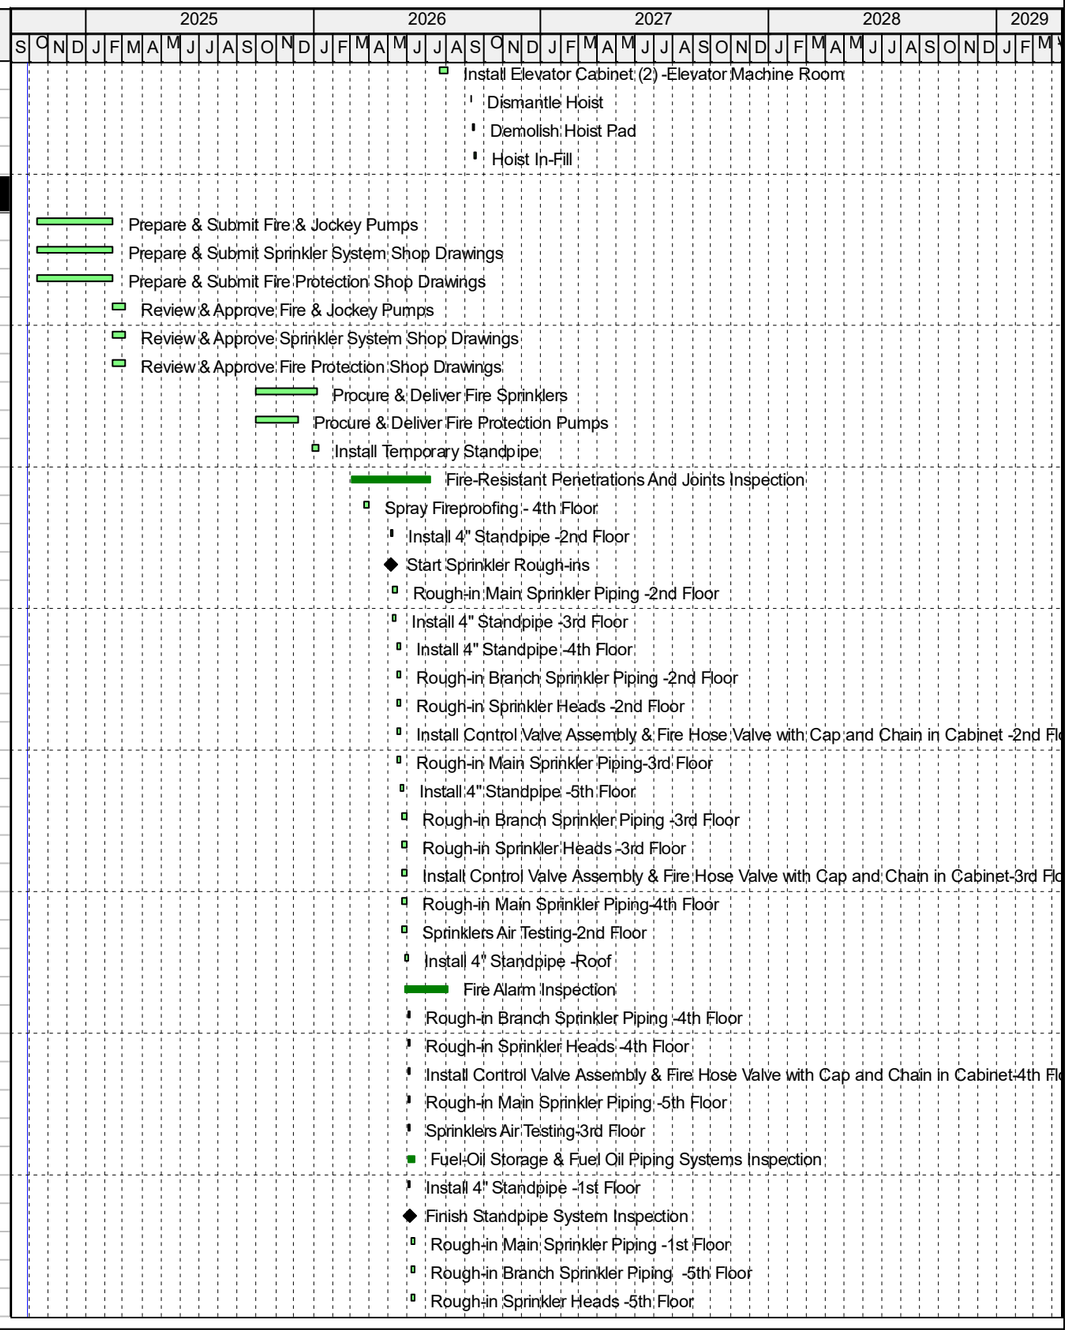

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-4340	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -5th Floor	5	08-Jun-26	12-Jun-26
CON-4250	Rough-in Main Sprinkler Piping -Roof	5	08-Jun-26	12-Jun-26
CON-4280	Sprinklers Air Testing-4th Floor	5	08-Jun-26	12-Jun-26
CON-5230	Rough-in Branch Sprinkler Piping -1st Floor	5	15-Jun-26	22-Jun-26
CON-5240	Rough-in Sprinkler Heads -1st Floor	5	15-Jun-26	22-Jun-26
CON-4430	Rough-in Branch Sprinkler Piping -Roof	5	15-Jun-26	22-Jun-26
CON-4440	Rough-in Sprinkler Heads -Roof	5	15-Jun-26	22-Jun-26
CON-4490	Sprinklers Air Testing-5th Floor	5	15-Jun-26	22-Jun-26
MIL-1330	Finish Sprinkler Rough-ins	0		22-Jun-26
CON-5270	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -1st Floor	5	23-Jun-26	29-Jun-26
CON-4650	Install 3 Way Roof Manifold -Roof	5	23-Jun-26	29-Jun-26
CON-5410	Sprinklers Air Testing-1st Floor	5	30-Jun-26	07-Jul-26
CON-5860	Install Sprinkler Booster Pump (SBP-1) -1st Floor	10	23-Jul-26	05-Aug-26
CON-6100	Install Jockey Pump (JP-1) -1st Floor	10	06-Aug-26	19-Aug-26
CLO-1280	Fire Alarm Testing & Commissioning	21	10-Aug-26	08-Sep-26
CLO-1160	Sprinkler/Domestic Booster Pumps Testing & Commissioning	14	20-Aug-26	09-Sep-26
CLO-1170	Sprinkler/Domestic Booster Pumps Inspection	3	10-Sep-26	14-Sep-26
CLO-1180	Sprinkler/Domestic Booster Pumps Sign-offs	0		14-Sep-26
DIV 15B-Plumbing		462	07-Oct-24	12-Aug-26
CON-7960	Obtain Gas Meter Layout From CON-ED	5	07-Oct-24	11-Oct-24
SUB-1010	Prepare & Submit Thermometers	40	15-Oct-24	11-Dec-24
SUB-1020	Prepare & Submit Pressure Gages	40	15-Oct-24	11-Dec-24
SUB-1030	Prepare & Submit Floor Drains	40	15-Oct-24	11-Dec-24
SUB-1040	Prepare & Submit Hangers & Supports	40	15-Oct-24	11-Dec-24
SUB-1430	Prepare & Submit Plumbing Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1600	Prepare & Submit Plumbing Fixtures	81	15-Oct-24	11-Feb-25
SUB-2170	Prepare & Submit Gas Pipes	81	15-Oct-24	11-Feb-25
SUB-2180	Prepare & Submit Water Heaters	81	15-Oct-24	11-Feb-25
SUB-2190	Prepare & Submit Pumping Apparatus & Tanks	81	15-Oct-24	11-Feb-25
SUB-3280	Prepare & Submit Valves Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3290	Prepare & Submit Valves Product Data	81	15-Oct-24	11-Feb-25
SUB-3300	Prepare & Submit Certification of Tests	81	15-Oct-24	11-Feb-25
SUB-3310	Prepare & Submit Domestic Water Sterilization Plan	81	15-Oct-24	11-Feb-25
SUB-3320	Prepare & Submit Tags, Charts & Identifications Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3330	Prepare & Submit Tags, Charts & Identifications Product Data	81	15-Oct-24	11-Feb-25
SUB-3340	Prepare & Submit Micselianeous Shop Drawing	81	15-Oct-24	11-Feb-25
APP-1160	Review & Approve Thermometers	21	12-Dec-24	01-Jan-25
APP-1170	Review & Approve Pressure Gages	21	12-Dec-24	01-Jan-25
APP-1180	Review & Approve Floor Drains	21	12-Dec-24	01-Jan-25
APP-1190	Review & Approve Hangers & Supports	21	12-Dec-24	01-Jan-25
APP-1660	Review & Approve Plumbing Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1740	Review & Approve Plumbing Fixtures	21	12-Feb-25	04-Mar-25
APP-2160	Review & Approve Gas Pipes	21	12-Feb-25	04-Mar-25
APP-2170	Review & Approve Water Heaters	21	12-Feb-25	04-Mar-25

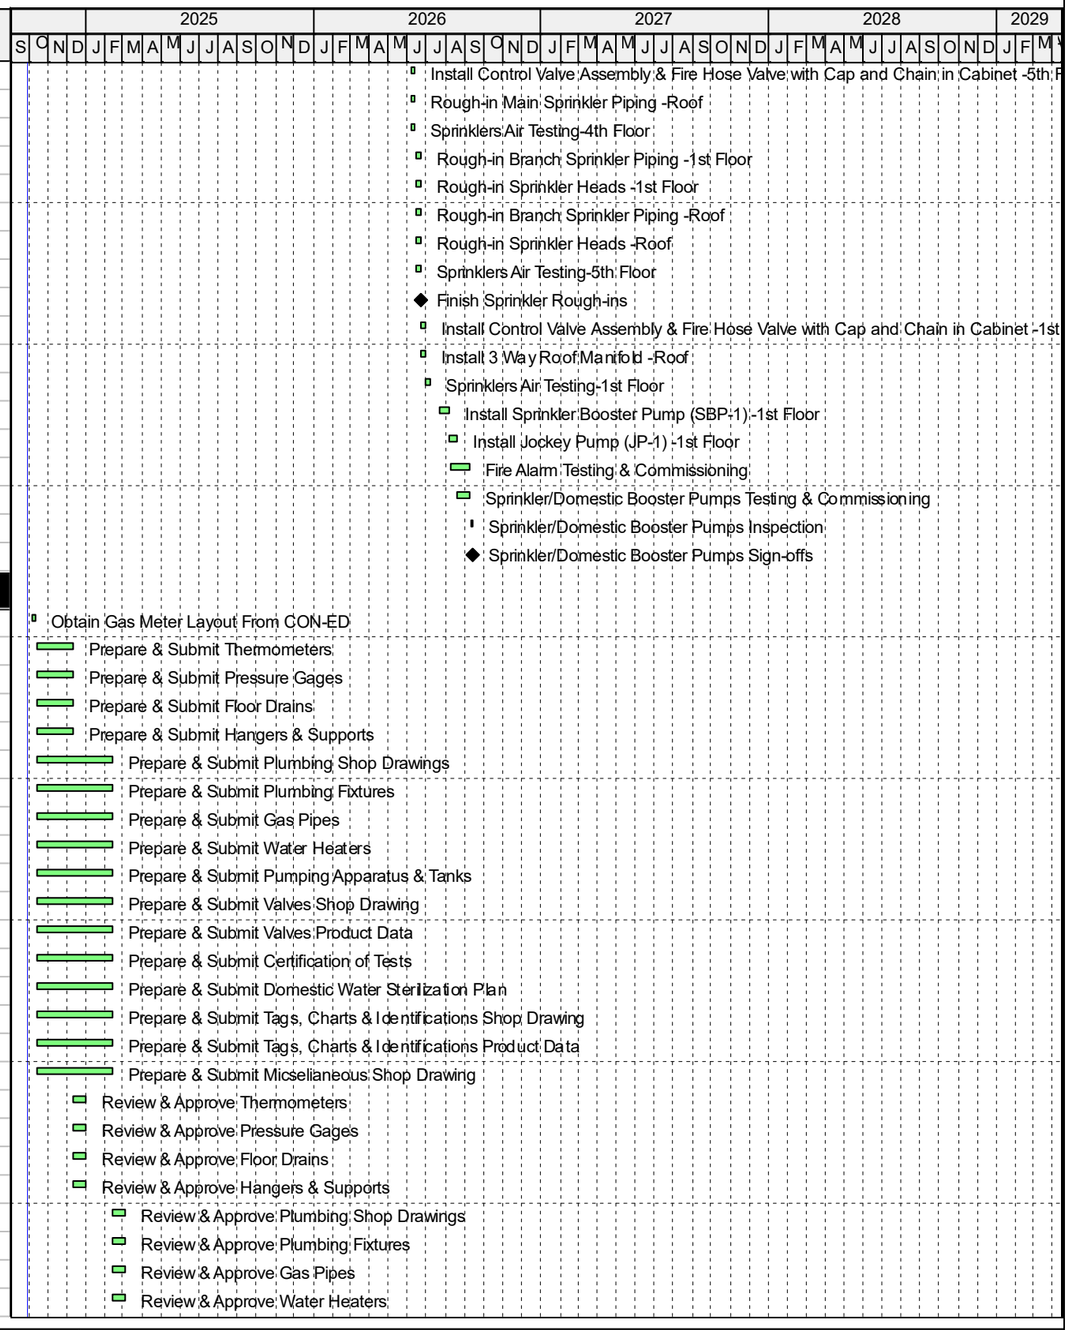

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
APP-2180	Review & Approve Pumping Apparatus & Tanks	21	12-Feb-25	04-Mar-25
APP-3280	Review & Approve Valves Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3290	Review & Approve Valves Product Data	21	12-Feb-25	04-Mar-25
APP-3300	Review & Approve Certification of Tests	21	12-Feb-25	04-Mar-25
APP-3310	Review & Approve Domestic Water Sterilization Plan	21	12-Feb-25	04-Mar-25
APP-3320	Review & Approve Tags, Charts & Identifications Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3330	Review & Approve Tags, Charts & Identifications Product Data	21	12-Feb-25	04-Mar-25
APP-3340	Review & Approve Micselianeous Shop Drawing	21	12-Feb-25	04-Mar-25
PRO-1060	Procure & Deliver Plumbing Fixtures	100	30-Sep-25	07-Jan-26
PRO-1250	Procure & Deliver Plumbing Pipes	60	30-Sep-25	28-Nov-25
PRO-1290	Procure & Deliver Plumbing Pumps	250	30-Sep-25	06-Jun-26
CON-4920	Install Floor Drains & Clean-outs -1st Floor	5	27-Nov-25	04-Dec-25
CON-3160	Install Floor Drains & Clean-outs -2nd Floor	5	19-Dec-25	26-Dec-25
I-1080	Standpipe System Inspection	111	29-Dec-25	05-Jun-26
CON-3320	Install Floor Drains & Clean-outs -3rd Floor	5	08-Jan-26	14-Jan-26
CON-3530	Install Floor Drains & Clean-outs -4th Floor	5	28-Jan-26	03-Feb-26
CON-3610	Install Floor Drains & Clean-outs -5th Floor	5	13-Feb-26	20-Feb-26
CON-1770	Install Roof Drains & Clean outs -Roof Floor	5	26-Feb-26	04-Mar-26
CON-1580	Install Plumbing Risers -2nd Floor	2	26-Feb-26	27-Feb-26
CON-1680	Install Plumbing Risers -3rd Floor	2	02-Mar-26	03-Mar-26
CON-1740	Install SSDS Risers -SSDS System -2nd Floor	2	02-Mar-26	03-Mar-26
CON-1780	Install Plumbing Risers -4th Floor	2	04-Mar-26	05-Mar-26
CON-1840	Install SSDS Risers -SSDS System -3rd Floor	2	04-Mar-26	05-Mar-26
CON-2070	Install Roof Drains & Clean outs - Mechanical Work - Roof Bulkhead	5	05-Mar-26	11-Mar-26
CON-1940	Install Plumbing Risers-5th Floor	1	06-Mar-26	06-Mar-26
CON-1970	Install SSDS Risers -SSDS System -4th Floor	2	06-Mar-26	09-Mar-26
CON-2000	Install SSDS Risers -SSDS System -5th Floor	1	09-Mar-26	09-Mar-26
CON-2630	Rough-in Gas Risers -2nd Floor	4	06-Apr-26	09-Apr-26
CON-3140	Install Plumbing Risers -1st Floor	2	10-Apr-26	13-Apr-26
CON-2740	Rough-in Domestic Water Piping -2nd Floor	4	10-Apr-26	15-Apr-26
CON-2750	Rough-in Gas Risers-3rd Floor	4	10-Apr-26	15-Apr-26
CON-3230	Install SSDS Risers -SSDS System -1st Floor	2	14-Apr-26	15-Apr-26
CON-2870	Rough-in Sanitary & Vent Piping -2nd Floor	4	16-Apr-26	21-Apr-26
CON-2880	Rough-in Domestic Water Piping -3rd Floor	4	16-Apr-26	21-Apr-26
CON-2890	Rough-in Gas Risers -4th Floor	4	16-Apr-26	21-Apr-26
CON-7970	Coordinate With CON-ED For Gas Service	7	16-Apr-26	24-Apr-26
CON-3020	Rough-in Storm Piping -2nd Floor	4	22-Apr-26	27-Apr-26
CON-3030	Rough-in Sanitary & Vent Piping -3rd Floor	4	22-Apr-26	27-Apr-26
CON-3040	Rough-in Domestic Water Piping -4th Floor	4	22-Apr-26	27-Apr-26
CON-3050	Rough-in Gas Risers & Piping -5th Floor	4	22-Apr-26	27-Apr-26
PRO-1990	Procure & Deliver Gas Meter Rig	60	25-Apr-26	23-Jun-26
CON-3170	Rough-in Storm Piping -3rd Floor	4	28-Apr-26	01-May-26
CON-3180	Rough-in Sanitary & Vent Piping -4th Floor	4	28-Apr-26	01-May-26
CON-3190	Rough-in Domestic Water Piping -5th Floor	4	28-Apr-26	01-May-26

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

PROJECS
ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3200	Plumbing Pressure Testing -2nd Floor	5	28-Apr-26	04-May-26
CON-3330	Rough-in Storm Piping -4th Floor	4	04-May-26	07-May-26
CON-3340	Rough-in Sanitary & Vent Piping -5th Floor	4	04-May-26	07-May-26
CON-3400	Install Hot Water Circulation Pump -5th Floor	5	04-May-26	08-May-26
CON-3410	Install Electric Hot Water Heater (EWH-1) -5th Floor	5	04-May-26	08-May-26
CON-3360	Plumbing Pressure Testing -3rd Floor	5	05-May-26	11-May-26
CON-4460	Rough-in Gas Risers -1st Floor	4	07-May-26	12-May-26
MIL-1260	Plumbing Rough-ins Start	0	07-May-26	
CON-4050	Plumbing Piping Insulation -2nd Floor	5	07-May-26	13-May-26
CON-3540	Rough-in Storm Piping -5th Floor	4	08-May-26	13-May-26
CON-3560	Plumbing Pressure Testing -4th Floor	5	12-May-26	18-May-26
CON-4590	Rough-in Domestic Water Piping-1st Floor	4	13-May-26	18-May-26
CON-3590	Plumbing Pressure Testing -5th Floor	5	14-May-26	20-May-26
CON-4190	Plumbing Piping Insulation -3rd Floor	5	14-May-26	20-May-26
CON-4690	Rough-in Sanitary & Vent Piping -1st Floor	4	19-May-26	22-May-26
CON-4390	Plumbing Piping Insulation -4th Floor	5	21-May-26	28-May-26
CON-4760	Rough-in Storm Piping -1st Floor	4	26-May-26	29-May-26
CON-4530	Plumbing Piping Insulation -5th Floor	5	29-May-26	04-Jun-26
MIL-1320	Plumbing Rough-ins Finish	0		29-May-26
CON-4900	Rough-in Fuel Oil Piping -Fuel Oil Room	3	01-Jun-26	03-Jun-26
CON-4940	Install Duplex Domestic Water Booster Pump System (BP-1&BP-2) -1st Floor	8	01-Jun-26	10-Jun-26
CON-4950	Install Duplex Ejector Pump System (EJ-1&EJ-2) -1st Floor	8	01-Jun-26	10-Jun-26
CON-4990	Install Fuel Oil Storage Tank (FOT-1) - Fuel Oil Room	3	03-Jun-26	05-Jun-26
CON-5020	Rough-in Fuel Oil Fill Piping -Fuel Oil Room	3	04-Jun-26	08-Jun-26
CON-5160	Install Fuel Oil Transfer Duplex Pump (FOP-1 & 2) -1st Floor	4	08-Jun-26	11-Jun-26
CON-5200	Rough-in Fuel Oil Vent Piping -Fuel Oil Room	4	09-Jun-26	12-Jun-26
CON-5050	Plumbing Pressure Testing -1st Floor	5	11-Jun-26	17-Jun-26
CON-5210	Plumbing Piping Insulation -1st Floor	5	18-Jun-26	25-Jun-26
CON-7990	Gas Authorization	5	24-Jun-26	30-Jun-26
CON-8000	Pink Slip	5	01-Jul-26	08-Jul-26
CON-5570	Install Plumbing Fixtures -2nd Floor	7	06-Jul-26	14-Jul-26
CON-5730	Install Plumbing Fixtures -3rd Floor	7	15-Jul-26	23-Jul-26
CLO-1140	SSDS System Testing & Commissioning	7	16-Jul-26	24-Jul-26
CON-5930	Install Plumbing Fixtures -4th Floor	7	24-Jul-26	03-Aug-26
CON-5300	Install Grease Interceptors - 1st Floor	5	28-Jul-26	03-Aug-26
CON-6090	Install Plumbing Fixtures -5th Floor	7	04-Aug-26	12-Aug-26
CON-6180	Install Plumbing Fixtures-1st Floor	5	06-Aug-26	12-Aug-26
DIV 15C-Mechanical		476	15-Oct-24	09-Sep-26
SUB-1000	Prepare & Submit Split Heat Pump System - SUB	60	15-Oct-24	10-Jan-25
SUB-1540	Prepare & Submit Mechanical Ducts	81	15-Oct-24	11-Feb-25
SUB-1550	Prepare & Submit Mechanical Piping	60	15-Oct-24	10-Jan-25
SUB-1710	Prepare & Submit Chillers Product Data	71	15-Oct-24	28-Jan-25
SUB-1720	Prepare & Submit Air Handling Units Product Data	71	15-Oct-24	28-Jan-25
SUB-1730	Prepare & Submit Boilers	71	15-Oct-24	28-Jan-25

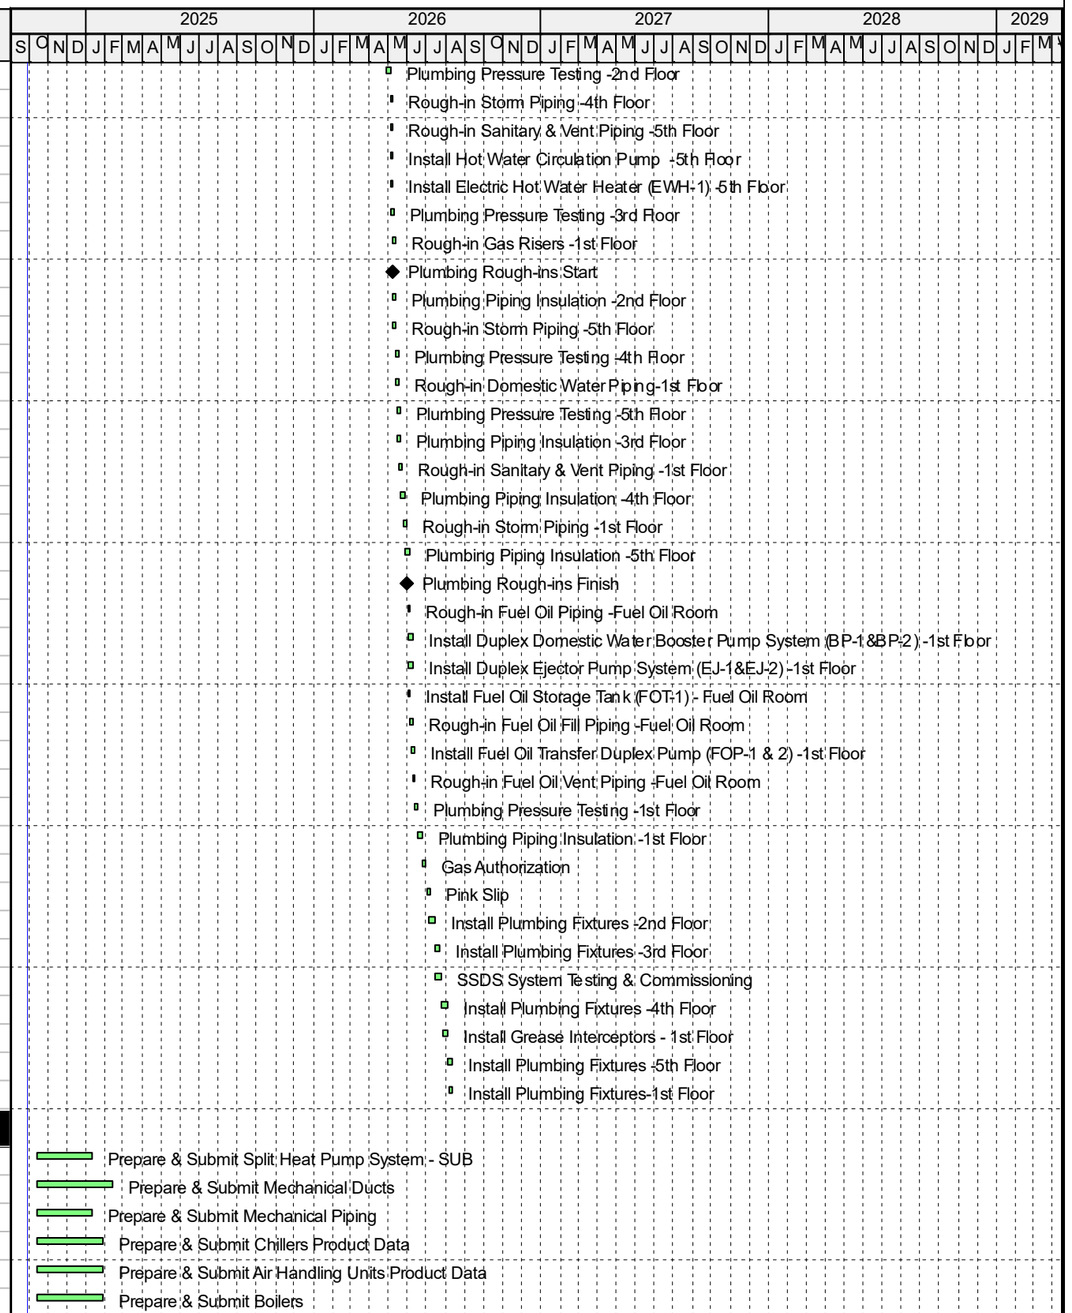

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

PROJECS
ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1760	Prepare & Submit Unit Cabinet Heaters	60	15-Oct-24	10-Jan-25
SUB-2200	Prepare & Submit HVAC Pumps	81	15-Oct-24	11-Feb-25
SUB-2210	Prepare & Submit Emergency Generator System Accessories	71	15-Oct-24	28-Jan-25
SUB-2220	Prepare & Submit Fuel Storage Equipment	81	15-Oct-24	11-Feb-25
SUB-2230	Prepare & Submit Natural Gas Leak Detection Equipment	81	15-Oct-24	11-Feb-25
SUB-2250	Prepare & Submit Temperature Control System	81	15-Oct-24	11-Feb-25
SUB-2260	Prepare & Submit Air Outlets & Inlets	81	15-Oct-24	11-Feb-25
SUB-3350	Prepare & Submit Valves (HVAC) Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3360	Prepare & Submit Valves (HVAC) Product Data	81	15-Oct-24	11-Feb-25
SUB-3370	Prepare & Submit Piping Insulation Schedule Listing Items	81	15-Oct-24	11-Feb-25
SUB-3380	Prepare & Submit Schedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	81	15-Oct-24	11-Feb-25
SUB-3390	Prepare & Submit Schedules Showing Manfacturers's Product Number Duct Work Insulation	81	15-Oct-24	11-Feb-25
SUB-3400	Prepare & Submit Hydronic Specialities Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3410	Prepare & Submit Hydronic Specialities Product Data	81	15-Oct-24	11-Feb-25
SUB-3420	Prepare & Submit Water Treatment Firm	81	15-Oct-24	11-Feb-25
SUB-3430	Prepare & Submit Chemical Products Product Data	81	15-Oct-24	11-Feb-25
SUB-3440	Prepare & Submit Detail of Gag for the Safety Relief Valves	71	15-Oct-24	28-Jan-25
SUB-3450	Prepare & Submit Boiler Accessories Maintenance Data	71	15-Oct-24	28-Jan-25
SUB-3460	Prepare & Submit Breeching Chimney Connectors and Chimneys Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3470	Prepare & Submit Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	81	15-Oct-24	11-Feb-25
APP-1250	Review & Approve Split Heat Pump System - SUB	21	11-Jan-25	31-Jan-25
APP-1280	Review & Approve Mechanical Piping	21	11-Jan-25	31-Jan-25
APP-1290	Review & Approve Unit Cabinet Heaters	21	11-Jan-25	31-Jan-25
APP-1820	Review & Approve Chillers Product Data	21	29-Jan-25	18-Feb-25
APP-1300	Review & Approve Air Handling Units Product Data	21	29-Jan-25	18-Feb-25
APP-1830	Review & Approve Boilers	21	29-Jan-25	18-Feb-25
APP-2200	Review & Approve Emergency Generator System Accessories	21	29-Jan-25	18-Feb-25
APP-3440	Review & Approve Detail of Gag for the Safety Relief Valves	21	29-Jan-25	18-Feb-25
APP-3450	Review & Approve Boiler Accessories Maintenance Data	21	29-Jan-25	18-Feb-25
APP-1730	Review & Approve Mechanical Ducts	21	12-Feb-25	04-Mar-25
APP-2190	Review & Approve HVAC Pumps	21	12-Feb-25	04-Mar-25
APP-2210	Review & Approve Fuel Storage Equipment	21	12-Feb-25	04-Mar-25
APP-2220	Review & Approve Natural Gas Leak Detection Equipment	21	12-Feb-25	04-Mar-25
APP-2240	Review & Approve Temperature Control System	21	12-Feb-25	04-Mar-25
APP-2250	Review & Approve Air Outlets & Inlets	21	12-Feb-25	04-Mar-25
APP-3350	Review & Approve Valves (HVAC) Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3360	Review & Approve Valves (HVAC) Product Data	21	12-Feb-25	04-Mar-25
APP-3370	Review & Approve Piping Insulation Schedule Listing Items	21	12-Feb-25	04-Mar-25
APP-3380	Review & Approve chedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	21	12-Feb-25	04-Mar-25
APP-3390	Review & Approve chedules Showing Manfacturers's Product Number Duct Work Insulation	21	12-Feb-25	04-Mar-25
APP-3400	Review & Approve Hydronic Specialities Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3410	Review & Approve Hydronic Specialities Product Data	21	12-Feb-25	04-Mar-25
APP-3420	Review & Approve Water Treatment Firm	21	12-Feb-25	04-Mar-25
APP-3430	Review & Approve Chemical Products Product Data	21	12-Feb-25	04-Mar-25

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
APP-3460	Review & Approve Breeching Chimney Connectors and Chimneys Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3470	Review & Approve Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	21	12-Feb-25	04-Mar-25
PRO-1020	Procure & Deliver Mechanical Piping	70	30-Sep-25	08-Dec-25
PRO-1030	Procure & Deliver Mechanical Ducts	70	30-Sep-25	08-Dec-25
PRO-1270	Procure & Deliver Mechanical Pumps	70	30-Sep-25	08-Dec-25
PRO-1470	Procure & Deliver Cabinet Heaters	126	30-Sep-25	02-Feb-26
PRO-1480	Procure & Deliver Chillers	170	30-Sep-25	18-Mar-26
PRO-1490	Procure & Deliver Air Handling Units	250	30-Sep-25	06-Jun-26
PRO-1500	Procure & Deliver Boilers	84	30-Sep-25	22-Dec-25
PRO-2040	Procure & Deliver VAV Units	170	30-Sep-25	18-Mar-26
MIL-1810	Crane Mobilization-Steel Installation start	0	05-Dec-25	
CON-1130	Install MEP Hangers & Sleeves- 2nd Floor	4	22-Dec-25	26-Dec-25
CON-1230	Install MEP Hangers & Sleeves-3rd Floor	4	09-Jan-26	14-Jan-26
CON-1310	Install MEP Hangers & Sleeves-4th Floor	4	29-Jan-26	03-Feb-26
CON-1400	Install MEP Hangers & Sleeves-5th Floor	4	17-Feb-26	20-Feb-26
CON-1410	Install Duct Risers-2nd Floor	1	23-Feb-26	23-Feb-26
MIL-1180	MEP Risers Start	0	23-Feb-26	
CON-1480	Rough-in Duct Work -2nd Floor	4	24-Feb-26	27-Feb-26
CON-1490	Install Duct Risers -3rd Floor	2	24-Feb-26	25-Feb-26
CON-1500	Install Mechanical Piping Risers-2nd Floor	2	24-Feb-26	25-Feb-26
MIL-1210	Duct Rough-ins Start	0	24-Feb-26	
CON-1510	Duct Leak Test -2nd Floor	2	24-Feb-26	25-Feb-26
CON-1560	Install Duct Risers -4th Floor	2	26-Feb-26	27-Feb-26
CON-1590	Install Mechanical Piping Risers -3rd Floor	2	26-Feb-26	27-Feb-26
CON-1600	Duct Leak Test -3rd Floor	2	26-Feb-26	27-Feb-26
CON-1610	Install MEP Hangers & Sleeves-Roof Floor	4	27-Feb-26	04-Mar-26
CON-1850	Rough-in Hot Water Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1860	Rough-in Hot Glycol Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1870	Rough-in Chilled Glycol Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1880	Rough-in Refrigerant Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1890	Rough-in Duct Work -3rd Floor	5	02-Mar-26	06-Mar-26
CON-1630	Install Duct Risers-5th Floor	2	02-Mar-26	03-Mar-26
CON-1690	Install Mechanical Piping Risers -4th Floor	2	02-Mar-26	03-Mar-26
CON-1700	Duct Leak Test -4th Floor	2	02-Mar-26	03-Mar-26
CON-1790	Install Mechanical Piping Risers-5th Floor	2	04-Mar-26	05-Mar-26
CON-1810	Duct Leak Test -5th Floor	1	04-Mar-26	04-Mar-26
MIL-1830	Crane Mobilization-Precast Sandwich Panels Installation Start	0	05-Mar-26	
CON-2160	Rough-in Refrigerant Piping-3rd Floor	7	09-Mar-26	17-Mar-26
CON-2170	Rough-in Duct Work -4th Floor	5	09-Mar-26	13-Mar-26
CON-2130	Rough-in Hot Water Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-2140	Rough-in Hot Glycol Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-2150	Rough-in Chilled Glycol Piping-3rd Floor	7	11-Mar-26	19-Mar-26
MIL-1820	Crane Mobilization-Steel Installation Finish	0		12-Mar-26
CON-2290	Rough-in Refrigerant Piping-4th Floor	7	16-Mar-26	24-Mar-26

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2300	Rough-in Duct Work-5th Floor	5	16-Mar-26	20-Mar-26
CON-2120	Install Air Cooled Chiller CH-1 -Roof Floor	7	17-Mar-26	25-Mar-26
MIL-1380	Crane Mobilization-Mechanical Subcontractor	78	17-Mar-26	07-Jul-26
CON-3980	Install VAV Boxes & Sound Attenuator Devices-2nd Floor	5	19-Mar-26	25-Mar-26
CON-2230	Install Emergency Generator -Bulkhead	7	19-Mar-26	27-Mar-26
CON-2260	Rough-in Hot Water Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-2270	Rough-in Hot Glycol Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-2280	Rough-in Chilled Glycol Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-2470	Rough-in Refrigerant Piping-5th Floor	7	23-Mar-26	31-Mar-26
CON-4140	Install VAV Boxes & Sound Attenuator Devices-3rd Floor	5	26-Mar-26	01-Apr-26
CON-2350	Install Air Cooled Chiller CH-2 -Roof Floor	7	26-Mar-26	03-Apr-26
CON-2440	Rough-in Hot Water Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-2450	Rough-in Hot Glycol Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-2460	Rough-in Chilled Glycol Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-4220	Install VAV Boxes & Sound Attenuator Devices-4th Floor	5	02-Apr-26	08-Apr-26
MIL-1840	Crane Mobilization-Precast Sandwich Panels Installation Finish	0		06-Apr-26
CON-2900	Install Duct Risers-1st Floor	1	07-Apr-26	07-Apr-26
I-1120	Mechanical System Inspection	69	07-Apr-26	15-Jul-26
CON-3060	Install Mechanical Piping Risers-1st Floor	2	08-Apr-26	09-Apr-26
CON-3070	Duct Leak Test -1st Floor	1	08-Apr-26	08-Apr-26
CON-3120	Rough-in Duct Work -1st Floor	4	09-Apr-26	14-Apr-26
CON-4330	Install VAV Boxes & Sound Attenuator Devices-5th Floor	5	09-Apr-26	15-Apr-26
MIL-1290	Duct Rough-ins Finish	0		14-Apr-26
CON-3460	Rough-in Hot Water Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3470	Rough-in Hot Glycol Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3480	Rough-in Chilled Glycol Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3490	Rough-in Refrigerant Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3970	Install VAV Boxes & Sound Attenuator Devices- 1st Floor	5	16-Apr-26	22-Apr-26
CON-3130	Install Electric Unit Heaters -3rd Floor	5	23-Apr-26	29-Apr-26
CON-3420	Install Electric Unit Heaters -4th Floor	5	30-Apr-26	06-May-26
CON-3640	Install Electric Unit Heaters -5th Floor	3	07-May-26	11-May-26
CON-4070	Install Duct Insulation -2nd Floor	8	07-May-26	18-May-26
CON-4320	Install Duct Insulation -3rd Floor	8	19-May-26	29-May-26
CON-4570	Install Duct Insulation -4th Floor	8	01-Jun-26	10-Jun-26
CON-2250	Install Air Handling Unit AHU-1 -Roof Floor	5	08-Jun-26	12-Jun-26
MIL-1460	Roof Top Units Installations Start	0	08-Jun-26	
CON-4710	Install Duct Insulation -5th Floor	8	11-Jun-26	23-Jun-26
MIL-2992	Finish Fuel-Oil Storage & Fuel Oil Piping Systems Inspection	0		11-Jun-26
CON-2430	Install Air Handling Unit AHU-2 -Roof Floor	5	15-Jun-26	22-Jun-26
CON-2560	Install Air Handling Unit AHU-3 -Roof Floor	5	23-Jun-26	29-Jun-26
CON-4840	Install Duct Insulation -1st Floor	8	24-Jun-26	06-Jul-26
CON-2720	Install Air Handling Unit AHU-4 -Roof Floor	5	30-Jun-26	07-Jul-26
CON-4670	Install Exhaust Fans -1st Floor	5	07-Jul-26	13-Jul-26
CLO-1010	HVAC Flush-Out	20	07-Jul-26	03-Aug-26

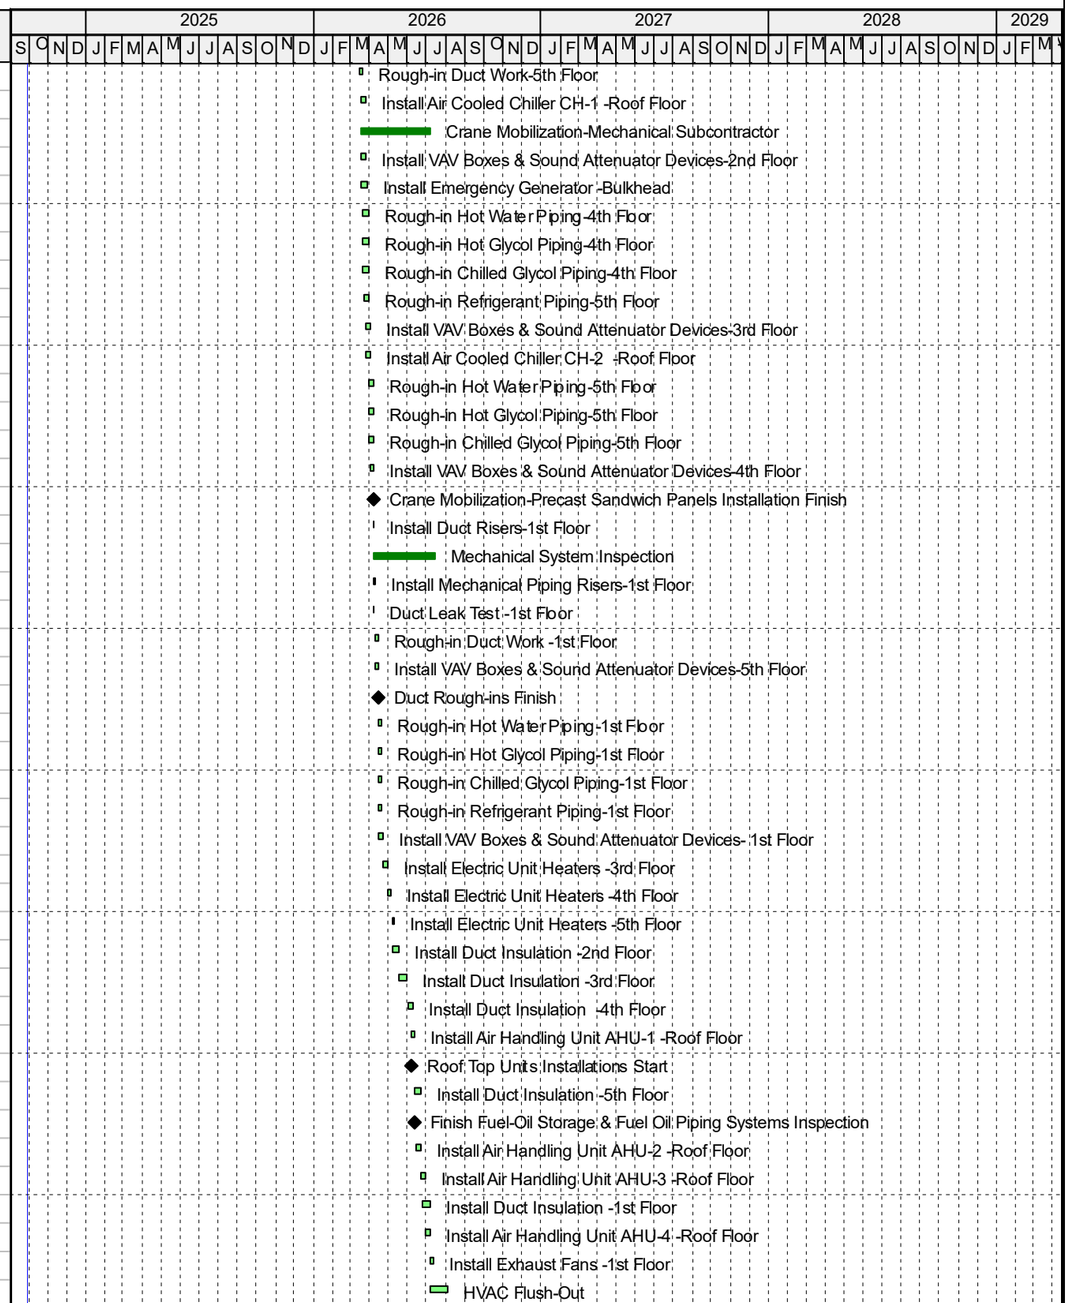

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

PROJECS
ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2860	Install Fume Hood Exhaust -Roof Floor	3	08-Jul-26	10-Jul-26
CON-5770	Install Air Cooled Condensing Unit ACCU - Mechanical Work - 5th Floor	5	08-Jul-26	14-Jul-26
CON-3000	Install Smoke Purge Fan -Roof Floor	3	13-Jul-26	15-Jul-26
CON-4870	Install Cabinet Unit Heaters With Fan CUH-1st Floor	3	14-Jul-26	16-Jul-26
CON-4880	Install Motorized Fire/Smoke Damper FSD - Mechanical Work - 1st Floor	7	14-Jul-26	22-Jul-26
MIL-1480	Roof Top Units Installations Finish	0		14-Jul-26
MIL-2972	Finish Mechanical System Inspection	0		15-Jul-26
CON-5060	Install Hot Glycol / Hot Water Cabinet Heater (CUH)-3rd Floor	4	17-Jul-26	22-Jul-26
CON-5070	Install Electric Unit Heaters -1st Floor	7	17-Jul-26	27-Jul-26
CON-6050	Install Boiler B-1-Boiler Room	5	23-Jul-26	29-Jul-26
CON-5260	Install Cabinet Unit Heater With Fan CUH -4th Floor	4	23-Jul-26	28-Jul-26
CON-5150	Install Air Conditioning Unit AC - Mechanical Work - 1st Floor	4	23-Jul-26	28-Jul-26
CON-5280	Install Convector Heater CV - Mechanical Work - 3rd Floor	4	23-Jul-26	28-Jul-26
CLO-1240	Elevator Sump Pump Testing & Commissioning	21	28-Jul-26	25-Aug-26
CLO-1270	Water Heater Testing & Commissioning	21	28-Jul-26	25-Aug-26
CON-5430	Install Hot Glycol / Hot Water Cabinet Heater (CUH)-5th Floor	4	29-Jul-26	03-Aug-26
CLO-1220	Emergency Generator Electric Load Test	3	29-Jul-26	31-Jul-26
CON-5320	Install Door Curtains DC - Mechanical Work - 1st Floor	7	29-Jul-26	06-Aug-26
CON-5450	Install Air Conditioning Unit AC - Mechanical Work - 3rd Floor	4	29-Jul-26	03-Aug-26
CON-6110	Install Boiler B-2-Boiler Room	5	30-Jul-26	05-Aug-26
CON-6120	Install Air Separator Units (AS-1 , AS-2 & AS-3)	2	30-Jul-26	31-Jul-26
CON-6130	Install Boiler Condensate ACID Neutralization Tubes -Boiler Room	2	30-Jul-26	31-Jul-26
CON-6200	Install Expansion Tanks (ET-1 , ET-2 & ET-3)	2	03-Aug-26	04-Aug-26
CON-6210	Install Glycol Make-up Units (GF-1 & GF-2 & GF-3)	2	03-Aug-26	04-Aug-26
CON-6220	Install Reduced Pressure Zone (RPZ) Devices -Boiler Room	2	03-Aug-26	04-Aug-26
PER-2640	Obtain Emergency Generator Permit	5	03-Aug-26	07-Aug-26
CON-5590	Install Exhaust Fan EF - Mechanical Work - 5th Floor	4	04-Aug-26	07-Aug-26
CLO-1290	Glycol System Testing & Commissioning	21	05-Aug-26	02-Sep-26
CON-6260	Install Heat Exchanger -Boiler Room	2	06-Aug-26	07-Aug-26
CON-5490	Install Convector Heater CV - Mechanical Work - 1st Floor	7	07-Aug-26	17-Aug-26
CON-6290	Install Hot Glycol Units Heaters (UH-5-1, UH-5-2)	2	10-Aug-26	11-Aug-26
CON-5630	Install Convector Heater CV - Mechanical Work - 5th Floor	3	10-Aug-26	12-Aug-26
CON-6330	Install Heat Pump Electric Hot Water Heater (HPWH#1&2)-Boiler Room	2	12-Aug-26	13-Aug-26
CLO-1000	Elevator Testing & Commissioning	20	12-Aug-26	09-Sep-26
CON-6340	Install Exhaust Fans -Boiler Room	2	14-Aug-26	17-Aug-26
CON-6350	Install Primary Hot Water Pump (GHWP 1 to 3) -Boiler Room	2	14-Aug-26	17-Aug-26
CON-6360	Install Primary Chilled Water Pump (GCHWP-1&2)-Boiler Room	2	14-Aug-26	17-Aug-26
CON-6400	Install Secondary Hot Water Pump(HWP-1&2)-Boiler Room	2	18-Aug-26	19-Aug-26
DIV 16-Electrical		483	15-Oct-24	19-Sep-26
SUB-1420	Prepare & Submit Electrical Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1520	Prepare & Submit Lighting Fixtures	71	15-Oct-24	28-Jan-25
SUB-1590	Prepare & Submit Electrical Equipment, Conduits, and Cables	20	15-Oct-24	12-Nov-24
SUB-1640	Prepare & Submit Fire Detectors & Alarms	81	15-Oct-24	11-Feb-25
SUB-1660	Prepare & Submit Signs	81	15-Oct-24	11-Feb-25

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1680	Prepare & Submit Telecommunication System Drawings	81	15-Oct-24	11-Feb-25
SUB-1690	Prepare & Submit Internet Protocol Digital Video Surveillance System using Digital Cameras	71	15-Oct-24	28-Jan-25
SUB-1740	Prepare & Submit Emergency Generator System Product Data	71	15-Oct-24	28-Jan-25
SUB-1750	Prepare & Submit Switch Gears Product Data	20	15-Oct-24	12-Nov-24
SUB-2140	Prepare & Submit Switch & Panel Boards	81	15-Oct-24	11-Feb-25
SUB-2150	Prepare & Submit Auditorium & Television Studio Dimming System Product Data	81	15-Oct-24	11-Feb-25
SUB-2160	Prepare & Submit Overcurrent Protective Devices Data	81	15-Oct-24	11-Feb-25
SUB-3480	Prepare & Submit Plate Heat Exchanger Maintenance Data	81	15-Oct-24	11-Feb-25
SUB-3490	Prepare & Submit Plate Heat Exchanger Product Data	81	15-Oct-24	11-Feb-25
SUB-3500	Prepare & Submit Coils Maintenance Data	81	15-Oct-24	11-Feb-25
SUB-3510	Prepare & Submit Coils Certifications	81	15-Oct-24	11-Feb-25
SUB-3520	Prepare & Submit Convectors Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3530	Prepare & Submit Convectors Product Data	81	15-Oct-24	11-Feb-25
SUB-3540	Prepare & Submit Fan Coils Units Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3550	Prepare & Submit Fan Coils Units Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-3560	Prepare & Submit Door Air Curtains Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3570	Prepare & Submit Door Air Curtains Product Data	81	15-Oct-24	11-Feb-25
SUB-3580	Prepare & Submit Centrifugal Fans Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3590	Prepare & Submit Centrifugal Fans Product Data	81	15-Oct-24	11-Feb-25
SUB-3600	Prepare & Submit Centrifugal Fans Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3610	Prepare & Submit Air Filters Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3620	Prepare & Submit Air Filters Product Data	81	15-Oct-24	11-Feb-25
SUB-3630	Prepare & Submit Air Filters Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3640	Prepare & Submit Duct Accessories Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3650	Prepare & Submit Damper Assemblies Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3660	Prepare & Submit Damper Assemblies Product Data	81	15-Oct-24	11-Feb-25
SUB-3670	Prepare & Submit Damper Assemblies Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3680	Prepare & Submit Variable Air Terminals Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3690	Prepare & Submit Variable Air Terminals Product Data	81	15-Oct-24	11-Feb-25
SUB-3700	Prepare & Submit Variable Air Terminals Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3710	Prepare & Submit AHU for Public Assemblies Sapces Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3720	Prepare & Submit AHU for Public Assemblies Sapces Product Data	81	15-Oct-24	11-Feb-25
SUB-3730	Prepare & Submit AHU for Public Assemblies Sapces Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3740	Prepare & Submit Control Systems Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3750	Prepare & Submit Truck Network Cable Schematic Diagram	81	15-Oct-24	11-Feb-25
CON-8010	Coordination With CON-ED For Temporary Electrical Power	10	07-Nov-24	21-Nov-24
APP-1080	Review & Approve Electrical Equipment, Conduits, and Cables	21	13-Nov-24	03-Dec-24
APP-1090	Review & Approve Switch Gears Product Data	21	13-Nov-24	03-Dec-24
CON-8020	Scheduling With CON-ED For Temporary Electrical Power	7	22-Nov-24	03-Dec-24
APP-1120	Review & Approve Lighting Fixtures	21	29-Jan-25	18-Feb-25
APP-1220	Review & Approve Internet Protocol Digital Video Surveillance System using Digital Cameras	35	29-Jan-25	04-Mar-25
APP-1070	Review & Approve Emergency Generator System Product Data	21	29-Jan-25	18-Feb-25
APP-1650	Review & Approve Electrical Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1770	Review & Approve Fire Detectors & Alarms	21	12-Feb-25	04-Mar-25

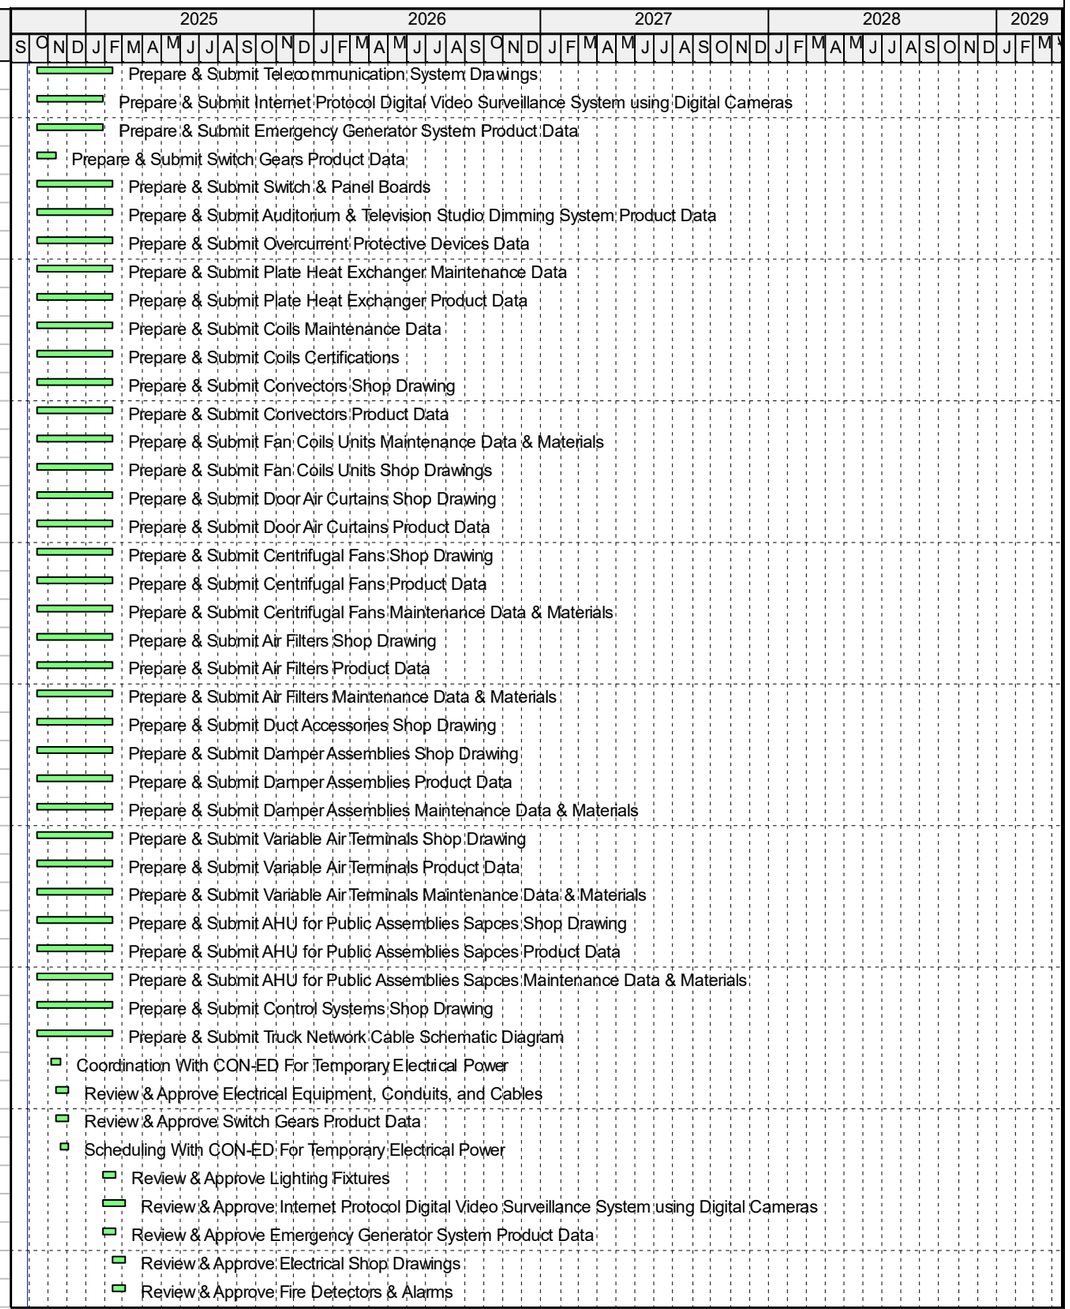

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1790	Review & Approve Signs	21	12-Feb-25	04-Mar-25
APP-1800	Review & Approve Telecommunication System Drawings	21	12-Feb-25	04-Mar-25
APP-2130	Review & Approve Switch & Panel Boards	21	12-Feb-25	04-Mar-25
APP-2140	Review & Approve Auditorium & Television Studio Dimming System Product Data	21	12-Feb-25	04-Mar-25
APP-2150	Review & Approve Overcurrent Protective Devices Data	21	12-Feb-25	04-Mar-25
APP-3480	Review & Approve Plate Heat Exchanger Maintenance Data	21	12-Feb-25	04-Mar-25
APP-3490	Review & Approve Plate Heat Exchanger Product Data	21	12-Feb-25	04-Mar-25
APP-3500	Review & Approve Coils Maintenance Data	21	12-Feb-25	04-Mar-25
APP-3510	Review & Approve Coils Certifications	21	12-Feb-25	04-Mar-25
APP-3520	Review & Approve Convectors Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3530	Review & Approve Convectors Product Data	21	12-Feb-25	04-Mar-25
APP-3540	Review & Approve Fan Coils Units Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3550	Review & Approve Fan Coils Units Shop Drawings	21	12-Feb-25	04-Mar-25
APP-3560	Review & Approve Door Air Curtains Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3570	Review & Approve Door Air Curtains Product Data	21	12-Feb-25	04-Mar-25
APP-3580	Review & Approve Centrifugal Fans Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3590	Review & Approve Centrifugal Fans Product Data	21	12-Feb-25	04-Mar-25
APP-3600	Review & Approve Centrifugal Fans Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3610	Review & Approve Air Filters Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3620	Review & Approve Air Filters Product Data	21	12-Feb-25	04-Mar-25
APP-3630	Review & Approve Air Filters Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3640	Review & Approve Duct Accessories Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3650	Review & Approve Damper Assemblies Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3660	Review & Approve Damper Assemblies Product Data	21	12-Feb-25	04-Mar-25
APP-3670	Review & Approve Damper Assemblies Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3680	Review & Approve Variable Air Terminals Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3690	Review & Approve Variable Air Terminals Product Data	21	12-Feb-25	04-Mar-25
APP-3700	Review & Approve Variable Air Terminals Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3710	Review & Approve AHU for Public Assemblies Sapces Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3720	Review & Approve AHU for Public Assemblies Sapces Product Data	21	12-Feb-25	04-Mar-25
APP-3730	Review & Approve AHU for Public Assemblies Sapces Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3740	Review & Approve Control Systems Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3750	Review & Approve Truck Network Cable Schematic Diagram	21	12-Feb-25	04-Mar-25
PRO-1140	Procure & Deliver Lighting Fixtures	60	30-Sep-25	28-Nov-25
PRO-1050	Procure & Deliver Electrical Equipment	130	30-Sep-25	06-Feb-26
PRO-1110	Procure & Deliver Fire Detectors & Alarms	60	30-Sep-25	28-Nov-25
PRO-1210	Procure & Deliver Signs	70	30-Sep-25	08-Dec-25
PRO-1260	Procure & Deliver Electrical Wires & Conduits	130	30-Sep-25	06-Feb-26
PRO-1310	Procure & Deliver Telecommunication System	60	30-Sep-25	28-Nov-25
PRO-1330	Procure & Deliver Cameras	60	30-Sep-25	28-Nov-25
PRO-1510	Procure & Deliver Emergency Generator	290	30-Sep-25	16-Jul-26
PRO-1520	Procure & Deliver Switch Gears	250	30-Sep-25	06-Jun-26
CON-8030	Procurement From CON-ED For Temporary Electrical Power	20	30-Sep-25	19-Oct-25
MIL-1850	Construction Start	0	30-Sep-25	

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-8040	CON-ED Work For Temporary Electrical Power	10	20-Oct-25	31-Oct-25
CON-1050	Install Underground Conduits & Wires -1st Floor	6	12-Nov-25	19-Nov-25
CON-99327	Install Lightning Protection System-1st Floor	2	03-Dec-25	04-Dec-25
CON-1710	Install Power Risers-2nd Floor	2	02-Mar-26	03-Mar-26
CON-1800	Install Low Voltage Risers-2nd Floor	2	04-Mar-26	05-Mar-26
CON-1820	Install Power Risers-3rd Floor	2	04-Mar-26	05-Mar-26
CON-99347	Install Lightning Protection System - Roof Floor	6	05-Mar-26	12-Mar-26
CON-1950	Install Low Voltage Risers-3rd Floor	2	06-Mar-26	09-Mar-26
CON-1960	Install Power Risers-4th Floor	2	06-Mar-26	09-Mar-26
CON-2040	Install Low Voltage Risers-4th Floor	2	10-Mar-26	11-Mar-26
CON-2050	Install Power Risers-5th Floor	3	10-Mar-26	12-Mar-26
CON-2180	Rough-in Power Conduits -2nd Floor	6	11-Mar-26	18-Mar-26
CON-2100	Install Low Voltage Risers-5th Floor	3	13-Mar-26	17-Mar-26
CON-99337	Install Lightning Protection system -5th Floor	3	13-Mar-26	17-Mar-26
CON-2320	Rough-in Power Conduits-3rd Floor	6	19-Mar-26	26-Mar-26
CON-2330	Rough-in Low-Voltage Conduits -2nd Floor	6	19-Mar-26	26-Mar-26
CON-2340	Power Wires Pulling -2nd Floor	6	19-Mar-26	26-Mar-26
CON-2640	Install Grounding Bars - 3rd Floor IDF Room	5	27-Mar-26	02-Apr-26
CON-2480	Rough-in Power Conduits-4th Floor	6	27-Mar-26	03-Apr-26
CON-2490	Low Voltage Wires Pulling -2nd Floor	6	27-Mar-26	03-Apr-26
CON-2500	Rough-in Low-Voltage Conduits-3rd Floor	6	27-Mar-26	03-Apr-26
CON-2510	Power Wires Pulling-3rd Floor	6	27-Mar-26	03-Apr-26
CON-2520	Install Voice Rack - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2530	Install Data Rack - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2540	Install Ground Bus Bar - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2800	Install Data rack - 3rd Floor IDF Room	8	03-Apr-26	14-Apr-26
CON-2830	Install IPDVS Equipment Rack - 3rd Floor IDF Room	4	03-Apr-26	08-Apr-26
CON-2810	Install Grounding Bars - 4th Floor IDF Room	5	06-Apr-26	10-Apr-26
CON-2650	Install Data Rack - 4th Floor IDF Room	7	06-Apr-26	14-Apr-26
CON-2660	Install Voice Rack - 4th Floor IDF Room	5	06-Apr-26	10-Apr-26
CON-2670	Install Wiring Devices -2nd Floor	7	06-Apr-26	14-Apr-26
CON-2680	Rough-in Power Conduits -5th Floor	6	06-Apr-26	13-Apr-26
CON-2690	Low Voltage Wires Pulling -3rd Floor	6	06-Apr-26	13-Apr-26
CON-2700	Rough-in Low-Voltage Conduits-4th Floor	6	06-Apr-26	13-Apr-26
CON-2710	Power Wires Pulling-4th Floor	6	06-Apr-26	13-Apr-26
MIL-1270	Electrical Rough-ins Start	0	09-Apr-26	
CON-2760	Install IPDVS Equipment Rack - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2770	Install Ladder Rack Cable Tray - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2780	Install BACnet Data Cabinet - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2820	Install Cable Ladder - 4th Floor IDF Room	5	13-Apr-26	17-Apr-26
CON-2840	Install Main Sound Rack - 34th Floor IDF Room	5	13-Apr-26	17-Apr-26
CON-3260	Install Power Risers-1st Floor	2	14-Apr-26	15-Apr-26
CON-2950	Rough-in Low-Voltage Conduits-5th Floor	6	14-Apr-26	21-Apr-26
CON-2960	Power Wires Pulling-5th Floor	6	14-Apr-26	21-Apr-26

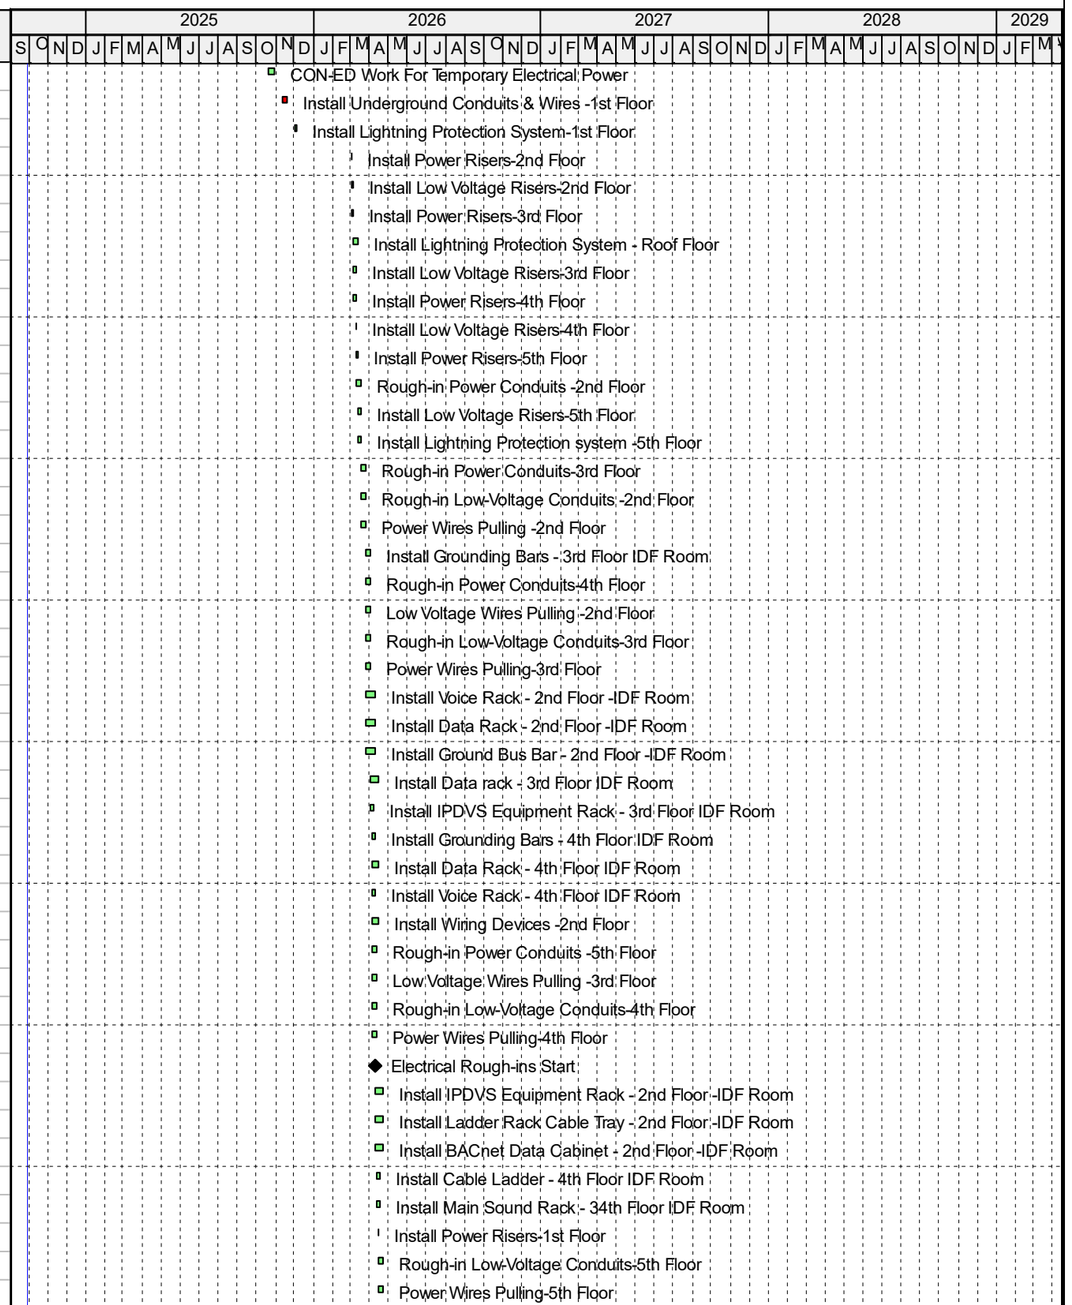

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3250	Install Voice Rack - 3rd Floor IDF Room	5	15-Apr-26	21-Apr-26
CON-2930	Install Wiring Devices -3rd Floor	7	15-Apr-26	23-Apr-26
CON-2940	Low Voltage Wires Pulling-4th Floor	6	15-Apr-26	22-Apr-26
CON-3350	Install Low Voltage Risers-1st Floor	2	16-Apr-26	17-Apr-26
CON-3110	Install IPDVS Equipment Rack - 4th Floor IDF Room	5	20-Apr-26	24-Apr-26
CON-3760	Rough-in Power Conduits -1st Floor	4	21-Apr-26	24-Apr-26
CON-3550	Install Cable Ladder - 3rd Floor IDF Room	5	22-Apr-26	28-Apr-26
CON-3570	Install Main Sound Rack - 3rd Floor IDF Room	5	22-Apr-26	28-Apr-26
CON-3290	Low Voltage Wires Pulling-5th Floor	6	23-Apr-26	30-Apr-26
CON-4730	Rough-in Conduits & Wires - Electric Service Room	6	23-Apr-26	30-Apr-26
CON-3280	Install Wiring Devices -4th Floor	7	24-Apr-26	04-May-26
CON-3910	Install Grounding System -1st Floor	5	27-Apr-26	01-May-26
CON-3920	Rough-in Low-Voltage Conduits-1st Floor	4	27-Apr-26	30-Apr-26
CON-3930	Power Wires Pulling-1st Floor	4	27-Apr-26	30-Apr-26
CON-3740	Install Ground Bus Bar - 1st Floor MDF Room	6	29-Apr-26	06-May-26
CON-4180	Low Voltage Wires Pulling -1st Floor	4	01-May-26	06-May-26
CON-4960	F/R/P Concrete Pad - Electric Service Room	6	01-May-26	08-May-26
CON-3660	Install Wiring Devices -5th Floor	8	05-May-26	14-May-26
MIL-1350	Electrical Rough-ins Finish	0		06-May-26
CON-4110	Install Voice Rack - 1st Floor MDF Room	6	07-May-26	14-May-26
CON-4500	Install SSDS Control Panel -1st Floor	5	07-May-26	13-May-26
CON-5180	Install Service Switchboard "SS-A"- Electric Service Room	5	11-May-26	15-May-26
CON-4510	Install Sound Rack - 1st Floor MDF Room	6	15-May-26	22-May-26
CON-4120	Install Project Connect Cabinet - 1st Floor MDF Room	8	15-May-26	27-May-26
CON-4470	Install Wiring Devices -1st Floor	7	15-May-26	26-May-26
CON-5510	Install Leak Detector - Electric Service Room	3	18-May-26	20-May-26
CON-5610	Install Sprinkler Booster Pump - Electric Service Room	4	21-May-26	27-May-26
CON-4520	Install Data Rack - 1st Floor MDF Room	6	26-May-26	02-Jun-26
CON-5640	Install Fire Alarm Normal ATS - Electric Service Room	4	28-May-26	02-Jun-26
CON-4550	Install UPS- 1st Floor MDF Room	9	03-Jun-26	15-Jun-26
CON-4130	Install BACnet Data Cabinet- 1st Floor MDF Room	9	03-Jun-26	15-Jun-26
CON-5780	Install Motorized Fire/Smoke Damper & Control Panel - Electric Service Room	5	03-Jun-26	09-Jun-26
CON-5790	Install Main Grounding Bus Bar - Electric Service Room	4	03-Jun-26	08-Jun-26
CON-9130	Install Switch Gear - Electric Service Room	5	08-Jun-26	12-Jun-26
CON-5840	Install Electric Unit Heater EUH-6 - Electric Service Room	4	10-Jun-26	15-Jun-26
CON-8060	CON-ED - Switchgear Inspection	4	15-Jun-26	18-Jun-26
CON-4780	Install IPDVS Equipment Rack - 1st Floor MDF Room	6	16-Jun-26	24-Jun-26
CON-5130	Install Lighting Fixtures -2nd Floor	5	18-Jun-26	25-Jun-26
CON-8070	CON-ED - Pull Power Cable to the Building	10	22-Jun-26	06-Jul-26
CON-4790	Install Ladder Rack Cable Tray- 1st Floor MDF Room	6	25-Jun-26	02-Jul-26
CON-5310	Install Fire alarm Sensors and Devises -2nd Floor	5	26-Jun-26	02-Jul-26
CON-5370	Install Lighting Fixtures -3rd Floor	6	29-Jun-26	07-Jul-26
CON-2580	Install Power Panels -Elevator Machine Room	7	02-Jul-26	13-Jul-26
CON-4770	Install PBX - 1st Floor MDF Room	8	06-Jul-26	15-Jul-26

Full Schedule Layout Grouped by Trade

Activity ID	Activity Name	Original Duration	Start	Finish
CON-5140	Install IPDVS Devices -2nd Floor	9	06-Jul-26	16-Jul-26
CLO-1120	MDF & IDF Rooms Testing & Commissioning	12	06-Jul-26	21-Jul-26
CON-8080	CON-ED - Terminate Power Cables	10	07-Jul-26	20-Jul-26
CON-5580	Install Lighting Fixtures -4th Floor	6	08-Jul-26	15-Jul-26
CON-5500	Install Fire alarm Sensors and Devises -3rd Floor	8	08-Jul-26	17-Jul-26
PRO-2000	Procure & Deliver Key Cutting Machine	74	08-Jul-26	19-Sep-26
CON-2790	Rough-in Conduits & Wires-Elevator Machine Room	6	14-Jul-26	21-Jul-26
CON-5960	F/R/P Concert Pad -Boiler Room	3	15-Jul-26	17-Jul-26
CON-5740	Install Lighting Fixtures -5th Floor	6	16-Jul-26	23-Jul-26
CON-3750	Install Emergency Generator- Roof Floor	4	17-Jul-26	22-Jul-26
CON-5440	Install IPDVS Devices -3rd Floor	9	17-Jul-26	29-Jul-26
CON-6000	Rough-in Conduits & Wires-Boiler Room	3	20-Jul-26	22-Jul-26
CON-5660	Install Fire alarm Sensors and Devises -4th Floor	7	20-Jul-26	28-Jul-26
CON-8090	CON-ED - Energize to the Building	5	21-Jul-26	27-Jul-26
MIL-1600	MDF Work Finish	0		21-Jul-26*
MIL-1610	IDF Work Finish	0		21-Jul-26*
CON-5380	Install Generator Connections -Roof Floor	4	23-Jul-26	28-Jul-26
CON-5940	Install Lighting Fixtures -1st Floor	7	24-Jul-26	03-Aug-26
CON-5830	Install Fire alarm Sensors and Devises -5th Floor	5	29-Jul-26	04-Aug-26
CON-5750	Install IPDVS Devices -4th Floor	9	30-Jul-26	11-Aug-26
CLO-1250	Emergency Generator Testing & Commissioning	21	03-Aug-26	31-Aug-26
CON-5950	Install Fire alarm Sensors and Devises -1st Floor	3	05-Aug-26	07-Aug-26
CLO-1020	Electrical System Testing & Commissioning	21	10-Aug-26	08-Sep-26
CON-6010	Install IPDVS Devices -5th Floor	9	12-Aug-26	24-Aug-26
CON-6410	Install Electric Unit Heater (EUH-3) - Boiler Room	2	18-Aug-26	19-Aug-26
CON-6420	Install Branch Panels (BRPP) -Boiler Room	2	18-Aug-26	19-Aug-26
CON-6040	Install IPDVS Devices -1st Floor	7	25-Aug-26	02-Sep-26
MIL-1620	IPDVS Work Finish	0		18-Sep-26*

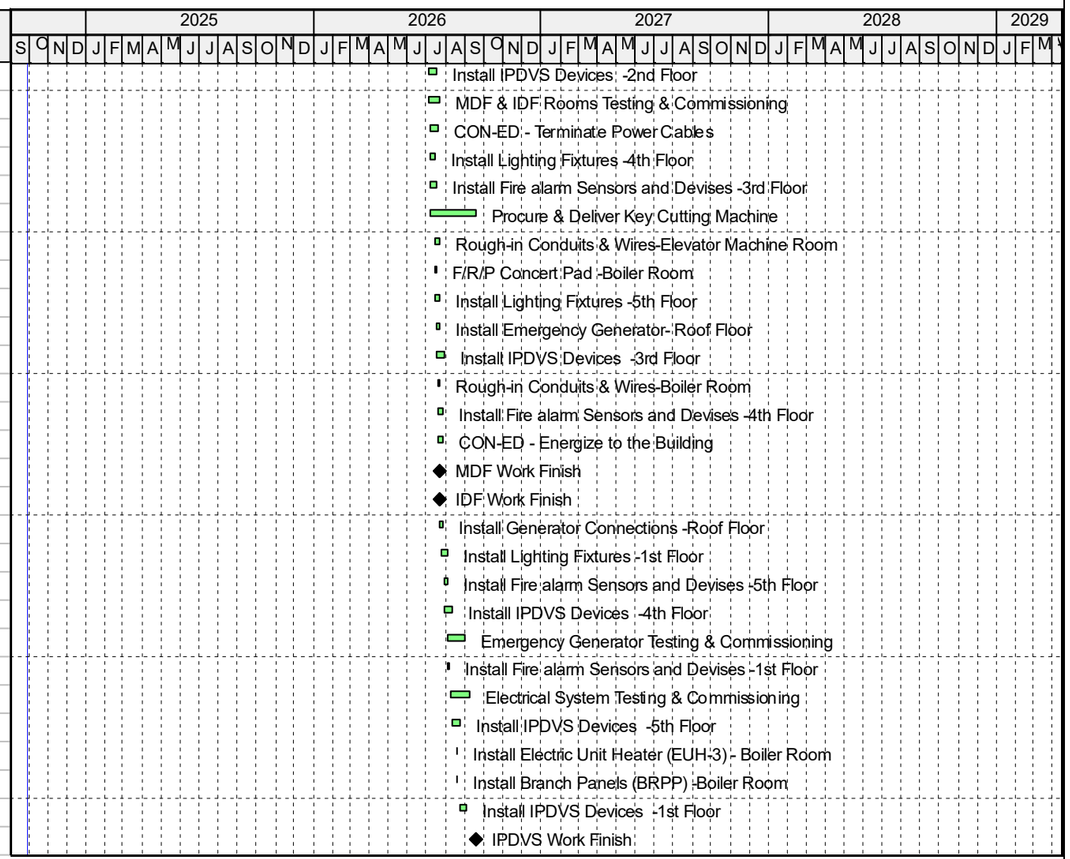

APPENDIX 8
Full Schedule Layout Grouped by RESP Code

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
SCA / Government		699	30-Sep-24	15-Aug-27
MIL-1000	NTP	0	30-Sep-24	
PRE-2590	Meeting With SCA to Review The Permit Requirements	14	30-Sep-24	18-Oct-24
MIL-2522	Site Access	365	30-Sep-24	29-Sep-25
APP-1000	Review & Approve Site Safety Plan	21	17-Oct-24	06-Nov-24
APP-1010	Review & Approve Foundation Product Data	21	22-Oct-24	11-Nov-24
APP-1020	Review & Approve Erosion Control and Sedimentation Plan	21	24-Oct-24	13-Nov-24
APP-1030	Review & Approve Existing Conditions Survey	21	29-Oct-24	18-Nov-24
APP-1040	Review & Approve Sustainable Materials	21	29-Oct-24	18-Nov-24
APP-1050	Review & Approve Site Furnishings Shop Drawings	21	05-Nov-24	25-Nov-24
APP-1060	Review & Approve Photo Submission - Temporary Fence	21	05-Nov-24	25-Nov-24
APP-1080	Review & Approve Electrical Equipment, Conduits, and Cables	21	13-Nov-24	03-Dec-24
APP-1090	Review & Approve Switch Gears Product Data	21	13-Nov-24	03-Dec-24
APP-1100	Review & Approve Concrete Reinforcement	21	27-Nov-24	17-Dec-24
APP-1110	Review & Approve Concrete Shop Drawings	21	27-Nov-24	17-Dec-24
APP-1130	Review & Approve QCP	21	27-Nov-24	17-Dec-24
APP-1140	Review & Approve Concrete Mix Design	21	27-Nov-24	17-Dec-24
APP-1150	Review & Approve Ductile Iron Pipes	21	07-Dec-24	27-Dec-24
APP-1160	Review & Approve Thermometers	21	12-Dec-24	01-Jan-25
APP-1170	Review & Approve Pressure Gages	21	12-Dec-24	01-Jan-25
APP-1180	Review & Approve Floor Drains	21	12-Dec-24	01-Jan-25
APP-1190	Review & Approve Hangers & Supports	21	12-Dec-24	01-Jan-25
APP-1200	Review & Approve SSDS Geotextile	21	12-Dec-24	01-Jan-25
APP-1230	Review & Approve Initial Underground Coordination Drawings	21	27-Dec-24	16-Jan-25
APP-1240	Review & Approve Baseline Schedule	21	31-Dec-24	20-Jan-25
APP-1250	Review & Approve Split Heat Pump System - SUB	21	11-Jan-25	31-Jan-25
APP-1260	Review & Approve Submittal Schedule	21	11-Jan-25	31-Jan-25
APP-1270	Review & Approve Acosutical Ceiling Tiles	21	11-Jan-25	31-Jan-25
APP-1280	Review & Approve Mechanical Piping	21	11-Jan-25	31-Jan-25
APP-1290	Review & Approve Unit Cabinet Heaters	21	11-Jan-25	31-Jan-25
APP-1210	Review & Approve Elevator Machine	21	29-Jan-25	18-Feb-25
APP-1120	Review & Approve Lighting Fixtures	21	29-Jan-25	18-Feb-25
APP-1780	Review & Approve Kitchen Equipment	21	29-Jan-25	18-Feb-25
APP-1310	Review & Approve Aluminum Projected Windows	21	29-Jan-25	18-Feb-25
APP-1220	Review & Approve Internet Protocol Digital Video Surveillance System using Digital Cameras	35	29-Jan-25	04-Mar-25
APP-1820	Review & Approve Chillers Product Data	21	29-Jan-25	18-Feb-25
APP-1300	Review & Approve Air Handling Units Product Data	21	29-Jan-25	18-Feb-25

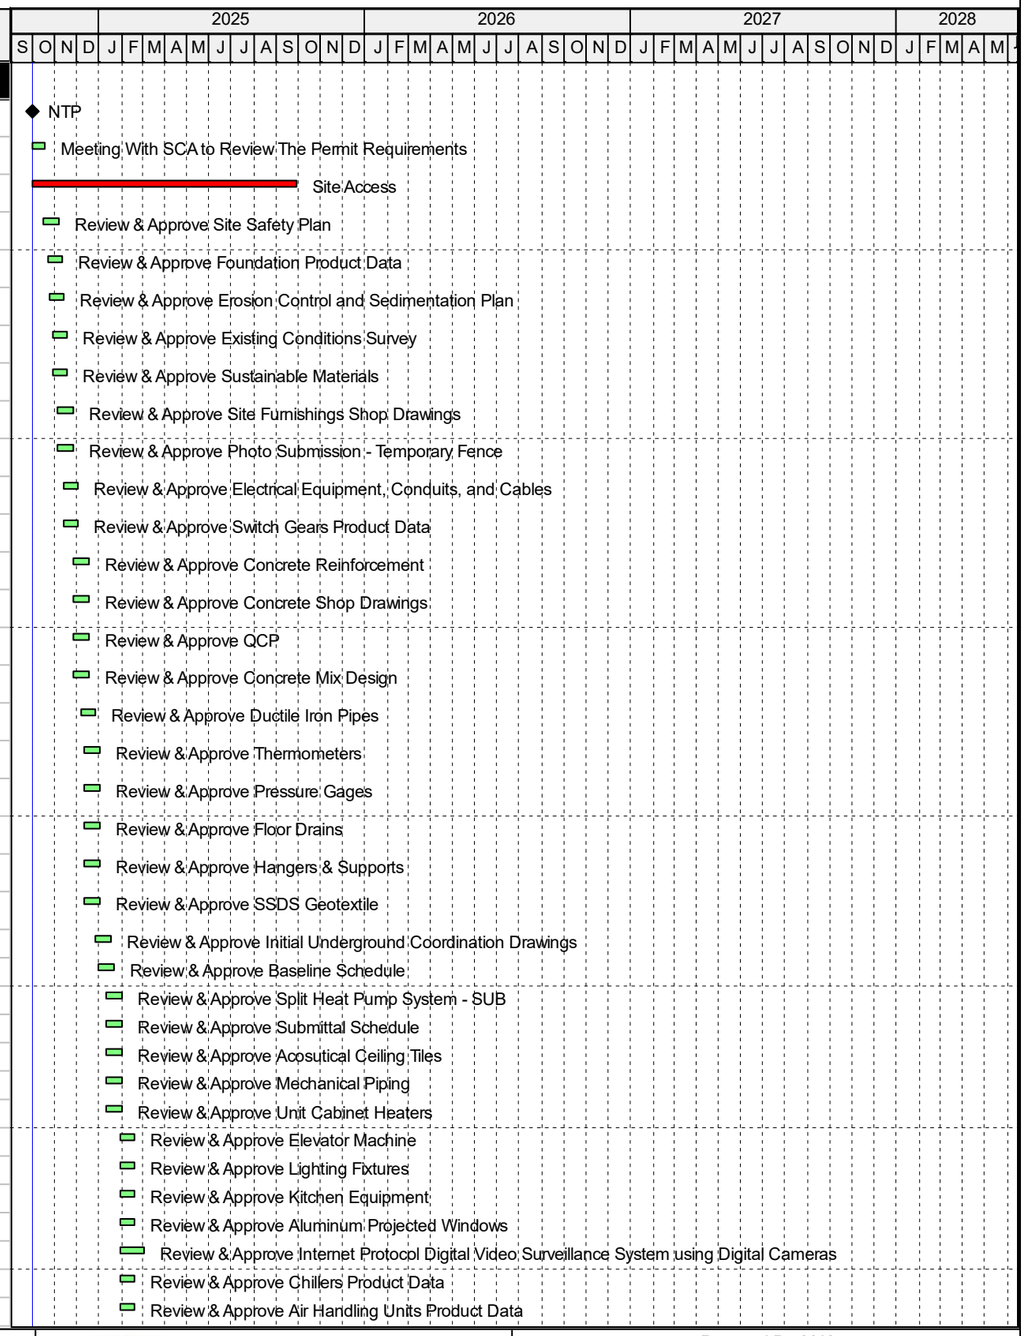

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1830	Review & Approve Boilers	21	29-Jan-25	18-Feb-25
APP-1070	Review & Approve Emergency Generator System Product Data	21	29-Jan-25	18-Feb-25
APP-1920	Review & Approve Precast Architectural Concrete	21	29-Jan-25	18-Feb-25
APP-1930	Review & Approve Unit Masonry Product Data	21	29-Jan-25	18-Feb-25
APP-1950	Review & Approve Structure Steel Drawings	21	29-Jan-25	18-Feb-25
APP-2200	Review & Approve Emergency Generator System Accessories	21	29-Jan-25	18-Feb-25
APP-2340	Review & Approve Tree Protection Plan	21	29-Jan-25	18-Feb-25
APP-3440	Review & Approve Detail of Gag for the Safety Relief Valves	21	29-Jan-25	18-Feb-25
APP-3450	Review & Approve Boiler Accessories Maintenance Data	21	29-Jan-25	18-Feb-25
APP-3760	Review & Approve Lighting Control Devices Shop Drawing	21	29-Jan-25	18-Feb-25
APP-3770	Review & Approve Lighting Control Devices Product Data	21	29-Jan-25	18-Feb-25
APP-3780	Review & Approve Lighting Control Devices Warranty	21	29-Jan-25	18-Feb-25
APP-1320	Review & Approve Stationary Metal Wall Louvers	21	31-Jan-25	20-Feb-25
APP-1330	Review & Approve Initial 1st Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1340	Review & Approve Initial 2nd Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1350	Review & Approve Initial 3rd Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1360	Review & Approve Initial 4th Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1370	Review & Approve Initial 5th Floor Coordination Drawings	21	04-Feb-25	24-Feb-25
APP-1380	Review & Approve Fire & Jockey Pumps	21	12-Feb-25	04-Mar-25
APP-1390	Review & Approve Interior Signage Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1400	Review & Approve Ceramic Tiles Product Data	21	12-Feb-25	04-Mar-25
APP-1410	Review & Approve Door Hardware Submittal	21	12-Feb-25	04-Mar-25
APP-1420	Review & Approve Painting	21	12-Feb-25	04-Mar-25
APP-1430	Review & Approve Door & Frame Corners Samples	21	12-Feb-25	04-Mar-25
APP-1440	Review & Approve Roof Drains & Clean Outs	21	12-Feb-25	04-Mar-25
APP-1450	Review & Approve Flashing & Sheet Metal Shop Drawing	21	12-Feb-25	04-Mar-25
APP-1460	Review & Approve Roofing Membrane Product Data	21	12-Feb-25	04-Mar-25
APP-1470	Review & Approve Perimeter Foundation Insulation Product Data	21	12-Feb-25	04-Mar-25
APP-1480	Review & Approve Crystalline Waterproofing Product Data	21	12-Feb-25	04-Mar-25
APP-1490	Review & Approve Suspension Assembly Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1500	Review & Approve Certification of Material	21	12-Feb-25	04-Mar-25
APP-1510	Review & Approve Formwork Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1520	Review & Approve Planting Schedule	21	12-Feb-25	04-Mar-25
APP-1530	Review & Approve Playgroung Equipment Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1540	Review & Approve Catch Basin Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1550	Review & Approve Concrete Curbs & Pavements Shop Drawing	21	12-Feb-25	04-Mar-25
APP-1560	Review & Approve Steel Curb Facing Shop Drawing	21	12-Feb-25	04-Mar-25
APP-1570	Review & Approve Asphaltic Concrete Paving	21	12-Feb-25	04-Mar-25
APP-1580	Review & Approve Gas Vapor Barrier Submittal & Inspection Schedule	21	12-Feb-25	04-Mar-25
APP-1590	Review & Approve Training Outline & Schedule	21	12-Feb-25	04-Mar-25
APP-1600	Review & Approve Temporary Ventilation Plan	21	12-Feb-25	04-Mar-25
APP-1610	Review & Approve Construction Indoor Air Quality Management Plan	21	12-Feb-25	04-Mar-25
APP-1620	Review & Approve CWM Plan	21	12-Feb-25	04-Mar-25
APP-1630	Review & Approve Heating Plan	21	12-Feb-25	04-Mar-25

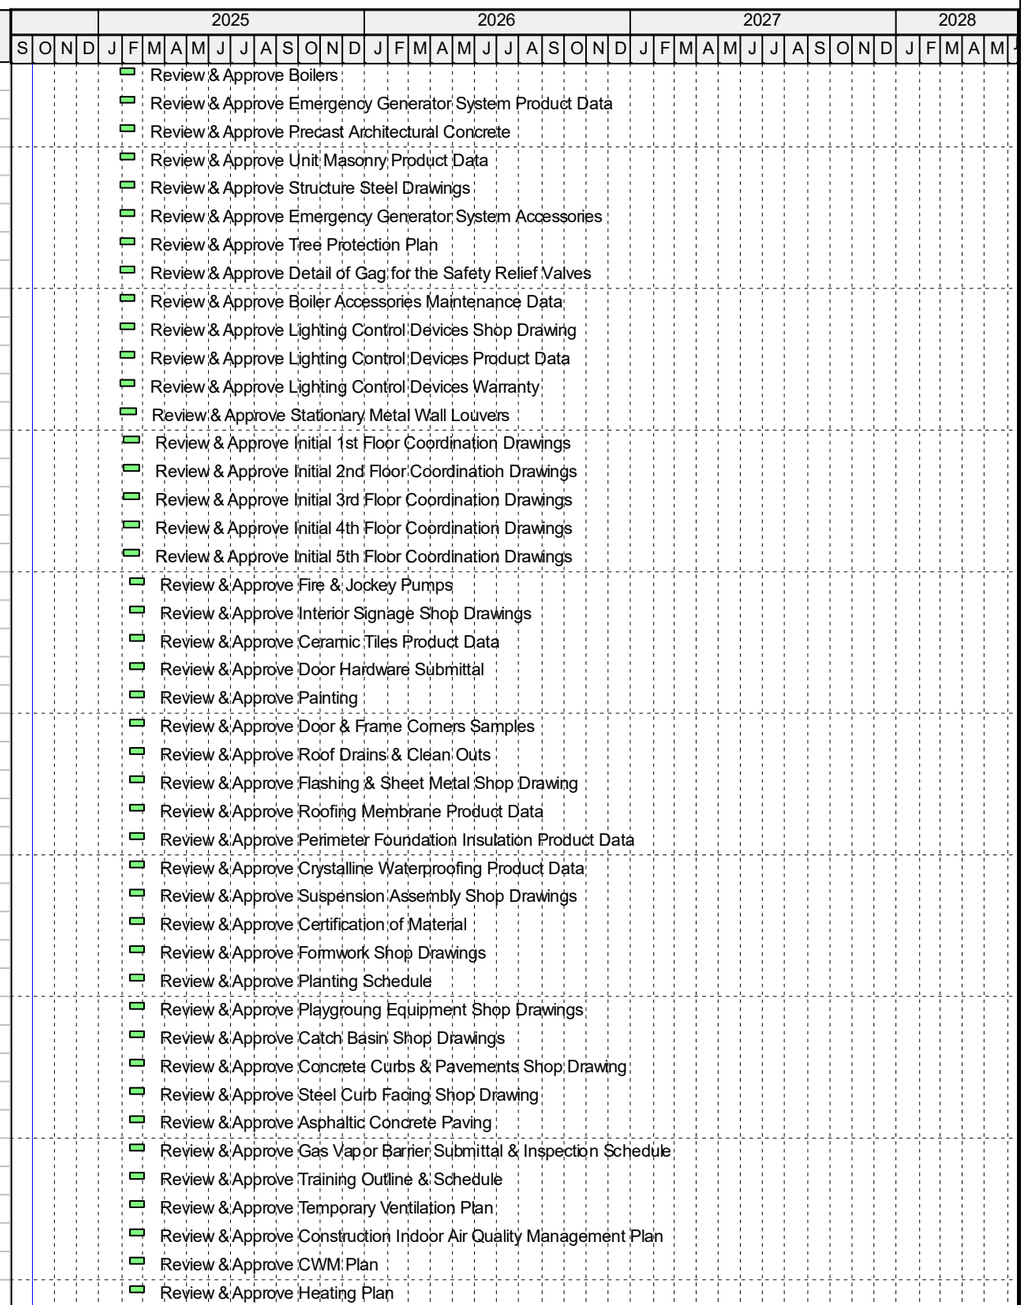

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
APP-1640	Review & Approve Sample Classroom Materials	21	12-Feb-25	04-Mar-25
APP-1650	Review & Approve Electrical Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1660	Review & Approve Plumbing Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1670	Review & Approve Sprinkler System Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1680	Review & Approve Gypsum Board	21	12-Feb-25	04-Mar-25
APP-1690	Review & Approve Floorings	21	12-Feb-25	04-Mar-25
APP-1700	Review & Approve Toilet Accessories	21	12-Feb-25	04-Mar-25
APP-1710	Review & Approve Millwork	21	12-Feb-25	04-Mar-25
APP-1720	Review & Approve Furniture	21	12-Feb-25	04-Mar-25
APP-1730	Review & Approve Mechanical Ducts	21	12-Feb-25	04-Mar-25
APP-1740	Review & Approve Plumbing Fixtures	21	12-Feb-25	04-Mar-25
APP-1750	Review & Approve Wood Doors	21	12-Feb-25	04-Mar-25
APP-1760	Review & Approve Fire Protection Shop Drawings	21	12-Feb-25	04-Mar-25
APP-1770	Review & Approve Fire Detectors & Alarms	21	12-Feb-25	04-Mar-25
APP-1790	Review & Approve Signs	21	12-Feb-25	04-Mar-25
APP-1800	Review & Approve Telecommunication System Drawings	21	12-Feb-25	04-Mar-25
APP-1840	Review & Approve Gymnasium Equipment	21	12-Feb-25	04-Mar-25
APP-1850	Review & Approve Supplemental Comissioning Requirements	21	12-Feb-25	04-Mar-25
APP-1860	Review & Approve Record Documents	21	12-Feb-25	04-Mar-25
APP-1870	Review & Approve Environmental Site Assessment Reports	21	12-Feb-25	04-Mar-25
APP-1880	Review & Approve Selective Removals & Demoloition	21	12-Feb-25	04-Mar-25
APP-1890	Review & Approve Trench Drains Prodcut Data	21	12-Feb-25	04-Mar-25
APP-1900	Review & Approve Chain Link Fences & Gates Drawings	21	12-Feb-25	04-Mar-25
APP-1910	Review & Approve Outdoor Game Equipment	21	12-Feb-25	04-Mar-25
APP-1940	Review & Approve Cast Stone Product Data	21	12-Feb-25	04-Mar-25
APP-1960	Review & Approve Metal Deck Product Data	21	12-Feb-25	04-Mar-25
APP-1970	Review & Approve Prefabricated Expansion Joint Covers	21	12-Feb-25	04-Mar-25
APP-1980	Review & Approve Self Adhering Sheet Air Barriers	21	12-Feb-25	04-Mar-25
APP-1990	Review & Approve Metal Plate Wall Panels	21	12-Feb-25	04-Mar-25
APP-2000	Review & Approve Security Screens & Barriers	21	12-Feb-25	04-Mar-25
APP-2010	Review & Approve Wood Flooring	21	12-Feb-25	04-Mar-25
APP-2020	Review & Approve Visual Display Boards	21	12-Feb-25	04-Mar-25
APP-2030	Review & Approve Metal Lockers	21	12-Feb-25	04-Mar-25
APP-2040	Review & Approve Fire Extinguishers & Cabinets	21	12-Feb-25	04-Mar-25
APP-2050	Review & Approve Library Equipment	21	12-Feb-25	04-Mar-25
APP-2060	Review & Approve Platform Curtains & Auditorium Window Curtains	21	12-Feb-25	04-Mar-25
APP-2070	Review & Approve Waste Handling Equipment	21	12-Feb-25	04-Mar-25
APP-2080	Review & Approve Domestic Equipment	21	12-Feb-25	04-Mar-25
APP-2090	Review & Approve Laboratory Equipment	21	12-Feb-25	04-Mar-25
APP-2100	Review & Approve Manufactured Wood Casework	21	12-Feb-25	04-Mar-25
APP-2110	Review & Approve Concrete Floating Floor Assembly	21	12-Feb-25	04-Mar-25
APP-2120	Review & Approve Hydraulic Vertical Wheelchair Lifts	21	12-Feb-25	04-Mar-25
APP-2130	Review & Approve Switch & Panel Boards	21	12-Feb-25	04-Mar-25
APP-2140	Review & Approve Auditorium & Television Studio Dimming System Product Data	21	12-Feb-25	04-Mar-25

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
APP-2150	Review & Approve Overcurrent Protective Devices Data	21	12-Feb-25	04-Mar-25
APP-2160	Review & Approve Gas Pipes	21	12-Feb-25	04-Mar-25
APP-2170	Review & Approve Water Heaters	21	12-Feb-25	04-Mar-25
APP-2180	Review & Approve Pumping Apparatus & Tanks	21	12-Feb-25	04-Mar-25
APP-2190	Review & Approve HVAC Pumps	21	12-Feb-25	04-Mar-25
APP-2210	Review & Approve Fuel Storage Equipment	21	12-Feb-25	04-Mar-25
APP-2220	Review & Approve Natural Gas Leak Detection Equipment	21	12-Feb-25	04-Mar-25
APP-2240	Review & Approve Temperature Control System	21	12-Feb-25	04-Mar-25
APP-2250	Review & Approve Air Outlets & Inlets	21	12-Feb-25	04-Mar-25
APP-2360	Review & Approve Adjacent Property and Structures Protection & Monitoring Plan	21	12-Feb-25	04-Mar-25
APP-2370	Review & Approve Ornamenta Metal Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2920	Review & Approve Documentation of Proper Disposal	21	12-Feb-25	04-Mar-25
APP-2930	Review & Approve Ornamenta Metal Product Data	21	12-Feb-25	04-Mar-25
APP-2960	Review & Approve Coiling Doors, Grilles and Shutters Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2970	Review & Approve Coiling Doors, Grilles and ShuttersProduct Data	21	12-Feb-25	04-Mar-25
APP-2980	Review & Approve Aluminum Framed Entrances & Storefronts Shop Drawings	21	12-Feb-25	04-Mar-25
APP-2990	Review & Approve Aluminum Framed Entrances & Storefronts Product Data	21	12-Feb-25	04-Mar-25
APP-3000	Review & Approve Thresholds, Weatherstripping and Seals Color Samples	21	12-Feb-25	04-Mar-25
APP-3010	Review & Approve Thresholds, Weatherstripping and Seals Product Data	21	12-Feb-25	04-Mar-25
APP-3020	Review & Approve Miscellaneous Glazing Samples	21	12-Feb-25	04-Mar-25
APP-3030	Review & Approve Miscellaneous Glazing Product Data	21	12-Feb-25	04-Mar-25
APP-3040	Review & Approve Fire Rated Glazing Samples	21	12-Feb-25	04-Mar-25
APP-3050	Review & Approve Fire Rated Glazing Product Data	21	12-Feb-25	04-Mar-25
APP-3060	Review & Approve Graffiti Resistant Coating Product Data	21	12-Feb-25	04-Mar-25
APP-3070	Review & Approve Special Coating Samples	21	12-Feb-25	04-Mar-25
APP-3080	Review & Approve Special Coating Product Data	21	12-Feb-25	04-Mar-25
APP-3090	Review & Approve Flagpole Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3100	Review & Approve Flagpole Product Data	21	12-Feb-25	04-Mar-25
APP-3110	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals	21	12-Feb-25	04-Mar-25
APP-3120	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	21	12-Feb-25	04-Mar-25
APP-3130	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	21	12-Feb-25	04-Mar-25
APP-3140	Review & Approve Wire Mesh Work Samples	21	12-Feb-25	04-Mar-25
APP-3150	Review & Approve Miscellaneous Glazing Shop drawings	21	12-Feb-25	04-Mar-25
APP-3160	Review & Approve Metal Storage Shelving Samples	21	12-Feb-25	04-Mar-25
APP-3170	Review & Approve Metal Storage Shelving Shop drawings	21	12-Feb-25	04-Mar-25
APP-3180	Review & Approve Mirrors Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3190	Review & Approve Mirrors Product Data	21	12-Feb-25	04-Mar-25
APP-3200	Review & Approve Mirrors Mastic Compatibility Test Reports & Certifications	21	12-Feb-25	04-Mar-25
APP-3210	Review & Approve Grab Bars Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3220	Review & Approve Grab Bars Product Data	21	12-Feb-25	04-Mar-25
APP-3230	Review & Approve Shop Equipment Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3240	Review & Approve Shop Equipment Product Data	21	12-Feb-25	04-Mar-25
APP-3250	Review & Approve Bleachers Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3260	Review & Approve Bleachers Product Data	21	12-Feb-25	04-Mar-25

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
APP-3270	Review & Approve Bleachers Manufacturer's Warranty	21	12-Feb-25	04-Mar-25
APP-3280	Review & Approve Valves Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3290	Review & Approve Valves Product Data	21	12-Feb-25	04-Mar-25
APP-3300	Review & Approve Certification of Tests	21	12-Feb-25	04-Mar-25
APP-3310	Review & Approve Domestic Water Sterilization Plan	21	12-Feb-25	04-Mar-25
APP-3320	Review & Approve Tags, Charts & Identifications Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3330	Review & Approve Tags, Charts & Identifications Product Data	21	12-Feb-25	04-Mar-25
APP-3340	Review & Approve Micselianeous Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3350	Review & Approve Valves (HVAC) Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3360	Review & Approve Valves (HVAC) Product Data	21	12-Feb-25	04-Mar-25
APP-3370	Review & Approve Piping Insulation Schedule Listing Items	21	12-Feb-25	04-Mar-25
APP-3380	Review & Approve chedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	21	12-Feb-25	04-Mar-25
APP-3390	Review & Approve chedules Showing Manfacturers's Product Number Duct Work Insulation	21	12-Feb-25	04-Mar-25
APP-3400	Review & Approve Hydronic Specialities Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3410	Review & Approve Hydronic Specialities Product Data	21	12-Feb-25	04-Mar-25
APP-3420	Review & Approve Water Treatment Firm	21	12-Feb-25	04-Mar-25
APP-3430	Review & Approve Chemical Products Product Data	21	12-Feb-25	04-Mar-25
APP-3460	Review & Approve Breeching Chimney Connectors and Chimneys Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3470	Review & Approve Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	21	12-Feb-25	04-Mar-25
APP-3480	Review & Approve Plate Heat Exchanger Maintenance Data	21	12-Feb-25	04-Mar-25
APP-3490	Review & Approve Plate Heat Exchanger Product Data	21	12-Feb-25	04-Mar-25
APP-3500	Review & Approve Coils Maintenance Data	21	12-Feb-25	04-Mar-25
APP-3510	Review & Approve Coils Certifications	21	12-Feb-25	04-Mar-25
APP-3520	Review & Approve Convectors Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3530	Review & Approve Convectors Product Data	21	12-Feb-25	04-Mar-25
APP-3540	Review & Approve Fan Coils Units Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3550	Review & Approve Fan Coils Units Shop Drawings	21	12-Feb-25	04-Mar-25
APP-3560	Review & Approve Door Air Curtains Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3570	Review & Approve Door Air Curtains Product Data	21	12-Feb-25	04-Mar-25
APP-3580	Review & Approve Centrifugal Fans Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3590	Review & Approve Centrifugal Fans Product Data	21	12-Feb-25	04-Mar-25
APP-3600	Review & Approve Centrifugal Fans Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3610	Review & Approve Air Filters Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3620	Review & Approve Air Filters Product Data	21	12-Feb-25	04-Mar-25
APP-3630	Review & Approve Air Filters Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3640	Review & Approve Duct Accessories Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3650	Review & Approve Damper Assemblies Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3660	Review & Approve Damper Assemblies Product Data	21	12-Feb-25	04-Mar-25
APP-3670	Review & Approve Damper Assemblies Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3680	Review & Approve Variable Air Terminals Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3690	Review & Approve Variable Air Terminals Product Data	21	12-Feb-25	04-Mar-25
APP-3700	Review & Approve Variable Air Terminals Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3710	Review & Approve AHU for Public Assemblies Sapces Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3720	Review & Approve AHU for Public Assemblies Sapces Product Data	21	12-Feb-25	04-Mar-25

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
APP-3730	Review & Approve AHU for Public Assemblies Sapces Maintenance Data & Materials	21	12-Feb-25	04-Mar-25
APP-3740	Review & Approve Control Systems Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3750	Review & Approve Truck Network Cable Schematic Diagram	21	12-Feb-25	04-Mar-25
APP-3790	Review & Approve Surge Protective Devices Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3800	Review & Approve Surge Protective Devices Product Data	21	12-Feb-25	04-Mar-25
APP-3810	Review & Approve Surge Protective Devices Warranty	21	12-Feb-25	04-Mar-25
APP-3820	Review & Approve Service Entrance Equipment Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3830	Review & Approve Service Entrance Equipment Product Data	21	12-Feb-25	04-Mar-25
APP-3840	Review & Approve Service Entrance Equipment Warranty	21	12-Feb-25	04-Mar-25
APP-3850	Review & Approve Enclosed Switches Product Data	21	12-Feb-25	04-Mar-25
APP-3860	Review & Approve Enclosed Switches Test Reports	21	12-Feb-25	04-Mar-25
APP-3870	Review & Approve Motors, Motor Control Centers and Starters Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3880	Review & Approve Motors, Motor Control Centers and Starters Product Data	21	12-Feb-25	04-Mar-25
APP-3890	Review & Approve Motors, Motor Control Centers and Starters Field Test Reports	21	12-Feb-25	04-Mar-25
APP-3900	Review & Approve Lightning Protection Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3920	Review & Approve Lightning Protection Test Reports	21	12-Feb-25	04-Mar-25
APP-3930	Review & Approve Fiber Optic Cabling system Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3940	Review & Approve Fiber Optic Cabling system Product Data	21	12-Feb-25	04-Mar-25
APP-3950	Review & Approve Fiber Optic Cabling system Samples	21	12-Feb-25	04-Mar-25
APP-3960	Review & Approve Sound, Intercome & Security System Shop Drawing	21	12-Feb-25	04-Mar-25
APP-3970	Review & Approve Sound, Intercome & Security System Programming Code and Password for the System	21	12-Feb-25	04-Mar-25
APP-3980	Review & Approve Sound, Intercome & Security System warranty	21	12-Feb-25	04-Mar-25
APP-3990	Review & Approve Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	21	12-Feb-25	04-Mar-25
APP-4000	Review & Approve Projection and Interactive Whiteboard Systems Wiring diagram	21	12-Feb-25	04-Mar-25
APP-4010	Review & Approve Self Corrective Clock System Shop Drawing	21	12-Feb-25	04-Mar-25
APP-4020	Review & Approve Self Corrective Clock System Product Data	21	12-Feb-25	04-Mar-25
APP-4030	Review & Approve Self Corrective Clock System Field Test Reports	21	12-Feb-25	04-Mar-25
APP-4040	Review & Approve Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	21	12-Feb-25	04-Mar-25
APP-4060	Review & Approve Steel Stairs Shop Drawings	21	12-Feb-25	04-Mar-25
APP-4070	Review & Approve Steel Stairs Product Data	21	12-Feb-25	04-Mar-25
APP-4080	Review & Approve Green School Submittal	21	12-Feb-25	04-Mar-25
APP-2260	Review & Approve Product Substitutions	21	13-Feb-25	05-Mar-25
APP-2270	Review & Approve Final Foundations Coordination Drawings	21	12-Mar-25	01-Apr-25
APP-2280	Review & Approve Final 1st Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2290	Review & Approve Final 2nd Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2300	Review & Approve Final 3rd Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2310	Review & Approve Final 4th Floor Coordination Drawings	21	03-May-25	23-May-25
APP-2320	Review & Approve Final 5th Floor Coordination Drawings	21	03-May-25	23-May-25
APP-1810	Review & Approve Roof Dunnage	21	28-Jun-25	18-Jul-25
APP-2900	Review & Approve Excavated Material Disposal Plan	21	06-Sep-25	26-Sep-25
APP-4050	Review & Approve Soil Sampling Plan	21	06-Sep-25	26-Sep-25
MIL-2832	Issuance of Excavation & Shoring Permit	0		29-Sep-25
MIL-2842	Issuance of Builders Pavement Permit	0		29-Sep-25
MIL-2852	Issuance of Permit to Enter (PTE)	0		29-Sep-25

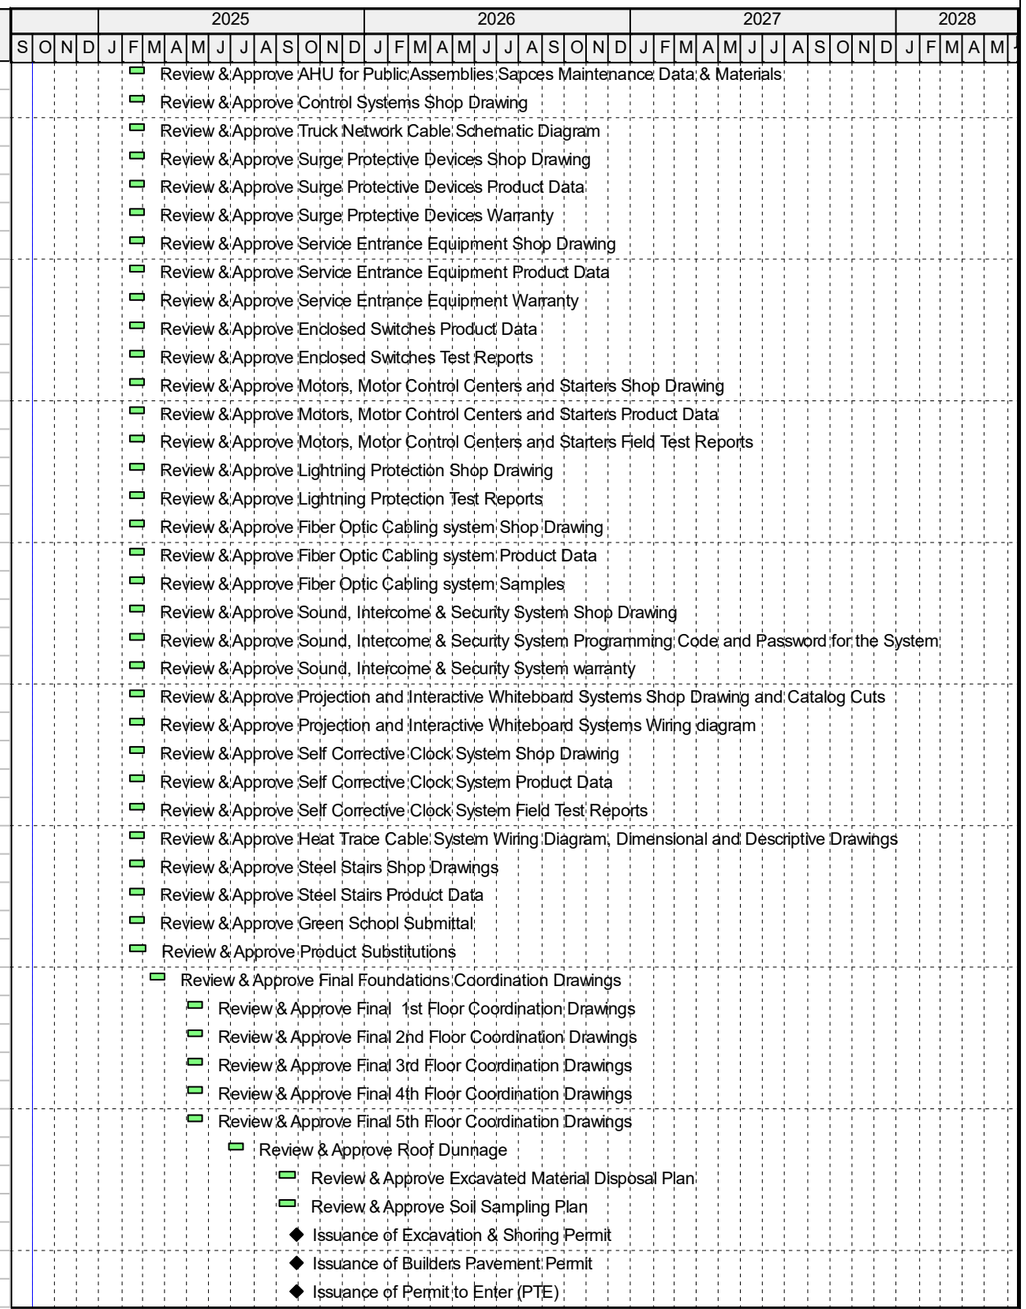

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
MIL-2862	Issuance of NYPA Permit	0		29-Sep-25
MIL-2872	Issuance of Construction Fences Permit	0		29-Sep-25
MIL-2882	Issuance of Sidewalk Shed Permits	0		29-Sep-25
MIL-2892	Issuance of CCD1	0		29-Sep-25
MIL-2902	Issuance of DOB Permit & Insurance	0		29-Sep-25
APP-2910	Review & Approve Backfill & Resue Plan	21	04-Oct-25	24-Oct-25
PRE-2620	Review & Approve FDNY Fuel Permit	21	21-Oct-25	10-Nov-25
I-1140	Structural Steel Inspection	58	05-Dec-25	02-Mar-26
I-1080	Standpipe System Inspection	111	29-Dec-25	05-Jun-26
MIL-2622	Deliveries of all owner-furnished equipment and/or materials	0		06-Feb-26
I-1020	Masonry Inspection	32	02-Mar-26	14-Apr-26
CON-1990	Approve Insulated Precast Concrete Sandwich Panel - Mock Up	2	09-Mar-26	10-Mar-26
CON-2210	Approve Windows Mock-Up	2	16-Mar-26	17-Mar-26
CON-2240	Approve Storefront System Mock-Up	2	23-Mar-26	24-Mar-26
I-1120	Mechanical System Inspection	69	07-Apr-26	15-Jul-26
CON-3300	Approve Fluid-Applied Protected Membrane Mock-Up	4	15-Apr-26	20-Apr-26
I-1040	Roofing Flood Testing Inspection	5	30-Apr-26	06-May-26
CON-5000	Mockup Room Inspection & Punchlist	5	27-May-26	02-Jun-26
I-1130	Fire Alarm Inspection	47	28-May-26	04-Aug-26
CON-9030	Install Furniture & Milling Work (Owner Provided & Installed) -2nd Floor	5	14-Jul-26	20-Jul-26
CON-9040	Install Furniture & Milling Work (Owner Provided & Installed) -3rd Floor	5	22-Jul-26	28-Jul-26
APP-2330	Review & Approve Remedial Closure Report	21	30-Jul-26	19-Aug-26
CON-9050	Install Furniture & Milling Work (Owner Provided & Installed) -4th Floor	5	30-Jul-26	05-Aug-26
CLO-1190	Pre-Elevator Test Inspection	5	05-Aug-26	11-Aug-26
CON-9060	Install Furniture & Milling Work (Owner Provided & Installed) -5th Floor	4	21-Aug-26	26-Aug-26
CON-9020	Install Furniture & Milling Work (Owner Provided & Installed) -1st Floor	3	31-Aug-26	02-Sep-26
CLO-1170	Sprinkler/Domestic Booster Pumps Inspection	3	10-Sep-26	14-Sep-26
CLO-1200	Elevator DOB Inspection	5	10-Sep-26	16-Sep-26
CLO-1150	FDNY Inspection	12	15-Sep-26	30-Sep-26
CLO-1040	Pre-TCO Inspection	11	18-Sep-26	02-Oct-26
MIL-1650	FDNY Inspection Finish	0		30-Sep-26
MIL-1510	TCO	0		19-Oct-26*
MIL-1550	Substantial Completion	0		17-Apr-27*
CLO-1080	Final Inspection	5	16-Jul-27	22-Jul-27
MIL-1560	Final Completion	0		15-Aug-27*
Navillus		699	30-Sep-24	15-Aug-27
MIL-1030	Project Duration(From NTP till TCO)	750	30-Sep-24	19-Oct-26
MIL-1040	Project Duration(From NTP till Substantial Completion)	930	30-Sep-24	17-Apr-27
PRE-2600	Prepare & Submit Permit Waiver Requests to SCA Chief Project Officer	5	30-Sep-24	04-Oct-24
MIL-1770	Project Duration(From NTP till Final Completion)	1050	30-Sep-24	15-Aug-27
CON-99257	Subcontractor Buyout	10	30-Sep-24	11-Oct-24
MIL-2542	Complete Subcontractor 'Buyout'	0		11-Oct-24
SUB-1000	Prepare & Submit Split Heat Pump System - SUB	60	15-Oct-24	10-Jan-25
SUB-1010	Prepare & Submit Thermometers	40	15-Oct-24	11-Dec-24

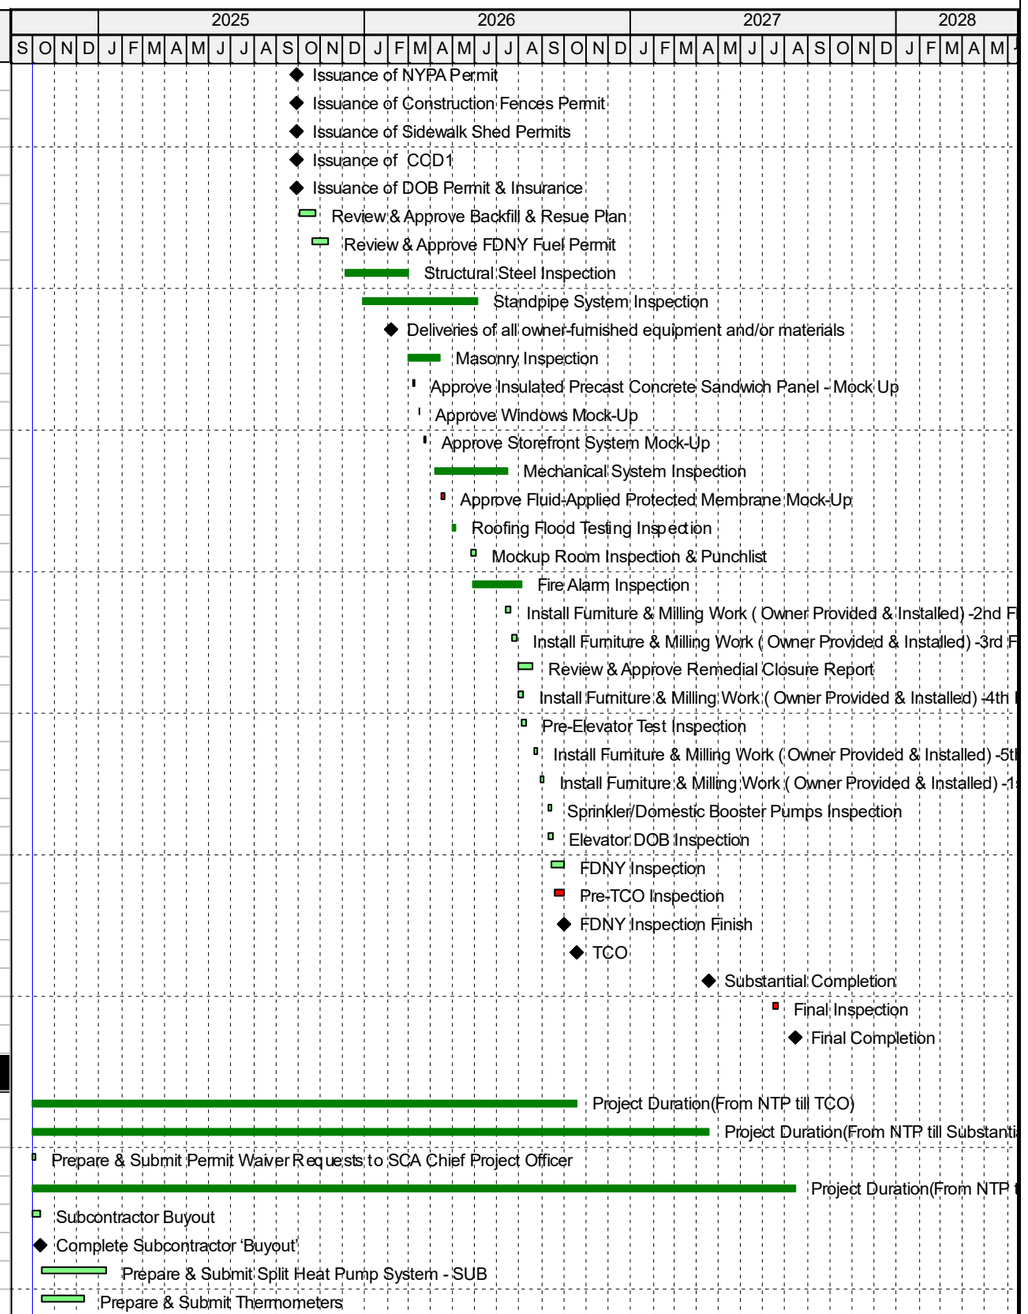

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1020	Prepare & Submit Pressure Gages	40	15-Oct-24	11-Dec-24
SUB-1030	Prepare & Submit Floor Drains	40	15-Oct-24	11-Dec-24
SUB-1040	Prepare & Submit Hangers & Supports	40	15-Oct-24	11-Dec-24
SUB-1050	Prepare & Submit Fire & Jockey Pumps	81	15-Oct-24	11-Feb-25
SUB-1060	Prepare & Submit Interior Signage Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1070	Prepare & Submit Ceramic Tiles Product Data	81	15-Oct-24	11-Feb-25
SUB-1080	Prepare & Submit Door Hardware Submittal	81	15-Oct-24	11-Feb-25
SUB-1090	Prepare & Submit Painting	81	15-Oct-24	11-Feb-25
SUB-1100	Prepare & Submit Door & Frame Corners Samples	81	15-Oct-24	11-Feb-25
SUB-1110	Prepare & Submit Roof Drains & Clean Outs	81	15-Oct-24	11-Feb-25
SUB-1120	Prepare & Submit Flashing & Sheet Metal Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-1130	Prepare & Submit Roofing Membrane Product Data	81	15-Oct-24	11-Feb-25
SUB-1140	Prepare & Submit Perimeter Foundation Insulation Product Data	81	15-Oct-24	11-Feb-25
SUB-1150	Prepare & Submit Crystalline Waterproofing Product Data	81	15-Oct-24	11-Feb-25
SUB-1160	Prepare & Submit Suspension Assembly Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1170	Prepare & Submit Certification of Material	81	15-Oct-24	11-Feb-25
SUB-1180	Prepare & Submit Concrete Reinforcement	30	15-Oct-24	26-Nov-24
SUB-1190	Prepare & Submit Formwork Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1200	Prepare & Submit Planting Schedule	81	15-Oct-24	11-Feb-25
SUB-1210	Prepare & Submit Site Furnishings Shop Drawings	15	15-Oct-24	04-Nov-24
SUB-1220	Prepare & Submit Playgroung Equipment Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1230	Prepare & Submit Ductile Iron Pipes	37	15-Oct-24	06-Dec-24
SUB-1240	Prepare & Submit Catch Basin Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1250	Prepare & Submit Concrete Curbs & Pavements Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-1260	Prepare & Submit Steel Curb Facing Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-1270	Prepare & Submit Asphaltic Concrete Paving	81	15-Oct-24	11-Feb-25
SUB-1280	Prepare & Submit SSDS Geotextile	40	15-Oct-24	11-Dec-24
SUB-1290	Prepare & Submit Gas Vapor Barrier Submittal & Inspection Schedule	81	15-Oct-24	11-Feb-25
SUB-1300	Prepare & Submit Existing Conditions Survey	10	15-Oct-24	28-Oct-24
SUB-1310	Prepare & Submit Training Outline & Schedule	81	15-Oct-24	11-Feb-25
SUB-1320	Prepare & Submit Product Substitutions	82	15-Oct-24	12-Feb-25
SUB-1330	Prepare & Submit Temporary Ventilation Plan	81	15-Oct-24	11-Feb-25
SUB-1340	Prepare & Submit Construction Indoor Air Quality Management Plan	81	15-Oct-24	11-Feb-25
SUB-1350	Prepare & Submit Site Safety Plan	2	15-Oct-24	16-Oct-24
SUB-1360	Prepare & Submit CWM Plan	81	15-Oct-24	11-Feb-25
SUB-1370	Prepare & Submit Photo Submission - Temporary Fence	15	15-Oct-24	04-Nov-24
SUB-1380	Prepare & Submit Heating Plan	81	15-Oct-24	11-Feb-25
SUB-1390	Prepare & Submit Sample Classroom Materials	81	15-Oct-24	11-Feb-25
SUB-1400	Prepare & Submit Sustainable Materials	10	15-Oct-24	28-Oct-24
SUB-1410	Prepare & Submit Submittal Schedule	60	15-Oct-24	10-Jan-25
SUB-1420	Prepare & Submit Electrical Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1430	Prepare & Submit Plumbing Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1440	Prepare & Submit Sprinkler System Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1450	Prepare & Submit Concrete Shop Drawings	30	15-Oct-24	26-Nov-24

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1460	Prepare & Submit Elevator Machine	71	15-Oct-24	28-Jan-25
SUB-1470	Prepare & Submit Gypsum Board	81	15-Oct-24	11-Feb-25
SUB-1480	Prepare & Submit Floorings	81	15-Oct-24	11-Feb-25
SUB-1490	Prepare & Submit Acosutical Ceiling Tiles	60	15-Oct-24	10-Jan-25
SUB-1500	Prepare & Submit Toilet Accessories	81	15-Oct-24	11-Feb-25
SUB-1510	Prepare & Submit Millwork	81	15-Oct-24	11-Feb-25
SUB-1520	Prepare & Submit Lighting Fixtures	71	15-Oct-24	28-Jan-25
SUB-1530	Prepare & Submit Furniture	81	15-Oct-24	11-Feb-25
SUB-1540	Prepare & Submit Mechanical Ducts	81	15-Oct-24	11-Feb-25
SUB-1550	Prepare & Submit Mechanical Piping	60	15-Oct-24	10-Jan-25
SUB-1560	Prepare & Submit Erosion Control and Sedimentation Plan	7	15-Oct-24	23-Oct-24
SUB-1570	Prepare & Submit QCP	30	15-Oct-24	26-Nov-24
SUB-1580	Prepare & Submit Concrete Mix Design	30	15-Oct-24	26-Nov-24
SUB-1590	Prepare & Submit Electrical Equipment, Conduits, and Cables	20	15-Oct-24	12-Nov-24
SUB-1600	Prepare & Submit Plumbing Fixtures	81	15-Oct-24	11-Feb-25
SUB-1610	Prepare & Submit Baseline Schedule	52	15-Oct-24	30-Dec-24
SUB-1620	Prepare & Submit Wood Doors	81	15-Oct-24	11-Feb-25
SUB-1630	Prepare & Submit Fire Protection Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1640	Prepare & Submit Fire Detectors & Alarms	81	15-Oct-24	11-Feb-25
SUB-1650	Prepare & Submit Kitchen Equipment	71	15-Oct-24	28-Jan-25
SUB-1660	Prepare & Submit Signs	81	15-Oct-24	11-Feb-25
SUB-1670	Prepare & Submit Aluminum Projected Windows	71	15-Oct-24	28-Jan-25
SUB-1680	Prepare & Submit Telecommunication System Drawings	81	15-Oct-24	11-Feb-25
SUB-1690	Prepare & Submit Internet Protocol Digital Video Surveillance System using Digital Cameras	71	15-Oct-24	28-Jan-25
SUB-1710	Prepare & Submit Chillers Product Data	71	15-Oct-24	28-Jan-25
SUB-1720	Prepare & Submit Air Handling Units Product Data	71	15-Oct-24	28-Jan-25
SUB-1730	Prepare & Submit Boilers	71	15-Oct-24	28-Jan-25
SUB-1740	Prepare & Submit Emergency Generator System Product Data	71	15-Oct-24	28-Jan-25
SUB-1750	Prepare & Submit Switch Gears Product Data	20	15-Oct-24	12-Nov-24
SUB-1760	Prepare & Submit Unit Cabinet Heaters	60	15-Oct-24	10-Jan-25
SUB-1770	Prepare & Submit Gymnasium Equipment	81	15-Oct-24	11-Feb-25
SUB-1780	Prepare & Submit Initial Underground Coordination Drawings	50	15-Oct-24	26-Dec-24
SUB-1790	Prepare & Submit Initial 1st Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1800	Prepare & Submit Initial 2nd Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1810	Prepare & Submit Initial 3rd Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1820	Prepare & Submit Initial 4th Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1830	Prepare & Submit Initial 5th Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1840	Prepare & Submit Supplemental Comissioning Requirements	81	15-Oct-24	11-Feb-25
SUB-1850	Prepare & Submit Record Documents	81	15-Oct-24	11-Feb-25
SUB-1860	Prepare & Submit Environmental Site Assessment Reports	81	15-Oct-24	11-Feb-25
SUB-1870	Prepare & Submit Selective Removals & Demoloition	81	15-Oct-24	11-Feb-25
SUB-1880	Prepare & Submit Foundation Product Data	5	15-Oct-24	21-Oct-24
SUB-1890	Prepare & Submit Trench Drains Product Data	81	15-Oct-24	11-Feb-25
SUB-1900	Prepare & Submit Chain Link Fences & Gates Drawings	81	15-Oct-24	11-Feb-25

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1910	Prepare & Submit Outdoor Game Equipment	81	15-Oct-24	11-Feb-25
SUB-1920	Prepare & Submit Precast Architectural Concrete	71	15-Oct-24	28-Jan-25
SUB-1930	Prepare & Submit Unit Masonry Product Data	71	15-Oct-24	28-Jan-25
SUB-1940	Prepare & Submit Cast Stone Product Data	81	15-Oct-24	11-Feb-25
SUB-1950	Prepare & Submit Structure Steel Drawings	71	15-Oct-24	28-Jan-25
SUB-1960	Prepare & Submit Metal Deck Product Data	81	15-Oct-24	11-Feb-25
SUB-1970	Prepare & Submit Prefabricated Expansion Joint Covers	81	15-Oct-24	11-Feb-25
SUB-1980	Prepare & Submit Self Adhering Sheet Air Barriers	81	15-Oct-24	11-Feb-25
SUB-1990	Prepare & Submit Metal Plate Wall Panels	81	15-Oct-24	11-Feb-25
SUB-2000	Prepare & Submit Security Screens & Barriers	81	15-Oct-24	11-Feb-25
SUB-2010	Prepare & Submit Wood Flooring	81	15-Oct-24	11-Feb-25
SUB-2020	Prepare & Submit Visual Display Boards	81	15-Oct-24	11-Feb-25
SUB-2030	Prepare & Submit Metal Lockers	81	15-Oct-24	11-Feb-25
SUB-2040	Prepare & Submit Fire Extinguishers & Cabinets	81	15-Oct-24	11-Feb-25
SUB-2050	Prepare & Submit Stationary Metal Wall Louvers	73	15-Oct-24	30-Jan-25
SUB-2060	Prepare & Submit Library Equipment	81	15-Oct-24	11-Feb-25
SUB-2070	Prepare & Submit Platform Curtains & Auditorium Window Curtains	81	15-Oct-24	11-Feb-25
SUB-2080	Prepare & Submit Waste Handling Equipment	81	15-Oct-24	11-Feb-25
SUB-2090	Prepare & Submit Domestic Equipment	81	15-Oct-24	11-Feb-25
SUB-2100	Prepare & Submit Laboratory Equipment	81	15-Oct-24	11-Feb-25
SUB-2110	Prepare & Submit Manufactured Wood Casework	81	15-Oct-24	11-Feb-25
SUB-2120	Prepare & Submit Concrete Floating Floor Assembly	81	15-Oct-24	11-Feb-25
SUB-2130	Prepare & Submit Hydraulic Vertical Wheelchair Lifts	81	15-Oct-24	11-Feb-25
SUB-2140	Prepare & Submit Switch & Panel Boards	81	15-Oct-24	11-Feb-25
SUB-2150	Prepare & Submit Auditorium & Television Studio Dimming System Product Data	81	15-Oct-24	11-Feb-25
SUB-2160	Prepare & Submit Overcurrent Protective Devices Data	81	15-Oct-24	11-Feb-25
SUB-2170	Prepare & Submit Gas Pipes	81	15-Oct-24	11-Feb-25
SUB-2180	Prepare & Submit Water Heaters	81	15-Oct-24	11-Feb-25
SUB-2190	Prepare & Submit Pumping Apparatus & Tanks	81	15-Oct-24	11-Feb-25
SUB-2200	Prepare & Submit HVAC Pumps	81	15-Oct-24	11-Feb-25
SUB-2210	Prepare & Submit Emergency Generator System Accessories	71	15-Oct-24	28-Jan-25
SUB-2220	Prepare & Submit Fuel Storage Equipment	81	15-Oct-24	11-Feb-25
SUB-2230	Prepare & Submit Natural Gas Leak Detection Equipment	81	15-Oct-24	11-Feb-25
SUB-2250	Prepare & Submit Temperature Control System	81	15-Oct-24	11-Feb-25
SUB-2260	Prepare & Submit Air Outlets & Inlets	81	15-Oct-24	11-Feb-25
SUB-2340	Prepare & Submit Tree Protection Plan	71	15-Oct-24	28-Jan-25
SUB-2360	Prepare & Submit Adjacent Property and Structures Protection & Monitoring Plan	81	15-Oct-24	11-Feb-25
SUB-2370	Prepare & Submit Ornamenta Metal Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2920	Prepare & Submit Documentation of Proper Disposal	81	15-Oct-24	11-Feb-25
SUB-2930	Prepare & Submit Ornamenta Metal Product Data	81	15-Oct-24	11-Feb-25
SUB-2960	Prepare & Submit Coiling Doors, Grilles and Shutters Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2970	Prepare & Submit Coiling Doors, Grilles and Shutters Product Data	81	15-Oct-24	11-Feb-25
SUB-2980	Prepare & Submit Aluminum Framed Entrances & Storefronts Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2990	Prepare & Submit Aluminum Framed Entrances & Storefronts Product Data	81	15-Oct-24	11-Feb-25

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-3000	Prepare & Submit Thresholds, Weatherstripping and Seals Color Samples	81	15-Oct-24	11-Feb-25
SUB-3010	Prepare & Submit Thresholds, Weatherstripping and Seals Product Data	81	15-Oct-24	11-Feb-25
SUB-3020	Prepare & Submit Miscellaneous Glazing Samples	81	15-Oct-24	11-Feb-25
SUB-3030	Prepare & Submit Miscellaneous Glazing Product Data	81	15-Oct-24	11-Feb-25
SUB-3040	Prepare & Submit Fire Rated Glazing Samples	81	15-Oct-24	11-Feb-25
SUB-3050	Prepare & Submit Fire Rated Glazing Product Data	81	15-Oct-24	11-Feb-25
SUB-3060	Prepare & Submit Graffiti Resistant Coating Product Data	81	15-Oct-24	11-Feb-25
SUB-3070	Prepare & Submit Special Coating Samples	81	15-Oct-24	11-Feb-25
SUB-3080	Prepare & Submit Special Coating Product Data	81	15-Oct-24	11-Feb-25
SUB-3090	Prepare & Submit Flagpole Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3100	Prepare & Submit Flagpole Product Data	81	15-Oct-24	11-Feb-25
SUB-3110	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals	81	15-Oct-24	11-Feb-25
SUB-3120	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-3130	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	81	15-Oct-24	11-Feb-25
SUB-3140	Prepare & Submit Wire Mesh Work Samples	81	15-Oct-24	11-Feb-25
SUB-3150	Prepare & Submit Wire Mesh Work Shop drawings	81	15-Oct-24	11-Feb-25
SUB-3160	Prepare & Submit Metal Storage Shelving Samples	81	15-Oct-24	11-Feb-25
SUB-3170	Prepare & Submit Metal Storage Shelving Shop drawings	81	15-Oct-24	11-Feb-25
SUB-3180	Prepare & Submit Mirrors Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3190	Prepare & Submit Mirrors Product Data	81	15-Oct-24	11-Feb-25
SUB-3200	Prepare & Submit Mirrors Mastic Compatibility Test Reports & Certifications	81	15-Oct-24	11-Feb-25
SUB-3210	Prepare & Submit Grab Bars Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3220	Prepare & Submit Grab Bars Product Data	81	15-Oct-24	11-Feb-25
SUB-3230	Prepare & Submit Shop Equipment Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3240	Prepare & Submit Shop Equipment Product Data	81	15-Oct-24	11-Feb-25
SUB-3250	Prepare & Submit Bleachers Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3260	Prepare & Submit Bleachers Product Data	81	15-Oct-24	11-Feb-25
SUB-3270	Prepare & Submit Bleachers Manufacturer's Warranty	81	15-Oct-24	11-Feb-25
SUB-3280	Prepare & Submit Valves Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3290	Prepare & Submit Valves Product Data	81	15-Oct-24	11-Feb-25
SUB-3300	Prepare & Submit Certification of Tests	81	15-Oct-24	11-Feb-25
SUB-3310	Prepare & Submit Domestic Water Sterilization Plan	81	15-Oct-24	11-Feb-25
SUB-3320	Prepare & Submit Tags, Charts & Identifications Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3330	Prepare & Submit Tags, Charts & Identifications Product Data	81	15-Oct-24	11-Feb-25
SUB-3340	Prepare & Submit Micselianeous Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3350	Prepare & Submit Valves (HVAC) Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3360	Prepare & Submit Valves (HVAC) Product Data	81	15-Oct-24	11-Feb-25
SUB-3370	Prepare & Submit Piping Insulation Schedule Listing Items	81	15-Oct-24	11-Feb-25
SUB-3380	Prepare & Submit Schedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	81	15-Oct-24	11-Feb-25
SUB-3390	Prepare & Submit Schedules Showing Manfacturers's Product Number Duct Work Insulation	81	15-Oct-24	11-Feb-25
SUB-3400	Prepare & Submit Hydronic Specialities Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3410	Prepare & Submit Hydronic Specialities Product Data	81	15-Oct-24	11-Feb-25
SUB-3420	Prepare & Submit Water Treatment Firm	81	15-Oct-24	11-Feb-25
SUB-3430	Prepare & Submit Chemical Products Product Data	81	15-Oct-24	11-Feb-25

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-3440	Prepare & Submit Detail of Gag for the Safety Relief Valves	71	15-Oct-24	28-Jan-25
SUB-3450	Prepare & Submit Boiler Accessories Maintenance Data	71	15-Oct-24	28-Jan-25
SUB-3460	Prepare & Submit Breeching Chimney Connectors and Chimneys Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3470	Prepare & Submit Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	81	15-Oct-24	11-Feb-25
SUB-3480	Prepare & Submit Plate Heat Exchanger Maintenance Data	81	15-Oct-24	11-Feb-25
SUB-3490	Prepare & Submit Plate Heat Exchanger Product Data	81	15-Oct-24	11-Feb-25
SUB-3500	Prepare & Submit Coils Maintenance Data	81	15-Oct-24	11-Feb-25
SUB-3510	Prepare & Submit Coils Certifications	81	15-Oct-24	11-Feb-25
SUB-3520	Prepare & Submit Convectors Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3530	Prepare & Submit Convectors Product Data	81	15-Oct-24	11-Feb-25
SUB-3540	Prepare & Submit Fan Coils Units Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3550	Prepare & Submit Fan Coils Units Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-3560	Prepare & Submit Door Air Curtains Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3570	Prepare & Submit Door Air Curtains Product Data	81	15-Oct-24	11-Feb-25
SUB-3580	Prepare & Submit Centrifugal Fans Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3590	Prepare & Submit Centrifugal Fans Product Data	81	15-Oct-24	11-Feb-25
SUB-3600	Prepare & Submit Centrifugal Fans Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3610	Prepare & Submit Air Filters Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3620	Prepare & Submit Air Filters Product Data	81	15-Oct-24	11-Feb-25
SUB-3630	Prepare & Submit Air Filters Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3640	Prepare & Submit Duct Accessories Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3650	Prepare & Submit Damper Assemblies Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3660	Prepare & Submit Damper Assemblies Product Data	81	15-Oct-24	11-Feb-25
SUB-3670	Prepare & Submit Damper Assemblies Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3680	Prepare & Submit Variable Air Terminals Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3690	Prepare & Submit Variable Air Terminals Product Data	81	15-Oct-24	11-Feb-25
SUB-3700	Prepare & Submit Variable Air Terminals Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3710	Prepare & Submit AHU for Public Assemblies Sapces Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3720	Prepare & Submit AHU for Public Assemblies Sapces Product Data	81	15-Oct-24	11-Feb-25
SUB-3730	Prepare & Submit AHU for Public Assemblies Sapces Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3740	Prepare & Submit Control Systems Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3750	Prepare & Submit Truck Network Cable Schematic Diagram	81	15-Oct-24	11-Feb-25
SUB-3760	Prepare & Submit Lighting Control Devices Shop Drawing	71	15-Oct-24	28-Jan-25
SUB-3770	Prepare & Submit Lighting Control Devices Product Data	71	15-Oct-24	28-Jan-25
SUB-3780	Prepare & Submit Lighting Control Devices Warranty	71	15-Oct-24	28-Jan-25
SUB-3790	Prepare & Submit Surge Protective Devices Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3800	Prepare & Submit Surge Protective Devices Product Data	81	15-Oct-24	11-Feb-25
SUB-3810	Prepare & Submit Surge Protective Devices Warranty	81	15-Oct-24	11-Feb-25
SUB-3820	Prepare & Submit Service Entrance Equipment Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3830	Prepare & Submit Service Entrance Equipment Product Data	81	15-Oct-24	11-Feb-25
SUB-3840	Prepare & Submit Service Entrance Equipment Warranty	81	15-Oct-24	11-Feb-25
SUB-3850	Prepare & Submit Enclosed Switches Product Data	81	15-Oct-24	11-Feb-25
SUB-3860	Prepare & Submit Enclosed Switches Test Reports	81	15-Oct-24	11-Feb-25
SUB-3870	Prepare & Submit Motors, Motor Control Centers and Starters Shop Drawing	81	15-Oct-24	11-Feb-25

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-3880	Prepare & Submit Motors, Motor Control Centers and Starters Product Data	81	15-Oct-24	11-Feb-25
SUB-3890	Prepare & Submit Motors, Motor Control Centers and Starters Field Test Reports	81	15-Oct-24	11-Feb-25
SUB-3900	Prepare & Submit Lightning Protection Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3920	Prepare & Submit Lightning Protection Test Reports	81	15-Oct-24	11-Feb-25
SUB-3930	Prepare & Submit Fiber Optic Cabling system Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3940	Prepare & Submit Fiber Optic Cabling system Product Data	81	15-Oct-24	11-Feb-25
SUB-3950	Prepare & Submit Fiber Optic Cabling system Samples	81	15-Oct-24	11-Feb-25
SUB-3960	Prepare & Submit Sound, Intercome & Security System Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3970	Prepare & Submit Sound, Intercome & Security System Programming Code and Password for the System	81	15-Oct-24	11-Feb-25
SUB-3980	Prepare & Submit Sound, Intercome & Security System Warranty	81	15-Oct-24	11-Feb-25
SUB-3990	Prepare & Submit Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	81	15-Oct-24	11-Feb-25
SUB-4000	Prepare & Submit Projection and Interactive Whiteboard Systems Wiring diagram	81	15-Oct-24	11-Feb-25
SUB-4010	Prepare & Submit Self Corrective Clock System Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-4020	Prepare & Submit Self Corrective Clock System Product Data	81	15-Oct-24	11-Feb-25
SUB-4030	Prepare & Submit Self Corrective Clock System Field Test Reports	81	15-Oct-24	11-Feb-25
SUB-4040	Prepare & Submit Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	81	15-Oct-24	11-Feb-25
SUB-4060	Prepare & Submit Steel Stairs Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-4070	Prepare & Submit Steel Stairs Product Data	81	15-Oct-24	11-Feb-25
SUB-4080	Prepare & Submit Green School Submittal	81	15-Oct-24	11-Feb-25
MIL-1660	Start Security Guard Services (30 Days From NTP)	0	30-Oct-24	
SUB-2270	Prepare & Submit Final Underground Coordination Drawings	37	17-Jan-25	11-Mar-25
SUB-2280	Prepare & Submit Final 1st Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2290	Prepare & Submit Final 2nd Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2300	Prepare & Submit Final 3rd Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2310	Prepare & Submit Final 4th Floor Coordination Drawings	49	25-Feb-25	02-May-25
SUB-2320	Prepare & Submit Final 5th Floor Coordination Drawings	49	25-Feb-25	02-May-25
MIL-2762	Green Schools Compliance Submission	0		04-Mar-25
SUB-1700	Prepare & Submit Roof Dunnage	81	05-Mar-25	27-Jun-25
MIL-1640	Provide Complete Set of Approved Coordination Drawings	0		23-May-25
SUB-2900	Prepare & Submit Excavated Material Disposal Plan	71	26-May-25	05-Sep-25
SUB-4050	Prepare & Submit Soil Sampling Plan	71	26-May-25	05-Sep-25
PRO-1590	Procure & Deliver Steel Columns	120	02-Jun-25	29-Sep-25
PRO-1120	Procure & Deliver Erosion Control and Sedimentation Devices	25	05-Sep-25	29-Sep-25
SUB-2910	Prepare & Submit Backfill & Resue Plan	20	08-Sep-25	03-Oct-25
PRE-2630	Obtain Builders Pavement Permit	10	16-Sep-25	29-Sep-25
PRE-2640	Obtain Excavation & Shoring Permit	10	16-Sep-25	29-Sep-25
PRE-2650	Obtain Permit to Enter (PTE) Amtrak	10	16-Sep-25	29-Sep-25
PRE-2660	Obtain NYPA Permit	10	16-Sep-25	29-Sep-25
PRE-2540	SCA Work Notification	7	23-Sep-25	29-Sep-25
PRE-1660	DOB Permit & Insurance	3	25-Sep-25	29-Sep-25
PRE-1460	Obtain Construction Fences Permit	3	25-Sep-25	29-Sep-25
PRE-2550	Obtain CCD1	3	25-Sep-25	29-Sep-25
PRE-2570	Obtain Sidewalk Shed Permits	3	25-Sep-25	29-Sep-25
MIL-2532	Submit Complete Permit Application	0		29-Sep-25

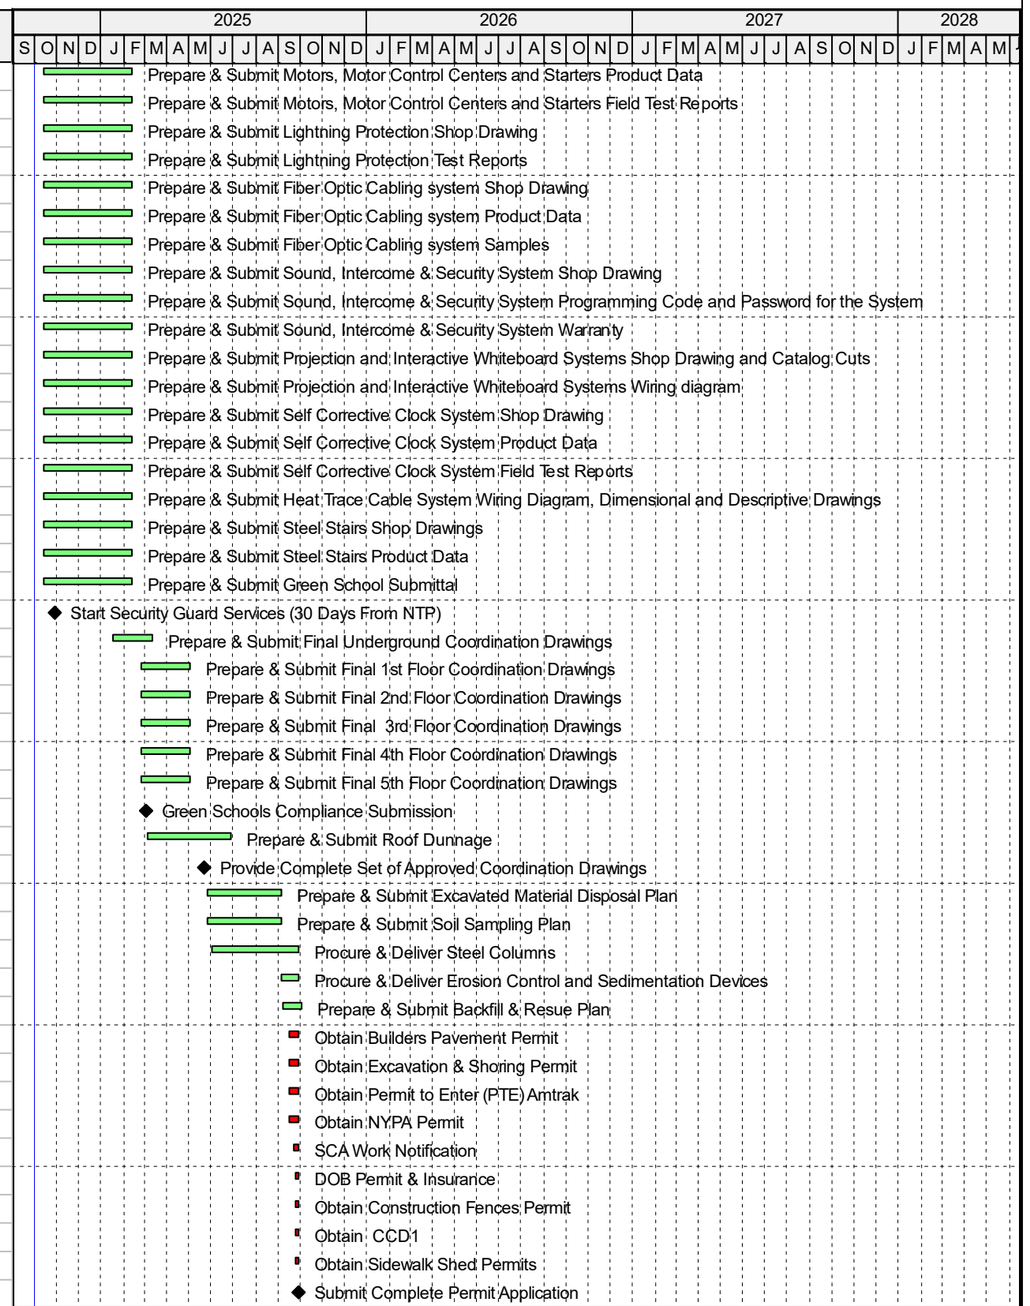

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1000	Mobilization	4	30-Sep-25	03-Oct-25
MIL-1060	Mobilization Start	0	30-Sep-25	
PRO-1420	Procure & Deliver Painting	70	30-Sep-25	08-Dec-25
PRO-1410	Procure & Deliver Door Frames	70	30-Sep-25	08-Dec-25
PRO-1200	Procure & Deliver Elevator Machine	112	30-Sep-25	19-Jan-26
PRO-1150	Procure & Deliver Gypsum Board	150	30-Sep-25	26-Feb-26
PRO-1160	Procure & Deliver Floorings	80	30-Sep-25	18-Dec-25
PRO-1170	Procure & Deliver Acosutical Ceiling Tiles	120	30-Sep-25	27-Jan-26
PRO-1190	Procure & Deliver Toilet Accessories	100	30-Sep-25	07-Jan-26
PRO-1000	Procure & Deliver Kitchen Equipment	180	30-Sep-25	28-Mar-26
PRO-1140	Procure & Deliver Lighting Fixtures	60	30-Sep-25	28-Nov-25
PRO-1010	Procure & Deliver Furnitures	130	30-Sep-25	06-Feb-26
PRO-1020	Procure & Deliver Mechanical Piping	70	30-Sep-25	08-Dec-25
PRO-1030	Procure & Deliver Mechanical Ducts	70	30-Sep-25	08-Dec-25
PRO-1050	Procure & Deliver Electrical Equipment	130	30-Sep-25	06-Feb-26
PRO-1060	Procure & Deliver Plumbing Fixtures	100	30-Sep-25	07-Jan-26
PRO-1070	Procure & Deliver Wood Doors	50	30-Sep-25	18-Nov-25
PRO-1090	Procure & Deliver Fire Sprinklers	100	30-Sep-25	07-Jan-26
PRO-1110	Procure & Deliver Fire Detectors & Alarms	60	30-Sep-25	28-Nov-25
PRO-1210	Procure & Deliver Signs	70	30-Sep-25	08-Dec-25
PRO-1220	Procure & Deliver Windows & Storefronts	154	30-Sep-25	02-Mar-26
PRO-1250	Procure & Deliver Plumbing Pipes	60	30-Sep-25	28-Nov-25
PRO-1260	Procure & Deliver Electrical Wires & Conduits	130	30-Sep-25	06-Feb-26
PRO-1270	Procure & Deliver Mechanical Pumps	70	30-Sep-25	08-Dec-25
PRO-1280	Procure & Deliver Fire Protection Pumps	70	30-Sep-25	08-Dec-25
PRO-1290	Procure & Deliver Plumbing Pumps	250	30-Sep-25	06-Jun-26
PRO-1310	Procure & Deliver Telecommunication System	60	30-Sep-25	28-Nov-25
PRO-1330	Procure & Deliver Cameras	60	30-Sep-25	28-Nov-25
PRO-1360	Procure & Deliver Metal Panel Ceilings	120	30-Sep-25	27-Jan-26
PRO-1380	Procure & Deliver Roof Dunnage	100	30-Sep-25	07-Jan-26
PRO-1470	Procure & Deliver Cabinet Heaters	126	30-Sep-25	02-Feb-26
PRO-1480	Procure & Deliver Chillers	170	30-Sep-25	18-Mar-26
PRO-1490	Procure & Deliver Air Handling Units	250	30-Sep-25	06-Jun-26
PRO-1500	Procure & Deliver Boilers	84	30-Sep-25	22-Dec-25
PRO-1510	Procure & Deliver Emergency Generator	290	30-Sep-25	16-Jul-26
PRO-1520	Procure & Deliver Switch Gears	250	30-Sep-25	06-Jun-26
PRO-1530	Procure & Deliver Hydraulic Vertical Wheelchair Lift	90	30-Sep-25	28-Dec-25
PRO-1560	Procure & Deliver Gymnasium Equipment	180	30-Sep-25	28-Mar-26
CON-7740	Protection Of All Overhead & Underground Utilities	263	30-Sep-25	19-Oct-26
PRO-1570	Procure & Deliver Precast Sandwich Panels	112	30-Sep-25	19-Jan-26
PRO-1580	Procure & Deliver Metal Deck	70	30-Sep-25	08-Dec-25
PRO-1600	Procure & Deliver Trusses	60	30-Sep-25	28-Nov-25
PRO-1610	Procure & Deliver Prefabricated Expansion Joint Covers	60	30-Sep-25	28-Nov-25
PRO-1620	Procure & Deliver Security Screens & Barriers	60	30-Sep-25	28-Nov-25

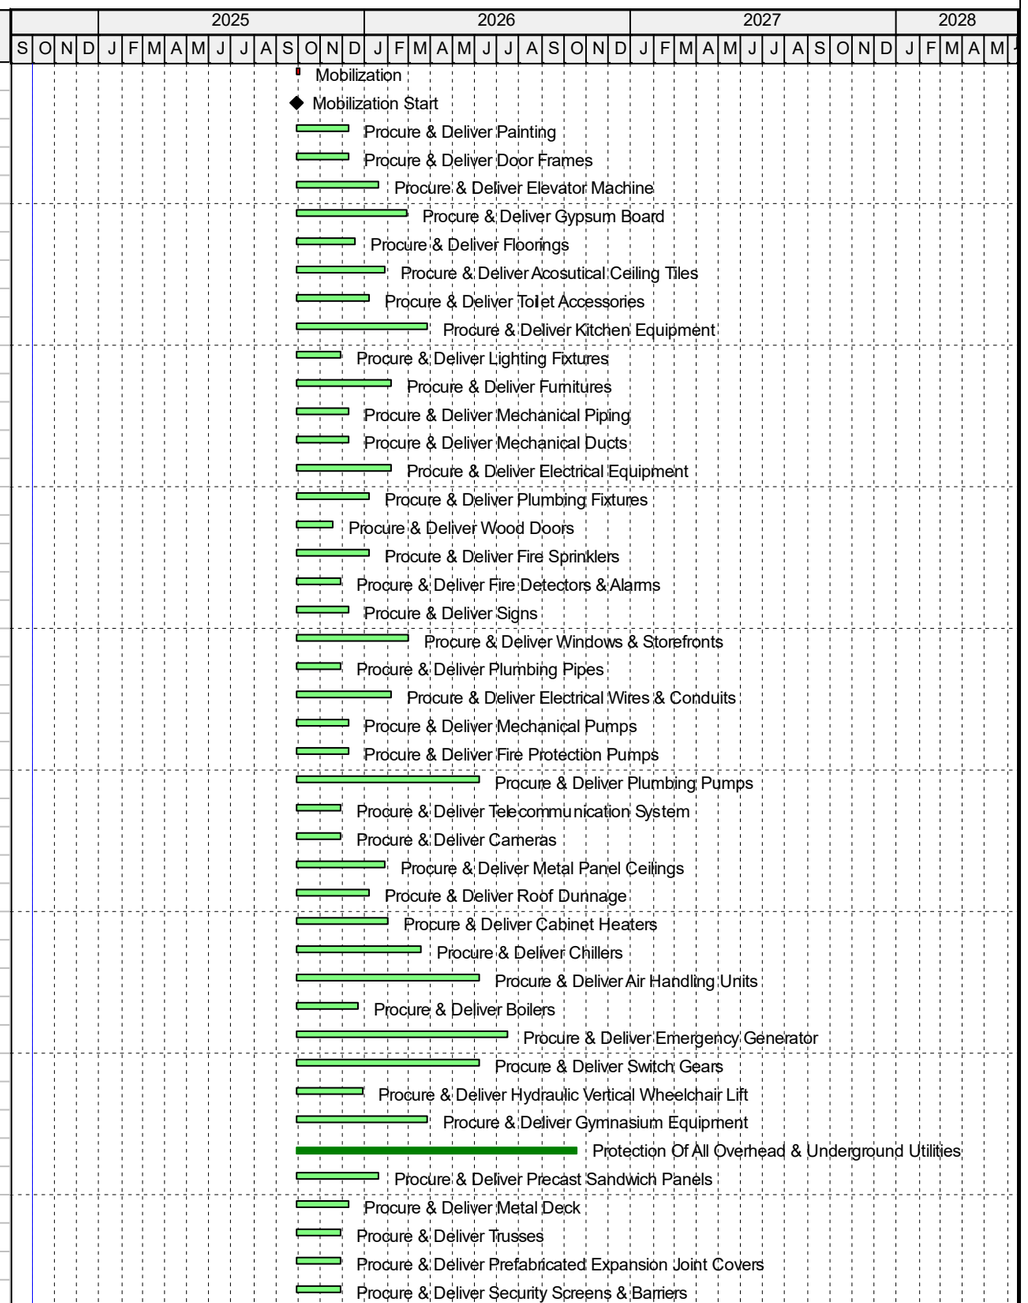

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
PRO-1630	Procure & Deliver Wood Flooring	120	30-Sep-25	27-Jan-26
PRO-1640	Procure & Deliver Concrete Floating Floor Assembly	120	30-Sep-25	27-Jan-26
PRO-1660	Procure & Deliver Auditorium Television Studio Dimming System	90	30-Sep-25	28-Dec-25
MIL-1850	Construction Start	0	30-Sep-25	
CON-9000	Protection & Restoration the adjacent Properties to Original Condition	263	30-Sep-25	19-Oct-26
PRO-2010	Procure & Deliver Steel Stairs Components	120	30-Sep-25	27-Jan-26
PRO-2020	Procure & Deliver Flagpole	60	30-Sep-25	28-Nov-25
PRO-2040	Procure & Deliver VAV Units	170	30-Sep-25	18-Mar-26
PRO-2050	Procure & Deliver Furnitures (Owner Responsibility)	130	30-Sep-25	06-Feb-26
MIL-1710	Complete Mobilization	0		03-Oct-25
CON-1080	Install Erosion Control Devices	2	06-Oct-25	07-Oct-25
CON-1010	Install Construction Signs	2	06-Oct-25	07-Oct-25
CON-1030	Install Construction Fences	2	06-Oct-25	07-Oct-25
PRE-2610	Prepare & Submit FDNY Fuel Permit	10	06-Oct-25	20-Oct-25
CON-9120	Soli Sampling	2	06-Oct-25	07-Oct-25
CON-7750	Install Field Offices	5	08-Oct-25	15-Oct-25
CON-9140	Excavation	5	08-Oct-25	15-Oct-25
CON-1040	F/R/P Concrete Walls & Beams -1st Floor	10	28-Oct-25	10-Nov-25
I-1010	Concrete Cast-IN-Place Inspection	86	28-Oct-25	04-Mar-26
MIL-2582	Start Concrete Placement	0	28-Oct-25	
MIL-2812	Start Foundation	0	28-Oct-25	
MIL-2912	Start Concrete Cast In Place Inspection	0	28-Oct-25	
CON-8050	Available Temporary Electrical Power For Testing MEP Equipment	0		31-Oct-25
CON-1050	Install Underground Conduits & Wires -1st Floor	6	12-Nov-25	19-Nov-25
CON-1060	Backfilling & Compaction -1st Floor	6	12-Nov-25	19-Nov-25
CON-1070	F/R/P SOG -1st Floor	10	20-Nov-25	04-Dec-25
PRO-1450	Procure & Deliver Playground Equipment	60	09-Dec-25	06-Feb-26
CON-1110	Install Metal Deck Slab -2nd Floor	4	22-Dec-25	26-Dec-25
MIL-1120	Metal Decking Start	0	22-Dec-25	
CON-8390	Install Sidewalk Sheds -South Elevation	4	29-Dec-25	02-Jan-26
CON-8400	Install Sidewalk Sheds -East Elevation	4	29-Dec-25	02-Jan-26
MIL-1720	Start Sidewalk Bridge Installations	0	29-Dec-25	
CON-1210	Install Metal Deck Slab - 3rd Floor	4	09-Jan-26	14-Jan-26
CON-1290	Install Metal Deck Slab - 4th Floor	4	29-Jan-26	03-Feb-26
CON-1380	Install Metal Deck Slab - 5th Floor	3	18-Feb-26	20-Feb-26
CON-1420	Layout -2nd Floor	3	23-Feb-26	25-Feb-26
MIL-1140	Layout Start	0	23-Feb-26	
MIL-1150	Masonry Walls Start	0	23-Feb-26	
CON-1430	Install Unit Masonry Mock-Up	1	23-Feb-26	23-Feb-26
CON-1470	Approve Unit Masonry Mock-Up	4	24-Feb-26	27-Feb-26
CON-1520	Install Top & Bottom Track-2nd Floor	4	26-Feb-26	03-Mar-26
CON-1530	Layout -3rd Floor	3	26-Feb-26	02-Mar-26
MIL-1160	Top & Bottom Track Start	0	26-Feb-26	
CON-1570	Install CMU Walls -2nd Floor	3	02-Mar-26	04-Mar-26

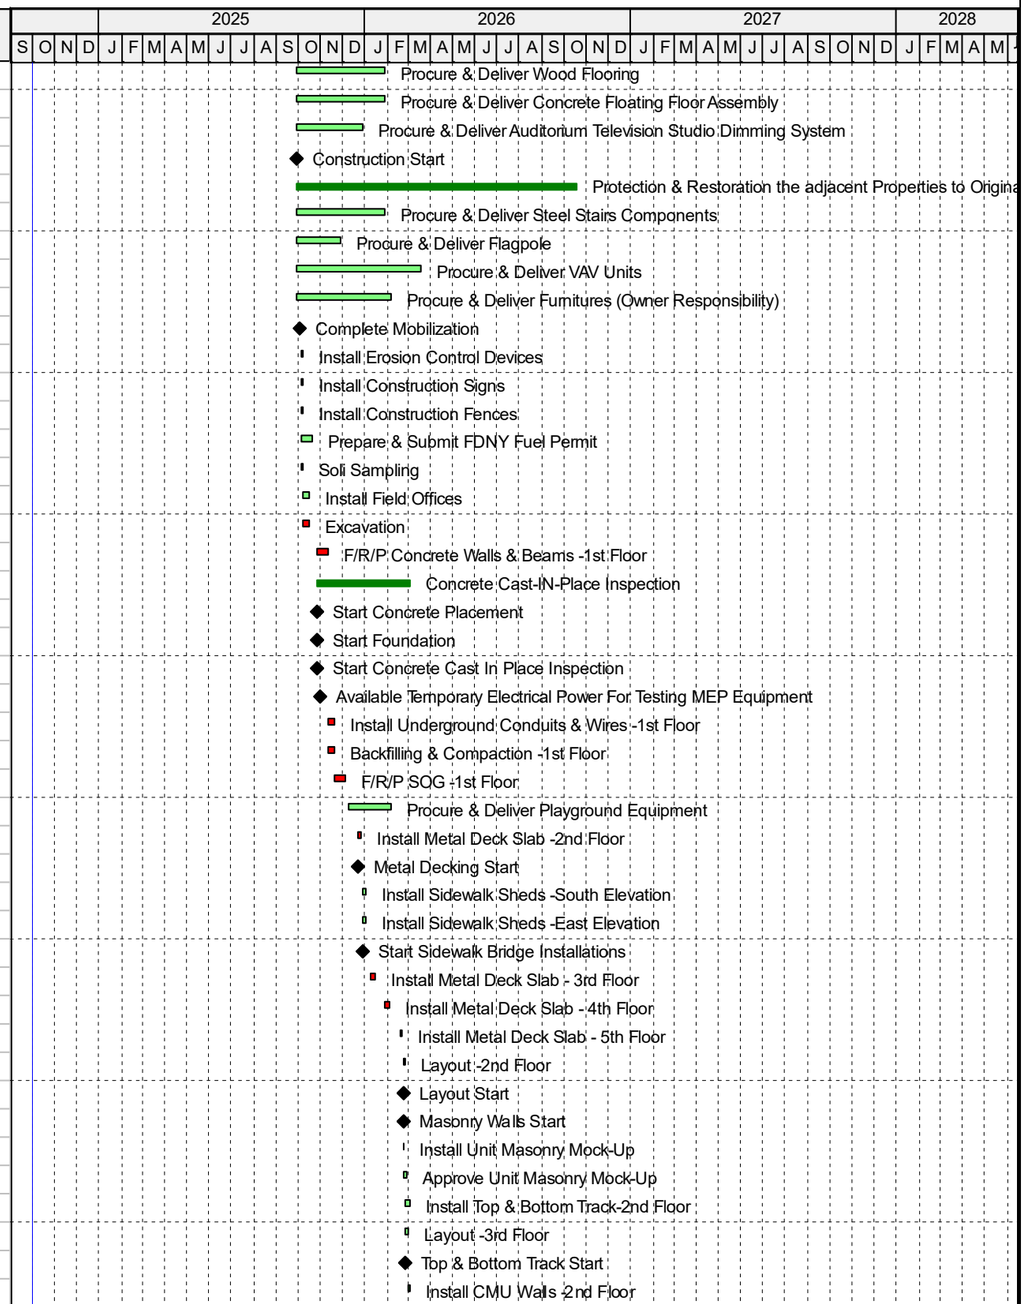

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1670	Layout -4th Floor	3	03-Mar-26	05-Mar-26
CON-1720	Install Metal Deck Slab -Roof Floor	2	03-Mar-26	04-Mar-26
CON-1640	Install Wall Steel Studs & Framing-2nd Floor	5	04-Mar-26	10-Mar-26
CON-1650	Install Top & Bottom Track-3rd Floor	4	04-Mar-26	09-Mar-26
CON-1660	Install CMU Walls -3rd Floor	3	05-Mar-26	09-Mar-26
MIL-2932	Start Masonry Inspection	0	05-Mar-26	
CON-1930	Layout -5th Floor	3	06-Mar-26	10-Mar-26
CON-1980	F/R/P Bulkhead Slab -Bulkhead	2	10-Mar-26	11-Mar-26
CON-1900	Install Wall Steel Studs & Framing-3rd Floor	5	10-Mar-26	16-Mar-26
CON-1910	Install Top & Bottom Track-4th Floor	4	10-Mar-26	13-Mar-26
CON-1920	Install CMU Walls -4th Floor	3	10-Mar-26	12-Mar-26
MIL-1170	Finish Concrete Work	0		11-Mar-26
MIL-1820	Crane Mobilization-Steel Installation Finish	0		12-Mar-26
CON-2030	Install CMU Walls -5th Floor	3	13-Mar-26	17-Mar-26
CON-2010	Install Wall Steel Studs & Framing-4th Floor	5	16-Mar-26	20-Mar-26
CON-2020	Install Top & Bottom Track-5th Floor	4	16-Mar-26	19-Mar-26
CON-2310	Install Ceiling Hangers & Supports-2nd Floor	4	16-Mar-26	19-Mar-26
MIL-2612	Start Suspended Ceiling Grid	0	16-Mar-26	
MIL-1380	Crane Mobilization-Mechanical Subcontractor	78	17-Mar-26	07-Jul-26
CON-2390	Install Ceiling Hangers & Supports-3rd Floor	4	20-Mar-26	25-Mar-26
CON-2200	Install Wall Steel Studs & Framing-5th Floor	5	23-Mar-26	27-Mar-26
I-1150	Concrete Precast Inspection	9	25-Mar-26	06-Apr-26
MIL-2922	Start Pre -Cast Concrete Inspection	0	25-Mar-26	
CON-2550	Install Ceiling Hangers & Supports-4th Floor	4	26-Mar-26	31-Mar-26
CON-2620	Install Ceiling Hangers & Supports-5th Floor	4	01-Apr-26	06-Apr-26
CON-2910	Layout -1st Floor	3	07-Apr-26	09-Apr-26
CON-2920	Pour Sloped Concrete Fill -5th Floor Roof	2	07-Apr-26	08-Apr-26
MIL-1230	5th Floor Roofing Start	0	07-Apr-26	
CON-3010	Pour Sloped Concrete Fill -Roof Floor	2	09-Apr-26	10-Apr-26
MIL-1200	Main Roofing Start	0	09-Apr-26	
MIL-1220	Layout Finish	0		09-Apr-26
CON-3080	Install Top & Bottom Track -1st Floor	4	10-Apr-26	15-Apr-26
CON-3090	Install CMU Walls -1st Floor	3	10-Apr-26	14-Apr-26
MIL-2942	Start In-Wall Inspection	0	10-Apr-26	
CON-3210	Install Fluid-Applied Protected Membrane Mock-Up	2	13-Apr-26	14-Apr-26
CON-3520	Install Ceiling Hangers & Supports -1st Floor	4	15-Apr-26	20-Apr-26
MIL-1250	Top & Bottom Track Finish	0		15-Apr-26
CON-3240	Install Wall Steel Studs & Framing -1st Floor	5	16-Apr-26	22-Apr-26
CON-9070	In-Wall Inspection-2nd Floor	2	16-Apr-26	17-Apr-26
CON-3430	Install Hot Fluid Applied Membrane -Roof Floor	3	21-Apr-26	23-Apr-26
CON-3440	Install Hot Fluid Applied Membrane -5th Floor Roof	4	21-Apr-26	24-Apr-26
CON-9080	In-Wall Inspection -3rd Floor	2	22-Apr-26	23-Apr-26
CON-3580	Install 6" Thick Rigid Insulation -5th Floor Roof	3	27-Apr-26	29-Apr-26
CON-9090	In-Wall Inspection -4th Floor	7	28-Apr-26	06-May-26

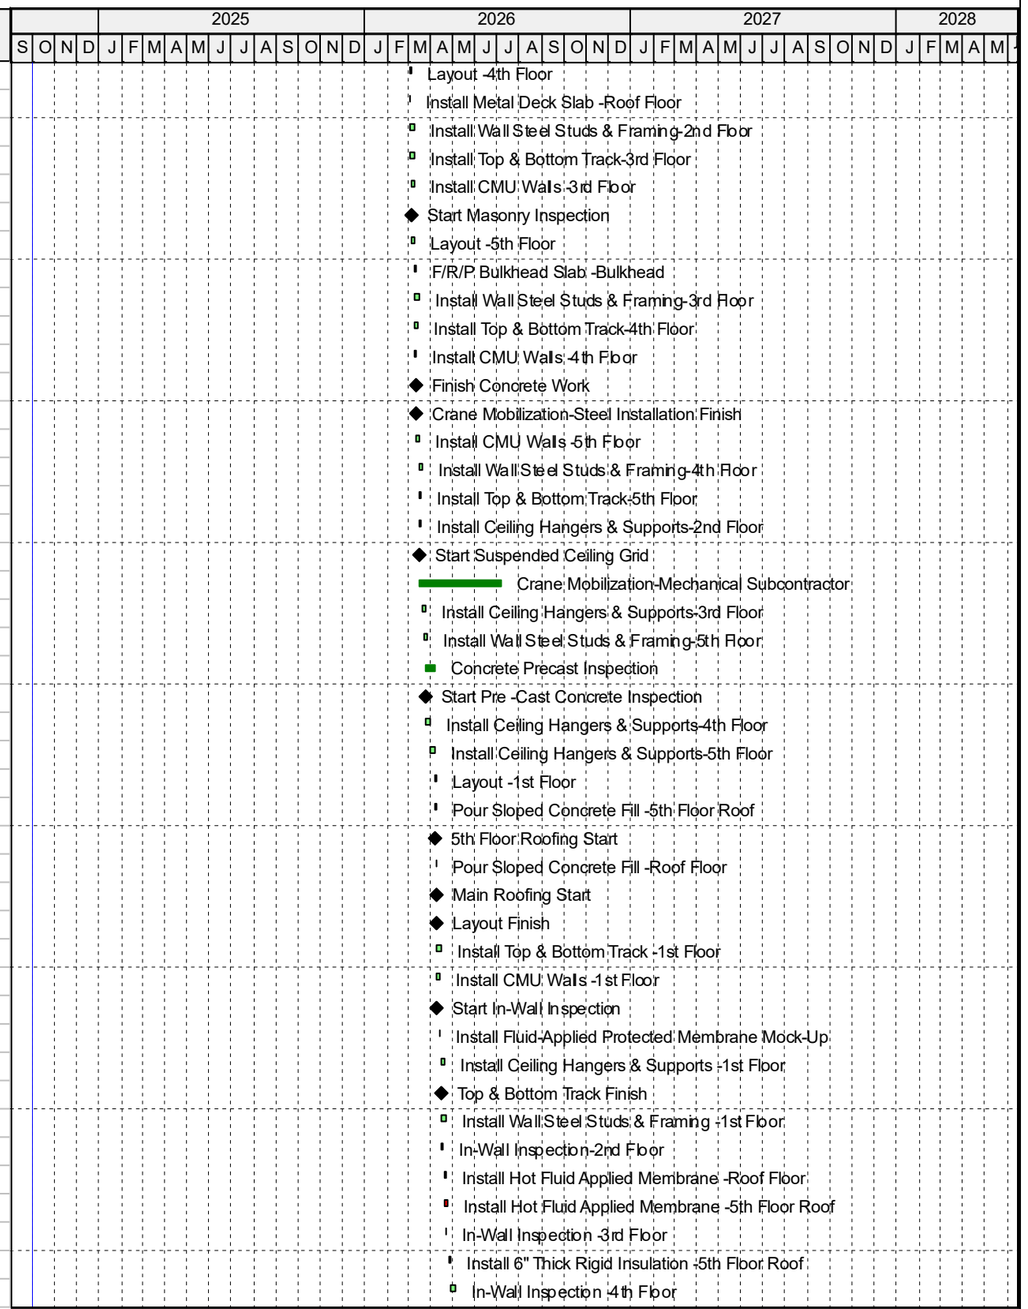

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3730	Install 6" Thick Rigid Insulation -Roof Floor	3	29-Apr-26	01-May-26
MIL-1400	Start Site Work	0	29-Apr-26	
CON-3710	Roof Flood Test -5th Floor Roof	4	30-Apr-26	05-May-26
CON-3780	Install Traffic Control Devices - 54th Avenue Street	3	01-May-26	05-May-26
CON-4960	F/R/P Concrete Pad - Electric Service Room	6	01-May-26	08-May-26
CON-3840	Roof Flood Test -Roof Floor	3	04-May-26	06-May-26
CON-9100	In-Wall Inspections -5th Floor	7	04-May-26	12-May-26
CON-3820	Install Filter Fabric -5th Floor Roof	3	06-May-26	08-May-26
CON-3850	Remove Existing Steel Faced Curb - 54th Avenue Street	3	06-May-26	08-May-26
CON-3860	Remove Existing Asphalt - 54th Avenue Street	4	06-May-26	11-May-26
CON-3870	Install Traffic Control Devices - 2nd Street	5	06-May-26	12-May-26
MIL-1340	BLDG Tight	0		06-May-26
CON-4020	Install Filter Fabric -Roof Floor	3	07-May-26	11-May-26
CON-4040	Install Walls GWB-Mockup Room	3	07-May-26	11-May-26
CON-4270	Install Gypsum Board Ceiling -Mockup Room	3	07-May-26	11-May-26
MIL-1360	Start Mockup Room Work	0	07-May-26	
MIL-1430	Start Architecture Finishes	0	07-May-26	
CON-3960	Install Concrete Pavers -5th Floor Roof	3	11-May-26	13-May-26
CON-4210	Install Concrete Pavers -Roof Floor	4	12-May-26	15-May-26
CON-3940	Remove Existing Electrical Manhole - 54th Avenue Street	4	12-May-26	15-May-26
CON-3900	Remove Existing Sidewalk - 2nd Street	5	13-May-26	19-May-26
MIL-1310	5th Floor Roofing Finish	0		13-May-26
MIL-1280	Main Roofing Finish	0		15-May-26
CON-4080	Install 5' Wide Silva Cells Under Concrete Pavement Strip - 54th Avenue Street	4	18-May-26	21-May-26
CON-9110	In-Wall Inspection -1st Floor	2	19-May-26	20-May-26
CON-3950	Install Pedestrian Ramps With Truncated Domes - 2nd Street	6	20-May-26	28-May-26
CON-4930	Install Furniture & Signs -Mockup Room	2	22-May-26	26-May-26
CON-4150	Pavement Replacement - 54th Avenue Street	4	22-May-26	28-May-26
MIL-1410	Mockup Room Ready For Inspection	0		26-May-26
MIL-1420	Finish Mockup Room	0		26-May-26
CON-4030	Install Gypsum Board Walls-2nd Floor	5	27-May-26	02-Jun-26
MIL-1440	Start Gypsum Board	0	27-May-26	
CON-4200	Tape Gypsum Board -2nd Floor	4	28-May-26	02-Jun-26
CON-4290	Install New Steel Faced Curb - 54th Avenue Street	4	29-May-26	03-Jun-26
CON-4300	Install Pedestrian Ramps With Truncated Domes - 54th Avenue Street	4	29-May-26	03-Jun-26
CON-4090	Remove Existing Steel Faced Curb - 2nd Street	6	29-May-26	05-Jun-26
CON-4890	F/R/P Concrete Pads -Fuel Oil Room	2	01-Jun-26	02-Jun-26
CON-4350	Install Ceramic Wall Tiles at Corridor-2nd Floor	7	03-Jun-26	11-Jun-26
CON-4360	Install Gypsum Board Walls-3rd Floor	5	03-Jun-26	09-Jun-26
CON-4370	Install Gypsum Board Ceiling -2nd Floor	6	03-Jun-26	10-Jun-26
CON-4540	Tape Gypsum Board -3rd Floor	4	04-Jun-26	09-Jun-26
CON-4400	Install 4" Concrete Sidewalk - 54th Avenue Street	5	04-Jun-26	10-Jun-26
CON-4410	Install 7" Concrete Sidewalk - 54th Avenue Street	5	04-Jun-26	10-Jun-26
CON-4160	Install New Steel Faced Curb - 2nd Street	6	08-Jun-26	15-Jun-26

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-4170	Install 4" Concrete Sidewalk - 2nd Street	7	08-Jun-26	16-Jun-26
CON-4620	Install Gypsum Board Walls-4th Floor	5	10-Jun-26	16-Jun-26
CON-4630	Install Gypsum Board Ceiling-3rd Floor	6	11-Jun-26	18-Jun-26
CON-4720	Tape Gypsum Board -4th Floor	4	11-Jun-26	16-Jun-26
CON-4560	Install Pavement Marking - 54th Avenue Street	3	11-Jun-26	15-Jun-26
CON-4610	Install Ceramic Wall Tiles at Corridor-3rd Floor	7	12-Jun-26	23-Jun-26
CON-4580	Remove Traffic Control Devices - 54th Avenue Street	3	16-Jun-26	18-Jun-26
CON-4310	Install 7" Concrete Sidewalk - 2nd Street	6	16-Jun-26	24-Jun-26
CON-4810	Install Gypsum Board Walls-5th Floor	5	17-Jun-26	24-Jun-26
CON-4970	Tape Gypsum Board -5th Floor	4	18-Jun-26	24-Jun-26
CON-4820	Install Gypsum Board Ceiling-4th Floor	6	22-Jun-26	29-Jun-26
CON-4800	Install Ceramic Wall Tiles at Corridor-4th Floor	7	24-Jun-26	02-Jul-26
CON-4420	Remove Traffic Control Devices - 2nd Street	5	25-Jun-26	01-Jul-26
CON-4450	Install Gypsum Board Walls-1st Floor	6	26-Jun-26	06-Jul-26
CON-5100	Install Gypsum Board Ceiling-5th Floor	6	30-Jun-26	08-Jul-26
CON-4600	Tape Gypsum Board -1st Floor	4	30-Jun-26	06-Jul-26
CON-4660	Excavation - Drainage Work - Building Perimeter	3	02-Jul-26	07-Jul-26
CON-5080	Install Ceramic Wall Tiles at Corridor-5th Floor	7	06-Jul-26	14-Jul-26
CON-4680	Install Ceramic Wall Tiles at Corridor -1st Floor	7	07-Jul-26	15-Jul-26
CON-5480	Install Gypsum Board Ceiling -1st Floor	6	08-Jul-26	15-Jul-26
CON-4740	Install Flood Barrier Wall - Drainage Work - Building Perimeter	3	08-Jul-26	10-Jul-26
PRO-2000	Procure & Deliver Key Cutting Machine	74	08-Jul-26	19-Sep-26
CON-4860	Install Drilled Caisson Supported Ventilation Structure - Drainage Work - Building Perimeter	3	13-Jul-26	15-Jul-26
CON-5090	Install Acoustical Ceiling Tiles-2nd Floor	5	14-Jul-26	20-Jul-26
CON-5960	F/R/P Concert Pad -Boiler Room	3	15-Jul-26	17-Jul-26
CON-5820	Install Signages-2nd Floor	5	21-Jul-26	27-Jul-26
CON-5330	Install Acoustical Ceiling Tiles-3rd Floor	5	22-Jul-26	28-Jul-26
CON-5870	Install Metal Panel Ceiling & Metal Geometric Ceiling -1st Floor	5	23-Jul-26	29-Jul-26
SUB-2330	Prepare & Submit Remedial Closure Report	3	27-Jul-26	29-Jul-26
CON-5810	Install Wall Pads - Gymnatorium	4	28-Jul-26	31-Jul-26
CON-9160	Excavate for Footings - Playground Area & Fences - Building Perimeter	2	28-Jul-26	29-Jul-26
CON-9010	Remove Steel Plate Protection over NYPA Easement - Playground Area & Fences - Building Perimeter	1	28-Jul-26	28-Jul-26
CON-6030	Install Signages-3rd Floor	5	29-Jul-26	04-Aug-26
CON-6120	Install Air Separator Units (AS-1 , AS-2 & AS-3)	2	30-Jul-26	31-Jul-26
CON-5520	Install Acoustical Ceiling Tiles-4th Floor	5	30-Jul-26	05-Aug-26
CON-9190	F/R/P Playground Equipment Footings - Playground Area & Fences - Building Perimeter	2	30-Jul-26	31-Jul-26
PER-2640	Obtain Emergency Generator Permit	5	03-Aug-26	07-Aug-26
CON-5470	Install Flush Concrete Curb - Playground Area & Fences - Building Perimeter	3	03-Aug-26	05-Aug-26
CON-5420	Install Asphalt Pavement - Playground Area & Fences - Building Perimeter	2	04-Aug-26	05-Aug-26
CON-5670	Install Acoustical Ceiling Tiles-5th Floor	5	06-Aug-26	12-Aug-26
CON-6160	Install Signages-4th Floor	5	06-Aug-26	12-Aug-26
CON-6020	Install 8" Acoustic Block Painted-Gymnatorium	7	06-Aug-26	14-Aug-26
CON-5600	Install Concrete Pavement Pedestrian Ramp With Painted Black Handrails - Playground Area & Fences - Building Perimeter	3	06-Aug-26	10-Aug-26
MIL-2802	Provision of Training Schedules (30 days prior to start of Training)	0	10-Aug-26	

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
MIL-2702	Finish Concrete Work	0		10-Aug-26
CON-5650	Install Playground Rubber Tile Safety Surface - Playground Area & Fences - Building Perimeter	3	11-Aug-26	13-Aug-26
CON-5800	Install Painted Asphalt Pavement & Painted Games On Asphalt Surface - Playground Area & Fences - Building Perimeter	3	14-Aug-26	18-Aug-26
CON-5850	Install Colored Athletic Wearing Surface Color - Playground Area & Fences - Building Perimeter	2	19-Aug-26	20-Aug-26
CON-5990	Install Playground Equipment - Playground Area & Fences - Building Perimeter	7	21-Aug-26	31-Aug-26
CON-6280	Install Signages- 5th Floor	5	27-Aug-26	02-Sep-26
CON-5880	Install Acoustical Ceiling Tiles -1st Floor	5	31-Aug-26	04-Sep-26
CON-6310	Install Security Screens & Barriers-1st Floor	3	31-Aug-26	02-Sep-26
CON-6140	Install Basketball Hoop - Playground Area & Fences - Building Perimeter	1	01-Sep-26	01-Sep-26
CON-6370	Install Signages-1st Floor	4	04-Sep-26	10-Sep-26
MIL-2722	Start Kitchen	0	04-Sep-26	
MIL-2662	Finishes and Ceiling Complete	0		04-Sep-26
CLO-1300	Provide Training	10	09-Sep-26	22-Sep-26
CLO-1030	Pre-Final Clean-Out	5	11-Sep-26	17-Sep-26
CLO-1110	Pre-TCO Punchlist	10	05-Oct-26	19-Oct-26
CLO-1050	Pre-Substantial Punchlist	105	20-Oct-26	17-Apr-27
CLO-1060	Prepare & Submit O&M Manuals	30	19-Apr-27	01-Jun-27
MIL-2782	Submission of Operations and Maintenance Manuals	0		01-Jun-27
CLO-1070	Prepare & Submit As-Built Drawings	30	02-Jun-27	15-Jul-27
CLO-1090	Final Clean Out	10	23-Jul-27	05-Aug-27
CLO-1100	Demobilization	10	06-Aug-27	15-Aug-27
Farley		4	14-Jul-26	17-Jul-26
CON-99247	Install Laboratory Equipment -3rd Floor	4	14-Jul-26	17-Jul-26
CON-ED		450	07-Oct-24	27-Jul-26
CON-7960	Obtain Gas Meter Layout From CON-ED	5	07-Oct-24	11-Oct-24
CON-8010	Coordination With CON-ED For Temporary Electrical Power	10	07-Nov-24	21-Nov-24
CON-8020	Scheduling With CON-ED For Temporary Electrical Power	7	22-Nov-24	03-Dec-24
CON-8030	Procurement From CON-ED For Temporary Electrical Power	20	30-Sep-25	19-Oct-25
CON-8040	CON-ED Work For Temporary Electrical Power	10	20-Oct-25	31-Oct-25
CON-7970	Coordinate With CON-ED For Gas Service	7	16-Apr-26	24-Apr-26
PRO-1990	Procure & Deliver Gas Meter Rig	60	25-Apr-26	23-Jun-26
CON-8060	CON-ED - Switchgear Inspection	4	15-Jun-26	18-Jun-26
CON-8070	CON-ED - Pull Power Cable to the Building	10	22-Jun-26	06-Jul-26
CON-7990	Gas Authorization	5	24-Jun-26	30-Jun-26
CON-8000	Pink Slip	5	01-Jul-26	08-Jul-26
CON-8080	CON-ED - Terminate Power Cables	10	07-Jul-26	20-Jul-26
CON-8090	CON-ED - Energize to the Building	5	21-Jul-26	27-Jul-26
MIL-2742	Permanent Power Available	0		27-Jul-26
EAI Inc.		193	16-Oct-25	24-Jul-26
CON-9898	Install Gas Permeable Aggregate -1st Floor	3	16-Oct-25	20-Oct-25
CON-98947	Install 4" slotted schedule 80 PVC Piping -1st Floor	3	16-Oct-25	20-Oct-25
CON-9888	Install Liquid Boot VI-20 Geomembrane -1st Floor	2	21-Oct-25	22-Oct-25
CON-1020	Install 60 Dry MILS Liquid Boot -1st Floor	3	23-Oct-25	27-Oct-25

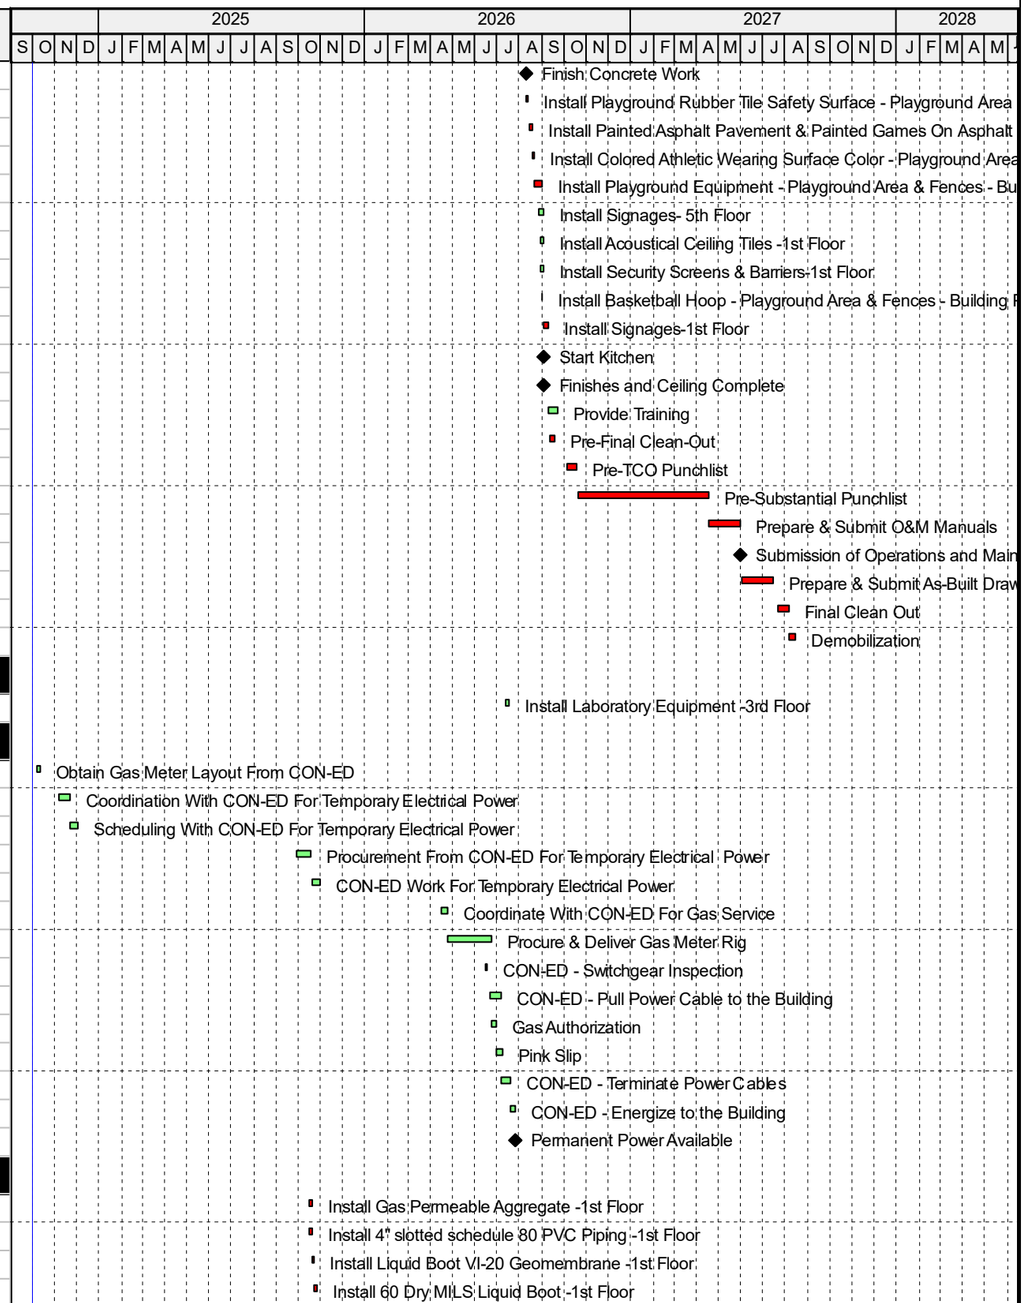

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-9777	Install Liquid Ultrashield G-1000 -1st Floor	2	24-Oct-25	27-Oct-25
CON-1740	Install SSDS Risers -SSDS System -2nd Floor	2	02-Mar-26	03-Mar-26
CON-1840	Install SSDS Risers -SSDS System -3rd Floor	2	04-Mar-26	05-Mar-26
CON-1970	Install SSDS Risers -SSDS System -4th Floor	2	06-Mar-26	09-Mar-26
CON-2000	Install SSDS Risers -SSDS System -5th Floor	1	09-Mar-26	09-Mar-26
CON-3230	Install SSDS Risers -SSDS System -1st Floor	2	14-Apr-26	15-Apr-26
CON-4500	Install SSDS Control Panel -1st Floor	5	07-May-26	13-May-26
CLO-1140	SSDS System Testing & Commissioning	7	16-Jul-26	24-Jul-26
Weir Welding		267	20-Feb-25	16-Mar-26
MIL-2572	Place Steel Mill Order	0	20-Feb-25	
CON-98787	Install Steel Columns -1st Floor	7	05-Dec-25	15-Dec-25
MIL-1810	Crane Mobilization-Steel Installation start	0	05-Dec-25	
CON-1090	Install Trusses -1st Floor	3	16-Dec-25	18-Dec-25
CON-1100	Install Framing Beams -1st Floor	4	16-Dec-25	19-Dec-25
CON-1150	Install Steel Canopy Framing -2nd Floor	5	29-Dec-25	05-Jan-26
CON-1170	Install Steel Columns -2nd Floor	3	29-Dec-25	31-Dec-25
CON-1190	Install Trusses -2nd Floor	4	02-Jan-26	07-Jan-26
CON-1200	Install Framing Beams -2nd Floor	5	02-Jan-26	08-Jan-26
CON-1240	Install Steel Columns - 3rd Floor	4	15-Jan-26	21-Jan-26
CON-1260	Install Trusses - 3rd Floor	3	22-Jan-26	26-Jan-26
CON-1270	Install Framing Beams - 3rd Floor	5	22-Jan-26	28-Jan-26
CON-99277	Install Steel Stairs -1st Floor	7	28-Jan-26	05-Feb-26
CON-1330	Install Steel Columns - 4th Floor	4	04-Feb-26	09-Feb-26
CON-99287	Install Steel Stairs -2nd Floor	3	06-Feb-26	10-Feb-26
CON-1360	Install Trusses - 4th Floor	3	10-Feb-26	12-Feb-26
CON-1370	Install Framing Beams - 4th Floor	5	10-Feb-26	17-Feb-26
CON-99297	Install Steel Stairs- 3rd Floor	4	11-Feb-26	17-Feb-26
CON-1440	Install Steel Columns - 5th Floor	3	23-Feb-26	25-Feb-26
CON-1460	F/R/P Piers - 5th Floor	5	23-Feb-26	27-Feb-26
CON-99307	Install Steel Stairs - 4th Floor	4	23-Feb-26	26-Feb-26
CON-1540	Install Trusses - 5th Floor	2	26-Feb-26	27-Feb-26
CON-1550	Install Framing Beams - 5th Floor	3	26-Feb-26	02-Mar-26
CON-99317	Install Steel Stairs - 5th Floor	3	27-Feb-26	03-Mar-26
CON-1620	Install Dunnage - 5th Floor	8	02-Mar-26	11-Mar-26
CON-1750	F/R/P Concrete Columns -Bulkhead	3	05-Mar-26	09-Mar-26
CON-1760	Install Dunnage-Roof Floor	8	05-Mar-26	16-Mar-26
CON-2060	Install Hoist Beam-Bulkhead	1	12-Mar-26	12-Mar-26
Eagle 1 Mechanical		165	27-Nov-25	28-Jul-26
CON-4920	Install Floor Drains & Clean-outs -1st Floor	5	27-Nov-25	04-Dec-25
CON-3160	Install Floor Drains & Clean-outs -2nd Floor	5	19-Dec-25	26-Dec-25
CON-3270	Install Temporary Standpipe	9	29-Dec-25	09-Jan-26
CON-3320	Install Floor Drains & Clean-outs -3rd Floor	5	08-Jan-26	14-Jan-26
CON-3530	Install Floor Drains & Clean-outs -4th Floor	5	28-Jan-26	03-Feb-26
CON-3610	Install Floor Drains & Clean-outs -5th Floor	5	13-Feb-26	20-Feb-26

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1770	Install Roof Drains & Clean outs -Roof Floor	5	26-Feb-26	04-Mar-26
CON-1580	Install Plumbing Risers -2nd Floor	2	26-Feb-26	27-Feb-26
CON-1680	Install Plumbing Risers -3rd Floor	2	02-Mar-26	03-Mar-26
CON-1780	Install Plumbing Risers -4th Floor	2	04-Mar-26	05-Mar-26
CON-2070	Install Roof Drains & Clean outs - Mechanical Work - Roof Bulkhead	5	05-Mar-26	11-Mar-26
CON-1940	Install Plumbing Risers-5th Floor	1	06-Mar-26	06-Mar-26
CON-2630	Rough-in Gas Risers -2nd Floor	4	06-Apr-26	09-Apr-26
CON-3140	Install Plumbing Risers -1st Floor	2	10-Apr-26	13-Apr-26
CON-2740	Rough-in Domestic Water Piping -2nd Floor	4	10-Apr-26	15-Apr-26
CON-2750	Rough-in Gas Risers-3rd Floor	4	10-Apr-26	15-Apr-26
CON-2870	Rough-in Sanitary & Vent Piping -2nd Floor	4	16-Apr-26	21-Apr-26
CON-2880	Rough-in Domestic Water Piping -3rd Floor	4	16-Apr-26	21-Apr-26
CON-2890	Rough-in Gas Risers -4th Floor	4	16-Apr-26	21-Apr-26
CON-3020	Rough-in Storm Piping -2nd Floor	4	22-Apr-26	27-Apr-26
CON-3030	Rough-in Sanitary & Vent Piping -3rd Floor	4	22-Apr-26	27-Apr-26
CON-3040	Rough-in Domestic Water Piping -4th Floor	4	22-Apr-26	27-Apr-26
CON-3050	Rough-in Gas Risers & Piping -5th Floor	4	22-Apr-26	27-Apr-26
CON-3600	Install Drainage Panels- Roof Floor	3	24-Apr-26	28-Apr-26
CON-3170	Rough-in Storm Piping -3rd Floor	4	28-Apr-26	01-May-26
CON-3180	Rough-in Sanitary & Vent Piping -4th Floor	4	28-Apr-26	01-May-26
CON-3190	Rough-in Domestic Water Piping -5th Floor	4	28-Apr-26	01-May-26
CON-3200	Plumbing Pressure Testing -2nd Floor	5	28-Apr-26	04-May-26
CON-3700	Install Drainage -5th Floor Roof	3	30-Apr-26	04-May-26
CON-3310	Install 4" Standpipe -2nd Floor	4	04-May-26	07-May-26
CON-3330	Rough-in Storm Piping -4th Floor	4	04-May-26	07-May-26
CON-3340	Rough-in Sanitary & Vent Piping -5th Floor	4	04-May-26	07-May-26
MIL-1300	Start Sprinkler Rough-ins	0	04-May-26	
CON-3400	Install Hot Water Circulation Pump -5th Floor	5	04-May-26	08-May-26
CON-3410	Install Electric Hot Water Heater (EWH-1) -5th Floor	5	04-May-26	08-May-26
CON-3360	Plumbing Pressure Testing -3rd Floor	5	05-May-26	11-May-26
CON-4460	Rough-in Gas Risers -1st Floor	4	07-May-26	12-May-26
MIL-1260	Plumbing Rough-ins Start	0	07-May-26	
CON-4050	Plumbing Piping Insulation -2nd Floor	5	07-May-26	13-May-26
CON-3500	Rough-in Main Sprinkler Piping -2nd Floor	5	08-May-26	14-May-26
CON-3510	Install 4" Standpipe -3rd Floor	4	08-May-26	13-May-26
CON-3540	Rough-in Storm Piping -5th Floor	4	08-May-26	13-May-26
CON-3560	Plumbing Pressure Testing -4th Floor	5	12-May-26	18-May-26
CON-4590	Rough-in Domestic Water Piping-1st Floor	4	13-May-26	18-May-26
CON-3650	Install 4" Standpipe -4th Floor	4	14-May-26	19-May-26
CON-3590	Plumbing Pressure Testing -5th Floor	5	14-May-26	20-May-26
CON-4190	Plumbing Piping Insulation -3rd Floor	5	14-May-26	20-May-26
CON-3670	Rough-in Branch Sprinkler Piping -2nd Floor	5	15-May-26	21-May-26
CON-3680	Rough-in Sprinkler Heads -2nd Floor	5	15-May-26	21-May-26
CON-3720	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -2nd Floor	5	15-May-26	21-May-26

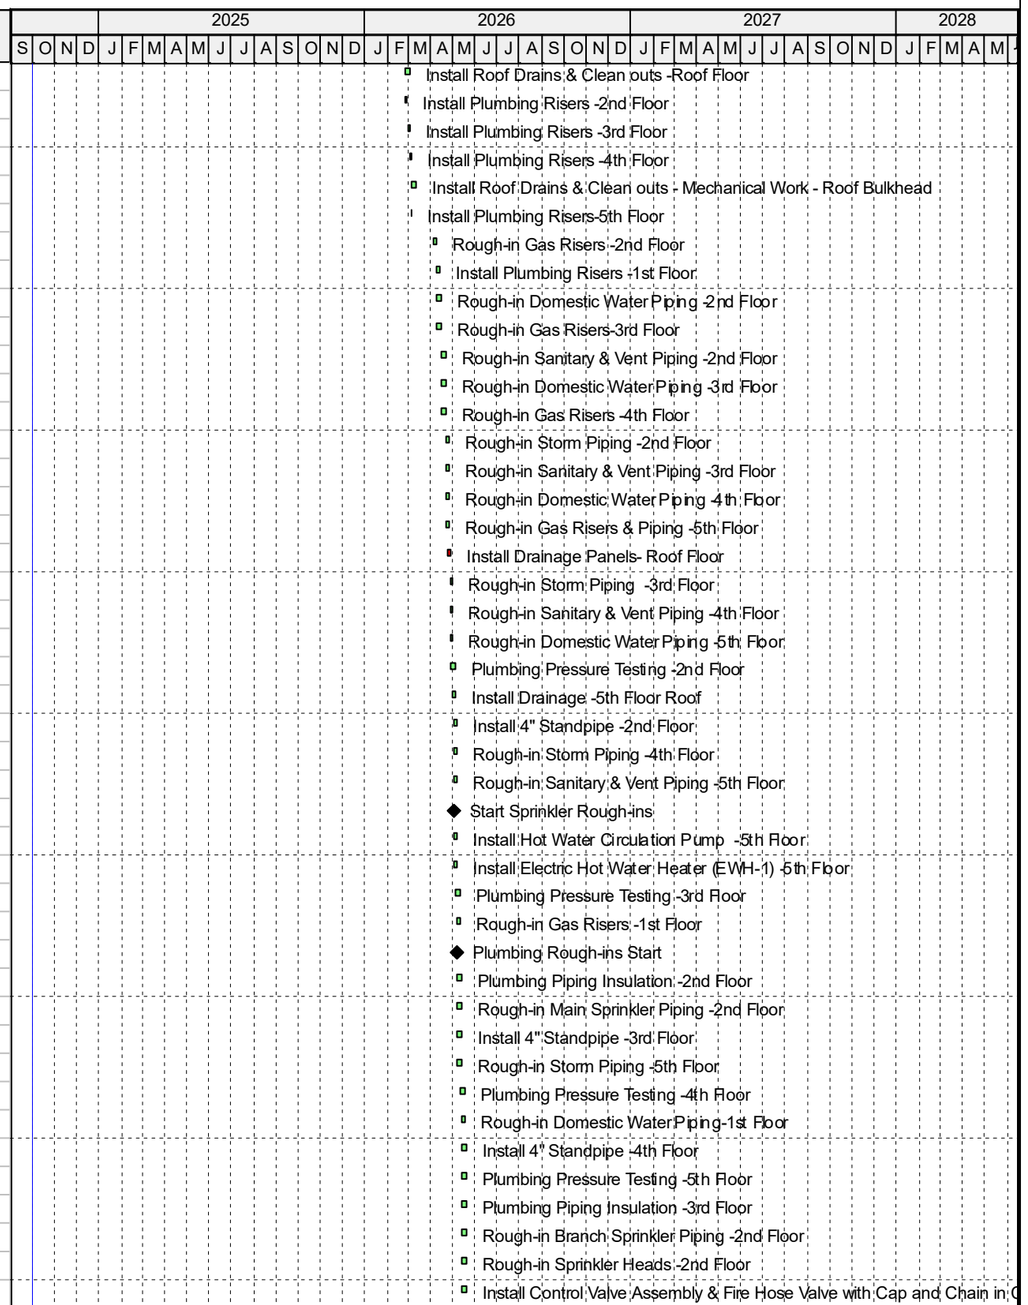

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3690	Rough-in Main Sprinkler Piping-3rd Floor	5	15-May-26	21-May-26
CON-4690	Rough-in Sanitary & Vent Piping -1st Floor	4	19-May-26	22-May-26
CON-3770	Install 4" Standpipe -5th Floor	4	20-May-26	26-May-26
CON-4390	Plumbing Piping Insulation -4th Floor	5	21-May-26	28-May-26
CON-3790	Rough-in Branch Sprinkler Piping -3rd Floor	5	22-May-26	29-May-26
CON-3800	Rough-in Sprinkler Heads -3rd Floor	5	22-May-26	29-May-26
CON-3880	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-3rd Floor	5	22-May-26	29-May-26
CON-3810	Rough-in Main Sprinkler Piping-4th Floor	5	22-May-26	29-May-26
CON-3830	Sprinklers Air Testing-2nd Floor	5	22-May-26	29-May-26
CON-4760	Rough-in Storm Piping -1st Floor	4	26-May-26	29-May-26
CON-3890	Install 4" Standpipe -Roof	4	27-May-26	01-Jun-26
CON-4530	Plumbing Piping Insulation -5th Floor	5	29-May-26	04-Jun-26
MIL-1320	Plumbing Rough-ins Finish	0		29-May-26
CON-3990	Rough-in Branch Sprinkler Piping -4th Floor	5	01-Jun-26	05-Jun-26
CON-4000	Rough-in Sprinkler Heads -4th Floor	5	01-Jun-26	05-Jun-26
CON-4100	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-4th Floor	5	01-Jun-26	05-Jun-26
CON-4010	Rough-in Main Sprinkler Piping -5th Floor	5	01-Jun-26	05-Jun-26
CON-4060	Sprinklers Air Testing-3rd Floor	5	01-Jun-26	05-Jun-26
CON-4940	Install Duplex Domestic Water Booster Pump System (BP-1&BP-2) -1st Floor	8	01-Jun-26	10-Jun-26
CON-4950	Install Duplex Ejector Pump System (EJ-1&EJ-2) -1st Floor	8	01-Jun-26	10-Jun-26
CON-4910	Install 4" Standpipe -1st Floor	4	02-Jun-26	05-Jun-26
MIL-2952	Finish Standpipe System Inspection	0		05-Jun-26
CON-5030	Rough-in Main Sprinkler Piping -1st Floor	5	08-Jun-26	12-Jun-26
CON-4230	Rough-in Branch Sprinkler Piping -5th Floor	5	08-Jun-26	12-Jun-26
CON-4240	Rough-in Sprinkler Heads -5th Floor	5	08-Jun-26	12-Jun-26
CON-4340	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -5th Floor	5	08-Jun-26	12-Jun-26
CON-4250	Rough-in Main Sprinkler Piping -Roof	5	08-Jun-26	12-Jun-26
CON-4280	Sprinklers Air Testing-4th Floor	5	08-Jun-26	12-Jun-26
CON-5050	Plumbing Pressure Testing -1st Floor	5	11-Jun-26	17-Jun-26
CON-5230	Rough-in Branch Sprinkler Piping -1st Floor	5	15-Jun-26	22-Jun-26
CON-5240	Rough-in Sprinkler Heads -1st Floor	5	15-Jun-26	22-Jun-26
CON-4430	Rough-in Branch Sprinkler Piping -Roof	5	15-Jun-26	22-Jun-26
CON-4440	Rough-in Sprinkler Heads -Roof	5	15-Jun-26	22-Jun-26
CON-4490	Sprinklers Air Testing-5th Floor	5	15-Jun-26	22-Jun-26
CON-5210	Plumbing Piping Insulation -1st Floor	5	18-Jun-26	25-Jun-26
MIL-1330	Finish Sprinkler Rough-ins	0		22-Jun-26
CON-5270	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -1st Floor	5	23-Jun-26	29-Jun-26
CON-4650	Install 3 Way Roof Manifold -Roof	5	23-Jun-26	29-Jun-26
CON-5410	Sprinklers Air Testing-1st Floor	5	30-Jun-26	07-Jul-26
MIL-2592	P&D - Connection to Roof Drains	0	28-Jul-26	
Grand Mechanical Corp.		187	22-Dec-25	18-Sep-26
CON-1130	Install MEP Hangers & Sleeves- 2nd Floor	4	22-Dec-25	26-Dec-25
CON-1230	Install MEP Hangers & Sleeves-3rd Floor	4	09-Jan-26	14-Jan-26
CON-1310	Install MEP Hangers & Sleeves-4th Floor	4	29-Jan-26	03-Feb-26

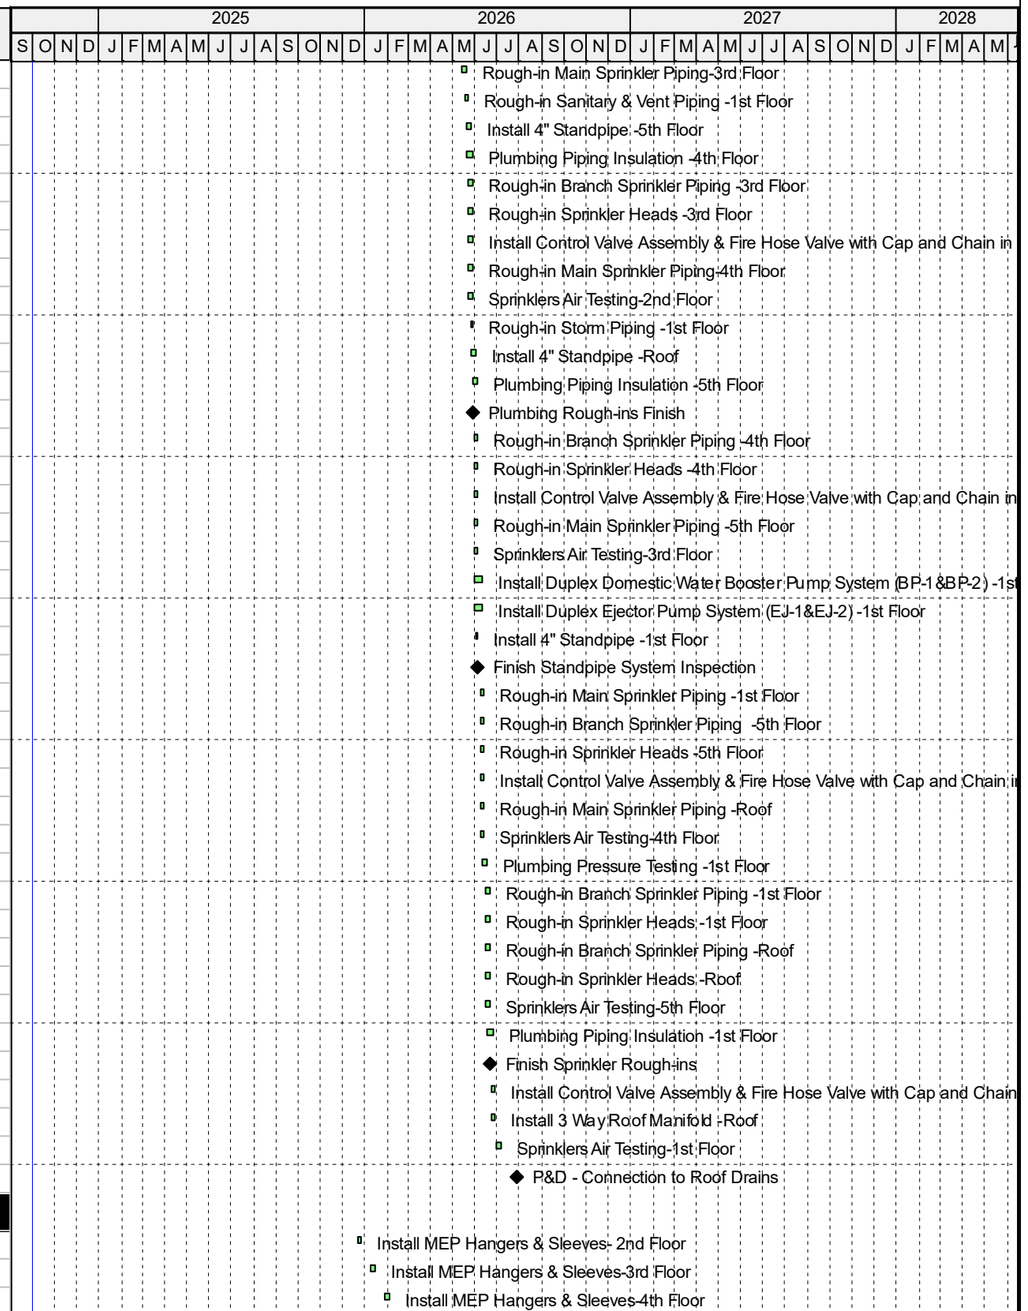

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-1400	Install MEP Hangers & Sleeves-5th Floor	4	17-Feb-26	20-Feb-26
CON-1410	Install Duct Risers-2nd Floor	1	23-Feb-26	23-Feb-26
MIL-1180	MEP Risers Start	0	23-Feb-26	
CON-1480	Rough-in Duct Work -2nd Floor	4	24-Feb-26	27-Feb-26
CON-1490	Install Duct Risers -3rd Floor	2	24-Feb-26	25-Feb-26
CON-1500	Install Mechanical Piping Risers-2nd Floor	2	24-Feb-26	25-Feb-26
MIL-1210	Duct Rough-ins Start	0	24-Feb-26	
CON-1510	Duct Leak Test -2nd Floor	2	24-Feb-26	25-Feb-26
CON-1560	Install Duct Risers -4th Floor	2	26-Feb-26	27-Feb-26
CON-1590	Install Mechanical Piping Risers -3rd Floor	2	26-Feb-26	27-Feb-26
CON-1600	Duct Leak Test -3rd Floor	2	26-Feb-26	27-Feb-26
CON-1610	Install MEP Hangers & Sleeves-Roof Floor	4	27-Feb-26	04-Mar-26
CON-1850	Rough-in Hot Water Piping -2nd Floor	7	02-Mar-26	10-Mar-26
CON-1860	Rough-in Hot Glycol Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1870	Rough-in Chilled Glycol Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1880	Rough-in Refrigerant Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-1890	Rough-in Duct Work -3rd Floor	5	02-Mar-26	06-Mar-26
CON-1630	Install Duct Risers-5th Floor	2	02-Mar-26	03-Mar-26
CON-1690	Install Mechanical Piping Risers -4th Floor	2	02-Mar-26	03-Mar-26
CON-1700	Duct Leak Test -4th Floor	2	02-Mar-26	03-Mar-26
CON-1790	Install Mechanical Piping Risers-5th Floor	2	04-Mar-26	05-Mar-26
CON-1810	Duct Leak Test -5th Floor	1	04-Mar-26	04-Mar-26
CON-2160	Rough-in Refrigerant Piping-3rd Floor	7	09-Mar-26	17-Mar-26
CON-2170	Rough-in Duct Work -4th Floor	5	09-Mar-26	13-Mar-26
CON-2130	Rough-in Hot Water Piping -3rd Floor	7	11-Mar-26	19-Mar-26
CON-2140	Rough-in Hot Glycol Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-2150	Rough-in Chilled Glycol Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-2190	Install Electric Unit Heater EUH - Mechanical Work - Roof Bulkhead	5	12-Mar-26	18-Mar-26
CON-2290	Rough-in Refrigerant Piping-4th Floor	7	16-Mar-26	24-Mar-26
CON-2300	Rough-in Duct Work-5th Floor	5	16-Mar-26	20-Mar-26
CON-2120	Install Air Cooled Chiller CH-1 -Roof Floor	7	17-Mar-26	25-Mar-26
CON-3980	Install VAV Boxes & Sound Attenuator Devices-2nd Floor	5	19-Mar-26	25-Mar-26
CON-2230	Install Emergency Generator -Bulkhead	7	19-Mar-26	27-Mar-26
CON-2260	Rough-in Hot Water Piping -4th Floor	7	20-Mar-26	30-Mar-26
CON-2270	Rough-in Hot Glycol Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-2280	Rough-in Chilled Glycol Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-2470	Rough-in Refrigerant Piping-5th Floor	7	23-Mar-26	31-Mar-26
CON-4140	Install VAV Boxes & Sound Attenuator Devices-3rd Floor	5	26-Mar-26	01-Apr-26
CON-2350	Install Air Cooled Chiller CH-2 -Roof Floor	7	26-Mar-26	03-Apr-26
CON-2360	Install Smoke Purge Fan SPF - Mechanical Work - Roof Bulkhead	3	26-Mar-26	30-Mar-26
CON-2440	Rough-in Hot Water Piping -5th Floor	7	31-Mar-26	08-Apr-26
CON-2450	Rough-in Hot Glycol Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-2460	Rough-in Chilled Glycol Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-4220	Install VAV Boxes & Sound Attenuator Devices-4th Floor	5	02-Apr-26	08-Apr-26

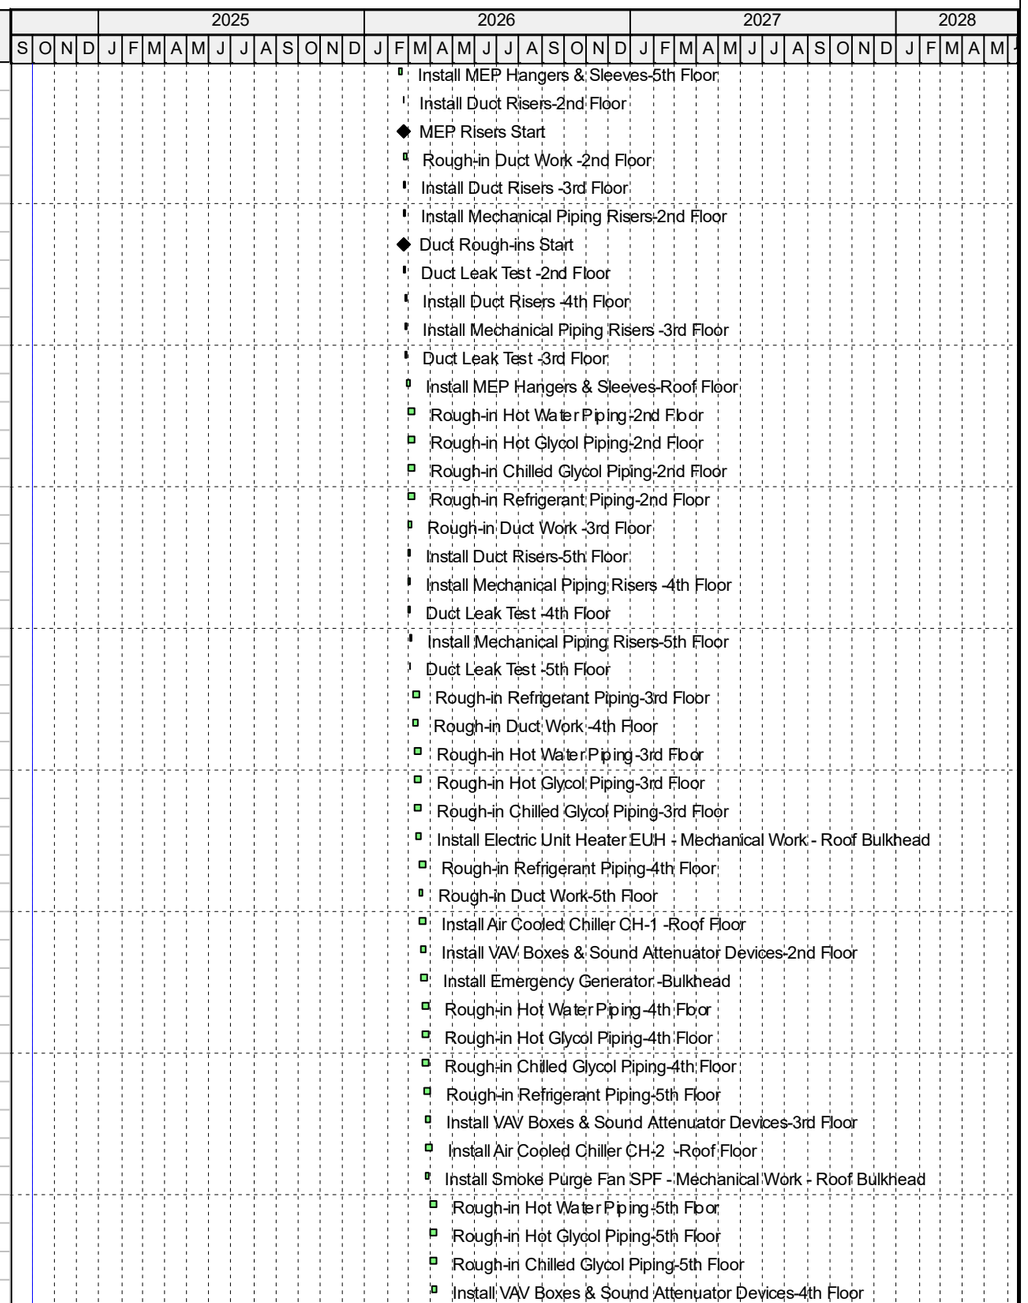

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2900	Install Duct Risers-1st Floor	1	07-Apr-26	07-Apr-26
CON-3060	Install Mechanical Piping Risers-1st Floor	2	08-Apr-26	09-Apr-26
CON-3070	Duct Leak Test -1st Floor	1	08-Apr-26	08-Apr-26
MIL-2602	Start Mechanical Distribution Lines	0	08-Apr-26	
CON-3120	Rough-in Duct Work -1st Floor	4	09-Apr-26	14-Apr-26
CON-4330	Install VAV Boxes & Sound Attenuator Devices-5th Floor	5	09-Apr-26	15-Apr-26
MIL-1290	Duct Rough-ins Finish	0		14-Apr-26
CON-3460	Rough-in Hot Water Piping -1st Floor	4	15-Apr-26	20-Apr-26
CON-3470	Rough-in Hot Glycol Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3480	Rough-in Chilled Glycol Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3490	Rough-in Refrigerant Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3970	Install VAV Boxes & Sound Attenuator Devices- 1st Floor	5	16-Apr-26	22-Apr-26
CON-2850	Install Electric Unit Heaters -2nd Floor	5	16-Apr-26	22-Apr-26
CON-3130	Install Electric Unit Heaters -3rd Floor	5	23-Apr-26	29-Apr-26
CON-3150	Install Convector Heater CV - Mechanical Work - 2nd Floor	5	23-Apr-26	29-Apr-26
CON-3420	Install Electric Unit Heaters -4th Floor	5	30-Apr-26	06-May-26
CON-3450	Install Air Conditioning Unit AC - Mechanical Work - 2nd Floor	4	30-Apr-26	05-May-26
CON-3640	Install Electric Unit Heaters -5th Floor	3	07-May-26	11-May-26
CON-4070	Install Duct Insulation -2nd Floor	8	07-May-26	18-May-26
CON-5180	Install Service Switchboard "SS-A"- Electric Service Room	5	11-May-26	15-May-26
CON-5510	Install Leak Detector - Electric Service Room	3	18-May-26	20-May-26
CON-4320	Install Duct Insulation -3rd Floor	8	19-May-26	29-May-26
CON-5610	Install Sprinkler Booster Pump - Electric Service Room	4	21-May-26	27-May-26
CON-5640	Install Fire Alarm Normal ATS - Electric Service Room	4	28-May-26	02-Jun-26
CON-4900	Rough-in Fuel Oil Piping -Fuel Oil Room	3	01-Jun-26	03-Jun-26
CON-4570	Install Duct Insulation -4th Floor	8	01-Jun-26	10-Jun-26
I-1110	Fuel-Oil Storage & Fuel Oil Piping Systems Inspection	9	01-Jun-26	11-Jun-26
CON-4990	Install Fuel Oil Storage Tank (FOT-1) - Fuel Oil Room	3	03-Jun-26	05-Jun-26
CON-5780	Install Motorized Fire/Smoke Damper & Control Panel - Electric Service Room	5	03-Jun-26	09-Jun-26
CON-5790	Install Main Grounding Bus Bar - Electric Service Room	4	03-Jun-26	08-Jun-26
CON-5020	Rough-in Fuel Oil Fill Piping -Fuel Oil Room	3	04-Jun-26	08-Jun-26
CON-2250	Install Air Handling Unit AHU-1 -Roof Floor	5	08-Jun-26	12-Jun-26
CON-5160	Install Fuel Oil Transfer Duplex Pump (FOP-1 & 2) -1st Floor	4	08-Jun-26	11-Jun-26
MIL-1460	Roof Top Units Installations Start	0	08-Jun-26	
CON-9130	Install Switch Gear - Electric Service Room	5	08-Jun-26	12-Jun-26
CON-5200	Rough-in Fuel Oil Vent Piping -Fuel Oil Room	4	09-Jun-26	12-Jun-26
CON-5840	Install Electric Unit Heater EUH-6 - Electric Service Room	4	10-Jun-26	15-Jun-26
CON-4710	Install Duct Insulation -5th Floor	8	11-Jun-26	23-Jun-26
CON-2430	Install Air Handling Unit AHU-2 -Roof Floor	5	15-Jun-26	22-Jun-26
CON-2560	Install Air Handling Unit AHU-3 -Roof Floor	5	23-Jun-26	29-Jun-26
CON-4840	Install Duct Insulation -1st Floor	8	24-Jun-26	06-Jul-26
CON-2720	Install Air Handling Unit AHU-4 -Roof Floor	5	30-Jun-26	07-Jul-26
MIL-2632	Finish HVAC	0		06-Jul-26
CON-4670	Install Exhaust Fans -1st Floor	5	07-Jul-26	13-Jul-26

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
CLO-1010	HVAC Flush-Out	20	07-Jul-26	03-Aug-26
MIL-2732	Start Mechanical and Electrical System Commissioning	0	07-Jul-26	
CON-2860	Install Fume Hood Exhaust -Roof Floor	3	08-Jul-26	10-Jul-26
CON-5770	Install Air Cooled Condensing Unit ACCU - Mechanical Work - 5th Floor	5	08-Jul-26	14-Jul-26
CON-3000	Install Smoke Purge Fan -Roof Floor	3	13-Jul-26	15-Jul-26
CON-4870	Install Cabinet Unit Heaters With Fan CUH-1st Floor	3	14-Jul-26	16-Jul-26
CON-4880	Install Motorized Fire/Smoke Damper FSD - Mechanical Work - 1st Floor	7	14-Jul-26	22-Jul-26
MIL-1480	Roof Top Units Installations Finish	0		14-Jul-26
MIL-2972	Finish Mechanical System Inspection	0		15-Jul-26
CON-5060	Install Hot Glycol / Hot Water Cabinet Heater (CUH)-3rd Floor	4	17-Jul-26	22-Jul-26
CON-5070	Install Electric Unit Heaters -1st Floor	7	17-Jul-26	27-Jul-26
CON-6050	Install Boiler B-1-Boiler Room	5	23-Jul-26	29-Jul-26
CON-5260	Install Cabinet Unit Heater With Fan CUH -4th Floor	4	23-Jul-26	28-Jul-26
CON-5860	Install Sprinkler Booster Pump (SBP-1) -1st Floor	10	23-Jul-26	05-Aug-26
CON-5150	Install Air Conditioning Unit AC - Mechanical Work - 1 st Floor	4	23-Jul-26	28-Jul-26
CON-5280	Install Convector Heater CV - Mechanical Work - 3rd Floor	4	23-Jul-26	28-Jul-26
CON-5300	Install Grease Interceptors - 1st Floor	5	28-Jul-26	03-Aug-26
CLO-1240	Elevator Sump Pump Testing & Commissioning	21	28-Jul-26	25-Aug-26
CLO-1270	Water Heater Testing & Commissioning	21	28-Jul-26	25-Aug-26
CON-5430	Install Hot Glycol / Hot Water Cabinet Heater (CUH)-5th Floor	4	29-Jul-26	03-Aug-26
CON-5320	Install Door Curtains DC - Mechanical Work - 1st Floor	7	29-Jul-26	06-Aug-26
CON-5450	Install Air Conditioning Unit AC - Mechanical Work - 3rd Floor	4	29-Jul-26	03-Aug-26
CON-5460	Install Convector Heater CV - Mechanical Work - 4th Floor	3	29-Jul-26	31-Jul-26
CON-6110	Install Boiler B-2-Boiler Room	5	30-Jul-26	05-Aug-26
CON-6130	Install Boiler Condensate ACID Neutralization Tubes -Boiler Room	2	30-Jul-26	31-Jul-26
CON-6200	Install Expansion Tanks (ET-1 , ET-2 & ET-3)	2	03-Aug-26	04-Aug-26
CON-6210	Install Glycol Make-up Units (GF-1 & GF-2 & GF-3)	2	03-Aug-26	04-Aug-26
CON-6220	Install Reduced Pressure Zone (RPZ) Devices -Boiler Room	2	03-Aug-26	04-Aug-26
MIL-2692	Building HVAC Flush-out	0		03-Aug-26
CON-5620	Install Air Conditioning Unit AC - Mechanical Work - 4th Floor	4	04-Aug-26	07-Aug-26
CON-5590	Install Exhaust Fan EF - Mechanical Work - 5th Floor	4	04-Aug-26	07-Aug-26
CLO-1230	Air Handling Unit Testing & Commissioning	21	04-Aug-26	01-Sep-26
CLO-1290	Glycol System Testing & Commissioning	21	05-Aug-26	02-Sep-26
CON-6260	Install Heat Exchanger -Boiler Room	2	06-Aug-26	07-Aug-26
CON-6100	Install Jockey Pump (JP-1) -1st Floor	10	06-Aug-26	19-Aug-26
CON-5490	Install Convector Heater CV - Mechanical Work - 1st Floor	7	07-Aug-26	17-Aug-26
CON-6290	Install Hot Glycol Units Heaters (UH-5-1, UH-5-2)	2	10-Aug-26	11-Aug-26
CON-5630	Install Convector Heater CV - Mechanical Work - 5th Floor	3	10-Aug-26	12-Aug-26
CLO-1260	HVAC Split System Testing & Commissioning	21	10-Aug-26	08-Sep-26
CON-6330	Install Heat Pump Electric Hot Water Heater (HPWH#1&2)-Boiler Room	2	12-Aug-26	13-Aug-26
CON-6340	Install Exhaust Fans -Boiler Room	2	14-Aug-26	17-Aug-26
CON-6350	Install Primary Hot Water Pump (GHWP 1 to 3) -Boiler Room	2	14-Aug-26	17-Aug-26
CON-6360	Install Primary Chilled Water Pump (GCHWP-1&2)-Boiler Room	2	14-Aug-26	17-Aug-26
CON-6240	Install Fine Tube Radiator FTR - Gymnatorium	5	17-Aug-26	21-Aug-26

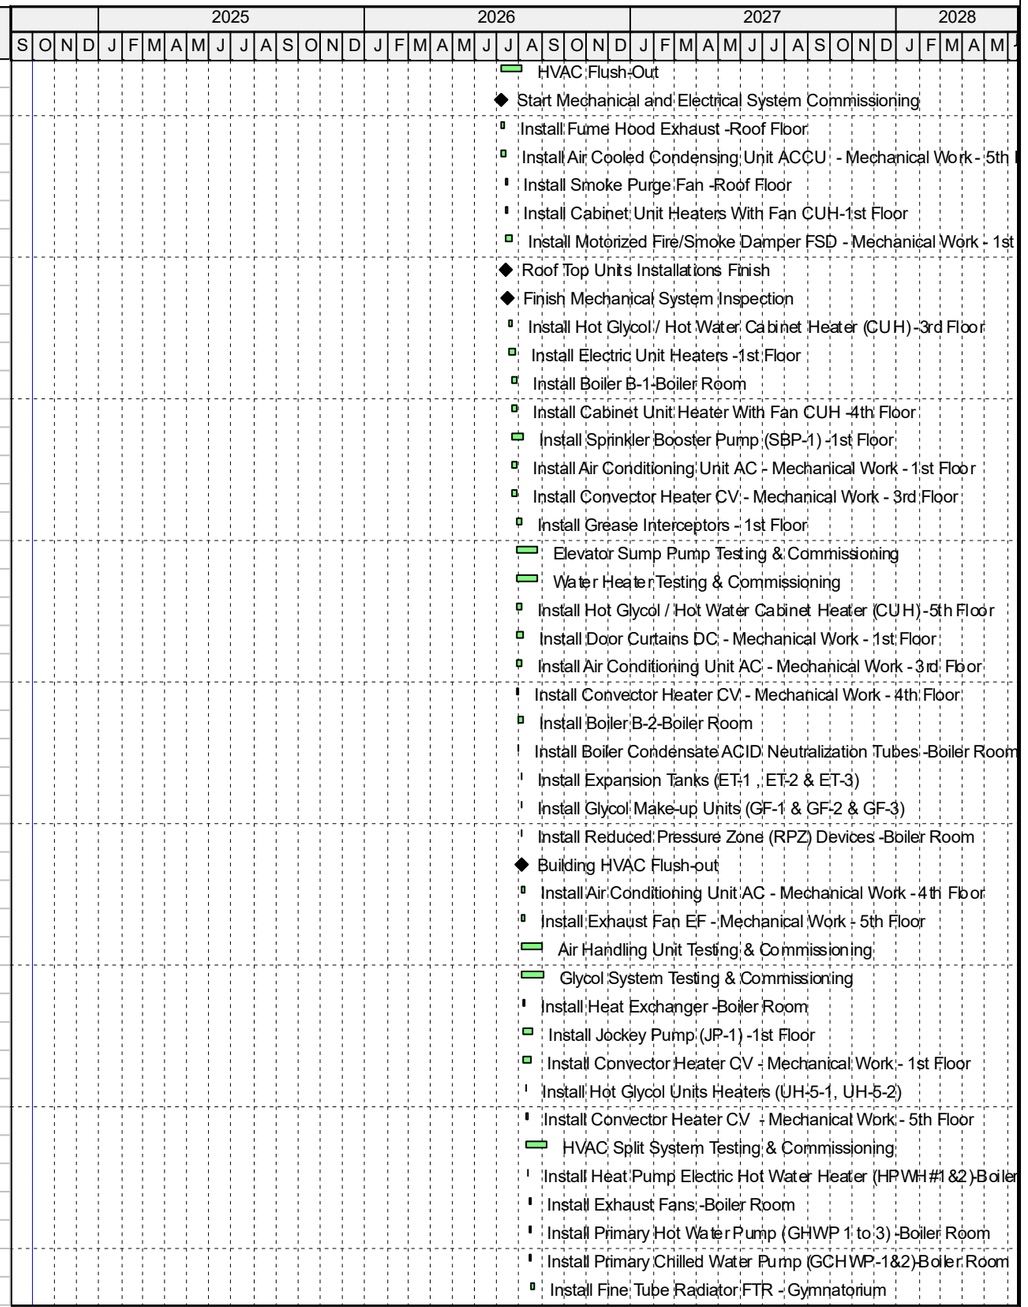

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-6400	Install Secondary Hot Water Pump(HWP-1&2)-Boiler Room	2	18-Aug-26	19-Aug-26
CON-6410	Install Electric Unit Heater (EUH-3) - Boiler Room	2	18-Aug-26	19-Aug-26
CON-6420	Install Branch Panels (BRPP) -Boiler Room	2	18-Aug-26	19-Aug-26
CLO-1160	Sprinkler/Domestic Booster Pumps Testing & Commissioning	14	20-Aug-26	09-Sep-26
CLO-1180	Sprinkler/Domestic Booster Pumps Sign-offs	0		14-Sep-26
MIL-2652	Finish Mechanical and Electrical System Commissioning	0		18-Sep-26
MIL-2772	Performance test for all mechanical equipment and low voltage systems	0		18-Sep-26
MIL-2792	Commissioning for all mechanical equipment and low voltage systems	0		18-Sep-26
Noble Elevators		191	29-Dec-25	30-Sep-26
CON-1160	Hoist Material Design	10	29-Dec-25	12-Jan-26
CON-1250	Approval of Hoist Design	7	13-Jan-26	19-Jan-26
CON-1280	Install Elevator Hoist Pad	5	20-Jan-26	26-Jan-26
CON-1320	Erect Material Hoist	5	27-Jan-26	02-Feb-26
MIL-1760	Start Elevator Work	0	07-May-26	
CON-99357	Install CMU Wall for Shaft -Elevator Machine Room	10	07-May-26	20-May-26
CON-99167	Install Elevator Guide Rails -Elevator Machine Room	8	21-May-26	02-Jun-26
CON-2090	Install Elevator Controller #1 -Elevator Machine Room	10	03-Jun-26	16-Jun-26
CON-2370	Install Elevator Controller #2 -Elevator Machine Room	10	17-Jun-26	01-Jul-26
CON-2580	Install Power Panels -Elevator Machine Room	7	02-Jul-26	13-Jul-26
CON-2790	Rough-in Conduits & Wires-Elevator Machine Room	6	14-Jul-26	21-Jul-26
CON-99157	Install Elevator Sump Pump -Elevator Machine Room	10	14-Jul-26	27-Jul-26
CON-3100	Install Elevator Cabinet (1) -Elevator Machine Room	10	22-Jul-26	04-Aug-26
CON-3620	Install Elevator Cabinet (2) -Elevator Machine Room	10	22-Jul-26	04-Aug-26
MIL-2822	Elevator Ready for Testing	0		11-Aug-26
CLO-1000	Elevator Testing & Commissioning	20	12-Aug-26	09-Sep-26
CON-6250	Install Hydraulic Vertical Wheelchair Lift -Gymnatorium	8	17-Aug-26	26-Aug-26
CON-5040	Dismantle Hoist	2	10-Sep-26	11-Sep-26
CON-5170	Demolish Hoist Pad	2	14-Sep-26	15-Sep-26
CON-5250	Hoist In-Fill	2	16-Sep-26	17-Sep-26
PER-2650	Elevator Equipment Use Permit	10	17-Sep-26	30-Sep-26
MIL-1670	Elevator Final Sign-off	0		30-Sep-26
RMD Electric		200	03-Dec-25	18-Sep-26
CON-99327	Install Lightning Protection System-1st Floor	2	03-Dec-25	04-Dec-25
CON-1710	Install Power Risers-2nd Floor	2	02-Mar-26	03-Mar-26
CON-1800	Install Low Voltage Risers-2nd Floor	2	04-Mar-26	05-Mar-26
CON-1820	Install Power Risers-3rd Floor	2	04-Mar-26	05-Mar-26
CON-99347	Install Lightning Protection System - Roof Floor	6	05-Mar-26	12-Mar-26
CON-1950	Install Low Voltage Risers-3rd Floor	2	06-Mar-26	09-Mar-26
CON-1960	Install Power Risers-4th Floor	2	06-Mar-26	09-Mar-26
CON-2040	Install Low Voltage Risers-4th Floor	2	10-Mar-26	11-Mar-26
CON-2050	Install Power Risers-5th Floor	3	10-Mar-26	12-Mar-26
CON-2180	Rough-in Power Conduits -2nd Floor	6	11-Mar-26	18-Mar-26
CON-2100	Install Low Voltage Risers-5th Floor	3	13-Mar-26	17-Mar-26
CON-99337	Install Lightning Protection system -5th Floor	3	13-Mar-26	17-Mar-26

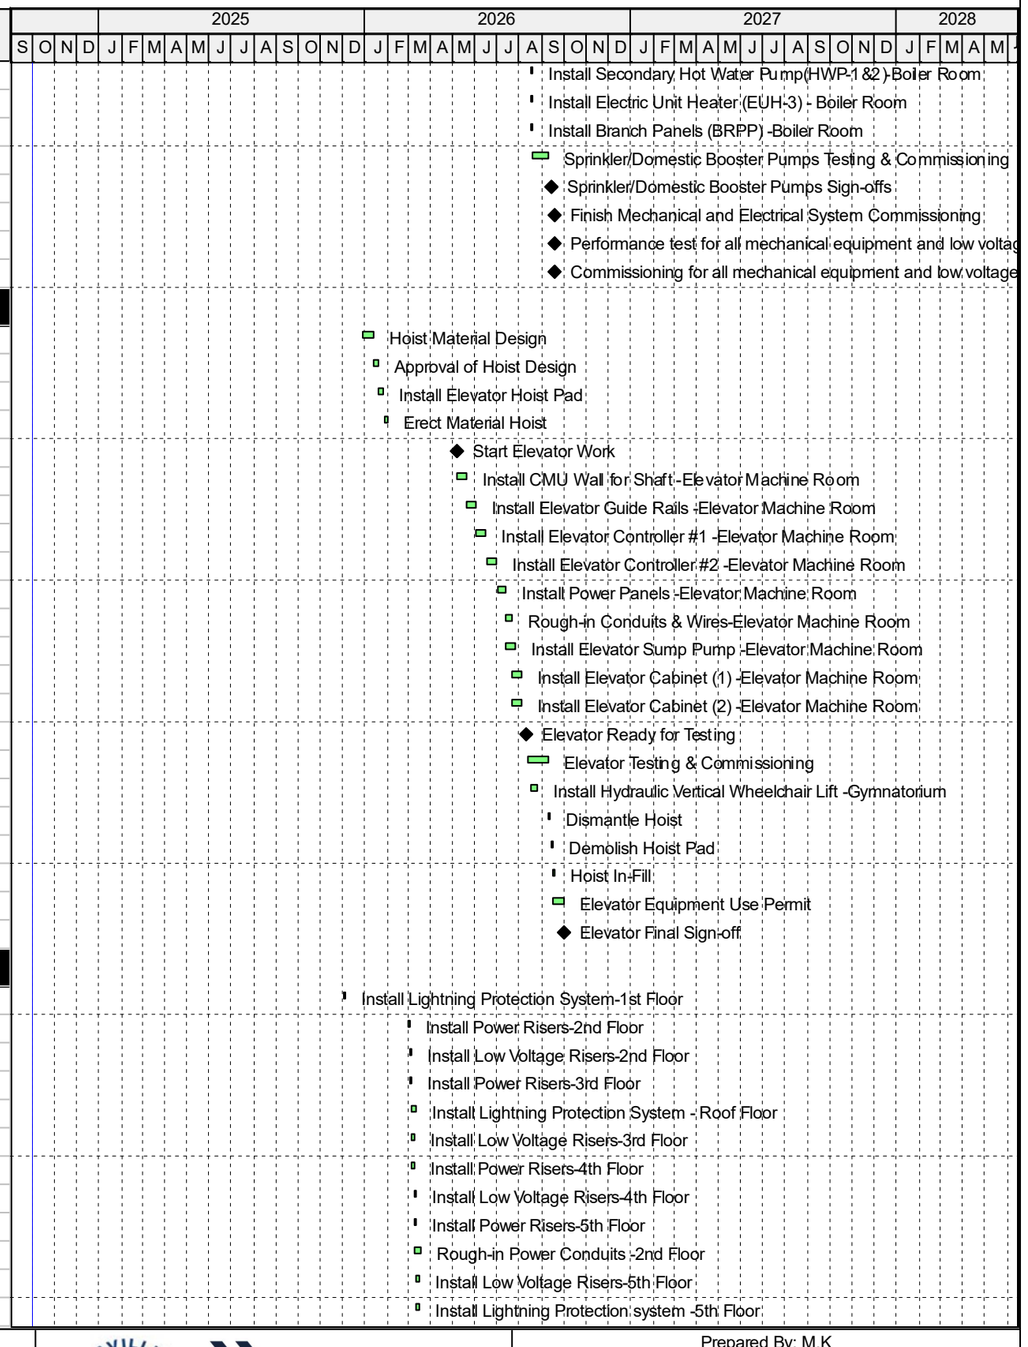

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2320	Rough-in Power Conduits-3rd Floor	6	19-Mar-26	26-Mar-26
CON-2330	Rough-in Low-Voltage Conduits -2nd Floor	6	19-Mar-26	26-Mar-26
CON-2340	Power Wires Pulling -2nd Floor	6	19-Mar-26	26-Mar-26
CON-2640	Install Grounding Bars - 3rd Floor IDF Room	5	27-Mar-26	02-Apr-26
CON-2480	Rough-in Power Conduits-4th Floor	6	27-Mar-26	03-Apr-26
CON-2490	Low Voltage Wires Pulling -2nd Floor	6	27-Mar-26	03-Apr-26
CON-2500	Rough-in Low-Voltage Conduits-3rd Floor	6	27-Mar-26	03-Apr-26
CON-2510	Power Wires Pulling-3rd Floor	6	27-Mar-26	03-Apr-26
CON-2520	Install Voice Rack - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2530	Install Data Rack - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2540	Install Ground Bus Bar - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-2800	Install Data rack - 3rd Floor IDF Room	8	03-Apr-26	14-Apr-26
CON-2830	Install IPDVS Equipment Rack - 3rd Floor IDF Room	4	03-Apr-26	08-Apr-26
CON-2810	Install Grounding Bars - 4th Floor IDF Room	5	06-Apr-26	10-Apr-26
CON-2650	Install Data Rack - 4th Floor IDF Room	7	06-Apr-26	14-Apr-26
CON-2660	Install Voice Rack - 4th Floor IDF Room	5	06-Apr-26	10-Apr-26
CON-2670	Install Wiring Devices -2nd Floor	7	06-Apr-26	14-Apr-26
CON-2680	Rough-in Power Conduits -5th Floor	6	06-Apr-26	13-Apr-26
CON-2690	Low Voltage Wires Pulling -3rd Floor	6	06-Apr-26	13-Apr-26
CON-2700	Rough-in Low-Voltage Conduits-4th Floor	6	06-Apr-26	13-Apr-26
CON-2710	Power Wires Pulling-4th Floor	6	06-Apr-26	13-Apr-26
MIL-1270	Electrical Rough-ins Start	0	09-Apr-26	
CON-2760	Install IPDVS Equipment Rack - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2770	Install Ladder Rack Cable Tray - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2780	Install BACnet Data Cabinet - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26
CON-2820	Install Cable Ladder - 4th Floor IDF Room	5	13-Apr-26	17-Apr-26
CON-2840	Install Main Sound Rack - 34th Floor IDF Room	5	13-Apr-26	17-Apr-26
CON-3260	Install Power Risers-1st Floor	2	14-Apr-26	15-Apr-26
CON-2950	Rough-in Low-Voltage Conduits-5th Floor	6	14-Apr-26	21-Apr-26
CON-2960	Power Wires Pulling-5th Floor	6	14-Apr-26	21-Apr-26
CON-3250	Install Voice Rack - 3rd Floor IDF Room	5	15-Apr-26	21-Apr-26
CON-2930	Install Wiring Devices -3rd Floor	7	15-Apr-26	23-Apr-26
CON-2940	Low Voltage Wires Pulling-4th Floor	6	15-Apr-26	22-Apr-26
CON-3350	Install Low Voltage Risers-1st Floor	2	16-Apr-26	17-Apr-26
MIL-2712	Start Low Voltage	0	16-Apr-26	
CON-3110	Install IPDVS Equipment Rack - 4th Floor IDF Room	5	20-Apr-26	24-Apr-26
CON-3760	Rough-in Power Conduits -1st Floor	4	21-Apr-26	24-Apr-26
CON-3550	Install Cable Ladder - 3rd Floor IDF Room	5	22-Apr-26	28-Apr-26
CON-3570	Install Main Sound Rack - 3rd Floor IDF Room	5	22-Apr-26	28-Apr-26
CON-3290	Low Voltage Wires Pulling-5th Floor	6	23-Apr-26	30-Apr-26
CON-4730	Rough-in Conduits & Wires - Electric Service Room	6	23-Apr-26	30-Apr-26
CON-3280	Install Wiring Devices -4th Floor	7	24-Apr-26	04-May-26
CON-3910	Install Grounding System -1st Floor	5	27-Apr-26	01-May-26
CON-3920	Rough-in Low-Voltage Conduits-1st Floor	4	27-Apr-26	30-Apr-26

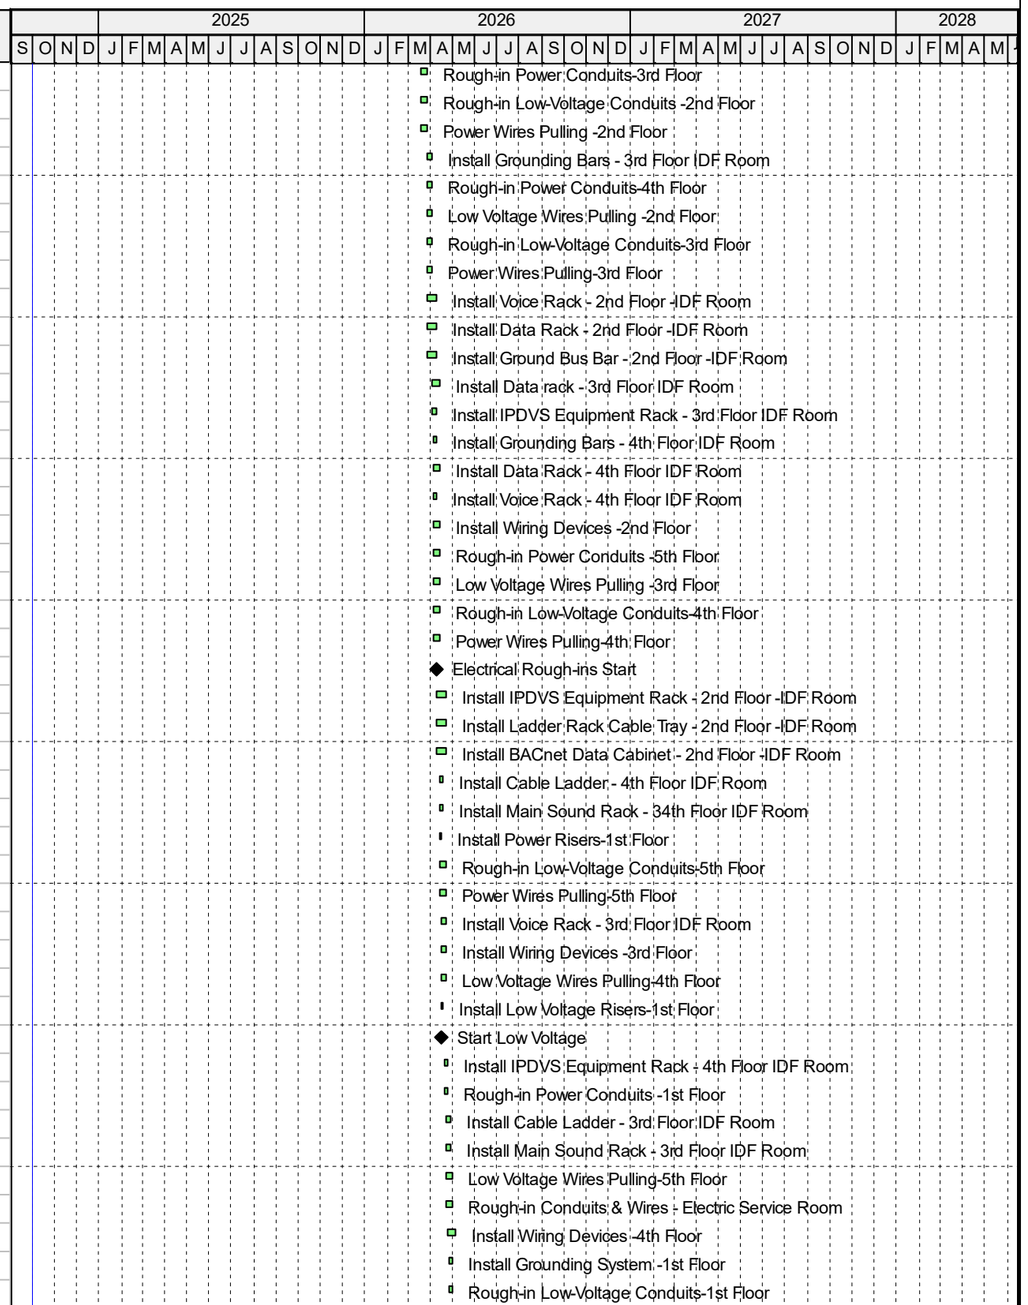

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3930	Power Wires Pulling-1st Floor	4	27-Apr-26	30-Apr-26
CON-3740	Install Ground Bus Bar - 1st Floor MDF Room	6	29-Apr-26	06-May-26
CON-4180	Low Voltage Wires Pulling -1st Floor	4	01-May-26	06-May-26
CON-3660	Install Wiring Devices -5th Floor	8	05-May-26	14-May-26
MIL-1350	Electrical Rough-ins Finish	0		06-May-26
CON-4110	Install Voice Rack - 1st Floor MDF Room	6	07-May-26	14-May-26
CON-4510	Install Sound Rack - 1st Floor MDF Room	6	15-May-26	22-May-26
CON-4120	Install Project Connect Cabinet - 1st Floor MDF Room	8	15-May-26	27-May-26
CON-4470	Install Wiring Devices -1st Floor	7	15-May-26	26-May-26
CON-4520	Install Data Rack - 1st Floor MDF Room	6	26-May-26	02-Jun-26
CON-4550	Install UPS- 1st Floor MDF Room	9	03-Jun-26	15-Jun-26
CON-4130	Install BACnet Data Cabinet- 1st Floor MDF Room	9	03-Jun-26	15-Jun-26
CON-4780	Install IPDVS Equipment Rack - 1st Floor MDF Room	6	16-Jun-26	24-Jun-26
CON-5130	Install Lighting Fixtures -2nd Floor	5	18-Jun-26	25-Jun-26
CON-98797	Install Intrusion System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-98847	Install Auxiliary System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-98897	Install Sound Clock System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-4790	Install Ladder Rack Cable Tray- 1st Floor MDF Room	6	25-Jun-26	02-Jul-26
CON-5310	Install Fire alarm Sensors and Devises -2nd Floor	5	26-Jun-26	02-Jul-26
CON-5370	Install Lighting Fixtures -3rd Floor	6	29-Jun-26	07-Jul-26
CON-98807	Install Intrusion System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-98857	Install Auxiliary System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-98907	Install Sound Clock System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-4770	Install PBX - 1st Floor MDF Room	8	06-Jul-26	15-Jul-26
CON-5140	Install IPDVS Devices -2nd Floor	9	06-Jul-26	16-Jul-26
CLO-1120	MDF & IDF Rooms Testing & Commissioning	12	06-Jul-26	21-Jul-26
MIL-2982	Finish Fire-Resistant Penetrations And Joints Inspection	0		06-Jul-26
CON-5580	Install Lighting Fixtures -4th Floor	6	08-Jul-26	15-Jul-26
CON-5500	Install Fire alarm Sensors and Devises -3rd Floor	8	08-Jul-26	17-Jul-26
CON-98817	Install Intrusion System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-98867	Install Auxiliary System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-98917	Install Sound Clock System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-5740	Install Lighting Fixtures -5th Floor	6	16-Jul-26	23-Jul-26
CON-98827	Install Intrusion System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-98877	Install Auxiliary System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-98927	Install Sound Clock System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-3750	Install Emergency Generator- Roof Floor	4	17-Jul-26	22-Jul-26
CON-5440	Install IPDVS Devices -3rd Floor	9	17-Jul-26	29-Jul-26
CON-6000	Rough-in Conduits & Wires-Boiler Room	3	20-Jul-26	22-Jul-26
CON-5660	Install Fire alarm Sensors and Devises -4th Floor	7	20-Jul-26	28-Jul-26
MIL-1600	MDF Work Finish	0		21-Jul-26*
MIL-1610	IDF Work Finish	0		21-Jul-26*
CON-5380	Install Generator Connections -Roof Floor	4	23-Jul-26	28-Jul-26
CON-5940	Install Lighting Fixtures -1st Floor	7	24-Jul-26	03-Aug-26

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K

Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-98937	Install Sound Clock System Components-1st Floor	3	24-Jul-26	28-Jul-26
CON-5830	Install Fire alarm Sensors and Devises -5th Floor	5	29-Jul-26	04-Aug-26
CLO-1220	Emergency Generator Electric Load Test	3	29-Jul-26	31-Jul-26
CON-98887	Install Auxiliary System Components-1st Floor	4	29-Jul-26	03-Aug-26
CON-5750	Install IPDVS Devices -4th Floor	9	30-Jul-26	11-Aug-26
CLO-1250	Emergency Generator Testing & Commissioning	21	03-Aug-26	31-Aug-26
CON-98837	Install Intrusion System Components-1st Floor	4	04-Aug-26	07-Aug-26
CON-5950	Install Fire alarm Sensors and Devises -1st Floor	3	05-Aug-26	07-Aug-26
MIL-1680	Emergency Generator Final Sign-off	0		07-Aug-26
MIL-2642	Finish Fire Alarm Signoff	0		07-Aug-26
MIL-2962	Finish Fire Alarm Inspection	0		07-Aug-26
CLO-1020	Electrical System Testing & Commissioning	21	10-Aug-26	08-Sep-26
CLO-1280	Fire Alarm Testing & Commissioning	21	10-Aug-26	08-Sep-26
CON-6010	Install IPDVS Devices -5th Floor	9	12-Aug-26	24-Aug-26
CON-6040	Install IPDVS Devices -1st Floor	7	25-Aug-26	02-Sep-26
CON-9150	Install LED Theatrical Lighting -Gymnatorium	4	25-Aug-26	28-Aug-26
CON-6390	Install Auditorium Television Studio Dimming System -Gymnatorium	7	27-Aug-26	04-Sep-26
CLO-1130	IPDVS System Testing & Commissioning	11	03-Sep-26	18-Sep-26
MIL-1620	IPDVS Work Finish	0		18-Sep-26*
Fine Group		87	03-Mar-26	06-Jul-26
CON-1180	Spray Fireproofing - 1st Floor	5	03-Mar-26	09-Mar-26
I-1100	Fire-Resistant Penetrations And Joints Inspection	87	03-Mar-26	06-Jul-26
CON-1220	Spray Fireproofing - 2nd Floor	5	10-Mar-26	16-Mar-26
CON-1300	Spray Fireproofing - 3rd Floor	5	17-Mar-26	23-Mar-26
CON-1390	Spray Fireproofing - 4th Floor	5	24-Mar-26	30-Mar-26
CON-1730	Spray Fireproofing - 5th Floor	3	31-Mar-26	02-Apr-26
CON-1120	Install Firestopping Mock-Up	2	01-Jun-26	02-Jun-26
CON-1140	Approve Firestopping Mock-Up	2	03-Jun-26	04-Jun-26
CON-4700	Install Firestopping-2nd Floor	3	05-Jun-26	09-Jun-26
MIL-1750	Start Firestopping	0	05-Jun-26	
CON-4850	Install Firestopping-3rd Floor	4	10-Jun-26	15-Jun-26
CON-5010	Install Firestopping-4th Floor	4	16-Jun-26	22-Jun-26
CON-5220	Install Firestopping-5th Floor	4	23-Jun-26	26-Jun-26
CON-5390	Install Firestopping-1st Floor	4	30-Jun-26	06-Jul-26
Coreslab Structures		44	05-Mar-26	05-May-26
CON-1830	Install Insulated Precast Concrete Sandwich Panel - Mock Up	2	05-Mar-26	06-Mar-26
MIL-1830	Crane Mobilization-Precast Sandwich Panels Installation Start	0	05-Mar-26	
CON-2380	Install Insulated Precast Concrete Sandwich Panel - West Elevation	3	25-Mar-26	27-Mar-26
CON-2420	Install Insulated Precast Concrete Sandwich Panel - South Elevation	5	25-Mar-26	31-Mar-26
CON-2610	Install Insulated Precast Concrete Sandwich Panel - East Elevation	4	01-Apr-26	06-Apr-26
CON-2730	Install Insulated Precast Concrete Sandwich Panel - North Elevation	4	01-Apr-26	06-Apr-26
MIL-1840	Crane Mobilization-Precast Sandwich Panels Installation Finish	0		06-Apr-26
CON-3220	Dismantle Sidewalk Sheds- South Elevation	2	29-Apr-26	30-Apr-26
CON-3630	Dismantle Sidewalk Sheds- East Elevation	2	04-May-26	05-May-26

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
MIL-1730	Sidewalk Sheds Dismantle Complete	0		05-May-26
Basec Corp		38	11-Mar-26	01-May-26
CON-2110	Install & Windows Mock-Up	3	11-Mar-26	13-Mar-26
CON-2220	Install Storefront System Mock-Up	3	18-Mar-26	20-Mar-26
CON-2400	Install Windows -West Elevation	5	30-Mar-26	03-Apr-26
CON-2410	Install Storefront System-West Elevation	5	30-Mar-26	03-Apr-26
MIL-1740	Start Windows	0	30-Mar-26	
CON-2590	Install Windows - South Elevation	10	01-Apr-26	14-Apr-26
CON-2600	Install Storefront System- South Elevation	10	01-Apr-26	14-Apr-26
CON-2570	Field Testing of Windows (5%)	5	06-Apr-26	10-Apr-26
CON-2970	Field Testing of Windows (50%)	5	15-Apr-26	21-Apr-26
CON-2980	Install Windows - East Elevation	8	15-Apr-26	24-Apr-26
CON-2990	Install Storefront System- East Elevation	8	15-Apr-26	24-Apr-26
CON-3380	Install Windows -North Elevation	10	15-Apr-26	28-Apr-26
CON-3390	Install Storefront System-North Elevation	10	15-Apr-26	28-Apr-26
CON-3370	Field Testing of Windows (90%)	5	27-Apr-26	01-May-26
MIL-1580	Window Installation Finish	0		28-Apr-26
Poletech		10	15-Apr-26	28-Apr-26
CON-99237	Install Flag Pole - South Elevation	10	15-Apr-26	28-Apr-26
Arch Mills		55	11-May-26	29-Jul-26
CON-4380	Install Doors & Hardware-Mockup Room	3	11-May-26	13-May-26
CON-4260	Install Door Frames-Mockup Room	2	12-May-26	13-May-26
CON-5120	Install Door Frames & Doors-2nd Floor	5	18-Jun-26	25-Jun-26
CON-5350	Install Door Frames & Doors-3rd Floor	5	29-Jun-26	06-Jul-26
CON-5540	Install Door Frames & Doors-4th Floor	5	07-Jul-26	13-Jul-26
CON-5680	Install Door Frames & Doors -5th Floor	5	16-Jul-26	22-Jul-26
CON-5920	Install Door Frames & Doors-1st Floor	5	23-Jul-26	29-Jul-26
Roebell		74	14-May-26	28-Aug-26
CON-4480	Paint First coat -Mockup Room	2	14-May-26	15-May-26
CON-4750	Paint Second coat-Mockup Room	2	20-May-26	21-May-26
MIL-1450	Start 1st Coat Painting	0	10-Jun-26	
CON-4830	Install First Coat Painting-2nd Floor	5	11-Jun-26	17-Jun-26
CON-5110	Install First Coat Painting-3rd Floor	5	22-Jun-26	26-Jun-26
CON-5340	Install First Coat Painting-4th Floor	5	29-Jun-26	06-Jul-26
CON-5560	Install Final Coat Painting-2nd Floor	6	06-Jul-26	13-Jul-26
CON-5530	Install First Coat Painting -5th Floor	5	09-Jul-26	15-Jul-26
CON-5700	Install Final Coat Painting-3rd Floor	6	14-Jul-26	21-Jul-26
CON-5720	Install First Coat Painting-1st Floor	5	16-Jul-26	22-Jul-26
CON-5900	Install Final Coat Painting-4th Floor	6	22-Jul-26	29-Jul-26
CON-6060	Install Final Coat Painting -5th Floor	6	13-Aug-26	20-Aug-26
CON-6170	Install Final Coat Painting-1st Floor	6	21-Aug-26	28-Aug-26
MIL-2672	Finish Painting	0		28-Aug-26
Pyramid		55	18-May-26	05-Aug-26

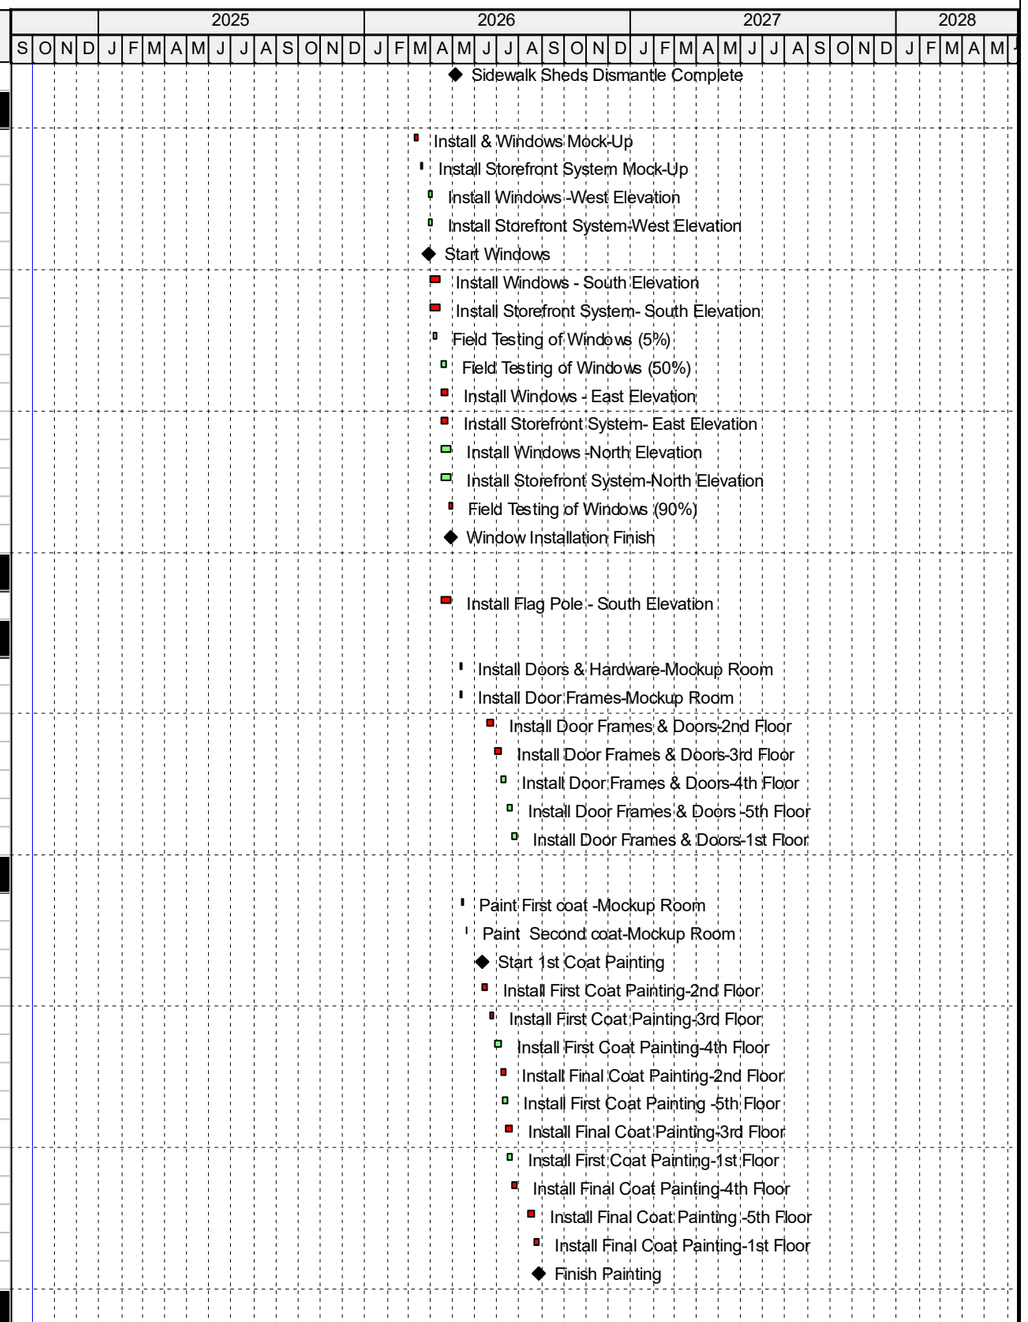

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

PROJECS
ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

Full Schedule Layout Grouped by Responsibility Code

Activity ID	Activity Name	Original Duration	Start	Finish
CON-4640	Flooring Finishes-Mockup Room	2	18-May-26	19-May-26
CON-5360	Install Flooring Tiles-2nd Floor	5	26-Jun-26	02-Jul-26
CON-5550	Install Flooring Tiles-3rd Floor	5	07-Jul-26	13-Jul-26
CON-5690	Install Flooring Tiles-4th Floor	5	14-Jul-26	20-Jul-26
CON-5760	Install Wood Floating Floor System -Gymnatorium	10	14-Jul-26	27-Jul-26
CON-5890	Install Flooring Tiles -5th Floor	5	23-Jul-26	29-Jul-26
CON-6080	Install Flooring Tiles-1st Floor	5	30-Jul-26	05-Aug-26
MFM Contracting		62	11-Jun-26	10-Sep-26
MIL-2992	Finish Fuel-Oil Storage & Fuel Oil Piping Systems Inspection	0		11-Jun-26
CON-4980	Install 4" & 6" & 10" & 12" DIP - Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
MIL-2562	Start Below Grade Plumbing and Other Utilities	0	16-Jul-26	
CON-9170	Install 8" Combined Water Service (2nd Street)- Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-9180	Install 6" Fire Water Service (54th Avenue Street)- Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-5190	Install Catch Basin - Drainage Work - Building Perimeter	2	21-Jul-26	22-Jul-26
CON-5290	Install Storm Inlet With Hood & Storm Hood - Drainage Work - Building Perimeter	2	23-Jul-26	24-Jul-26
CON-5400	Install Trench Drain - Drainage Work - Building Perimeter	1	27-Jul-26	27-Jul-26
MIL-1470	Finish Site Work	0		10-Sep-26
Nu-Tech Furnishing		28	06-Jul-26	12-Aug-26
CON-5570	Install Plumbing Fixtures -2nd Floor	7	06-Jul-26	14-Jul-26
CON-5730	Install Plumbing Fixtures -3rd Floor	7	15-Jul-26	23-Jul-26
CON-5930	Install Plumbing Fixtures -4th Floor	7	24-Jul-26	03-Aug-26
CON-6090	Install Plumbing Fixtures -5th Floor	7	04-Aug-26	12-Aug-26
CON-6180	Install Plumbing Fixtures-1st Floor	5	06-Aug-26	12-Aug-26
Elli		38	14-Jul-26	03-Sep-26
CON-5710	Install Furniture & Milling Work (Contractor Provided & Installed) -2nd Floor	5	14-Jul-26	20-Jul-26
CON-5910	Install Furniture & Milling Work (Contractor Provided & Installed) -3rd Floor	5	22-Jul-26	28-Jul-26
CON-6070	Install Furniture & Milling Work (Contractor Provided & Installed) -4th Floor	5	30-Jul-26	05-Aug-26
CON-6150	Install Furniture & Milling Work (Contractor Provided & Installed) -5th Floor	4	21-Aug-26	26-Aug-26
CON-6300	Install Furniture & Milling Work (Contractor Provided & Installed) -1st Floor	4	31-Aug-26	03-Sep-26
ACME		225	30-Sep-25	24-Aug-26
PRO-2030	Procure & Deliver Bleachers	130	30-Sep-25	06-Feb-26
CON-5970	Install Retractable Basketball Goal Assembly -Gymnatorium	3	03-Aug-26	05-Aug-26
CON-99217	Install Bleachers -Gymnatorium	3	12-Aug-26	14-Aug-26
CON-6230	Install Gym Equipment -Gymnatorium -Gymnatorium	6	17-Aug-26	24-Aug-26
City Gates		3	30-Jul-26	03-Aug-26
CON-99267	Install Rolling Doors-1st Floor	3	30-Jul-26	03-Aug-26
Eagle Fence		6	02-Sep-26	10-Sep-26
CON-6190	Install Wrought Iron Fence Double Gate - Playground Area - Building Perimeter	3	02-Sep-26	04-Sep-26
CON-6270	Install Chain Link Fence - Playground Area & Fences - Building Perimeter	3	08-Sep-26	10-Sep-26
Samtell		9	31-Aug-26	11-Sep-26
CON-6320	Install Cafeteria Equipment-1st Floor	4	31-Aug-26	03-Sep-26
CON-6380	Install Food Service Equipment-1st Floor	5	04-Sep-26	11-Sep-26

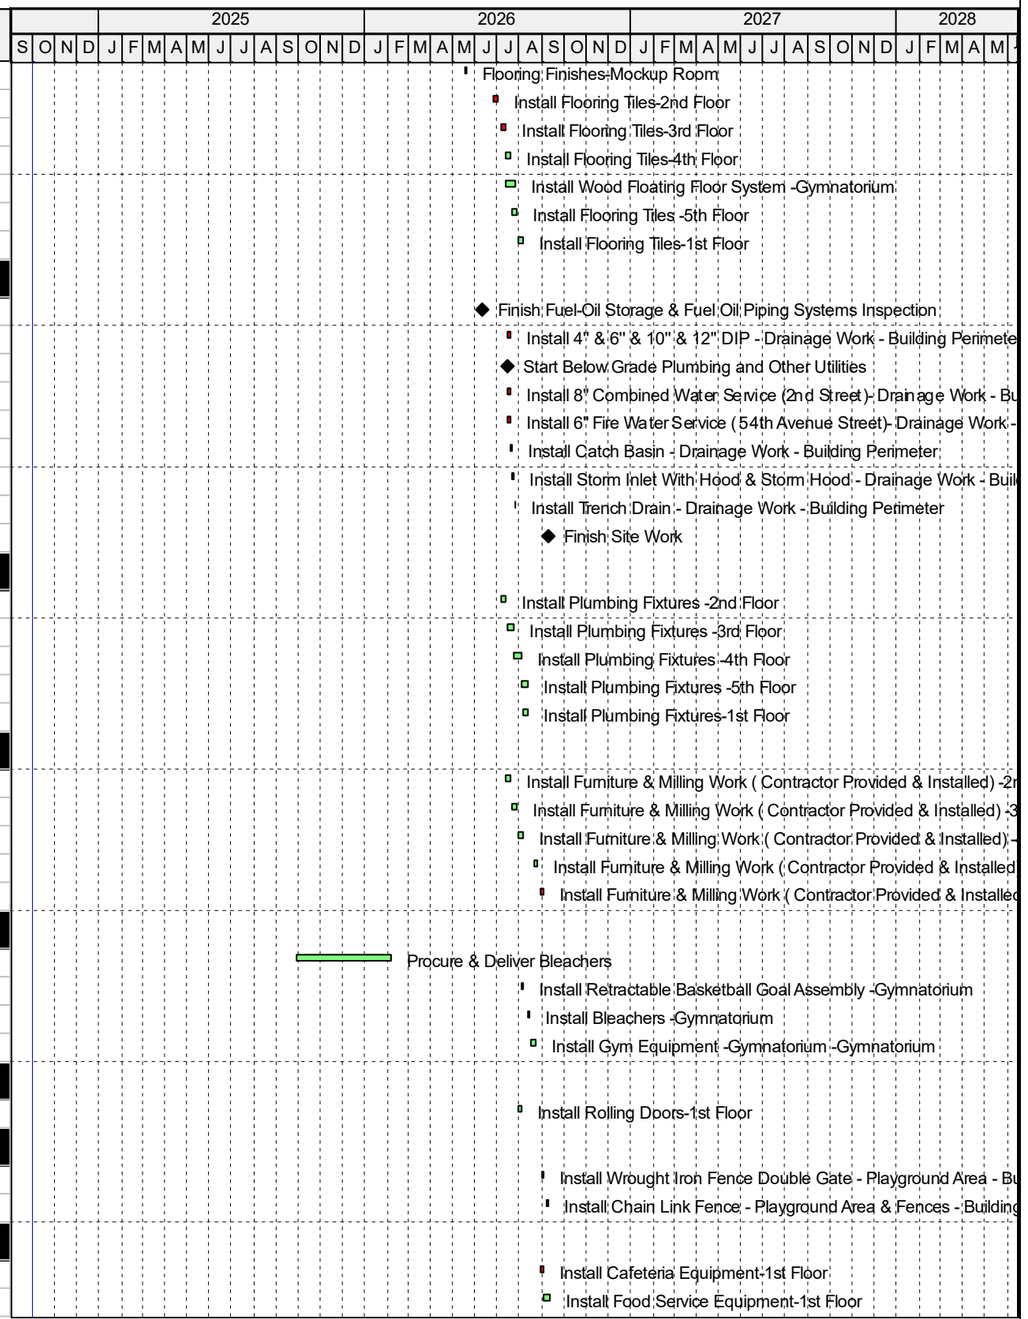

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By: M.K			
Date	Revision	Checked	Approved
21-Mar-25	00	AR	

APPENDIX 9
Longest Path Layout

Longest Path Layout

Activity ID	Activity Name	Original Duration	Start	Finish
New Building PS/IS 341Q - Baseline Schedule Rev 01		699	30-Sep-24	15-Aug-27
Pre-construction		699	30-Sep-24	15-Aug-27
Milestones		699	30-Sep-24	15-Aug-27
Major Milestones		699	30-Sep-24	15-Aug-27
MIL-1000	NTP	0	30-Sep-24	
MIL-1030	Project Duration(From NTP till TCO)	750	30-Sep-24	19-Oct-26
MIL-1040	Project Duration(From NTP till Substantial Completion)	930	30-Sep-24	17-Apr-27
MIL-1770	Project Duration(From NTP till Final Completion)	1050	30-Sep-24	15-Aug-27
MIL-2522	Site Access	365	30-Sep-24	29-Sep-25
MIL-1850	Construction Start	0	30-Sep-25	
MIL-1510	TCO	0		19-Oct-26*
MIL-1550	Substantial Completion	0		17-Apr-27*
MIL-1560	Final Completion	0		15-Aug-27
Contract Milestones		237	29-Sep-25	10-Sep-26
MIL-2532	Submit Complete Permit Application	0		29-Sep-25
MIL-2842	Issuance of Builders Pavement Permit	0		29-Sep-25
MIL-2852	Issuance of Permit to Enter (PTE)	0		29-Sep-25
MIL-2862	Issuance of NYPA Permit	0		29-Sep-25
MIL-2872	Issuance of Construction Fences Permit	0		29-Sep-25
MIL-2882	Issuance of Sidewalk Shed Permits	0		29-Sep-25
MIL-2892	Issuance of CCD1	0		29-Sep-25
MIL-2902	Issuance of DOB Permit & Insurance	0		29-Sep-25
MIL-1060	Mobilization Start	0	30-Sep-25	
MIL-1710	Complete Mobilization	0		03-Oct-25
MIL-2582	Start Concrete Placement	0	28-Oct-25	
MIL-2812	Start Foundation	0	28-Oct-25	
MIL-2912	Start Concrete Cast In Place Inspection	0	28-Oct-25	
MIL-1810	Crane Mobilization-Steel Installation start	0	05-Dec-25	
MIL-1120	Metal Decking Start	0	22-Dec-25	
MIL-1830	Crane Mobilization-Precast Sandwich Panels Installation Start	0	05-Mar-26	
MIL-2922	Start Pre -Cast Concrete Inspection	0	25-Mar-26	
MIL-1840	Crane Mobilization-Precast Sandwich Panels Installation Finish	0		06-Apr-26
MIL-1230	5th Floor Roofing Start	0	07-Apr-26	
MIL-1200	Main Roofing Start	0	09-Apr-26	
MIL-1340	BLDG Tight	0		06-May-26
MIL-1360	Start Mockup Room Work	0	07-May-26	
MIL-1430	Start Architecture Finishes	0	07-May-26	
MIL-1420	Finish Mockup Room	0		26-May-26
MIL-1440	Start Gypsum Board	0	27-May-26	
MIL-2702	Finish Concrete Work	0		10-Aug-26
MIL-2672	Finish Painting	0		28-Aug-26
MIL-1470	Finish Site Work	0		10-Sep-26
Permits		10	16-Sep-25	29-Sep-25
PRE-2630	Obtain Builders Pavement Permit	10	16-Sep-25	29-Sep-25

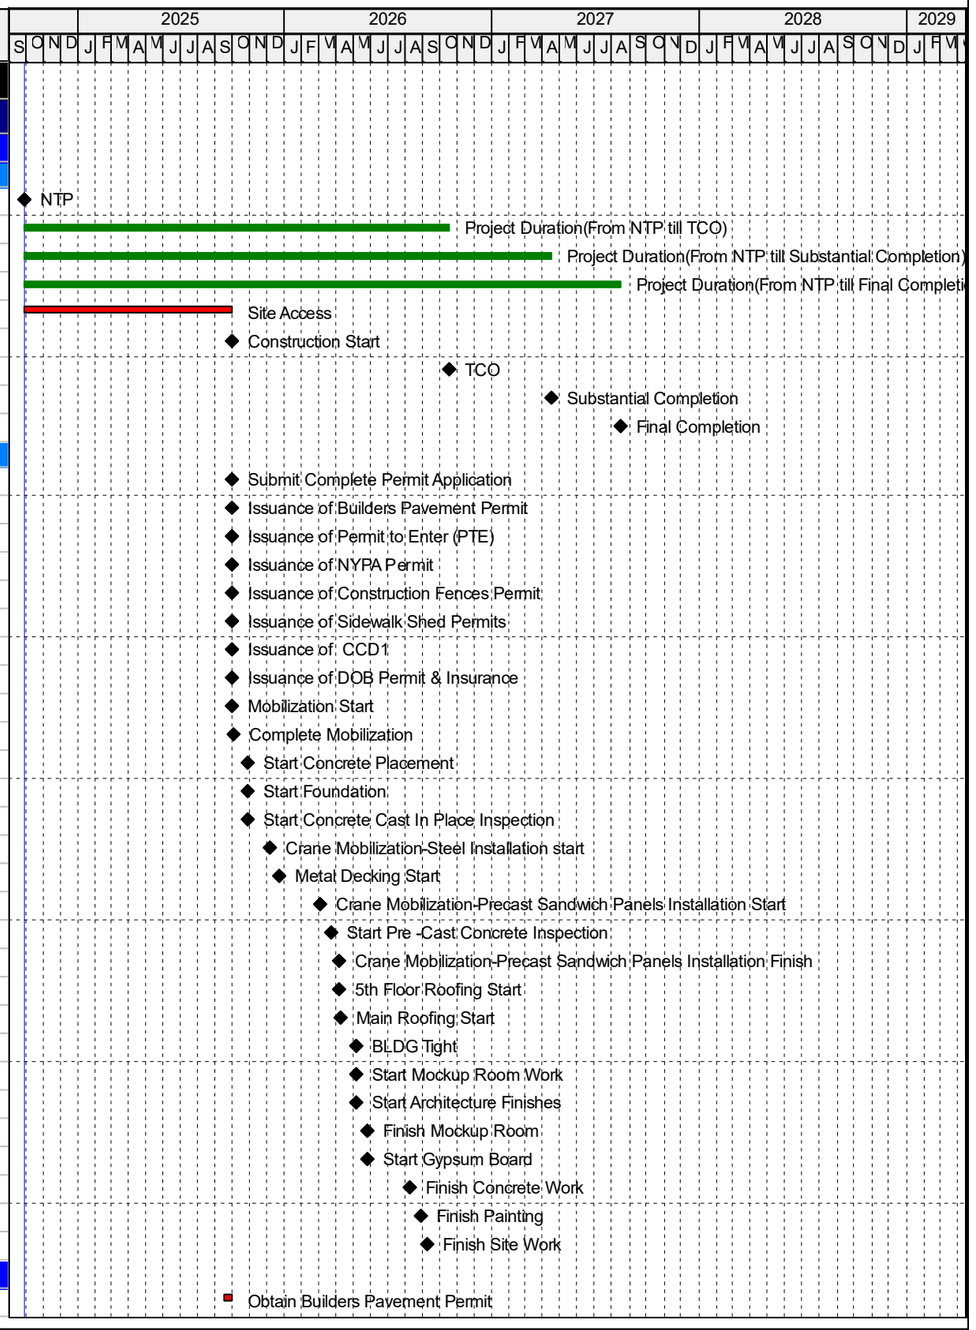

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

New Building PS/IS 341Q - Baseline Schedule Rev 01

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By : M.K

Date	**Revision**	**Checked**	**Approved**
21-Mar-25	00	A.A	

Longest Path Layout

Activity ID	Activity Name	Original Duration	Start	Finish
PRE-2640	Obtain Excavation & Shoring Permit	10	16-Sep-25	29-Sep-25
PRE-2650	Obtain Permit to Enter (PTE) Amtrak	10	16-Sep-25	29-Sep-25
PRE-2660	Obtain NYPA Permit	10	16-Sep-25	29-Sep-25
PRE-2540	SCA Work Notification	7	23-Sep-25	29-Sep-25
PRE-1660	DOB Permit & Insurance	3	25-Sep-25	29-Sep-25
PRE-1460	Obtain Construction Fences Permit	3	25-Sep-25	29-Sep-25
PRE-2550	Obtain CCD1	3	25-Sep-25	29-Sep-25
PRE-2570	Obtain Sidewalk Shed Permits	3	25-Sep-25	29-Sep-25
Mobilization		263	30-Sep-25	19-Oct-26
CON-1000	Mobilization	4	30-Sep-25	03-Oct-25
CON-7740	Protection Of All Overhead & Underground Utilities	263	30-Sep-25	19-Oct-26
CON-9000	Protection & Restoration the adjacent Properties to Original Condition	263	30-Sep-25	19-Oct-26
CON-9120	Soli Sampling	2	06-Oct-25	07-Oct-25
CON-9140	Excavation	5	08-Oct-25	15-Oct-25
Construction		226	16-Oct-25	10-Sep-26
First Floor		226	16-Oct-25	10-Sep-26
SSDS		8	16-Oct-25	27-Oct-25
CON-9898	Install Gas Permeable Aggregate -1st Floor	3	16-Oct-25	20-Oct-25
CON-98947	Install 4" slotted schedule 80 PVC Piping -1st Floor	3	16-Oct-25	20-Oct-25
CON-9888	Install Liquid Boot VI-20 Geomembrane -1st Floor	2	21-Oct-25	22-Oct-25
CON-1020	Install 60 Dry MILS Liquid Boot -1st Floor	3	23-Oct-25	27-Oct-25
CON-9777	Install Liquid Ultrashield G-1000 -1st Floor	2	24-Oct-25	27-Oct-25
Structure-1st Floor		37	28-Oct-25	19-Dec-25
CON-1040	F/R/P Concrete Walls & Beams -1st Floor	10	28-Oct-25	10-Nov-25
CON-1050	Install Underground Conduits & Wires -1st Floor	6	12-Nov-25	19-Nov-25
CON-1060	Backfilling & Compaction -1st Floor	6	12-Nov-25	19-Nov-25
CON-1070	F/R/P SOG -1st Floor	10	20-Nov-25	04-Dec-25
CON-98787	Install Steel Columns -1st Floor	7	05-Dec-25	15-Dec-25
CON-1100	Install Framing Beams -1st Floor	4	16-Dec-25	19-Dec-25
Architecture-1st Floor		14	21-Aug-26	10-Sep-26
Finishes-1st Floor		14	21-Aug-26	10-Sep-26
CON-6170	Install Final Coat Painting-1st Floor	6	21-Aug-26	28-Aug-26
CON-6300	Install Furniture & Milling Work (Contractor Provided & Installed) -1st Floor	4	31-Aug-26	03-Sep-26
CON-6320	Install Cafeteria Equipment-1st Floor	4	31-Aug-26	03-Sep-26
CON-6370	Install Signages-1st Floor	4	04-Sep-26	10-Sep-26
Second Floor		139	22-Dec-25	13-Jul-26
Structure-2nd Floor		12	22-Dec-25	08-Jan-26
CON-1110	Install Metal Deck Slab -2nd Floor	4	22-Dec-25	26-Dec-25
CON-1170	Install Steel Columns -2nd Floor	3	29-Dec-25	31-Dec-25
CON-1200	Install Framing Beams -2nd Floor	5	02-Jan-26	08-Jan-26
Architecture-2nd Floor		32	27-May-26	13-Jul-26
Interior Walls-2nd Floor		5	27-May-26	02-Jun-26
CON-4030	Install Gypsum Board Walls-2nd Floor	5	27-May-26	02-Jun-26
Ceiling-2nd Floor		6	03-Jun-26	10-Jun-26
CON-4370	Install Gypsum Board Ceiling -2nd Floor	6	03-Jun-26	10-Jun-26

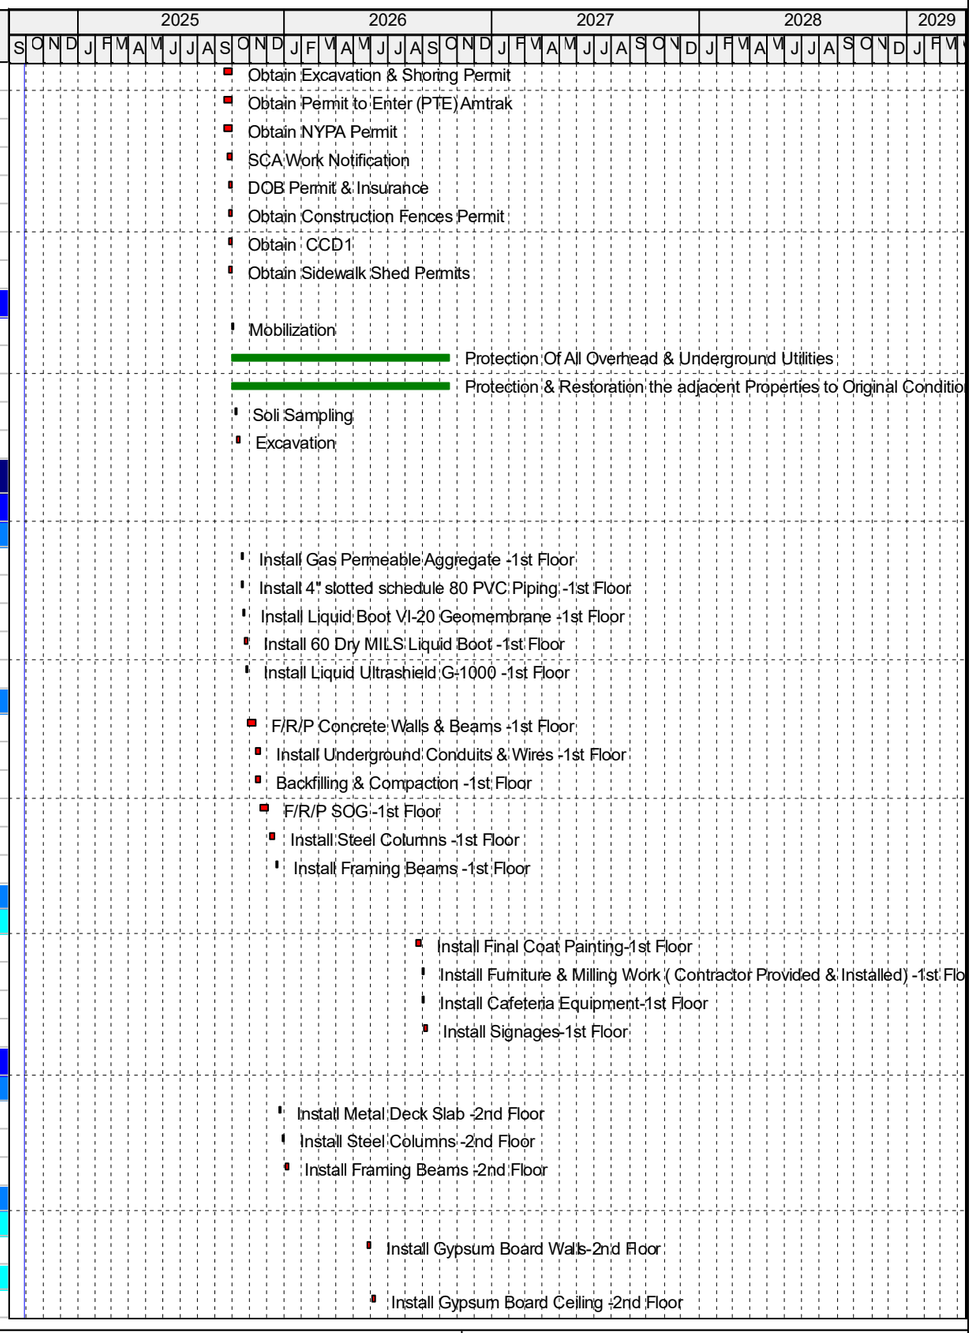

Longest Path Layout

Activity ID	Activity Name	Original Duration	Start	Finish
Finishes-2nd Floor		21	11-Jun-26	13-Jul-26
CON-4830	Install First Coat Painting-2nd Floor	5	11-Jun-26	17-Jun-26
CON-5120	Install Door Frames & Doors-2nd Floor	5	18-Jun-26	25-Jun-26
CON-5360	Install Flooring Tiles-2nd Floor	5	26-Jun-26	02-Jul-26
CON-5560	Install Final Coat Painting-2nd Floor	6	06-Jul-26	13-Jul-26
Third Floor		133	09-Jan-26	21-Jul-26
Structure -3rd Floor		13	09-Jan-26	28-Jan-26
CON-1210	Install Metal Deck Slab - 3rd Floor	4	09-Jan-26	14-Jan-26
CON-1240	Install Steel Columns - 3rd Floor	4	15-Jan-26	21-Jan-26
CON-1270	Install Framing Beams - 3rd Floor	5	22-Jan-26	28-Jan-26
Architecture -3rd Floor		27	11-Jun-26	21-Jul-26
Ceiling -3rd Floor		6	11-Jun-26	18-Jun-26
CON-4630	Install Gypsum Board Ceiling-3rd Floor	6	11-Jun-26	18-Jun-26
Finishes -3rd Floor		21	22-Jun-26	21-Jul-26
CON-5110	Install First Coat Painting-3rd Floor	5	22-Jun-26	26-Jun-26
CON-5350	Install Door Frames & Doors-3rd Floor	5	29-Jun-26	06-Jul-26
CON-5550	Install Flooring Tiles-3rd Floor	5	07-Jul-26	13-Jul-26
CON-5700	Install Final Coat Painting-3rd Floor	6	14-Jul-26	21-Jul-26
Fourth Floor		131	29-Jan-26	05-Aug-26
Structure -4th Floor		13	29-Jan-26	17-Feb-26
CON-1290	Install Metal Deck Slab - 4th Floor	4	29-Jan-26	03-Feb-26
CON-1330	Install Steel Columns - 4th Floor	4	04-Feb-26	09-Feb-26
CON-1370	Install Framing Beams - 4th Floor	5	10-Feb-26	17-Feb-26
Architecture-4th Floor		11	22-Jul-26	05-Aug-26
Ceiling-4th Floor		5	30-Jul-26	05-Aug-26
CON-5520	Install Acoustical Ceiling Tiles-4th Floor	5	30-Jul-26	05-Aug-26
Finishes-4th Floor		6	22-Jul-26	29-Jul-26
CON-5900	Install Final Coat Painting-4th Floor	6	22-Jul-26	29-Jul-26
Fifth Floor		129	18-Feb-26	20-Aug-26
Structure -5th Floor		9	18-Feb-26	02-Mar-26
CON-1380	Install Metal Deck Slab - 5th Floor	3	18-Feb-26	20-Feb-26
CON-1440	Install Steel Columns - 5th Floor	3	23-Feb-26	25-Feb-26
CON-1550	Install Framing Beams - 5th Floor	3	26-Feb-26	02-Mar-26
Architecture -5th Floor		11	06-Aug-26	20-Aug-26
Ceiling -5th Floor		5	06-Aug-26	12-Aug-26
CON-5670	Install Acoustical Ceiling Tiles-5th Floor	5	06-Aug-26	12-Aug-26
Finishes -5th Floor		6	13-Aug-26	20-Aug-26
CON-6060	Install Final Coat Painting -5th Floor	6	13-Aug-26	20-Aug-26
Roof		2	03-Mar-26	04-Mar-26
Structure -Roof Floor		2	03-Mar-26	04-Mar-26
CON-1720	Install Metal Deck Slab -Roof Floor	2	03-Mar-26	04-Mar-26
Elevations		44	05-Mar-26	05-May-26
West Elevation		17	05-Mar-26	27-Mar-26
CON-1830	Install Insulated Precast Concrete Sandwich Panel - Mock Up	2	05-Mar-26	06-Mar-26
CON-1990	Approve Insulated Precast Concrete Sandwich Panel - Mock Up	2	09-Mar-26	10-Mar-26
CON-2110	Install & Windows Mock-Up	3	11-Mar-26	13-Mar-26

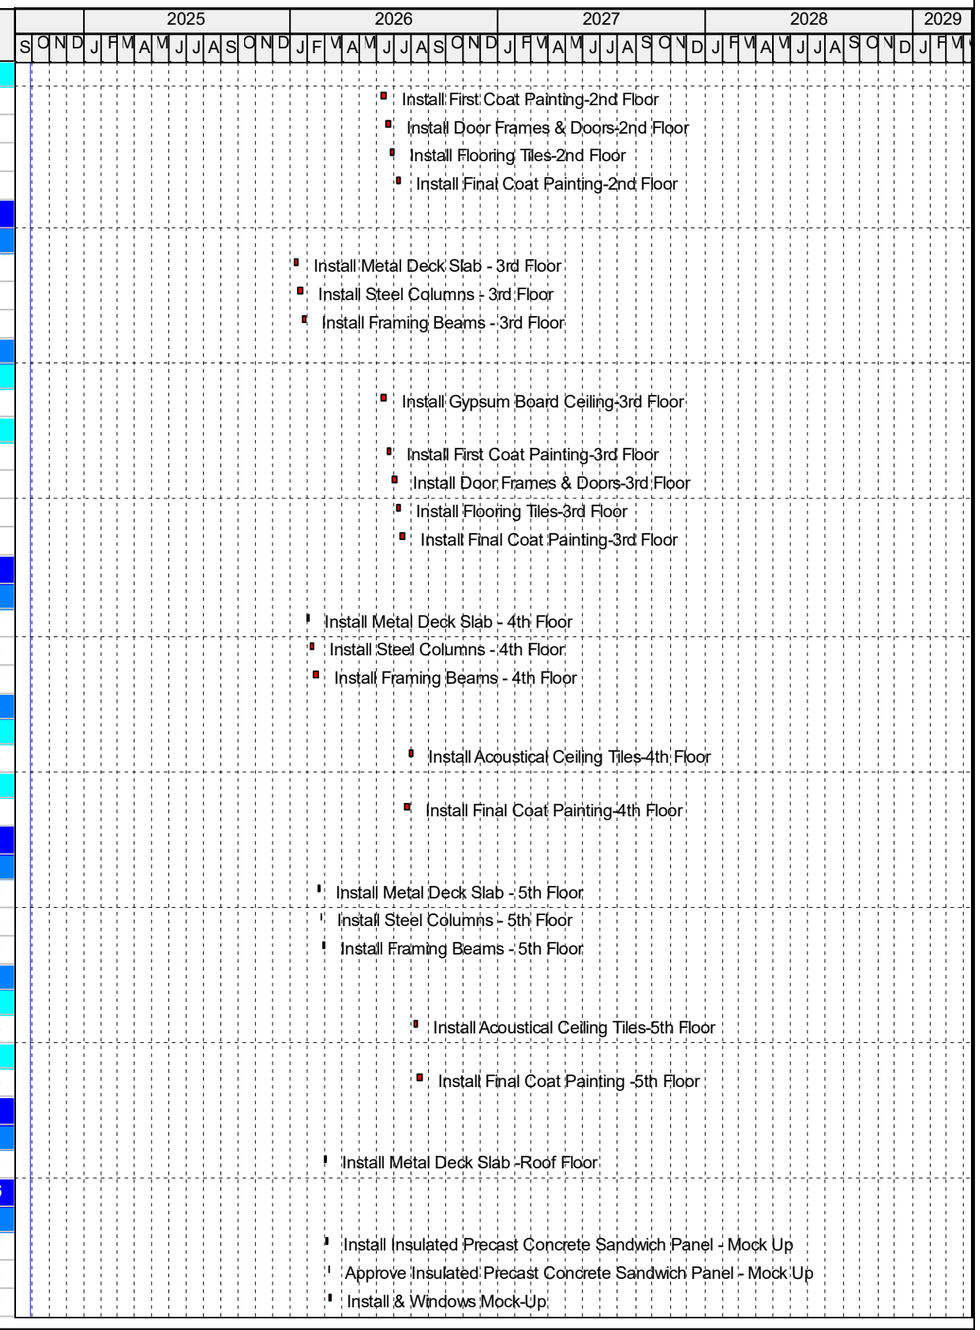

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By : M.K

Date	**Revision**	**Checked**	**Approved**
21-Mar-25	00	A.A	

Longest Path Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-2210	Approve Windows Mock-Up	2	16-Mar-26	17-Mar-26
CON-2220	Install Storefront System Mock-Up	3	18-Mar-26	20-Mar-26
CON-2240	Approve Storefront System Mock-Up	2	23-Mar-26	24-Mar-26
CON-2380	Install Insulated Precast Concrete Sandwich Panel - West Elevation	3	25-Mar-26	27-Mar-26
South Elevation		27	25-Mar-26	30-Apr-26
CON-2420	Install Insulated Precast Concrete Sandwich Panel - South Elevation	5	25-Mar-26	31-Mar-26
CON-2590	Install Windows - South Elevation	10	01-Apr-26	14-Apr-26
CON-2600	Install Storefront System- South Elevation	10	01-Apr-26	14-Apr-26
CON-99237	Install Flag Pole - South Elevation	10	15-Apr-26	28-Apr-26
CON-3220	Dismantle Sidewalk Sheds- South Elevation	2	29-Apr-26	30-Apr-26
East Elevation		25	01-Apr-26	05-May-26
CON-2610	Install Insulated Precast Concrete Sandwich Panel - East Elevation	4	01-Apr-26	06-Apr-26
CON-2980	Install Windows - East Elevation	8	15-Apr-26	24-Apr-26
CON-2990	Install Storefront System- East Elevation	8	15-Apr-26	24-Apr-26
CON-3370	Field Testing of Windows (90%)	5	27-Apr-26	01-May-26
CON-3630	Dismantle Sidewalk Sheds- East Elevation	2	04-May-26	05-May-26
North Elevation		25	01-Apr-26	05-May-26
CON-2730	Install Insulated Precast Concrete Sandwich Panel - North Elevation	4	01-Apr-26	06-Apr-26
MIL-1730	Sidewalk Sheds Dismantle Complete	0		05-May-26
Roofing		22	07-Apr-26	06-May-26
5th Floor		21	07-Apr-26	05-May-26
CON-2920	Pour Sloped Concrete Fill -5th Floor Roof	2	07-Apr-26	08-Apr-26
CON-3210	Install Fluid-Applied Protected Membrane Mock-Up	2	13-Apr-26	14-Apr-26
CON-3300	Approve Fluid-Applied Protected Membrane Mock-Up	4	15-Apr-26	20-Apr-26
CON-3440	Install Hot Fluid Applied Membrane -5th Floor Roof	4	21-Apr-26	24-Apr-26
CON-3580	Install 6" Thick Rigid Insulation -5th Floor Roof	3	27-Apr-26	29-Apr-26
CON-3710	Roof Flood Test -5th Floor Roof	4	30-Apr-26	05-May-26
Main Roof		20	09-Apr-26	06-May-26
CON-3010	Pour Sloped Concrete Fill -Roof Floor	2	09-Apr-26	10-Apr-26
CON-3430	Install Hot Fluid Applied Membrane -Roof Floor	3	21-Apr-26	23-Apr-26
CON-3600	Install Drainage Panels- Roof Floor	3	24-Apr-26	28-Apr-26
CON-3730	Install 6" Thick Rigid Insulation -Roof Floor	3	29-Apr-26	01-May-26
CON-3840	Roof Flood Test -Roof Floor	3	04-May-26	06-May-26
Mockup Room		13	07-May-26	26-May-26
CON-4040	Install Walls GWB-Mockup Room	3	07-May-26	11-May-26
CON-4380	Install Doors & Hardware-Mockup Room	3	11-May-26	13-May-26
CON-4260	Install Door Frames-Mockup Room	2	12-May-26	13-May-26
CON-4480	Paint First coat -Mockup Room	2	14-May-26	15-May-26
CON-4640	Flooring Finishes-Mockup Room	2	18-May-26	19-May-26
CON-4750	Paint Second coat-Mockup Room	2	20-May-26	21-May-26
CON-4930	Install Furniture & Signs -Mockup Room	2	22-May-26	26-May-26
Site Work		91	01-May-26	10-Sep-26
54th Avenue Street		3	01-May-26	05-May-26
CON-3780	Install Traffic Control Devices - 54th Avenue Street	3	01-May-26	05-May-26
2ND Street		39	06-May-26	01-Jul-26

Longest Path Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-3870	Install Traffic Control Devices - 2nd Street	5	06-May-26	12-May-26
CON-3900	Remove Existing Sidewalk - 2nd Street	5	13-May-26	19-May-26
CON-3950	Install Pedestrian Ramps With Truncated Domes - 2nd Street	6	20-May-26	28-May-26
CON-4090	Remove Existing Steel Faced Curb - 2nd Street	6	29-May-26	05-Jun-26
CON-4160	Install New Steel Faced Curb - 2nd Street	6	08-Jun-26	15-Jun-26
CON-4310	Install 7" Concrete Sidewalk - 2nd Street	6	16-Jun-26	24-Jun-26
CON-4420	Remove Traffic Control Devices - 2nd Street	5	25-Jun-26	01-Jul-26
Building Perimeter		49	02-Jul-26	10-Sep-26
Drainage Work		17	02-Jul-26	27-Jul-26
CON-4660	Excavation - Drainage Work - Building Perimeter	3	02-Jul-26	07-Jul-26
CON-4740	Install Flood Barrier Wall - Drainage Work - Building Perimeter	3	08-Jul-26	10-Jul-26
CON-4860	Install Drilled Caisson Supported Ventilation Structure - Drainage Work - Building Perimeter	3	13-Jul-26	15-Jul-26
CON-4980	Install 4" & 6" & 10" & 12" DIP - Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-9170	Install 8" Combined Water Service (2nd Street)- Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-9180	Install 6" Fire Water Service (54th Avenue Street)- Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26
CON-5190	Install Catch Basin - Drainage Work - Building Perimeter	2	21-Jul-26	22-Jul-26
CON-5290	Install Storm Inlet With Hood & Storm Hood - Drainage Work - Building Perimeter	2	23-Jul-26	24-Jul-26
CON-5400	Install Trench Drain - Drainage Work - Building Perimeter	1	27-Jul-26	27-Jul-26
Playground Area & Fences		32	28-Jul-26	10-Sep-26
CON-9160	Excavate for Footings - Playground Area & Fences - Building Perimeter	2	28-Jul-26	29-Jul-26
CON-9190	F/R/P Playground Equipment Footings - Playground Area & Fences - Building Perimeter	2	30-Jul-26	31-Jul-26
CON-5470	Install Flush Concrete Curb - Playground Area & Fences - Building Perimeter	3	03-Aug-26	05-Aug-26
CON-5600	Install Concrete Pavement Pedestrian Ramp With Painted Black Handrails - Playground Area & Fences - Building Perimeter	3	06-Aug-26	10-Aug-26
CON-5650	Install Playground Rubber Tile Safety Surface - Playground Area & Fences - Building Perimeter	3	11-Aug-26	13-Aug-26
CON-5800	Install Painted Asphalt Pavement & Painted Games On Asphalt Surface - Playground Area & Fences - Building Perimeter	3	14-Aug-26	18-Aug-26
CON-5850	Install Colored Athletic Wearing Surface Color - Playground Area & Fences - Building Perimeter	2	19-Aug-26	20-Aug-26
CON-5990	Install Playground Equipment - Playground Area & Fences - Building Perimeter	7	21-Aug-26	31-Aug-26
CON-6140	Install Basketball Hoop - Playground Area & Fences - Building Perimeter	1	01-Sep-26	01-Sep-26
CON-6190	Install Wrought Iron Fence Double Gate - Playground Area - Building Perimeter	3	02-Sep-26	04-Sep-26
CON-6270	Install Chain Link Fence - Playground Area & Fences - Building Perimeter	3	08-Sep-26	10-Sep-26
Close-out		430	28-Oct-25	15-Aug-27
Special Inspection		131	28-Oct-25	06-May-26
I-1010	Concrete Cast-IN-Place Inspection	86	28-Oct-25	04-Mar-26
I-1140	Structural Steel Inspection	58	05-Dec-25	02-Mar-26
I-1150	Concrete Precast Inspection	9	25-Mar-26	06-Apr-26
I-1040	Roofing Flood Testing Inspection	5	30-Apr-26	06-May-26
Demobilization		212	11-Sep-26	15-Aug-27
CLO-1030	Pre-Final Clean-Out	5	11-Sep-26	17-Sep-26
CLO-1040	Pre-TCO Inspection	11	18-Sep-26	02-Oct-26
CLO-1110	Pre-TCO Punchlist	10	05-Oct-26	19-Oct-26
CLO-1050	Pre-Substantial Punchlist	105	20-Oct-26	17-Apr-27
CLO-1060	Prepare & Submit O&M Manuals	30	19-Apr-27	01-Jun-27
CLO-1070	Prepare & Submit As-Built Drawings	30	02-Jun-27	15-Jul-27
CLO-1080	Final Inspection	5	16-Jul-27	22-Jul-27

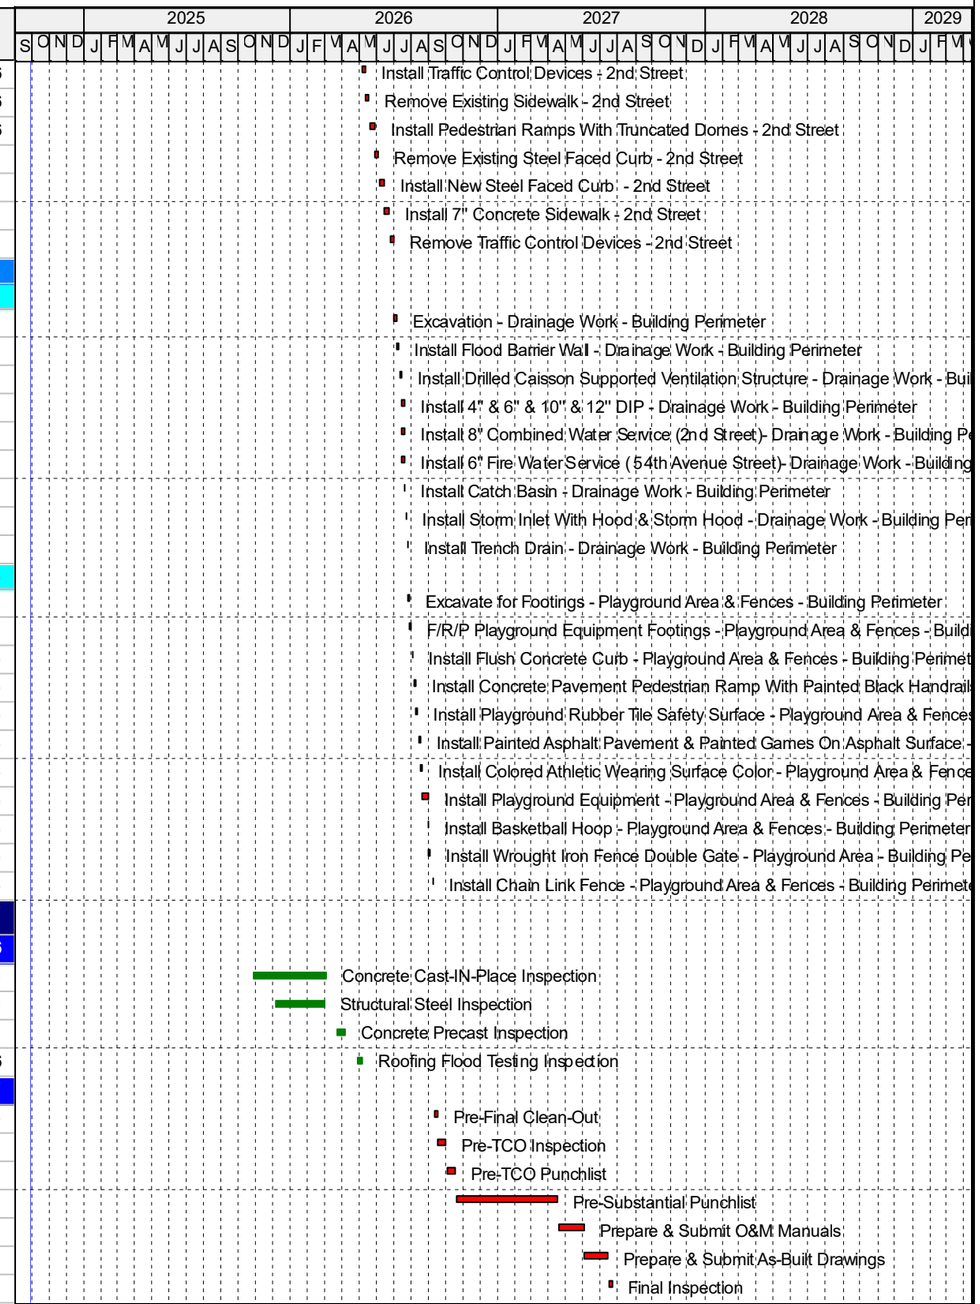

Longest Path Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CLO-1090	Final Clean Out	10	23-Jul-27	05-Aug-27
CLO-1100	Demobilization	10	06-Aug-27	15-Aug-27



APPENDIX 10
One Month Lookahead

One Month Lookahead

Activity ID	Activity Name	Original Duration	Start	Finish
New Building PS/IS 341Q - Baseline Schedule Rev 01		250	30-Sep-24	29-Sep-25
Pre-construction		250	30-Sep-24	29-Sep-25
Milestones		250	30-Sep-24	29-Sep-25
Major Milestones		250	30-Sep-24	29-Sep-25
MIL-1000	NTP	0	30-Sep-24	
MIL-2522	Site Access	365	30-Sep-24	29-Sep-25
Contract Milestones		0	11-Oct-24	11-Oct-24
MIL-2542	Complete Subcontractor 'Buyout'	0		11-Oct-24
Permits		14	30-Sep-24	18-Oct-24
PRE-2590	Meeting With SCA to Review The Permit Requirements	14	30-Sep-24	18-Oct-24
PRE-2600	Prepare & Submit Permit Waiver Requests to SCA Chief Project Officer	5	30-Sep-24	04-Oct-24
Mobilization		10	30-Sep-24	11-Oct-24
CON-99257	Subcontractor Buyout	10	30-Sep-24	11-Oct-24
Utilities Coordination		5	07-Oct-24	11-Oct-24
Gas Coordination		5	07-Oct-24	11-Oct-24
CON-7960	Obtain Gas Meter Layout From CON-ED	5	07-Oct-24	11-Oct-24
Procurement		82	15-Oct-24	12-Feb-25
Submittals & Approvals		82	15-Oct-24	12-Feb-25
Division 01 - General Requirements		82	15-Oct-24	12-Feb-25
Spec Section S01300 - Submittals		75	15-Oct-24	03-Feb-25
SUB-1410	Prepare & Submit Submittal Schedule	60	15-Oct-24	10-Jan-25
SUB-1780	Prepare & Submit Initial Underground Coordination Drawings	50	15-Oct-24	26-Dec-24
SUB-1790	Prepare & Submit Initial 1st Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1800	Prepare & Submit Initial 2nd Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1810	Prepare & Submit Initial 3rd Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1820	Prepare & Submit Initial 4th Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
SUB-1830	Prepare & Submit Initial 5th Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25
Spec Section S01311 - Progress Schedule		52	15-Oct-24	30-Dec-24
SUB-1610	Prepare & Submit Baseline Schedule	52	15-Oct-24	30-Dec-24
Spec Section S01352 - Sustainability Requirements		24	15-Oct-24	18-Nov-24
SUB-1400	Prepare & Submit Sustainable Materials	10	15-Oct-24	28-Oct-24
APP-1040	Review & Approve Sustainable Materials	21	29-Oct-24	18-Nov-24
Spec Section S01400 - Quality Control		30	15-Oct-24	26-Nov-24
SUB-1570	Prepare & Submit QCP	30	15-Oct-24	26-Nov-24
Spec Section S01426 - Sample Classroom		81	15-Oct-24	11-Feb-25
SUB-1390	Prepare & Submit Sample Classroom Materials	81	15-Oct-24	11-Feb-25
Spec Section S01500 - Temporary Facilities and Controls		81	15-Oct-24	11-Feb-25
SUB-1370	Prepare & Submit Photo Submission - Temporary Fence	15	15-Oct-24	04-Nov-24
SUB-1380	Prepare & Submit Heating Plan	81	15-Oct-24	11-Feb-25
SUB-2340	Prepare & Submit Tree Protection Plan	71	15-Oct-24	28-Jan-25
Spec Section S01524 - Construction Waste Management		81	15-Oct-24	11-Feb-25
SUB-1360	Prepare & Submit CWM Plan	81	15-Oct-24	11-Feb-25
Spec Section S01535 - Safety Program		17	15-Oct-24	06-Nov-24
SUB-1350	Prepare & Submit Site Safety Plan	2	15-Oct-24	16-Oct-24
APP-1000	Review & Approve Site Safety Plan	21	17-Oct-24	06-Nov-24
Spec Section S01550 - Indoor Air Quality (IAQ) Requirements		81	15-Oct-24	11-Feb-25
SUB-1340	Prepare & Submit Construction Indoor Air Quality Management Plan	81	15-Oct-24	11-Feb-25
Spec Section S01560 - Installation Sequence of Finish Materials		81	15-Oct-24	11-Feb-25

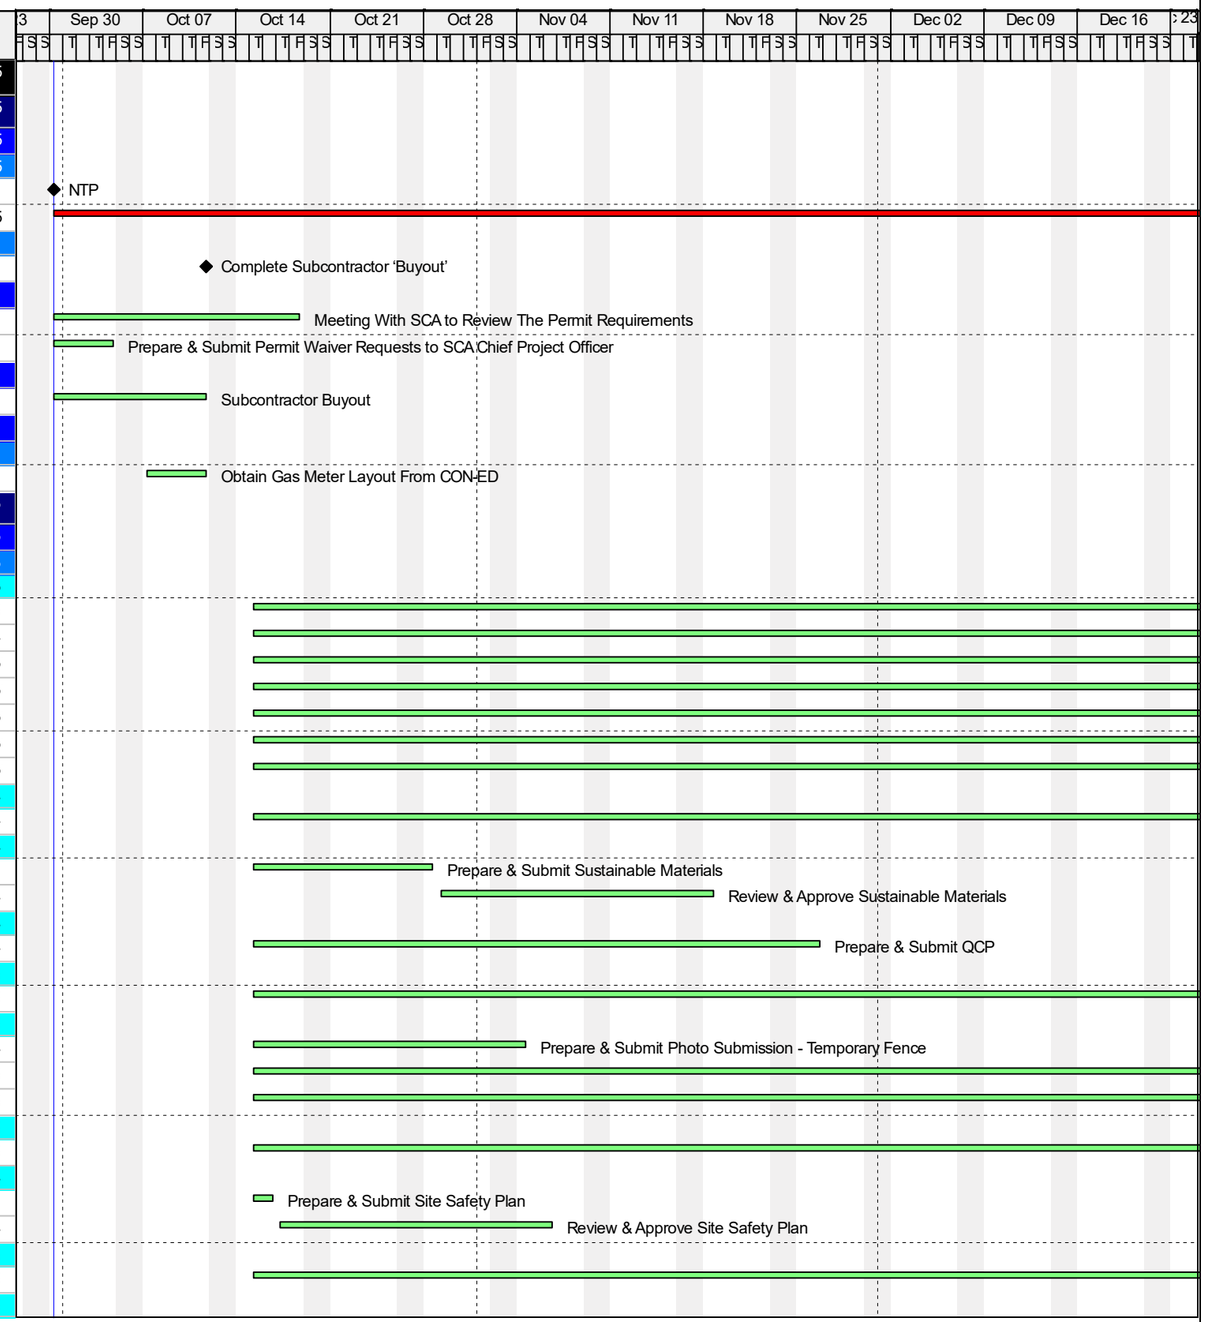

One Month Lookahead

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1330	Prepare & Submit Temporary Ventilation Plan	81	15-Oct-24	11-Feb-25
Spec Section S01630 - Product Substitutions		82	15-Oct-24	12-Feb-25
SUB-1320	Prepare & Submit Product Substitutions	82	15-Oct-24	12-Feb-25
Spec Section S01650 - Facility Start-Up, Demonstration, and Training		81	15-Oct-24	11-Feb-25
SUB-1310	Prepare & Submit Training Outline & Schedule	81	15-Oct-24	11-Feb-25
Spec Section S01660 - Supplemental Commissioning Requirements		81	15-Oct-24	11-Feb-25
SUB-1840	Prepare & Submit Supplemental Comissioning Requirements	81	15-Oct-24	11-Feb-25
Spec Section S01720 - Record Documents		81	15-Oct-24	11-Feb-25
SUB-1850	Prepare & Submit Record Documents	81	15-Oct-24	11-Feb-25
Division 02 - Site Work		81	15-Oct-24	11-Feb-25
Spec Section 02010 - Environmental Site Assessment Reports		81	15-Oct-24	11-Feb-25
SUB-1860	Prepare & Submit Environmental Site Assessment Reports	81	15-Oct-24	11-Feb-25
Spec Section 02070 - Selective Removals & Demoloition		81	15-Oct-24	11-Feb-25
SUB-1870	Prepare & Submit Selective Removals & Demoloition	81	15-Oct-24	11-Feb-25
Spec Section 02090 - Environmental Management Of Excavated Material And Fill/Backfill		81	15-Oct-24	11-Feb-25
SUB-2920	Prepare & Submit Documentation of Proper Disposal	81	15-Oct-24	11-Feb-25
Spec Section 02200 - Earthwork		21	15-Oct-24	13-Nov-24
SUB-1560	Prepare & Submit Erosion Control and Sedimentation Plan	7	15-Oct-24	23-Oct-24
APP-1020	Review & Approve Erosion Control and Sedimentation Plan	21	24-Oct-24	13-Nov-24
Spec Section 02100 - Site Preparation		24	15-Oct-24	18-Nov-24
SUB-1300	Prepare & Submit Existing Conditions Survey	10	15-Oct-24	28-Oct-24
APP-1030	Review & Approve Existing Conditions Survey	21	29-Oct-24	18-Nov-24
Spec Section 02220 - Gas Vapor Barrier (Fluid Applied)		81	15-Oct-24	11-Feb-25
SUB-1290	Prepare & Submit Gas Vapor Barrier Submittal & Inspection Schedule	81	15-Oct-24	11-Feb-25
Spec Section 02221 - Sub-Slab Depressurization System		40	15-Oct-24	11-Dec-24
SUB-1280	Prepare & Submit SSDS Geotextile	40	15-Oct-24	11-Dec-24
Spec Section 02250 - Foundation & Other Change Adjustements		19	15-Oct-24	11-Nov-24
SUB-1880	Prepare & Submit Foundation Product Data	5	15-Oct-24	21-Oct-24
APP-1010	Review & Approve Foundation Product Data	21	22-Oct-24	11-Nov-24
Spec Section 02260 - Excavation Support And Monitoring		81	15-Oct-24	11-Feb-25
SUB-2360	Prepare & Submit Adjacent Property and Structures Protection & Monitoring Plan	81	15-Oct-24	11-Feb-25
Spec Section 02511 - Asphaltic Concrete Paving		81	15-Oct-24	11-Feb-25
SUB-1270	Prepare & Submit Asphaltic Concrete Paving	81	15-Oct-24	11-Feb-25
Spec Section 02513 - Sidewalk and Street Paving		81	15-Oct-24	11-Feb-25
SUB-1260	Prepare & Submit Steel Curb Facing Shop Drawing	81	15-Oct-24	11-Feb-25
Spec Section 02521 - Concrete Curbs and Pavements		81	15-Oct-24	11-Feb-25
SUB-1250	Prepare & Submit Concrete Curbs & Pavements Shop Drawing	81	15-Oct-24	11-Feb-25
Spec Section 02721 - Trench Drains		81	15-Oct-24	11-Feb-25
SUB-1890	Prepare & Submit Trench Drains Product Data	81	15-Oct-24	11-Feb-25
Spec Section 02722 - PC Basins, Detention Basins, and Manholes		81	15-Oct-24	11-Feb-25
SUB-1240	Prepare & Submit Catch Basin Shop Drawings	81	15-Oct-24	11-Feb-25
Spec Section 02723 - Storm Drainage Systems		37	15-Oct-24	06-Dec-24
SUB-1230	Prepare & Submit Ductile Iron Pipes	37	15-Oct-24	06-Dec-24
Spec Section 02831 - Chain Link Fences & Gates		81	15-Oct-24	11-Feb-25
SUB-1900	Prepare & Submit Chain Link Fences & Gates Drawings	81	15-Oct-24	11-Feb-25
Spec Section 02860 - Early Childhood Playground Equipment		81	15-Oct-24	11-Feb-25
SUB-1220	Prepare & Submit Playgroung Equipment Shop Drawings	81	15-Oct-24	11-Feb-25
Spec Section 02862 - Outdoor Game Equipment		81	15-Oct-24	11-Feb-25
SUB-1910	Prepare & Submit Outdoor Game Equipment	81	15-Oct-24	11-Feb-25
Spec Section 02870 - Site & Street Furnishings		15	15-Oct-24	04-Nov-24

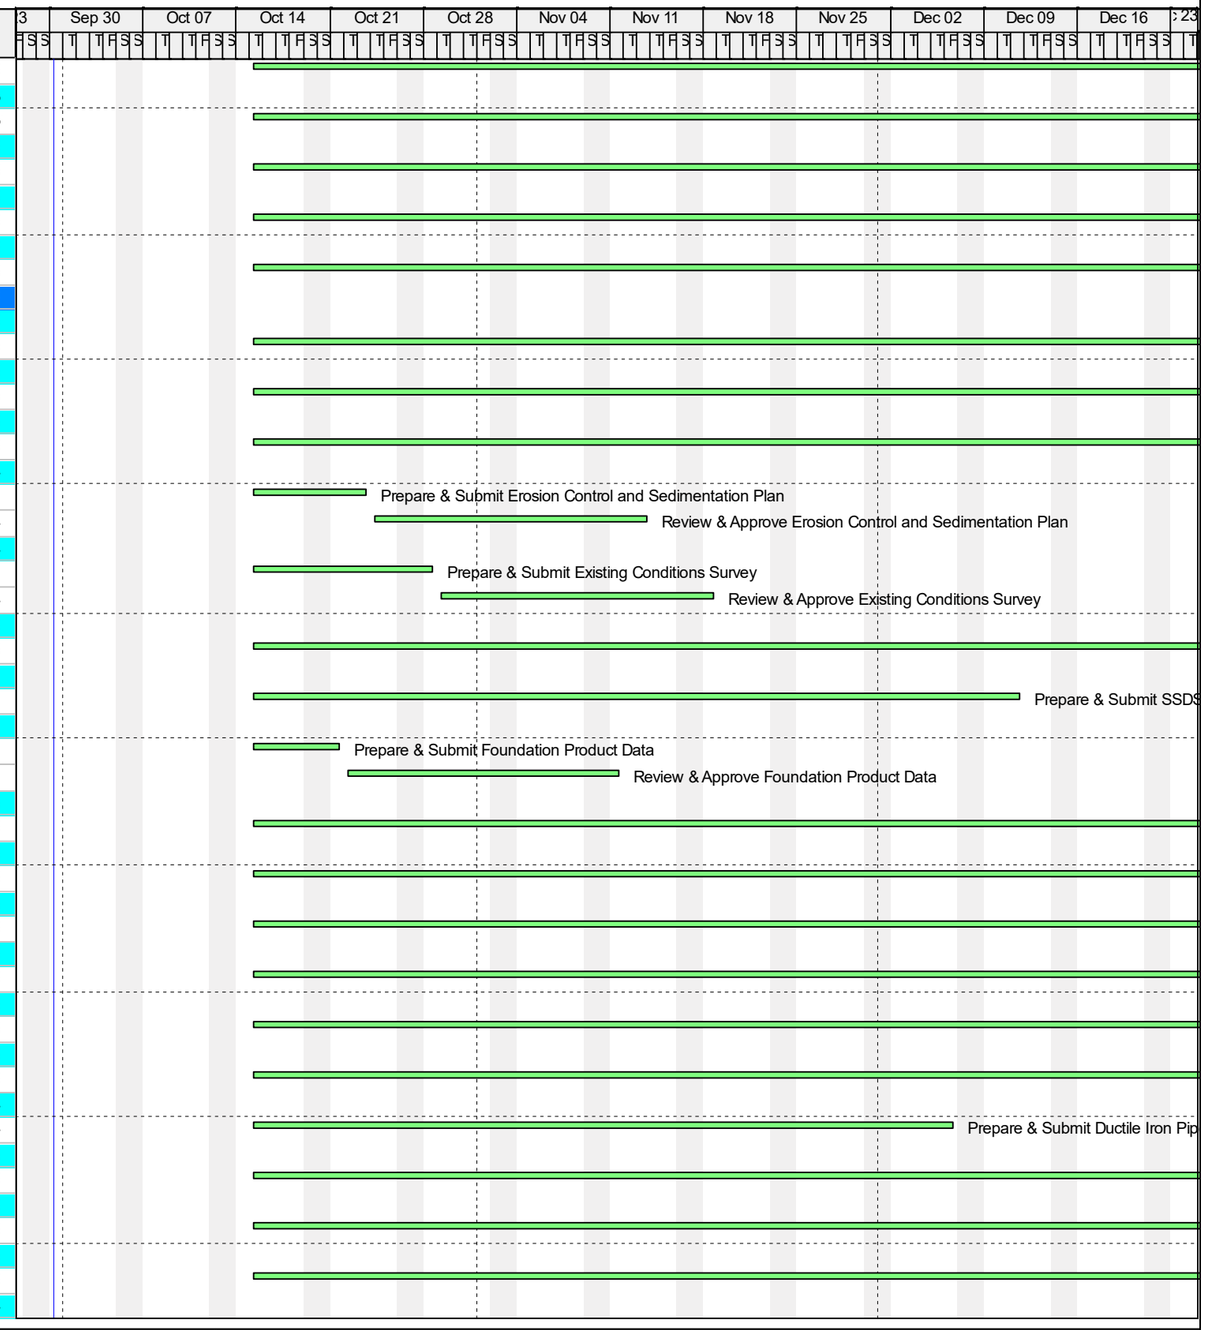

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By : M.K

Date	Revision	Checked	Approved
21-Mar-25	00	A.A	

One Month Lookahead

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-1210	Prepare & Submit Site Furnishings Shop Drawings	15	15-Oct-24	04-Nov-24
Spec Section 02900 - Landscaping		81	15-Oct-24	11-Feb-25
SUB-1200	Prepare & Submit Planting Schedule	81	15-Oct-24	11-Feb-25
Division 03 - Concrete		81	15-Oct-24	11-Feb-25
Spec Section 03100 - Concrete Formwork		81	15-Oct-24	11-Feb-25
SUB-1190	Prepare & Submit Formwork Shop Drawings	81	15-Oct-24	11-Feb-25
Spec Section 03200 - Concrete Reinforcement		30	15-Oct-24	26-Nov-24
SUB-1180	Prepare & Submit Concrete Reinforcement	30	15-Oct-24	26-Nov-24
Spec Section 03300 - Cast in Place Concrete		30	15-Oct-24	26-Nov-24
SUB-1450	Prepare & Submit Concrete Shop Drawings	30	15-Oct-24	26-Nov-24
SUB-1580	Prepare & Submit Concrete Mix Design	30	15-Oct-24	26-Nov-24
Spec Section 03450 - Precast Architectural Concrete		71	15-Oct-24	28-Jan-25
SUB-1920	Prepare & Submit Precast Architectural Concrete	71	15-Oct-24	28-Jan-25
Spec Section 03542 - Cement Based Self Leveling Underlayment		81	15-Oct-24	11-Feb-25
SUB-1170	Prepare & Submit Certification of Material	81	15-Oct-24	11-Feb-25
Division 04 - Masonry		81	15-Oct-24	11-Feb-25
Spec Section 04200 - Unit Masonry		71	15-Oct-24	28-Jan-25
SUB-1930	Prepare & Submit Unit Masonry Product Data	71	15-Oct-24	28-Jan-25
Spec Section 04435 - Cast Stone		81	15-Oct-24	11-Feb-25
SUB-1940	Prepare & Submit Cast Stone Product Data	81	15-Oct-24	11-Feb-25
Division 05 - Metals		81	15-Oct-24	11-Feb-25
Spec Section 05120 - Structural Steel		71	15-Oct-24	28-Jan-25
SUB-1950	Prepare & Submit Structure Steel Drawings	71	15-Oct-24	28-Jan-25
Spec Section 05170 - Support System for Suspended Ceilings		81	15-Oct-24	11-Feb-25
SUB-1160	Prepare & Submit Suspension Assembly Shop Drawings	81	15-Oct-24	11-Feb-25
Spec Section 05300 - Metal Deck		81	15-Oct-24	11-Feb-25
SUB-1960	Prepare & Submit Metal Deck Product Data	81	15-Oct-24	11-Feb-25
Spec Section 05710 - Steel Stairs		81	15-Oct-24	11-Feb-25
SUB-4060	Prepare & Submit Steel Stairs Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-4070	Prepare & Submit Steel Stairs Product Data	81	15-Oct-24	11-Feb-25
Spec Section 05700 - Ornamental Metal		81	15-Oct-24	11-Feb-25
SUB-2370	Prepare & Submit Ornamenta Metal Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2930	Prepare & Submit Ornamenta Metal Product Data	81	15-Oct-24	11-Feb-25
Spec Section 05810 - Prefabricated Expansion Joint Covers		81	15-Oct-24	11-Feb-25
SUB-1970	Prepare & Submit Prefabricated Expansion Joint Covers	81	15-Oct-24	11-Feb-25
Division 06 - Wood & Plastics		81	15-Oct-24	11-Feb-25
Spec Section 06200 - Finish Carpentry		81	15-Oct-24	11-Feb-25
SUB-1530	Prepare & Submit Furniture	81	15-Oct-24	11-Feb-25
Spec Section 06410 - Custom Casework		81	15-Oct-24	11-Feb-25
SUB-1510	Prepare & Submit Millwork	81	15-Oct-24	11-Feb-25
Division 07 - Thermal & Moisture Protection		81	15-Oct-24	11-Feb-25
Spec Section 07147 - Crystalline Waterproofing		81	15-Oct-24	11-Feb-25
SUB-1150	Prepare & Submit Crystalline Waterproofing Product Data	81	15-Oct-24	11-Feb-25
Spec Section 07211 - Perimeter Foundation Insulation		81	15-Oct-24	11-Feb-25
SUB-1140	Prepare & Submit Perimeter Foundation Insulation Product Data	81	15-Oct-24	11-Feb-25
Spec Section 07271 - Self Adhering Sheet Air Barriers		81	15-Oct-24	11-Feb-25
SUB-1980	Prepare & Submit Self Adhering Sheet Air Barriers	81	15-Oct-24	11-Feb-25
Spec Section 07414 - Metal Plate Wall Panels		81	15-Oct-24	11-Feb-25
SUB-1990	Prepare & Submit Metal Plate Wall Panels	81	15-Oct-24	11-Feb-25
SUB-4080	Prepare & Submit Green School Submittal	81	15-Oct-24	11-Feb-25

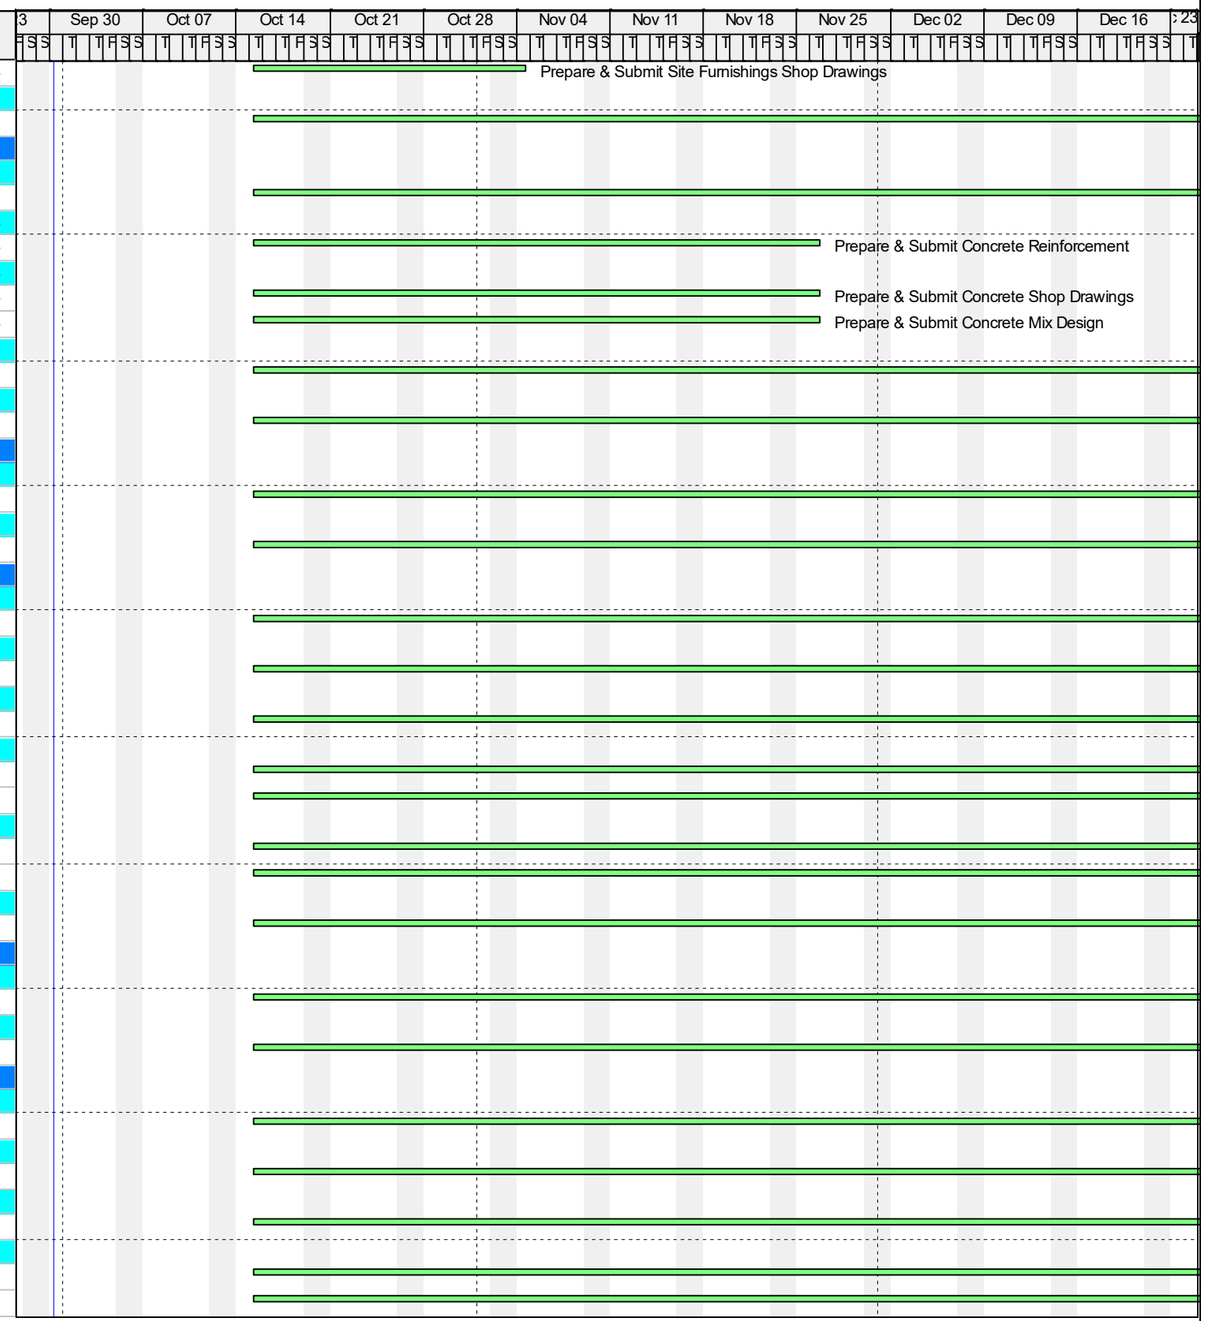

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

New Building PS/IS 341Q - Baseline Schedule Rev 01

NAVILLUS BUILDING THE WORLD AROUND YOU

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By : M.K

Date	**Revision**	**Checked**	**Approved**
21-Mar-25	00	A.A	

One Month Lookahead

Activity ID	Activity Name	Original Duration	Start	Finish
Spec Section 07560 - Fluid Applied Protected Membrane Roofing		81	15-Oct-24	11-Feb-25
SUB-1130	Prepare & Submit Roofing Membrane Product Data	81	15-Oct-24	11-Feb-25
Spec Section 07600 - Flashing and Sheet Metal		81	15-Oct-24	11-Feb-25
SUB-1120	Prepare & Submit Flashing & Sheet Metal Shop Drawing	81	15-Oct-24	11-Feb-25
Spec Section 07720 - Roof Accessories		81	15-Oct-24	11-Feb-25
SUB-1110	Prepare & Submit Roof Drains & Clean Outs	81	15-Oct-24	11-Feb-25
Division 08 - Doors & Windows		81	15-Oct-24	11-Feb-25
Spec Section 08110 - Steel Doors and Frames		81	15-Oct-24	11-Feb-25
SUB-1100	Prepare & Submit Door & Frame Corners Samples	81	15-Oct-24	11-Feb-25
Spec Section 08210 - Wood Doors		81	15-Oct-24	11-Feb-25
SUB-1620	Prepare & Submit Wood Doors	81	15-Oct-24	11-Feb-25
Spec Section 08330 - Coiling Doors, Grilles And Shutters		81	15-Oct-24	11-Feb-25
SUB-2960	Prepare & Submit Coiling Doors, Grilles and Shutters Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2970	Prepare & Submit Coiling Doors, Grilles and Shutters Product Data	81	15-Oct-24	11-Feb-25
Spec Section 08411 - Aluminum Framed Entrances And Storefronts		81	15-Oct-24	11-Feb-25
SUB-2980	Prepare & Submit Aluminum Framed Entrances & Storefronts Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-2990	Prepare & Submit Aluminum Framed Entrances & Storefronts Product Data	81	15-Oct-24	11-Feb-25
Spec Section 08521 - Fire Rated Glazing Systems		81	15-Oct-24	11-Feb-25
SUB-3040	Prepare & Submit Fire Rated Glazing Samples	81	15-Oct-24	11-Feb-25
SUB-3050	Prepare & Submit Fire Rated Glazing Product Data	81	15-Oct-24	11-Feb-25
Spec Section 08524 - Aluminum Projected Windows		71	15-Oct-24	28-Jan-25
SUB-1670	Prepare & Submit Aluminum Projected Windows	71	15-Oct-24	28-Jan-25
Spec Section 08662 - Security Screens & Barriers		81	15-Oct-24	11-Feb-25
SUB-2000	Prepare & Submit Security Screens & Barriers	81	15-Oct-24	11-Feb-25
Spec Section 08710 - Finish Hardware		81	15-Oct-24	11-Feb-25
SUB-1080	Prepare & Submit Door Hardware Submittal	81	15-Oct-24	11-Feb-25
Spec Section 08730 - Thresholds, Weatherstripping And Seals		81	15-Oct-24	11-Feb-25
SUB-3000	Prepare & Submit Thresholds, Weatherstripping and Seals Color Samples	81	15-Oct-24	11-Feb-25
SUB-3010	Prepare & Submit Thresholds, Weatherstripping and Seals Product Data	81	15-Oct-24	11-Feb-25
Spec Section 08800 - Miscellaneous Glazing		81	15-Oct-24	11-Feb-25
SUB-3020	Prepare & Submit Miscellaneous Glazing Samples	81	15-Oct-24	11-Feb-25
SUB-3030	Prepare & Submit Miscellaneous Glazing Product Data	81	15-Oct-24	11-Feb-25
Division 09 - Finishes		81	15-Oct-24	11-Feb-25
Spec Section 09260 - Gypsum Board Assemblies		81	15-Oct-24	11-Feb-25
SUB-1470	Prepare & Submit Gypsum Board	81	15-Oct-24	11-Feb-25
Spec Section 09310 - Ceramic Tiles		81	15-Oct-24	11-Feb-25
SUB-1070	Prepare & Submit Ceramic Tiles Product Data	81	15-Oct-24	11-Feb-25
Spec Section 09510 - Acoustical Ceilings		60	15-Oct-24	10-Jan-25
SUB-1490	Prepare & Submit Acosutical Ceiling Tiles	60	15-Oct-24	10-Jan-25
Spec Section 09590 - Wood Flooring		81	15-Oct-24	11-Feb-25
SUB-2010	Prepare & Submit Wood Flooring	81	15-Oct-24	11-Feb-25
Spec Section 09650 - Resilient Flooring		81	15-Oct-24	11-Feb-25
SUB-1480	Prepare & Submit Floorings	81	15-Oct-24	11-Feb-25
Spec Section 09800 - Special Coatings		81	15-Oct-24	11-Feb-25
SUB-3070	Prepare & Submit Special Coating Samples	81	15-Oct-24	11-Feb-25
SUB-3080	Prepare & Submit Special Coating Product Data	81	15-Oct-24	11-Feb-25
Spec Section 09860 - Grafiti Resistant Coatings		81	15-Oct-24	11-Feb-25
SUB-3060	Prepare & Submit Graffiti Resistant Coating Product Data	81	15-Oct-24	11-Feb-25
Spec Section 09900 - Painting		81	15-Oct-24	11-Feb-25
SUB-1090	Prepare & Submit Painting	81	15-Oct-24	11-Feb-25

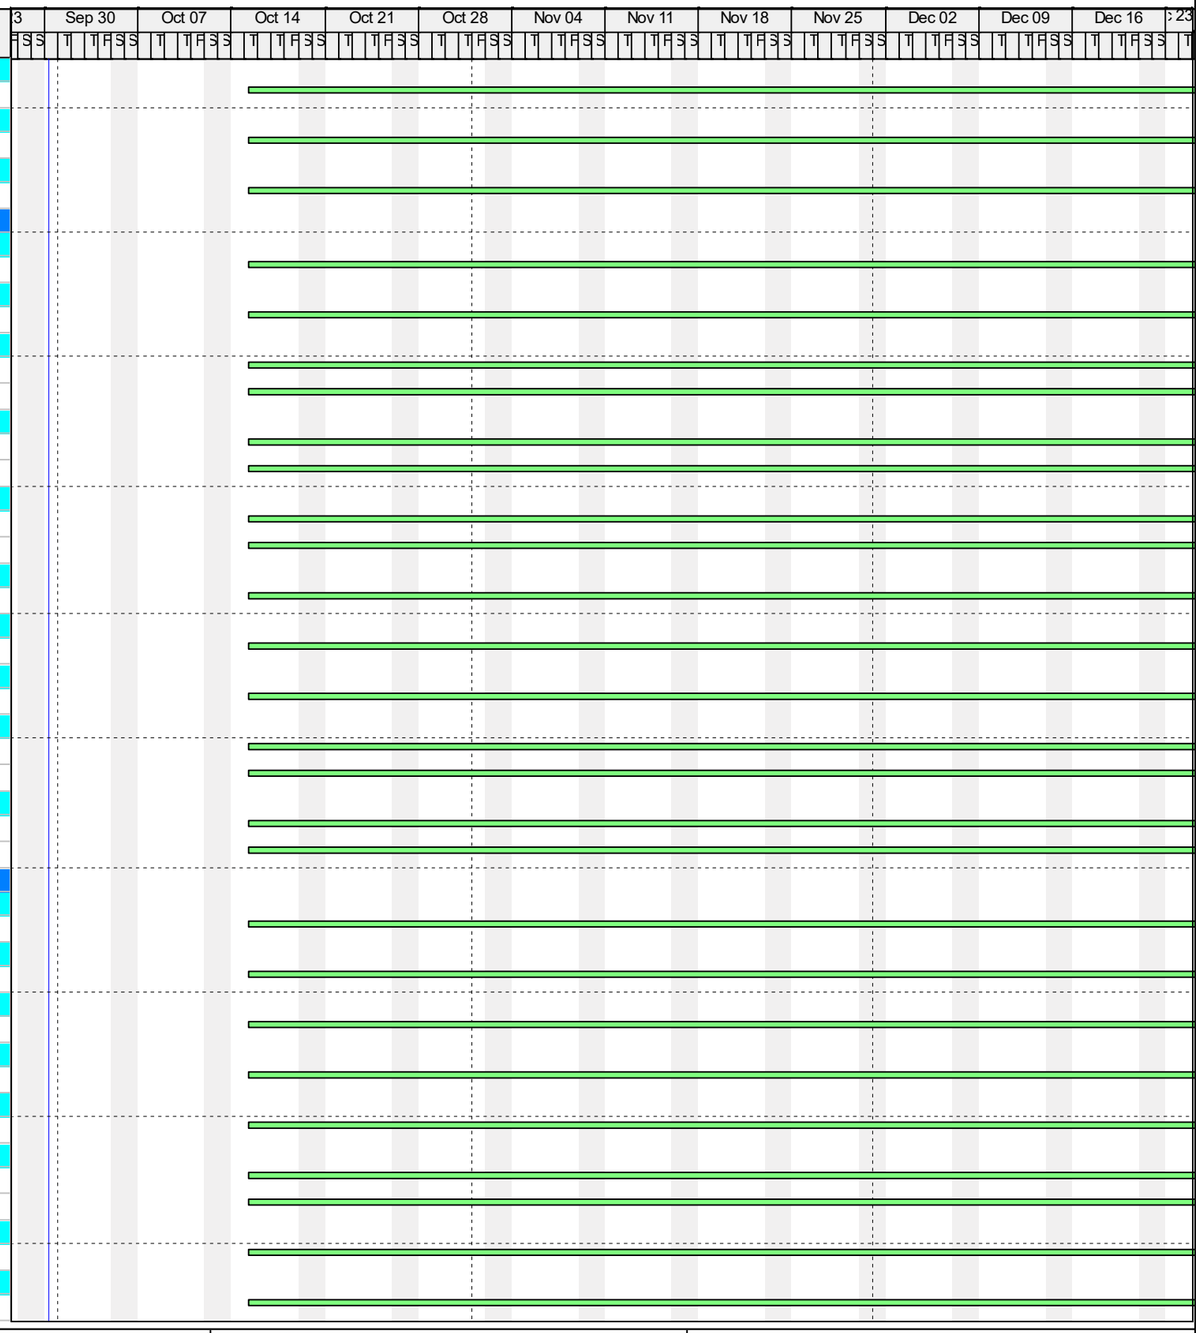

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By : M.K

Date	Revision	Checked	Approved
21-Mar-25	00	A.A	

One Month Lookahead

Activity ID	Activity Name	Original Duration	Start	Finish
Division 10 - Specialties		81	15-Oct-24	11-Feb-25
Spec Section 10100 - Visual Display Boards		81	15-Oct-24	11-Feb-25
SUB-2020	Prepare & Submit Visual Display Boards	81	15-Oct-24	11-Feb-25
Spec Section 10350 - Flagpole		81	15-Oct-24	11-Feb-25
SUB-3090	Prepare & Submit Flagpole Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3100	Prepare & Submit Flagpole Product Data	81	15-Oct-24	11-Feb-25
Spec Section 10400 - Identification Devices		81	15-Oct-24	11-Feb-25
SUB-1060	Prepare & Submit Interior Signage Shop Drawings	81	15-Oct-24	11-Feb-25
Spec Section 10415 - Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases		81	15-Oct-24	11-Feb-25
SUB-3110	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals	81	15-Oct-24	11-Feb-25
SUB-3120	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-3130	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	81	15-Oct-24	11-Feb-25
Spec Section 10505 - Metal Lockers		81	15-Oct-24	11-Feb-25
SUB-2030	Prepare & Submit Metal Lockers	81	15-Oct-24	11-Feb-25
Spec Section 10522 - Fire Extinguishers & Cabinets		81	15-Oct-24	11-Feb-25
SUB-2040	Prepare & Submit Fire Extinguishers & Cabinets	81	15-Oct-24	11-Feb-25
Spec Section 10605 - Wire Mesh Work		81	15-Oct-24	11-Feb-25
SUB-3140	Prepare & Submit Wire Mesh Work Samples	81	15-Oct-24	11-Feb-25
SUB-3150	Prepare & Submit Wire Mesh Work Shop drawings	81	15-Oct-24	11-Feb-25
Spec Section 10675 - Metal Storage Shelving		81	15-Oct-24	11-Feb-25
SUB-3160	Prepare & Submit Metal Storage Shelving Samples	81	15-Oct-24	11-Feb-25
SUB-3170	Prepare & Submit Metal Storage Shelving Shop drawings	81	15-Oct-24	11-Feb-25
Spec Section 10720 - Window Guards		73	15-Oct-24	30-Jan-25
SUB-2050	Prepare & Submit Stationary Metal Wall Louvers	73	15-Oct-24	30-Jan-25
Spec Section 10810 - Toilet & Bath Accessories		81	15-Oct-24	11-Feb-25
SUB-1500	Prepare & Submit Toilet Accessories	81	15-Oct-24	11-Feb-25
Spec Section 10830 - Mirrors		81	15-Oct-24	11-Feb-25
SUB-3180	Prepare & Submit Mirrors Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3190	Prepare & Submit Mirrors Product Data	81	15-Oct-24	11-Feb-25
SUB-3200	Prepare & Submit Mirrors Mastic Compatibility Test Reports & Certifications	81	15-Oct-24	11-Feb-25
Spec Section 10840 - Grab Bars		81	15-Oct-24	11-Feb-25
SUB-3210	Prepare & Submit Grab Bars Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3220	Prepare & Submit Grab Bars Product Data	81	15-Oct-24	11-Feb-25
Division 11 - Equipment		81	15-Oct-24	11-Feb-25
Spec Section 11050 - Library Equipment		81	15-Oct-24	11-Feb-25
SUB-2060	Prepare & Submit Library Equipment	81	15-Oct-24	11-Feb-25
Spec Section 11061 - Platform Curtains & Auditorium Window Curtains		81	15-Oct-24	11-Feb-25
SUB-2070	Prepare & Submit Platform Curtains & Auditorium Window Curtains	81	15-Oct-24	11-Feb-25
Spec Section 11172 - Waste Handling Equipment		81	15-Oct-24	11-Feb-25
SUB-2080	Prepare & Submit Waste Handling Equipment	81	15-Oct-24	11-Feb-25
Spec Section 11400 - Food Service Equipment		71	15-Oct-24	28-Jan-25
SUB-1650	Prepare & Submit Kitchen Equipment	71	15-Oct-24	28-Jan-25
Spec Section 11450 - Domestic Type Equipment		81	15-Oct-24	11-Feb-25
SUB-2090	Prepare & Submit Domestic Equipment	81	15-Oct-24	11-Feb-25
Spec Section 11480 - Gymnasium Equipment		81	15-Oct-24	11-Feb-25
SUB-1770	Prepare & Submit Gymnasium Equipment	81	15-Oct-24	11-Feb-25
Spec Section 11500 - Shop Equipment		81	15-Oct-24	11-Feb-25
SUB-3230	Prepare & Submit Shop Equipment Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3240	Prepare & Submit Shop Equipment Product Data	81	15-Oct-24	11-Feb-25
Spec Section 11600 - Laboratory Equipment		81	15-Oct-24	11-Feb-25

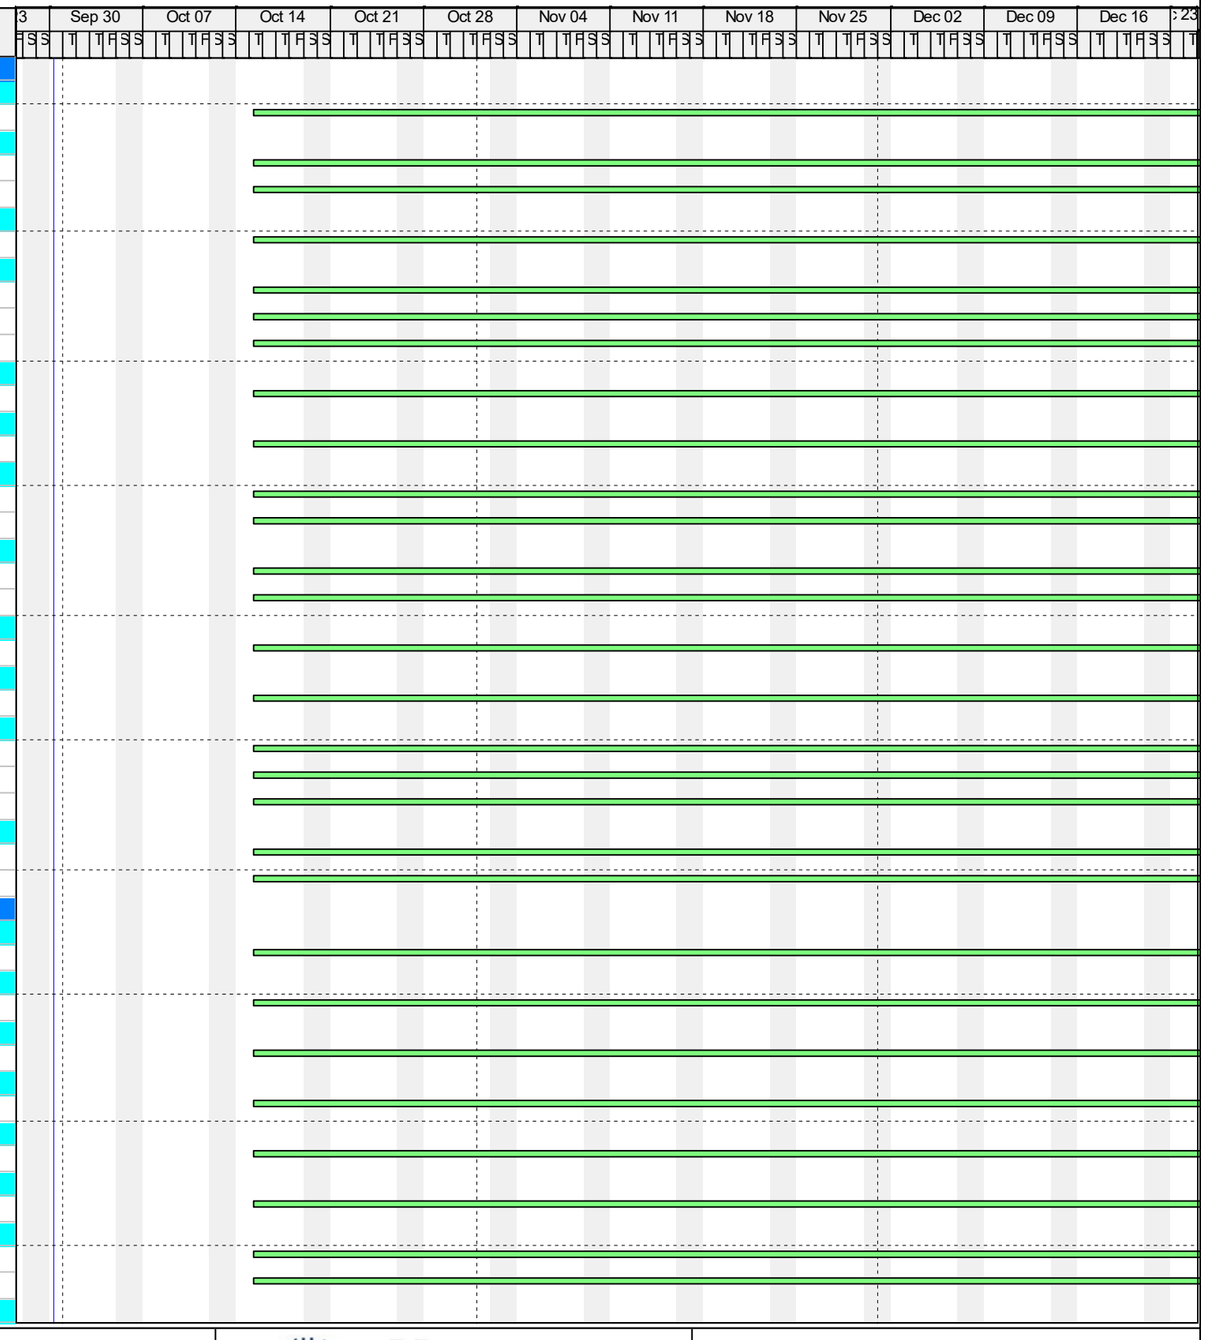

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By : M.K

Date	Revision	Checked	Approved
21-Mar-25	00	A.A	

One Month Lookahead

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-2100	Prepare & Submit Laboratory Equipment	81	15-Oct-24	11-Feb-25
Division 12 - Furnishings		81	15-Oct-24	11-Feb-25
Spec Section 12761 - Bleachers		81	15-Oct-24	11-Feb-25
SUB-3250	Prepare & Submit Bleachers Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3260	Prepare & Submit Bleachers Product Data	81	15-Oct-24	11-Feb-25
SUB-3270	Prepare & Submit Bleachers Manufacturer's Warranty	81	15-Oct-24	11-Feb-25
Spec Section 12302 - Manufactured Wood Casework		81	15-Oct-24	11-Feb-25
SUB-2110	Prepare & Submit Manufactured Wood Casework	81	15-Oct-24	11-Feb-25
Division 13 - Special Construction		81	15-Oct-24	11-Feb-25
Spec Section 13487 - Concrete Floating Floor Assembly		81	15-Oct-24	11-Feb-25
SUB-2120	Prepare & Submit Concrete Floating Floor Assembly	81	15-Oct-24	11-Feb-25
Division 14 - Conveying Systems		81	15-Oct-24	11-Feb-25
Spec Section 14211 - Geared Traction Passenger Elevators		71	15-Oct-24	28-Jan-25
SUB-1460	Prepare & Submit Elevator Machine	71	15-Oct-24	28-Jan-25
Spec Section 14420 - Hydraulic Vertical Wheelchair Lifts		81	15-Oct-24	11-Feb-25
SUB-2130	Prepare & Submit Hydraulic Vertical Wheelchair Lifts	81	15-Oct-24	11-Feb-25
Division 15 - Mechanical		81	15-Oct-24	11-Feb-25
Division 15A - Fire Protection		81	15-Oct-24	11-Feb-25
Spec Section 15330 - Sprinkler System		81	15-Oct-24	11-Feb-25
SUB-1440	Prepare & Submit Sprinkler System Shop Drawings	81	15-Oct-24	11-Feb-25
Spec Section 15333 - Fire Pumps - Sprinkler Booster Pumps		81	15-Oct-24	11-Feb-25
SUB-1050	Prepare & Submit Fire & Jockey Pumps	81	15-Oct-24	11-Feb-25
SUB-1630	Prepare & Submit Fire Protection Shop Drawings	81	15-Oct-24	11-Feb-25
Division 15B - Plumbing & Drainage		81	15-Oct-24	11-Feb-25
Spec Section 15410 - Plumbing Piping		81	15-Oct-24	11-Feb-25
SUB-1430	Prepare & Submit Plumbing Shop Drawings	81	15-Oct-24	11-Feb-25
Spec Section 15411 - Hangers and Supports		40	15-Oct-24	11-Dec-24
SUB-1040	Prepare & Submit Hangers & Supports	40	15-Oct-24	11-Dec-24
Spec Section 15412 - Valves		81	15-Oct-24	11-Feb-25
SUB-3280	Prepare & Submit Valves Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3290	Prepare & Submit Valves Product Data	81	15-Oct-24	11-Feb-25
Spec Section 15414 - Tests		81	15-Oct-24	11-Feb-25
SUB-3300	Prepare & Submit Certification of Tests	81	15-Oct-24	11-Feb-25
SUB-3310	Prepare & Submit Domestic Water Sterilization Plan	81	15-Oct-24	11-Feb-25
Spec Section 15415 - Drainage		40	15-Oct-24	11-Dec-24
SUB-1030	Prepare & Submit Floor Drains	40	15-Oct-24	11-Dec-24
Spec Section 15416 - Gas Piping System		81	15-Oct-24	11-Feb-25
SUB-2170	Prepare & Submit Gas Pipes	81	15-Oct-24	11-Feb-25
Spec Section 15417 - Cold Water Supply		40	15-Oct-24	11-Dec-24
SUB-1020	Prepare & Submit Pressure Gages	40	15-Oct-24	11-Dec-24
Spec Section 15418 - Hot Water Supply		40	15-Oct-24	11-Dec-24
SUB-1010	Prepare & Submit Thermometers	40	15-Oct-24	11-Dec-24
Spec Section 15431 - Tags, Charts, And Identification		81	15-Oct-24	11-Feb-25
SUB-3320	Prepare & Submit Tags, Charts & Identifications Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3330	Prepare & Submit Tags, Charts & Identifications Product Data	81	15-Oct-24	11-Feb-25
Spec Section 15432 - Miscellaneous		81	15-Oct-24	11-Feb-25
SUB-3340	Prepare & Submit Micselianeous Shop Drawing	81	15-Oct-24	11-Feb-25
Spec Section 15440 - Plumbing Fixtures		81	15-Oct-24	11-Feb-25
SUB-1600	Prepare & Submit Plumbing Fixtures	81	15-Oct-24	11-Feb-25
Spec Section 15451 - Water Heaters		81	15-Oct-24	11-Feb-25

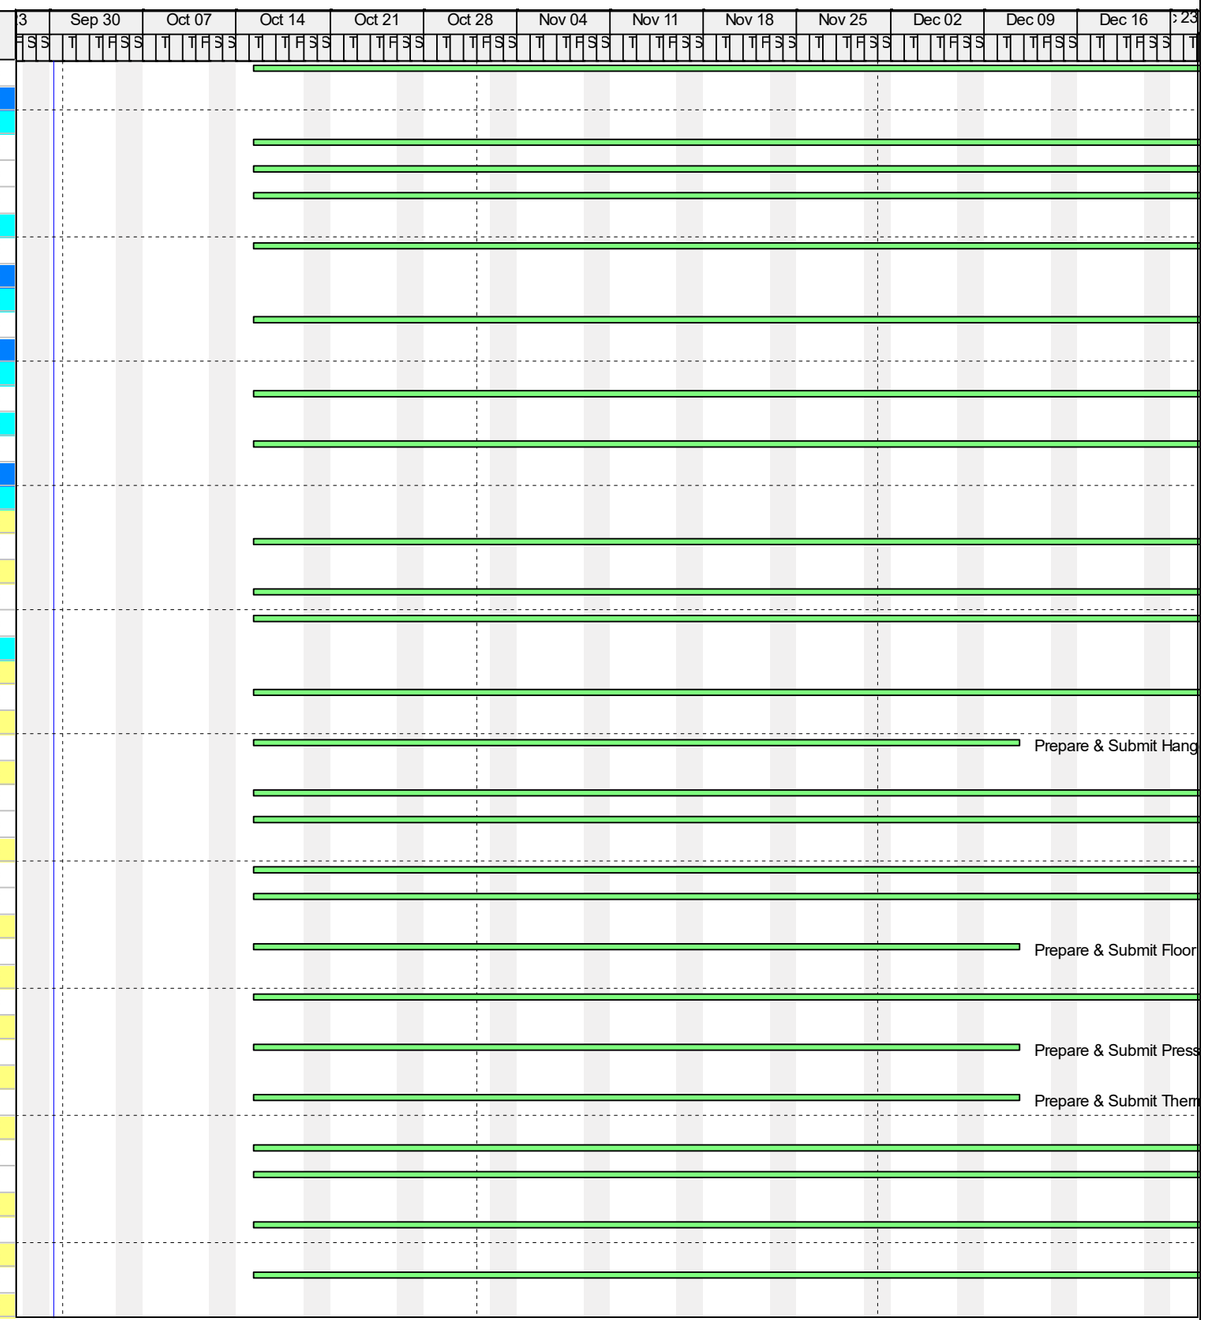

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By : M.K

Date	Revision	Checked	Approved
21-Mar-25	00	A.A	

One Month Lookahead

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-2180	Prepare & Submit Water Heaters	81	15-Oct-24	11-Feb-25
Spec Section 15453 - Pumping Apparatus & Tanks		81	15-Oct-24	11-Feb-25
SUB-2190	Prepare & Submit Pumping Apparatus & Tanks	81	15-Oct-24	11-Feb-25
Division 15C - Heating & Ventilation & Air Conditioning		81	15-Oct-24	11-Feb-25
Spec Section 15510 - HVAC Piping		60	15-Oct-24	10-Jan-25
SUB-1550	Prepare & Submit Mechanical Piping	60	15-Oct-24	10-Jan-25
Spec Section 15511 - Valves (Hvac)		81	15-Oct-24	11-Feb-25
SUB-3350	Prepare & Submit Valves (HVAC) Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3360	Prepare & Submit Valves (HVAC) Product Data	81	15-Oct-24	11-Feb-25
Spec Section 15512 - Piping Insulation (Hvac)		81	15-Oct-24	11-Feb-25
SUB-3370	Prepare & Submit Piping Insulation Schedule Listing Items	81	15-Oct-24	11-Feb-25
Spec Section 15513 - Equipment Insulation (Hvac)		81	15-Oct-24	11-Feb-25
SUB-3380	Prepare & Submit Schedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	81	15-Oct-24	11-Feb-25
Spec Section 15514 - Ductwork Insulation		81	15-Oct-24	11-Feb-25
SUB-3390	Prepare & Submit Schedules Showing Manfacturers's Product Number Duct Work Insulation	81	15-Oct-24	11-Feb-25
Spec Section 15515 - Hydronic Specialties		81	15-Oct-24	11-Feb-25
SUB-3400	Prepare & Submit Hydronic Specialities Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3410	Prepare & Submit Hydronic Specialities Product Data	81	15-Oct-24	11-Feb-25
Spec Section 15517 - Water Treatment For Hydronic Systems		81	15-Oct-24	11-Feb-25
SUB-3420	Prepare & Submit Water Treatment Firm	81	15-Oct-24	11-Feb-25
SUB-3430	Prepare & Submit Chemical Products Product Data	81	15-Oct-24	11-Feb-25
Spec Section 15540 - HVAC Pumps		81	15-Oct-24	11-Feb-25
SUB-2200	Prepare & Submit HVAC Pumps	81	15-Oct-24	11-Feb-25
Spec Section 15565 - Hot Water Condensing Boilers		71	15-Oct-24	28-Jan-25
SUB-1730	Prepare & Submit Boilers	71	15-Oct-24	28-Jan-25
Spec Section 15570 - Boiler Accessories		71	15-Oct-24	28-Jan-25
SUB-3440	Prepare & Submit Detail of Gag for the Safety Relief Valves	71	15-Oct-24	28-Jan-25
SUB-3450	Prepare & Submit Boiler Accessories Maintenance Data	71	15-Oct-24	28-Jan-25
Spec Section 15575 - Breeching Chimney Connectors And Chimneys		81	15-Oct-24	11-Feb-25
SUB-3460	Prepare & Submit Breeching Chimney Connectors and Chimneys Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3470	Prepare & Submit Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	81	15-Oct-24	11-Feb-25
Spec Section 15792 - Coils		81	15-Oct-24	11-Feb-25
SUB-3500	Prepare & Submit Coils Maintenance Data	81	15-Oct-24	11-Feb-25
SUB-3510	Prepare & Submit Coils Certifications	81	15-Oct-24	11-Feb-25
Spec Section 15835 - Convectors		81	15-Oct-24	11-Feb-25
SUB-3520	Prepare & Submit Convectors Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3530	Prepare & Submit Convectors Product Data	81	15-Oct-24	11-Feb-25
Spec Section 15838 - Fan Coil Units		81	15-Oct-24	11-Feb-25
SUB-3540	Prepare & Submit Fan Coils Units Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
SUB-3550	Prepare & Submit Fan Coils Units Shop Drawings	81	15-Oct-24	11-Feb-25
Spec Section 15839 - Door Air Curtains		81	15-Oct-24	11-Feb-25
SUB-3560	Prepare & Submit Door Air Curtains Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3570	Prepare & Submit Door Air Curtains Product Data	81	15-Oct-24	11-Feb-25
Spec Section 15860 - Centrifugal Fans		81	15-Oct-24	11-Feb-25
SUB-3580	Prepare & Submit Centrifugal Fans Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3590	Prepare & Submit Centrifugal Fans Product Data	81	15-Oct-24	11-Feb-25
SUB-3600	Prepare & Submit Centrifugal Fans Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
Spec Section 15885 - Air Filters		81	15-Oct-24	11-Feb-25
SUB-3610	Prepare & Submit Air Filters Shop Drawing	81	15-Oct-24	11-Feb-25

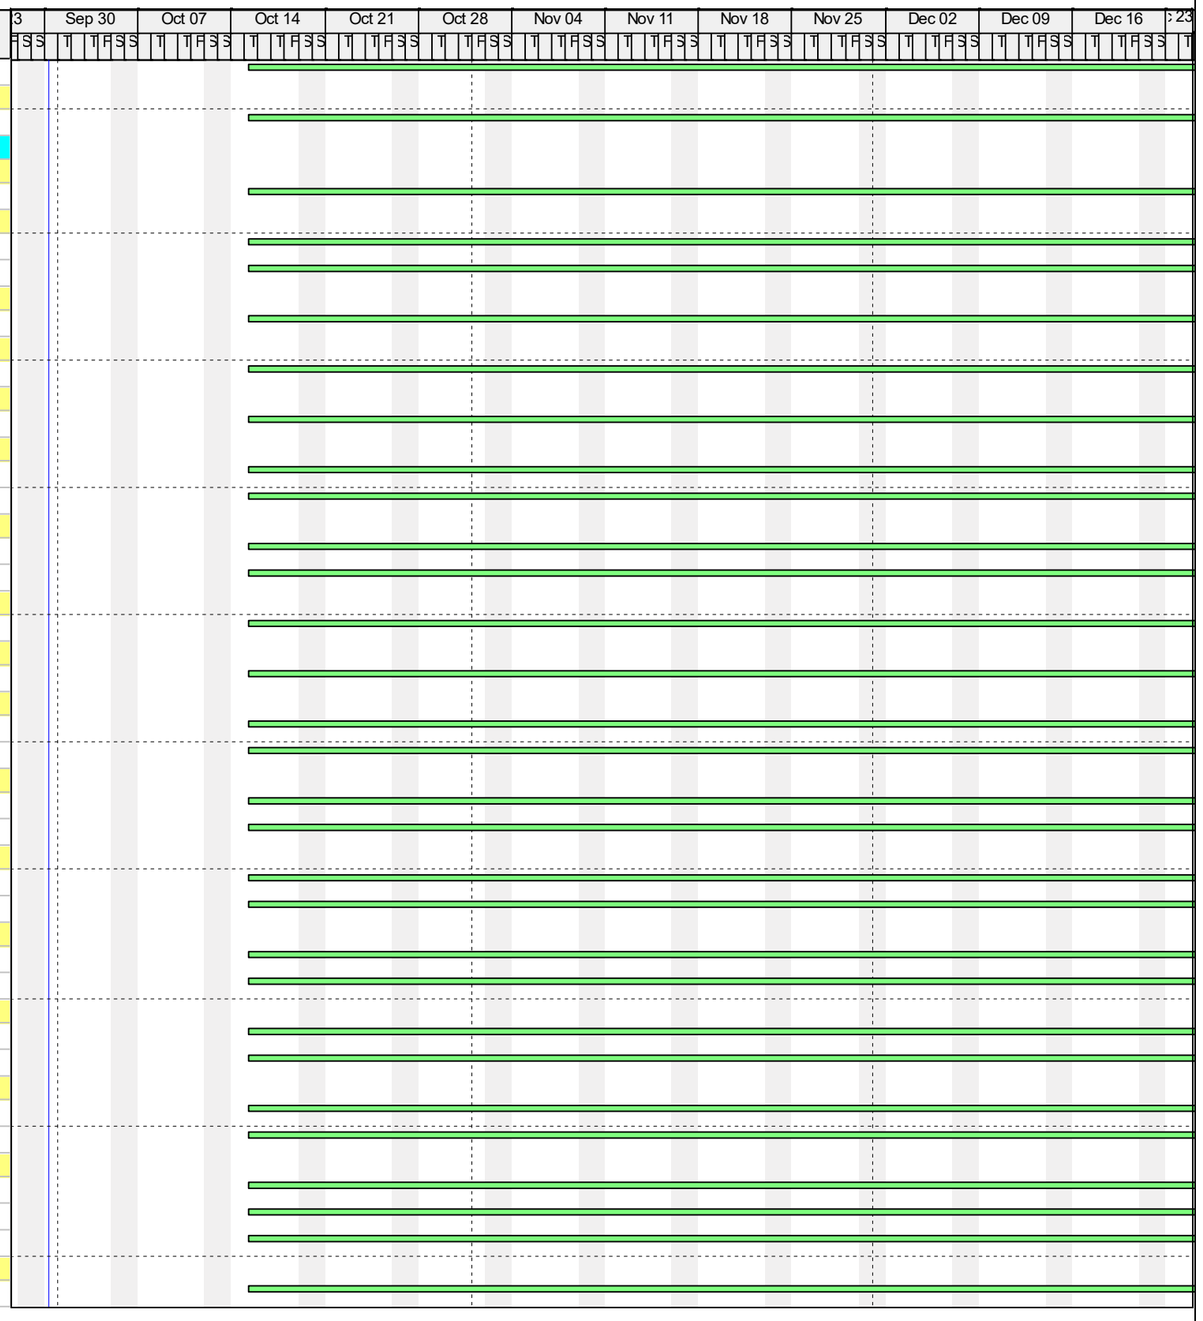

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

PROJECS ENGINEERING CONSULTING SERVICES

Prepared By : M.K

Date	Revision	Checked	Approved
21-Mar-25	00	A.A	

One Month Lookahead

Activity ID	Activity Name	Original Duration	Start	Finish
SUB-3620	Prepare & Submit Air Filters Product Data	81	15-Oct-24	11-Feb-25
SUB-3630	Prepare & Submit Air Filters Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
Spec Section 15590 - Emergency Generator System Accessories		71	15-Oct-24	28-Jan-25
SUB-2210	Prepare & Submit Emergency Generator System Accessories	71	15-Oct-24	28-Jan-25
Spec Section 15594 - Fuel Storage Equipment		81	15-Oct-24	11-Feb-25
SUB-2220	Prepare & Submit Fuel Storage Equipment	81	15-Oct-24	11-Feb-25
Spec Section 15596 - Natural Gas Leak Detection Equipment		81	15-Oct-24	11-Feb-25
SUB-2230	Prepare & Submit Natural Gas Leak Detection Equipment	81	15-Oct-24	11-Feb-25
Spec Section 15660 - Packaged Modular Outdoor Chillers		71	15-Oct-24	28-Jan-25
SUB-1710	Prepare & Submit Chillers Product Data	71	15-Oct-24	28-Jan-25
Spec Section 15670 - Plate Heat Exchangers		81	15-Oct-24	11-Feb-25
SUB-3480	Prepare & Submit Plate Heat Exchanger Maintenance Data	81	15-Oct-24	11-Feb-25
SUB-3490	Prepare & Submit Plate Heat Exchanger Product Data	81	15-Oct-24	11-Feb-25
Spec Section 15783 - Split Heat Pump System		60	15-Oct-24	10-Jan-25
SUB-1000	Prepare & Submit Split Heat Pump System - SUB	60	15-Oct-24	10-Jan-25
Spec Section 15836 - Unit Heaters Cabinet Heaters		60	15-Oct-24	10-Jan-25
SUB-1760	Prepare & Submit Unit Cabinet Heaters	60	15-Oct-24	10-Jan-25
Spec Section 15852 - Air Handling Units		71	15-Oct-24	28-Jan-25
SUB-1720	Prepare & Submit Air Handling Units Product Data	71	15-Oct-24	28-Jan-25
Spec Section 15891 - Metal Ductwork		81	15-Oct-24	11-Feb-25
SUB-1540	Prepare & Submit Mechanical Ducts	81	15-Oct-24	11-Feb-25
Spec Section 15940 - Air Outlets & Inlets		81	15-Oct-24	11-Feb-25
SUB-2260	Prepare & Submit Air Outlets & Inlets	81	15-Oct-24	11-Feb-25
Spec Section 15970 - Temperature Control System		81	15-Oct-24	11-Feb-25
SUB-2250	Prepare & Submit Temperature Control System	81	15-Oct-24	11-Feb-25
Spec Section 15910 - Duct Accessories		81	15-Oct-24	11-Feb-25
SUB-3640	Prepare & Submit Duct Accessories Shop Drawing	81	15-Oct-24	11-Feb-25
Spec Section 15915 - Damper Assemblies		81	15-Oct-24	11-Feb-25
SUB-3650	Prepare & Submit Damper Assemblies Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3660	Prepare & Submit Damper Assemblies Product Data	81	15-Oct-24	11-Feb-25
SUB-3670	Prepare & Submit Damper Assemblies Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
Spec Section 15935 - Air Handling Units For Public Assembly Spaces		81	15-Oct-24	11-Feb-25
SUB-3710	Prepare & Submit AHU for Public Assemblies Sapces Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3720	Prepare & Submit AHU for Public Assemblies Sapces Product Data	81	15-Oct-24	11-Feb-25
SUB-3730	Prepare & Submit AHU for Public Assemblies Sapces Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
Spec Section 15930 - Variable Air Terminals		81	15-Oct-24	11-Feb-25
SUB-3680	Prepare & Submit Variable Air Terminals Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3690	Prepare & Submit Variable Air Terminals Product Data	81	15-Oct-24	11-Feb-25
SUB-3700	Prepare & Submit Variable Air Terminals Maintenance Data & Materials	81	15-Oct-24	11-Feb-25
Spec Section 15973 - Facility Management Systems Integration		81	15-Oct-24	11-Feb-25
SUB-3740	Prepare & Submit Control Systems Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3750	Prepare & Submit Truck Network Cable Schematic Diagram	81	15-Oct-24	11-Feb-25
Division 16 - Electrical		81	15-Oct-24	11-Feb-25
Spec Section 16010 - Gen Provisions for Elec Work		81	15-Oct-24	11-Feb-25
SUB-1420	Prepare & Submit Electrical Shop Drawings	81	15-Oct-24	11-Feb-25
SUB-1590	Prepare & Submit Electrical Equipment, Conduits, and Cables	20	15-Oct-24	12-Nov-24
SUB-1750	Prepare & Submit Switch Gears Product Data	20	15-Oct-24	12-Nov-24
Spec Section 16120 - Wiring Systems		81	15-Oct-24	11-Feb-25
SUB-1680	Prepare & Submit Telecommunication System Drawings	81	15-Oct-24	11-Feb-25

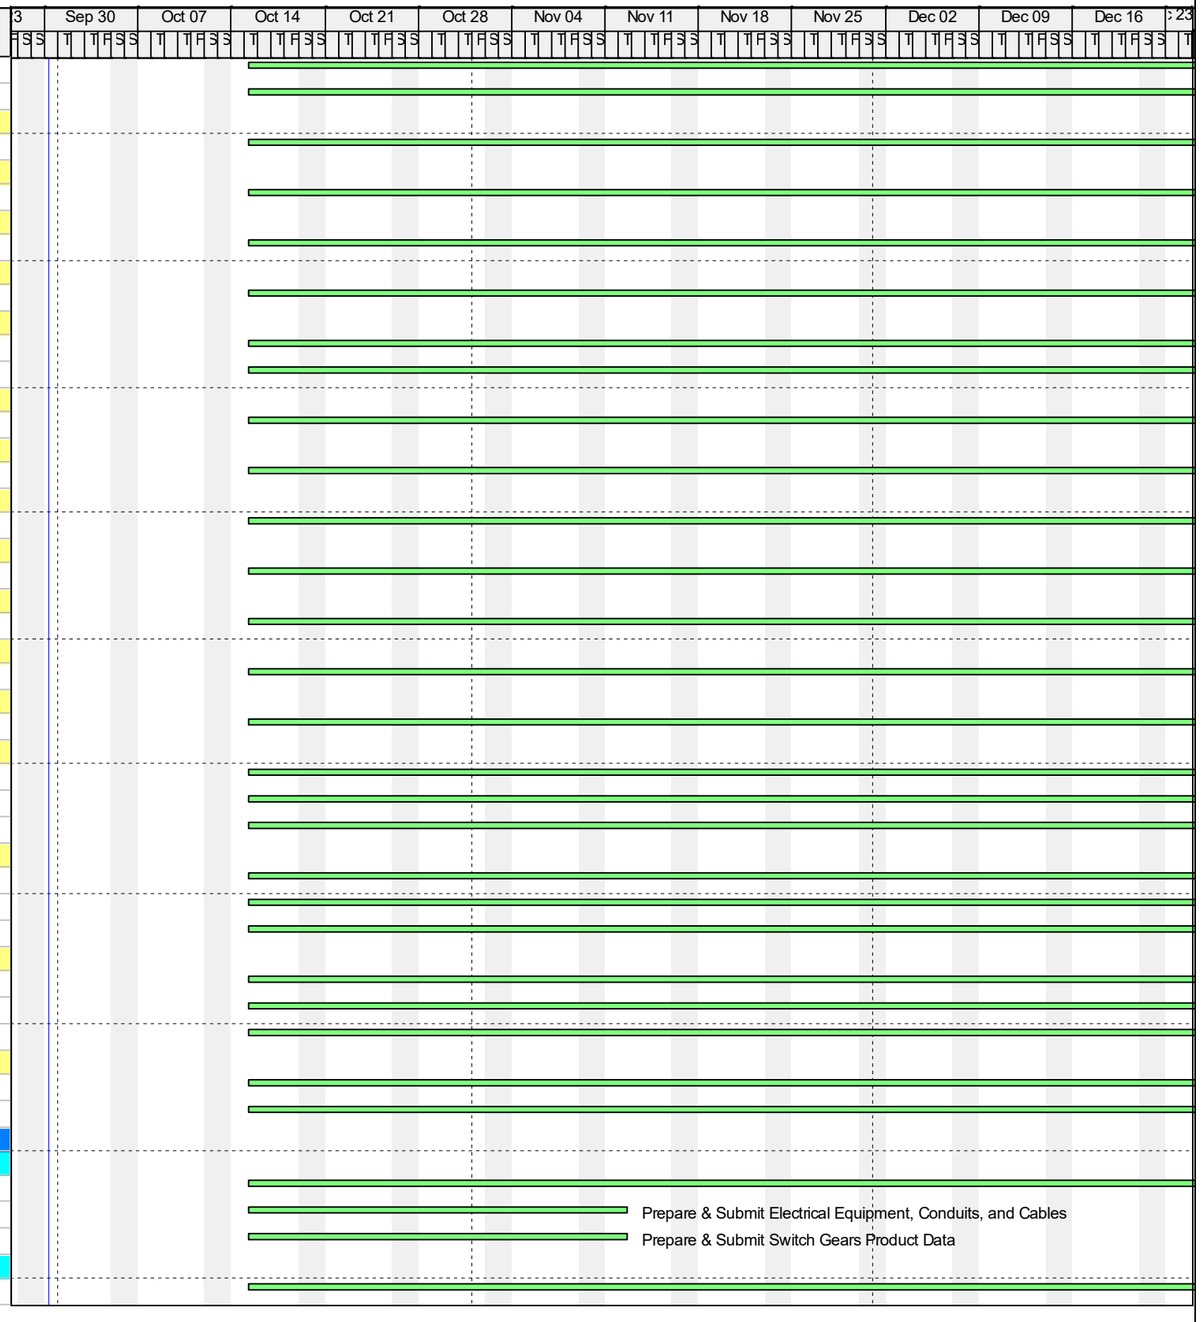

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLD AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By : M.K

Date	Revision	Checked	Approved
21-Mar-25	00	A.A	

One Month Lookahead

Activity ID	Activity Name	Original Duration	Start	Finish
Spec Section 16145 - Lighting Control Devices		71	15-Oct-24	28-Jan-25
SUB-3760	Prepare & Submit Lighting Control Devices Shop Drawing	71	15-Oct-24	28-Jan-25
SUB-3770	Prepare & Submit Lighting Control Devices Product Data	71	15-Oct-24	28-Jan-25
SUB-3780	Prepare & Submit Lighting Control Devices Warranty	71	15-Oct-24	28-Jan-25
Spec Section 16231- Emergency Generator System		71	15-Oct-24	28-Jan-25
SUB-1740	Prepare & Submit Emergency Generator System Product Data	71	15-Oct-24	28-Jan-25
Spec Section 16289 - Surge Protective Devices		81	15-Oct-24	11-Feb-25
SUB-3790	Prepare & Submit Surge Protective Devices Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3800	Prepare & Submit Surge Protective Devices Product Data	81	15-Oct-24	11-Feb-25
SUB-3810	Prepare & Submit Surge Protective Devices Warranty	81	15-Oct-24	11-Feb-25
Spec Section 16420 - Service Entrance Equipment		81	15-Oct-24	11-Feb-25
SUB-3820	Prepare & Submit Service Entrance Equipment Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3830	Prepare & Submit Service Entrance Equipment Product Data	81	15-Oct-24	11-Feb-25
SUB-3840	Prepare & Submit Service Entrance Equipment Warranty	81	15-Oct-24	11-Feb-25
Spec Section 16441- Enclosed Switches		81	15-Oct-24	11-Feb-25
SUB-3850	Prepare & Submit Enclosed Switches Product Data	81	15-Oct-24	11-Feb-25
SUB-3860	Prepare & Submit Enclosed Switches Test Reports	81	15-Oct-24	11-Feb-25
Spec Section 16480 - Motors, Motor Control Centers, Starters And Control Equipment		81	15-Oct-24	11-Feb-25
SUB-3870	Prepare & Submit Motors, Motor Control Centers and Starters Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3880	Prepare & Submit Motors, Motor Control Centers and Starters Product Data	81	15-Oct-24	11-Feb-25
SUB-3890	Prepare & Submit Motors, Motor Control Centers and Starters Field Test Reports	81	15-Oct-24	11-Feb-25
Spec Section 16425 - Switch Boards & Panel Boards		81	15-Oct-24	11-Feb-25
SUB-2140	Prepare & Submit Switch & Panel Boards	81	15-Oct-24	11-Feb-25
Spec Section 16471 - Auditorium & Television Studio Dimming System		81	15-Oct-24	11-Feb-25
SUB-2150	Prepare & Submit Auditorium & Television Studio Dimming System Product Data	81	15-Oct-24	11-Feb-25
Spec Section 16475 - Overcurrent Protective Devices		81	15-Oct-24	11-Feb-25
SUB-2160	Prepare & Submit Overcurrent Protective Devices Data	81	15-Oct-24	11-Feb-25
Spec Section 16502 - Interior Lighting Fixtures		71	15-Oct-24	28-Jan-25
SUB-1520	Prepare & Submit Lighting Fixtures	71	15-Oct-24	28-Jan-25
Spec Section 16520 - Illuminated Exit Sign		81	15-Oct-24	11-Feb-25
SUB-1660	Prepare & Submit Signs	81	15-Oct-24	11-Feb-25
Spec Section 16670 - Lightning Protection		81	15-Oct-24	11-Feb-25
SUB-3900	Prepare & Submit Lightning Protection Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3920	Prepare & Submit Lightning Protection Test Reports	81	15-Oct-24	11-Feb-25
Spec Section 16720 - Fire Detection Alarm System with COC		81	15-Oct-24	11-Feb-25
SUB-1640	Prepare & Submit Fire Detectors & Alarms	81	15-Oct-24	11-Feb-25
Spec Section 16728 - Fiber Optic Cabling System		81	15-Oct-24	11-Feb-25
SUB-3930	Prepare & Submit Fiber Optic Cabling system Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3940	Prepare & Submit Fiber Optic Cabling system Product Data	81	15-Oct-24	11-Feb-25
SUB-3950	Prepare & Submit Fiber Optic Cabling system Samples	81	15-Oct-24	11-Feb-25
Spec Section 16770 - Sound, Intercom & Teacher Activated Security System		81	15-Oct-24	11-Feb-25
SUB-3960	Prepare & Submit Sound, Intercome & Security System Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-3970	Prepare & Submit Sound, Intercome & Security System Programming Code and Password for the System	81	15-Oct-24	11-Feb-25
SUB-3980	Prepare & Submit Sound, Intercome & Security System Warranty	81	15-Oct-24	11-Feb-25
Spec Section 16771 - Projection And Interactive Whiteboard Systems		81	15-Oct-24	11-Feb-25
SUB-3990	Prepare & Submit Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	81	15-Oct-24	11-Feb-25
SUB-4000	Prepare & Submit Projection and Interactive Whiteboard Systems Wiring diagram	81	15-Oct-24	11-Feb-25
Spec Section 16785 - Internet Protocol Digital Video Surveillance System using Digital Cameras		71	15-Oct-24	28-Jan-25
SUB-1690	Prepare & Submit Internet Protocol Digital Video Surveillance System using Digital Cameras	71	15-Oct-24	28-Jan-25

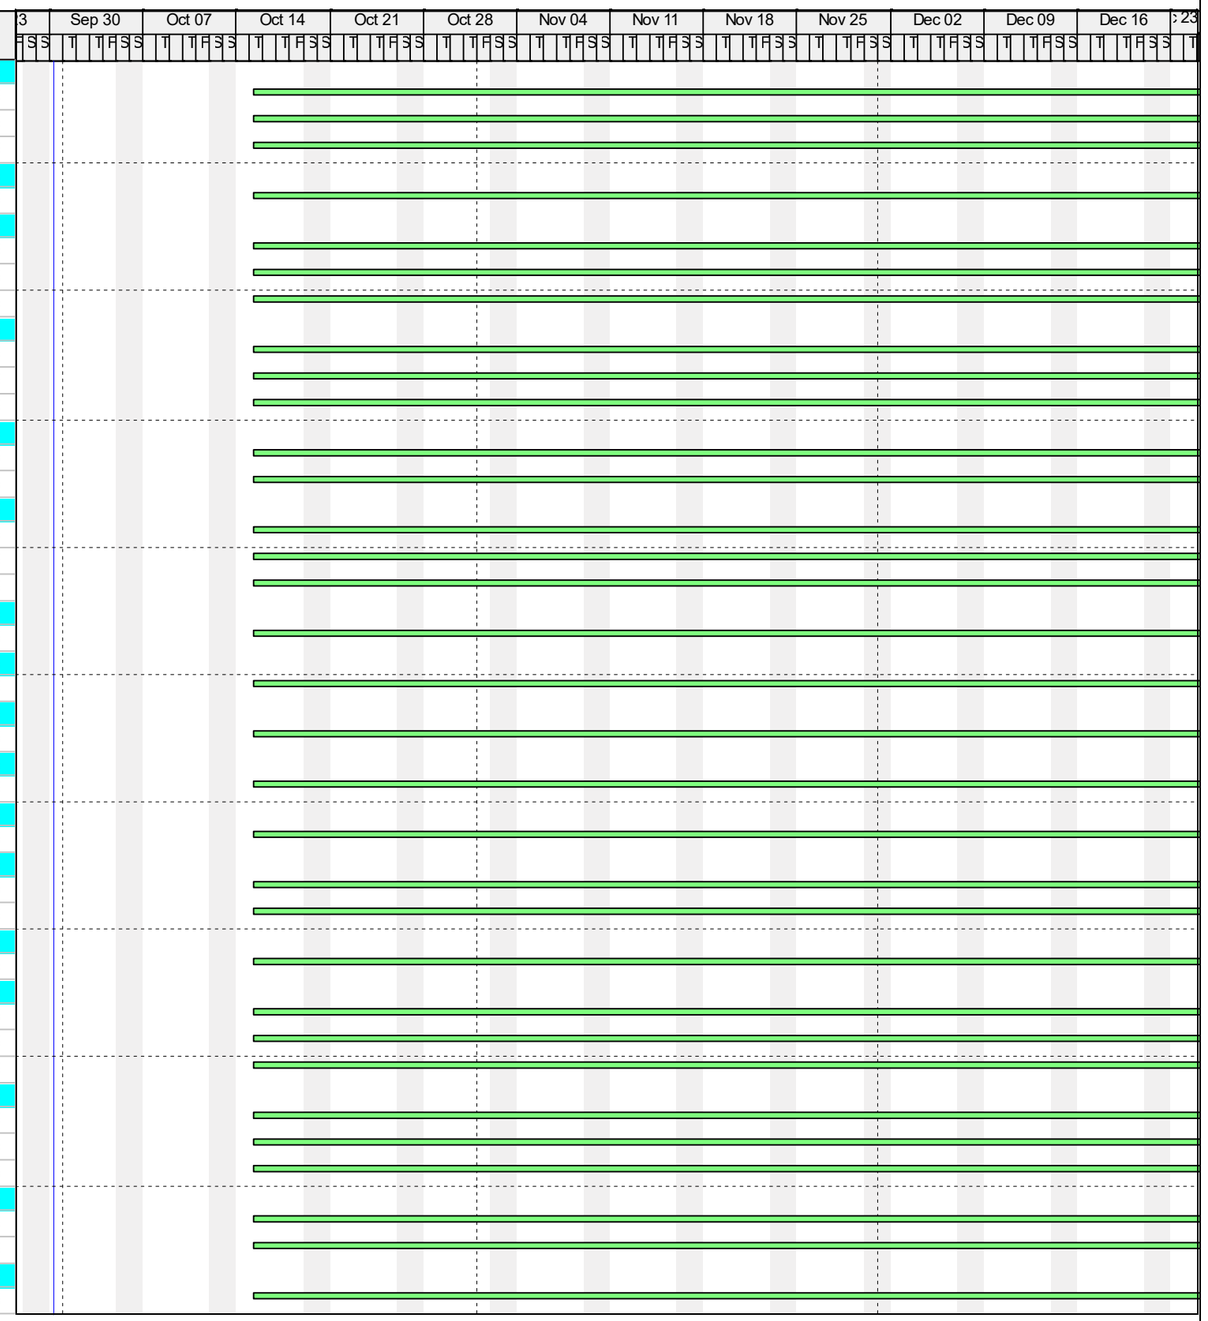

One Month Lookahead

Activity ID	Activity Name	Original Duration	Start	Finish
Spec Section 16791 - Self-Corrective Clock System		81	15-Oct-24	11-Feb-25
SUB-4010	Prepare & Submit Self Corrective Clock System Shop Drawing	81	15-Oct-24	11-Feb-25
SUB-4020	Prepare & Submit Self Corrective Clock System Product Data	81	15-Oct-24	11-Feb-25
SUB-4030	Prepare & Submit Self Corrective Clock System Field Test Reports	81	15-Oct-24	11-Feb-25
Spec Section 16855 - Heat Trace Cable System		81	15-Oct-24	11-Feb-25
SUB-4040	Prepare & Submit Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	81	15-Oct-24	11-Feb-25



APPENDIX 11
Near Critical Path

Near Critical Path Layout

Activity ID	Activity Name	Original Duration	Start	Finish
New Building PS/IS 341Q - Baseline Schedule Rev 01		405	20-Feb-25	30-Sep-26
Pre-construction		387	20-Feb-25	04-Sep-26
Milestones		387	20-Feb-25	04-Sep-26
Contract Milestones		387	20-Feb-25	04-Sep-26
MIL-2572	Place Steel Mill Order	0	20-Feb-25	
MIL-2612	Start Suspended Ceiling Grid	0	16-Mar-26	
MIL-2602	Start Mechanical Distribution Lines	0	08-Apr-26	
MIL-2712	Start Low Voltage	0	16-Apr-26	
MIL-2732	Start Mechanical and Electrical System Commissioning	0	07-Jul-26	
MIL-2562	Start Below Grade Plumbing and Other Utilities	0	16-Jul-26	
MIL-2742	Permanent Power Available	0		27-Jul-26
MIL-2592	P&D - Connection to Roof Drains	0	28-Jul-26	
MIL-2802	Provision of Training Schedules (30 days prior to start of Training)	0	10-Aug-26	
MIL-2722	Start Kitchen	0	04-Sep-26	
Construction		137	23-Feb-26	04-Sep-26
First Floor		106	07-Apr-26	04-Sep-26
Mechanical- 1st Floor		92	07-Apr-26	17-Aug-26
HVAC Rough-ins-1st Floor		10	07-Apr-26	20-Apr-26
CON-2900	Install Duct Risers-1st Floor	1	07-Apr-26	07-Apr-26
CON-3070	Duct Leak Test -1st Floor	1	08-Apr-26	08-Apr-26
CON-3120	Rough-in Duct Work -1st Floor	4	09-Apr-26	14-Apr-26
CON-3460	Rough-in Hot Water Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3470	Rough-in Hot Glycol Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3480	Rough-in Chilled Glycol Piping-1st Floor	4	15-Apr-26	20-Apr-26
CON-3490	Rough-in Refrigerant Piping-1st Floor	4	15-Apr-26	20-Apr-26
Mechanical Equipment-1st Floor		30	07-Jul-26	17-Aug-26
CON-4670	Install Exhaust Fans -1st Floor	5	07-Jul-26	13-Jul-26
CON-4870	Install Cabinet Unit Heaters With Fan CUH-1st Floor	3	14-Jul-26	16-Jul-26
CON-4880	Install Motorized Fire/Smoke Damper FSD - Mechanical Work - 1st Floor	7	14-Jul-26	22-Jul-26
CON-5150	Install Air Conditioning Unit AC - Mechanical Work - 1st Floor	4	23-Jul-26	28-Jul-26
CON-5320	Install Door Curtains DC - Mechanical Work - 1st Floor	7	29-Jul-26	06-Aug-26
CON-5490	Install Convector Heater CV - Mechanical Work - 1st Floor	7	07-Aug-26	17-Aug-26
Plumbing-1st Floor		34	07-May-26	25-Jun-26
CON-4460	Rough-in Gas Risers -1st Floor	4	07-May-26	12-May-26
CON-4590	Rough-in Domestic Water Piping-1st Floor	4	13-May-26	18-May-26
CON-4690	Rough-in Sanitary & Vent Piping -1st Floor	4	19-May-26	22-May-26
CON-4760	Rough-in Storm Piping -1st Floor	4	26-May-26	29-May-26
CON-4940	Install Duplex Domestic Water Booster Pump System (BP-1&BP-2) -1st Floor	8	01-Jun-26	10-Jun-26
CON-4950	Install Duplex Ejector Pump System (EJ-1&EJ-2) -1st Floor	8	01-Jun-26	10-Jun-26
CON-5050	Plumbing Pressure Testing -1st Floor	5	11-Jun-26	17-Jun-26
CON-5210	Plumbing Piping Insulation -1st Floor	5	18-Jun-26	25-Jun-26
Fire Protection-1st Floor		20	23-Jul-26	19-Aug-26
CON-5860	Install Sprinkler Booster Pump (SBP-1) -1st Floor	10	23-Jul-26	05-Aug-26
CON-6100	Install Jockey Pump (JP-1) -1st Floor	10	06-Aug-26	19-Aug-26

Near Critical Path Layout

Activity ID	Activity Name	Original Duration	Start	Finish
Electrical-1st Floor		94	21-Apr-26	02-Sep-26
CON-3760	Rough-in Power Conduits -1st Floor	4	21-Apr-26	24-Apr-26
CON-3920	Rough-in Low-Voltage Conduits-1st Floor	4	27-Apr-26	30-Apr-26
CON-3930	Power Wires Pulling-1st Floor	4	27-Apr-26	30-Apr-26
CON-4180	Low Voltage Wires Pulling -1st Floor	4	01-May-26	06-May-26
CON-5950	Install Fire alarm Sensors and Devises -1st Floor	3	05-Aug-26	07-Aug-26
CON-6040	Install IPDVS Devices -1st Floor	7	25-Aug-26	02-Sep-26
Architecture-1st Floor		76	19-May-26	04-Sep-26
Interior Walls-1st Floor		32	19-May-26	06-Jul-26
CON-9110	In-Wall Inspection -1st Floor	2	19-May-26	20-May-26
CON-1120	Install Firestopping Mock-Up	2	01-Jun-26	02-Jun-26
CON-1140	Approve Firestopping Mock-Up	2	03-Jun-26	04-Jun-26
MIL-1750	Start Firestopping	0	05-Jun-26	
CON-4450	Install Gypsum Board Walls-1st Floor	6	26-Jun-26	06-Jul-26
CON-4600	Tape Gypsum Board -1st Floor	4	30-Jun-26	06-Jul-26
CON-5390	Install Firestopping-1st Floor	4	30-Jun-26	06-Jul-26
Ceiling-1st Floor		32	23-Jul-26	04-Sep-26
CON-5870	Install Metal Panel Ceiling & Metal Geometric Ceiling -1st Floor	5	23-Jul-26	29-Jul-26
CON-5880	Install Acoustical Ceiling Tiles -1st Floor	5	31-Aug-26	04-Sep-26
Finishes-1st Floor		30	23-Jul-26	02-Sep-26
CON-5920	Install Door Frames & Doors-1st Floor	5	23-Jul-26	29-Jul-26
CON-6080	Install Flooring Tiles-1st Floor	5	30-Jul-26	05-Aug-26
CON-99267	Install Rolling Doors-1st Floor	3	30-Jul-26	03-Aug-26
CON-6310	Install Security Screens & Barriers-1st Floor	3	31-Aug-26	02-Sep-26
Second Floor		103	23-Feb-26	20-Jul-26
Mechanical-2nd Floor		61	23-Feb-26	18-May-26
HVAC Rough-ins-2nd Floor		61	23-Feb-26	18-May-26
CON-1410	Install Duct Risers-2nd Floor	1	23-Feb-26	23-Feb-26
CON-1480	Rough-in Duct Work -2nd Floor	4	24-Feb-26	27-Feb-26
CON-1880	Rough-in Refrigerant Piping-2nd Floor	7	02-Mar-26	10-Mar-26
CON-4070	Install Duct Insulation -2nd Floor	8	07-May-26	18-May-26
Plumbing-2nd Floor		16	06-Apr-26	27-Apr-26
CON-2630	Rough-in Gas Risers -2nd Floor	4	06-Apr-26	09-Apr-26
CON-2740	Rough-in Domestic Water Piping -2nd Floor	4	10-Apr-26	15-Apr-26
CON-2870	Rough-in Sanitary & Vent Piping -2nd Floor	4	16-Apr-26	21-Apr-26
CON-3020	Rough-in Storm Piping -2nd Floor	4	22-Apr-26	27-Apr-26
Electrical-2nd Floor		89	11-Mar-26	16-Jul-26
CON-2180	Rough-in Power Conduits -2nd Floor	6	11-Mar-26	18-Mar-26
CON-2330	Rough-in Low-Voltage Conduits -2nd Floor	6	19-Mar-26	26-Mar-26
CON-2340	Power Wires Pulling -2nd Floor	6	19-Mar-26	26-Mar-26
CON-2490	Low Voltage Wires Pulling -2nd Floor	6	27-Mar-26	03-Apr-26
CON-2540	Install Ground Bus Bar - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26
CON-98797	Install Intrusion System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-98847	Install Auxiliary System Components-2nd Floor	6	18-Jun-26	26-Jun-26
CON-98897	Install Sound Clock System Components-2nd Floor	6	18-Jun-26	26-Jun-26

Near Critical Path Layout

Activity ID	Activity Name	Original Duration	Start	Finish
CON-5140	Install IPDVS Devices -2nd Floor	9	06-Jul-26	16-Jul-26
Fire Protection-2nd Floor		14	04-May-26	21-May-26
CON-3310	Install 4" Standpipe -2nd Floor	4	04-May-26	07-May-26
CON-3500	Rough-in Main Sprinkler Piping -2nd Floor	5	08-May-26	14-May-26
CON-3670	Rough-in Branch Sprinkler Piping -2nd Floor	5	15-May-26	21-May-26
CON-3680	Rough-in Sprinkler Heads -2nd Floor	5	15-May-26	21-May-26
Architecture-2nd Floor		36	28-May-26	20-Jul-26
Interior Walls-2nd Floor		9	28-May-26	09-Jun-26
CON-4200	Tape Gypsum Board -2nd Floor	4	28-May-26	02-Jun-26
CON-4700	Install Firestopping-2nd Floor	3	05-Jun-26	09-Jun-26
Ceiling-2nd Floor		5	14-Jul-26	20-Jul-26
CON-5090	Install Acoustical Ceiling Tiles-2nd Floor	5	14-Jul-26	20-Jul-26
Third Floor		98	11-Mar-26	29-Jul-26
Mechanical -3rd Floor		97	11-Mar-26	28-Jul-26
HVAC Rough-ins -3rd Floor		57	11-Mar-26	29-May-26
CON-2150	Rough-in Chilled Glycol Piping-3rd Floor	7	11-Mar-26	19-Mar-26
CON-4320	Install Duct Insulation -3rd Floor	8	19-May-26	29-May-26
Mechanical Equipment -3rd Floor		8	17-Jul-26	28-Jul-26
CON-5060	Install Hot Glycol / Hot Water Cabinet Heater (CUH) -3rd Floor	4	17-Jul-26	22-Jul-26
CON-5280	Install Convector Heater CV - Mechanical Work - 3rd Floor	4	23-Jul-26	28-Jul-26
Plumbing -3rd Floor		16	10-Apr-26	01-May-26
CON-2750	Rough-in Gas Risers-3rd Floor	4	10-Apr-26	15-Apr-26
CON-2880	Rough-in Domestic Water Piping -3rd Floor	4	16-Apr-26	21-Apr-26
CON-3030	Rough-in Sanitary & Vent Piping -3rd Floor	4	22-Apr-26	27-Apr-26
CON-3170	Rough-in Storm Piping -3rd Floor	4	28-Apr-26	01-May-26
Electrical -3rd Floor		86	27-Mar-26	29-Jul-26
CON-2640	Install Grounding Bars - 3rd Floor IDF Room	5	27-Mar-26	02-Apr-26
CON-2800	Install Data rack - 3rd Floor IDF Room	8	03-Apr-26	14-Apr-26
CON-2830	Install IPDVS Equipment Rack - 3rd Floor IDF Room	4	03-Apr-26	08-Apr-26
CON-3250	Install Voice Rack - 3rd Floor IDF Room	5	15-Apr-26	21-Apr-26
CON-3570	Install Main Sound Rack - 3rd Floor IDF Room	5	22-Apr-26	28-Apr-26
CON-5440	Install IPDVS Devices -3rd Floor	9	17-Jul-26	29-Jul-26
Fire Protection -3rd Floor		15	08-May-26	29-May-26
CON-3510	Install 4" Standpipe -3rd Floor	4	08-May-26	13-May-26
CON-3690	Rough-in Main Sprinkler Piping-3rd Floor	5	15-May-26	21-May-26
CON-3790	Rough-in Branch Sprinkler Piping -3rd Floor	5	22-May-26	29-May-26
CON-3800	Rough-in Sprinkler Heads -3rd Floor	5	22-May-26	29-May-26
Architecture -3rd Floor		37	04-Jun-26	28-Jul-26
Interior Walls -3rd Floor		8	04-Jun-26	15-Jun-26
CON-4540	Tape Gypsum Board -3rd Floor	4	04-Jun-26	09-Jun-26
CON-4850	Install Firestopping-3rd Floor	4	10-Jun-26	15-Jun-26
Ceiling -3rd Floor		5	22-Jul-26	28-Jul-26
CON-5330	Install Acoustical Ceiling Tiles-3rd Floor	5	22-Jul-26	28-Jul-26
Finishes -3rd Floor		6	29-Jun-26	07-Jul-26
CON-98857	Install Auxiliary System Components-3rd Floor	6	29-Jun-26	07-Jul-26
CON-98907	Install Sound Clock System Components-3rd Floor	6	29-Jun-26	07-Jul-26

Near Critical Path Layout

Activity ID	Activity Name	Original Duration	Start	Finish
Fourth Floor		109	09-Mar-26	11-Aug-26
Mechanical-4th Floor		102	09-Mar-26	31-Jul-26
HVAC Rough-ins-4th Floor		67	09-Mar-26	10-Jun-26
CON-2170	Rough-in Duct Work -4th Floor	5	09-Mar-26	13-Mar-26
CON-2280	Rough-in Chilled Glycol Piping-4th Floor	7	20-Mar-26	30-Mar-26
CON-4570	Install Duct Insulation -4th Floor	8	01-Jun-26	10-Jun-26
Mechanical Equipment-4th Floor		7	23-Jul-26	31-Jul-26
CON-5260	Install Cabinet Unit Heater With Fan CUH -4th Floor	4	23-Jul-26	28-Jul-26
CON-5460	Install Convector Heater CV - Mechanical Work - 4th Floor	3	29-Jul-26	31-Jul-26
Electrical-4th Floor		25	08-Jul-26	11-Aug-26
CON-98817	Install Intrusion System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-98867	Install Auxiliary System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-98917	Install Sound Clock System Components-4th Floor	6	08-Jul-26	15-Jul-26
CON-5750	Install IPDVS Devices -4th Floor	9	30-Jul-26	11-Aug-26
Fire Protection-4th Floor		16	14-May-26	05-Jun-26
CON-3650	Install 4" Standpipe -4th Floor	4	14-May-26	19-May-26
CON-3810	Rough-in Main Sprinkler Piping-4th Floor	5	22-May-26	29-May-26
CON-3990	Rough-in Branch Sprinkler Piping -4th Floor	5	01-Jun-26	05-Jun-26
CON-4000	Rough-in Sprinkler Heads -4th Floor	5	01-Jun-26	05-Jun-26
Architecture-4th Floor		26	11-Jun-26	20-Jul-26
Interior Walls-4th Floor		15	11-Jun-26	02-Jul-26
CON-4720	Tape Gypsum Board -4th Floor	4	11-Jun-26	16-Jun-26
CON-5010	Install Firestopping-4th Floor	4	16-Jun-26	22-Jun-26
CON-4800	Install Ceramic Wall Tiles at Corridor-4th Floor	7	24-Jun-26	02-Jul-26
Ceiling-4th Floor		6	22-Jun-26	29-Jun-26
CON-4820	Install Gypsum Board Ceiling-4th Floor	6	22-Jun-26	29-Jun-26
Finishes-4th Floor		15	29-Jun-26	20-Jul-26
CON-5340	Install First Coat Painting-4th Floor	5	29-Jun-26	06-Jul-26
CON-5540	Install Door Frames & Doors-4th Floor	5	07-Jul-26	13-Jul-26
CON-5690	Install Flooring Tiles-4th Floor	5	14-Jul-26	20-Jul-26
Fifth Floor		115	16-Mar-26	26-Aug-26
Mechanical -5th Floor		105	16-Mar-26	12-Aug-26
HVAC Rough-ins -5th Floor		70	16-Mar-26	23-Jun-26
CON-2300	Rough-in Duct Work-5th Floor	5	16-Mar-26	20-Mar-26
CON-2460	Rough-in Chilled Glycol Piping-5th Floor	7	31-Mar-26	08-Apr-26
CON-4710	Install Duct Insulation -5th Floor	8	11-Jun-26	23-Jun-26
Mechanical Equipment -5th Floor		11	29-Jul-26	12-Aug-26
CON-5430	Install Hot Glycol / Hot Water Cabinet Heater (CUH)-5th Floor	4	29-Jul-26	03-Aug-26
CON-5590	Install Exhaust Fan EF - Mechanical Work - 5th Floor	4	04-Aug-26	07-Aug-26
CON-5630	Install Convector Heater CV - Mechanical Work - 5th Floor	3	10-Aug-26	12-Aug-26
Electrical -5th Floor		28	16-Jul-26	24-Aug-26
CON-5740	Install Lighting Fixtures -5th Floor	6	16-Jul-26	23-Jul-26
CON-98827	Install Intrusion System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-98877	Install Auxiliary System Components -5th Floor	6	16-Jul-26	23-Jul-26
CON-5830	Install Fire alarm Sensors and Devises -5th Floor	5	29-Jul-26	04-Aug-26
CON-6010	Install IPDVS Devices -5th Floor	9	12-Aug-26	24-Aug-26

Start: 30-Sep-24
Finish: 15-Aug-27
Data Date: 30-Sep-24

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaini...
Critical ...
Milestone

NAVILLUS BUILDING THE WORLDS AROUND YOU
PROJECS ENGINEERING CONSULTING SERVICES

Prepared By : M.K

Date	**Revision**	**Checked**	**Approved**
21-Mar-25	00	A.A	

Near Critical Path Layout

Activity ID	Activity Name	Original Duration	Start	Finish
Fire Protection -5th Floor		10	01-Jun-26	12-Jun-26
CON-4010	Rough-in Main Sprinkler Piping -5th Floor	5	01-Jun-26	05-Jun-26
CON-4230	Rough-in Branch Sprinkler Piping -5th Floor	5	08-Jun-26	12-Jun-26
CON-4240	Rough-in Sprinkler Heads -5th Floor	5	08-Jun-26	12-Jun-26
Architecture -5th Floor		48	18-Jun-26	26-Aug-26
Interior Walls -5th Floor		6	18-Jun-26	26-Jun-26
CON-4970	Tape Gypsum Board -5th Floor	4	18-Jun-26	24-Jun-26
CON-5220	Install Firestopping-5th Floor	4	23-Jun-26	26-Jun-26
Finishes -5th Floor		30	16-Jul-26	26-Aug-26
CON-5680	Install Door Frames & Doors -5th Floor	5	16-Jul-26	22-Jul-26
CON-5890	Install Flooring Tiles -5th Floor	5	23-Jul-26	29-Jul-26
CON-6150	Install Furniture & Milling Work (Contractor Provided & Installed) -5th Floor	4	21-Aug-26	26-Aug-26
CON-9060	Install Furniture & Milling Work (Owner Provided & Installed) -5th Floor	4	21-Aug-26	26-Aug-26
Elevations		22	30-Mar-26	28-Apr-26
West Elevation		5	30-Mar-26	03-Apr-26
CON-2400	Install Windows -West Elevation	5	30-Mar-26	03-Apr-26
MIL-1740	Start Windows	0	30-Mar-26	
South Elevation		5	15-Apr-26	21-Apr-26
CON-2970	Field Testing of Windows (50%)	5	15-Apr-26	21-Apr-26
North Elevation		10	15-Apr-26	28-Apr-26
CON-3380	Install Windows -North Elevation	10	15-Apr-26	28-Apr-26
CON-3390	Install Storefront System-North Elevation	10	15-Apr-26	28-Apr-26
Special Rooms		90	29-Apr-26	04-Sep-26
MDF Room 127A -1st Floor		53	29-Apr-26	15-Jul-26
CON-3740	Install Ground Bus Bar - 1st Floor MDF Room	6	29-Apr-26	06-May-26
CON-4110	Install Voice Rack - 1st Floor MDF Room	6	07-May-26	14-May-26
CON-4510	Install Sound Rack - 1st Floor MDF Room	6	15-May-26	22-May-26
CON-4120	Install Project Connect Cabinet - 1st Floor MDF Room	8	15-May-26	27-May-26
CON-4520	Install Data Rack - 1st Floor MDF Room	6	26-May-26	02-Jun-26
CON-4550	Install UPS- 1st Floor MDF Room	9	03-Jun-26	15-Jun-26
CON-4130	Install BACnet Data Cabinet- 1st Floor MDF Room	9	03-Jun-26	15-Jun-26
CON-4780	Install IPDVS Equipment Rack - 1st Floor MDF Room	6	16-Jun-26	24-Jun-26
CON-4790	Install Ladder Rack Cable Tray- 1st Floor MDF Room	6	25-Jun-26	02-Jul-26
CON-4770	Install PBX - 1st Floor MDF Room	8	06-Jul-26	15-Jul-26
Gymatorium - 4th Floor		39	14-Jul-26	04-Sep-26
CON-5760	Install Wood Floating Floor System -Gymnatorium	10	14-Jul-26	27-Jul-26
CON-5810	Install Wall Pads - Gymnatorium	4	28-Jul-26	31-Jul-26
CON-5970	Install Retractable Basketball Goal Assembly -Gymnatorium	3	03-Aug-26	05-Aug-26
CON-6020	Install 8" Acoustic Block Painted-Gymnatorium	7	06-Aug-26	14-Aug-26
CON-99217	Install Bleachers -Gymnatorium	3	12-Aug-26	14-Aug-26
CON-6230	Install Gym Equipment -Gymnatorium -Gymnatorium	6	17-Aug-26	24-Aug-26
CON-6240	Install Fine Tube Radiator FTR - Gymnatorium	5	17-Aug-26	21-Aug-26
CON-6250	Install Hydraulic Vertical Wheelchair Lift -Gymnatorium	8	17-Aug-26	26-Aug-26
CON-9150	Install LED Theatrical Lighting -Gymnatorium	4	25-Aug-26	28-Aug-26
CON-6390	Install Auditorium Television Studio Dimming System -Gymnatorium	7	27-Aug-26	04-Sep-26

Near Critical Path Layout

Activity ID	Activity Name	Original Duration	Start	Finish
Site Work		41	08-Jun-26	05-Aug-26
2ND Street		7	08-Jun-26	16-Jun-26
CON-4170	Install 4" Concrete Sidewalk - 2nd Street	7	08-Jun-26	16-Jun-26
Building Perimeter		7	28-Jul-26	05-Aug-26
Playground Area & Fences		7	28-Jul-26	05-Aug-26
CON-9010	Remove Steel Plate Protection over NYPA Easement - Playground Area & Fences - Building Perimeter	1	28-Jul-26	28-Jul-26
CON-5420	Install Asphalt Pavement - Playground Area & Fences - Building Perimeter	2	04-Aug-26	05-Aug-26
Close-out		62	06-Jul-26	30-Sep-26
Testing & Commissioning		62	06-Jul-26	30-Sep-26
CLO-1120	MDF & IDF Rooms Testing & Commissioning	12	06-Jul-26	21-Jul-26
CLO-1010	HVAC Flush-Out	20	07-Jul-26	03-Aug-26
CLO-1160	Sprinkler/Domestic Booster Pumps Testing & Commissioning	14	20-Aug-26	09-Sep-26
CLO-1130	IPDVS System Testing & Commissioning	11	03-Sep-26	18-Sep-26
CLO-1170	Sprinkler/Domestic Booster Pumps Inspection	3	10-Sep-26	14-Sep-26
CLO-1180	Sprinkler/Domestic Booster Pumps Sign-offs	0		14-Sep-26
CLO-1150	FDNY Inspection	12	15-Sep-26	30-Sep-26
MIL-1650	FDNY Inspection Finish	0		30-Sep-26

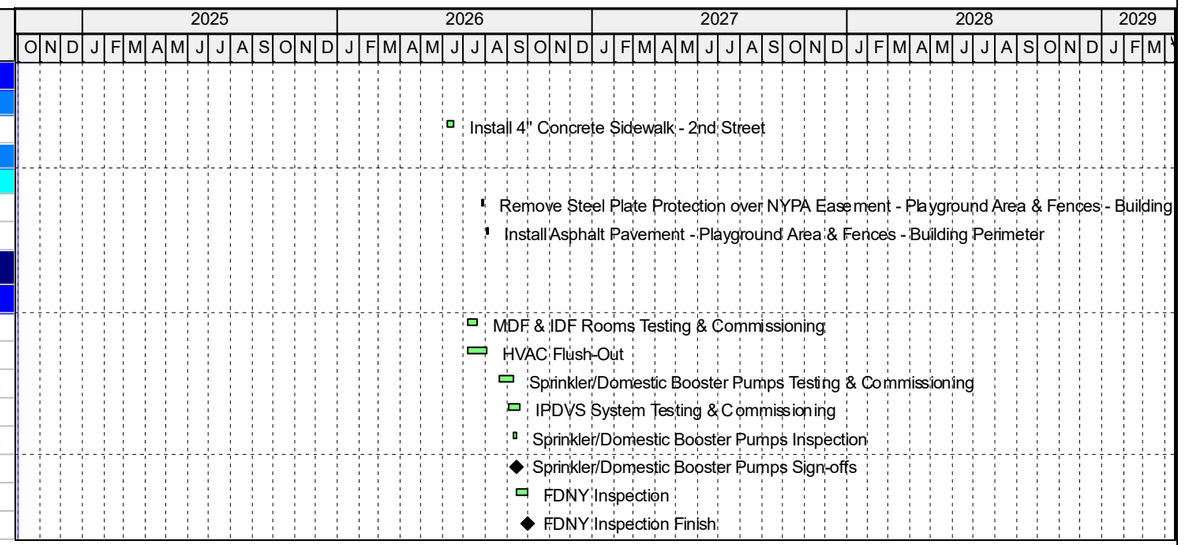

APPENDIX12
Activity Report

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
MIL-1000	NTP	0	0	30-Sep-24		0			30-Sep-24		30-Sep-24		Not Started
MIL-1030	Project Duration(From NTP till TCO)	750	750	30-Sep-24	19-Oct-26	0			30-Sep-24	19-Oct-26	30-Sep-24	19-Oct-26	Not Started
MIL-1040	Project Duration(From NTP till Substantial Completion)	930	930	30-Sep-24	17-Apr-27	0			30-Sep-24	17-Apr-27	30-Sep-24	17-Apr-27	Not Started
PRE-2590	Meeting With SCA to Review The Permit Requirements	14	14	30-Sep-24	18-Oct-24	231			30-Sep-24	18-Oct-24	03-Sep-25	22-Sep-25	Not Started
PRE-2600	Prepare & Submit Permit Waiver Requests to SCA Chief Project Officer	5	5	30-Sep-24	04-Oct-24	445			30-Sep-24	04-Oct-24	14-Jul-26	20-Jul-26	Not Started
MIL-1770	Project Duration(From NTP till Final Completion)	1050	1050	30-Sep-24	15-Aug-27	0			30-Sep-24	15-Aug-27	30-Sep-24	15-Aug-27	Not Started
MIL-2522	Site Access	365	365	30-Sep-24	29-Sep-25	0			30-Sep-24	29-Sep-25	30-Sep-24	29-Sep-25	Not Started
CON-99257	Subcontractor Buyout	10	10	30-Sep-24	11-Oct-24	6			30-Sep-24	11-Oct-24	08-Oct-24	22-Oct-24	Not Started
CON-7960	Obtain Gas Meter Layout From CON-ED	5	5	07-Oct-24	11-Oct-24	445			07-Oct-24	11-Oct-24	21-Jul-26	27-Jul-26	Not Started
MIL-2542	Complete Subcontractor 'Buyout'	0	0		11-Oct-24	240				11-Oct-24		29-Sep-25	Not Started
SUB-1000	Prepare & Submit Split Heat Pump System - SUB	60	60	15-Oct-24	10-Jan-25	393			15-Oct-24	10-Jan-25	12-May-26	06-Aug-26	Not Started
SUB-1010	Prepare & Submit Thermometers	40	40	15-Oct-24	11-Dec-24	321			15-Oct-24	11-Dec-24	29-Jan-26	26-Mar-26	Not Started
SUB-1020	Prepare & Submit Pressure Gages	40	40	15-Oct-24	11-Dec-24	293			15-Oct-24	11-Dec-24	17-Dec-25	13-Feb-26	Not Started
SUB-1030	Prepare & Submit Floor Drains	40	40	15-Oct-24	11-Dec-24	344			15-Oct-24	11-Dec-24	04-Mar-26	28-Apr-26	Not Started
SUB-1040	Prepare & Submit Hangers & Supports	40	40	15-Oct-24	11-Dec-24	275			15-Oct-24	11-Dec-24	20-Nov-25	20-Jan-26	Not Started
SUB-1050	Prepare & Submit Fire & Jockey Pumps	81	81	15-Oct-24	11-Feb-25	311			15-Oct-24	11-Feb-25	14-Jan-26	08-May-26	Not Started
SUB-1060	Prepare & Submit Interior Signage Shop Drawings	81	81	15-Oct-24	11-Feb-25	377			15-Oct-24	11-Feb-25	20-Apr-26	13-Aug-26	Not Started
SUB-1070	Prepare & Submit Ceramic Tiles Product Data	81	81	15-Oct-24	11-Feb-25	335			15-Oct-24	11-Feb-25	19-Feb-26	12-Jun-26	Not Started
SUB-1080	Prepare & Submit Door Hardware Submittal	81	81	15-Oct-24	11-Feb-25	323			15-Oct-24	11-Feb-25	02-Feb-26	27-May-26	Not Started
SUB-1090	Prepare & Submit Painting	81	81	15-Oct-24	11-Feb-25	269			15-Oct-24	11-Feb-25	12-Nov-25	11-Mar-26	Not Started
SUB-1100	Prepare & Submit Door & Frame Corners Samples	81	81	15-Oct-24	11-Feb-25	247			15-Oct-24	11-Feb-25	09-Oct-25	06-Feb-26	Not Started
SUB-1110	Prepare & Submit Roof Drains & Clean Outs	81	81	15-Oct-24	11-Feb-25	323			15-Oct-24	11-Feb-25	02-Feb-26	27-May-26	Not Started
SUB-1120	Prepare & Submit Flashing & Sheet Metal Shop Drawing	81	81	15-Oct-24	11-Feb-25	283			15-Oct-24	11-Feb-25	03-Dec-25	31-Mar-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
SUB-1130	Prepare & Submit Roofing Membrane Product Data	81	81	15-Oct-24	11-Feb-25	282			15-Oct-24	11-Feb-25	02-Dec-25	30-Mar-26	Not Started
SUB-1140	Prepare & Submit Perimeter Foundation Insulation Product Data	81	81	15-Oct-24	11-Feb-25	164			15-Oct-24	11-Feb-25	11-Jun-25	06-Oct-25	Not Started
SUB-1150	Prepare & Submit Crystalline Waterproofing Product Data	81	81	15-Oct-24	11-Feb-25	276			15-Oct-24	11-Feb-25	21-Nov-25	20-Mar-26	Not Started
SUB-1160	Prepare & Submit Suspension Assembly Shop Drawings	81	81	15-Oct-24	11-Feb-25	309			15-Oct-24	11-Feb-25	12-Jan-26	06-May-26	Not Started
SUB-1170	Prepare & Submit Certification of Material	81	81	15-Oct-24	11-Feb-25	379			15-Oct-24	11-Feb-25	22-Apr-26	17-Aug-26	Not Started
SUB-1180	Prepare & Submit Concrete Reinforcement	30	30	15-Oct-24	26-Nov-24	231			15-Oct-24	26-Nov-24	17-Sep-25	29-Oct-25	Not Started
SUB-1190	Prepare & Submit Formwork Shop Drawings	81	81	15-Oct-24	11-Feb-25	180			15-Oct-24	11-Feb-25	07-Jul-25	29-Oct-25	Not Started
SUB-1200	Prepare & Submit Planting Schedule	81	81	15-Oct-24	11-Feb-25	144			15-Oct-24	11-Feb-25	13-May-25	08-Sep-25	Not Started
SUB-1210	Prepare & Submit Site Furnishings Shop Drawings	15	15	15-Oct-24	04-Nov-24	219			15-Oct-24	04-Nov-24	29-Aug-25	19-Sep-25	Not Started
SUB-1220	Prepare & Submit Playgroung Equipment Shop Drawings	81	81	15-Oct-24	11-Feb-25	320			15-Oct-24	11-Feb-25	28-Jan-26	21-May-26	Not Started
SUB-1230	Prepare & Submit Ductile Iron Pipes	37	37	15-Oct-24	06-Dec-24	391			15-Oct-24	06-Dec-24	08-May-26	01-Jul-26	Not Started
SUB-1240	Prepare & Submit Catch Basin Shop Drawings	81	81	15-Oct-24	11-Feb-25	345			15-Oct-24	11-Feb-25	05-Mar-26	29-Jun-26	Not Started
SUB-1250	Prepare & Submit Concrete Curbs & Pavements Shop Drawing	81	81	15-Oct-24	11-Feb-25	343			15-Oct-24	11-Feb-25	03-Mar-26	25-Jun-26	Not Started
SUB-1260	Prepare & Submit Steel Curb Facing Shop Drawing	81	81	15-Oct-24	11-Feb-25	316			15-Oct-24	11-Feb-25	22-Jan-26	15-May-26	Not Started
SUB-1270	Prepare & Submit Asphaltic Concrete Paving	81	81	15-Oct-24	11-Feb-25	357			15-Oct-24	11-Feb-25	23-Mar-26	16-Jul-26	Not Started
SUB-1280	Prepare & Submit SSDS Geotextile	40	40	15-Oct-24	11-Dec-24	200			15-Oct-24	11-Dec-24	04-Aug-25	29-Sep-25	Not Started
SUB-1290	Prepare & Submit Gas Vapor Barrier Submittal & Inspection Schedule	81	81	15-Oct-24	11-Feb-25	156			15-Oct-24	11-Feb-25	30-May-25	24-Sep-25	Not Started
SUB-1300	Prepare & Submit Existing Conditions Survey	10	10	15-Oct-24	28-Oct-24	215			15-Oct-24	28-Oct-24	25-Aug-25	08-Sep-25	Not Started
SUB-1310	Prepare & Submit Training Outline & Schedule	81	81	15-Oct-24	11-Feb-25	341			15-Oct-24	11-Feb-25	27-Feb-26	23-Jun-26	Not Started
SUB-1320	Prepare & Submit Product Substitutions	82	82	15-Oct-24	12-Feb-25	384			15-Oct-24	12-Feb-25	29-Apr-26	25-Aug-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
SUB-1330	Prepare & Submit Temporary Ventilation Plan	81	81	15-Oct-24	11-Feb-25	274			15-Oct-24	11-Feb-25	19-Nov-25	18-Mar-26	Not Started
SUB-1340	Prepare & Submit Construction Indoor Air Quality Management Plan	81	81	15-Oct-24	11-Feb-25	274			15-Oct-24	11-Feb-25	19-Nov-25	18-Mar-26	Not Started
SUB-1350	Prepare & Submit Site Safety Plan	2	2	15-Oct-24	16-Oct-24	214			15-Oct-24	16-Oct-24	22-Aug-25	25-Aug-25	Not Started
SUB-1360	Prepare & Submit CWM Plan	81	81	15-Oct-24	11-Feb-25	404			15-Oct-24	11-Feb-25	28-May-26	22-Sep-26	Not Started
SUB-1370	Prepare & Submit Photo Submission - Temporary Fence	15	15	15-Oct-24	04-Nov-24	219			15-Oct-24	04-Nov-24	29-Aug-25	19-Sep-25	Not Started
SUB-1380	Prepare & Submit Heating Plan	81	81	15-Oct-24	11-Feb-25	300			15-Oct-24	11-Feb-25	29-Dec-25	23-Apr-26	Not Started
SUB-1390	Prepare & Submit Sample Classroom Materials	81	81	15-Oct-24	11-Feb-25	308			15-Oct-24	11-Feb-25	09-Jan-26	05-May-26	Not Started
SUB-1400	Prepare & Submit Sustainable Materials	10	10	15-Oct-24	28-Oct-24	215			15-Oct-24	28-Oct-24	25-Aug-25	08-Sep-25	Not Started
SUB-1410	Prepare & Submit Submittal Schedule	60	60	15-Oct-24	10-Jan-25	534			15-Oct-24	10-Jan-25	11-Dec-26	26-Mar-27	Not Started
SUB-1420	Prepare & Submit Electrical Shop Drawings	81	81	15-Oct-24	11-Feb-25	168			15-Oct-24	11-Feb-25	17-Jun-25	10-Oct-25	Not Started
SUB-1430	Prepare & Submit Plumbing Shop Drawings	81	81	15-Oct-24	11-Feb-25	215			15-Oct-24	11-Feb-25	25-Aug-25	19-Dec-25	Not Started
SUB-1440	Prepare & Submit Sprinkler System Shop Drawings	81	81	15-Oct-24	11-Feb-25	237			15-Oct-24	11-Feb-25	25-Sep-25	23-Jan-26	Not Started
SUB-1450	Prepare & Submit Concrete Shop Drawings	30	30	15-Oct-24	26-Nov-24	231			15-Oct-24	26-Nov-24	17-Sep-25	29-Oct-25	Not Started
SUB-1460	Prepare & Submit Elevator Machine	71	71	15-Oct-24	28-Jan-25	237			15-Oct-24	28-Jan-25	25-Sep-25	08-Jan-26	Not Started
SUB-1470	Prepare & Submit Gypsum Board	81	81	15-Oct-24	11-Feb-25	195			15-Oct-24	11-Feb-25	28-Jul-25	20-Nov-25	Not Started
SUB-1480	Prepare & Submit Floorings	81	81	15-Oct-24	11-Feb-25	246			15-Oct-24	11-Feb-25	08-Oct-25	05-Feb-26	Not Started
SUB-1490	Prepare & Submit Acosutical Ceiling Tiles	60	60	15-Oct-24	10-Jan-25	279			15-Oct-24	10-Jan-25	26-Nov-25	24-Feb-26	Not Started
SUB-1500	Prepare & Submit Toilet Accessories	81	81	15-Oct-24	11-Feb-25	311			15-Oct-24	11-Feb-25	14-Jan-26	08-May-26	Not Started
SUB-1510	Prepare & Submit Millwork	81	81	15-Oct-24	11-Feb-25	369			15-Oct-24	11-Feb-25	08-Apr-26	03-Aug-26	Not Started
SUB-1520	Prepare & Submit Lighting Fixtures	71	71	15-Oct-24	28-Jan-25	291			15-Oct-24	28-Jan-25	15-Dec-25	27-Mar-26	Not Started
SUB-1530	Prepare & Submit Furniture	81	81	15-Oct-24	11-Feb-25	215			15-Oct-24	11-Feb-25	25-Aug-25	19-Dec-25	Not Started
SUB-1540	Prepare & Submit Mechanical Ducts	81	81	15-Oct-24	11-Feb-25	196			15-Oct-24	11-Feb-25	29-Jul-25	21-Nov-25	Not Started
SUB-1550	Prepare & Submit Mechanical Piping	60	60	15-Oct-24	10-Jan-25	221			15-Oct-24	10-Jan-25	03-Sep-25	27-Nov-25	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
SUB-1560	Prepare & Submit Erosion Control and Sedimentation Plan	7	7	15-Oct-24	23-Oct-24	211			15-Oct-24	23-Oct-24	19-Aug-25	27-Aug-25	Not Started
SUB-1570	Prepare & Submit QCP	30	30	15-Oct-24	26-Nov-24	195			15-Oct-24	26-Nov-24	28-Jul-25	08-Sep-25	Not Started
SUB-1580	Prepare & Submit Concrete Mix Design	30	30	15-Oct-24	26-Nov-24	231			15-Oct-24	26-Nov-24	17-Sep-25	29-Oct-25	Not Started
SUB-1590	Prepare & Submit Electrical Equipment, Conduits, and Cables	20	20	15-Oct-24	12-Nov-24	229			15-Oct-24	12-Nov-24	15-Sep-25	10-Oct-25	Not Started
SUB-1600	Prepare & Submit Plumbing Fixtures	81	81	15-Oct-24	11-Feb-25	311			15-Oct-24	11-Feb-25	14-Jan-26	08-May-26	Not Started
SUB-1610	Prepare & Submit Baseline Schedule	52	52	15-Oct-24	30-Dec-24	173			15-Oct-24	30-Dec-24	25-Jun-25	08-Sep-25	Not Started
SUB-1620	Prepare & Submit Wood Doors	81	81	15-Oct-24	11-Feb-25	261			15-Oct-24	11-Feb-25	30-Oct-25	27-Feb-26	Not Started
SUB-1630	Prepare & Submit Fire Protection Shop Drawings	81	81	15-Oct-24	11-Feb-25	311			15-Oct-24	11-Feb-25	14-Jan-26	08-May-26	Not Started
SUB-1640	Prepare & Submit Fire Detectors & Alarms	81	81	15-Oct-24	11-Feb-25	286			15-Oct-24	11-Feb-25	08-Dec-25	03-Apr-26	Not Started
SUB-1650	Prepare & Submit Kitchen Equipment	71	71	15-Oct-24	28-Jan-25	266			15-Oct-24	28-Jan-25	06-Nov-25	20-Feb-26	Not Started
SUB-1660	Prepare & Submit Signs	81	81	15-Oct-24	11-Feb-25	270			15-Oct-24	11-Feb-25	13-Nov-25	12-Mar-26	Not Started
SUB-1670	Prepare & Submit Aluminum Projected Windows	71	71	15-Oct-24	28-Jan-25	175			15-Oct-24	28-Jan-25	27-Jun-25	07-Oct-25	Not Started
SUB-1680	Prepare & Submit Telecommunication System Drawings	81	81	15-Oct-24	11-Feb-25	294			15-Oct-24	11-Feb-25	18-Dec-25	15-Apr-26	Not Started
SUB-1690	Prepare & Submit Internet Protocol Digital Video Surveillance System using Digital Cameras	71	71	15-Oct-24	28-Jan-25	294			15-Oct-24	28-Jan-25	18-Dec-25	01-Apr-26	Not Started
SUB-1710	Prepare & Submit Chillers Product Data	71	71	15-Oct-24	28-Jan-25	116			15-Oct-24	28-Jan-25	03-Apr-25	15-Jul-25	Not Started
SUB-1720	Prepare & Submit Air Handling Units Product Data	71	71	15-Oct-24	28-Jan-25	160			15-Oct-24	28-Jan-25	05-Jun-25	16-Sep-25	Not Started
SUB-1730	Prepare & Submit Boilers	71	71	15-Oct-24	28-Jan-25	304			15-Oct-24	28-Jan-25	05-Jan-26	15-Apr-26	Not Started
SUB-1740	Prepare & Submit Emergency Generator System Product Data	71	71	15-Oct-24	28-Jan-25	163			15-Oct-24	28-Jan-25	10-Jun-25	19-Sep-25	Not Started
SUB-1750	Prepare & Submit Switch Gears Product Data	20	20	15-Oct-24	12-Nov-24	218			15-Oct-24	12-Nov-24	28-Aug-25	25-Sep-25	Not Started
SUB-1760	Prepare & Submit Unit Cabinet Heaters	60	60	15-Oct-24	10-Jan-25	275			15-Oct-24	10-Jan-25	20-Nov-25	18-Feb-26	Not Started
SUB-1770	Prepare & Submit Gymnasium Equipment	81	81	15-Oct-24	11-Feb-25	244			15-Oct-24	11-Feb-25	06-Oct-25	03-Feb-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
SUB-1780	Prepare & Submit Initial Underground Coordination Drawings	50	50	15-Oct-24	26-Dec-24	42			15-Oct-24	26-Dec-24	16-Dec-24	27-Feb-25	Not Started
SUB-1790	Prepare & Submit Initial 1st Floor MEP Coordination Drawings	75	75	15-Oct-24	03-Feb-25	6			15-Oct-24	03-Feb-25	23-Oct-24	11-Feb-25	Not Started
SUB-1800	Prepare & Submit Initial 2nd Floor MEP Coordination Drawings	75	75	15-Oct-24	03-Feb-25	6			15-Oct-24	03-Feb-25	23-Oct-24	11-Feb-25	Not Started
SUB-1810	Prepare & Submit Initial 3rd Floor MEP Coordination Drawings	75	75	15-Oct-24	03-Feb-25	6			15-Oct-24	03-Feb-25	23-Oct-24	11-Feb-25	Not Started
SUB-1820	Prepare & Submit Initial 4th Floor MEP Coordination Drawings	75	75	15-Oct-24	03-Feb-25	6			15-Oct-24	03-Feb-25	23-Oct-24	11-Feb-25	Not Started
SUB-1830	Prepare & Submit Initial 5th Floor MEP Coordination Drawings	75	75	15-Oct-24	03-Feb-25	6			15-Oct-24	03-Feb-25	23-Oct-24	11-Feb-25	Not Started
SUB-1840	Prepare & Submit Supplemental Comissioning Requirements	81	81	15-Oct-24	11-Feb-25	335			15-Oct-24	11-Feb-25	19-Feb-26	12-Jun-26	Not Started
SUB-1850	Prepare & Submit Record Documents	81	81	15-Oct-24	11-Feb-25	144			15-Oct-24	11-Feb-25	13-May-25	08-Sep-25	Not Started
SUB-1860	Prepare & Submit Environmental Site Assessment Reports	81	81	15-Oct-24	11-Feb-25	290			15-Oct-24	11-Feb-25	12-Dec-25	09-Apr-26	Not Started
SUB-1870	Prepare & Submit Selective Removals & Demoloition	81	81	15-Oct-24	11-Feb-25	298			15-Oct-24	11-Feb-25	24-Dec-25	21-Apr-26	Not Started
SUB-1880	Prepare & Submit Foundation Product Data	5	5	15-Oct-24	21-Oct-24	240			15-Oct-24	21-Oct-24	30-Sep-25	06-Oct-25	Not Started
SUB-1890	Prepare & Submit Trench Drains Product Data	81	81	15-Oct-24	11-Feb-25	348			15-Oct-24	11-Feb-25	10-Mar-26	02-Jul-26	Not Started
SUB-1900	Prepare & Submit Chain Link Fences & Gates Drawings	81	81	15-Oct-24	11-Feb-25	153			15-Oct-24	11-Feb-25	26-May-25	19-Sep-25	Not Started
SUB-1910	Prepare & Submit Outdoor Game Equipment	81	81	15-Oct-24	11-Feb-25	320			15-Oct-24	11-Feb-25	28-Jan-26	21-May-26	Not Started
SUB-1920	Prepare & Submit Precast Architectural Concrete	71	71	15-Oct-24	28-Jan-25	198			15-Oct-24	28-Jan-25	31-Jul-25	10-Nov-25	Not Started
SUB-1930	Prepare & Submit Unit Masonry Product Data	71	71	15-Oct-24	28-Jan-25	331			15-Oct-24	28-Jan-25	12-Feb-26	22-May-26	Not Started
SUB-1940	Prepare & Submit Cast Stone Product Data	81	81	15-Oct-24	11-Feb-25	268			15-Oct-24	11-Feb-25	10-Nov-25	10-Mar-26	Not Started
SUB-1950	Prepare & Submit Structure Steel Drawings	71	71	15-Oct-24	28-Jan-25	117			15-Oct-24	28-Jan-25	04-Apr-25	16-Jul-25	Not Started
SUB-1960	Prepare & Submit Metal Deck Product Data	81	81	15-Oct-24	11-Feb-25	153			15-Oct-24	11-Feb-25	26-May-25	19-Sep-25	Not Started
SUB-1970	Prepare & Submit Prefabricated Expansion Joint Covers	81	81	15-Oct-24	11-Feb-25	161			15-Oct-24	11-Feb-25	06-Jun-25	01-Oct-25	Not Started
SUB-1980	Prepare & Submit Self Adhering Sheet Air Barriers	81	81	15-Oct-24	11-Feb-25	283			15-Oct-24	11-Feb-25	03-Dec-25	31-Mar-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
SUB-1990	Prepare & Submit Metal Plate Wall Panels	81	81	15-Oct-24	11-Feb-25	323			15-Oct-24	11-Feb-25	02-Feb-26	27-May-26	Not Started
SUB-2000	Prepare & Submit Security Screens & Barriers	81	81	15-Oct-24	11-Feb-25	334			15-Oct-24	11-Feb-25	18-Feb-26	11-Jun-26	Not Started
SUB-2010	Prepare & Submit Wood Flooring	81	81	15-Oct-24	11-Feb-25	259			15-Oct-24	11-Feb-25	28-Oct-25	25-Feb-26	Not Started
SUB-2020	Prepare & Submit Visual Display Boards	81	81	15-Oct-24	11-Feb-25	373			15-Oct-24	11-Feb-25	14-Apr-26	07-Aug-26	Not Started
SUB-2030	Prepare & Submit Metal Lockers	81	81	15-Oct-24	11-Feb-25	373			15-Oct-24	11-Feb-25	14-Apr-26	07-Aug-26	Not Started
SUB-2040	Prepare & Submit Fire Extinguishers & Cabinets	81	81	15-Oct-24	11-Feb-25	314			15-Oct-24	11-Feb-25	20-Jan-26	13-May-26	Not Started
SUB-2050	Prepare & Submit Stationary Metal Wall Louvers	73	73	15-Oct-24	30-Jan-25	173			15-Oct-24	30-Jan-25	25-Jun-25	07-Oct-25	Not Started
SUB-2060	Prepare & Submit Library Equipment	81	81	15-Oct-24	11-Feb-25	388			15-Oct-24	11-Feb-25	05-May-26	28-Aug-26	Not Started
SUB-2070	Prepare & Submit Platform Curtains & Auditorium Window Curtains	81	81	15-Oct-24	11-Feb-25	393			15-Oct-24	11-Feb-25	12-May-26	04-Sep-26	Not Started
SUB-2080	Prepare & Submit Waste Handling Equipment	81	81	15-Oct-24	11-Feb-25	144			15-Oct-24	11-Feb-25	13-May-25	08-Sep-25	Not Started
SUB-2090	Prepare & Submit Domestic Equipment	81	81	15-Oct-24	11-Feb-25	256			15-Oct-24	11-Feb-25	23-Oct-25	20-Feb-26	Not Started
SUB-2100	Prepare & Submit Laboratory Equipment	81	81	15-Oct-24	11-Feb-25	388			15-Oct-24	11-Feb-25	05-May-26	28-Aug-26	Not Started
SUB-2110	Prepare & Submit Manufactured Wood Casework	81	81	15-Oct-24	11-Feb-25	215			15-Oct-24	11-Feb-25	25-Aug-25	19-Dec-25	Not Started
SUB-2120	Prepare & Submit Concrete Floating Floor Assembly	81	81	15-Oct-24	11-Feb-25	259			15-Oct-24	11-Feb-25	28-Oct-25	25-Feb-26	Not Started
SUB-2130	Prepare & Submit Hydraulic Vertical Wheelchair Lifts	81	81	15-Oct-24	11-Feb-25	305			15-Oct-24	11-Feb-25	06-Jan-26	30-Apr-26	Not Started
SUB-2140	Prepare & Submit Switch & Panel Boards	81	81	15-Oct-24	11-Feb-25	157			15-Oct-24	11-Feb-25	02-Jun-25	25-Sep-25	Not Started
SUB-2150	Prepare & Submit Auditorium & Television Studio Dimming System Product Data	81	81	15-Oct-24	11-Feb-25	313			15-Oct-24	11-Feb-25	16-Jan-26	12-May-26	Not Started
SUB-2160	Prepare & Submit Overcurrent Protective Devices Data	81	81	15-Oct-24	11-Feb-25	144			15-Oct-24	11-Feb-25	13-May-25	08-Sep-25	Not Started
SUB-2170	Prepare & Submit Gas Pipes	81	81	15-Oct-24	11-Feb-25	296			15-Oct-24	11-Feb-25	22-Dec-25	17-Apr-26	Not Started
SUB-2180	Prepare & Submit Water Heaters	81	81	15-Oct-24	11-Feb-25	339			15-Oct-24	11-Feb-25	25-Feb-26	18-Jun-26	Not Started
SUB-2190	Prepare & Submit Pumping Apparatus & Tanks	81	81	15-Oct-24	11-Feb-25	366			15-Oct-24	11-Feb-25	03-Apr-26	29-Jul-26	Not Started
SUB-2200	Prepare & Submit HVAC Pumps	81	81	15-Oct-24	11-Feb-25	374			15-Oct-24	11-Feb-25	15-Apr-26	10-Aug-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
SUB-2210	Prepare & Submit Emergency Generator System Accessories	71	71	15-Oct-24	28-Jan-25	359			15-Oct-24	28-Jan-25	25-Mar-26	06-Jul-26	Not Started
SUB-2220	Prepare & Submit Fuel Storage Equipment	81	81	15-Oct-24	11-Feb-25	371			15-Oct-24	11-Feb-25	10-Apr-26	05-Aug-26	Not Started
SUB-2230	Prepare & Submit Natural Gas Leak Detection Equipment	81	81	15-Oct-24	11-Feb-25	341			15-Oct-24	11-Feb-25	27-Feb-26	23-Jun-26	Not Started
SUB-2250	Prepare & Submit Temperature Control System	81	81	15-Oct-24	11-Feb-25	321			15-Oct-24	11-Feb-25	29-Jan-26	22-May-26	Not Started
SUB-2260	Prepare & Submit Air Outlets & Inlets	81	81	15-Oct-24	11-Feb-25	276			15-Oct-24	11-Feb-25	21-Nov-25	20-Mar-26	Not Started
SUB-2340	Prepare & Submit Tree Protection Plan	71	71	15-Oct-24	28-Jan-25	154			15-Oct-24	28-Jan-25	28-May-25	08-Sep-25	Not Started
SUB-2360	Prepare & Submit Adjacent Property and Structures Protection & Monitoring Plan	81	81	15-Oct-24	11-Feb-25	593			15-Oct-24	11-Feb-25	26-Mar-27	23-Jul-27	Not Started
SUB-2370	Prepare & Submit Ornamenta Metal Shop Drawings	81	81	15-Oct-24	11-Feb-25	153			15-Oct-24	11-Feb-25	26-May-25	19-Sep-25	Not Started
SUB-2920	Prepare & Submit Documentation of Proper Disposal	81	81	15-Oct-24	11-Feb-25	333			15-Oct-24	11-Feb-25	17-Feb-26	10-Jun-26	Not Started
SUB-2930	Prepare & Submit Ornamenta Metal Product Data	81	81	15-Oct-24	11-Feb-25	153			15-Oct-24	11-Feb-25	26-May-25	19-Sep-25	Not Started
SUB-2960	Prepare & Submit Coiling Doors, Grilles and Shutters Shop Drawings	81	81	15-Oct-24	11-Feb-25	364			15-Oct-24	11-Feb-25	01-Apr-26	27-Jul-26	Not Started
SUB-2970	Prepare & Submit Coiling Doors, Grilles and Shutters Product Data	81	81	15-Oct-24	11-Feb-25	364			15-Oct-24	11-Feb-25	01-Apr-26	27-Jul-26	Not Started
SUB-2980	Prepare & Submit Aluminum Framed Entrances & Storefronts Shop Drawings	81	81	15-Oct-24	11-Feb-25	165			15-Oct-24	11-Feb-25	12-Jun-25	07-Oct-25	Not Started
SUB-2990	Prepare & Submit Aluminum Framed Entrances & Storefronts Product Data	81	81	15-Oct-24	11-Feb-25	165			15-Oct-24	11-Feb-25	12-Jun-25	07-Oct-25	Not Started
SUB-3000	Prepare & Submit Thresholds, Weatherstripping and Seals Color Samples	81	81	15-Oct-24	11-Feb-25	253			15-Oct-24	11-Feb-25	20-Oct-25	17-Feb-26	Not Started
SUB-3010	Prepare & Submit Thresholds, Weatherstripping and Seals Product Data	81	81	15-Oct-24	11-Feb-25	253			15-Oct-24	11-Feb-25	20-Oct-25	17-Feb-26	Not Started
SUB-3020	Prepare & Submit Miscellaneous Glazing Samples	81	81	15-Oct-24	11-Feb-25	253			15-Oct-24	11-Feb-25	20-Oct-25	17-Feb-26	Not Started
SUB-3030	Prepare & Submit Miscellaneous Glazing Product Data	81	81	15-Oct-24	11-Feb-25	253			15-Oct-24	11-Feb-25	20-Oct-25	17-Feb-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
SUB-3040	Prepare & Submit Fire Rated Glazing Samples	81	81	15-Oct-24	11-Feb-25	253			15-Oct-24	11-Feb-25	20-Oct-25	17-Feb-26	Not Started
SUB-3050	Prepare & Submit Fire Rated Glazing Product Data	81	81	15-Oct-24	11-Feb-25	253			15-Oct-24	11-Feb-25	20-Oct-25	17-Feb-26	Not Started
SUB-3060	Prepare & Submit Graffiti Resistant Coating Product Data	81	81	15-Oct-24	11-Feb-25	250			15-Oct-24	11-Feb-25	15-Oct-25	11-Feb-26	Not Started
SUB-3070	Prepare & Submit Special Coating Samples	81	81	15-Oct-24	11-Feb-25	188			15-Oct-24	11-Feb-25	17-Jul-25	10-Nov-25	Not Started
SUB-3080	Prepare & Submit Special Coating Product Data	81	81	15-Oct-24	11-Feb-25	188			15-Oct-24	11-Feb-25	17-Jul-25	10-Nov-25	Not Started
SUB-3090	Prepare & Submit Flagpole Shop Drawing	81	81	15-Oct-24	11-Feb-25	237			15-Oct-24	11-Feb-25	25-Sep-25	23-Jan-26	Not Started
SUB-3100	Prepare & Submit Flagpole Product Data	81	81	15-Oct-24	11-Feb-25	237			15-Oct-24	11-Feb-25	25-Sep-25	23-Jan-26	Not Started
SUB-3110	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals	81	81	15-Oct-24	11-Feb-25	215			15-Oct-24	11-Feb-25	25-Aug-25	19-Dec-25	Not Started
SUB-3120	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	81	81	15-Oct-24	11-Feb-25	215			15-Oct-24	11-Feb-25	25-Aug-25	19-Dec-25	Not Started
SUB-3130	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	81	81	15-Oct-24	11-Feb-25	215			15-Oct-24	11-Feb-25	25-Aug-25	19-Dec-25	Not Started
SUB-3140	Prepare & Submit Wire Mesh Work Samples	81	81	15-Oct-24	11-Feb-25	253			15-Oct-24	11-Feb-25	20-Oct-25	17-Feb-26	Not Started
SUB-3150	Prepare & Submit Wire Mesh Work Shop drawings	81	81	15-Oct-24	11-Feb-25	253			15-Oct-24	11-Feb-25	20-Oct-25	17-Feb-26	Not Started
SUB-3160	Prepare & Submit Metal Storage Shelving Samples	81	81	15-Oct-24	11-Feb-25	215			15-Oct-24	11-Feb-25	25-Aug-25	19-Dec-25	Not Started
SUB-3170	Prepare & Submit Metal Storage Shelving Shop drawings	81	81	15-Oct-24	11-Feb-25	215			15-Oct-24	11-Feb-25	25-Aug-25	19-Dec-25	Not Started
SUB-3180	Prepare & Submit Mirrors Shop Drawing	81	81	15-Oct-24	11-Feb-25	305			15-Oct-24	11-Feb-25	06-Jan-26	30-Apr-26	Not Started
SUB-3190	Prepare & Submit Mirrors Product Data	81	81	15-Oct-24	11-Feb-25	305			15-Oct-24	11-Feb-25	06-Jan-26	30-Apr-26	Not Started
SUB-3200	Prepare & Submit Mirrors Mastic Compatibility Test Reports & Certifications	81	81	15-Oct-24	11-Feb-25	305			15-Oct-24	11-Feb-25	06-Jan-26	30-Apr-26	Not Started
SUB-3210	Prepare & Submit Grab Bars Shop Drawing	81	81	15-Oct-24	11-Feb-25	311			15-Oct-24	11-Feb-25	14-Jan-26	08-May-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
SUB-3220	Prepare & Submit Grab Bars Product Data	81	81	15-Oct-24	11-Feb-25	311			15-Oct-24	11-Feb-25	14-Jan-26	08-May-26	Not Started
SUB-3230	Prepare & Submit Shop Equipment Shop Drawing	81	81	15-Oct-24	11-Feb-25	144			15-Oct-24	11-Feb-25	13-May-25	08-Sep-25	Not Started
SUB-3240	Prepare & Submit Shop Equipment Product Data	81	81	15-Oct-24	11-Feb-25	144			15-Oct-24	11-Feb-25	13-May-25	08-Sep-25	Not Started
SUB-3250	Prepare & Submit Bleachers Shop Drawing	81	81	15-Oct-24	11-Feb-25	276			15-Oct-24	11-Feb-25	21-Nov-25	20-Mar-26	Not Started
SUB-3260	Prepare & Submit Bleachers Product Data	81	81	15-Oct-24	11-Feb-25	276			15-Oct-24	11-Feb-25	21-Nov-25	20-Mar-26	Not Started
SUB-3270	Prepare & Submit Bleachers Manufacturer's Warranty	81	81	15-Oct-24	11-Feb-25	276			15-Oct-24	11-Feb-25	21-Nov-25	20-Mar-26	Not Started
SUB-3280	Prepare & Submit Valves Shop Drawing	81	81	15-Oct-24	11-Feb-25	233			15-Oct-24	11-Feb-25	19-Sep-25	16-Jan-26	Not Started
SUB-3290	Prepare & Submit Valves Product Data	81	81	15-Oct-24	11-Feb-25	233			15-Oct-24	11-Feb-25	19-Sep-25	16-Jan-26	Not Started
SUB-3300	Prepare & Submit Certification of Tests	81	81	15-Oct-24	11-Feb-25	144			15-Oct-24	11-Feb-25	13-May-25	08-Sep-25	Not Started
SUB-3310	Prepare & Submit Domestic Water Sterilization Plan	81	81	15-Oct-24	11-Feb-25	144			15-Oct-24	11-Feb-25	13-May-25	08-Sep-25	Not Started
SUB-3320	Prepare & Submit Tags, Charts & Identifications Shop Drawing	81	81	15-Oct-24	11-Feb-25	144			15-Oct-24	11-Feb-25	13-May-25	08-Sep-25	Not Started
SUB-3330	Prepare & Submit Tags, Charts & Identifications Product Data	81	81	15-Oct-24	11-Feb-25	144			15-Oct-24	11-Feb-25	13-May-25	08-Sep-25	Not Started
SUB-3340	Prepare & Submit Micselianeous Shop Drawing	81	81	15-Oct-24	11-Feb-25	144			15-Oct-24	11-Feb-25	13-May-25	08-Sep-25	Not Started
SUB-3350	Prepare & Submit Valves (HVAC) Shop Drawing	81	81	15-Oct-24	11-Feb-25	196			15-Oct-24	11-Feb-25	29-Jul-25	21-Nov-25	Not Started
SUB-3360	Prepare & Submit Valves (HVAC) Product Data	81	81	15-Oct-24	11-Feb-25	196			15-Oct-24	11-Feb-25	29-Jul-25	21-Nov-25	Not Started
SUB-3370	Prepare & Submit Piping Insulation Schedule Listing Items	81	81	15-Oct-24	11-Feb-25	200			15-Oct-24	11-Feb-25	04-Aug-25	27-Nov-25	Not Started
SUB-3380	Prepare & Submit Schedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	81	81	15-Oct-24	11-Feb-25	150			15-Oct-24	11-Feb-25	21-May-25	16-Sep-25	Not Started
SUB-3390	Prepare & Submit Schedules Showing Manfacturers's Product Number Duct Work Insulation	81	81	15-Oct-24	11-Feb-25	298			15-Oct-24	11-Feb-25	24-Dec-25	21-Apr-26	Not Started
SUB-3400	Prepare & Submit Hydronic Specialities Shop Drawing	81	81	15-Oct-24	11-Feb-25	150			15-Oct-24	11-Feb-25	21-May-25	16-Sep-25	Not Started
SUB-3410	Prepare & Submit Hydronic	81	81	15-Oct-24	11-Feb-25	150			15-Oct-24	11-Feb-25	21-May-25	16-Sep-25	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
	Specialities Product Data												
SUB-3420	Prepare & Submit Water Treatment Firm	81	81	15-Oct-24	11-Feb-25	150			15-Oct-24	11-Feb-25	21-May-25	16-Sep-25	Not Started
SUB-3430	Prepare & Submit Chemical Products Product Data	81	81	15-Oct-24	11-Feb-25	150			15-Oct-24	11-Feb-25	21-May-25	16-Sep-25	Not Started
SUB-3440	Prepare & Submit Detail of Gag for the Safety Relief Valves	71	71	15-Oct-24	28-Jan-25	304			15-Oct-24	28-Jan-25	05-Jan-26	15-Apr-26	Not Started
SUB-3450	Prepare & Submit Boiler Accessories Maintenance Data	71	71	15-Oct-24	28-Jan-25	304			15-Oct-24	28-Jan-25	05-Jan-26	15-Apr-26	Not Started
SUB-3460	Prepare & Submit Breeching Chimney Connectors and Chimneys Shop Drawing	81	81	15-Oct-24	11-Feb-25	351			15-Oct-24	11-Feb-25	13-Mar-26	08-Jul-26	Not Started
SUB-3470	Prepare & Submit Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	81	81	15-Oct-24	11-Feb-25	351			15-Oct-24	11-Feb-25	13-Mar-26	08-Jul-26	Not Started
SUB-3480	Prepare & Submit Plate Heat Exchanger Maintenance Data	81	81	15-Oct-24	11-Feb-25	294			15-Oct-24	11-Feb-25	18-Dec-25	15-Apr-26	Not Started
SUB-3490	Prepare & Submit Plate Heat Exchanger Product Data	81	81	15-Oct-24	11-Feb-25	294			15-Oct-24	11-Feb-25	18-Dec-25	15-Apr-26	Not Started
SUB-3500	Prepare & Submit Coils Maintenance Data	81	81	15-Oct-24	11-Feb-25	369			15-Oct-24	11-Feb-25	08-Apr-26	03-Aug-26	Not Started
SUB-3510	Prepare & Submit Coils Certifications	81	81	15-Oct-24	11-Feb-25	369			15-Oct-24	11-Feb-25	08-Apr-26	03-Aug-26	Not Started
SUB-3520	Prepare & Submit Convectors Shop Drawing	81	81	15-Oct-24	11-Feb-25	344			15-Oct-24	11-Feb-25	04-Mar-26	26-Jun-26	Not Started
SUB-3530	Prepare & Submit Convectors Product Data	81	81	15-Oct-24	11-Feb-25	344			15-Oct-24	11-Feb-25	04-Mar-26	26-Jun-26	Not Started
SUB-3540	Prepare & Submit Fan Coils Units Maintenance Data & Materials	81	81	15-Oct-24	11-Feb-25	342			15-Oct-24	11-Feb-25	02-Mar-26	24-Jun-26	Not Started
SUB-3550	Prepare & Submit Fan Coils Units Shop Drawings	81	81	15-Oct-24	11-Feb-25	342			15-Oct-24	11-Feb-25	02-Mar-26	24-Jun-26	Not Started
SUB-3560	Prepare & Submit Door Air Curtains Shop Drawing	81	81	15-Oct-24	11-Feb-25	372			15-Oct-24	11-Feb-25	13-Apr-26	06-Aug-26	Not Started
SUB-3570	Prepare & Submit Door Air Curtains Product Data	81	81	15-Oct-24	11-Feb-25	372			15-Oct-24	11-Feb-25	13-Apr-26	06-Aug-26	Not Started
SUB-3580	Prepare & Submit Centrifugal Fans Shop Drawing	81	81	15-Oct-24	11-Feb-25	338			15-Oct-24	11-Feb-25	24-Feb-26	17-Jun-26	Not Started
SUB-3590	Prepare & Submit Centrifugal Fans Product Data	81	81	15-Oct-24	11-Feb-25	338			15-Oct-24	11-Feb-25	24-Feb-26	17-Jun-26	Not Started
SUB-3600	Prepare & Submit Centrifugal Fans Maintenance Data & Materials	81	81	15-Oct-24	11-Feb-25	338			15-Oct-24	11-Feb-25	24-Feb-26	17-Jun-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
SUB-3610	Prepare & Submit Air Filters Shop Drawing	81	81	15-Oct-24	11-Feb-25	150			15-Oct-24	11-Feb-25	21-May-25	16-Sep-25	Not Started
SUB-3620	Prepare & Submit Air Filters Product Data	81	81	15-Oct-24	11-Feb-25	150			15-Oct-24	11-Feb-25	21-May-25	16-Sep-25	Not Started
SUB-3630	Prepare & Submit Air Filters Maintenance Data & Materials	81	81	15-Oct-24	11-Feb-25	150			15-Oct-24	11-Feb-25	21-May-25	16-Sep-25	Not Started
SUB-3640	Prepare & Submit Duct Accessories Shop Drawing	81	81	15-Oct-24	11-Feb-25	196			15-Oct-24	11-Feb-25	29-Jul-25	21-Nov-25	Not Started
SUB-3650	Prepare & Submit Damper Assemblies Shop Drawing	81	81	15-Oct-24	11-Feb-25	351			15-Oct-24	11-Feb-25	13-Mar-26	08-Jul-26	Not Started
SUB-3660	Prepare & Submit Damper Assemblies Product Data	81	81	15-Oct-24	11-Feb-25	351			15-Oct-24	11-Feb-25	13-Mar-26	08-Jul-26	Not Started
SUB-3670	Prepare & Submit Damper Assemblies Maintenance Data & Materials	81	81	15-Oct-24	11-Feb-25	351			15-Oct-24	11-Feb-25	13-Mar-26	08-Jul-26	Not Started
SUB-3680	Prepare & Submit Variable Air Terminals Shop Drawing	81	81	15-Oct-24	11-Feb-25	188			15-Oct-24	11-Feb-25	17-Jul-25	10-Nov-25	Not Started
SUB-3690	Prepare & Submit Variable Air Terminals Product Data	81	81	15-Oct-24	11-Feb-25	188			15-Oct-24	11-Feb-25	17-Jul-25	10-Nov-25	Not Started
SUB-3700	Prepare & Submit Variable Air Terminals Maintenance Data & Materials	81	81	15-Oct-24	11-Feb-25	188			15-Oct-24	11-Feb-25	17-Jul-25	10-Nov-25	Not Started
SUB-3710	Prepare & Submit AHU for Public Assemblies Sapces Shop Drawing	81	81	15-Oct-24	11-Feb-25	106			15-Oct-24	11-Feb-25	20-Mar-25	15-Jul-25	Not Started
SUB-3720	Prepare & Submit AHU for Public Assemblies Sapces Product Data	81	81	15-Oct-24	11-Feb-25	106			15-Oct-24	11-Feb-25	20-Mar-25	15-Jul-25	Not Started
SUB-3730	Prepare & Submit AHU for Public Assemblies Sapces Maintenance Data & Materials	81	81	15-Oct-24	11-Feb-25	150			15-Oct-24	11-Feb-25	21-May-25	16-Sep-25	Not Started
SUB-3740	Prepare & Submit Control Systems Shop Drawing	81	81	15-Oct-24	11-Feb-25	150			15-Oct-24	11-Feb-25	21-May-25	16-Sep-25	Not Started
SUB-3750	Prepare & Submit Truck Network Cable Schematic Diagram	81	81	15-Oct-24	11-Feb-25	150			15-Oct-24	11-Feb-25	21-May-25	16-Sep-25	Not Started
SUB-3760	Prepare & Submit Lighting Control Devices Shop Drawing	71	71	15-Oct-24	28-Jan-25	294			15-Oct-24	28-Jan-25	18-Dec-25	01-Apr-26	Not Started
SUB-3770	Prepare & Submit Lighting Control Devices Product Data	71	71	15-Oct-24	28-Jan-25	294			15-Oct-24	28-Jan-25	18-Dec-25	01-Apr-26	Not Started
SUB-3780	Prepare & Submit Lighting Control Devices Warranty	71	71	15-Oct-24	28-Jan-25	294			15-Oct-24	28-Jan-25	18-Dec-25	01-Apr-26	Not Started
SUB-3790	Prepare & Submit Surge Protective Devices Shop Drawing	81	81	15-Oct-24	11-Feb-25	332			15-Oct-24	11-Feb-25	13-Feb-26	09-Jun-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
SUB-3800	Prepare & Submit Surge Protective Devices Product Data	81	81	15-Oct-24	11-Feb-25	332			15-Oct-24	11-Feb-25	13-Feb-26	09-Jun-26	Not Started
SUB-3810	Prepare & Submit Surge Protective Devices Warranty	81	81	15-Oct-24	11-Feb-25	332			15-Oct-24	11-Feb-25	13-Feb-26	09-Jun-26	Not Started
SUB-3820	Prepare & Submit Service Entrance Equipment Shop Drawing	81	81	15-Oct-24	11-Feb-25	333			15-Oct-24	11-Feb-25	17-Feb-26	10-Jun-26	Not Started
SUB-3830	Prepare & Submit Service Entrance Equipment Product Data	81	81	15-Oct-24	11-Feb-25	333			15-Oct-24	11-Feb-25	17-Feb-26	10-Jun-26	Not Started
SUB-3840	Prepare & Submit Service Entrance Equipment Warranty	81	81	15-Oct-24	11-Feb-25	333			15-Oct-24	11-Feb-25	17-Feb-26	10-Jun-26	Not Started
SUB-3850	Prepare & Submit Enclosed Switches Product Data	81	81	15-Oct-24	11-Feb-25	321			15-Oct-24	11-Feb-25	29-Jan-26	22-May-26	Not Started
SUB-3860	Prepare & Submit Enclosed Switches Test Reports	81	81	15-Oct-24	11-Feb-25	321			15-Oct-24	11-Feb-25	29-Jan-26	22-May-26	Not Started
SUB-3870	Prepare & Submit Motors, Motor Control Centers and Starters Shop Drawing	81	81	15-Oct-24	11-Feb-25	351			15-Oct-24	11-Feb-25	13-Mar-26	08-Jul-26	Not Started
SUB-3880	Prepare & Submit Motors, Motor Control Centers and Starters Product Data	81	81	15-Oct-24	11-Feb-25	351			15-Oct-24	11-Feb-25	13-Mar-26	08-Jul-26	Not Started
SUB-3890	Prepare & Submit Motors, Motor Control Centers and Starters Field Test Reports	81	81	15-Oct-24	11-Feb-25	351			15-Oct-24	11-Feb-25	13-Mar-26	08-Jul-26	Not Started
SUB-3900	Prepare & Submit Lightning Protection Shop Drawing	81	81	15-Oct-24	11-Feb-25	284			15-Oct-24	11-Feb-25	04-Dec-25	01-Apr-26	Not Started
SUB-3920	Prepare & Submit Lightning Protection Test Reports	81	81	15-Oct-24	11-Feb-25	284			15-Oct-24	11-Feb-25	04-Dec-25	01-Apr-26	Not Started
SUB-3930	Prepare & Submit Fiber Optic Cabling system Shop Drawing	81	81	15-Oct-24	11-Feb-25	259			15-Oct-24	11-Feb-25	28-Oct-25	25-Feb-26	Not Started
SUB-3940	Prepare & Submit Fiber Optic Cabling system Product Data	81	81	15-Oct-24	11-Feb-25	259			15-Oct-24	11-Feb-25	28-Oct-25	25-Feb-26	Not Started
SUB-3950	Prepare & Submit Fiber Optic Cabling system Samples	81	81	15-Oct-24	11-Feb-25	259			15-Oct-24	11-Feb-25	28-Oct-25	25-Feb-26	Not Started
SUB-3960	Prepare & Submit Sound, Intercome & Security System Shop Drawing	81	81	15-Oct-24	11-Feb-25	326			15-Oct-24	11-Feb-25	05-Feb-26	01-Jun-26	Not Started
SUB-3970	Prepare & Submit Sound, Intercome & Security System Programming Code and Password for the System	81	81	15-Oct-24	11-Feb-25	326			15-Oct-24	11-Feb-25	05-Feb-26	01-Jun-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
SUB-3980	Prepare & Submit Sound, Intercome & Security System Warranty	81	81	15-Oct-24	11-Feb-25	326			15-Oct-24	11-Feb-25	05-Feb-26	01-Jun-26	Not Started
SUB-3990	Prepare & Submit Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	81	81	15-Oct-24	11-Feb-25	369			15-Oct-24	11-Feb-25	08-Apr-26	03-Aug-26	Not Started
SUB-4000	Prepare & Submit Projection and Interactive Whiteboard Systems Wiring diagram	81	81	15-Oct-24	11-Feb-25	369			15-Oct-24	11-Feb-25	08-Apr-26	03-Aug-26	Not Started
SUB-4010	Prepare & Submit Self Corrective Clock System Shop Drawing	81	81	15-Oct-24	11-Feb-25	326			15-Oct-24	11-Feb-25	05-Feb-26	01-Jun-26	Not Started
SUB-4020	Prepare & Submit Self Corrective Clock System Product Data	81	81	15-Oct-24	11-Feb-25	326			15-Oct-24	11-Feb-25	05-Feb-26	01-Jun-26	Not Started
SUB-4030	Prepare & Submit Self Corrective Clock System Field Test Reports	81	81	15-Oct-24	11-Feb-25	326			15-Oct-24	11-Feb-25	05-Feb-26	01-Jun-26	Not Started
SUB-4040	Prepare & Submit Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	81	81	15-Oct-24	11-Feb-25	364			15-Oct-24	11-Feb-25	01-Apr-26	27-Jul-26	Not Started
SUB-4060	Prepare & Submit Steel Stairs Shop Drawings	81	81	15-Oct-24	11-Feb-25	219			15-Oct-24	11-Feb-25	29-Aug-25	26-Dec-25	Not Started
SUB-4070	Prepare & Submit Steel Stairs Product Data	81	81	15-Oct-24	11-Feb-25	219			15-Oct-24	11-Feb-25	29-Aug-25	26-Dec-25	Not Started
SUB-4080	Prepare & Submit Green School Submittal	81	81	15-Oct-24	11-Feb-25	144			15-Oct-24	11-Feb-25	13-May-25	08-Sep-25	Not Started
APP-1000	Review & Approve Site Safety Plan	21	21	17-Oct-24	06-Nov-24	313			17-Oct-24	06-Nov-24	26-Aug-25	15-Sep-25	Not Started
APP-1010	Review & Approve Foundation Product Data	21	21	22-Oct-24	11-Nov-24	350			22-Oct-24	11-Nov-24	07-Oct-25	27-Oct-25	Not Started
APP-1020	Review & Approve Erosion Control and Sedimentation Plan	21	21	24-Oct-24	13-Nov-24	308			24-Oct-24	13-Nov-24	28-Aug-25	17-Sep-25	Not Started
APP-1030	Review & Approve Existing Conditions Survey	21	21	29-Oct-24	18-Nov-24	315			29-Oct-24	18-Nov-24	09-Sep-25	29-Sep-25	Not Started
APP-1040	Review & Approve Sustainable Materials	21	21	29-Oct-24	18-Nov-24	315			29-Oct-24	18-Nov-24	09-Sep-25	29-Sep-25	Not Started
MIL-1660	Start Security Guard Services (30 Days From NTP)	0	0	30-Oct-24		335			30-Oct-24		30-Sep-25		Not Started
APP-1050	Review & Approve Site Furnishings Shop Drawings	21	21	05-Nov-24	25-Nov-24	321			05-Nov-24	25-Nov-24	22-Sep-25	12-Oct-25	Not Started
APP-1060	Review & Approve Photo Submission - Temporary Fence	21	21	05-Nov-24	25-Nov-24	321			05-Nov-24	25-Nov-24	22-Sep-25	12-Oct-25	Not Started
CON-8010	Coordination With CON-ED For Temporary Electrical Power	10	10	07-Nov-24	21-Nov-24	371			07-Nov-24	21-Nov-24	05-May-26	18-May-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
APP-1080	Review & Approve Electrical Equipment, Conduits, and Cables	21	21	13-Nov-24	03-Dec-24	332			13-Nov-24	03-Dec-24	11-Oct-25	31-Oct-25	Not Started
APP-1090	Review & Approve Switch Gears Product Data	21	21	13-Nov-24	03-Dec-24	317			13-Nov-24	03-Dec-24	26-Sep-25	16-Oct-25	Not Started
CON-8020	Scheduling With CON-ED For Temporary Electrical Power	7	7	22-Nov-24	03-Dec-24	371			22-Nov-24	03-Dec-24	19-May-26	28-May-26	Not Started
APP-1100	Review & Approve Concrete Reinforcement	21	21	27-Nov-24	17-Dec-24	337			27-Nov-24	17-Dec-24	30-Oct-25	19-Nov-25	Not Started
APP-1110	Review & Approve Concrete Shop Drawings	21	21	27-Nov-24	17-Dec-24	337			27-Nov-24	17-Dec-24	30-Oct-25	19-Nov-25	Not Started
APP-1130	Review & Approve QCP	21	21	27-Nov-24	17-Dec-24	286			27-Nov-24	17-Dec-24	09-Sep-25	29-Sep-25	Not Started
APP-1140	Review & Approve Concrete Mix Design	21	21	27-Nov-24	17-Dec-24	337			27-Nov-24	17-Dec-24	30-Oct-25	19-Nov-25	Not Started
APP-1150	Review & Approve Ductile Iron Pipes	21	21	07-Dec-24	27-Dec-24	572			07-Dec-24	27-Dec-24	02-Jul-26	22-Jul-26	Not Started
APP-1160	Review & Approve Thermometers	21	21	12-Dec-24	01-Jan-25	470			12-Dec-24	01-Jan-25	27-Mar-26	16-Apr-26	Not Started
APP-1170	Review & Approve Pressure Gages	21	21	12-Dec-24	01-Jan-25	432			12-Dec-24	01-Jan-25	17-Feb-26	09-Mar-26	Not Started
APP-1180	Review & Approve Floor Drains	21	21	12-Dec-24	01-Jan-25	503			12-Dec-24	01-Jan-25	29-Apr-26	19-May-26	Not Started
APP-1190	Review & Approve Hangers & Supports	21	21	12-Dec-24	01-Jan-25	405			12-Dec-24	01-Jan-25	21-Jan-26	10-Feb-26	Not Started
APP-1200	Review & Approve SSDS Geotextile	21	21	12-Dec-24	01-Jan-25	292			12-Dec-24	01-Jan-25	30-Sep-25	20-Oct-25	Not Started
APP-1230	Review & Approve Initial Underground Coordination Drawings	21	21	27-Dec-24	16-Jan-25	63			27-Dec-24	16-Jan-25	28-Feb-25	20-Mar-25	Not Started
APP-1240	Review & Approve Baseline Schedule	21	21	31-Dec-24	20-Jan-25	252			31-Dec-24	20-Jan-25	09-Sep-25	29-Sep-25	Not Started
APP-1250	Review & Approve Split Heat Pump System - SUB	21	21	11-Jan-25	31-Jan-25	573			11-Jan-25	31-Jan-25	07-Aug-26	27-Aug-26	Not Started
APP-1260	Review & Approve Submittal Schedule	21	21	11-Jan-25	31-Jan-25	807			11-Jan-25	31-Jan-25	29-Mar-27	18-Apr-27	Not Started
APP-1270	Review & Approve Acosutical Ceiling Tiles	21	21	11-Jan-25	31-Jan-25	410			11-Jan-25	31-Jan-25	25-Feb-26	17-Mar-26	Not Started
APP-1280	Review & Approve Mechanical Piping	21	21	11-Jan-25	31-Jan-25	324			11-Jan-25	31-Jan-25	01-Dec-25	21-Dec-25	Not Started
APP-1290	Review & Approve Unit Cabinet Heaters	21	21	11-Jan-25	31-Jan-25	404			11-Jan-25	31-Jan-25	19-Feb-26	11-Mar-26	Not Started
SUB-2270	Prepare & Submit Final Underground Coordination Drawings	37	37	17-Jan-25	11-Mar-25	44			17-Jan-25	11-Mar-25	21-Mar-25	12-May-25	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
APP-1210	Review & Approve Elevator Machine	21	21	29-Jan-25	18-Feb-25	345			29-Jan-25	18-Feb-25	09-Jan-26	29-Jan-26	Not Started
APP-1120	Review & Approve Lighting Fixtures	21	21	29-Jan-25	18-Feb-25	424			29-Jan-25	18-Feb-25	29-Mar-26	18-Apr-26	Not Started
APP-1780	Review & Approve Kitchen Equipment	21	21	29-Jan-25	18-Feb-25	389			29-Jan-25	18-Feb-25	22-Feb-26	14-Mar-26	Not Started
APP-1310	Review & Approve Aluminum Projected Windows	21	21	29-Jan-25	18-Feb-25	252			29-Jan-25	18-Feb-25	08-Oct-25	28-Oct-25	Not Started
APP-1220	Review & Approve Internet Protocol Digital Video Surveillance System using Digital Cameras	35	35	29-Jan-25	04-Mar-25	428			29-Jan-25	04-Mar-25	02-Apr-26	06-May-26	Not Started
APP-1820	Review & Approve Chillers Product Data	21	21	29-Jan-25	18-Feb-25	168			29-Jan-25	18-Feb-25	16-Jul-25	05-Aug-25	Not Started
APP-1300	Review & Approve Air Handling Units Product Data	21	21	29-Jan-25	18-Feb-25	231			29-Jan-25	18-Feb-25	17-Sep-25	07-Oct-25	Not Started
APP-1830	Review & Approve Boilers	21	21	29-Jan-25	18-Feb-25	442			29-Jan-25	18-Feb-25	16-Apr-26	06-May-26	Not Started
APP-1070	Review & Approve Emergency Generator System Product Data	21	21	29-Jan-25	18-Feb-25	234			29-Jan-25	18-Feb-25	20-Sep-25	10-Oct-25	Not Started
APP-1920	Review & Approve Precast Architectural Concrete	21	21	29-Jan-25	18-Feb-25	287			29-Jan-25	18-Feb-25	12-Nov-25	02-Dec-25	Not Started
APP-1930	Review & Approve Unit Masonry Product Data	21	21	29-Jan-25	18-Feb-25	481			29-Jan-25	18-Feb-25	25-May-26	14-Jun-26	Not Started
APP-1950	Review & Approve Structure Steel Drawings	21	21	29-Jan-25	18-Feb-25	169			29-Jan-25	18-Feb-25	17-Jul-25	06-Aug-25	Not Started
APP-2200	Review & Approve Emergency Generator System Accessories	21	21	29-Jan-25	18-Feb-25	524			29-Jan-25	18-Feb-25	07-Jul-26	27-Jul-26	Not Started
APP-2340	Review & Approve Tree Protection Plan	21	21	29-Jan-25	18-Feb-25	223			29-Jan-25	18-Feb-25	09-Sep-25	29-Sep-25	Not Started
APP-3440	Review & Approve Detail of Gag for the Safety Relief Valves	21	21	29-Jan-25	18-Feb-25	442			29-Jan-25	18-Feb-25	16-Apr-26	06-May-26	Not Started
APP-3450	Review & Approve Boiler Accessories Maintenance Data	21	21	29-Jan-25	18-Feb-25	442			29-Jan-25	18-Feb-25	16-Apr-26	06-May-26	Not Started
APP-3760	Review & Approve Lighting Control Devices Shop Drawing	21	21	29-Jan-25	18-Feb-25	428			29-Jan-25	18-Feb-25	02-Apr-26	22-Apr-26	Not Started
APP-3770	Review & Approve Lighting Control Devices Product Data	21	21	29-Jan-25	18-Feb-25	428			29-Jan-25	18-Feb-25	02-Apr-26	22-Apr-26	Not Started
APP-3780	Review & Approve Lighting Control Devices Warranty	21	21	29-Jan-25	18-Feb-25	428			29-Jan-25	18-Feb-25	02-Apr-26	22-Apr-26	Not Started
APP-1320	Review & Approve Stationary Metal Wall Louvers	21	21	31-Jan-25	20-Feb-25	250			31-Jan-25	20-Feb-25	08-Oct-25	28-Oct-25	Not Started
APP-1330	Review & Approve Initial 1st Floor Coordination Drawings	21	21	04-Feb-25	24-Feb-25	8			04-Feb-25	24-Feb-25	12-Feb-25	04-Mar-25	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
APP-1340	Review & Approve Initial 2nd Floor Coordination Drawings	21	21	04-Feb-25	24-Feb-25	8			04-Feb-25	24-Feb-25	12-Feb-25	04-Mar-25	Not Started
APP-1350	Review & Approve Initial 3rd Floor Coordination Drawings	21	21	04-Feb-25	24-Feb-25	8			04-Feb-25	24-Feb-25	12-Feb-25	04-Mar-25	Not Started
APP-1360	Review & Approve Initial 4th Floor Coordination Drawings	21	21	04-Feb-25	24-Feb-25	8			04-Feb-25	24-Feb-25	12-Feb-25	04-Mar-25	Not Started
APP-1370	Review & Approve Initial 5th Floor Coordination Drawings	21	21	04-Feb-25	24-Feb-25	8			04-Feb-25	24-Feb-25	12-Feb-25	04-Mar-25	Not Started
APP-1380	Review & Approve Fire & Jockey Pumps	21	21	12-Feb-25	04-Mar-25	453			12-Feb-25	04-Mar-25	11-May-26	31-May-26	Not Started
APP-1390	Review & Approve Interior Signage Shop Drawings	21	21	12-Feb-25	04-Mar-25	548			12-Feb-25	04-Mar-25	14-Aug-26	03-Sep-26	Not Started
APP-1400	Review & Approve Ceramic Tiles Product Data	21	21	12-Feb-25	04-Mar-25	488			12-Feb-25	04-Mar-25	15-Jun-26	05-Jul-26	Not Started
APP-1410	Review & Approve Door Hardware Submittal	21	21	12-Feb-25	04-Mar-25	470			12-Feb-25	04-Mar-25	28-May-26	17-Jun-26	Not Started
APP-1420	Review & Approve Painting	21	21	12-Feb-25	04-Mar-25	393			12-Feb-25	04-Mar-25	12-Mar-26	01-Apr-26	Not Started
APP-1430	Review & Approve Door & Frame Corners Samples	21	21	12-Feb-25	04-Mar-25	362			12-Feb-25	04-Mar-25	09-Feb-26	01-Mar-26	Not Started
APP-1440	Review & Approve Roof Drains & Clean Outs	21	21	12-Feb-25	04-Mar-25	470			12-Feb-25	04-Mar-25	28-May-26	17-Jun-26	Not Started
APP-1450	Review & Approve Flashing & Sheet Metal Shop Drawing	21	21	12-Feb-25	04-Mar-25	413			12-Feb-25	04-Mar-25	01-Apr-26	21-Apr-26	Not Started
APP-1460	Review & Approve Roofing Membrane Product Data	21	21	12-Feb-25	04-Mar-25	412			12-Feb-25	04-Mar-25	31-Mar-26	20-Apr-26	Not Started
APP-1470	Review & Approve Perimeter Foundation Insulation Product Data	21	21	12-Feb-25	04-Mar-25	237			12-Feb-25	04-Mar-25	07-Oct-25	27-Oct-25	Not Started
APP-1480	Review & Approve Crystalline Waterproofing Product Data	21	21	12-Feb-25	04-Mar-25	404			12-Feb-25	04-Mar-25	23-Mar-26	12-Apr-26	Not Started
APP-1490	Review & Approve Suspension Assembly Shop Drawings	21	21	12-Feb-25	04-Mar-25	449			12-Feb-25	04-Mar-25	07-May-26	27-May-26	Not Started
APP-1500	Review & Approve Certification of Material	21	21	12-Feb-25	04-Mar-25	552			12-Feb-25	04-Mar-25	18-Aug-26	07-Sep-26	Not Started
APP-1510	Review & Approve Formwork Shop Drawings	21	21	12-Feb-25	04-Mar-25	260			12-Feb-25	04-Mar-25	30-Oct-25	19-Nov-25	Not Started
APP-1520	Review & Approve Planting Schedule	21	21	12-Feb-25	04-Mar-25	209			12-Feb-25	04-Mar-25	09-Sep-25	29-Sep-25	Not Started
APP-1530	Review & Approve Playgroung Equipment Shop Drawings	21	21	12-Feb-25	04-Mar-25	464			12-Feb-25	04-Mar-25	22-May-26	11-Jun-26	Not Started
APP-1540	Review & Approve Catch Basin Shop Drawings	21	21	12-Feb-25	04-Mar-25	503			12-Feb-25	04-Mar-25	30-Jun-26	20-Jul-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
APP-1550	Review & Approve Concrete Curbs & Pavements Shop Drawing	21	21	12-Feb-25	04-Mar-25	499			12-Feb-25	04-Mar-25	26-Jun-26	16-Jul-26	Not Started
APP-1560	Review & Approve Steel Curb Facing Shop Drawing	21	21	12-Feb-25	04-Mar-25	460			12-Feb-25	04-Mar-25	18-May-26	07-Jun-26	Not Started
APP-1570	Review & Approve Asphaltic Concrete Paving	21	21	12-Feb-25	04-Mar-25	520			12-Feb-25	04-Mar-25	17-Jul-26	06-Aug-26	Not Started
APP-1580	Review & Approve Gas Vapor Barrier Submittal & Inspection Schedule	21	21	12-Feb-25	04-Mar-25	225			12-Feb-25	04-Mar-25	25-Sep-25	15-Oct-25	Not Started
APP-1590	Review & Approve Training Outline & Schedule	21	21	12-Feb-25	04-Mar-25	497			12-Feb-25	04-Mar-25	24-Jun-26	14-Jul-26	Not Started
APP-1600	Review & Approve Temporary Ventilation Plan	21	21	12-Feb-25	04-Mar-25	400			12-Feb-25	04-Mar-25	19-Mar-26	08-Apr-26	Not Started
APP-1610	Review & Approve Construction Indoor Air Quality Management Plan	21	21	12-Feb-25	04-Mar-25	400			12-Feb-25	04-Mar-25	19-Mar-26	08-Apr-26	Not Started
APP-1620	Review & Approve CWM Plan	21	21	12-Feb-25	04-Mar-25	588			12-Feb-25	04-Mar-25	23-Sep-26	13-Oct-26	Not Started
APP-1630	Review & Approve Heating Plan	21	21	12-Feb-25	04-Mar-25	436			12-Feb-25	04-Mar-25	24-Apr-26	14-May-26	Not Started
APP-1640	Review & Approve Sample Classroom Materials	21	21	12-Feb-25	04-Mar-25	448			12-Feb-25	04-Mar-25	06-May-26	26-May-26	Not Started
APP-1650	Review & Approve Electrical Shop Drawings	21	21	12-Feb-25	04-Mar-25	241			12-Feb-25	04-Mar-25	11-Oct-25	31-Oct-25	Not Started
APP-1660	Review & Approve Plumbing Shop Drawings	21	21	12-Feb-25	04-Mar-25	312			12-Feb-25	04-Mar-25	21-Dec-25	10-Jan-26	Not Started
APP-1670	Review & Approve Sprinkler System Shop Drawings	21	21	12-Feb-25	04-Mar-25	348			12-Feb-25	04-Mar-25	26-Jan-26	15-Feb-26	Not Started
APP-1680	Review & Approve Gypsum Board	21	21	12-Feb-25	04-Mar-25	282			12-Feb-25	04-Mar-25	21-Nov-25	11-Dec-25	Not Started
APP-1690	Review & Approve Floorings	21	21	12-Feb-25	04-Mar-25	359			12-Feb-25	04-Mar-25	06-Feb-26	26-Feb-26	Not Started
APP-1700	Review & Approve Toilet Accessories	21	21	12-Feb-25	04-Mar-25	453			12-Feb-25	04-Mar-25	11-May-26	31-May-26	Not Started
APP-1710	Review & Approve Millwork	21	21	12-Feb-25	04-Mar-25	538			12-Feb-25	04-Mar-25	04-Aug-26	24-Aug-26	Not Started
APP-1720	Review & Approve Furniture	21	21	12-Feb-25	04-Mar-25	313			12-Feb-25	04-Mar-25	22-Dec-25	11-Jan-26	Not Started
APP-1730	Review & Approve Mechanical Ducts	21	21	12-Feb-25	04-Mar-25	285			12-Feb-25	04-Mar-25	24-Nov-25	14-Dec-25	Not Started
APP-1740	Review & Approve Plumbing Fixtures	21	21	12-Feb-25	04-Mar-25	453			12-Feb-25	04-Mar-25	11-May-26	31-May-26	Not Started
APP-1750	Review & Approve Wood Doors	21	21	12-Feb-25	04-Mar-25	382			12-Feb-25	04-Mar-25	01-Mar-26	21-Mar-26	Not Started
APP-1760	Review & Approve Fire Protection Shop Drawings	21	21	12-Feb-25	04-Mar-25	453			12-Feb-25	04-Mar-25	11-May-26	31-May-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
APP-1770	Review & Approve Fire Detectors & Alarms	21	21	12-Feb-25	04-Mar-25	418			12-Feb-25	04-Mar-25	06-Apr-26	26-Apr-26	Not Started
APP-1790	Review & Approve Signs	21	21	12-Feb-25	04-Mar-25	394			12-Feb-25	04-Mar-25	13-Mar-26	02-Apr-26	Not Started
APP-1800	Review & Approve Telecommunication System Drawings	21	21	12-Feb-25	04-Mar-25	428			12-Feb-25	04-Mar-25	16-Apr-26	06-May-26	Not Started
APP-1840	Review & Approve Gymnasium Equipment	21	21	12-Feb-25	04-Mar-25	357			12-Feb-25	04-Mar-25	04-Feb-26	24-Feb-26	Not Started
APP-1850	Review & Approve Supplemental Comissioning Requirements	21	21	12-Feb-25	04-Mar-25	488			12-Feb-25	04-Mar-25	15-Jun-26	05-Jul-26	Not Started
APP-1860	Review & Approve Record Documents	21	21	12-Feb-25	04-Mar-25	209			12-Feb-25	04-Mar-25	09-Sep-25	29-Sep-25	Not Started
APP-1870	Review & Approve Environmental Site Assessment Reports	21	21	12-Feb-25	04-Mar-25	422			12-Feb-25	04-Mar-25	10-Apr-26	30-Apr-26	Not Started
APP-1880	Review & Approve Selective Removals & Demoloition	21	21	12-Feb-25	04-Mar-25	434			12-Feb-25	04-Mar-25	22-Apr-26	12-May-26	Not Started
APP-1890	Review & Approve Trench Drains Prodcut Data	21	21	12-Feb-25	04-Mar-25	509			12-Feb-25	04-Mar-25	06-Jul-26	26-Jul-26	Not Started
APP-1900	Review & Approve Chain Link Fences & Gates Drawings	21	21	12-Feb-25	04-Mar-25	222			12-Feb-25	04-Mar-25	22-Sep-25	12-Oct-25	Not Started
APP-1910	Review & Approve Outdoor Game Equipment	21	21	12-Feb-25	04-Mar-25	464			12-Feb-25	04-Mar-25	22-May-26	11-Jun-26	Not Started
APP-1940	Review & Approve Cast Stone Product Data	21	21	12-Feb-25	04-Mar-25	392			12-Feb-25	04-Mar-25	11-Mar-26	31-Mar-26	Not Started
APP-1960	Review & Approve Metal Deck Product Data	21	21	12-Feb-25	04-Mar-25	222			12-Feb-25	04-Mar-25	22-Sep-25	12-Oct-25	Not Started
APP-1970	Review & Approve Prefabricated Expansion Joint Covers	21	21	12-Feb-25	04-Mar-25	232			12-Feb-25	04-Mar-25	02-Oct-25	22-Oct-25	Not Started
APP-1980	Review & Approve Self Adhering Sheet Air Barriers	21	21	12-Feb-25	04-Mar-25	413			12-Feb-25	04-Mar-25	01-Apr-26	21-Apr-26	Not Started
APP-1990	Review & Approve Metal Plate Wall Panels	21	21	12-Feb-25	04-Mar-25	470			12-Feb-25	04-Mar-25	28-May-26	17-Jun-26	Not Started
APP-2000	Review & Approve Security Screens & Barriers	21	21	12-Feb-25	04-Mar-25	485			12-Feb-25	04-Mar-25	12-Jun-26	02-Jul-26	Not Started
APP-2010	Review & Approve Wood Flooring	21	21	12-Feb-25	04-Mar-25	379			12-Feb-25	04-Mar-25	26-Feb-26	18-Mar-26	Not Started
APP-2020	Review & Approve Visual Display Boards	21	21	12-Feb-25	04-Mar-25	544			12-Feb-25	04-Mar-25	10-Aug-26	30-Aug-26	Not Started
APP-2030	Review & Approve Metal Lockers	21	21	12-Feb-25	04-Mar-25	544			12-Feb-25	04-Mar-25	10-Aug-26	30-Aug-26	Not Started
APP-2040	Review & Approve Fire Extinguishers & Cabinets	21	21	12-Feb-25	04-Mar-25	456			12-Feb-25	04-Mar-25	14-May-26	03-Jun-26	Not Started
APP-2050	Review & Approve Library	21	21	12-Feb-25	04-Mar-25	565			12-Feb-25	04-Mar-25	31-Aug-26	20-Sep-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
APP-2060	Review & Approve Platform Curtains & Auditorium Window Curtains	21	21	12-Feb-25	04-Mar-25	572			12-Feb-25	04-Mar-25	07-Sep-26	27-Sep-26	Not Started
APP-2070	Review & Approve Waste Handling Equipment	21	21	12-Feb-25	04-Mar-25	209			12-Feb-25	04-Mar-25	09-Sep-25	29-Sep-25	Not Started
APP-2080	Review & Approve Domestic Equipment	21	21	12-Feb-25	04-Mar-25	375			12-Feb-25	04-Mar-25	22-Feb-26	14-Mar-26	Not Started
APP-2090	Review & Approve Laboratory Equipment	21	21	12-Feb-25	04-Mar-25	565			12-Feb-25	04-Mar-25	31-Aug-26	20-Sep-26	Not Started
APP-2100	Review & Approve Manufactured Wood Casework	21	21	12-Feb-25	04-Mar-25	313			12-Feb-25	04-Mar-25	22-Dec-25	11-Jan-26	Not Started
APP-2110	Review & Approve Concrete Floating Floor Assembly	21	21	12-Feb-25	04-Mar-25	379			12-Feb-25	04-Mar-25	26-Feb-26	18-Mar-26	Not Started
APP-2120	Review & Approve Hydraulic Vertical Wheelchair Lifts	21	21	12-Feb-25	04-Mar-25	443			12-Feb-25	04-Mar-25	01-May-26	21-May-26	Not Started
APP-2130	Review & Approve Switch & Panel Boards	21	21	12-Feb-25	04-Mar-25	226			12-Feb-25	04-Mar-25	26-Sep-25	16-Oct-25	Not Started
APP-2140	Review & Approve Auditorium & Television Studio Dimming System Product Data	21	21	12-Feb-25	04-Mar-25	455			12-Feb-25	04-Mar-25	13-May-26	02-Jun-26	Not Started
APP-2150	Review & Approve Overcurrent Protective Devices Data	21	21	12-Feb-25	04-Mar-25	209			12-Feb-25	04-Mar-25	09-Sep-25	29-Sep-25	Not Started
APP-2160	Review & Approve Gas Pipes	21	21	12-Feb-25	04-Mar-25	432			12-Feb-25	04-Mar-25	20-Apr-26	10-May-26	Not Started
APP-2170	Review & Approve Water Heaters	21	21	12-Feb-25	04-Mar-25	495			12-Feb-25	04-Mar-25	22-Jun-26	12-Jul-26	Not Started
APP-2180	Review & Approve Pumping Apparatus & Tanks	21	21	12-Feb-25	04-Mar-25	533			12-Feb-25	04-Mar-25	30-Jul-26	19-Aug-26	Not Started
APP-2190	Review & Approve HVAC Pumps	21	21	12-Feb-25	04-Mar-25	545			12-Feb-25	04-Mar-25	11-Aug-26	31-Aug-26	Not Started
APP-2210	Review & Approve Fuel Storage Equipment	21	21	12-Feb-25	04-Mar-25	540			12-Feb-25	04-Mar-25	06-Aug-26	26-Aug-26	Not Started
APP-2220	Review & Approve Natural Gas Leak Detection Equipment	21	21	12-Feb-25	04-Mar-25	497			12-Feb-25	04-Mar-25	24-Jun-26	14-Jul-26	Not Started
APP-2240	Review & Approve Temperature Control System	21	21	12-Feb-25	04-Mar-25	467			12-Feb-25	04-Mar-25	25-May-26	14-Jun-26	Not Started
APP-2250	Review & Approve Air Outlets & Inlets	21	21	12-Feb-25	04-Mar-25	404			12-Feb-25	04-Mar-25	23-Mar-26	12-Apr-26	Not Started
APP-2360	Review & Approve Adjacent Property and Structures Protection & Monitoring Plan	21	21	12-Feb-25	04-Mar-25	894			12-Feb-25	04-Mar-25	26-Jul-27	15-Aug-27	Not Started
APP-2370	Review & Approve Ornamenta Metal Shop Drawings	21	21	12-Feb-25	04-Mar-25	222			12-Feb-25	04-Mar-25	22-Sep-25	12-Oct-25	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
APP-2920	Review & Approve Documentation of Proper Disposal	21	21	12-Feb-25	04-Mar-25	484			12-Feb-25	04-Mar-25	11-Jun-26	01-Jul-26	Not Started
APP-2930	Review & Approve Ornamenta Metal Product Data	21	21	12-Feb-25	04-Mar-25	222			12-Feb-25	04-Mar-25	22-Sep-25	12-Oct-25	Not Started
APP-2960	Review & Approve Coiling Doors, Grilles and Shutters Shop Drawings	21	21	12-Feb-25	04-Mar-25	531			12-Feb-25	04-Mar-25	28-Jul-26	17-Aug-26	Not Started
APP-2970	Review & Approve Coiling Doors, Grilles and ShuttersProduct Data	21	21	12-Feb-25	04-Mar-25	531			12-Feb-25	04-Mar-25	28-Jul-26	17-Aug-26	Not Started
APP-2980	Review & Approve Aluminum Framed Entrances & Storefronts Shop Drawings	21	21	12-Feb-25	04-Mar-25	238			12-Feb-25	04-Mar-25	08-Oct-25	28-Oct-25	Not Started
APP-2990	Review & Approve Aluminum Framed Entrances & Storefronts Product Data	21	21	12-Feb-25	04-Mar-25	238			12-Feb-25	04-Mar-25	08-Oct-25	28-Oct-25	Not Started
APP-3000	Review & Approve Thresholds, Weatherstripping and Seals Color Samples	21	21	12-Feb-25	04-Mar-25	371			12-Feb-25	04-Mar-25	18-Feb-26	10-Mar-26	Not Started
APP-3010	Review & Approve Thresholds, Weatherstripping and Seals Product Data	21	21	12-Feb-25	04-Mar-25	371			12-Feb-25	04-Mar-25	18-Feb-26	10-Mar-26	Not Started
APP-3020	Review & Approve Miscellaneous Glazing Samples	21	21	12-Feb-25	04-Mar-25	371			12-Feb-25	04-Mar-25	18-Feb-26	10-Mar-26	Not Started
APP-3030	Review & Approve Miscellaneous Glazing Product Data	21	21	12-Feb-25	04-Mar-25	371			12-Feb-25	04-Mar-25	18-Feb-26	10-Mar-26	Not Started
APP-3040	Review & Approve Fire Rated Glazing Samples	21	21	12-Feb-25	04-Mar-25	371			12-Feb-25	04-Mar-25	18-Feb-26	10-Mar-26	Not Started
APP-3050	Review & Approve Fire Rated Glazing Product Data	21	21	12-Feb-25	04-Mar-25	371			12-Feb-25	04-Mar-25	18-Feb-26	10-Mar-26	Not Started
APP-3060	Review & Approve Graffiti Resistant Coating Product Data	21	21	12-Feb-25	04-Mar-25	365			12-Feb-25	04-Mar-25	12-Feb-26	04-Mar-26	Not Started
APP-3070	Review & Approve Special Coating Samples	21	21	12-Feb-25	04-Mar-25	273			12-Feb-25	04-Mar-25	12-Nov-25	02-Dec-25	Not Started
APP-3080	Review & Approve Special Coating Product Data	21	21	12-Feb-25	04-Mar-25	273			12-Feb-25	04-Mar-25	12-Nov-25	02-Dec-25	Not Started
APP-3090	Review & Approve Flagpole Shop Drawing	21	21	12-Feb-25	04-Mar-25	346			12-Feb-25	04-Mar-25	24-Jan-26	13-Feb-26	Not Started
APP-3100	Review & Approve Flagpole Product Data	21	21	12-Feb-25	04-Mar-25	346			12-Feb-25	04-Mar-25	24-Jan-26	13-Feb-26	Not Started
APP-3110	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases	21	21	12-Feb-25	04-Mar-25	313			12-Feb-25	04-Mar-25	22-Dec-25	11-Jan-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
	Sustainability Submittals												
APP-3120	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	21	21	12-Feb-25	04-Mar-25	313			12-Feb-25	04-Mar-25	22-Dec-25	11-Jan-26	Not Started
APP-3130	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	21	21	12-Feb-25	04-Mar-25	313			12-Feb-25	04-Mar-25	22-Dec-25	11-Jan-26	Not Started
APP-3140	Review & Approve Wire Mesh Work Samples	21	21	12-Feb-25	04-Mar-25	371			12-Feb-25	04-Mar-25	18-Feb-26	10-Mar-26	Not Started
APP-3150	Review & Approve Miscellaneous Glazing Shop drawings	21	21	12-Feb-25	04-Mar-25	371			12-Feb-25	04-Mar-25	18-Feb-26	10-Mar-26	Not Started
APP-3160	Review & Approve Metal Storage Shelving Samples	21	21	12-Feb-25	04-Mar-25	313			12-Feb-25	04-Mar-25	22-Dec-25	11-Jan-26	Not Started
APP-3170	Review & Approve Metal Storage Shelving Shop drawings	21	21	12-Feb-25	04-Mar-25	313			12-Feb-25	04-Mar-25	22-Dec-25	11-Jan-26	Not Started
APP-3180	Review & Approve Mirrors Shop Drawing	21	21	12-Feb-25	04-Mar-25	443			12-Feb-25	04-Mar-25	01-May-26	21-May-26	Not Started
APP-3190	Review & Approve Mirrors Product Data	21	21	12-Feb-25	04-Mar-25	443			12-Feb-25	04-Mar-25	01-May-26	21-May-26	Not Started
APP-3200	Review & Approve Mirrors Mastic Compatibility Test Reports & Certifications	21	21	12-Feb-25	04-Mar-25	443			12-Feb-25	04-Mar-25	01-May-26	21-May-26	Not Started
APP-3210	Review & Approve Grab Bars Shop Drawing	21	21	12-Feb-25	04-Mar-25	453			12-Feb-25	04-Mar-25	11-May-26	31-May-26	Not Started
APP-3220	Review & Approve Grab Bars Product Data	21	21	12-Feb-25	04-Mar-25	453			12-Feb-25	04-Mar-25	11-May-26	31-May-26	Not Started
APP-3230	Review & Approve Shop Equipment Shop Drawing	21	21	12-Feb-25	04-Mar-25	209			12-Feb-25	04-Mar-25	09-Sep-25	29-Sep-25	Not Started
APP-3240	Review & Approve Shop Equipment Product Data	21	21	12-Feb-25	04-Mar-25	209			12-Feb-25	04-Mar-25	09-Sep-25	29-Sep-25	Not Started
APP-3250	Review & Approve Bleachers Shop Drawing	21	21	12-Feb-25	04-Mar-25	402			12-Feb-25	04-Mar-25	21-Mar-26	10-Apr-26	Not Started
APP-3260	Review & Approve Bleachers Product Data	21	21	12-Feb-25	04-Mar-25	402			12-Feb-25	04-Mar-25	21-Mar-26	10-Apr-26	Not Started
APP-3270	Review & Approve Bleachers Manufacturer's Warranty	21	21	12-Feb-25	04-Mar-25	402			12-Feb-25	04-Mar-25	21-Mar-26	10-Apr-26	Not Started
APP-3280	Review & Approve Valves Shop Drawing	21	21	12-Feb-25	04-Mar-25	340			12-Feb-25	04-Mar-25	18-Jan-26	07-Feb-26	Not Started
APP-3290	Review & Approve Valves Product Data	21	21	12-Feb-25	04-Mar-25	340			12-Feb-25	04-Mar-25	18-Jan-26	07-Feb-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
APP-3300	Review & Approve Certification of Tests	21	21	12-Feb-25	04-Mar-25	209			12-Feb-25	04-Mar-25	09-Sep-25	29-Sep-25	Not Started
APP-3310	Review & Approve Domestic Water Sterilization Plan	21	21	12-Feb-25	04-Mar-25	209			12-Feb-25	04-Mar-25	09-Sep-25	29-Sep-25	Not Started
APP-3320	Review & Approve Tags, Charts & Identifications Shop Drawing	21	21	12-Feb-25	04-Mar-25	209			12-Feb-25	04-Mar-25	09-Sep-25	29-Sep-25	Not Started
APP-3330	Review & Approve Tags, Charts & Identifications Product Data	21	21	12-Feb-25	04-Mar-25	209			12-Feb-25	04-Mar-25	09-Sep-25	29-Sep-25	Not Started
APP-3340	Review & Approve Micselianeous Shop Drawing	21	21	12-Feb-25	04-Mar-25	209			12-Feb-25	04-Mar-25	09-Sep-25	29-Sep-25	Not Started
APP-3350	Review & Approve Valves (HVAC) Shop Drawing	21	21	12-Feb-25	04-Mar-25	285			12-Feb-25	04-Mar-25	24-Nov-25	14-Dec-25	Not Started
APP-3360	Review & Approve Valves (HVAC) Product Data	21	21	12-Feb-25	04-Mar-25	285			12-Feb-25	04-Mar-25	24-Nov-25	14-Dec-25	Not Started
APP-3370	Review & Approve Piping Insulation Schedule Listing Items	21	21	12-Feb-25	04-Mar-25	292			12-Feb-25	04-Mar-25	01-Dec-25	21-Dec-25	Not Started
APP-3380	Review & Approve chedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	21	21	12-Feb-25	04-Mar-25	217			12-Feb-25	04-Mar-25	17-Sep-25	07-Oct-25	Not Started
APP-3390	Review & Approve chedules Showing Manfacturers's Product Number Duct Work Insulation	21	21	12-Feb-25	04-Mar-25	434			12-Feb-25	04-Mar-25	22-Apr-26	12-May-26	Not Started
APP-3400	Review & Approve Hydronic Specialities Shop Drawing	21	21	12-Feb-25	04-Mar-25	217			12-Feb-25	04-Mar-25	17-Sep-25	07-Oct-25	Not Started
APP-3410	Review & Approve Hydronic Specialities Product Data	21	21	12-Feb-25	04-Mar-25	217			12-Feb-25	04-Mar-25	17-Sep-25	07-Oct-25	Not Started
APP-3420	Review & Approve Water Treatment Firm	21	21	12-Feb-25	04-Mar-25	217			12-Feb-25	04-Mar-25	17-Sep-25	07-Oct-25	Not Started
APP-3430	Review & Approve Chemical Products Product Data	21	21	12-Feb-25	04-Mar-25	217			12-Feb-25	04-Mar-25	17-Sep-25	07-Oct-25	Not Started
APP-3460	Review & Approve Breeching Chimney Connectors and Chimneys Shop Drawing	21	21	12-Feb-25	04-Mar-25	512			12-Feb-25	04-Mar-25	09-Jul-26	29-Jul-26	Not Started
APP-3470	Review & Approve Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	21	21	12-Feb-25	04-Mar-25	512			12-Feb-25	04-Mar-25	09-Jul-26	29-Jul-26	Not Started
APP-3480	Review & Approve Plate Heat Exchanger Maintenance Data	21	21	12-Feb-25	04-Mar-25	428			12-Feb-25	04-Mar-25	16-Apr-26	06-May-26	Not Started
APP-3490	Review & Approve Plate Heat Exchanger Product Data	21	21	12-Feb-25	04-Mar-25	428			12-Feb-25	04-Mar-25	16-Apr-26	06-May-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
APP-3500	Review & Approve Coils Maintenance Data	21	21	12-Feb-25	04-Mar-25	538			12-Feb-25	04-Mar-25	04-Aug-26	24-Aug-26	Not Started
APP-3510	Review & Approve Coils Certifications	21	21	12-Feb-25	04-Mar-25	538			12-Feb-25	04-Mar-25	04-Aug-26	24-Aug-26	Not Started
APP-3520	Review & Approve Convectors Shop Drawing	21	21	12-Feb-25	04-Mar-25	502			12-Feb-25	04-Mar-25	29-Jun-26	19-Jul-26	Not Started
APP-3530	Review & Approve Convectors Product Data	21	21	12-Feb-25	04-Mar-25	502			12-Feb-25	04-Mar-25	29-Jun-26	19-Jul-26	Not Started
APP-3540	Review & Approve Fan Coils Units Maintenance Data & Materials	21	21	12-Feb-25	04-Mar-25	498			12-Feb-25	04-Mar-25	25-Jun-26	15-Jul-26	Not Started
APP-3550	Review & Approve Fan Coils Units Shop Drawings	21	21	12-Feb-25	04-Mar-25	498			12-Feb-25	04-Mar-25	25-Jun-26	15-Jul-26	Not Started
APP-3560	Review & Approve Door Air Curtains Shop Drawing	21	21	12-Feb-25	04-Mar-25	541			12-Feb-25	04-Mar-25	07-Aug-26	27-Aug-26	Not Started
APP-3570	Review & Approve Door Air Curtains Product Data	21	21	12-Feb-25	04-Mar-25	541			12-Feb-25	04-Mar-25	07-Aug-26	27-Aug-26	Not Started
APP-3580	Review & Approve Centrifugal Fans Shop Drawing	21	21	12-Feb-25	04-Mar-25	491			12-Feb-25	04-Mar-25	18-Jun-26	08-Jul-26	Not Started
APP-3590	Review & Approve Centrifugal Fans Product Data	21	21	12-Feb-25	04-Mar-25	491			12-Feb-25	04-Mar-25	18-Jun-26	08-Jul-26	Not Started
APP-3600	Review & Approve Centrifugal Fans Maintenance Data & Materials	21	21	12-Feb-25	04-Mar-25	491			12-Feb-25	04-Mar-25	18-Jun-26	08-Jul-26	Not Started
APP-3610	Review & Approve Air Filters Shop Drawing	21	21	12-Feb-25	04-Mar-25	217			12-Feb-25	04-Mar-25	17-Sep-25	07-Oct-25	Not Started
APP-3620	Review & Approve Air Filters Product Data	21	21	12-Feb-25	04-Mar-25	217			12-Feb-25	04-Mar-25	17-Sep-25	07-Oct-25	Not Started
APP-3630	Review & Approve Air Filters Maintenance Data & Materials	21	21	12-Feb-25	04-Mar-25	217			12-Feb-25	04-Mar-25	17-Sep-25	07-Oct-25	Not Started
APP-3640	Review & Approve Duct Accessories Shop Drawing	21	21	12-Feb-25	04-Mar-25	285			12-Feb-25	04-Mar-25	24-Nov-25	14-Dec-25	Not Started
APP-3650	Review & Approve Damper Assemblies Shop Drawing	21	21	12-Feb-25	04-Mar-25	512			12-Feb-25	04-Mar-25	09-Jul-26	29-Jul-26	Not Started
APP-3660	Review & Approve Damper Assemblies Product Data	21	21	12-Feb-25	04-Mar-25	512			12-Feb-25	04-Mar-25	09-Jul-26	29-Jul-26	Not Started
APP-3670	Review & Approve Damper Assemblies Maintenance Data & Materials	21	21	12-Feb-25	04-Mar-25	512			12-Feb-25	04-Mar-25	09-Jul-26	29-Jul-26	Not Started
APP-3680	Review & Approve Variable Air Terminals Shop Drawing	21	21	12-Feb-25	04-Mar-25	273			12-Feb-25	04-Mar-25	12-Nov-25	02-Dec-25	Not Started
APP-3690	Review & Approve Variable Air Terminals Product Data	21	21	12-Feb-25	04-Mar-25	273			12-Feb-25	04-Mar-25	12-Nov-25	02-Dec-25	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
APP-3700	Review & Approve Variable Air Terminals Maintenance Data & Materials	21	21	12-Feb-25	04-Mar-25	273			12-Feb-25	04-Mar-25	12-Nov-25	02-Dec-25	Not Started
APP-3710	Review & Approve AHU for Public Assemblies Sapces Shop Drawing	21	21	12-Feb-25	04-Mar-25	154			12-Feb-25	04-Mar-25	16-Jul-25	05-Aug-25	Not Started
APP-3720	Review & Approve AHU for Public Assemblies Sapces Product Data	21	21	12-Feb-25	04-Mar-25	154			12-Feb-25	04-Mar-25	16-Jul-25	05-Aug-25	Not Started
APP-3730	Review & Approve AHU for Public Assemblies Sapces Maintenance Data & Materials	21	21	12-Feb-25	04-Mar-25	217			12-Feb-25	04-Mar-25	17-Sep-25	07-Oct-25	Not Started
APP-3740	Review & Approve Control Systems Shop Drawing	21	21	12-Feb-25	04-Mar-25	217			12-Feb-25	04-Mar-25	17-Sep-25	07-Oct-25	Not Started
APP-3750	Review & Approve Truck Network Cable Schematic Diagram	21	21	12-Feb-25	04-Mar-25	217			12-Feb-25	04-Mar-25	17-Sep-25	07-Oct-25	Not Started
APP-3790	Review & Approve Surge Protective Devices Shop Drawing	21	21	12-Feb-25	04-Mar-25	483			12-Feb-25	04-Mar-25	10-Jun-26	30-Jun-26	Not Started
APP-3800	Review & Approve Surge Protective Devices Product Data	21	21	12-Feb-25	04-Mar-25	483			12-Feb-25	04-Mar-25	10-Jun-26	30-Jun-26	Not Started
APP-3810	Review & Approve Surge Protective Devices Warranty	21	21	12-Feb-25	04-Mar-25	483			12-Feb-25	04-Mar-25	10-Jun-26	30-Jun-26	Not Started
APP-3820	Review & Approve Service Entrance Equipment Shop Drawing	21	21	12-Feb-25	04-Mar-25	484			12-Feb-25	04-Mar-25	11-Jun-26	01-Jul-26	Not Started
APP-3830	Review & Approve Service Entrance Equipment Product Data	21	21	12-Feb-25	04-Mar-25	484			12-Feb-25	04-Mar-25	11-Jun-26	01-Jul-26	Not Started
APP-3840	Review & Approve Service Entrance Equipment Warranty	21	21	12-Feb-25	04-Mar-25	484			12-Feb-25	04-Mar-25	11-Jun-26	01-Jul-26	Not Started
APP-3850	Review & Approve Enclosed Switches Product Data	21	21	12-Feb-25	04-Mar-25	468			12-Feb-25	04-Mar-25	26-May-26	15-Jun-26	Not Started
APP-3860	Review & Approve Enclosed Switches Test Reports	21	21	12-Feb-25	04-Mar-25	468			12-Feb-25	04-Mar-25	26-May-26	15-Jun-26	Not Started
APP-3870	Review & Approve Motors, Motor Control Centers and Starters Shop Drawing	21	21	12-Feb-25	04-Mar-25	512			12-Feb-25	04-Mar-25	09-Jul-26	29-Jul-26	Not Started
APP-3880	Review & Approve Motors, Motor Control Centers and Starters Product Data	21	21	12-Feb-25	04-Mar-25	512			12-Feb-25	04-Mar-25	09-Jul-26	29-Jul-26	Not Started
APP-3890	Review & Approve Motors, Motor Control Centers and Starters Field	21	21	12-Feb-25	04-Mar-25	512			12-Feb-25	04-Mar-25	09-Jul-26	29-Jul-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
	Test Reports												
APP-3900	Review & Approve Lightning Protection Shop Drawing	21	21	12-Feb-25	04-Mar-25	414			12-Feb-25	04-Mar-25	02-Apr-26	22-Apr-26	Not Started
APP-3920	Review & Approve Lightning Protection Test Reports	21	21	12-Feb-25	04-Mar-25	414			12-Feb-25	04-Mar-25	02-Apr-26	22-Apr-26	Not Started
APP-3930	Review & Approve Fiber Optic Cabling system Shop Drawing	21	21	12-Feb-25	04-Mar-25	379			12-Feb-25	04-Mar-25	26-Feb-26	18-Mar-26	Not Started
APP-3940	Review & Approve Fiber Optic Cabling system Product Data	21	21	12-Feb-25	04-Mar-25	379			12-Feb-25	04-Mar-25	26-Feb-26	18-Mar-26	Not Started
APP-3950	Review & Approve Fiber Optic Cabling system Samples	21	21	12-Feb-25	04-Mar-25	379			12-Feb-25	04-Mar-25	26-Feb-26	18-Mar-26	Not Started
APP-3960	Review & Approve Sound, Intercome & Security System Shop Drawing	21	21	12-Feb-25	04-Mar-25	475			12-Feb-25	04-Mar-25	02-Jun-26	22-Jun-26	Not Started
APP-3970	Review & Approve Sound, Intercome & Security System Programming Code and Password for the System	21	21	12-Feb-25	04-Mar-25	475			12-Feb-25	04-Mar-25	02-Jun-26	22-Jun-26	Not Started
APP-3980	Review & Approve Sound, Intercome & Security System warranty	21	21	12-Feb-25	04-Mar-25	475			12-Feb-25	04-Mar-25	02-Jun-26	22-Jun-26	Not Started
APP-3990	Review & Approve Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	21	21	12-Feb-25	04-Mar-25	538			12-Feb-25	04-Mar-25	04-Aug-26	24-Aug-26	Not Started
APP-4000	Review & Approve Projection and Interactive Whiteboard Systems Wiring diagram	21	21	12-Feb-25	04-Mar-25	538			12-Feb-25	04-Mar-25	04-Aug-26	24-Aug-26	Not Started
APP-4010	Review & Approve Self Corrective Clock System Shop Drawing	21	21	12-Feb-25	04-Mar-25	475			12-Feb-25	04-Mar-25	02-Jun-26	22-Jun-26	Not Started
APP-4020	Review & Approve Self Corrective Clock System Product Data	21	21	12-Feb-25	04-Mar-25	475			12-Feb-25	04-Mar-25	02-Jun-26	22-Jun-26	Not Started
APP-4030	Review & Approve Self Corrective Clock System Field Test Reports	21	21	12-Feb-25	04-Mar-25	475			12-Feb-25	04-Mar-25	02-Jun-26	22-Jun-26	Not Started
APP-4040	Review & Approve Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	21	21	12-Feb-25	04-Mar-25	531			12-Feb-25	04-Mar-25	28-Jul-26	17-Aug-26	Not Started
APP-4060	Review & Approve Steel Stairs Shop Drawings	21	21	12-Feb-25	04-Mar-25	319			12-Feb-25	04-Mar-25	28-Dec-25	17-Jan-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
APP-4070	Review & Approve Steel Stairs Product Data	21	21	12-Feb-25	04-Mar-25	319			12-Feb-25	04-Mar-25	28-Dec-25	17-Jan-26	Not Started
APP-4080	Review & Approve Green School Submittal	21	21	12-Feb-25	04-Mar-25	209			12-Feb-25	04-Mar-25	09-Sep-25	29-Sep-25	Not Started
APP-2260	Review & Approve Product Substitutions	21	21	13-Feb-25	05-Mar-25	559			13-Feb-25	05-Mar-25	26-Aug-26	15-Sep-26	Not Started
MIL-2572	Place Steel Mill Order	0	0	20-Feb-25		117			20-Feb-25		07-Aug-25		Not Started
SUB-2280	Prepare & Submit Final 1st Floor Coordination Drawings	49	49	25-Feb-25	02-May-25	6			25-Feb-25	02-May-25	05-Mar-25	12-May-25	Not Started
SUB-2290	Prepare & Submit Final 2nd Floor Coordination Drawings	49	49	25-Feb-25	02-May-25	6			25-Feb-25	02-May-25	05-Mar-25	12-May-25	Not Started
SUB-2300	Prepare & Submit Final 3rd Floor Coordination Drawings	49	49	25-Feb-25	02-May-25	6			25-Feb-25	02-May-25	05-Mar-25	12-May-25	Not Started
SUB-2310	Prepare & Submit Final 4th Floor Coordination Drawings	49	49	25-Feb-25	02-May-25	6			25-Feb-25	02-May-25	05-Mar-25	12-May-25	Not Started
SUB-2320	Prepare & Submit Final 5th Floor Coordination Drawings	49	49	25-Feb-25	02-May-25	6			25-Feb-25	02-May-25	05-Mar-25	12-May-25	Not Started
MIL-2762	Green Schools Compliance Submission	0	0		04-Mar-25	145				04-Mar-25		29-Sep-25	Not Started
SUB-1700	Prepare & Submit Roof Dunnage	81	81	05-Mar-25	27-Jun-25	107			05-Mar-25	27-Jun-25	06-Aug-25	02-Dec-25	Not Started
APP-2270	Review & Approve Final Foundations Coordination Drawings	21	21	12-Mar-25	01-Apr-25	62			12-Mar-25	01-Apr-25	13-May-25	02-Jun-25	Not Started
APP-2280	Review & Approve Final 1st Floor Coordination Drawings	21	21	03-May-25	23-May-25	10			03-May-25	23-May-25	13-May-25	02-Jun-25	Not Started
APP-2290	Review & Approve Final 2nd Floor Coordination Drawings	21	21	03-May-25	23-May-25	10			03-May-25	23-May-25	13-May-25	02-Jun-25	Not Started
APP-2300	Review & Approve Final 3rd Floor Coordination Drawings	21	21	03-May-25	23-May-25	10			03-May-25	23-May-25	13-May-25	02-Jun-25	Not Started
APP-2310	Review & Approve Final 4th Floor Coordination Drawings	21	21	03-May-25	23-May-25	10			03-May-25	23-May-25	13-May-25	02-Jun-25	Not Started
APP-2320	Review & Approve Final 5th Floor Coordination Drawings	21	21	03-May-25	23-May-25	10			03-May-25	23-May-25	13-May-25	02-Jun-25	Not Started
MIL-1640	Provide Complete Set of Approved Coordination Drawings	0	0		23-May-25	5				23-May-25		02-Jun-25	Not Started
SUB-2900	Prepare & Submit Excavated Material Disposal Plan	71	71	26-May-25	05-Sep-25	7			26-May-25	05-Sep-25	05-Jun-25	16-Sep-25	Not Started
SUB-4050	Prepare & Submit Soil Sampling Plan	71	71	26-May-25	05-Sep-25	5			26-May-25	05-Sep-25	03-Jun-25	12-Sep-25	Not Started
PRO-1590	Procure & Deliver Steel Columns	120	120	02-Jun-25	29-Sep-25	66			02-Jun-25	29-Sep-25	07-Aug-25	04-Dec-25	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
APP-1810	Review & Approve Roof Dunnage	21	21	28-Jun-25	18-Jul-25	158			28-Jun-25	18-Jul-25	03-Dec-25	23-Dec-25	Not Started
PRO-1120	Procure & Deliver Erosion Control and Sedimentation Devices	25	25	05-Sep-25	29-Sep-25	13			05-Sep-25	29-Sep-25	18-Sep-25	12-Oct-25	Not Started
APP-2900	Review & Approve Excavated Material Disposal Plan	21	21	06-Sep-25	26-Sep-25	11			06-Sep-25	26-Sep-25	17-Sep-25	07-Oct-25	Not Started
APP-4050	Review & Approve Soil Sampling Plan	21	21	06-Sep-25	26-Sep-25	9			06-Sep-25	26-Sep-25	15-Sep-25	05-Oct-25	Not Started
SUB-2910	Prepare & Submit Backfill & Resue Plan	20	20	08-Sep-25	03-Oct-25	11			08-Sep-25	03-Oct-25	23-Sep-25	21-Oct-25	Not Started
PRE-2630	Obtain Builders Pavement Permit	10	10	16-Sep-25	29-Sep-25	0			16-Sep-25	29-Sep-25	16-Sep-25	29-Sep-25	Not Started
PRE-2640	Obtain Excavation & Shoring Permit	10	10	16-Sep-25	29-Sep-25	0			16-Sep-25	29-Sep-25	16-Sep-25	29-Sep-25	Not Started
PRE-2650	Obtain Permit to Enter (PTE) Amtrak	10	10	16-Sep-25	29-Sep-25	0			16-Sep-25	29-Sep-25	16-Sep-25	29-Sep-25	Not Started
PRE-2660	Obtain NYPA Permit	10	10	16-Sep-25	29-Sep-25	0			16-Sep-25	29-Sep-25	16-Sep-25	29-Sep-25	Not Started
PRE-2540	SCA Work Notification	7	7	23-Sep-25	29-Sep-25	0			23-Sep-25	29-Sep-25	23-Sep-25	29-Sep-25	Not Started
PRE-1660	DOB Permit & Insurance	3	3	25-Sep-25	29-Sep-25	0			25-Sep-25	29-Sep-25	25-Sep-25	29-Sep-25	Not Started
PRE-1460	Obtain Construction Fences Permit	3	3	25-Sep-25	29-Sep-25	0			25-Sep-25	29-Sep-25	25-Sep-25	29-Sep-25	Not Started
PRE-2550	Obtain CCD1	3	3	25-Sep-25	29-Sep-25	0			25-Sep-25	29-Sep-25	25-Sep-25	29-Sep-25	Not Started
PRE-2570	Obtain Sidewalk Shed Permits	3	3	25-Sep-25	29-Sep-25	0			25-Sep-25	29-Sep-25	25-Sep-25	29-Sep-25	Not Started
MIL-2532	Submit Complete Permit Application	0	0		29-Sep-25	0				29-Sep-25		29-Sep-25	Not Started
MIL-2832	Issuance of Excavation & Shoring Permit	0	0		29-Sep-25	6				29-Sep-25		07-Oct-25	Not Started
MIL-2842	Issuance of Builders Pavement Permit	0	0		29-Sep-25	0				29-Sep-25		29-Sep-25	Not Started
MIL-2852	Issuance of Permit to Enter (PTE)	0	0		29-Sep-25	0				29-Sep-25		29-Sep-25	Not Started
MIL-2862	Issuance of NYPA Permit	0	0		29-Sep-25	0				29-Sep-25		29-Sep-25	Not Started
MIL-2872	Issuance of Construction Fences Permit	0	0		29-Sep-25	0				29-Sep-25		29-Sep-25	Not Started
MIL-2882	Issuance of Sidewalk Shed Permits	0	0		29-Sep-25	0				29-Sep-25		29-Sep-25	Not Started
MIL-2892	Issuance of CCD1	0	0		29-Sep-25	0				29-Sep-25		29-Sep-25	Not Started
MIL-2902	Issuance of DOB Permit & Insurance	0	0		29-Sep-25	0				29-Sep-25		29-Sep-25	Not Started
CON-1000	Mobilization	4	4	30-Sep-25	03-Oct-25	0			30-Sep-25	03-Oct-25	30-Sep-25	03-Oct-25	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
MIL-1060	Mobilization Start	0	0	30-Sep-25		0			30-Sep-25		30-Sep-25		Not Started
PRO-1420	Procure & Deliver Painting	70	70	30-Sep-25	08-Dec-25	184			30-Sep-25	08-Dec-25	02-Apr-26	10-Jun-26	Not Started
PRO-1410	Procure & Deliver Door Frames	70	70	30-Sep-25	08-Dec-25	153			30-Sep-25	08-Dec-25	02-Mar-26	10-May-26	Not Started
PRO-1200	Procure & Deliver Elevator Machine	112	112	30-Sep-25	19-Jan-26	122			30-Sep-25	19-Jan-26	30-Jan-26	21-May-26	Not Started
PRO-1150	Procure & Deliver Gypsum Board	150	150	30-Sep-25	26-Feb-26	73			30-Sep-25	26-Feb-26	12-Dec-25	10-May-26	Not Started
PRO-1160	Procure & Deliver Floorings	80	80	30-Sep-25	18-Dec-25	150			30-Sep-25	18-Dec-25	27-Feb-26	17-May-26	Not Started
PRO-1170	Procure & Deliver Acosutical Ceiling Tiles	120	120	30-Sep-25	27-Jan-26	169			30-Sep-25	27-Jan-26	18-Mar-26	15-Jul-26	Not Started
PRO-1190	Procure & Deliver Toilet Accessories	100	100	30-Sep-25	07-Jan-26	244			30-Sep-25	07-Jan-26	01-Jun-26	08-Sep-26	Not Started
PRO-1000	Procure & Deliver Kitchen Equipment	180	180	30-Sep-25	28-Mar-26	166			30-Sep-25	28-Mar-26	15-Mar-26	10-Sep-26	Not Started
PRO-1140	Procure & Deliver Lighting Fixtures	60	60	30-Sep-25	28-Nov-25	201			30-Sep-25	28-Nov-25	19-Apr-26	17-Jun-26	Not Started
PRO-1010	Procure & Deliver Furnitures	130	130	30-Sep-25	06-Feb-26	104			30-Sep-25	06-Feb-26	12-Jan-26	21-May-26	Not Started
PRO-1020	Procure & Deliver Mechanical Piping	70	70	30-Sep-25	08-Dec-25	83			30-Sep-25	08-Dec-25	22-Dec-25	01-Mar-26	Not Started
PRO-1030	Procure & Deliver Mechanical Ducts	70	70	30-Sep-25	08-Dec-25	76			30-Sep-25	08-Dec-25	15-Dec-25	22-Feb-26	Not Started
PRO-1050	Procure & Deliver Electrical Equipment	130	130	30-Sep-25	06-Feb-26	144			30-Sep-25	06-Feb-26	21-Feb-26	30-Jun-26	Not Started
PRO-1060	Procure & Deliver Plumbing Fixtures	100	100	30-Sep-25	07-Jan-26	244			30-Sep-25	07-Jan-26	01-Jun-26	08-Sep-26	Not Started
PRO-1070	Procure & Deliver Wood Doors	50	50	30-Sep-25	18-Nov-25	173			30-Sep-25	18-Nov-25	22-Mar-26	10-May-26	Not Started
PRO-1090	Procure & Deliver Fire Sprinklers	100	100	30-Sep-25	07-Jan-26	139			30-Sep-25	07-Jan-26	16-Feb-26	26-May-26	Not Started
PRO-1110	Procure & Deliver Fire Detectors & Alarms	60	60	30-Sep-25	28-Nov-25	209			30-Sep-25	28-Nov-25	27-Apr-26	25-Jun-26	Not Started
PRO-1210	Procure & Deliver Signs	70	70	30-Sep-25	08-Dec-25	185			30-Sep-25	08-Dec-25	03-Apr-26	11-Jun-26	Not Started
PRO-1220	Procure & Deliver Windows & Storefronts	154	154	30-Sep-25	02-Mar-26	29			30-Sep-25	02-Mar-26	29-Oct-25	31-Mar-26	Not Started
PRO-1250	Procure & Deliver Plumbing Pipes	60	60	30-Sep-25	28-Nov-25	131			30-Sep-25	28-Nov-25	08-Feb-26	08-Apr-26	Not Started
PRO-1260	Procure & Deliver Electrical Wires & Conduits	130	130	30-Sep-25	06-Feb-26	32			30-Sep-25	06-Feb-26	01-Nov-25	10-Mar-26	Not Started
PRO-1270	Procure & Deliver Mechanical Pumps	70	70	30-Sep-25	08-Dec-25	262			30-Sep-25	08-Dec-25	19-Jun-26	27-Aug-26	Not Started
PRO-1280	Procure & Deliver Fire Protection Pumps	70	70	30-Sep-25	08-Dec-25	244			30-Sep-25	08-Dec-25	01-Jun-26	09-Aug-26	Not Started
PRO-1290	Procure & Deliver Plumbing	250	250	30-Sep-25	06-Jun-26	103			30-Sep-25	06-Jun-26	11-Jan-26	17-Sep-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
	Pumps												
PRO-1310	Procure & Deliver Telecommunication System	60	60	30-Sep-25	28-Nov-25	219			30-Sep-25	28-Nov-25	07-May-26	05-Jul-26	Not Started
PRO-1330	Procure & Deliver Cameras	60	60	30-Sep-25	28-Nov-25	219			30-Sep-25	28-Nov-25	07-May-26	05-Jul-26	Not Started
PRO-1360	Procure & Deliver Metal Panel Ceilings	120	120	30-Sep-25	27-Jan-26	198			30-Sep-25	27-Jan-26	16-Apr-26	13-Aug-26	Not Started
PRO-1380	Procure & Deliver Roof Dunnage	100	100	30-Sep-25	07-Jan-26	85			30-Sep-25	07-Jan-26	24-Dec-25	02-Apr-26	Not Started
PRO-1470	Procure & Deliver Cabinet Heaters	126	126	30-Sep-25	02-Feb-26	163			30-Sep-25	02-Feb-26	12-Mar-26	15-Jul-26	Not Started
PRO-1480	Procure & Deliver Chillers	170	170	30-Sep-25	18-Mar-26	515			30-Sep-25	18-Mar-26	27-Feb-27	15-Aug-27	Not Started
PRO-1490	Procure & Deliver Air Handling Units	250	250	30-Sep-25	06-Jun-26	8			30-Sep-25	06-Jun-26	08-Oct-25	14-Jun-26	Not Started
PRO-1500	Procure & Deliver Boilers	84	84	30-Sep-25	22-Dec-25	219			30-Sep-25	22-Dec-25	07-May-26	29-Jul-26	Not Started
PRO-1510	Procure & Deliver Emergency Generator	290	290	30-Sep-25	16-Jul-26	11			30-Sep-25	16-Jul-26	11-Oct-25	27-Jul-26	Not Started
PRO-1520	Procure & Deliver Switch Gears	250	250	30-Sep-25	06-Jun-26	17			30-Sep-25	06-Jun-26	17-Oct-25	23-Jun-26	Not Started
PRO-1530	Procure & Deliver Hydraulic Vertical Wheelchair Lift	90	90	30-Sep-25	28-Dec-25	234			30-Sep-25	28-Dec-25	22-May-26	19-Aug-26	Not Started
PRO-1560	Procure & Deliver Gymnasium Equipment	180	180	30-Sep-25	28-Mar-26	148			30-Sep-25	28-Mar-26	25-Feb-26	23-Aug-26	Not Started
CON-7740	Protection Of All Overhead & Underground Utilities	263	263	30-Sep-25	19-Oct-26	0			30-Sep-25	19-Oct-26	30-Sep-25	19-Oct-26	Not Started
CON-8030	Procurement From CON-ED For Temporary Electrical Power	20	20	30-Sep-25	19-Oct-25	241			30-Sep-25	19-Oct-25	29-May-26	17-Jun-26	Not Started
PRO-1570	Procure & Deliver Precast Sandwich Panels	112	112	30-Sep-25	19-Jan-26	64			30-Sep-25	19-Jan-26	03-Dec-25	24-Mar-26	Not Started
PRO-1580	Procure & Deliver Metal Deck	70	70	30-Sep-25	08-Dec-25	13			30-Sep-25	08-Dec-25	13-Oct-25	21-Dec-25	Not Started
PRO-1600	Procure & Deliver Trusses	60	60	30-Sep-25	28-Nov-25	159			30-Sep-25	28-Nov-25	08-Mar-26	06-May-26	Not Started
PRO-1610	Procure & Deliver Prefabricated Expansion Joint Covers	60	60	30-Sep-25	28-Nov-25	23			30-Sep-25	28-Nov-25	23-Oct-25	21-Dec-25	Not Started
PRO-1620	Procure & Deliver Security Screens & Barriers	60	60	30-Sep-25	28-Nov-25	276			30-Sep-25	28-Nov-25	03-Jul-26	31-Aug-26	Not Started
PRO-1630	Procure & Deliver Wood Flooring	120	120	30-Sep-25	27-Jan-26	170			30-Sep-25	27-Jan-26	19-Mar-26	16-Jul-26	Not Started
PRO-1640	Procure & Deliver Concrete Floating Floor Assembly	120	120	30-Sep-25	27-Jan-26	170			30-Sep-25	27-Jan-26	19-Mar-26	16-Jul-26	Not Started
PRO-1660	Procure & Deliver Auditorium Television Studio Dimming System	90	90	30-Sep-25	28-Dec-25	246			30-Sep-25	28-Dec-25	03-Jun-26	31-Aug-26	Not Started
MIL-1850	Construction Start	0	0	30-Sep-25		0			30-Sep-25		30-Sep-25		Not Started
CON-9000	Protection & Restoration the	263	263	30-Sep-25	19-Oct-26	186			30-Sep-25	19-Oct-26	30-Sep-25	13-Aug-27	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
	adjacent Properties to Original Condition												
PRO-2010	Procure & Deliver Steel Stairs Components	120	120	30-Sep-25	27-Jan-26	110			30-Sep-25	27-Jan-26	18-Jan-26	17-May-26	Not Started
PRO-2020	Procure & Deliver Flagpole	60	60	30-Sep-25	28-Nov-25	137			30-Sep-25	28-Nov-25	14-Feb-26	14-Apr-26	Not Started
PRO-2030	Procure & Deliver Bleachers	130	130	30-Sep-25	06-Feb-26	193			30-Sep-25	06-Feb-26	11-Apr-26	18-Aug-26	Not Started
PRO-2040	Procure & Deliver VAV Units	170	170	30-Sep-25	18-Mar-26	64			30-Sep-25	18-Mar-26	03-Dec-25	21-May-26	Not Started
PRO-2050	Procure & Deliver Furnitures (Owner Responsibility)	130	130	30-Sep-25	06-Feb-26	199			30-Sep-25	06-Feb-26	17-Apr-26	24-Aug-26	Not Started
MIL-1710	Complete Mobilization	0	0		03-Oct-25	0				03-Oct-25		03-Oct-25	Not Started
APP-2910	Review & Approve Backfill & Resue Plan	21	21	04-Oct-25	24-Oct-25	18			04-Oct-25	24-Oct-25	22-Oct-25	11-Nov-25	Not Started
CON-1080	Install Erosion Control Devices	2	2	06-Oct-25	07-Oct-25	5			06-Oct-25	07-Oct-25	13-Oct-25	15-Oct-25	Not Started
CON-1010	Install Construction Signs	2	2	06-Oct-25	07-Oct-25	5			06-Oct-25	07-Oct-25	13-Oct-25	15-Oct-25	Not Started
CON-1030	Install Construction Fences	2	2	06-Oct-25	07-Oct-25	5			06-Oct-25	07-Oct-25	13-Oct-25	15-Oct-25	Not Started
PRE-2610	Prepare & Submit FDNY Fuel Permit	10	10	06-Oct-25	20-Oct-25	191			06-Oct-25	20-Oct-25	14-Jul-26	27-Jul-26	Not Started
CON-9120	Soli Sampling	2	2	06-Oct-25	07-Oct-25	0			06-Oct-25	07-Oct-25	06-Oct-25	07-Oct-25	Not Started
CON-7750	Install Field Offices	5	5	08-Oct-25	15-Oct-25	169			08-Oct-25	15-Oct-25	12-Jun-26	18-Jun-26	Not Started
CON-9140	Excavation	5	5	08-Oct-25	15-Oct-25	0			08-Oct-25	15-Oct-25	08-Oct-25	15-Oct-25	Not Started
CON-9898	Install Gas Permeable Aggregate -1st Floor	3	3	16-Oct-25	20-Oct-25	0			16-Oct-25	20-Oct-25	16-Oct-25	20-Oct-25	Not Started
CON-98947	Install 4" slotted schedule 80 PVC Piping -1st Floor	3	3	16-Oct-25	20-Oct-25	0			16-Oct-25	20-Oct-25	16-Oct-25	20-Oct-25	Not Started
CON-8040	CON-ED Work For Temporary Electrical Power	10	10	20-Oct-25	31-Oct-25	166			20-Oct-25	31-Oct-25	18-Jun-26	02-Jul-26	Not Started
PRE-2620	Review & Approve FDNY Fuel Permit	21	21	21-Oct-25	10-Nov-25	280			21-Oct-25	10-Nov-25	28-Jul-26	17-Aug-26	Not Started
CON-9888	Install Liquid Boot VI-20 Geomembrane -1st Floor	2	2	21-Oct-25	22-Oct-25	0			21-Oct-25	22-Oct-25	21-Oct-25	22-Oct-25	Not Started
CON-1020	Install 60 Dry MILS Liquid Boot -1st Floor	3	3	23-Oct-25	27-Oct-25	0			23-Oct-25	27-Oct-25	23-Oct-25	27-Oct-25	Not Started
CON-9777	Install Liquid Ultrashield G-1000 -1st Floor	2	2	24-Oct-25	27-Oct-25	0			24-Oct-25	27-Oct-25	24-Oct-25	27-Oct-25	Not Started
CON-1040	F/R/P Concrete Walls & Beams -1st Floor	10	10	28-Oct-25	10-Nov-25	0			28-Oct-25	10-Nov-25	28-Oct-25	10-Nov-25	Not Started
I-1010	Concrete Cast-IN-Place Inspection	86	86	28-Oct-25	04-Mar-26	0			28-Oct-25	04-Mar-26	28-Oct-25	04-Mar-26	Not Started
MIL-2582	Start Concrete Placement	0	0	28-Oct-25		0			28-Oct-25		28-Oct-25		Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
MIL-2812	Start Foundation	0	0	28-Oct-25		0			28-Oct-25		28-Oct-25		Not Started
MIL-2912	Start Concrete Cast In Place Inspection	0	0	28-Oct-25		430			28-Oct-25		13-Aug-27		Not Started
CON-8050	Available Temporary Electrical Power For Testing MEP Equipment	0	0		31-Oct-25	166				31-Oct-25		02-Jul-26	Not Started
CON-1050	Install Underground Conduits & Wires -1st Floor	6	6	12-Nov-25	19-Nov-25	0			12-Nov-25	19-Nov-25	12-Nov-25	19-Nov-25	Not Started
CON-1060	Backfilling & Compaction -1st Floor	6	6	12-Nov-25	19-Nov-25	0			12-Nov-25	19-Nov-25	12-Nov-25	19-Nov-25	Not Started
CON-1070	F/R/P SOG -1st Floor	10	10	20-Nov-25	04-Dec-25	0			20-Nov-25	04-Dec-25	20-Nov-25	04-Dec-25	Not Started
CON-4920	Install Floor Drains & Clean-outs -1st Floor	5	5	27-Nov-25	04-Dec-25	173			27-Nov-25	04-Dec-25	07-Aug-26	13-Aug-26	Not Started
CON-99327	Install Lightning Protection System-1st Floor	2	2	03-Dec-25	04-Dec-25	97			03-Dec-25	04-Dec-25	23-Apr-26	24-Apr-26	Not Started
CON-98787	Install Steel Columns -1st Floor	7	7	05-Dec-25	15-Dec-25	0			05-Dec-25	15-Dec-25	05-Dec-25	15-Dec-25	Not Started
MIL-1810	Crane Mobilization-Steel Installation start	0	0	05-Dec-25		0			05-Dec-25		05-Dec-25		Not Started
I-1140	Structural Steel Inspection	58	58	05-Dec-25	02-Mar-26	0			05-Dec-25	02-Mar-26	05-Dec-25	02-Mar-26	Not Started
PRO-1450	Procure & Deliver Playground Equipment	60	60	09-Dec-25	06-Feb-26	185			09-Dec-25	06-Feb-26	12-Jun-26	10-Aug-26	Not Started
CON-1090	Install Trusses -1st Floor	3	3	16-Dec-25	18-Dec-25	98			16-Dec-25	18-Dec-25	07-May-26	11-May-26	Not Started
CON-1100	Install Framing Beams -1st Floor	4	4	16-Dec-25	19-Dec-25	0			16-Dec-25	19-Dec-25	16-Dec-25	19-Dec-25	Not Started
CON-3160	Install Floor Drains & Clean-outs -2nd Floor	5	5	19-Dec-25	26-Dec-25	104			19-Dec-25	26-Dec-25	20-May-26	27-May-26	Not Started
CON-1110	Install Metal Deck Slab -2nd Floor	4	4	22-Dec-25	26-Dec-25	0			22-Dec-25	26-Dec-25	22-Dec-25	26-Dec-25	Not Started
CON-1130	Install MEP Hangers & Sleeves-2nd Floor	4	4	22-Dec-25	26-Dec-25	34			22-Dec-25	26-Dec-25	11-Feb-26	17-Feb-26	Not Started
MIL-1120	Metal Decking Start	0	0	22-Dec-25		0			22-Dec-25		22-Dec-25		Not Started
CON-1150	Install Steel Canopy Framing -2nd Floor	5	5	29-Dec-25	05-Jan-26	177			29-Dec-25	05-Jan-26	11-Sep-26	17-Sep-26	Not Started
CON-1160	Hoist Material Design	10	10	29-Dec-25	12-Jan-26	110			29-Dec-25	12-Jan-26	05-Jun-26	18-Jun-26	Not Started
CON-8390	Install Sidewalk Sheds -South Elevation	4	4	29-Dec-25	02-Jan-26	120			29-Dec-25	02-Jan-26	22-Jun-26	25-Jun-26	Not Started
CON-8400	Install Sidewalk Sheds -East Elevation	4	4	29-Dec-25	02-Jan-26	120			29-Dec-25	02-Jan-26	22-Jun-26	25-Jun-26	Not Started
MIL-1720	Start Sidewalk Bridge Installations	0	0	29-Dec-25		120			29-Dec-25		22-Jun-26		Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-1170	Install Steel Columns -2nd Floor	3	3	29-Dec-25	31-Dec-25	0			29-Dec-25	31-Dec-25	29-Dec-25	31-Dec-25	Not Started
I-1080	Standpipe System Inspection	111	111	29-Dec-25	05-Jun-26	8			29-Dec-25	05-Jun-26	21-May-26	17-Jun-26	Not Started
CON-3270	Install Temporary Standpipe	9	9	29-Dec-25	09-Jan-26	100			29-Dec-25	09-Jan-26	21-May-26	03-Jun-26	Not Started
CON-1190	Install Trusses -2nd Floor	4	4	02-Jan-26	07-Jan-26	103			02-Jan-26	07-Jan-26	01-Jun-26	04-Jun-26	Not Started
CON-1200	Install Framing Beams -2nd Floor	5	5	02-Jan-26	08-Jan-26	0			02-Jan-26	08-Jan-26	02-Jan-26	08-Jan-26	Not Started
CON-3320	Install Floor Drains & Clean-outs -3rd Floor	5	5	08-Jan-26	14-Jan-26	97			08-Jan-26	14-Jan-26	28-May-26	03-Jun-26	Not Started
CON-1230	Install MEP Hangers & Sleeves-3rd Floor	4	4	09-Jan-26	14-Jan-26	26			09-Jan-26	14-Jan-26	18-Feb-26	23-Feb-26	Not Started
CON-1210	Install Metal Deck Slab - 3rd Floor	4	4	09-Jan-26	14-Jan-26	0			09-Jan-26	14-Jan-26	09-Jan-26	14-Jan-26	Not Started
CON-1250	Approval of Hoist Design	7	7	13-Jan-26	19-Jan-26	157			13-Jan-26	19-Jan-26	19-Jun-26	25-Jun-26	Not Started
CON-1240	Install Steel Columns - 3rd Floor	4	4	15-Jan-26	21-Jan-26	0			15-Jan-26	21-Jan-26	15-Jan-26	21-Jan-26	Not Started
CON-1280	Install Elevator Hoist Pad	5	5	20-Jan-26	26-Jan-26	110			20-Jan-26	26-Jan-26	26-Jun-26	02-Jul-26	Not Started
CON-1260	Install Trusses - 3rd Floor	3	3	22-Jan-26	26-Jan-26	94			22-Jan-26	26-Jan-26	05-Jun-26	09-Jun-26	Not Started
CON-1270	Install Framing Beams - 3rd Floor	5	5	22-Jan-26	28-Jan-26	0			22-Jan-26	28-Jan-26	22-Jan-26	28-Jan-26	Not Started
CON-1320	Erect Material Hoist	5	5	27-Jan-26	02-Feb-26	110			27-Jan-26	02-Feb-26	06-Jul-26	10-Jul-26	Not Started
CON-3530	Install Floor Drains & Clean-outs -4th Floor	5	5	28-Jan-26	03-Feb-26	89			28-Jan-26	03-Feb-26	04-Jun-26	10-Jun-26	Not Started
CON-99277	Install Steel Stairs -1st Floor	7	7	28-Jan-26	05-Feb-26	77			28-Jan-26	05-Feb-26	18-May-26	27-May-26	Not Started
CON-1310	Install MEP Hangers & Sleeves-4th Floor	4	4	29-Jan-26	03-Feb-26	25			29-Jan-26	03-Feb-26	06-Mar-26	11-Mar-26	Not Started
CON-1290	Install Metal Deck Slab - 4th Floor	4	4	29-Jan-26	03-Feb-26	0			29-Jan-26	03-Feb-26	29-Jan-26	03-Feb-26	Not Started
CON-1330	Install Steel Columns - 4th Floor	4	4	04-Feb-26	09-Feb-26	0			04-Feb-26	09-Feb-26	04-Feb-26	09-Feb-26	Not Started
CON-99287	Install Steel Stairs -2nd Floor	3	3	06-Feb-26	10-Feb-26	77			06-Feb-26	10-Feb-26	28-May-26	01-Jun-26	Not Started
MIL-2622	Deliveries of all owner-furnished equipment and/or materials	0	0		06-Feb-26	137				06-Feb-26		24-Aug-26	Not Started
CON-1360	Install Trusses - 4th Floor	3	3	10-Feb-26	12-Feb-26	84			10-Feb-26	12-Feb-26	10-Jun-26	12-Jun-26	Not Started
CON-1370	Install Framing Beams - 4th Floor	5	5	10-Feb-26	17-Feb-26	0			10-Feb-26	17-Feb-26	10-Feb-26	17-Feb-26	Not Started
CON-99297	Install Steel Stairs- 3rd Floor	4	4	11-Feb-26	17-Feb-26	77			11-Feb-26	17-Feb-26	02-Jun-26	05-Jun-26	Not Started
CON-3610	Install Floor Drains & Clean-outs -5th Floor	5	5	13-Feb-26	20-Feb-26	82			13-Feb-26	20-Feb-26	11-Jun-26	17-Jun-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-1400	Install MEP Hangers & Sleeves-5th Floor	4	4	17-Feb-26	20-Feb-26	23			17-Feb-26	20-Feb-26	20-Mar-26	25-Mar-26	Not Started
CON-1380	Install Metal Deck Slab - 5th Floor	3	3	18-Feb-26	20-Feb-26	0			18-Feb-26	20-Feb-26	18-Feb-26	20-Feb-26	Not Started
CON-1410	Install Duct Risers-2nd Floor	1	1	23-Feb-26	23-Feb-26	0			23-Feb-26	23-Feb-26	23-Feb-26	23-Feb-26	Not Started
CON-1420	Layout -2nd Floor	3	3	23-Feb-26	25-Feb-26	52			23-Feb-26	25-Feb-26	06-May-26	08-May-26	Not Started
MIL-1140	Layout Start	0	0	23-Feb-26		52			23-Feb-26		06-May-26		Not Started
MIL-1150	Masonry Walls Start	0	0	23-Feb-26		74			23-Feb-26		08-Jun-26		Not Started
MIL-1180	MEP Risers Start	0	0	23-Feb-26		0			23-Feb-26		23-Feb-26		Not Started
CON-1430	Install Unit Masonry Mock-Up	1	1	23-Feb-26	23-Feb-26	74			23-Feb-26	23-Feb-26	08-Jun-26	08-Jun-26	Not Started
CON-1440	Install Steel Columns - 5th Floor	3	3	23-Feb-26	25-Feb-26	0			23-Feb-26	25-Feb-26	23-Feb-26	25-Feb-26	Not Started
CON-1460	F/R/P Piers - 5th Floor	5	5	23-Feb-26	27-Feb-26	86			23-Feb-26	27-Feb-26	25-Jun-26	01-Jul-26	Not Started
CON-99307	Install Steel Stairs - 4th Floor	4	4	23-Feb-26	26-Feb-26	74			23-Feb-26	26-Feb-26	08-Jun-26	11-Jun-26	Not Started
CON-1480	Rough-in Duct Work -2nd Floor	4	4	24-Feb-26	27-Feb-26	0			24-Feb-26	27-Feb-26	24-Feb-26	27-Feb-26	Not Started
CON-1490	Install Duct Risers -3rd Floor	2	2	24-Feb-26	25-Feb-26	8			24-Feb-26	25-Feb-26	06-Mar-26	09-Mar-26	Not Started
CON-1500	Install Mechanical Piping Risers-2nd Floor	2	2	24-Feb-26	25-Feb-26	28			24-Feb-26	25-Feb-26	03-Apr-26	06-Apr-26	Not Started
MIL-1210	Duct Rough-ins Start	0	0	24-Feb-26		0			24-Feb-26		24-Feb-26		Not Started
CON-1510	Duct Leak Test -2nd Floor	2	2	24-Feb-26	25-Feb-26	8			24-Feb-26	25-Feb-26	06-Mar-26	09-Mar-26	Not Started
CON-1470	Approve Unit Masonry Mock-Up	4	4	24-Feb-26	27-Feb-26	74			24-Feb-26	27-Feb-26	09-Jun-26	12-Jun-26	Not Started
CON-1560	Install Duct Risers -4th Floor	2	2	26-Feb-26	27-Feb-26	13			26-Feb-26	27-Feb-26	17-Mar-26	18-Mar-26	Not Started
CON-1520	Install Top & Bottom Track-2nd Floor	4	4	26-Feb-26	03-Mar-26	52			26-Feb-26	03-Mar-26	11-May-26	14-May-26	Not Started
CON-1530	Layout -3rd Floor	3	3	26-Feb-26	02-Mar-26	53			26-Feb-26	02-Mar-26	12-May-26	14-May-26	Not Started
CON-1770	Install Roof Drains & Clean outs -Roof Floor	5	5	26-Feb-26	04-Mar-26	79			26-Feb-26	04-Mar-26	18-Jun-26	25-Jun-26	Not Started
CON-1580	Install Plumbing Risers -2nd Floor	2	2	26-Feb-26	27-Feb-26	28			26-Feb-26	27-Feb-26	07-Apr-26	08-Apr-26	Not Started
CON-1590	Install Mechanical Piping Risers -3rd Floor	2	2	26-Feb-26	27-Feb-26	30			26-Feb-26	27-Feb-26	09-Apr-26	10-Apr-26	Not Started
MIL-1160	Top & Bottom Track Start	0	0	26-Feb-26		52			26-Feb-26		11-May-26		Not Started
CON-1600	Duct Leak Test -3rd Floor	2	2	26-Feb-26	27-Feb-26	8			26-Feb-26	27-Feb-26	10-Mar-26	11-Mar-26	Not Started
CON-1540	Install Trusses - 5th Floor	2	2	26-Feb-26	27-Feb-26	76			26-Feb-26	27-Feb-26	15-Jun-26	16-Jun-26	Not Started
CON-1550	Install Framing Beams - 5th Floor	3	3	26-Feb-26	02-Mar-26	0			26-Feb-26	02-Mar-26	26-Feb-26	02-Mar-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-1610	Install MEP Hangers & Sleeves-Roof Floor	4	4	27-Feb-26	04-Mar-26	19			27-Feb-26	04-Mar-26	26-Mar-26	31-Mar-26	Not Started
CON-99317	Install Steel Stairs - 5th Floor	3	3	27-Feb-26	03-Mar-26	74			27-Feb-26	03-Mar-26	12-Jun-26	16-Jun-26	Not Started
CON-1850	Rough-in Hot Water Piping-2nd Floor	7	7	02-Mar-26	10-Mar-26	44			02-Mar-26	10-Mar-26	01-May-26	11-May-26	Not Started
CON-1860	Rough-in Hot Glycol Piping-2nd Floor	7	7	02-Mar-26	10-Mar-26	66			02-Mar-26	10-Mar-26	03-Jun-26	11-Jun-26	Not Started
CON-1870	Rough-in Chilled Glycol Piping-2nd Floor	7	7	02-Mar-26	10-Mar-26	6			02-Mar-26	10-Mar-26	10-Mar-26	18-Mar-26	Not Started
CON-1880	Rough-in Refrigerant Piping-2nd Floor	7	7	02-Mar-26	10-Mar-26	0			02-Mar-26	10-Mar-26	02-Mar-26	10-Mar-26	Not Started
CON-1890	Rough-in Duct Work -3rd Floor	5	5	02-Mar-26	06-Mar-26	8			02-Mar-26	06-Mar-26	12-Mar-26	18-Mar-26	Not Started
CON-1630	Install Duct Risers-5th Floor	2	2	02-Mar-26	03-Mar-26	19			02-Mar-26	03-Mar-26	27-Mar-26	30-Mar-26	Not Started
CON-1570	Install CMU Walls -2nd Floor	3	3	02-Mar-26	04-Mar-26	80			02-Mar-26	04-Mar-26	24-Jun-26	26-Jun-26	Not Started
CON-1680	Install Plumbing Risers -3rd Floor	2	2	02-Mar-26	03-Mar-26	30			02-Mar-26	03-Mar-26	13-Apr-26	14-Apr-26	Not Started
CON-1690	Install Mechanical Piping Risers -4th Floor	2	2	02-Mar-26	03-Mar-26	38			02-Mar-26	03-Mar-26	23-Apr-26	24-Apr-26	Not Started
CON-1700	Duct Leak Test -4th Floor	2	2	02-Mar-26	03-Mar-26	13			02-Mar-26	03-Mar-26	19-Mar-26	20-Mar-26	Not Started
CON-1710	Install Power Risers-2nd Floor	2	2	02-Mar-26	03-Mar-26	87			02-Mar-26	03-Mar-26	06-Jul-26	07-Jul-26	Not Started
CON-1740	Install SSDS Risers -SSDS System -2nd Floor	2	2	02-Mar-26	03-Mar-26	36			02-Mar-26	03-Mar-26	21-Apr-26	22-Apr-26	Not Started
I-1020	Masonry Inspection	32	32	02-Mar-26	14-Apr-26	45			02-Mar-26	14-Apr-26	17-Jun-26	17-Jun-26	Not Started
CON-1620	Install Dunnage - 5th Floor	8	8	02-Mar-26	11-Mar-26	86			02-Mar-26	11-Mar-26	02-Jul-26	14-Jul-26	Not Started
CON-1670	Layout -4th Floor	3	3	03-Mar-26	05-Mar-26	54			03-Mar-26	05-Mar-26	18-May-26	20-May-26	Not Started
CON-1720	Install Metal Deck Slab -Roof Floor	2	2	03-Mar-26	04-Mar-26	0			03-Mar-26	04-Mar-26	03-Mar-26	04-Mar-26	Not Started
CON-1180	Spray Fireproofing - 1st Floor	5	5	03-Mar-26	09-Mar-26	50			03-Mar-26	09-Mar-26	12-May-26	18-May-26	Not Started
I-1100	Fire-Resistant Penetrations And Joints Inspection	87	87	03-Mar-26	06-Jul-26	10			03-Mar-26	06-Jul-26	12-May-26	20-Jul-26	Not Started
CON-1640	Install Wall Steel Studs & Framing-2nd Floor	5	5	04-Mar-26	10-Mar-26	52			04-Mar-26	10-Mar-26	15-May-26	21-May-26	Not Started
CON-1650	Install Top & Bottom Track-3rd Floor	4	4	04-Mar-26	09-Mar-26	52			04-Mar-26	09-Mar-26	15-May-26	20-May-26	Not Started
CON-1780	Install Plumbing Risers -4th Floor	2	2	04-Mar-26	05-Mar-26	38			04-Mar-26	05-Mar-26	27-Apr-26	28-Apr-26	Not Started
CON-1790	Install Mechanical Piping Risers-5th Floor	2	2	04-Mar-26	05-Mar-26	42			04-Mar-26	05-Mar-26	01-May-26	04-May-26	Not Started
CON-1800	Install Low Voltage Risers-2nd Floor	2	2	04-Mar-26	05-Mar-26	88			04-Mar-26	05-Mar-26	09-Jul-26	10-Jul-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-1810	Duct Leak Test -5th Floor	1	1	04-Mar-26	04-Mar-26	19			04-Mar-26	04-Mar-26	31-Mar-26	31-Mar-26	Not Started
CON-1820	Install Power Risers-3rd Floor	2	2	04-Mar-26	05-Mar-26	87			04-Mar-26	05-Mar-26	08-Jul-26	09-Jul-26	Not Started
CON-1840	Install SSDS Risers -SSDS System -3rd Floor	2	2	04-Mar-26	05-Mar-26	36			04-Mar-26	05-Mar-26	23-Apr-26	24-Apr-26	Not Started
CON-1750	F/R/P Concrete Columns -Bulkhead	3	3	05-Mar-26	09-Mar-26	50			05-Mar-26	09-Mar-26	14-May-26	18-May-26	Not Started
CON-1760	Install Dunnage-Roof Floor	8	8	05-Mar-26	16-Mar-26	21			05-Mar-26	16-Mar-26	03-Apr-26	14-Apr-26	Not Started
CON-1660	Install CMU Walls -3rd Floor	3	3	05-Mar-26	09-Mar-26	80			05-Mar-26	09-Mar-26	29-Jun-26	01-Jul-26	Not Started
CON-1830	Install Insulated Precast Concrete Sandwich Panel - Mock Up	2	2	05-Mar-26	06-Mar-26	0			05-Mar-26	06-Mar-26	05-Mar-26	06-Mar-26	Not Started
CON-2070	Install Roof Drains & Clean outs - Mechanical Work - Roof Bulkhead	5	5	05-Mar-26	11-Mar-26	79			05-Mar-26	11-Mar-26	26-Jun-26	02-Jul-26	Not Started
MIL-1830	Crane Mobilization-Precast Sandwich Panels Installation Start	0	0	05-Mar-26		0			05-Mar-26		05-Mar-26		Not Started
CON-99347	Install Lightning Protection System - Roof Floor	6	6	05-Mar-26	12-Mar-26	65			05-Mar-26	12-Mar-26	05-Jun-26	12-Jun-26	Not Started
MIL-2932	Start Masonry Inspection	0	0	05-Mar-26		80			05-Mar-26		29-Jun-26		Not Started
CON-1930	Layout -5th Floor	3	3	06-Mar-26	10-Mar-26	56			06-Mar-26	10-Mar-26	26-May-26	28-May-26	Not Started
CON-1940	Install Plumbing Risers-5th Floor	1	1	06-Mar-26	06-Mar-26	42			06-Mar-26	06-Mar-26	05-May-26	05-May-26	Not Started
CON-1950	Install Low Voltage Risers-3rd Floor	2	2	06-Mar-26	09-Mar-26	88			06-Mar-26	09-Mar-26	13-Jul-26	14-Jul-26	Not Started
CON-1960	Install Power Risers-4th Floor	2	2	06-Mar-26	09-Mar-26	87			06-Mar-26	09-Mar-26	10-Jul-26	13-Jul-26	Not Started
CON-1970	Install SSDS Risers -SSDS System -4th Floor	2	2	06-Mar-26	09-Mar-26	36			06-Mar-26	09-Mar-26	27-Apr-26	28-Apr-26	Not Started
CON-2160	Rough-in Refrigerant Piping-3rd Floor	7	7	09-Mar-26	17-Mar-26	20			09-Mar-26	17-Mar-26	06-Apr-26	14-Apr-26	Not Started
CON-2170	Rough-in Duct Work -4th Floor	5	5	09-Mar-26	13-Mar-26	10			09-Mar-26	13-Mar-26	23-Mar-26	27-Mar-26	Not Started
CON-1990	Approve Insulated Precast Concrete Sandwich Panel - Mock Up	2	2	09-Mar-26	10-Mar-26	0			09-Mar-26	10-Mar-26	09-Mar-26	10-Mar-26	Not Started
CON-2000	Install SSDS Risers -SSDS System -5th Floor	1	1	09-Mar-26	09-Mar-26	122			09-Mar-26	09-Mar-26	31-Aug-26	31-Aug-26	Not Started
CON-1980	F/R/P Bulkhead Slab -Bulkhead	2	2	10-Mar-26	11-Mar-26	50			10-Mar-26	11-Mar-26	19-May-26	20-May-26	Not Started
CON-1900	Install Wall Steel Studs & Framing-3rd Floor	5	5	10-Mar-26	16-Mar-26	56			10-Mar-26	16-Mar-26	28-May-26	03-Jun-26	Not Started
CON-1910	Install Top & Bottom Track-4th Floor	4	4	10-Mar-26	13-Mar-26	52			10-Mar-26	13-Mar-26	21-May-26	27-May-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-1920	Install CMU Walls -4th Floor	3	3	10-Mar-26	12-Mar-26	80			10-Mar-26	12-Mar-26	02-Jul-26	07-Jul-26	Not Started
CON-2040	Install Low Voltage Risers-4th Floor	2	2	10-Mar-26	11-Mar-26	88			10-Mar-26	11-Mar-26	15-Jul-26	16-Jul-26	Not Started
CON-2050	Install Power Risers-5th Floor	3	3	10-Mar-26	12-Mar-26	87			10-Mar-26	12-Mar-26	14-Jul-26	16-Jul-26	Not Started
CON-1220	Spray Fireproofing - 2nd Floor	5	5	10-Mar-26	16-Mar-26	50			10-Mar-26	16-Mar-26	19-May-26	26-May-26	Not Started
CON-2130	Rough-in Hot Water Piping-3rd Floor	7	7	11-Mar-26	19-Mar-26	44			11-Mar-26	19-Mar-26	12-May-26	20-May-26	Not Started
CON-2140	Rough-in Hot Glycol Piping-3rd Floor	7	7	11-Mar-26	19-Mar-26	66			11-Mar-26	19-Mar-26	12-Jun-26	23-Jun-26	Not Started
CON-2150	Rough-in Chilled Glycol Piping-3rd Floor	7	7	11-Mar-26	19-Mar-26	6			11-Mar-26	19-Mar-26	19-Mar-26	27-Mar-26	Not Started
CON-2180	Rough-in Power Conduits -2nd Floor	6	6	11-Mar-26	18-Mar-26	0			11-Mar-26	18-Mar-26	11-Mar-26	18-Mar-26	Not Started
CON-2110	Install & Windows Mock-Up	3	3	11-Mar-26	13-Mar-26	0			11-Mar-26	13-Mar-26	11-Mar-26	13-Mar-26	Not Started
MIL-1170	Finish Concrete Work	0	0		11-Mar-26	84				11-Mar-26		10-Jul-26	Not Started
CON-2060	Install Hoist Beam-Bulkhead	1	1	12-Mar-26	12-Mar-26	50			12-Mar-26	12-Mar-26	21-May-26	21-May-26	Not Started
CON-2190	Install Electric Unit Heater EUH - Mechanical Work - Roof Bulkhead	5	5	12-Mar-26	18-Mar-26	79			12-Mar-26	18-Mar-26	06-Jul-26	10-Jul-26	Not Started
MIL-1820	Crane Mobilization-Steel Installation Finish	0	0		12-Mar-26	131				12-Mar-26		17-Sep-26	Not Started
CON-2030	Install CMU Walls -5th Floor	3	3	13-Mar-26	17-Mar-26	80			13-Mar-26	17-Mar-26	08-Jul-26	10-Jul-26	Not Started
CON-2100	Install Low Voltage Risers-5th Floor	3	3	13-Mar-26	17-Mar-26	87			13-Mar-26	17-Mar-26	17-Jul-26	21-Jul-26	Not Started
CON-99337	Install Lightning Protection system -5th Floor	3	3	13-Mar-26	17-Mar-26	87			13-Mar-26	17-Mar-26	17-Jul-26	21-Jul-26	Not Started
CON-2290	Rough-in Refrigerant Piping-4th Floor	7	7	16-Mar-26	24-Mar-26	25			16-Mar-26	24-Mar-26	20-Apr-26	28-Apr-26	Not Started
CON-2300	Rough-in Duct Work-5th Floor	5	5	16-Mar-26	20-Mar-26	12			16-Mar-26	20-Mar-26	01-Apr-26	07-Apr-26	Not Started
CON-2010	Install Wall Steel Studs & Framing-4th Floor	5	5	16-Mar-26	20-Mar-26	52			16-Mar-26	20-Mar-26	28-May-26	03-Jun-26	Not Started
CON-2020	Install Top & Bottom Track-5th Floor	4	4	16-Mar-26	19-Mar-26	53			16-Mar-26	19-Mar-26	29-May-26	03-Jun-26	Not Started
CON-2310	Install Ceiling Hangers & Supports-2nd Floor	4	4	16-Mar-26	19-Mar-26	52			16-Mar-26	19-Mar-26	28-May-26	02-Jun-26	Not Started
CON-2210	Approve Windows Mock-Up	2	2	16-Mar-26	17-Mar-26	0			16-Mar-26	17-Mar-26	16-Mar-26	17-Mar-26	Not Started
MIL-2612	Start Suspended Ceiling Grid	0	0	16-Mar-26		52			16-Mar-26		28-May-26		Not Started
CON-2120	Install Air Cooled Chiller CH-1 -Roof Floor	7	7	17-Mar-26	25-Mar-26	56			17-Mar-26	25-Mar-26	04-Jun-26	12-Jun-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
MIL-1380	Crane Mobilization-Mechanical Subcontractor	78	78	17-Mar-26	07-Jul-26	33			17-Mar-26	07-Jul-26	15-Apr-26	21-Aug-26	Not Started
CON-1300	Spray Fireproofing - 3rd Floor	5	5	17-Mar-26	23-Mar-26	55			17-Mar-26	23-Mar-26	03-Jun-26	09-Jun-26	Not Started
CON-2220	Install Storefront System Mock-Up	3	3	18-Mar-26	20-Mar-26	0			18-Mar-26	20-Mar-26	18-Mar-26	20-Mar-26	Not Started
CON-3980	Install VAV Boxes & Sound Attenuator Devices-2nd Floor	5	5	19-Mar-26	25-Mar-26	46			19-Mar-26	25-Mar-26	22-May-26	29-May-26	Not Started
CON-2320	Rough-in Power Conduits-3rd Floor	6	6	19-Mar-26	26-Mar-26	26			19-Mar-26	26-Mar-26	24-Apr-26	01-May-26	Not Started
CON-2330	Rough-in Low-Voltage Conduits -2nd Floor	6	6	19-Mar-26	26-Mar-26	0			19-Mar-26	26-Mar-26	19-Mar-26	26-Mar-26	Not Started
CON-2340	Power Wires Pulling -2nd Floor	6	6	19-Mar-26	26-Mar-26	3			19-Mar-26	26-Mar-26	24-Mar-26	31-Mar-26	Not Started
CON-2230	Install Emergency Generator -Bulkhead	7	7	19-Mar-26	27-Mar-26	79			19-Mar-26	27-Mar-26	13-Jul-26	21-Jul-26	Not Started
CON-2260	Rough-in Hot Water Piping-4th Floor	7	7	20-Mar-26	30-Mar-26	44			20-Mar-26	30-Mar-26	21-May-26	01-Jun-26	Not Started
CON-2270	Rough-in Hot Glycol Piping-4th Floor	7	7	20-Mar-26	30-Mar-26	66			20-Mar-26	30-Mar-26	24-Jun-26	02-Jul-26	Not Started
CON-2280	Rough-in Chilled Glycol Piping-4th Floor	7	7	20-Mar-26	30-Mar-26	6			20-Mar-26	30-Mar-26	30-Mar-26	07-Apr-26	Not Started
CON-2390	Install Ceiling Hangers & Supports-3rd Floor	4	4	20-Mar-26	25-Mar-26	54			20-Mar-26	25-Mar-26	05-Jun-26	10-Jun-26	Not Started
CON-2470	Rough-in Refrigerant Piping-5th Floor	7	7	23-Mar-26	31-Mar-26	25			23-Mar-26	31-Mar-26	27-Apr-26	05-May-26	Not Started
CON-2200	Install Wall Steel Studs & Framing-5th Floor	5	5	23-Mar-26	27-Mar-26	52			23-Mar-26	27-Mar-26	04-Jun-26	10-Jun-26	Not Started
CON-2240	Approve Storefront System Mock-Up	2	2	23-Mar-26	24-Mar-26	0			23-Mar-26	24-Mar-26	23-Mar-26	24-Mar-26	Not Started
CON-1390	Spray Fireproofing - 4th Floor	5	5	24-Mar-26	30-Mar-26	55			24-Mar-26	30-Mar-26	10-Jun-26	16-Jun-26	Not Started
CON-2380	Install Insulated Precast Concrete Sandwich Panel - West Elevation	3	3	25-Mar-26	27-Mar-26	0			25-Mar-26	27-Mar-26	25-Mar-26	27-Mar-26	Not Started
CON-2420	Install Insulated Precast Concrete Sandwich Panel - South Elevation	5	5	25-Mar-26	31-Mar-26	0			25-Mar-26	31-Mar-26	25-Mar-26	31-Mar-26	Not Started
I-1150	Concrete Precast Inspection	9	9	25-Mar-26	06-Apr-26	0			25-Mar-26	06-Apr-26	25-Mar-26	06-Apr-26	Not Started
MIL-2922	Start Pre -Cast Concrete Inspection	0	0	25-Mar-26		330			25-Mar-26		13-Aug-27		Not Started
CON-4140	Install VAV Boxes & Sound Attenuator Devices-3rd Floor	5	5	26-Mar-26	01-Apr-26	46			26-Mar-26	01-Apr-26	01-Jun-26	05-Jun-26	Not Started
CON-2550	Install Ceiling Hangers & Supports-4th Floor	4	4	26-Mar-26	31-Mar-26	58			26-Mar-26	31-Mar-26	17-Jun-26	23-Jun-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-2350	Install Air Cooled Chiller CH-2 -Roof Floor	7	7	26-Mar-26	03-Apr-26	69			26-Mar-26	03-Apr-26	06-Jul-26	14-Jul-26	Not Started
CON-2360	Install Smoke Purge Fan SPF - Mechanical Work - Roof Bulkhead	3	3	26-Mar-26	30-Mar-26	119			26-Mar-26	30-Mar-26	15-Sep-26	17-Sep-26	Not Started
CON-2640	Install Grounding Bars - 3rd Floor IDF Room	5	5	27-Mar-26	02-Apr-26	0			27-Mar-26	02-Apr-26	27-Mar-26	02-Apr-26	Not Started
CON-2480	Rough-in Power Conduits-4th Floor	6	6	27-Mar-26	03-Apr-26	26			27-Mar-26	03-Apr-26	04-May-26	11-May-26	Not Started
CON-2490	Low Voltage Wires Pulling -2nd Floor	6	6	27-Mar-26	03-Apr-26	3			27-Mar-26	03-Apr-26	01-Apr-26	08-Apr-26	Not Started
CON-2500	Rough-in Low-Voltage Conduits-3rd Floor	6	6	27-Mar-26	03-Apr-26	35			27-Mar-26	03-Apr-26	15-May-26	22-May-26	Not Started
CON-2510	Power Wires Pulling-3rd Floor	6	6	27-Mar-26	03-Apr-26	26			27-Mar-26	03-Apr-26	04-May-26	11-May-26	Not Started
CON-2520	Install Voice Rack - 2nd Floor -IDF Room	10	10	27-Mar-26	09-Apr-26	50			27-Mar-26	09-Apr-26	08-Jun-26	22-Jun-26	Not Started
CON-2530	Install Data Rack - 2nd Floor -IDF Room	10	10	27-Mar-26	09-Apr-26	50			27-Mar-26	09-Apr-26	08-Jun-26	22-Jun-26	Not Started
CON-2540	Install Ground Bus Bar - 2nd Floor -IDF Room	10	10	27-Mar-26	09-Apr-26	0			27-Mar-26	09-Apr-26	27-Mar-26	09-Apr-26	Not Started
CON-2400	Install Windows -West Elevation	5	5	30-Mar-26	03-Apr-26	2			30-Mar-26	03-Apr-26	01-Apr-26	07-Apr-26	Not Started
CON-2410	Install Storefront System-West Elevation	5	5	30-Mar-26	03-Apr-26	115			30-Mar-26	03-Apr-26	11-Sep-26	17-Sep-26	Not Started
MIL-1740	Start Windows	0	0	30-Mar-26		2			30-Mar-26		01-Apr-26		Not Started
CON-2440	Rough-in Hot Water Piping-5th Floor	7	7	31-Mar-26	08-Apr-26	44			31-Mar-26	08-Apr-26	02-Jun-26	10-Jun-26	Not Started
CON-2450	Rough-in Hot Glycol Piping-5th Floor	7	7	31-Mar-26	08-Apr-26	66			31-Mar-26	08-Apr-26	06-Jul-26	14-Jul-26	Not Started
CON-2460	Rough-in Chilled Glycol Piping-5th Floor	7	7	31-Mar-26	08-Apr-26	6			31-Mar-26	08-Apr-26	08-Apr-26	16-Apr-26	Not Started
CON-1730	Spray Fireproofing - 5th Floor	3	3	31-Mar-26	02-Apr-26	55			31-Mar-26	02-Apr-26	17-Jun-26	22-Jun-26	Not Started
CON-2620	Install Ceiling Hangers & Supports-5th Floor	4	4	01-Apr-26	06-Apr-26	60			01-Apr-26	06-Apr-26	26-Jun-26	01-Jul-26	Not Started
CON-2590	Install Windows - South Elevation	10	10	01-Apr-26	14-Apr-26	0			01-Apr-26	14-Apr-26	01-Apr-26	14-Apr-26	Not Started
CON-2600	Install Storefront System- South Elevation	10	10	01-Apr-26	14-Apr-26	0			01-Apr-26	14-Apr-26	01-Apr-26	14-Apr-26	Not Started
CON-2610	Install Insulated Precast Concrete Sandwich Panel - East Elevation	4	4	01-Apr-26	06-Apr-26	0			01-Apr-26	06-Apr-26	01-Apr-26	06-Apr-26	Not Started
CON-2730	Install Insulated Precast Concrete Sandwich Panel - North Elevation	4	4	01-Apr-26	06-Apr-26	0			01-Apr-26	06-Apr-26	01-Apr-26	06-Apr-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-4220	Install VAV Boxes & Sound Attenuator Devices-4th Floor	5	5	02-Apr-26	08-Apr-26	46			02-Apr-26	08-Apr-26	08-Jun-26	12-Jun-26	Not Started
CON-2800	Install Data rack - 3rd Floor IDF Room	8	8	03-Apr-26	14-Apr-26	0			03-Apr-26	14-Apr-26	03-Apr-26	14-Apr-26	Not Started
CON-2830	Install IPDVS Equipment Rack - 3rd Floor IDF Room	4	4	03-Apr-26	08-Apr-26	4			03-Apr-26	08-Apr-26	09-Apr-26	14-Apr-26	Not Started
CON-2630	Rough-in Gas Risers -2nd Floor	4	4	06-Apr-26	09-Apr-26	3			06-Apr-26	09-Apr-26	09-Apr-26	14-Apr-26	Not Started
CON-2810	Install Grounding Bars - 4th Floor IDF Room	5	5	06-Apr-26	10-Apr-26	106			06-Apr-26	10-Apr-26	04-Sep-26	11-Sep-26	Not Started
CON-2650	Install Data Rack - 4th Floor IDF Room	7	7	06-Apr-26	14-Apr-26	61			06-Apr-26	14-Apr-26	02-Jul-26	13-Jul-26	Not Started
CON-2660	Install Voice Rack - 4th Floor IDF Room	5	5	06-Apr-26	10-Apr-26	70			06-Apr-26	10-Apr-26	16-Jul-26	22-Jul-26	Not Started
CON-2670	Install Wiring Devices -2nd Floor	7	7	06-Apr-26	14-Apr-26	60			06-Apr-26	14-Apr-26	01-Jul-26	10-Jul-26	Not Started
CON-2680	Rough-in Power Conduits -5th Floor	6	6	06-Apr-26	13-Apr-26	26			06-Apr-26	13-Apr-26	12-May-26	19-May-26	Not Started
CON-2690	Low Voltage Wires Pulling -3rd Floor	6	6	06-Apr-26	13-Apr-26	61			06-Apr-26	13-Apr-26	02-Jul-26	10-Jul-26	Not Started
CON-2700	Rough-in Low-Voltage Conduits-4th Floor	6	6	06-Apr-26	13-Apr-26	35			06-Apr-26	13-Apr-26	26-May-26	02-Jun-26	Not Started
CON-2710	Power Wires Pulling-4th Floor	6	6	06-Apr-26	13-Apr-26	26			06-Apr-26	13-Apr-26	12-May-26	19-May-26	Not Started
CON-2570	Field Testing of Windows (5%)	5	5	06-Apr-26	10-Apr-26	131			06-Apr-26	10-Apr-26	13-Oct-26	19-Oct-26	Not Started
MIL-1840	Crane Mobilization-Precast Sandwich Panels Installation Finish	0	0		06-Apr-26	0				06-Apr-26		06-Apr-26	Not Started
CON-2900	Install Duct Risers-1st Floor	1	1	07-Apr-26	07-Apr-26	2			07-Apr-26	07-Apr-26	09-Apr-26	09-Apr-26	Not Started
CON-2910	Layout -1st Floor	3	3	07-Apr-26	09-Apr-26	44			07-Apr-26	09-Apr-26	09-Jun-26	11-Jun-26	Not Started
CON-2920	Pour Sloped Concrete Fill -5th Floor Roof	2	2	07-Apr-26	08-Apr-26	0			07-Apr-26	08-Apr-26	07-Apr-26	08-Apr-26	Not Started
MIL-1230	5th Floor Roofing Start	0	0	07-Apr-26		0			07-Apr-26		07-Apr-26		Not Started
I-1120	Mechanical System Inspection	69	69	07-Apr-26	15-Jul-26	33			07-Apr-26	15-Jul-26	09-Apr-26	31-Aug-26	Not Started
CON-3060	Install Mechanical Piping Risers-1st Floor	2	2	08-Apr-26	09-Apr-26	7			08-Apr-26	09-Apr-26	17-Apr-26	20-Apr-26	Not Started
CON-3070	Duct Leak Test -1st Floor	1	1	08-Apr-26	08-Apr-26	2			08-Apr-26	08-Apr-26	10-Apr-26	10-Apr-26	Not Started
MIL-2602	Start Mechanical Distribution Lines	0	0	08-Apr-26		7			08-Apr-26		17-Apr-26		Not Started
CON-3120	Rough-in Duct Work -1st Floor	4	4	09-Apr-26	14-Apr-26	2			09-Apr-26	14-Apr-26	13-Apr-26	16-Apr-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-4330	Install VAV Boxes & Sound Attenuator Devices-5th Floor	5	5	09-Apr-26	15-Apr-26	46			09-Apr-26	15-Apr-26	15-Jun-26	22-Jun-26	Not Started
CON-3010	Pour Sloped Concrete Fill -Roof Floor	2	2	09-Apr-26	10-Apr-26	0			09-Apr-26	10-Apr-26	09-Apr-26	10-Apr-26	Not Started
MIL-1200	Main Roofing Start	0	0	09-Apr-26		0			09-Apr-26		09-Apr-26		Not Started
MIL-1270	Electrical Rough-ins Start	0	0	09-Apr-26		10			09-Apr-26		23-Apr-26		Not Started
MIL-1220	Layout Finish	0	0		09-Apr-26	44				09-Apr-26		11-Jun-26	Not Started
CON-3080	Install Top & Bottom Track -1st Floor	4	4	10-Apr-26	15-Apr-26	44			10-Apr-26	15-Apr-26	12-Jun-26	17-Jun-26	Not Started
CON-3090	Install CMU Walls -1st Floor	3	3	10-Apr-26	14-Apr-26	45			10-Apr-26	14-Apr-26	15-Jun-26	17-Jun-26	Not Started
CON-3140	Install Plumbing Risers -1st Floor	2	2	10-Apr-26	13-Apr-26	7			10-Apr-26	13-Apr-26	21-Apr-26	22-Apr-26	Not Started
CON-2740	Rough-in Domestic Water Piping -2nd Floor	4	4	10-Apr-26	15-Apr-26	3			10-Apr-26	15-Apr-26	15-Apr-26	20-Apr-26	Not Started
CON-2750	Rough-in Gas Risers-3rd Floor	4	4	10-Apr-26	15-Apr-26	3			10-Apr-26	15-Apr-26	15-Apr-26	20-Apr-26	Not Started
CON-2760	Install IPDVS Equipment Rack - 2nd Floor -IDF Room	8	8	10-Apr-26	21-Apr-26	50			10-Apr-26	21-Apr-26	23-Jun-26	02-Jul-26	Not Started
CON-2770	Install Ladder Rack Cable Tray - 2nd Floor -IDF Room	8	8	10-Apr-26	21-Apr-26	50			10-Apr-26	21-Apr-26	23-Jun-26	02-Jul-26	Not Started
CON-2780	Install BACnet Data Cabinet - 2nd Floor -IDF Room	8	8	10-Apr-26	21-Apr-26	62			10-Apr-26	21-Apr-26	10-Jul-26	21-Jul-26	Not Started
MIL-2942	Start In-Wall Inspection	0	0	10-Apr-26		30			10-Apr-26		22-May-26		Not Started
CON-2820	Install Cable Ladder - 4th Floor IDF Room	5	5	13-Apr-26	17-Apr-26	70			13-Apr-26	17-Apr-26	23-Jul-26	29-Jul-26	Not Started
CON-3210	Install Fluid-Applied Protected Membrane Mock-Up	2	2	13-Apr-26	14-Apr-26	0			13-Apr-26	14-Apr-26	13-Apr-26	14-Apr-26	Not Started
CON-2840	Install Main Sound Rack - 34th Floor IDF Room	5	5	13-Apr-26	17-Apr-26	101			13-Apr-26	17-Apr-26	04-Sep-26	11-Sep-26	Not Started
CON-3230	Install SSDS Risers -SSDS System -1st Floor	2	2	14-Apr-26	15-Apr-26	17			14-Apr-26	15-Apr-26	07-May-26	08-May-26	Not Started
CON-3260	Install Power Risers-1st Floor	2	2	14-Apr-26	15-Apr-26	7			14-Apr-26	15-Apr-26	23-Apr-26	24-Apr-26	Not Started
CON-2950	Rough-in Low-Voltage Conduits-5th Floor	6	6	14-Apr-26	21-Apr-26	35			14-Apr-26	21-Apr-26	03-Jun-26	10-Jun-26	Not Started
CON-2960	Power Wires Pulling-5th Floor	6	6	14-Apr-26	21-Apr-26	26			14-Apr-26	21-Apr-26	20-May-26	28-May-26	Not Started
MIL-1290	Duct Rough-ins Finish	0	0		14-Apr-26	2				14-Apr-26		16-Apr-26	Not Started
CON-3460	Rough-in Hot Water Piping-1st Floor	4	4	15-Apr-26	20-Apr-26	2			15-Apr-26	20-Apr-26	17-Apr-26	22-Apr-26	Not Started
CON-3470	Rough-in Hot Glycol Piping-1st Floor	4	4	15-Apr-26	20-Apr-26	2			15-Apr-26	20-Apr-26	17-Apr-26	22-Apr-26	Not Started
CON-3480	Rough-in Chilled Glycol Piping-1st	4	4	15-Apr-26	20-Apr-26	2			15-Apr-26	20-Apr-26	17-Apr-26	22-Apr-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-3490	Rough-in Refrigerant Piping-1st Floor	4	4	15-Apr-26	20-Apr-26	2			15-Apr-26	20-Apr-26	17-Apr-26	22-Apr-26	Not Started
CON-3520	Install Ceiling Hangers & Supports -1st Floor	4	4	15-Apr-26	20-Apr-26	56			15-Apr-26	20-Apr-26	07-Jul-26	10-Jul-26	Not Started
CON-3250	Install Voice Rack - 3rd Floor IDF Room	5	5	15-Apr-26	21-Apr-26	0			15-Apr-26	21-Apr-26	15-Apr-26	21-Apr-26	Not Started
CON-2930	Install Wiring Devices -3rd Floor	7	7	15-Apr-26	23-Apr-26	60			15-Apr-26	23-Apr-26	13-Jul-26	21-Jul-26	Not Started
CON-2940	Low Voltage Wires Pulling-4th Floor	6	6	15-Apr-26	22-Apr-26	61			15-Apr-26	22-Apr-26	14-Jul-26	21-Jul-26	Not Started
CON-3300	Approve Fluid-Applied Protected Membrane Mock-Up	4	4	15-Apr-26	20-Apr-26	0			15-Apr-26	20-Apr-26	15-Apr-26	20-Apr-26	Not Started
CON-2970	Field Testing of Windows (50%)	5	5	15-Apr-26	21-Apr-26	5			15-Apr-26	21-Apr-26	22-Apr-26	28-Apr-26	Not Started
CON-2980	Install Windows - East Elevation	8	8	15-Apr-26	24-Apr-26	0			15-Apr-26	24-Apr-26	15-Apr-26	24-Apr-26	Not Started
CON-2990	Install Storefront System- East Elevation	8	8	15-Apr-26	24-Apr-26	0			15-Apr-26	24-Apr-26	15-Apr-26	24-Apr-26	Not Started
CON-3380	Install Windows -North Elevation	10	10	15-Apr-26	28-Apr-26	2			15-Apr-26	28-Apr-26	17-Apr-26	30-Apr-26	Not Started
CON-3390	Install Storefront System-North Elevation	10	10	15-Apr-26	28-Apr-26	2			15-Apr-26	28-Apr-26	17-Apr-26	30-Apr-26	Not Started
CON-99237	Install Flag Pole - South Elevation	10	10	15-Apr-26	28-Apr-26	0			15-Apr-26	28-Apr-26	15-Apr-26	28-Apr-26	Not Started
MIL-1250	Top & Bottom Track Finish	0	0		15-Apr-26	44				15-Apr-26		17-Jun-26	Not Started
CON-3970	Install VAV Boxes & Sound Attenuator Devices- 1st Floor	5	5	16-Apr-26	22-Apr-26	46			16-Apr-26	22-Apr-26	23-Jun-26	29-Jun-26	Not Started
CON-2850	Install Electric Unit Heaters -2nd Floor	5	5	16-Apr-26	22-Apr-26	59			16-Apr-26	22-Apr-26	13-Jul-26	17-Jul-26	Not Started
CON-3240	Install Wall Steel Studs & Framing -1st Floor	5	5	16-Apr-26	22-Apr-26	44			16-Apr-26	22-Apr-26	18-Jun-26	25-Jun-26	Not Started
CON-2870	Rough-in Sanitary & Vent Piping -2nd Floor	4	4	16-Apr-26	21-Apr-26	3			16-Apr-26	21-Apr-26	21-Apr-26	24-Apr-26	Not Started
CON-2880	Rough-in Domestic Water Piping -3rd Floor	4	4	16-Apr-26	21-Apr-26	3			16-Apr-26	21-Apr-26	21-Apr-26	24-Apr-26	Not Started
CON-2890	Rough-in Gas Risers -4th Floor	4	4	16-Apr-26	21-Apr-26	9			16-Apr-26	21-Apr-26	29-Apr-26	04-May-26	Not Started
CON-3350	Install Low Voltage Risers-1st Floor	2	2	16-Apr-26	17-Apr-26	7			16-Apr-26	17-Apr-26	27-Apr-26	28-Apr-26	Not Started
CON-7970	Coordinate With CON-ED For Gas Service	7	7	16-Apr-26	24-Apr-26	70			16-Apr-26	24-Apr-26	28-Jul-26	05-Aug-26	Not Started
MIL-2712	Start Low Voltage	0	0	16-Apr-26		7			16-Apr-26		27-Apr-26		Not Started
CON-9070	In-Wall Inspection-2nd Floor	2	2	16-Apr-26	17-Apr-26	26			16-Apr-26	17-Apr-26	22-May-26	26-May-26	Not Started
CON-3110	Install IPDVS Equipment Rack - 4th Floor IDF Room	5	5	20-Apr-26	24-Apr-26	101			20-Apr-26	24-Apr-26	14-Sep-26	18-Sep-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-3430	Install Hot Fluid Applied Membrane -Roof Floor	3	3	21-Apr-26	23-Apr-26	0			21-Apr-26	23-Apr-26	21-Apr-26	23-Apr-26	Not Started
CON-3440	Install Hot Fluid Applied Membrane -5th Floor Roof	4	4	21-Apr-26	24-Apr-26	1			21-Apr-26	24-Apr-26	22-Apr-26	27-Apr-26	Not Started
CON-3760	Rough-in Power Conduits -1st Floor	4	4	21-Apr-26	24-Apr-26	2			21-Apr-26	24-Apr-26	23-Apr-26	28-Apr-26	Not Started
CON-3020	Rough-in Storm Piping -2nd Floor	4	4	22-Apr-26	27-Apr-26	3			22-Apr-26	27-Apr-26	27-Apr-26	30-Apr-26	Not Started
CON-3030	Rough-in Sanitary & Vent Piping -3rd Floor	4	4	22-Apr-26	27-Apr-26	3			22-Apr-26	27-Apr-26	27-Apr-26	30-Apr-26	Not Started
CON-3040	Rough-in Domestic Water Piping -4th Floor	4	4	22-Apr-26	27-Apr-26	9			22-Apr-26	27-Apr-26	05-May-26	08-May-26	Not Started
CON-3050	Rough-in Gas Risers & Piping -5th Floor	4	4	22-Apr-26	27-Apr-26	10			22-Apr-26	27-Apr-26	06-May-26	11-May-26	Not Started
CON-3550	Install Cable Ladder - 3rd Floor IDF Room	5	5	22-Apr-26	28-Apr-26	45			22-Apr-26	28-Apr-26	26-Jun-26	02-Jul-26	Not Started
CON-3570	Install Main Sound Rack - 3rd Floor IDF Room	5	5	22-Apr-26	28-Apr-26	0			22-Apr-26	28-Apr-26	22-Apr-26	28-Apr-26	Not Started
CON-9080	In-Wall Inspection -3rd Floor	2	2	22-Apr-26	23-Apr-26	28			22-Apr-26	23-Apr-26	02-Jun-26	03-Jun-26	Not Started
CON-3130	Install Electric Unit Heaters -3rd Floor	5	5	23-Apr-26	29-Apr-26	59			23-Apr-26	29-Apr-26	20-Jul-26	24-Jul-26	Not Started
CON-3290	Low Voltage Wires Pulling-5th Floor	6	6	23-Apr-26	30-Apr-26	61			23-Apr-26	30-Apr-26	22-Jul-26	29-Jul-26	Not Started
CON-3150	Install Convector Heater CV - Mechanical Work - 2nd Floor	5	5	23-Apr-26	29-Apr-26	59			23-Apr-26	29-Apr-26	20-Jul-26	24-Jul-26	Not Started
CON-4730	Rough-in Conduits & Wires - Electric Service Room	6	6	23-Apr-26	30-Apr-26	25			23-Apr-26	30-Apr-26	29-May-26	05-Jun-26	Not Started
CON-3600	Install Drainage Panels- Roof Floor	3	3	24-Apr-26	28-Apr-26	0			24-Apr-26	28-Apr-26	24-Apr-26	28-Apr-26	Not Started
CON-3280	Install Wiring Devices -4th Floor	7	7	24-Apr-26	04-May-26	60			24-Apr-26	04-May-26	22-Jul-26	30-Jul-26	Not Started
PRO-1990	Procure & Deliver Gas Meter Rig	60	60	25-Apr-26	23-Jun-26	103			25-Apr-26	23-Jun-26	06-Aug-26	04-Oct-26	Not Started
CON-3580	Install 6" Thick Rigid Insulation -5th Floor Roof	3	3	27-Apr-26	29-Apr-26	1			27-Apr-26	29-Apr-26	28-Apr-26	30-Apr-26	Not Started
CON-3910	Install Grounding System -1st Floor	5	5	27-Apr-26	01-May-26	42			27-Apr-26	01-May-26	26-Jun-26	02-Jul-26	Not Started
CON-3920	Rough-in Low-Voltage Conduits-1st Floor	4	4	27-Apr-26	30-Apr-26	2			27-Apr-26	30-Apr-26	29-Apr-26	04-May-26	Not Started
CON-3930	Power Wires Pulling-1st Floor	4	4	27-Apr-26	30-Apr-26	2			27-Apr-26	30-Apr-26	29-Apr-26	04-May-26	Not Started
CON-3370	Field Testing of Windows (90%)	5	5	27-Apr-26	01-May-26	0			27-Apr-26	01-May-26	27-Apr-26	01-May-26	Not Started
CON-3170	Rough-in Storm Piping -3rd Floor	4	4	28-Apr-26	01-May-26	3			28-Apr-26	01-May-26	01-May-26	06-May-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-3180	Rough-in Sanitary & Vent Piping -4th Floor	4	4	28-Apr-26	01-May-26	9			28-Apr-26	01-May-26	11-May-26	14-May-26	Not Started
CON-3190	Rough-in Domestic Water Piping -5th Floor	4	4	28-Apr-26	01-May-26	10			28-Apr-26	01-May-26	12-May-26	15-May-26	Not Started
CON-3200	Plumbing Pressure Testing -2nd Floor	5	5	28-Apr-26	04-May-26	88			28-Apr-26	04-May-26	02-Sep-26	09-Sep-26	Not Started
CON-9090	In-Wall Inspection -4th Floor	7	7	28-Apr-26	06-May-26	26			28-Apr-26	06-May-26	04-Jun-26	12-Jun-26	Not Started
MIL-1580	Window Installation Finish	0	0		28-Apr-26	6				28-Apr-26		06-May-26	Not Started
CON-3730	Install 6" Thick Rigid Insulation -Roof Floor	3	3	29-Apr-26	01-May-26	0			29-Apr-26	01-May-26	29-Apr-26	01-May-26	Not Started
CON-3740	Install Ground Bus Bar - 1st Floor MDF Room	6	6	29-Apr-26	06-May-26	0			29-Apr-26	06-May-26	29-Apr-26	06-May-26	Not Started
MIL-1400	Start Site Work	0	0	29-Apr-26		2			29-Apr-26		01-May-26		Not Started
CON-3220	Dismantle Sidewalk Sheds- South Elevation	2	2	29-Apr-26	30-Apr-26	0			29-Apr-26	30-Apr-26	29-Apr-26	30-Apr-26	Not Started
CON-3420	Install Electric Unit Heaters -4th Floor	5	5	30-Apr-26	06-May-26	59			30-Apr-26	06-May-26	27-Jul-26	31-Jul-26	Not Started
CON-3700	Install Drainage -5th Floor Roof	3	3	30-Apr-26	04-May-26	88			30-Apr-26	04-May-26	04-Sep-26	09-Sep-26	Not Started
CON-3710	Roof Flood Test -5th Floor Roof	4	4	30-Apr-26	05-May-26	1			30-Apr-26	05-May-26	01-May-26	06-May-26	Not Started
CON-3450	Install Air Conditioning Unit AC - Mechanical Work - 2nd Floor	4	4	30-Apr-26	05-May-26	59			30-Apr-26	05-May-26	27-Jul-26	30-Jul-26	Not Started
I-1040	Roofing Flood Testing Inspection	5	5	30-Apr-26	06-May-26	0			30-Apr-26	06-May-26	01-May-26	06-May-26	Not Started
CON-4180	Low Voltage Wires Pulling -1st Floor	4	4	01-May-26	06-May-26	2			01-May-26	06-May-26	05-May-26	08-May-26	Not Started
CON-3780	Install Traffic Control Devices - 54th Avenue Street	3	3	01-May-26	05-May-26	0			01-May-26	05-May-26	01-May-26	05-May-26	Not Started
CON-4960	F/R/P Concrete Pad - Electric Service Room	6	6	01-May-26	08-May-26	25			01-May-26	08-May-26	08-Jun-26	15-Jun-26	Not Started
CON-3310	Install 4" Standpipe -2nd Floor	4	4	04-May-26	07-May-26	3			04-May-26	07-May-26	07-May-26	12-May-26	Not Started
CON-3330	Rough-in Storm Piping -4th Floor	4	4	04-May-26	07-May-26	9			04-May-26	07-May-26	15-May-26	20-May-26	Not Started
CON-3340	Rough-in Sanitary & Vent Piping -5th Floor	4	4	04-May-26	07-May-26	10			04-May-26	07-May-26	18-May-26	21-May-26	Not Started
MIL-1300	Start Sprinkler Rough-ins	0	0	04-May-26		32			04-May-26		18-Jun-26		Not Started
CON-3840	Roof Flood Test -Roof Floor	3	3	04-May-26	06-May-26	0			04-May-26	06-May-26	04-May-26	06-May-26	Not Started
CON-3630	Dismantle Sidewalk Sheds- East Elevation	2	2	04-May-26	05-May-26	0			04-May-26	05-May-26	04-May-26	05-May-26	Not Started
CON-3400	Install Hot Water Circulation Pump -5th Floor	5	5	04-May-26	08-May-26	94			04-May-26	08-May-26	17-Sep-26	23-Sep-26	Not Started
CON-3410	Install Electric Hot Water Heater	5	5	04-May-26	08-May-26	94			04-May-26	08-May-26	17-Sep-26	23-Sep-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
	(LVL 4) Sub Area:												
CON-9100	In-Wall Inspections -5th Floor	7	7	04-May-26	12-May-26	27			04-May-26	12-May-26	11-Jun-26	22-Jun-26	Not Started
CON-3660	Install Wiring Devices -5th Floor	8	8	05-May-26	14-May-26	60			05-May-26	14-May-26	31-Jul-26	11-Aug-26	Not Started
CON-3360	Plumbing Pressure Testing -3rd Floor	5	5	05-May-26	11-May-26	88			05-May-26	11-May-26	10-Sep-26	16-Sep-26	Not Started
MIL-1730	Sidewalk Sheds Dismantle Complete	0	0		05-May-26	0				05-May-26		05-May-26	Not Started
CON-3820	Install Filter Fabric -5th Floor Roof	3	3	06-May-26	08-May-26	87			06-May-26	08-May-26	10-Sep-26	14-Sep-26	Not Started
CON-3850	Remove Existing Steel Faced Curb - 54th Avenue Street	3	3	06-May-26	08-May-26	42			06-May-26	08-May-26	08-Jul-26	10-Jul-26	Not Started
CON-3860	Remove Existing Asphalt - 54th Avenue Street	4	4	06-May-26	11-May-26	41			06-May-26	11-May-26	07-Jul-26	10-Jul-26	Not Started
CON-3870	Install Traffic Control Devices - 2nd Street	5	5	06-May-26	12-May-26	0			06-May-26	12-May-26	06-May-26	12-May-26	Not Started
MIL-1340	BLDG Tight	0	0		06-May-26	0				06-May-26		06-May-26	Not Started
MIL-1350	Electrical Rough-ins Finish	0	0		06-May-26	57				06-May-26		29-Jul-26	Not Started
CON-3640	Install Electric Unit Heaters -5th Floor	3	3	07-May-26	11-May-26	59			07-May-26	11-May-26	03-Aug-26	05-Aug-26	Not Started
CON-4020	Install Filter Fabric -Roof Floor	3	3	07-May-26	11-May-26	84			07-May-26	11-May-26	08-Sep-26	10-Sep-26	Not Started
CON-4460	Rough-in Gas Risers -1st Floor	4	4	07-May-26	12-May-26	2			07-May-26	12-May-26	11-May-26	14-May-26	Not Started
CON-4110	Install Voice Rack - 1st Floor MDF Room	6	6	07-May-26	14-May-26	0			07-May-26	14-May-26	07-May-26	14-May-26	Not Started
CON-4040	Install Walls GWB-Mockup Room	3	3	07-May-26	11-May-26	0			07-May-26	11-May-26	07-May-26	11-May-26	Not Started
CON-4270	Install Gypsum Board Ceiling -Mockup Room	3	3	07-May-26	11-May-26	2			07-May-26	11-May-26	11-May-26	13-May-26	Not Started
MIL-1360	Start Mockup Room Work	0	0	07-May-26		0			07-May-26		07-May-26		Not Started
MIL-1430	Start Architecture Finishes	0	0	07-May-26		0			07-May-26		07-May-26		Not Started
MIL-1260	Plumbing Rough-ins Start	0	0	07-May-26		2			07-May-26		11-May-26		Not Started
CON-4050	Plumbing Piping Insulation -2nd Floor	5	5	07-May-26	13-May-26	86			07-May-26	13-May-26	10-Sep-26	16-Sep-26	Not Started
CON-4070	Install Duct Insulation -2nd Floor	8	8	07-May-26	18-May-26	4			07-May-26	18-May-26	13-May-26	22-May-26	Not Started
MIL-1760	Start Elevator Work	0	0	07-May-26		11			07-May-26		22-May-26		Not Started
CON-4500	Install SSDS Control Panel -1st Floor	5	5	07-May-26	13-May-26	54			07-May-26	13-May-26	27-Jul-26	31-Jul-26	Not Started
CON-99357	Install CMU Wall for Shaft -Elevator Machine Room	10	10	07-May-26	20-May-26	11			07-May-26	20-May-26	22-May-26	05-Jun-26	Not Started
CON-3500	Rough-in Main Sprinkler Piping -2nd Floor	5	5	08-May-26	14-May-26	3			08-May-26	14-May-26	13-May-26	19-May-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-3510	Install 4" Standpipe -3rd Floor	4	4	08-May-26	13-May-26	4			08-May-26	13-May-26	14-May-26	19-May-26	Not Started
CON-3540	Rough-in Storm Piping -5th Floor	4	4	08-May-26	13-May-26	10			08-May-26	13-May-26	22-May-26	28-May-26	Not Started
CON-3960	Install Concrete Pavers -5th Floor Roof	3	3	11-May-26	13-May-26	87			11-May-26	13-May-26	15-Sep-26	17-Sep-26	Not Started
CON-4380	Install Doors & Hardware-Mockup Room	3	3	11-May-26	13-May-26	0			11-May-26	13-May-26	11-May-26	13-May-26	Not Started
CON-5180	Install Service Switchboard "SS-A"- Electric Service Room	5	5	11-May-26	15-May-26	25			11-May-26	15-May-26	16-Jun-26	23-Jun-26	Not Started
CON-4260	Install Door Frames-Mockup Room	2	2	12-May-26	13-May-26	0			12-May-26	13-May-26	12-May-26	13-May-26	Not Started
CON-3560	Plumbing Pressure Testing -4th Floor	5	5	12-May-26	18-May-26	88			12-May-26	18-May-26	17-Sep-26	23-Sep-26	Not Started
CON-4210	Install Concrete Pavers -Roof Floor	4	4	12-May-26	15-May-26	85			12-May-26	15-May-26	14-Sep-26	17-Sep-26	Not Started
CON-3940	Remove Existing Electrical Manhole - 54th Avenue Street	4	4	12-May-26	15-May-26	41			12-May-26	15-May-26	13-Jul-26	16-Jul-26	Not Started
CON-4590	Rough-in Domestic Water Piping-1st Floor	4	4	13-May-26	18-May-26	2			13-May-26	18-May-26	15-May-26	20-May-26	Not Started
CON-3900	Remove Existing Sidewalk - 2nd Street	5	5	13-May-26	19-May-26	0			13-May-26	19-May-26	13-May-26	19-May-26	Not Started
MIL-1310	5th Floor Roofing Finish	0	0		13-May-26	87				13-May-26		17-Sep-26	Not Started
CON-3650	Install 4" Standpipe -4th Floor	4	4	14-May-26	19-May-26	5			14-May-26	19-May-26	21-May-26	27-May-26	Not Started
CON-4480	Paint First coat -Mockup Room	2	2	14-May-26	15-May-26	0			14-May-26	15-May-26	14-May-26	15-May-26	Not Started
CON-3590	Plumbing Pressure Testing -5th Floor	5	5	14-May-26	20-May-26	91			14-May-26	20-May-26	24-Sep-26	30-Sep-26	Not Started
CON-4190	Plumbing Piping Insulation -3rd Floor	5	5	14-May-26	20-May-26	86			14-May-26	20-May-26	17-Sep-26	23-Sep-26	Not Started
CON-3670	Rough-in Branch Sprinkler Piping -2nd Floor	5	5	15-May-26	21-May-26	7			15-May-26	21-May-26	27-May-26	02-Jun-26	Not Started
CON-3680	Rough-in Sprinkler Heads -2nd Floor	5	5	15-May-26	21-May-26	7			15-May-26	21-May-26	27-May-26	02-Jun-26	Not Started
CON-3720	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -2nd Floor	5	5	15-May-26	21-May-26	13			15-May-26	21-May-26	04-Jun-26	10-Jun-26	Not Started
CON-3690	Rough-in Main Sprinkler Piping-3rd Floor	5	5	15-May-26	21-May-26	3			15-May-26	21-May-26	20-May-26	27-May-26	Not Started
CON-4510	Install Sound Rack - 1st Floor MDF Room	6	6	15-May-26	22-May-26	0			15-May-26	22-May-26	15-May-26	22-May-26	Not Started
CON-4120	Install Project Connect Cabinet - 1st Floor MDF Room	8	8	15-May-26	27-May-26	4			15-May-26	27-May-26	21-May-26	02-Jun-26	Not Started
CON-4470	Install Wiring Devices -1st Floor	7	7	15-May-26	26-May-26	90			15-May-26	26-May-26	24-Sep-26	02-Oct-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
MIL-1280	Main Roofing Finish	0	0		15-May-26	85				15-May-26		17-Sep-26	Not Started
CON-4640	Flooring Finishes-Mockup Room	2	2	18-May-26	19-May-26	0			18-May-26	19-May-26	18-May-26	19-May-26	Not Started
CON-5510	Install Leak Detector - Electric Service Room	3	3	18-May-26	20-May-26	39			18-May-26	20-May-26	15-Jul-26	17-Jul-26	Not Started
CON-4080	Install 5' Wide Silva Cells Under Concrete Pavement Strip - 54th Avenue Street	4	4	18-May-26	21-May-26	41			18-May-26	21-May-26	17-Jul-26	22-Jul-26	Not Started
CON-4690	Rough-in Sanitary & Vent Piping -1st Floor	4	4	19-May-26	22-May-26	2			19-May-26	22-May-26	21-May-26	27-May-26	Not Started
CON-4320	Install Duct Insulation -3rd Floor	8	8	19-May-26	29-May-26	4			19-May-26	29-May-26	26-May-26	04-Jun-26	Not Started
CON-9110	In-Wall Inspection -1st Floor	2	2	19-May-26	20-May-26	26			19-May-26	20-May-26	26-Jun-26	29-Jun-26	Not Started
CON-3770	Install 4" Standpipe -5th Floor	4	4	20-May-26	26-May-26	6			20-May-26	26-May-26	29-May-26	03-Jun-26	Not Started
CON-4750	Paint Second coat-Mockup Room	2	2	20-May-26	21-May-26	0			20-May-26	21-May-26	20-May-26	21-May-26	Not Started
CON-3950	Install Pedestrian Ramps With Truncated Domes - 2nd Street	6	6	20-May-26	28-May-26	0			20-May-26	28-May-26	20-May-26	28-May-26	Not Started
CON-4390	Plumbing Piping Insulation -4th Floor	5	5	21-May-26	28-May-26	86			21-May-26	28-May-26	24-Sep-26	30-Sep-26	Not Started
CON-5610	Install Sprinkler Booster Pump - Electric Service Room	4	4	21-May-26	27-May-26	39			21-May-26	27-May-26	20-Jul-26	23-Jul-26	Not Started
CON-99167	Install Elevator Guide Rails -Elevator Machine Room	8	8	21-May-26	02-Jun-26	11			21-May-26	02-Jun-26	08-Jun-26	17-Jun-26	Not Started
CON-3790	Rough-in Branch Sprinkler Piping -3rd Floor	5	5	22-May-26	29-May-26	8			22-May-26	29-May-26	04-Jun-26	10-Jun-26	Not Started
CON-3800	Rough-in Sprinkler Heads -3rd Floor	5	5	22-May-26	29-May-26	8			22-May-26	29-May-26	04-Jun-26	10-Jun-26	Not Started
CON-3880	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-3rd Floor	5	5	22-May-26	29-May-26	13			22-May-26	29-May-26	11-Jun-26	17-Jun-26	Not Started
CON-3810	Rough-in Main Sprinkler Piping-4th Floor	5	5	22-May-26	29-May-26	3			22-May-26	29-May-26	28-May-26	03-Jun-26	Not Started
CON-4930	Install Furniture & Signs -Mockup Room	2	2	22-May-26	26-May-26	0			22-May-26	26-May-26	22-May-26	26-May-26	Not Started
CON-3830	Sprinklers Air Testing-2nd Floor	5	5	22-May-26	29-May-26	13			22-May-26	29-May-26	11-Jun-26	17-Jun-26	Not Started
CON-4150	Pavement Replacement - 54th Avenue Street	4	4	22-May-26	28-May-26	41			22-May-26	28-May-26	23-Jul-26	28-Jul-26	Not Started
CON-4760	Rough-in Storm Piping -1st Floor	4	4	26-May-26	29-May-26	2			26-May-26	29-May-26	28-May-26	02-Jun-26	Not Started
CON-4520	Install Data Rack - 1st Floor MDF Room	6	6	26-May-26	02-Jun-26	0			26-May-26	02-Jun-26	26-May-26	02-Jun-26	Not Started
MIL-1410	Mockup Room Ready For Inspection	0	0		26-May-26	1				26-May-26		27-May-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
MIL-1420	Finish Mockup Room	0	0		26-May-26	0				26-May-26		26-May-26	Not Started
CON-3890	Install 4" Standpipe -Roof	4	4	27-May-26	01-Jun-26	7			27-May-26	01-Jun-26	05-Jun-26	10-Jun-26	Not Started
CON-4030	Install Gypsum Board Walls-2nd Floor	5	5	27-May-26	02-Jun-26	0			27-May-26	02-Jun-26	27-May-26	02-Jun-26	Not Started
CON-5000	Mockup Room Inspection & Punchlist	5	5	27-May-26	02-Jun-26	1			27-May-26	02-Jun-26	28-May-26	03-Jun-26	Not Started
MIL-1440	Start Gypsum Board	0	0	27-May-26		0			27-May-26		27-May-26		Not Started
CON-4200	Tape Gypsum Board -2nd Floor	4	4	28-May-26	02-Jun-26	14			28-May-26	02-Jun-26	17-Jun-26	23-Jun-26	Not Started
CON-5640	Install Fire Alarm Normal ATS - Electric Service Room	4	4	28-May-26	02-Jun-26	39			28-May-26	02-Jun-26	24-Jul-26	29-Jul-26	Not Started
I-1130	Fire Alarm Inspection	47	47	28-May-26	04-Aug-26	2			28-May-26	04-Aug-26	24-Jul-26	06-Aug-26	Not Started
CON-4530	Plumbing Piping Insulation -5th Floor	5	5	29-May-26	04-Jun-26	86			29-May-26	04-Jun-26	01-Oct-26	07-Oct-26	Not Started
CON-4290	Install New Steel Faced Curb - 54th Avenue Street	4	4	29-May-26	03-Jun-26	41			29-May-26	03-Jun-26	29-Jul-26	03-Aug-26	Not Started
CON-4300	Install Pedestrian Ramps With Truncated Domes - 54th Avenue Street	4	4	29-May-26	03-Jun-26	41			29-May-26	03-Jun-26	29-Jul-26	03-Aug-26	Not Started
CON-4090	Remove Existing Steel Faced Curb - 2nd Street	6	6	29-May-26	05-Jun-26	0			29-May-26	05-Jun-26	29-May-26	05-Jun-26	Not Started
MIL-1320	Plumbing Rough-ins Finish	0	0		29-May-26	2				29-May-26		02-Jun-26	Not Started
CON-4890	F/R/P Concrete Pads -Fuel Oil Room	2	2	01-Jun-26	02-Jun-26	47			01-Jun-26	02-Jun-26	07-Aug-26	10-Aug-26	Not Started
CON-4900	Rough-in Fuel Oil Piping -Fuel Oil Room	3	3	01-Jun-26	03-Jun-26	54			01-Jun-26	03-Jun-26	18-Aug-26	20-Aug-26	Not Started
CON-3990	Rough-in Branch Sprinkler Piping -4th Floor	5	5	01-Jun-26	05-Jun-26	11			01-Jun-26	05-Jun-26	16-Jun-26	23-Jun-26	Not Started
CON-4000	Rough-in Sprinkler Heads -4th Floor	5	5	01-Jun-26	05-Jun-26	11			01-Jun-26	05-Jun-26	16-Jun-26	23-Jun-26	Not Started
CON-4100	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-4th Floor	5	5	01-Jun-26	05-Jun-26	13			01-Jun-26	05-Jun-26	18-Jun-26	25-Jun-26	Not Started
CON-4010	Rough-in Main Sprinkler Piping -5th Floor	5	5	01-Jun-26	05-Jun-26	3			01-Jun-26	05-Jun-26	04-Jun-26	10-Jun-26	Not Started
CON-4060	Sprinklers Air Testing-3rd Floor	5	5	01-Jun-26	05-Jun-26	13			01-Jun-26	05-Jun-26	18-Jun-26	25-Jun-26	Not Started
CON-4570	Install Duct Insulation -4th Floor	8	8	01-Jun-26	10-Jun-26	4			01-Jun-26	10-Jun-26	05-Jun-26	16-Jun-26	Not Started
CON-1120	Install Firestopping Mock-Up	2	2	01-Jun-26	02-Jun-26	1			01-Jun-26	02-Jun-26	02-Jun-26	03-Jun-26	Not Started
CON-4940	Install Duplex Domestic Water Booster Pump System (BP-1&BP-2) -1st Floor	8	8	01-Jun-26	10-Jun-26	2			01-Jun-26	10-Jun-26	03-Jun-26	12-Jun-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-4950	Install Duplex Ejector Pump System (EJ-1&EJ-2) -1st Floor	8	8	01-Jun-26	10-Jun-26	2			01-Jun-26	10-Jun-26	03-Jun-26	12-Jun-26	Not Started
I-1110	Fuel-Oil Storage & Fuel Oil Piping Systems Inspection	9	9	01-Jun-26	11-Jun-26	59			01-Jun-26	11-Jun-26	07-Aug-26	04-Sep-26	Not Started
CON-4910	Install 4" Standpipe -1st Floor	4	4	02-Jun-26	05-Jun-26	8			02-Jun-26	05-Jun-26	12-Jun-26	17-Jun-26	Not Started
CON-4990	Install Fuel Oil Storage Tank (FOT-1) - Fuel Oil Room	3	3	03-Jun-26	05-Jun-26	59			03-Jun-26	05-Jun-26	27-Aug-26	31-Aug-26	Not Started
CON-4350	Install Ceramic Wall Tiles at Corridor-2nd Floor	7	7	03-Jun-26	11-Jun-26	21			03-Jun-26	11-Jun-26	06-Jul-26	14-Jul-26	Not Started
CON-4360	Install Gypsum Board Walls-3rd Floor	5	5	03-Jun-26	09-Jun-26	1			03-Jun-26	09-Jun-26	04-Jun-26	10-Jun-26	Not Started
CON-4370	Install Gypsum Board Ceiling -2nd Floor	6	6	03-Jun-26	10-Jun-26	0			03-Jun-26	10-Jun-26	03-Jun-26	10-Jun-26	Not Started
CON-2090	Install Elevator Controller #1 -Elevator Machine Room	10	10	03-Jun-26	16-Jun-26	11			03-Jun-26	16-Jun-26	18-Jun-26	02-Jul-26	Not Started
CON-1140	Approve Firestopping Mock-Up	2	2	03-Jun-26	04-Jun-26	1			03-Jun-26	04-Jun-26	04-Jun-26	05-Jun-26	Not Started
CON-4550	Install UPS- 1st Floor MDF Room	9	9	03-Jun-26	15-Jun-26	0			03-Jun-26	15-Jun-26	03-Jun-26	15-Jun-26	Not Started
CON-4130	Install BACnet Data Cabinet- 1st Floor MDF Room	9	9	03-Jun-26	15-Jun-26	16			03-Jun-26	15-Jun-26	26-Jun-26	09-Jul-26	Not Started
CON-5780	Install Motorized Fire/Smoke Damper & Control Panel - Electric Service Room	5	5	03-Jun-26	09-Jun-26	39			03-Jun-26	09-Jun-26	30-Jul-26	05-Aug-26	Not Started
CON-5790	Install Main Grounding Bus Bar - Electric Service Room	4	4	03-Jun-26	08-Jun-26	70			03-Jun-26	08-Jun-26	14-Sep-26	17-Sep-26	Not Started
CON-5020	Rough-in Fuel Oil Fill Piping -Fuel Oil Room	3	3	04-Jun-26	08-Jun-26	54			04-Jun-26	08-Jun-26	21-Aug-26	25-Aug-26	Not Started
CON-4540	Tape Gypsum Board -3rd Floor	4	4	04-Jun-26	09-Jun-26	13			04-Jun-26	09-Jun-26	24-Jun-26	29-Jun-26	Not Started
CON-4400	Install 4" Concrete Sidewalk - 54th Avenue Street	5	5	04-Jun-26	10-Jun-26	65			04-Jun-26	10-Jun-26	08-Sep-26	14-Sep-26	Not Started
CON-4410	Install 7" Concrete Sidewalk - 54th Avenue Street	5	5	04-Jun-26	10-Jun-26	41			04-Jun-26	10-Jun-26	04-Aug-26	10-Aug-26	Not Started
CON-4700	Install Firestopping-2nd Floor	3	3	05-Jun-26	09-Jun-26	1			05-Jun-26	09-Jun-26	08-Jun-26	10-Jun-26	Not Started
MIL-1750	Start Firestopping	0	0	05-Jun-26		1			05-Jun-26		08-Jun-26		Not Started
MIL-2952	Finish Standpipe System Inspection	0	0		05-Jun-26	8				05-Jun-26		17-Jun-26	Not Started
CON-2250	Install Air Handling Unit AHU-1 -Roof Floor	5	5	08-Jun-26	12-Jun-26	5			08-Jun-26	12-Jun-26	15-Jun-26	22-Jun-26	Not Started
CON-5160	Install Fuel Oil Transfer Duplex Pump (FOP-1 & 2) -1st Floor	4	4	08-Jun-26	11-Jun-26	59			08-Jun-26	11-Jun-26	01-Sep-26	04-Sep-26	Not Started
CON-5030	Rough-in Main Sprinkler Piping -1st Floor	5	5	08-Jun-26	12-Jun-26	8			08-Jun-26	12-Jun-26	18-Jun-26	25-Jun-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-4230	Rough-in Branch Sprinkler Piping -5th Floor	5	5	08-Jun-26	12-Jun-26	12			08-Jun-26	12-Jun-26	25-Jun-26	01-Jul-26	Not Started
CON-4240	Rough-in Sprinkler Heads -5th Floor	5	5	08-Jun-26	12-Jun-26	12			08-Jun-26	12-Jun-26	25-Jun-26	01-Jul-26	Not Started
CON-4340	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -5th Floor	5	5	08-Jun-26	12-Jun-26	13			08-Jun-26	12-Jun-26	26-Jun-26	02-Jul-26	Not Started
CON-4250	Rough-in Main Sprinkler Piping -Roof	5	5	08-Jun-26	12-Jun-26	3			08-Jun-26	12-Jun-26	11-Jun-26	17-Jun-26	Not Started
MIL-1460	Roof Top Units Installations Start	0	0	08-Jun-26		25			08-Jun-26		15-Jul-26		Not Started
CON-4280	Sprinklers Air Testing-4th Floor	5	5	08-Jun-26	12-Jun-26	13			08-Jun-26	12-Jun-26	26-Jun-26	02-Jul-26	Not Started
CON-4160	Install New Steel Faced Curb - 2nd Street	6	6	08-Jun-26	15-Jun-26	0			08-Jun-26	15-Jun-26	08-Jun-26	15-Jun-26	Not Started
CON-4170	Install 4" Concrete Sidewalk - 2nd Street	7	7	08-Jun-26	16-Jun-26	5			08-Jun-26	16-Jun-26	15-Jun-26	24-Jun-26	Not Started
CON-9130	Install Switch Gear - Electric Service Room	5	5	08-Jun-26	12-Jun-26	11			08-Jun-26	12-Jun-26	24-Jun-26	30-Jun-26	Not Started
CON-5200	Rough-in Fuel Oil Vent Piping -Fuel Oil Room	4	4	09-Jun-26	12-Jun-26	54			09-Jun-26	12-Jun-26	26-Aug-26	31-Aug-26	Not Started
CON-4620	Install Gypsum Board Walls-4th Floor	5	5	10-Jun-26	16-Jun-26	3			10-Jun-26	16-Jun-26	15-Jun-26	22-Jun-26	Not Started
MIL-1450	Start 1st Coat Painting	0	0	10-Jun-26		1			10-Jun-26		11-Jun-26		Not Started
CON-4850	Install Firestopping-3rd Floor	4	4	10-Jun-26	15-Jun-26	3			10-Jun-26	15-Jun-26	15-Jun-26	18-Jun-26	Not Started
CON-5840	Install Electric Unit Heater EUH-6 - Electric Service Room	4	4	10-Jun-26	15-Jun-26	39			10-Jun-26	15-Jun-26	06-Aug-26	11-Aug-26	Not Started
CON-4630	Install Gypsum Board Ceiling-3rd Floor	6	6	11-Jun-26	18-Jun-26	0			11-Jun-26	18-Jun-26	11-Jun-26	18-Jun-26	Not Started
CON-4830	Install First Coat Painting-2nd Floor	5	5	11-Jun-26	17-Jun-26	0			11-Jun-26	17-Jun-26	11-Jun-26	17-Jun-26	Not Started
CON-5050	Plumbing Pressure Testing -1st Floor	5	5	11-Jun-26	17-Jun-26	2			11-Jun-26	17-Jun-26	15-Jun-26	22-Jun-26	Not Started
CON-4710	Install Duct Insulation -5th Floor	8	8	11-Jun-26	23-Jun-26	4			11-Jun-26	23-Jun-26	17-Jun-26	29-Jun-26	Not Started
CON-4720	Tape Gypsum Board -4th Floor	4	4	11-Jun-26	16-Jun-26	12			11-Jun-26	16-Jun-26	30-Jun-26	06-Jul-26	Not Started
CON-4560	Install Pavement Marking - 54th Avenue Street	3	3	11-Jun-26	15-Jun-26	62			11-Jun-26	15-Jun-26	10-Sep-26	14-Sep-26	Not Started
MIL-2992	Finish Fuel-Oil Storage & Fuel Oil Piping Systems Inspection	0	0		11-Jun-26	67				11-Jun-26		17-Sep-26	Not Started
CON-4610	Install Ceramic Wall Tiles at Corridor-3rd Floor	7	7	12-Jun-26	23-Jun-26	21			12-Jun-26	23-Jun-26	15-Jul-26	23-Jul-26	Not Started
CON-2430	Install Air Handling Unit AHU-2 -Roof Floor	5	5	15-Jun-26	22-Jun-26	5			15-Jun-26	22-Jun-26	23-Jun-26	29-Jun-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-5230	Rough-in Branch Sprinkler Piping -1st Floor	5	5	15-Jun-26	22-Jun-26	8			15-Jun-26	22-Jun-26	26-Jun-26	02-Jul-26	Not Started
CON-5240	Rough-in Sprinkler Heads -1st Floor	5	5	15-Jun-26	22-Jun-26	8			15-Jun-26	22-Jun-26	26-Jun-26	02-Jul-26	Not Started
CON-4430	Rough-in Branch Sprinkler Piping -Roof	5	5	15-Jun-26	22-Jun-26	3			15-Jun-26	22-Jun-26	18-Jun-26	25-Jun-26	Not Started
CON-4440	Rough-in Sprinkler Heads -Roof	5	5	15-Jun-26	22-Jun-26	8			15-Jun-26	22-Jun-26	26-Jun-26	02-Jul-26	Not Started
CON-4490	Sprinklers Air Testing-5th Floor	5	5	15-Jun-26	22-Jun-26	13			15-Jun-26	22-Jun-26	06-Jul-26	10-Jul-26	Not Started
CON-8060	CON-ED - Switchgear Inspection	4	4	15-Jun-26	18-Jun-26	11			15-Jun-26	18-Jun-26	01-Jul-26	07-Jul-26	Not Started
CON-5010	Install Firestopping-4th Floor	4	4	16-Jun-26	22-Jun-26	5			16-Jun-26	22-Jun-26	24-Jun-26	29-Jun-26	Not Started
CON-4780	Install IPDVS Equipment Rack - 1st Floor MDF Room	6	6	16-Jun-26	24-Jun-26	0			16-Jun-26	24-Jun-26	16-Jun-26	24-Jun-26	Not Started
CON-4580	Remove Traffic Control Devices - 54th Avenue Street	3	3	16-Jun-26	18-Jun-26	62			16-Jun-26	18-Jun-26	15-Sep-26	17-Sep-26	Not Started
CON-4310	Install 7" Concrete Sidewalk - 2nd Street	6	6	16-Jun-26	24-Jun-26	0			16-Jun-26	24-Jun-26	16-Jun-26	24-Jun-26	Not Started
CON-4810	Install Gypsum Board Walls-5th Floor	5	5	17-Jun-26	24-Jun-26	3			17-Jun-26	24-Jun-26	23-Jun-26	29-Jun-26	Not Started
CON-2370	Install Elevator Controller #2 -Elevator Machine Room	10	10	17-Jun-26	01-Jul-26	11			17-Jun-26	01-Jul-26	06-Jul-26	17-Jul-26	Not Started
CON-5120	Install Door Frames & Doors-2nd Floor	5	5	18-Jun-26	25-Jun-26	0			18-Jun-26	25-Jun-26	18-Jun-26	25-Jun-26	Not Started
CON-5130	Install Lighting Fixtures -2nd Floor	5	5	18-Jun-26	25-Jun-26	0			18-Jun-26	25-Jun-26	18-Jun-26	25-Jun-26	Not Started
CON-5210	Plumbing Piping Insulation -1st Floor	5	5	18-Jun-26	25-Jun-26	2			18-Jun-26	25-Jun-26	23-Jun-26	29-Jun-26	Not Started
CON-4970	Tape Gypsum Board -5th Floor	4	4	18-Jun-26	24-Jun-26	11			18-Jun-26	24-Jun-26	07-Jul-26	10-Jul-26	Not Started
CON-98797	Install Intrusion System Components-2nd Floor	6	6	18-Jun-26	26-Jun-26	9			18-Jun-26	26-Jun-26	02-Jul-26	10-Jul-26	Not Started
CON-98847	Install Auxiliary System Components-2nd Floor	6	6	18-Jun-26	26-Jun-26	5			18-Jun-26	26-Jun-26	26-Jun-26	06-Jul-26	Not Started
CON-98897	Install Sound Clock System Components-2nd Floor	6	6	18-Jun-26	26-Jun-26	2			18-Jun-26	26-Jun-26	23-Jun-26	30-Jun-26	Not Started
CON-4820	Install Gypsum Board Ceiling-4th Floor	6	6	22-Jun-26	29-Jun-26	2			22-Jun-26	29-Jun-26	24-Jun-26	01-Jul-26	Not Started
CON-5110	Install First Coat Painting-3rd Floor	5	5	22-Jun-26	26-Jun-26	0			22-Jun-26	26-Jun-26	22-Jun-26	26-Jun-26	Not Started
CON-8070	CON-ED - Pull Power Cable to the Building	10	10	22-Jun-26	06-Jul-26	11			22-Jun-26	06-Jul-26	08-Jul-26	21-Jul-26	Not Started
MIL-1330	Finish Sprinkler Rough-ins	0	0		22-Jun-26	13				22-Jun-26		10-Jul-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-2560	Install Air Handling Unit AHU-3 -Roof Floor	5	5	23-Jun-26	29-Jun-26	5			23-Jun-26	29-Jun-26	30-Jun-26	07-Jul-26	Not Started
CON-5270	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -1st Floor	5	5	23-Jun-26	29-Jun-26	3			23-Jun-26	29-Jun-26	26-Jun-26	02-Jul-26	Not Started
CON-5220	Install Firestopping-5th Floor	4	4	23-Jun-26	26-Jun-26	9			23-Jun-26	26-Jun-26	07-Jul-26	10-Jul-26	Not Started
CON-4650	Install 3 Way Roof Manifold -Roof	5	5	23-Jun-26	29-Jun-26	77			23-Jun-26	29-Jun-26	13-Oct-26	19-Oct-26	Not Started
CON-4800	Install Ceramic Wall Tiles at Corridor-4th Floor	7	7	24-Jun-26	02-Jul-26	21			24-Jun-26	02-Jul-26	24-Jul-26	03-Aug-26	Not Started
CON-4840	Install Duct Insulation -1st Floor	8	8	24-Jun-26	06-Jul-26	4			24-Jun-26	06-Jul-26	30-Jun-26	10-Jul-26	Not Started
CON-7990	Gas Authorization	5	5	24-Jun-26	30-Jun-26	71			24-Jun-26	30-Jun-26	05-Oct-26	09-Oct-26	Not Started
CON-4790	Install Ladder Rack Cable Tray-1st Floor MDF Room	6	6	25-Jun-26	02-Jul-26	0			25-Jun-26	02-Jul-26	25-Jun-26	02-Jul-26	Not Started
CON-4420	Remove Traffic Control Devices - 2nd Street	5	5	25-Jun-26	01-Jul-26	0			25-Jun-26	01-Jul-26	25-Jun-26	01-Jul-26	Not Started
CON-4450	Install Gypsum Board Walls-1st Floor	6	6	26-Jun-26	06-Jul-26	2			26-Jun-26	06-Jul-26	30-Jun-26	08-Jul-26	Not Started
CON-5360	Install Flooring Tiles-2nd Floor	5	5	26-Jun-26	02-Jul-26	0			26-Jun-26	02-Jul-26	26-Jun-26	02-Jul-26	Not Started
CON-5310	Install Fire alarm Sensors and Devises -2nd Floor	5	5	26-Jun-26	02-Jul-26	0			26-Jun-26	02-Jul-26	26-Jun-26	02-Jul-26	Not Started
CON-5340	Install First Coat Painting-4th Floor	5	5	29-Jun-26	06-Jul-26	1			29-Jun-26	06-Jul-26	30-Jun-26	07-Jul-26	Not Started
CON-5350	Install Door Frames & Doors-3rd Floor	5	5	29-Jun-26	06-Jul-26	0			29-Jun-26	06-Jul-26	29-Jun-26	06-Jul-26	Not Started
CON-5370	Install Lighting Fixtures -3rd Floor	6	6	29-Jun-26	07-Jul-26	2			29-Jun-26	07-Jul-26	01-Jul-26	09-Jul-26	Not Started
CON-98807	Install Intrusion System Components-3rd Floor	6	6	29-Jun-26	07-Jul-26	9			29-Jun-26	07-Jul-26	13-Jul-26	20-Jul-26	Not Started
CON-98857	Install Auxiliary System Components-3rd Floor	6	6	29-Jun-26	07-Jul-26	5			29-Jun-26	07-Jul-26	07-Jul-26	14-Jul-26	Not Started
CON-98907	Install Sound Clock System Components-3rd Floor	6	6	29-Jun-26	07-Jul-26	2			29-Jun-26	07-Jul-26	01-Jul-26	09-Jul-26	Not Started
CON-2720	Install Air Handling Unit AHU-4 -Roof Floor	5	5	30-Jun-26	07-Jul-26	5			30-Jun-26	07-Jul-26	08-Jul-26	14-Jul-26	Not Started
CON-5100	Install Gypsum Board Ceiling-5th Floor	6	6	30-Jun-26	08-Jul-26	2			30-Jun-26	08-Jul-26	02-Jul-26	10-Jul-26	Not Started
CON-5410	Sprinklers Air Testing-1st Floor	5	5	30-Jun-26	07-Jul-26	3			30-Jun-26	07-Jul-26	06-Jul-26	10-Jul-26	Not Started
CON-4600	Tape Gypsum Board -1st Floor	4	4	30-Jun-26	06-Jul-26	10			30-Jun-26	06-Jul-26	15-Jul-26	20-Jul-26	Not Started
CON-5390	Install Firestopping-1st Floor	4	4	30-Jun-26	06-Jul-26	10			30-Jun-26	06-Jul-26	15-Jul-26	20-Jul-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-8000	Pink Slip	5	5	01-Jul-26	08-Jul-26	71			01-Jul-26	08-Jul-26	13-Oct-26	19-Oct-26	Not Started
CON-2580	Install Power Panels -Elevator Machine Room	7	7	02-Jul-26	13-Jul-26	11			02-Jul-26	13-Jul-26	20-Jul-26	28-Jul-26	Not Started
CON-4660	Excavation - Drainage Work - Building Perimeter	3	3	02-Jul-26	07-Jul-26	0			02-Jul-26	07-Jul-26	02-Jul-26	07-Jul-26	Not Started
CON-5080	Install Ceramic Wall Tiles at Corridor-5th Floor	7	7	06-Jul-26	14-Jul-26	21			06-Jul-26	14-Jul-26	04-Aug-26	12-Aug-26	Not Started
CON-5560	Install Final Coat Painting-2nd Floor	6	6	06-Jul-26	13-Jul-26	0			06-Jul-26	13-Jul-26	06-Jul-26	13-Jul-26	Not Started
CON-5570	Install Plumbing Fixtures -2nd Floor	7	7	06-Jul-26	14-Jul-26	46			06-Jul-26	14-Jul-26	09-Sep-26	17-Sep-26	Not Started
CON-4770	Install PBX - 1st Floor MDF Room	8	8	06-Jul-26	15-Jul-26	4			06-Jul-26	15-Jul-26	10-Jul-26	21-Jul-26	Not Started
CON-5140	Install IPDVS Devices -2nd Floor	9	9	06-Jul-26	16-Jul-26	0			06-Jul-26	16-Jul-26	06-Jul-26	16-Jul-26	Not Started
CLO-1120	MDF & IDF Rooms Testing & Commissioning	12	12	06-Jul-26	21-Jul-26	0			06-Jul-26	21-Jul-26	06-Jul-26	21-Jul-26	Not Started
MIL-2632	Finish HVAC	0	0		06-Jul-26	6				06-Jul-26		14-Jul-26	Not Started
MIL-2982	Finish Fire-Resistant Penetrations And Joints Inspection	0	0		06-Jul-26	10				06-Jul-26		20-Jul-26	Not Started
CON-4670	Install Exhaust Fans -1st Floor	5	5	07-Jul-26	13-Jul-26	2			07-Jul-26	13-Jul-26	09-Jul-26	15-Jul-26	Not Started
CON-4680	Install Ceramic Wall Tiles at Corridor -1st Floor	7	7	07-Jul-26	15-Jul-26	21			07-Jul-26	15-Jul-26	05-Aug-26	13-Aug-26	Not Started
CON-5540	Install Door Frames & Doors-4th Floor	5	5	07-Jul-26	13-Jul-26	1			07-Jul-26	13-Jul-26	08-Jul-26	14-Jul-26	Not Started
CON-5550	Install Flooring Tiles-3rd Floor	5	5	07-Jul-26	13-Jul-26	0			07-Jul-26	13-Jul-26	07-Jul-26	13-Jul-26	Not Started
CLO-1010	HVAC Flush-Out	20	20	07-Jul-26	03-Aug-26	6			07-Jul-26	03-Aug-26	15-Jul-26	11-Aug-26	Not Started
MIL-2732	Start Mechanical and Electrical System Commissioning	0	0	07-Jul-26		6			07-Jul-26		15-Jul-26		Not Started
CON-8080	CON-ED - Terminate Power Cables	10	10	07-Jul-26	20-Jul-26	11			07-Jul-26	20-Jul-26	22-Jul-26	04-Aug-26	Not Started
CON-2860	Install Fume Hood Exhaust -Roof Floor	3	3	08-Jul-26	10-Jul-26	33			08-Jul-26	10-Jul-26	24-Aug-26	26-Aug-26	Not Started
CON-5480	Install Gypsum Board Ceiling -1st Floor	6	6	08-Jul-26	15-Jul-26	3			08-Jul-26	15-Jul-26	13-Jul-26	20-Jul-26	Not Started
CON-5580	Install Lighting Fixtures -4th Floor	6	6	08-Jul-26	15-Jul-26	4			08-Jul-26	15-Jul-26	14-Jul-26	21-Jul-26	Not Started
CON-5500	Install Fire alarm Sensors and Devises -3rd Floor	8	8	08-Jul-26	17-Jul-26	2			08-Jul-26	17-Jul-26	10-Jul-26	21-Jul-26	Not Started
CON-5770	Install Air Cooled Condensing Unit	5	5	08-Jul-26	14-Jul-26	5			08-Jul-26	14-Jul-26	15-Jul-26	21-Jul-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
	ACCS - Mechanical Work - 5th Floor												
CON-4740	Install Flood Barrier Wall - Drainage Work - Building Perimeter	3	3	08-Jul-26	10-Jul-26	0			08-Jul-26	10-Jul-26	08-Jul-26	10-Jul-26	Not Started
CON-98817	Install Intrusion System Components-4th Floor	6	6	08-Jul-26	15-Jul-26	9			08-Jul-26	15-Jul-26	21-Jul-26	28-Jul-26	Not Started
CON-98867	Install Auxiliary System Components-4th Floor	6	6	08-Jul-26	15-Jul-26	5			08-Jul-26	15-Jul-26	15-Jul-26	22-Jul-26	Not Started
CON-98917	Install Sound Clock System Components-4th Floor	6	6	08-Jul-26	15-Jul-26	2			08-Jul-26	15-Jul-26	10-Jul-26	17-Jul-26	Not Started
PRO-2000	Procure & Deliver Key Cutting Machine	74	74	08-Jul-26	19-Sep-26	30			08-Jul-26	19-Sep-26	07-Aug-26	19-Oct-26	Not Started
CON-5530	Install First Coat Painting -5th Floor	5	5	09-Jul-26	15-Jul-26	2			09-Jul-26	15-Jul-26	13-Jul-26	17-Jul-26	Not Started
CON-3000	Install Smoke Purge Fan -Roof Floor	3	3	13-Jul-26	15-Jul-26	33			13-Jul-26	15-Jul-26	27-Aug-26	31-Aug-26	Not Started
CON-4860	Install Drilled Caisson Supported Ventilation Structure - Drainage Work - Building Perimeter	3	3	13-Jul-26	15-Jul-26	0			13-Jul-26	15-Jul-26	13-Jul-26	15-Jul-26	Not Started
CON-4870	Install Cabinet Unit Heaters With Fan CUH-1st Floor	3	3	14-Jul-26	16-Jul-26	2			14-Jul-26	16-Jul-26	16-Jul-26	20-Jul-26	Not Started
CON-5090	Install Acoustical Ceiling Tiles-2nd Floor	5	5	14-Jul-26	20-Jul-26	2			14-Jul-26	20-Jul-26	16-Jul-26	22-Jul-26	Not Started
CON-5690	Install Flooring Tiles-4th Floor	5	5	14-Jul-26	20-Jul-26	1			14-Jul-26	20-Jul-26	15-Jul-26	21-Jul-26	Not Started
CON-5700	Install Final Coat Painting-3rd Floor	6	6	14-Jul-26	21-Jul-26	0			14-Jul-26	21-Jul-26	14-Jul-26	21-Jul-26	Not Started
CON-5710	Install Furniture & Milling Work (Contractor Provided & Installed) -2nd Floor	5	5	14-Jul-26	20-Jul-26	43			14-Jul-26	20-Jul-26	14-Sep-26	18-Sep-26	Not Started
CON-2790	Rough-in Conduits & Wires-Elevator Machine Room	6	6	14-Jul-26	21-Jul-26	12			14-Jul-26	21-Jul-26	30-Jul-26	06-Aug-26	Not Started
CON-5760	Install Wood Floating Floor System -Gymnatorium	10	10	14-Jul-26	27-Jul-26	3			14-Jul-26	27-Jul-26	17-Jul-26	30-Jul-26	Not Started
CON-4880	Install Motorized Fire/Smoke Damper FSD - Mechanical Work - 1st Floor	7	7	14-Jul-26	22-Jul-26	22			14-Jul-26	22-Jul-26	13-Aug-26	21-Aug-26	Not Started
CON-9030	Install Furniture & Milling Work (Owner Provided & Installed) -2nd Floor	5	5	14-Jul-26	20-Jul-26	43			14-Jul-26	20-Jul-26	14-Sep-26	18-Sep-26	Not Started
CON-99157	Install Elevator Sump Pump -Elevator Machine Room	10	10	14-Jul-26	27-Jul-26	11			14-Jul-26	27-Jul-26	29-Jul-26	11-Aug-26	Not Started
CON-99247	Install Laboratory Equipment -3rd	4	4	14-Jul-26	17-Jul-26	49			14-Jul-26	17-Jul-26	22-Sep-26	25-Sep-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
MIL-1480	Roof Top Units Installations Finish	0	0		14-Jul-26	5				14-Jul-26		21-Jul-26	Not Started
CON-5730	Install Plumbing Fixtures -3rd Floor	7	7	15-Jul-26	23-Jul-26	46			15-Jul-26	23-Jul-26	18-Sep-26	28-Sep-26	Not Started
CON-5960	F/R/P Concert Pad -Boiler Room	3	3	15-Jul-26	17-Jul-26	5			15-Jul-26	17-Jul-26	22-Jul-26	24-Jul-26	Not Started
MIL-2972	Finish Mechanical System Inspection	0	0		15-Jul-26	33				15-Jul-26		31-Aug-26	Not Started
CON-5680	Install Door Frames & Doors -5th Floor	5	5	16-Jul-26	22-Jul-26	10			16-Jul-26	22-Jul-26	30-Jul-26	05-Aug-26	Not Started
CON-5720	Install First Coat Painting-1st Floor	5	5	16-Jul-26	22-Jul-26	3			16-Jul-26	22-Jul-26	21-Jul-26	27-Jul-26	Not Started
CON-5740	Install Lighting Fixtures -5th Floor	6	6	16-Jul-26	23-Jul-26	5			16-Jul-26	23-Jul-26	23-Jul-26	30-Jul-26	Not Started
CLO-1140	SSDS System Testing & Commissioning	7	7	16-Jul-26	24-Jul-26	33			16-Jul-26	24-Jul-26	01-Sep-26	10-Sep-26	Not Started
CON-4980	Install 4" & 6" & 10" & 12" DIP - Drainage Work - Building Perimeter	3	3	16-Jul-26	20-Jul-26	0			16-Jul-26	20-Jul-26	16-Jul-26	20-Jul-26	Not Started
CON-98827	Install Intrusion System Components -5th Floor	6	6	16-Jul-26	23-Jul-26	9			16-Jul-26	23-Jul-26	29-Jul-26	05-Aug-26	Not Started
CON-98877	Install Auxiliary System Components -5th Floor	6	6	16-Jul-26	23-Jul-26	5			16-Jul-26	23-Jul-26	23-Jul-26	30-Jul-26	Not Started
CON-98927	Install Sound Clock System Components -5th Floor	6	6	16-Jul-26	23-Jul-26	2			16-Jul-26	23-Jul-26	20-Jul-26	27-Jul-26	Not Started
MIL-2562	Start Below Grade Plumbing and Other Utilities	0	0	16-Jul-26		7			16-Jul-26		27-Jul-26		Not Started
CON-9170	Install 8" Combined Water Service (2nd Street)- Drainage Work - Building Perimeter	3	3	16-Jul-26	20-Jul-26	0			16-Jul-26	20-Jul-26	16-Jul-26	20-Jul-26	Not Started
CON-9180	Install 6" Fire Water Service (54th Avenue Street)- Drainage Work - Building Perimeter	3	3	16-Jul-26	20-Jul-26	0			16-Jul-26	20-Jul-26	16-Jul-26	20-Jul-26	Not Started
CON-5060	Install Hot Glycol / Hot Water Cabinet Heater (CUH) -3rd Floor	4	4	17-Jul-26	22-Jul-26	2			17-Jul-26	22-Jul-26	21-Jul-26	24-Jul-26	Not Started
CON-5070	Install Electric Unit Heaters -1st Floor	7	7	17-Jul-26	27-Jul-26	11			17-Jul-26	27-Jul-26	03-Aug-26	11-Aug-26	Not Started
CON-3750	Install Emergency Generator-Roof Floor	4	4	17-Jul-26	22-Jul-26	7			17-Jul-26	22-Jul-26	28-Jul-26	31-Jul-26	Not Started
CON-5440	Install IPDVS Devices -3rd Floor	9	9	17-Jul-26	29-Jul-26	0			17-Jul-26	29-Jul-26	17-Jul-26	29-Jul-26	Not Started
CON-6000	Rough-in Conduits & Wires-Boiler Room	3	3	20-Jul-26	22-Jul-26	5			20-Jul-26	22-Jul-26	27-Jul-26	29-Jul-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-5660	Install Fire alarm Sensors and Devises -4th Floor	7	7	20-Jul-26	28-Jul-26	2			20-Jul-26	28-Jul-26	22-Jul-26	30-Jul-26	Not Started
CON-5820	Install Signages-2nd Floor	5	5	21-Jul-26	27-Jul-26	43			21-Jul-26	27-Jul-26	21-Sep-26	25-Sep-26	Not Started
CON-5190	Install Catch Basin - Drainage Work - Building Perimeter	2	2	21-Jul-26	22-Jul-26	0			21-Jul-26	22-Jul-26	21-Jul-26	22-Jul-26	Not Started
CON-8090	CON-ED - Energize to the Building	5	5	21-Jul-26	27-Jul-26	11			21-Jul-26	27-Jul-26	05-Aug-26	11-Aug-26	Not Started
MIL-1600	MDF Work Finish	0	0		21-Jul-26*	0				21-Jul-26		21-Jul-26	Not Started
MIL-1610	IDF Work Finish	0	0		21-Jul-26*	0				21-Jul-26		21-Jul-26	Not Started
CON-5330	Install Acoustical Ceiling Tiles-3rd Floor	5	5	22-Jul-26	28-Jul-26	1			22-Jul-26	28-Jul-26	23-Jul-26	29-Jul-26	Not Started
CON-5900	Install Final Coat Painting-4th Floor	6	6	22-Jul-26	29-Jul-26	0			22-Jul-26	29-Jul-26	22-Jul-26	29-Jul-26	Not Started
CON-5910	Install Furniture & Milling Work (Contractor Provided & Installed) -3rd Floor	5	5	22-Jul-26	28-Jul-26	42			22-Jul-26	28-Jul-26	21-Sep-26	25-Sep-26	Not Started
CON-3100	Install Elevator Cabinet (1) -Elevator Machine Room	10	10	22-Jul-26	04-Aug-26	12			22-Jul-26	04-Aug-26	07-Aug-26	20-Aug-26	Not Started
CON-3620	Install Elevator Cabinet (2) -Elevator Machine Room	10	10	22-Jul-26	04-Aug-26	12			22-Jul-26	04-Aug-26	07-Aug-26	20-Aug-26	Not Started
CON-9040	Install Furniture & Milling Work (Owner Provided & Installed) -3rd Floor	5	5	22-Jul-26	28-Jul-26	42			22-Jul-26	28-Jul-26	21-Sep-26	25-Sep-26	Not Started
CON-6050	Install Boiler B-1-Boiler Room	5	5	23-Jul-26	29-Jul-26	5			23-Jul-26	29-Jul-26	30-Jul-26	05-Aug-26	Not Started
CON-5260	Install Cabinet Unit Heater With Fan CUH -4th Floor	4	4	23-Jul-26	28-Jul-26	3			23-Jul-26	28-Jul-26	28-Jul-26	31-Jul-26	Not Started
CON-5860	Install Sprinkler Booster Pump (SBP-1) -1st Floor	10	10	23-Jul-26	05-Aug-26	12			23-Jul-26	05-Aug-26	10-Aug-26	21-Aug-26	Not Started
CON-5870	Install Metal Panel Ceiling & Metal Geometric Ceiling -1st Floor	5	5	23-Jul-26	29-Jul-26	16			23-Jul-26	29-Jul-26	14-Aug-26	20-Aug-26	Not Started
CON-5890	Install Flooring Tiles -5th Floor	5	5	23-Jul-26	29-Jul-26	10			23-Jul-26	29-Jul-26	06-Aug-26	12-Aug-26	Not Started
CON-5920	Install Door Frames & Doors-1st Floor	5	5	23-Jul-26	29-Jul-26	11			23-Jul-26	29-Jul-26	07-Aug-26	13-Aug-26	Not Started
CON-5380	Install Generator Connections -Roof Floor	4	4	23-Jul-26	28-Jul-26	7			23-Jul-26	28-Jul-26	03-Aug-26	06-Aug-26	Not Started
CON-5150	Install Air Conditioning Unit AC - Mechanical Work - 1st Floor	4	4	23-Jul-26	28-Jul-26	22			23-Jul-26	28-Jul-26	24-Aug-26	27-Aug-26	Not Started
CON-5280	Install Convector Heater CV - Mechanical Work - 3rd Floor	4	4	23-Jul-26	28-Jul-26	2			23-Jul-26	28-Jul-26	27-Jul-26	30-Jul-26	Not Started
CON-5290	Install Storm Inlet With Hood & Storm Hood - Drainage Work - Building Perimeter	2	2	23-Jul-26	24-Jul-26	0			23-Jul-26	24-Jul-26	23-Jul-26	24-Jul-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-5930	Install Plumbing Fixtures -4th Floor	7	7	24-Jul-26	03-Aug-26	46			24-Jul-26	03-Aug-26	29-Sep-26	07-Oct-26	Not Started
CON-5940	Install Lighting Fixtures -1st Floor	7	7	24-Jul-26	03-Aug-26	6			24-Jul-26	03-Aug-26	03-Aug-26	11-Aug-26	Not Started
CON-98937	Install Sound Clock System Components-1st Floor	3	3	24-Jul-26	28-Jul-26	2			24-Jul-26	28-Jul-26	28-Jul-26	30-Jul-26	Not Started
SUB-2330	Prepare & Submit Remedial Closure Report	3	3	27-Jul-26	29-Jul-26	42			27-Jul-26	29-Jul-26	24-Sep-26	28-Sep-26	Not Started
CON-5400	Install Trench Drain - Drainage Work - Building Perimeter	1	1	27-Jul-26	27-Jul-26	0			27-Jul-26	27-Jul-26	27-Jul-26	27-Jul-26	Not Started
MIL-2742	Permanent Power Available	0	0		27-Jul-26	11				27-Jul-26		11-Aug-26	Not Started
CON-5300	Install Grease Interceptors - 1st Floor	5	5	28-Jul-26	03-Aug-26	32			28-Jul-26	03-Aug-26	11-Sep-26	17-Sep-26	Not Started
CON-5810	Install Wall Pads - Gymnatorium	4	4	28-Jul-26	31-Jul-26	3			28-Jul-26	31-Jul-26	31-Jul-26	05-Aug-26	Not Started
MIL-2592	P&D - Connection to Roof Drains	0	0	28-Jul-26		37			28-Jul-26		18-Sep-26		Not Started
CLO-1240	Elevator Sump Pump Testing & Commissioning	21	21	28-Jul-26	25-Aug-26	11			28-Jul-26	25-Aug-26	12-Aug-26	10-Sep-26	Not Started
CLO-1270	Water Heater Testing & Commissioning	21	21	28-Jul-26	25-Aug-26	11			28-Jul-26	25-Aug-26	12-Aug-26	10-Sep-26	Not Started
CON-9160	Excavate for Footings - Playground Area & Fences - Building Perimeter	2	2	28-Jul-26	29-Jul-26	0			28-Jul-26	29-Jul-26	28-Jul-26	29-Jul-26	Not Started
CON-9010	Remove Steel Plate Protection over NYPA Easement - Playground Area & Fences - Building Perimeter	1	1	28-Jul-26	28-Jul-26	7			28-Jul-26	28-Jul-26	06-Aug-26	06-Aug-26	Not Started
CON-5430	Install Hot Glycol / Hot Water Cabinet Heater (CUH) -5th Floor	4	4	29-Jul-26	03-Aug-26	6			29-Jul-26	03-Aug-26	06-Aug-26	11-Aug-26	Not Started
CON-6030	Install Signages-3rd Floor	5	5	29-Jul-26	04-Aug-26	42			29-Jul-26	04-Aug-26	28-Sep-26	02-Oct-26	Not Started
CON-5830	Install Fire alarm Sensors and Devises -5th Floor	5	5	29-Jul-26	04-Aug-26	2			29-Jul-26	04-Aug-26	31-Jul-26	06-Aug-26	Not Started
CLO-1220	Emergency Generator Electric Load Test	3	3	29-Jul-26	31-Jul-26	7			29-Jul-26	31-Jul-26	07-Aug-26	11-Aug-26	Not Started
CON-5320	Install Door Curtains DC - Mechanical Work - 1st Floor	7	7	29-Jul-26	06-Aug-26	22			29-Jul-26	06-Aug-26	28-Aug-26	08-Sep-26	Not Started
CON-5450	Install Air Conditioning Unit AC - Mechanical Work - 3rd Floor	4	4	29-Jul-26	03-Aug-26	2			29-Jul-26	03-Aug-26	31-Jul-26	05-Aug-26	Not Started
CON-5460	Install Convector Heater CV - Mechanical Work - 4th Floor	3	3	29-Jul-26	31-Jul-26	3			29-Jul-26	31-Jul-26	03-Aug-26	05-Aug-26	Not Started
CON-98887	Install Auxiliary System Components-1st Floor	4	4	29-Jul-26	03-Aug-26	2			29-Jul-26	03-Aug-26	31-Jul-26	05-Aug-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-6110	Install Boiler B-2-Boiler Room	5	5	30-Jul-26	05-Aug-26	5			30-Jul-26	05-Aug-26	06-Aug-26	12-Aug-26	Not Started
CON-6120	Install Air Separator Units (AS-1 , AS-2 & AS-3)	2	2	30-Jul-26	31-Jul-26	5			30-Jul-26	31-Jul-26	06-Aug-26	07-Aug-26	Not Started
CON-6130	Install Boiler Condensate ACID Neutralization Tubes -Boiler Room	2	2	30-Jul-26	31-Jul-26	13			30-Jul-26	31-Jul-26	18-Aug-26	19-Aug-26	Not Started
CON-5520	Install Acoustical Ceiling Tiles-4th Floor	5	5	30-Jul-26	05-Aug-26	0			30-Jul-26	05-Aug-26	30-Jul-26	05-Aug-26	Not Started
CON-6070	Install Furniture & Milling Work (Contractor Provided & Installed) -4th Floor	5	5	30-Jul-26	05-Aug-26	41			30-Jul-26	05-Aug-26	28-Sep-26	02-Oct-26	Not Started
CON-6080	Install Flooring Tiles-1st Floor	5	5	30-Jul-26	05-Aug-26	11			30-Jul-26	05-Aug-26	14-Aug-26	20-Aug-26	Not Started
CON-5750	Install IPDVS Devices -4th Floor	9	9	30-Jul-26	11-Aug-26	0			30-Jul-26	11-Aug-26	30-Jul-26	11-Aug-26	Not Started
APP-2330	Review & Approve Remedial Closure Report	21	21	30-Jul-26	19-Aug-26	61			30-Jul-26	19-Aug-26	29-Sep-26	19-Oct-26	Not Started
CON-9050	Install Furniture & Milling Work (Owner Provided & Installed) -4th Floor	5	5	30-Jul-26	05-Aug-26	41			30-Jul-26	05-Aug-26	28-Sep-26	02-Oct-26	Not Started
CON-9190	F/R/P Playground Equipment Footings - Playground Area & Fences - Building Perimeter	2	2	30-Jul-26	31-Jul-26	0			30-Jul-26	31-Jul-26	30-Jul-26	31-Jul-26	Not Started
CON-99267	Install Rolling Doors-1st Floor	3	3	30-Jul-26	03-Aug-26	13			30-Jul-26	03-Aug-26	18-Aug-26	20-Aug-26	Not Started
CON-6200	Install Expansion Tanks (ET-1 , ET-2 & ET-3)	2	2	03-Aug-26	04-Aug-26	13			03-Aug-26	04-Aug-26	20-Aug-26	21-Aug-26	Not Started
CON-6210	Install Glycol Make-up Units (GF-1 & GF-2 & GF-3)	2	2	03-Aug-26	04-Aug-26	5			03-Aug-26	04-Aug-26	10-Aug-26	11-Aug-26	Not Started
CON-6220	Install Reduced Pressure Zone (RPZ) Devices -Boiler Room	2	2	03-Aug-26	04-Aug-26	13			03-Aug-26	04-Aug-26	20-Aug-26	21-Aug-26	Not Started
CON-5970	Install Retractable Basketball Goal Assembly -Gymnatorium	3	3	03-Aug-26	05-Aug-26	3			03-Aug-26	05-Aug-26	06-Aug-26	10-Aug-26	Not Started
PER-2640	Obtain Emergency Generator Permit	5	5	03-Aug-26	07-Aug-26	49			03-Aug-26	07-Aug-26	13-Oct-26	19-Oct-26	Not Started
CON-5470	Install Flush Concrete Curb - Playground Area & Fences - Building Perimeter	3	3	03-Aug-26	05-Aug-26	0			03-Aug-26	05-Aug-26	03-Aug-26	05-Aug-26	Not Started
CLO-1250	Emergency Generator Testing & Commissioning	21	21	03-Aug-26	31-Aug-26	7			03-Aug-26	31-Aug-26	12-Aug-26	10-Sep-26	Not Started
MIL-2692	Building HVAC Flush-out	0	0		03-Aug-26	6				03-Aug-26		11-Aug-26	Not Started
CON-6090	Install Plumbing Fixtures -5th Floor	7	7	04-Aug-26	12-Aug-26	46			04-Aug-26	12-Aug-26	08-Oct-26	19-Oct-26	Not Started
CON-5620	Install Air Conditioning Unit AC -	4	4	04-Aug-26	07-Aug-26	2			04-Aug-26	07-Aug-26	06-Aug-26	11-Aug-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-5590	Install Exhaust Fan EF - Mechanical Work - 5th Floor	4	4	04-Aug-26	07-Aug-26	20			04-Aug-26	07-Aug-26	01-Sep-26	04-Sep-26	Not Started
CON-5420	Install Asphalt Pavement - Playground Area & Fences - Building Perimeter	2	2	04-Aug-26	05-Aug-26	3			04-Aug-26	05-Aug-26	07-Aug-26	10-Aug-26	Not Started
CON-98837	Install Intrusion System Components-1st Floor	4	4	04-Aug-26	07-Aug-26	2			04-Aug-26	07-Aug-26	06-Aug-26	11-Aug-26	Not Started
CLO-1230	Air Handling Unit Testing & Commissioning	21	21	04-Aug-26	01-Sep-26	6			04-Aug-26	01-Sep-26	12-Aug-26	10-Sep-26	Not Started
CON-5950	Install Fire alarm Sensors and Devises -1st Floor	3	3	05-Aug-26	07-Aug-26	2			05-Aug-26	07-Aug-26	07-Aug-26	11-Aug-26	Not Started
CLO-1190	Pre-Elevator Test Inspection	5	5	05-Aug-26	11-Aug-26	12			05-Aug-26	11-Aug-26	21-Aug-26	27-Aug-26	Not Started
CLO-1290	Glycol System Testing & Commissioning	21	21	05-Aug-26	02-Sep-26	5			05-Aug-26	02-Sep-26	12-Aug-26	10-Sep-26	Not Started
CON-6260	Install Heat Exchanger -Boiler Room	2	2	06-Aug-26	07-Aug-26	12			06-Aug-26	07-Aug-26	24-Aug-26	25-Aug-26	Not Started
CON-6100	Install Jockey Pump (JP-1) -1st Floor	10	10	06-Aug-26	19-Aug-26	12			06-Aug-26	19-Aug-26	24-Aug-26	04-Sep-26	Not Started
CON-5670	Install Acoustical Ceiling Tiles-5th Floor	5	5	06-Aug-26	12-Aug-26	0			06-Aug-26	12-Aug-26	06-Aug-26	12-Aug-26	Not Started
CON-6160	Install Signages-4th Floor	5	5	06-Aug-26	12-Aug-26	41			06-Aug-26	12-Aug-26	05-Oct-26	09-Oct-26	Not Started
CON-6180	Install Plumbing Fixtures-1st Floor	5	5	06-Aug-26	12-Aug-26	36			06-Aug-26	12-Aug-26	28-Sep-26	02-Oct-26	Not Started
CON-6020	Install 8" Acoustic Block Painted-Gymnatorium	7	7	06-Aug-26	14-Aug-26	3			06-Aug-26	14-Aug-26	11-Aug-26	19-Aug-26	Not Started
CON-5600	Install Concrete Pavement Pedestrian Ramp With Painted Black Handrails - Playground Area & Fences - Building Perimeter	3	3	06-Aug-26	10-Aug-26	0			06-Aug-26	10-Aug-26	06-Aug-26	10-Aug-26	Not Started
CON-5490	Install Convector Heater CV - Mechanical Work - 1st Floor	7	7	07-Aug-26	17-Aug-26	22			07-Aug-26	17-Aug-26	09-Sep-26	17-Sep-26	Not Started
MIL-1680	Emergency Generator Final Sign-off	0	0		07-Aug-26	49				07-Aug-26		19-Oct-26	Not Started
MIL-2642	Finish Fire Alarm Signoff	0	0		07-Aug-26	2				07-Aug-26		11-Aug-26	Not Started
MIL-2962	Finish Fire Alarm Inspection	0	0		07-Aug-26	2				07-Aug-26		11-Aug-26	Not Started
CON-6290	Install Hot Glycol Units Heaters (UH-5-1, UH-5-2)	2	2	10-Aug-26	11-Aug-26	12			10-Aug-26	11-Aug-26	26-Aug-26	27-Aug-26	Not Started
CLO-1020	Electrical System Testing & Commissioning	21	21	10-Aug-26	08-Sep-26	2			10-Aug-26	08-Sep-26	12-Aug-26	10-Sep-26	Not Started
CON-5630	Install Convector Heater CV -	3	3	10-Aug-26	12-Aug-26	20			10-Aug-26	12-Aug-26	08-Sep-26	10-Sep-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
MIL-2802	Provision of Training Schedules (30 days prior to start of Training)	0	0	10-Aug-26		219			10-Aug-26		23-Jul-27		Not Started
CLO-1260	HVAC Split System Testing & Commissioning	21	21	10-Aug-26	08-Sep-26	2			10-Aug-26	08-Sep-26	12-Aug-26	10-Sep-26	Not Started
CLO-1280	Fire Alarm Testing & Commissioning	21	21	10-Aug-26	08-Sep-26	2			10-Aug-26	08-Sep-26	12-Aug-26	10-Sep-26	Not Started
MIL-2702	Finish Concrete Work	0	0		10-Aug-26	0				10-Aug-26		10-Aug-26	Not Started
CON-5650	Install Playground Rubber Tile Safety Surface - Playground Area & Fences - Building Perimeter	3	3	11-Aug-26	13-Aug-26	0			11-Aug-26	13-Aug-26	11-Aug-26	13-Aug-26	Not Started
MIL-2822	Elevator Ready for Testing	0	0		11-Aug-26	12				11-Aug-26		27-Aug-26	Not Started
CON-6330	Install Heat Pump Electric Hot Water Heater (HPWH#1&2)-Boiler Room	2	2	12-Aug-26	13-Aug-26	12			12-Aug-26	13-Aug-26	28-Aug-26	31-Aug-26	Not Started
CON-6010	Install IPDVS Devices -5th Floor	9	9	12-Aug-26	24-Aug-26	0			12-Aug-26	24-Aug-26	12-Aug-26	24-Aug-26	Not Started
CLO-1000	Elevator Testing & Commissioning	20	20	12-Aug-26	09-Sep-26	12			12-Aug-26	09-Sep-26	28-Aug-26	25-Sep-26	Not Started
CON-99217	Install Bleachers -Gymnatorium	3	3	12-Aug-26	14-Aug-26	5			12-Aug-26	14-Aug-26	19-Aug-26	21-Aug-26	Not Started
CON-6060	Install Final Coat Painting -5th Floor	6	6	13-Aug-26	20-Aug-26	0			13-Aug-26	20-Aug-26	13-Aug-26	20-Aug-26	Not Started
CON-6340	Install Exhaust Fans -Boiler Room	2	2	14-Aug-26	17-Aug-26	12			14-Aug-26	17-Aug-26	01-Sep-26	02-Sep-26	Not Started
CON-6350	Install Primary Hot Water Pump (GHWP 1 to 3) -Boiler Room	2	2	14-Aug-26	17-Aug-26	12			14-Aug-26	17-Aug-26	01-Sep-26	02-Sep-26	Not Started
CON-6360	Install Primary Chilled Water Pump (GCHWP-1&2)-Boiler Room	2	2	14-Aug-26	17-Aug-26	12			14-Aug-26	17-Aug-26	01-Sep-26	02-Sep-26	Not Started
CON-5800	Install Painted Asphalt Pavement & Painted Games On Asphalt Surface - Playground Area & Fences - Building Perimeter	3	3	14-Aug-26	18-Aug-26	0			14-Aug-26	18-Aug-26	14-Aug-26	18-Aug-26	Not Started
CON-6230	Install Gym Equipment -Gymnatorium -Gymnatorium	6	6	17-Aug-26	24-Aug-26	5			17-Aug-26	24-Aug-26	24-Aug-26	31-Aug-26	Not Started
CON-6240	Install Fine Tube Radiator FTR - Gymnatorium	5	5	17-Aug-26	21-Aug-26	6			17-Aug-26	21-Aug-26	25-Aug-26	31-Aug-26	Not Started
CON-6250	Install Hydraulic Vertical Wheelchair Lift -Gymnatorium	8	8	17-Aug-26	26-Aug-26	3			17-Aug-26	26-Aug-26	20-Aug-26	31-Aug-26	Not Started
CON-6400	Install Secondary Hot Water Pump(HWP-1&2)-Boiler Room	2	2	18-Aug-26	19-Aug-26	12			18-Aug-26	19-Aug-26	03-Sep-26	04-Sep-26	Not Started
CON-6410	Install Electric Unit Heater (EUH-3) - Boiler Room	2	2	18-Aug-26	19-Aug-26	20			18-Aug-26	19-Aug-26	16-Sep-26	17-Sep-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-6420	Install Branch Panels (BRPP) -Boiler Room	2	2	18-Aug-26	19-Aug-26	20			18-Aug-26	19-Aug-26	16-Sep-26	17-Sep-26	Not Started
CON-5850	Install Colored Athletic Wearing Surface Color - Playground Area & Fences - Building Perimeter	2	2	19-Aug-26	20-Aug-26	0			19-Aug-26	20-Aug-26	19-Aug-26	20-Aug-26	Not Started
CLO-1160	Sprinkler/Domestic Booster Pumps Testing & Commissioning	14	14	20-Aug-26	09-Sep-26	12			20-Aug-26	09-Sep-26	08-Sep-26	25-Sep-26	Not Started
CON-6150	Install Furniture & Milling Work (Contractor Provided & Installed) -5th Floor	4	4	21-Aug-26	26-Aug-26	2			21-Aug-26	26-Aug-26	25-Aug-26	28-Aug-26	Not Started
CON-6170	Install Final Coat Painting-1st Floor	6	6	21-Aug-26	28-Aug-26	0			21-Aug-26	28-Aug-26	21-Aug-26	28-Aug-26	Not Started
CON-5990	Install Playground Equipment - Playground Area & Fences - Building Perimeter	7	7	21-Aug-26	31-Aug-26	0			21-Aug-26	31-Aug-26	21-Aug-26	31-Aug-26	Not Started
CON-9060	Install Furniture & Milling Work (Owner Provided & Installed) -5th Floor	4	4	21-Aug-26	26-Aug-26	2			21-Aug-26	26-Aug-26	25-Aug-26	28-Aug-26	Not Started
CON-6040	Install IPDVS Devices -1st Floor	7	7	25-Aug-26	02-Sep-26	0			25-Aug-26	02-Sep-26	25-Aug-26	02-Sep-26	Not Started
CON-9150	Install LED Theatrical Lighting -Gymnatorium	4	4	25-Aug-26	28-Aug-26	34			25-Aug-26	28-Aug-26	14-Oct-26	19-Oct-26	Not Started
CON-6280	Install Signages- 5th Floor	5	5	27-Aug-26	02-Sep-26	31			27-Aug-26	02-Sep-26	13-Oct-26	19-Oct-26	Not Started
CON-6390	Install Auditorium Television Studio Dimming System -Gymnatorium	7	7	27-Aug-26	04-Sep-26	3			27-Aug-26	04-Sep-26	01-Sep-26	10-Sep-26	Not Started
MIL-2672	Finish Painting	0	0		28-Aug-26	0				28-Aug-26		28-Aug-26	Not Started
CON-5880	Install Acoustical Ceiling Tiles -1st Floor	5	5	31-Aug-26	04-Sep-26	29			31-Aug-26	04-Sep-26	13-Oct-26	19-Oct-26	Not Started
CON-6300	Install Furniture & Milling Work (Contractor Provided & Installed) -1st Floor	4	4	31-Aug-26	03-Sep-26	0			31-Aug-26	03-Sep-26	31-Aug-26	03-Sep-26	Not Started
CON-6310	Install Security Screens & Barriers-1st Floor	3	3	31-Aug-26	02-Sep-26	1			31-Aug-26	02-Sep-26	01-Sep-26	03-Sep-26	Not Started
CON-6320	Install Cafeteria Equipment-1st Floor	4	4	31-Aug-26	03-Sep-26	0			31-Aug-26	03-Sep-26	31-Aug-26	03-Sep-26	Not Started
CON-9020	Install Furniture & Milling Work (Owner Provided & Installed) -1st Floor	3	3	31-Aug-26	02-Sep-26	1			31-Aug-26	02-Sep-26	01-Sep-26	03-Sep-26	Not Started
CON-6140	Install Basketball Hoop - Playground Area & Fences - Building Perimeter	1	1	01-Sep-26	01-Sep-26	0			01-Sep-26	01-Sep-26	01-Sep-26	01-Sep-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
CON-6190	Install Wrought Iron Fence Double Gate - Playground Area - Building Perimeter	3	3	02-Sep-26	04-Sep-26	0			02-Sep-26	04-Sep-26	02-Sep-26	04-Sep-26	Not Started
CLO-1130	IPDVS System Testing & Commissioning	11	11	03-Sep-26	18-Sep-26	0			03-Sep-26	18-Sep-26	03-Sep-26	18-Sep-26	Not Started
CON-6370	Install Signages-1st Floor	4	4	04-Sep-26	10-Sep-26	0			04-Sep-26	10-Sep-26	04-Sep-26	10-Sep-26	Not Started
CON-6380	Install Food Service Equipment-1st Floor	5	5	04-Sep-26	11-Sep-26	25			04-Sep-26	11-Sep-26	13-Oct-26	19-Oct-26	Not Started
MIL-2722	Start Kitchen	0	0	04-Sep-26		25			04-Sep-26		13-Oct-26		Not Started
MIL-2662	Finishes and Ceiling Complete	0	0		04-Sep-26	29				04-Sep-26		19-Oct-26	Not Started
CON-6270	Install Chain Link Fence - Playground Area & Fences - Building Perimeter	3	3	08-Sep-26	10-Sep-26	0			08-Sep-26	10-Sep-26	08-Sep-26	10-Sep-26	Not Started
CLO-1300	Provide Training	10	10	09-Sep-26	22-Sep-26	198			09-Sep-26	22-Sep-26	23-Jul-27	05-Aug-27	Not Started
CON-5040	Dismantle Hoist	2	2	10-Sep-26	11-Sep-26	21			10-Sep-26	11-Sep-26	09-Oct-26	13-Oct-26	Not Started
CLO-1170	Sprinkler/Domestic Booster Pumps Inspection	3	3	10-Sep-26	14-Sep-26	12			10-Sep-26	14-Sep-26	28-Sep-26	30-Sep-26	Not Started
CLO-1200	Elevator DOB Inspection	5	5	10-Sep-26	16-Sep-26	12			10-Sep-26	16-Sep-26	28-Sep-26	02-Oct-26	Not Started
MIL-1470	Finish Site Work	0	0		10-Sep-26	0				10-Sep-26		10-Sep-26	Not Started
CLO-1030	Pre-Final Clean-Out	5	5	11-Sep-26	17-Sep-26	0			11-Sep-26	17-Sep-26	11-Sep-26	17-Sep-26	Not Started
CON-5170	Demolish Hoist Pad	2	2	14-Sep-26	15-Sep-26	21			14-Sep-26	15-Sep-26	14-Oct-26	15-Oct-26	Not Started
CLO-1180	Sprinkler/Domestic Booster Pumps Sign-offs	0	0		14-Sep-26	16				14-Sep-26		30-Sep-26	Not Started
CLO-1150	FDNY Inspection	12	12	15-Sep-26	30-Sep-26	12			15-Sep-26	30-Sep-26	01-Oct-26	19-Oct-26	Not Started
CON-5250	Hoist In-Fill	2	2	16-Sep-26	17-Sep-26	21			16-Sep-26	17-Sep-26	16-Oct-26	19-Oct-26	Not Started
PER-2650	Elevator Equipment Use Permit	10	10	17-Sep-26	30-Sep-26	12			17-Sep-26	30-Sep-26	05-Oct-26	19-Oct-26	Not Started
CLO-1040	Pre-TCO Inspection	11	11	18-Sep-26	02-Oct-26	0			18-Sep-26	02-Oct-26	18-Sep-26	02-Oct-26	Not Started
MIL-1620	IPDVS Work Finish	0	0		18-Sep-26*	0				18-Sep-26		18-Sep-26	Not Started
MIL-2652	Finish Mechanical and Electrical System Commissioning	0	0		18-Sep-26	20				18-Sep-26		19-Oct-26	Not Started
MIL-2772	Performance test for all mechanical equipment and low voltage systems	0	0		18-Sep-26	20				18-Sep-26		19-Oct-26	Not Started
MIL-2792	Commissioning for all mechanical equipment and low voltage systems	0	0		18-Sep-26	20				18-Sep-26		19-Oct-26	Not Started
MIL-1650	FDNY Inspection Finish	0	0		30-Sep-26	12				30-Sep-26		19-Oct-26	Not Started

Activities Report

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Activity Status
MIL-1670	Elevator Final Sign-off	0	0		30-Sep-26	12				30-Sep-26		19-Oct-26	Not Started
CLO-1110	Pre-TCO Punchlist	10	10	05-Oct-26	19-Oct-26	0			05-Oct-26	19-Oct-26	05-Oct-26	19-Oct-26	Not Started
MIL-1510	TCO	0	0		19-Oct-26*	0				19-Oct-26		19-Oct-26	Not Started
CLO-1050	Pre-Substantial Punchlist	105	105	20-Oct-26	17-Apr-27	0			20-Oct-26	17-Apr-27	20-Oct-26	17-Apr-27	Not Started
MIL-1550	Substantial Completion	0	0		17-Apr-27*	0				17-Apr-27		17-Apr-27	Not Started
CLO-1060	Prepare & Submit O&M Manuals	30	30	19-Apr-27	01-Jun-27	0			19-Apr-27	01-Jun-27	19-Apr-27	01-Jun-27	Not Started
MIL-2782	Submission of Operations and Maintenance Manuals	0	0		01-Jun-27	51				01-Jun-27		13-Aug-27	Not Started
CLO-1070	Prepare & Submit As-Built Drawings	30	30	02-Jun-27	15-Jul-27	0			02-Jun-27	15-Jul-27	02-Jun-27	15-Jul-27	Not Started
CLO-1080	Final Inspection	5	5	16-Jul-27	22-Jul-27	0			16-Jul-27	22-Jul-27	16-Jul-27	22-Jul-27	Not Started
CLO-1090	Final Clean Out	10	10	23-Jul-27	05-Aug-27	0			23-Jul-27	05-Aug-27	23-Jul-27	05-Aug-27	Not Started
CLO-1100	Demobilization	10	10	06-Aug-27	15-Aug-27	0			06-Aug-27	15-Aug-27	06-Aug-27	15-Aug-27	Not Started
MIL-1560	Final Completion	0	0		15-Aug-27*	0				15-Aug-27		15-Aug-27	Not Started

APPENDIX 13
Total Float Report

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-1000	Mobilization	4	30-Sep-25	03-Oct-25	Not Started	0
CON-98787	Install Steel Columns -1st Floor	7	05-Dec-25	15-Dec-25	Not Started	0
CON-1110	Install Metal Deck Slab -2nd Floor	4	22-Dec-25	26-Dec-25	Not Started	0
CON-1070	F/R/P SOG -1st Floor	10	20-Nov-25	04-Dec-25	Not Started	0
CON-1410	Install Duct Risers-2nd Floor	1	23-Feb-26	23-Feb-26	Not Started	0
CON-1480	Rough-in Duct Work -2nd Floor	4	24-Feb-26	27-Feb-26	Not Started	0
CON-1880	Rough-in Refrigerant Piping-2nd Floor	7	02-Mar-26	10-Mar-26	Not Started	0
CON-3010	Pour Sloped Concrete Fill -Roof Floor	2	09-Apr-26	10-Apr-26	Not Started	0
CON-3430	Install Hot Fluid Applied Membrane -Roof Floor	3	21-Apr-26	23-Apr-26	Not Started	0
CON-3730	Install 6" Thick Rigid Insulation -Roof Floor	3	29-Apr-26	01-May-26	Not Started	0
CON-3600	Install Drainage Panels- Roof Floor	3	24-Apr-26	28-Apr-26	Not Started	0
CON-2920	Pour Sloped Concrete Fill -5th Floor Roof	2	07-Apr-26	08-Apr-26	Not Started	0
CON-4030	Install Gypsum Board Walls-2nd Floor	5	27-May-26	02-Jun-26	Not Started	0
CON-4370	Install Gypsum Board Ceiling -2nd Floor	6	03-Jun-26	10-Jun-26	Not Started	0
CON-4630	Install Gypsum Board Ceiling-3rd Floor	6	11-Jun-26	18-Jun-26	Not Started	0
CON-5520	Install Acoustical Ceiling Tiles-4th Floor	5	30-Jul-26	05-Aug-26	Not Started	0
CON-5670	Install Acoustical Ceiling Tiles-5th Floor	5	06-Aug-26	12-Aug-26	Not Started	0
CON-6060	Install Final Coat Painting -5th Floor	6	13-Aug-26	20-Aug-26	Not Started	0
CON-5900	Install Final Coat Painting-4th Floor	6	22-Jul-26	29-Jul-26	Not Started	0
CON-5110	Install First Coat Painting-3rd Floor	5	22-Jun-26	26-Jun-26	Not Started	0
CON-5350	Install Door Frames & Doors-3rd Floor	5	29-Jun-26	06-Jul-26	Not Started	0
CON-5550	Install Flooring Tiles-3rd Floor	5	07-Jul-26	13-Jul-26	Not Started	0
CON-5700	Install Final Coat Painting-3rd Floor	6	14-Jul-26	21-Jul-26	Not Started	0
CON-4830	Install First Coat Painting-2nd Floor	5	11-Jun-26	17-Jun-26	Not Started	0
CON-5120	Install Door Frames & Doors-2nd Floor	5	18-Jun-26	25-Jun-26	Not Started	0
CON-5360	Install Flooring Tiles-2nd Floor	5	26-Jun-26	02-Jul-26	Not Started	0
CON-5560	Install Final Coat Painting-2nd Floor	6	06-Jul-26	13-Jul-26	Not Started	0
CON-6170	Install Final Coat Painting-1st Floor	6	21-Aug-26	28-Aug-26	Not Started	0
CON-6300	Install Furniture & Milling Work (Contractor Provided & Installed) -1st Floor	4	31-Aug-26	03-Sep-26	Not Started	0
CON-6370	Install Signages-1st Floor	4	04-Sep-26	10-Sep-26	Not Started	0
CON-1050	Install Underground Conduits & Wires -1st Floor	6	12-Nov-25	19-Nov-25	Not Started	0
CON-2640	Install Grounding Bars - 3rd Floor IDF Room	5	27-Mar-26	02-Apr-26	Not Started	0
CON-2800	Install Data rack - 3rd Floor IDF Room	8	03-Apr-26	14-Apr-26	Not Started	0
CON-3250	Install Voice Rack - 3rd Floor IDF Room	5	15-Apr-26	21-Apr-26	Not Started	0
CON-4110	Install Voice Rack - 1st Floor MDF Room	6	07-May-26	14-May-26	Not Started	0
CON-4510	Install Sound Rack - 1st Floor MDF Room	6	15-May-26	22-May-26	Not Started	0
CON-4520	Install Data Rack - 1st Floor MDF Room	6	26-May-26	02-Jun-26	Not Started	0
CON-3740	Install Ground Bus Bar - 1st Floor MDF Room	6	29-Apr-26	06-May-26	Not Started	0
CON-6040	Install IPDVS Devices -1st Floor	7	25-Aug-26	02-Sep-26	Not Started	0
MIL-1340	BLDG Tight	0		06-May-26	Not Started	0
CON-2180	Rough-in Power Conduits -2nd Floor	6	11-Mar-26	18-Mar-26	Not Started	0
CON-5130	Install Lighting Fixtures -2nd Floor	5	18-Jun-26	25-Jun-26	Not Started	0
CON-5310	Install Fire alarm Sensors and Devises -2nd Floor	5	26-Jun-26	02-Jul-26	Not Started	0
CON-5140	Install IPDVS Devices -2nd Floor	9	06-Jul-26	16-Jul-26	Not Started	0
CON-6010	Install IPDVS Devices -5th Floor	9	12-Aug-26	24-Aug-26	Not Started	0
CON-5750	Install IPDVS Devices -4th Floor	9	30-Jul-26	11-Aug-26	Not Started	0
CON-5440	Install IPDVS Devices -3rd Floor	9	17-Jul-26	29-Jul-26	Not Started	0
CON-4260	Install Door Frames-Mockup Room	2	12-May-26	13-May-26	Not Started	0

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-4640	Flooring Finishes-Mockup Room	2	18-May-26	19-May-26	Not Started	0
CON-4750	Paint Second coat-Mockup Room	2	20-May-26	21-May-26	Not Started	0
CON-4480	Paint First coat -Mockup Room	2	14-May-26	15-May-26	Not Started	0
CON-4380	Install Doors & Hardware-Mockup Room	3	11-May-26	13-May-26	Not Started	0
CON-4930	Install Furniture & Signs -Mockup Room	2	22-May-26	26-May-26	Not Started	0
CON-4040	Install Walls GWB-Mockup Room	3	07-May-26	11-May-26	Not Started	0
MIL-1360	Start Mockup Room Work	0	07-May-26		Not Started	0
MIL-1420	Finish Mockup Room	0		26-May-26	Not Started	0
MIL-1430	Start Architecture Finishes	0	07-May-26		Not Started	0
CLO-1030	Pre-Final Clean-Out	5	11-Sep-26	17-Sep-26	Not Started	0
CLO-1040	Pre-TCO Inspection	11	18-Sep-26	02-Oct-26	Not Started	0
MIL-1510	TCO	0		19-Oct-26*	Not Started	0
CLO-1050	Pre-Substantial Punchlist	105	20-Oct-26	17-Apr-27	Not Started	0
MIL-1550	Substantial Completion	0		17-Apr-27*	Not Started	0
MIL-1060	Mobilization Start	0	30-Sep-25		Not Started	0
MIL-1120	Metal Decking Start	0	22-Dec-25		Not Started	0
MIL-1180	MEP Risers Start	0	23-Feb-26		Not Started	0
MIL-1210	Duct Rough-ins Start	0	24-Feb-26		Not Started	0
MIL-1230	5th Floor Roofing Start	0	07-Apr-26		Not Started	0
MIL-1200	Main Roofing Start	0	09-Apr-26		Not Started	0
MIL-1470	Finish Site Work	0		10-Sep-26	Not Started	0
MIL-1440	Start Gypsum Board	0	27-May-26		Not Started	0
MIL-1000	NTP	0	30-Sep-24		Not Started	0
CLO-1060	Prepare & Submit O&M Manuals	30	19-Apr-27	01-Jun-27	Not Started	0
CLO-1070	Prepare & Submit As-Built Drawings	30	02-Jun-27	15-Jul-27	Not Started	0
CLO-1080	Final Inspection	5	16-Jul-27	22-Jul-27	Not Started	0
CLO-1090	Final Clean Out	10	23-Jul-27	05-Aug-27	Not Started	0
CLO-1100	Demobilization	10	06-Aug-27	15-Aug-27	Not Started	0
MIL-1560	Final Completion	0		15-Aug-27*	Not Started	0
MIL-1030	Project Duration(From NTP till TCO)	750	30-Sep-24	19-Oct-26	Not Started	0
MIL-1040	Project Duration(From NTP till Substantial Completion)	930	30-Sep-24	17-Apr-27	Not Started	0
PRE-2540	SCA Work Notification	7	23-Sep-25	29-Sep-25	Not Started	0
PRE-1660	DOB Permit & Insurance	3	25-Sep-25	29-Sep-25	Not Started	0
PRE-1460	Obtain Construction Fences Permit	3	25-Sep-25	29-Sep-25	Not Started	0
PRE-2550	Obtain CCD1	3	25-Sep-25	29-Sep-25	Not Started	0
PRE-2570	Obtain Sidewalk Shed Permits	3	25-Sep-25	29-Sep-25	Not Started	0
CON-2330	Rough-in Low-Voltage Conduits -2nd Floor	6	19-Mar-26	26-Mar-26	Not Started	0
CLO-1110	Pre-TCO Punchlist	10	05-Oct-26	19-Oct-26	Not Started	0
CON-1060	Backfilling & Compaction -1st Floor	6	12-Nov-25	19-Nov-25	Not Started	0
CLO-1120	MDF & IDF Rooms Testing & Commissioning	12	06-Jul-26	21-Jul-26	Not Started	0
CLO-1130	IPDVS System Testing & Commissioning	11	03-Sep-26	18-Sep-26	Not Started	0
MIL-1600	MDF Work Finish	0		21-Jul-26*	Not Started	0
MIL-1610	IDF Work Finish	0		21-Jul-26*	Not Started	0
MIL-1620	IPDVS Work Finish	0		18-Sep-26*	Not Started	0
CON-7740	Protection Of All Overhead & Underground Utilities	263	30-Sep-25	19-Oct-26	Not Started	0
CON-3210	Install Fluid-Applied Protected Membrane Mock-Up	2	13-Apr-26	14-Apr-26	Not Started	0
CON-3300	Approve Fluid-Applied Protected Membrane Mock-Up	4	15-Apr-26	20-Apr-26	Not Started	0
CON-2110	Install & Windows Mock-Up	3	11-Mar-26	13-Mar-26	Not Started	0

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-2210	Approve Windows Mock-Up	2	16-Mar-26	17-Mar-26	Not Started	0
CON-2220	Install Storefront System Mock-Up	3	18-Mar-26	20-Mar-26	Not Started	0
CON-2240	Approve Storefront System Mock-Up	2	23-Mar-26	24-Mar-26	Not Started	0
CON-3840	Roof Flood Test -Roof Floor	3	04-May-26	06-May-26	Not Started	0
MIL-1710	Complete Mobilization	0		03-Oct-25	Not Started	0
MIL-1730	Sidewalk Sheds Dismantle Complete	0		05-May-26	Not Started	0
PRE-2630	Obtain Builders Pavement Permit	10	16-Sep-25	29-Sep-25	Not Started	0
PRE-2640	Obtain Excavation & Shoring Permit	10	16-Sep-25	29-Sep-25	Not Started	0
MIL-1770	Project Duration(From NTP till Final Completion)	1050	30-Sep-24	15-Aug-27	Not Started	0
CON-1100	Install Framing Beams -1st Floor	4	16-Dec-25	19-Dec-25	Not Started	0
CON-1040	F/R/P Concrete Walls & Beams -1st Floor	10	28-Oct-25	10-Nov-25	Not Started	0
CON-1170	Install Steel Columns -2nd Floor	3	29-Dec-25	31-Dec-25	Not Started	0
CON-1200	Install Framing Beams -2nd Floor	5	02-Jan-26	08-Jan-26	Not Started	0
CON-1210	Install Metal Deck Slab - 3rd Floor	4	09-Jan-26	14-Jan-26	Not Started	0
CON-1240	Install Steel Columns - 3rd Floor	4	15-Jan-26	21-Jan-26	Not Started	0
CON-1270	Install Framing Beams - 3rd Floor	5	22-Jan-26	28-Jan-26	Not Started	0
CON-1290	Install Metal Deck Slab - 4th Floor	4	29-Jan-26	03-Feb-26	Not Started	0
CON-1330	Install Steel Columns - 4th Floor	4	04-Feb-26	09-Feb-26	Not Started	0
CON-1370	Install Framing Beams - 4th Floor	5	10-Feb-26	17-Feb-26	Not Started	0
CON-1380	Install Metal Deck Slab - 5th Floor	3	18-Feb-26	20-Feb-26	Not Started	0
CON-1440	Install Steel Columns - 5th Floor	3	23-Feb-26	25-Feb-26	Not Started	0
CON-1550	Install Framing Beams - 5th Floor	3	26-Feb-26	02-Mar-26	Not Started	0
CON-1720	Install Metal Deck Slab -Roof Floor	2	03-Mar-26	04-Mar-26	Not Started	0
CON-1830	Install Insulated Precast Concrete Sandwich Panel - Mock Up	2	05-Mar-26	06-Mar-26	Not Started	0
CON-1990	Approve Insulated Precast Concrete Sandwich Panel - Mock Up	2	09-Mar-26	10-Mar-26	Not Started	0
CON-2380	Install Insulated Precast Concrete Sandwich Panel - West Elevation	3	25-Mar-26	27-Mar-26	Not Started	0
CON-2590	Install Windows - South Elevation	10	01-Apr-26	14-Apr-26	Not Started	0
CON-2600	Install Storefront System- South Elevation	10	01-Apr-26	14-Apr-26	Not Started	0
CON-3220	Dismantle Sidewalk Sheds- South Elevation	2	29-Apr-26	30-Apr-26	Not Started	0
CON-2420	Install Insulated Precast Concrete Sandwich Panel - South Elevation	5	25-Mar-26	31-Mar-26	Not Started	0
CON-2980	Install Windows - East Elevation	8	15-Apr-26	24-Apr-26	Not Started	0
CON-2990	Install Storefront System- East Elevation	8	15-Apr-26	24-Apr-26	Not Started	0
CON-3370	Field Testing of Windows (90%)	5	27-Apr-26	01-May-26	Not Started	0
CON-3630	Dismantle Sidewalk Sheds- East Elevation	2	04-May-26	05-May-26	Not Started	0
CON-2610	Install Insulated Precast Concrete Sandwich Panel - East Elevation	4	01-Apr-26	06-Apr-26	Not Started	0
CON-2730	Install Insulated Precast Concrete Sandwich Panel - North Elevation	4	01-Apr-26	06-Apr-26	Not Started	0
CON-4780	Install IPDVS Equipment Rack - 1st Floor MDF Room	6	16-Jun-26	24-Jun-26	Not Started	0
CON-4790	Install Ladder Rack Cable Tray- 1st Floor MDF Room	6	25-Jun-26	02-Jul-26	Not Started	0
CON-4550	Install UPS- 1st Floor MDF Room	9	03-Jun-26	15-Jun-26	Not Started	0
CON-2540	Install Ground Bus Bar - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26	Not Started	0
CON-3570	Install Main Sound Rack - 3rd Floor IDF Room	5	22-Apr-26	28-Apr-26	Not Started	0
CON-3780	Install Traffic Control Devices - 54th Avenue Street	3	01-May-26	05-May-26	Not Started	0
CON-3870	Install Traffic Control Devices - 2nd Street	5	06-May-26	12-May-26	Not Started	0
CON-4310	Install 7" Concrete Sidewalk - 2nd Street	6	16-Jun-26	24-Jun-26	Not Started	0
CON-3950	Install Pedestrian Ramps With Truncated Domes - 2nd Street	6	20-May-26	28-May-26	Not Started	0

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-4090	Remove Existing Steel Faced Curb - 2nd Street	6	29-May-26	05-Jun-26	Not Started	0
CON-4160	Install New Steel Faced Curb - 2nd Street	6	08-Jun-26	15-Jun-26	Not Started	0
CON-3900	Remove Existing Sidewalk - 2nd Street	5	13-May-26	19-May-26	Not Started	0
CON-4420	Remove Traffic Control Devices - 2nd Street	5	25-Jun-26	01-Jul-26	Not Started	0
CON-6190	Install Wrought Iron Fence Double Gate - Playground Area - Building Perimeter	3	02-Sep-26	04-Sep-26	Not Started	0
CON-5600	Install Concrete Pavement Pedestrian Ramp With Painted Black Handrails - Playground Area & Fences - Building Perimeter	3	06-Aug-26	10-Aug-26	Not Started	0
CON-6270	Install Chain Link Fence - Playground Area & Fences - Building Perimeter	3	08-Sep-26	10-Sep-26	Not Started	0
CON-5800	Install Painted Asphalt Pavement & Painted Games On Asphalt Surface - Playground Area & Fences - Building Perimeter	3	14-Aug-26	18-Aug-26	Not Started	0
CON-5650	Install Playground Rubber Tile Safety Surface - Playground Area & Fences - Building Perimeter	3	11-Aug-26	13-Aug-26	Not Started	0
CON-5990	Install Playground Equipment - Playground Area & Fences - Building Perimeter	7	21-Aug-26	31-Aug-26	Not Started	0
CON-5850	Install Colored Athletic Wearing Surface Color - Playground Area & Fences - Building Perimeter	2	19-Aug-26	20-Aug-26	Not Started	0
CON-5470	Install Flush Concrete Curb - Playground Area & Fences - Building Perimeter	3	03-Aug-26	05-Aug-26	Not Started	0
CON-6140	Install Basketball Hoop - Playground Area & Fences - Building Perimeter	1	01-Sep-26	01-Sep-26	Not Started	0
CON-4740	Install Flood Barrier Wall - Drainage Work - Building Perimeter	3	08-Jul-26	10-Jul-26	Not Started	0
CON-4980	Install 4" & 6" & 10" & 12" DIP - Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26	Not Started	0
CON-5400	Install Trench Drain - Drainage Work - Building Perimeter	1	27-Jul-26	27-Jul-26	Not Started	0
CON-5290	Install Storm Inlet With Hood & Storm Hood - Drainage Work - Building Perimeter	2	23-Jul-26	24-Jul-26	Not Started	0
CON-5190	Install Catch Basin - Drainage Work - Building Perimeter	2	21-Jul-26	22-Jul-26	Not Started	0
CON-4860	Install Drilled Caisson Supported Ventilation Structure - Drainage Work - Building Perimeter	3	13-Jul-26	15-Jul-26	Not Started	0
CON-4660	Excavation - Drainage Work - Building Perimeter	3	02-Jul-26	07-Jul-26	Not Started	0
MIL-1810	Crane Mobilization-Steel Installation start	0	05-Dec-25		Not Started	0
MIL-1830	Crane Mobilization-Precast Sandwich Panels Installation Start	0	05-Mar-26		Not Started	0
MIL-1840	Crane Mobilization-Precast Sandwich Panels Installation Finish	0		06-Apr-26	Not Started	0
CON-9898	Install Gas Permeable Aggregate -1st Floor	3	16-Oct-25	20-Oct-25	Not Started	0
CON-9888	Install Liquid Boot VI-20 Geomembrane -1st Floor	2	21-Oct-25	22-Oct-25	Not Started	0
CON-1020	Install 60 Dry MILS Liquid Boot -1st Floor	3	23-Oct-25	27-Oct-25	Not Started	0
CON-9777	Install Liquid Ultrashield G-1000 -1st Floor	2	24-Oct-25	27-Oct-25	Not Started	0
I-1010	Concrete Cast-IN-Place Inspection	86	28-Oct-25	04-Mar-26	Not Started	0
I-1040	Roofing Flood Testing Inspection	5	30-Apr-26	06-May-26	Not Started	0
I-1140	Structural Steel Inspection	58	05-Dec-25	02-Mar-26	Not Started	0
I-1150	Concrete Precast Inspection	9	25-Mar-26	06-Apr-26	Not Started	0
CON-6320	Install Cafeteria Equipment-1st Floor	4	31-Aug-26	03-Sep-26	Not Started	0
MIL-2522	Site Access	365	30-Sep-24	29-Sep-25	Not Started	0
MIL-1850	Construction Start	0	30-Sep-25		Not Started	0
PRE-2650	Obtain Permit to Enter (PTE) Amtrak	10	16-Sep-25	29-Sep-25	Not Started	0
CON-98947	Install 4" slotted schedule 80 PVC Piping -1st Floor	3	16-Oct-25	20-Oct-25	Not Started	0
MIL-2532	Submit Complete Permit Application	0		29-Sep-25	Not Started	0

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
MIL-2582	Start Concrete Placement	0	28-Oct-25		Not Started	0
MIL-2672	Finish Painting	0		28-Aug-26	Not Started	0
MIL-2702	Finish Concrete Work	0		10-Aug-26	Not Started	0
MIL-2812	Start Foundation	0	28-Oct-25		Not Started	0
PRE-2660	Obtain NYPA Permit	10	16-Sep-25	29-Sep-25	Not Started	0
MIL-2842	Issuance of Builders Pavement Permit	0		29-Sep-25	Not Started	0
MIL-2852	Issuance of Permit to Enter (PTE)	0		29-Sep-25	Not Started	0
MIL-2862	Issuance of NYPA Permit	0		29-Sep-25	Not Started	0
MIL-2872	Issuance of Construction Fences Permit	0		29-Sep-25	Not Started	0
MIL-2882	Issuance of Sidewalk Shed Permits	0		29-Sep-25	Not Started	0
MIL-2892	Issuance of CCD1	0		29-Sep-25	Not Started	0
MIL-2902	Issuance of DOB Permit & Insurance	0		29-Sep-25	Not Started	0
CON-9120	Soli Sampling	2	06-Oct-25	07-Oct-25	Not Started	0
CON-9140	Excavation	5	08-Oct-25	15-Oct-25	Not Started	0
CON-9190	F/R/P Playground Equipment Footings - Playground Area & Fences - Building Perimeter	2	30-Jul-26	31-Jul-26	Not Started	0
CON-9160	Excavate for Footings - Playground Area & Fences - Building Perimeter	2	28-Jul-26	29-Jul-26	Not Started	0
CON-9170	Install 8" Combined Water Service (2nd Street)- Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26	Not Started	0
CON-9180	Install 6" Fire Water Service (54th Avenue Street)- Drainage Work - Building Perimeter	3	16-Jul-26	20-Jul-26	Not Started	0
CON-99237	Install Flag Pole - South Elevation	10	15-Apr-26	28-Apr-26	Not Started	0
CON-3440	Install Hot Fluid Applied Membrane -5th Floor Roof	4	21-Apr-26	24-Apr-26	Not Started	1
CON-3580	Install 6" Thick Rigid Insulation -5th Floor Roof	3	27-Apr-26	29-Apr-26	Not Started	1
CON-4360	Install Gypsum Board Walls-3rd Floor	5	03-Jun-26	09-Jun-26	Not Started	1
CON-5330	Install Acoustical Ceiling Tiles-3rd Floor	5	22-Jul-26	28-Jul-26	Not Started	1
CON-5340	Install First Coat Painting-4th Floor	5	29-Jun-26	06-Jul-26	Not Started	1
CON-5540	Install Door Frames & Doors-4th Floor	5	07-Jul-26	13-Jul-26	Not Started	1
CON-5690	Install Flooring Tiles-4th Floor	5	14-Jul-26	20-Jul-26	Not Started	1
MIL-1410	Mockup Room Ready For Inspection	0		26-May-26	Not Started	1
CON-5000	Mockup Room Inspection & Punchlist	5	27-May-26	02-Jun-26	Not Started	1
MIL-1450	Start 1st Coat Painting	0	10-Jun-26		Not Started	1
CON-4700	Install Firestopping-2nd Floor	3	05-Jun-26	09-Jun-26	Not Started	1
CON-1120	Install Firestopping Mock-Up	2	01-Jun-26	02-Jun-26	Not Started	1
CON-1140	Approve Firestopping Mock-Up	2	03-Jun-26	04-Jun-26	Not Started	1
CON-3710	Roof Flood Test -5th Floor Roof	4	30-Apr-26	05-May-26	Not Started	1
MIL-1750	Start Firestopping	0	05-Jun-26		Not Started	1
CON-6310	Install Security Screens & Barriers-1st Floor	3	31-Aug-26	02-Sep-26	Not Started	1
CON-9020	Install Furniture & Milling Work (Owner Provided & Installed) -1st Floor	3	31-Aug-26	02-Sep-26	Not Started	1
CON-4670	Install Exhaust Fans -1st Floor	5	07-Jul-26	13-Jul-26	Not Started	2
CON-4870	Install Cabinet Unit Heaters With Fan CUH-1st Floor	3	14-Jul-26	16-Jul-26	Not Started	2
CON-5060	Install Hot Glycol / Hot Water Cabinet Heater (CUH) -3rd Floor	4	17-Jul-26	22-Jul-26	Not Started	2
CON-2900	Install Duct Risers-1st Floor	1	07-Apr-26	07-Apr-26	Not Started	2
CON-3120	Rough-in Duct Work -1st Floor	4	09-Apr-26	14-Apr-26	Not Started	2
CON-3460	Rough-in Hot Water Piping-1st Floor	4	15-Apr-26	20-Apr-26	Not Started	2
CON-3470	Rough-in Hot Glycol Piping-1st Floor	4	15-Apr-26	20-Apr-26	Not Started	2
CON-3480	Rough-in Chilled Glycol Piping-1st Floor	4	15-Apr-26	20-Apr-26	Not Started	2
CON-3490	Rough-in Refrigerant Piping-1st Floor	4	15-Apr-26	20-Apr-26	Not Started	2
CON-4450	Install Gypsum Board Walls-1st Floor	6	26-Jun-26	06-Jul-26	Not Started	2
CON-5090	Install Acoustical Ceiling Tiles-2nd Floor	5	14-Jul-26	20-Jul-26	Not Started	2

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-4820	Install Gypsum Board Ceiling-4th Floor	6	22-Jun-26	29-Jun-26	Not Started	2
CON-5100	Install Gypsum Board Ceiling-5th Floor	6	30-Jun-26	08-Jul-26	Not Started	2
CON-5530	Install First Coat Painting -5th Floor	5	09-Jul-26	15-Jul-26	Not Started	2
CON-6150	Install Furniture & Milling Work (Contractor Provided & Installed) -5th Floor	4	21-Aug-26	26-Aug-26	Not Started	2
CON-2400	Install Windows -West Elevation	5	30-Mar-26	03-Apr-26	Not Started	2
CON-4460	Rough-in Gas Risers -1st Floor	4	07-May-26	12-May-26	Not Started	2
CON-4590	Rough-in Domestic Water Piping-1st Floor	4	13-May-26	18-May-26	Not Started	2
CON-4690	Rough-in Sanitary & Vent Piping -1st Floor	4	19-May-26	22-May-26	Not Started	2
CON-4760	Rough-in Storm Piping -1st Floor	4	26-May-26	29-May-26	Not Started	2
CON-3760	Rough-in Power Conduits -1st Floor	4	21-Apr-26	24-Apr-26	Not Started	2
CON-5950	Install Fire alarm Sensors and Devises -1st Floor	3	05-Aug-26	07-Aug-26	Not Started	2
CON-5830	Install Fire alarm Sensors and Devises -5th Floor	5	29-Jul-26	04-Aug-26	Not Started	2
CON-5660	Install Fire alarm Sensors and Devises -4th Floor	7	20-Jul-26	28-Jul-26	Not Started	2
CON-5370	Install Lighting Fixtures -3rd Floor	6	29-Jun-26	07-Jul-26	Not Started	2
CON-5500	Install Fire alarm Sensors and Devises -3rd Floor	8	08-Jul-26	17-Jul-26	Not Started	2
CON-4180	Low Voltage Wires Pulling -1st Floor	4	01-May-26	06-May-26	Not Started	2
CON-4270	Install Gypsum Board Ceiling -Mockup Room	3	07-May-26	11-May-26	Not Started	2
CLO-1020	Electrical System Testing & Commissioning	21	10-Aug-26	08-Sep-26	Not Started	2
MIL-1290	Duct Rough-ins Finish	0		14-Apr-26	Not Started	2
MIL-1260	Plumbing Rough-ins Start	0	07-May-26		Not Started	2
MIL-1320	Plumbing Rough-ins Finish	0		29-May-26	Not Started	2
MIL-1400	Start Site Work	0	29-Apr-26		Not Started	2
CON-3070	Duct Leak Test -1st Floor	1	08-Apr-26	08-Apr-26	Not Started	2
CON-5050	Plumbing Pressure Testing -1st Floor	5	11-Jun-26	17-Jun-26	Not Started	2
CON-5210	Plumbing Piping Insulation -1st Floor	5	18-Jun-26	25-Jun-26	Not Started	2
CON-3920	Rough-in Low-Voltage Conduits-1st Floor	4	27-Apr-26	30-Apr-26	Not Started	2
CON-3930	Power Wires Pulling-1st Floor	4	27-Apr-26	30-Apr-26	Not Started	2
MIL-1740	Start Windows	0	30-Mar-26		Not Started	2
CON-3380	Install Windows -North Elevation	10	15-Apr-26	28-Apr-26	Not Started	2
CON-3390	Install Storefront System-North Elevation	10	15-Apr-26	28-Apr-26	Not Started	2
CON-4940	Install Duplex Domestic Water Booster Pump System (BP-1&BP-2) -1st Floor	8	01-Jun-26	10-Jun-26	Not Started	2
CON-4950	Install Duplex Ejector Pump System (EJ-1&EJ-2) -1st Floor	8	01-Jun-26	10-Jun-26	Not Started	2
CON-5280	Install Convector Heater CV - Mechanical Work - 3rd Floor	4	23-Jul-26	28-Jul-26	Not Started	2
CON-5450	Install Air Conditioning Unit AC - Mechanical Work - 3rd Floor	4	29-Jul-26	03-Aug-26	Not Started	2
CON-5620	Install Air Conditioning Unit AC - Mechanical Work - 4th Floor	4	04-Aug-26	07-Aug-26	Not Started	2
I-1130	Fire Alarm Inspection	47	28-May-26	04-Aug-26	Not Started	2
CON-98837	Install Intrusion System Components-1st Floor	4	04-Aug-26	07-Aug-26	Not Started	2
CON-98887	Install Auxiliary System Components-1st Floor	4	29-Jul-26	03-Aug-26	Not Started	2
CON-98927	Install Sound Clock System Components -5th Floor	6	16-Jul-26	23-Jul-26	Not Started	2
CON-98917	Install Sound Clock System Components-4th Floor	6	08-Jul-26	15-Jul-26	Not Started	2
CON-98907	Install Sound Clock System Components-3rd Floor	6	29-Jun-26	07-Jul-26	Not Started	2
CON-98897	Install Sound Clock System Components-2nd Floor	6	18-Jun-26	26-Jun-26	Not Started	2
CON-98937	Install Sound Clock System Components-1st Floor	3	24-Jul-26	28-Jul-26	Not Started	2

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
MIL-2642	Finish Fire Alarm Signoff	0		07-Aug-26	Not Started	2
CON-9060	Install Furniture & Milling Work (Owner Provided & Installed) -5th Floor	4	21-Aug-26	26-Aug-26	Not Started	2
CLO-1260	HVAC Split System Testing & Commissioning	21	10-Aug-26	08-Sep-26	Not Started	2
CLO-1280	Fire Alarm Testing & Commissioning	21	10-Aug-26	08-Sep-26	Not Started	2
MIL-2962	Finish Fire Alarm Inspection	0		07-Aug-26	Not Started	2
CON-5260	Install Cabinet Unit Heater With Fan CUH -4th Floor	4	23-Jul-26	28-Jul-26	Not Started	3
CON-5270	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -1st Floor	5	23-Jun-26	29-Jun-26	Not Started	3
CON-3500	Rough-in Main Sprinkler Piping -2nd Floor	5	08-May-26	14-May-26	Not Started	3
CON-3310	Install 4" Standpipe -2nd Floor	4	04-May-26	07-May-26	Not Started	3
CON-3690	Rough-in Main Sprinkler Piping-3rd Floor	5	15-May-26	21-May-26	Not Started	3
CON-3810	Rough-in Main Sprinkler Piping-4th Floor	5	22-May-26	29-May-26	Not Started	3
CON-4010	Rough-in Main Sprinkler Piping -5th Floor	5	01-Jun-26	05-Jun-26	Not Started	3
CON-4250	Rough-in Main Sprinkler Piping -Roof	5	08-Jun-26	12-Jun-26	Not Started	3
CON-4430	Rough-in Branch Sprinkler Piping -Roof	5	15-Jun-26	22-Jun-26	Not Started	3
CON-5480	Install Gypsum Board Ceiling -1st Floor	6	08-Jul-26	15-Jul-26	Not Started	3
CON-4620	Install Gypsum Board Walls-4th Floor	5	10-Jun-26	16-Jun-26	Not Started	3
CON-4810	Install Gypsum Board Walls-5th Floor	5	17-Jun-26	24-Jun-26	Not Started	3
CON-5720	Install First Coat Painting-1st Floor	5	16-Jul-26	22-Jul-26	Not Started	3
CON-2630	Rough-in Gas Risers -2nd Floor	4	06-Apr-26	09-Apr-26	Not Started	3
CON-2740	Rough-in Domestic Water Piping -2nd Floor	4	10-Apr-26	15-Apr-26	Not Started	3
CON-2870	Rough-in Sanitary & Vent Piping -2nd Floor	4	16-Apr-26	21-Apr-26	Not Started	3
CON-3020	Rough-in Storm Piping -2nd Floor	4	22-Apr-26	27-Apr-26	Not Started	3
CON-2750	Rough-in Gas Risers-3rd Floor	4	10-Apr-26	15-Apr-26	Not Started	3
CON-2880	Rough-in Domestic Water Piping -3rd Floor	4	16-Apr-26	21-Apr-26	Not Started	3
CON-3030	Rough-in Sanitary & Vent Piping -3rd Floor	4	22-Apr-26	27-Apr-26	Not Started	3
CON-3170	Rough-in Storm Piping -3rd Floor	4	28-Apr-26	01-May-26	Not Started	3
CON-2490	Low Voltage Wires Pulling -2nd Floor	6	27-Mar-26	03-Apr-26	Not Started	3
CON-5410	Sprinklers Air Testing-1st Floor	5	30-Jun-26	07-Jul-26	Not Started	3
CON-2340	Power Wires Pulling -2nd Floor	6	19-Mar-26	26-Mar-26	Not Started	3
CON-5760	Install Wood Floating Floor System -Gymnatorium	10	14-Jul-26	27-Jul-26	Not Started	3
CON-5810	Install Wall Pads - Gymnatorium	4	28-Jul-26	31-Jul-26	Not Started	3
CON-5970	Install Retractable Basketball Goal Assembly -Gymnatorium	3	03-Aug-26	05-Aug-26	Not Started	3
CON-4850	Install Firestopping-3rd Floor	4	10-Jun-26	15-Jun-26	Not Started	3
CON-6020	Install 8" Acoustic Block Painted-Gymnatorium	7	06-Aug-26	14-Aug-26	Not Started	3
CON-5460	Install Convector Heater CV - Mechanical Work - 4th Floor	3	29-Jul-26	31-Jul-26	Not Started	3
CON-5420	Install Asphalt Pavement - Playground Area & Fences - Building Perimeter	2	04-Aug-26	05-Aug-26	Not Started	3
CON-6250	Install Hydraulic Vertical Wheelchair Lift -Gymnatorium	8	17-Aug-26	26-Aug-26	Not Started	3
CON-6390	Install Auditorium Television Studio Dimming System -Gymnatorium	7	27-Aug-26	04-Sep-26	Not Started	3
CON-3510	Install 4" Standpipe -3rd Floor	4	08-May-26	13-May-26	Not Started	4
CON-4770	Install PBX - 1st Floor MDF Room	8	06-Jul-26	15-Jul-26	Not Started	4
CON-4120	Install Project Connect Cabinet - 1st Floor MDF Room	8	15-May-26	27-May-26	Not Started	4
CON-5580	Install Lighting Fixtures -4th Floor	6	08-Jul-26	15-Jul-26	Not Started	4
CON-4840	Install Duct Insulation -1st Floor	8	24-Jun-26	06-Jul-26	Not Started	4
CON-4070	Install Duct Insulation -2nd Floor	8	07-May-26	18-May-26	Not Started	4
CON-4320	Install Duct Insulation -3rd Floor	8	19-May-26	29-May-26	Not Started	4

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-4570	Install Duct Insulation -4th Floor	8	01-Jun-26	10-Jun-26	Not Started	4
CON-4710	Install Duct Insulation -5th Floor	8	11-Jun-26	23-Jun-26	Not Started	4
CON-2830	Install IPDVS Equipment Rack - 3rd Floor IDF Room	4	03-Apr-26	08-Apr-26	Not Started	4
CON-1080	Install Erosion Control Devices	2	06-Oct-25	07-Oct-25	Not Started	5
CON-1010	Install Construction Signs	2	06-Oct-25	07-Oct-25	Not Started	5
CON-1030	Install Construction Fences	2	06-Oct-25	07-Oct-25	Not Started	5
CON-2250	Install Air Handling Unit AHU-1 -Roof Floor	5	08-Jun-26	12-Jun-26	Not Started	5
CON-2430	Install Air Handling Unit AHU-2 -Roof Floor	5	15-Jun-26	22-Jun-26	Not Started	5
CON-2560	Install Air Handling Unit AHU-3 -Roof Floor	5	23-Jun-26	29-Jun-26	Not Started	5
CON-2720	Install Air Handling Unit AHU-4 -Roof Floor	5	30-Jun-26	07-Jul-26	Not Started	5
CON-6050	Install Boiler B-1-Boiler Room	5	23-Jul-26	29-Jul-26	Not Started	5
CON-6110	Install Boiler B-2-Boiler Room	5	30-Jul-26	05-Aug-26	Not Started	5
CON-6120	Install Air Separator Units (AS-1 , AS-2 & AS-3)	2	30-Jul-26	31-Jul-26	Not Started	5
CON-6210	Install Glycol Make-up Units (GF-1 & GF-2 & GF-3)	2	03-Aug-26	04-Aug-26	Not Started	5
CON-3650	Install 4" Standpipe -4th Floor	4	14-May-26	19-May-26	Not Started	5
CON-6000	Rough-in Conduits & Wires-Boiler Room	3	20-Jul-26	22-Jul-26	Not Started	5
CON-5740	Install Lighting Fixtures -5th Floor	6	16-Jul-26	23-Jul-26	Not Started	5
MIL-1480	Roof Top Units Installations Finish	0		14-Jul-26	Not Started	5
CON-6230	Install Gym Equipment -Gymnatorium -Gymnatorium	6	17-Aug-26	24-Aug-26	Not Started	5
MIL-1640	Provide Complete Set of Approved Coordination Drawings	0		23-May-25	Not Started	5
CON-5010	Install Firestopping-4th Floor	4	16-Jun-26	22-Jun-26	Not Started	5
CON-2970	Field Testing of Windows (50%)	5	15-Apr-26	21-Apr-26	Not Started	5
CON-5770	Install Air Cooled Condensing Unit ACCU - Mechanical Work - 5th Floor	5	08-Jul-26	14-Jul-26	Not Started	5
CON-4170	Install 4" Concrete Sidewalk - 2nd Street	7	08-Jun-26	16-Jun-26	Not Started	5
CON-5960	F/R/P Concert Pad -Boiler Room	3	15-Jul-26	17-Jul-26	Not Started	5
CON-98877	Install Auxiliary System Components -5th Floor	6	16-Jul-26	23-Jul-26	Not Started	5
CON-98867	Install Auxiliary System Components-4th Floor	6	08-Jul-26	15-Jul-26	Not Started	5
CON-98857	Install Auxiliary System Components-3rd Floor	6	29-Jun-26	07-Jul-26	Not Started	5
CON-98847	Install Auxiliary System Components-2nd Floor	6	18-Jun-26	26-Jun-26	Not Started	5
SUB-4050	Prepare & Submit Soil Sampling Plan	71	26-May-25	05-Sep-25	Not Started	5
CLO-1290	Glycol System Testing & Commissioning	21	05-Aug-26	02-Sep-26	Not Started	5
CON-99217	Install Bleachers -Gymnatorium	3	12-Aug-26	14-Aug-26	Not Started	5
CON-5430	Install Hot Glycol / Hot Water Cabinet Heater (CUH) -5th Floor	4	29-Jul-26	03-Aug-26	Not Started	6
CON-1870	Rough-in Chilled Glycol Piping-2nd Floor	7	02-Mar-26	10-Mar-26	Not Started	6
CON-2150	Rough-in Chilled Glycol Piping-3rd Floor	7	11-Mar-26	19-Mar-26	Not Started	6
CON-2280	Rough-in Chilled Glycol Piping-4th Floor	7	20-Mar-26	30-Mar-26	Not Started	6
CON-2460	Rough-in Chilled Glycol Piping-5th Floor	7	31-Mar-26	08-Apr-26	Not Started	6
CON-3770	Install 4" Standpipe -5th Floor	4	20-May-26	26-May-26	Not Started	6
CON-5940	Install Lighting Fixtures -1st Floor	7	24-Jul-26	03-Aug-26	Not Started	6
CLO-1010	HVAC Flush-Out	20	07-Jul-26	03-Aug-26	Not Started	6
MIL-1580	Window Installation Finish	0		28-Apr-26	Not Started	6
SUB-1790	Prepare & Submit Initial 1st Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25	Not Started	6
SUB-1800	Prepare & Submit Initial 2nd Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25	Not Started	6
SUB-1810	Prepare & Submit Initial 3rd Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25	Not Started	6

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
SUB-1820	Prepare & Submit Initial 4th Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25	Not Started	6
SUB-1830	Prepare & Submit Initial 5th Floor MEP Coordination Drawings	75	15-Oct-24	03-Feb-25	Not Started	6
SUB-2280	Prepare & Submit Final 1st Floor Coordination Drawings	49	25-Feb-25	02-May-25	Not Started	6
SUB-2290	Prepare & Submit Final 2nd Floor Coordination Drawings	49	25-Feb-25	02-May-25	Not Started	6
SUB-2300	Prepare & Submit Final 3rd Floor Coordination Drawings	49	25-Feb-25	02-May-25	Not Started	6
SUB-2310	Prepare & Submit Final 4th Floor Coordination Drawings	49	25-Feb-25	02-May-25	Not Started	6
SUB-2320	Prepare & Submit Final 5th Floor Coordination Drawings	49	25-Feb-25	02-May-25	Not Started	6
CON-6240	Install Fine Tube Radiator FTR - Gymnatorium	5	17-Aug-26	21-Aug-26	Not Started	6
MIL-2632	Finish HVAC	0		06-Jul-26	Not Started	6
MIL-2692	Building HVAC Flush-out	0		03-Aug-26	Not Started	6
MIL-2732	Start Mechanical and Electrical System Commissioning	0	07-Jul-26		Not Started	6
MIL-2832	Issuance of Excavation & Shoring Permit	0		29-Sep-25	Not Started	6
CLO-1230	Air Handling Unit Testing & Commissioning	21	04-Aug-26	01-Sep-26	Not Started	6
CON-99257	Subcontractor Buyout	10	30-Sep-24	11-Oct-24	Not Started	6
CON-3670	Rough-in Branch Sprinkler Piping -2nd Floor	5	15-May-26	21-May-26	Not Started	7
CON-3680	Rough-in Sprinkler Heads -2nd Floor	5	15-May-26	21-May-26	Not Started	7
CON-3890	Install 4" Standpipe -Roof	4	27-May-26	01-Jun-26	Not Started	7
CON-3140	Install Plumbing Risers -1st Floor	2	10-Apr-26	13-Apr-26	Not Started	7
CON-3750	Install Emergency Generator- Roof Floor	4	17-Jul-26	22-Jul-26	Not Started	7
CON-3060	Install Mechanical Piping Risers-1st Floor	2	08-Apr-26	09-Apr-26	Not Started	7
CON-3350	Install Low Voltage Risers-1st Floor	2	16-Apr-26	17-Apr-26	Not Started	7
CON-3260	Install Power Risers-1st Floor	2	14-Apr-26	15-Apr-26	Not Started	7
CON-5380	Install Generator Connections -Roof Floor	4	23-Jul-26	28-Jul-26	Not Started	7
CLO-1220	Emergency Generator Electric Load Test	3	29-Jul-26	31-Jul-26	Not Started	7
SUB-2900	Prepare & Submit Excavated Material Disposal Plan	71	26-May-25	05-Sep-25	Not Started	7
MIL-2562	Start Below Grade Plumbing and Other Utilities	0	16-Jul-26		Not Started	7
MIL-2602	Start Mechanical Distribution Lines	0	08-Apr-26		Not Started	7
MIL-2712	Start Low Voltage	0	16-Apr-26		Not Started	7
CLO-1250	Emergency Generator Testing & Commissioning	21	03-Aug-26	31-Aug-26	Not Started	7
CON-9010	Remove Steel Plate Protection over NYPA Easement - Playground Area & Fences - Building Perimeter	1	28-Jul-26	28-Jul-26	Not Started	7
CON-1490	Install Duct Risers -3rd Floor	2	24-Feb-26	25-Feb-26	Not Started	8
CON-1890	Rough-in Duct Work -3rd Floor	5	02-Mar-26	06-Mar-26	Not Started	8
CON-5030	Rough-in Main Sprinkler Piping -1st Floor	5	08-Jun-26	12-Jun-26	Not Started	8
CON-5230	Rough-in Branch Sprinkler Piping -1st Floor	5	15-Jun-26	22-Jun-26	Not Started	8
CON-5240	Rough-in Sprinkler Heads -1st Floor	5	15-Jun-26	22-Jun-26	Not Started	8
CON-4910	Install 4" Standpipe -1st Floor	4	02-Jun-26	05-Jun-26	Not Started	8
CON-3790	Rough-in Branch Sprinkler Piping -3rd Floor	5	22-May-26	29-May-26	Not Started	8
CON-3800	Rough-in Sprinkler Heads -3rd Floor	5	22-May-26	29-May-26	Not Started	8
CON-4440	Rough-in Sprinkler Heads -Roof	5	15-Jun-26	22-Jun-26	Not Started	8
PRO-1490	Procure & Deliver Air Handling Units	250	30-Sep-25	06-Jun-26	Not Started	8
CON-1510	Duct Leak Test -2nd Floor	2	24-Feb-26	25-Feb-26	Not Started	8
CON-1600	Duct Leak Test -3rd Floor	2	26-Feb-26	27-Feb-26	Not Started	8
APP-1330	Review & Approve Initial 1st Floor Coordination Drawings	21	04-Feb-25	24-Feb-25	Not Started	8
APP-1340	Review & Approve Initial 2nd Floor Coordination Drawings	21	04-Feb-25	24-Feb-25	Not Started	8

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
APP-1350	Review & Approve Initial 3rd Floor Coordination Drawings	21	04-Feb-25	24-Feb-25	Not Started	8
APP-1360	Review & Approve Initial 4th Floor Coordination Drawings	21	04-Feb-25	24-Feb-25	Not Started	8
APP-1370	Review & Approve Initial 5th Floor Coordination Drawings	21	04-Feb-25	24-Feb-25	Not Started	8
I-1080	Standpipe System Inspection	111	29-Dec-25	05-Jun-26	Not Started	8
MIL-2952	Finish Standpipe System Inspection	0		05-Jun-26	Not Started	8
CON-2890	Rough-in Gas Risers -4th Floor	4	16-Apr-26	21-Apr-26	Not Started	9
CON-3040	Rough-in Domestic Water Piping -4th Floor	4	22-Apr-26	27-Apr-26	Not Started	9
CON-3180	Rough-in Sanitary & Vent Piping -4th Floor	4	28-Apr-26	01-May-26	Not Started	9
CON-3330	Rough-in Storm Piping -4th Floor	4	04-May-26	07-May-26	Not Started	9
CON-5220	Install Firestopping-5th Floor	4	23-Jun-26	26-Jun-26	Not Started	9
CON-98827	Install Intrusion System Components -5th Floor	6	16-Jul-26	23-Jul-26	Not Started	9
CON-98817	Install Intrusion System Components-4th Floor	6	08-Jul-26	15-Jul-26	Not Started	9
CON-98807	Install Intrusion System Components-3rd Floor	6	29-Jun-26	07-Jul-26	Not Started	9
CON-98797	Install Intrusion System Components-2nd Floor	6	18-Jun-26	26-Jun-26	Not Started	9
APP-4050	Review & Approve Soil Sampling Plan	21	06-Sep-25	26-Sep-25	Not Started	9
CON-2170	Rough-in Duct Work -4th Floor	5	09-Mar-26	13-Mar-26	Not Started	10
CON-5680	Install Door Frames & Doors -5th Floor	5	16-Jul-26	22-Jul-26	Not Started	10
CON-5890	Install Flooring Tiles -5th Floor	5	23-Jul-26	29-Jul-26	Not Started	10
CON-3050	Rough-in Gas Risers & Piping -5th Floor	4	22-Apr-26	27-Apr-26	Not Started	10
CON-3190	Rough-in Domestic Water Piping -5th Floor	4	28-Apr-26	01-May-26	Not Started	10
CON-3340	Rough-in Sanitary & Vent Piping -5th Floor	4	04-May-26	07-May-26	Not Started	10
CON-3540	Rough-in Storm Piping -5th Floor	4	08-May-26	13-May-26	Not Started	10
MIL-1270	Electrical Rough-ins Start	0	09-Apr-26		Not Started	10
CON-4600	Tape Gypsum Board -1st Floor	4	30-Jun-26	06-Jul-26	Not Started	10
APP-2280	Review & Approve Final 1st Floor Coordination Drawings	21	03-May-25	23-May-25	Not Started	10
APP-2290	Review & Approve Final 2nd Floor Coordination Drawings	21	03-May-25	23-May-25	Not Started	10
APP-2300	Review & Approve Final 3rd Floor Coordination Drawings	21	03-May-25	23-May-25	Not Started	10
APP-2310	Review & Approve Final 4th Floor Coordination Drawings	21	03-May-25	23-May-25	Not Started	10
APP-2320	Review & Approve Final 5th Floor Coordination Drawings	21	03-May-25	23-May-25	Not Started	10
CON-5390	Install Firestopping-1st Floor	4	30-Jun-26	06-Jul-26	Not Started	10
I-1100	Fire-Resistant Penetrations And Joints Inspection	87	03-Mar-26	06-Jul-26	Not Started	10
MIL-2982	Finish Fire-Resistant Penetrations And Joints Inspection	0		06-Jul-26	Not Started	10
CON-5070	Install Electric Unit Heaters -1st Floor	7	17-Jul-26	27-Jul-26	Not Started	11
CON-3990	Rough-in Branch Sprinkler Piping -4th Floor	5	01-Jun-26	05-Jun-26	Not Started	11
CON-4000	Rough-in Sprinkler Heads -4th Floor	5	01-Jun-26	05-Jun-26	Not Started	11
CON-5920	Install Door Frames & Doors-1st Floor	5	23-Jul-26	29-Jul-26	Not Started	11
CON-6080	Install Flooring Tiles-1st Floor	5	30-Jul-26	05-Aug-26	Not Started	11
CON-2090	Install Elevator Controller #1 -Elevator Machine Room	10	03-Jun-26	16-Jun-26	Not Started	11
CON-2370	Install Elevator Controller #2 -Elevator Machine Room	10	17-Jun-26	01-Jul-26	Not Started	11
CON-2580	Install Power Panels -Elevator Machine Room	7	02-Jul-26	13-Jul-26	Not Started	11
PRO-1510	Procure & Deliver Emergency Generator	290	30-Sep-25	16-Jul-26	Not Started	11
CON-4970	Tape Gypsum Board -5th Floor	4	18-Jun-26	24-Jun-26	Not Started	11
MIL-1760	Start Elevator Work	0	07-May-26		Not Started	11

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
APP-2900	Review & Approve Excavated Material Disposal Plan	21	06-Sep-25	26-Sep-25	Not Started	11
SUB-2910	Prepare & Submit Backfill & Resue Plan	20	08-Sep-25	03-Oct-25	Not Started	11
MIL-2742	Permanent Power Available	0		27-Jul-26	Not Started	11
CON-8060	CON-ED - Switchgear Inspection	4	15-Jun-26	18-Jun-26	Not Started	11
CON-8070	CON-ED - Pull Power Cable to the Building	10	22-Jun-26	06-Jul-26	Not Started	11
CON-8080	CON-ED - Terminate Power Cables	10	07-Jul-26	20-Jul-26	Not Started	11
CON-8090	CON-ED - Energize to the Building	5	21-Jul-26	27-Jul-26	Not Started	11
CON-9130	Install Switch Gear - Electric Service Room	5	08-Jun-26	12-Jun-26	Not Started	11
CLO-1240	Elevator Sump Pump Testing & Commissioning	21	28-Jul-26	25-Aug-26	Not Started	11
CLO-1270	Water Heater Testing & Commissioning	21	28-Jul-26	25-Aug-26	Not Started	11
CON-99157	Install Elevator Sump Pump -Elevator Machine Room	10	14-Jul-26	27-Jul-26	Not Started	11
CON-99167	Install Elevator Guide Rails -Elevator Machine Room	8	21-May-26	02-Jun-26	Not Started	11
CON-99357	Install CMU Wall for Shaft -Elevator Machine Room	10	07-May-26	20-May-26	Not Started	11
CON-6340	Install Exhaust Fans -Boiler Room	2	14-Aug-26	17-Aug-26	Not Started	12
CON-6260	Install Heat Exchanger -Boiler Room	2	06-Aug-26	07-Aug-26	Not Started	12
CON-6350	Install Primary Hot Water Pump (GHWP 1 to 3) -Boiler Room	2	14-Aug-26	17-Aug-26	Not Started	12
CON-6360	Install Primary Chilled Water Pump (GCHWP-1&2)-Boiler Room	2	14-Aug-26	17-Aug-26	Not Started	12
CON-6400	Install Secondary Hot Water Pump(HWP-1&2)-Boiler Room	2	18-Aug-26	19-Aug-26	Not Started	12
CON-6290	Install Hot Glycol Units Heaters (UH-5-1, UH-5-2)	2	10-Aug-26	11-Aug-26	Not Started	12
CON-2300	Rough-in Duct Work-5th Floor	5	16-Mar-26	20-Mar-26	Not Started	12
CON-5860	Install Sprinkler Booster Pump (SBP-1) -1st Floor	10	23-Jul-26	05-Aug-26	Not Started	12
CON-6100	Install Jockey Pump (JP-1) -1st Floor	10	06-Aug-26	19-Aug-26	Not Started	12
CON-4230	Rough-in Branch Sprinkler Piping -5th Floor	5	08-Jun-26	12-Jun-26	Not Started	12
CON-4240	Rough-in Sprinkler Heads -5th Floor	5	08-Jun-26	12-Jun-26	Not Started	12
CON-6330	Install Heat Pump Electric Hot Water Heater (HPWH#1&2)-Boiler Room	2	12-Aug-26	13-Aug-26	Not Started	12
CON-2790	Rough-in Conduits & Wires-Elevator Machine Room	6	14-Jul-26	21-Jul-26	Not Started	12
CON-3100	Install Elevator Cabinet (1) -Elevator Machine Room	10	22-Jul-26	04-Aug-26	Not Started	12
CLO-1000	Elevator Testing & Commissioning	20	12-Aug-26	09-Sep-26	Not Started	12
CON-3620	Install Elevator Cabinet (2) -Elevator Machine Room	10	22-Jul-26	04-Aug-26	Not Started	12
CON-4720	Tape Gypsum Board -4th Floor	4	11-Jun-26	16-Jun-26	Not Started	12
MIL-1650	FDNY Inspection Finish	0		30-Sep-26	Not Started	12
CLO-1150	FDNY Inspection	12	15-Sep-26	30-Sep-26	Not Started	12
CLO-1160	Sprinkler/Domestic Booster Pumps Testing & Commissioning	14	20-Aug-26	09-Sep-26	Not Started	12
CLO-1170	Sprinkler/Domestic Booster Pumps Inspection	3	10-Sep-26	14-Sep-26	Not Started	12
CLO-1190	Pre-Elevator Test Inspection	5	05-Aug-26	11-Aug-26	Not Started	12
CLO-1200	Elevator DOB Inspection	5	10-Sep-26	16-Sep-26	Not Started	12
PER-2650	Elevator Equipment Use Permit	10	17-Sep-26	30-Sep-26	Not Started	12
MIL-1670	Elevator Final Sign-off	0		30-Sep-26	Not Started	12
MIL-2822	Elevator Ready for Testing	0		11-Aug-26	Not Started	12
CON-6200	Install Expansion Tanks (ET-1 , ET-2 & ET-3)	2	03-Aug-26	04-Aug-26	Not Started	13
CON-1560	Install Duct Risers -4th Floor	2	26-Feb-26	27-Feb-26	Not Started	13
CON-3720	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -2nd Floor	5	15-May-26	21-May-26	Not Started	13
CON-3880	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-3rd Floor	5	22-May-26	29-May-26	Not Started	13

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-4100	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-4th Floor	5	01-Jun-26	05-Jun-26	Not Started	13
CON-4340	Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -5th Floor	5	08-Jun-26	12-Jun-26	Not Started	13
CON-6220	Install Reduced Pressure Zone (RPZ) Devices -Boiler Room	2	03-Aug-26	04-Aug-26	Not Started	13
CON-6130	Install Boiler Condensate ACID Neutralization Tubes -Boiler Room	2	30-Jul-26	31-Jul-26	Not Started	13
MIL-1330	Finish Sprinkler Rough-ins	0		22-Jun-26	Not Started	13
PRO-1120	Procure & Deliver Erosion Control and Sedimentation Devices	25	05-Sep-25	29-Sep-25	Not Started	13
CON-1700	Duct Leak Test -4th Floor	2	02-Mar-26	03-Mar-26	Not Started	13
CON-3830	Sprinklers Air Testing-2nd Floor	5	22-May-26	29-May-26	Not Started	13
CON-4060	Sprinklers Air Testing-3rd Floor	5	01-Jun-26	05-Jun-26	Not Started	13
CON-4280	Sprinklers Air Testing-4th Floor	5	08-Jun-26	12-Jun-26	Not Started	13
CON-4490	Sprinklers Air Testing-5th Floor	5	15-Jun-26	22-Jun-26	Not Started	13
CON-4540	Tape Gypsum Board -3rd Floor	4	04-Jun-26	09-Jun-26	Not Started	13
PRO-1580	Procure & Deliver Metal Deck	70	30-Sep-25	08-Dec-25	Not Started	13
CON-99267	Install Rolling Doors-1st Floor	3	30-Jul-26	03-Aug-26	Not Started	13
CON-4200	Tape Gypsum Board -2nd Floor	4	28-May-26	02-Jun-26	Not Started	14
CON-5870	Install Metal Panel Ceiling & Metal Geometric Ceiling -1st Floor	5	23-Jul-26	29-Jul-26	Not Started	16
CLO-1180	Sprinkler/Domestic Booster Pumps Sign-offs	0		14-Sep-26	Not Started	16
CON-4130	Install BACnet Data Cabinet- 1st Floor MDF Room	9	03-Jun-26	15-Jun-26	Not Started	16
CON-3230	Install SSDS Risers -SSDS System -1st Floor	2	14-Apr-26	15-Apr-26	Not Started	17
PRO-1520	Procure & Deliver Switch Gears	250	30-Sep-25	06-Jun-26	Not Started	17
APP-2910	Review & Approve Backfill & Resue Plan	21	04-Oct-25	24-Oct-25	Not Started	18
CON-1630	Install Duct Risers-5th Floor	2	02-Mar-26	03-Mar-26	Not Started	19
CON-1610	Install MEP Hangers & Sleeves-Roof Floor	4	27-Feb-26	04-Mar-26	Not Started	19
CON-1810	Duct Leak Test -5th Floor	1	04-Mar-26	04-Mar-26	Not Started	19
CON-2160	Rough-in Refrigerant Piping-3rd Floor	7	09-Mar-26	17-Mar-26	Not Started	20
CON-6410	Install Electric Unit Heater (EUH-3) - Boiler Room	2	18-Aug-26	19-Aug-26	Not Started	20
CON-6420	Install Branch Panels (BRPP) -Boiler Room	2	18-Aug-26	19-Aug-26	Not Started	20
CON-5590	Install Exhaust Fan EF - Mechanical Work - 5th Floor	4	04-Aug-26	07-Aug-26	Not Started	20
CON-5630	Install Convector Heater CV - Mechanical Work - 5th Floor	3	10-Aug-26	12-Aug-26	Not Started	20
MIL-2652	Finish Mechanical and Electrical System Commissioning	0		18-Sep-26	Not Started	20
MIL-2772	Performance test for all mechanical equipment and low voltage systems	0		18-Sep-26	Not Started	20
MIL-2792	Commissioning for all mechanical equipment and low voltage systems	0		18-Sep-26	Not Started	20
CON-1760	Install Dunnage-Roof Floor	8	05-Mar-26	16-Mar-26	Not Started	21
CON-4680	Install Ceramic Wall Tiles at Corridor -1st Floor	7	07-Jul-26	15-Jul-26	Not Started	21
CON-4350	Install Ceramic Wall Tiles at Corridor-2nd Floor	7	03-Jun-26	11-Jun-26	Not Started	21
CON-4610	Install Ceramic Wall Tiles at Corridor-3rd Floor	7	12-Jun-26	23-Jun-26	Not Started	21
CON-4800	Install Ceramic Wall Tiles at Corridor-4th Floor	7	24-Jun-26	02-Jul-26	Not Started	21
CON-5080	Install Ceramic Wall Tiles at Corridor-5th Floor	7	06-Jul-26	14-Jul-26	Not Started	21
CON-5040	Dismantle Hoist	2	10-Sep-26	11-Sep-26	Not Started	21
CON-5170	Demolish Hoist Pad	2	14-Sep-26	15-Sep-26	Not Started	21
CON-5250	Hoist In-Fill	2	16-Sep-26	17-Sep-26	Not Started	21

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-4880	Install Motorized Fire/Smoke Damper FSD - Mechanical Work - 1st Floor	7	14-Jul-26	22-Jul-26	Not Started	22
CON-5150	Install Air Conditioning Unit AC - Mechanical Work - 1st Floor	4	23-Jul-26	28-Jul-26	Not Started	22
CON-5320	Install Door Curtains DC - Mechanical Work - 1st Floor	7	29-Jul-26	06-Aug-26	Not Started	22
CON-5490	Install Convector Heater CV - Mechanical Work - 1st Floor	7	07-Aug-26	17-Aug-26	Not Started	22
CON-1400	Install MEP Hangers & Sleeves-5th Floor	4	17-Feb-26	20-Feb-26	Not Started	23
PRO-1610	Procure & Deliver Prefabricated Expansion Joint Covers	60	30-Sep-25	28-Nov-25	Not Started	23
CON-1310	Install MEP Hangers & Sleeves-4th Floor	4	29-Jan-26	03-Feb-26	Not Started	25
CON-2290	Rough-in Refrigerant Piping-4th Floor	7	16-Mar-26	24-Mar-26	Not Started	25
CON-2470	Rough-in Refrigerant Piping-5th Floor	7	23-Mar-26	31-Mar-26	Not Started	25
CON-6380	Install Food Service Equipment-1st Floor	5	04-Sep-26	11-Sep-26	Not Started	25
MIL-1460	Roof Top Units Installations Start	0	08-Jun-26		Not Started	25
CON-4730	Rough-in Conduits & Wires - Electric Service Room	6	23-Apr-26	30-Apr-26	Not Started	25
CON-5180	Install Service Switchboard "SS-A"- Electric Service Room	5	11-May-26	15-May-26	Not Started	25
CON-4960	F/R/P Concrete Pad - Electric Service Room	6	01-May-26	08-May-26	Not Started	25
MIL-2722	Start Kitchen	0	04-Sep-26		Not Started	25
CON-1230	Install MEP Hangers & Sleeves-3rd Floor	4	09-Jan-26	14-Jan-26	Not Started	26
CON-2680	Rough-in Power Conduits -5th Floor	6	06-Apr-26	13-Apr-26	Not Started	26
CON-2480	Rough-in Power Conduits-4th Floor	6	27-Mar-26	03-Apr-26	Not Started	26
CON-2320	Rough-in Power Conduits-3rd Floor	6	19-Mar-26	26-Mar-26	Not Started	26
CON-2960	Power Wires Pulling-5th Floor	6	14-Apr-26	21-Apr-26	Not Started	26
CON-2710	Power Wires Pulling-4th Floor	6	06-Apr-26	13-Apr-26	Not Started	26
CON-2510	Power Wires Pulling-3rd Floor	6	27-Mar-26	03-Apr-26	Not Started	26
CON-9110	In-Wall Inspection -1st Floor	2	19-May-26	20-May-26	Not Started	26
CON-9070	In-Wall Inspection-2nd Floor	2	16-Apr-26	17-Apr-26	Not Started	26
CON-9090	In-Wall Inspection -4th Floor	7	28-Apr-26	06-May-26	Not Started	26
CON-9100	In-Wall Inspections -5th Floor	7	04-May-26	12-May-26	Not Started	27
CON-1580	Install Plumbing Risers -2nd Floor	2	26-Feb-26	27-Feb-26	Not Started	28
CON-1500	Install Mechanical Piping Risers-2nd Floor	2	24-Feb-26	25-Feb-26	Not Started	28
CON-9080	In-Wall Inspection -3rd Floor	2	22-Apr-26	23-Apr-26	Not Started	28
CON-5880	Install Acoustical Ceiling Tiles -1st Floor	5	31-Aug-26	04-Sep-26	Not Started	29
PRO-1220	Procure & Deliver Windows & Storefronts	154	30-Sep-25	02-Mar-26	Not Started	29
MIL-2662	Finishes and Ceiling Complete	0		04-Sep-26	Not Started	29
CON-1680	Install Plumbing Risers -3rd Floor	2	02-Mar-26	03-Mar-26	Not Started	30
CON-1590	Install Mechanical Piping Risers -3rd Floor	2	26-Feb-26	27-Feb-26	Not Started	30
PRO-2000	Procure & Deliver Key Cutting Machine	74	08-Jul-26	19-Sep-26	Not Started	30
MIL-2942	Start In-Wall Inspection	0	10-Apr-26		Not Started	30
CON-6280	Install Signages- 5th Floor	5	27-Aug-26	02-Sep-26	Not Started	31
CON-5300	Install Grease Interceptors - 1st Floor	5	28-Jul-26	03-Aug-26	Not Started	32
MIL-1300	Start Sprinkler Rough-ins	0	04-May-26		Not Started	32
PRO-1260	Procure & Deliver Electrical Wires & Conduits	130	30-Sep-25	06-Feb-26	Not Started	32
CON-2860	Install Fume Hood Exhaust -Roof Floor	3	08-Jul-26	10-Jul-26	Not Started	33
CON-3000	Install Smoke Purge Fan -Roof Floor	3	13-Jul-26	15-Jul-26	Not Started	33
MIL-1380	Crane Mobilization-Mechanical Subcontractor	78	17-Mar-26	07-Jul-26	Not Started	33
CLO-1140	SSDS System Testing & Commissioning	7	16-Jul-26	24-Jul-26	Not Started	33
I-1120	Mechanical System Inspection	69	07-Apr-26	15-Jul-26	Not Started	33
MIL-2972	Finish Mechanical System Inspection	0		15-Jul-26	Not Started	33
CON-1130	Install MEP Hangers & Sleeves- 2nd Floor	4	22-Dec-25	26-Dec-25	Not Started	34

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-9150	Install LED Theatrical Lighting -Gymnatorium	4	25-Aug-26	28-Aug-26	Not Started	34
CON-2950	Rough-in Low-Voltage Conduits-5th Floor	6	14-Apr-26	21-Apr-26	Not Started	35
CON-2700	Rough-in Low-Voltage Conduits-4th Floor	6	06-Apr-26	13-Apr-26	Not Started	35
CON-2500	Rough-in Low-Voltage Conduits-3rd Floor	6	27-Mar-26	03-Apr-26	Not Started	35
CON-6180	Install Plumbing Fixtures-1st Floor	5	06-Aug-26	12-Aug-26	Not Started	36
CON-1740	Install SSDS Risers -SSDS System -2nd Floor	2	02-Mar-26	03-Mar-26	Not Started	36
CON-1840	Install SSDS Risers -SSDS System -3rd Floor	2	04-Mar-26	05-Mar-26	Not Started	36
CON-1970	Install SSDS Risers -SSDS System -4th Floor	2	06-Mar-26	09-Mar-26	Not Started	36
MIL-2592	P&D - Connection to Roof Drains	0	28-Jul-26		Not Started	37
CON-1780	Install Plumbing Risers -4th Floor	2	04-Mar-26	05-Mar-26	Not Started	38
CON-1690	Install Mechanical Piping Risers -4th Floor	2	02-Mar-26	03-Mar-26	Not Started	38
CON-5840	Install Electric Unit Heater EUH-6 - Electric Service Room	4	10-Jun-26	15-Jun-26	Not Started	39
CON-5510	Install Leak Detector - Electric Service Room	3	18-May-26	20-May-26	Not Started	39
CON-5780	Install Motorized Fire/Smoke Damper & Control Panel - Electric Service Room	5	03-Jun-26	09-Jun-26	Not Started	39
CON-5640	Install Fire Alarm Normal ATS - Electric Service Room	4	28-May-26	02-Jun-26	Not Started	39
CON-5610	Install Sprinkler Booster Pump - Electric Service Room	4	21-May-26	27-May-26	Not Started	39
CON-6070	Install Furniture & Milling Work (Contractor Provided & Installed) -4th Floor	5	30-Jul-26	05-Aug-26	Not Started	41
CON-6160	Install Signages-4th Floor	5	06-Aug-26	12-Aug-26	Not Started	41
CON-4290	Install New Steel Faced Curb - 54th Avenue Street	4	29-May-26	03-Jun-26	Not Started	41
CON-3860	Remove Existing Asphalt - 54th Avenue Street	4	06-May-26	11-May-26	Not Started	41
CON-4080	Install 5' Wide Silva Cells Under Concrete Pavement Strip - 54th Avenue Street	4	18-May-26	21-May-26	Not Started	41
CON-4150	Pavement Replacement - 54th Avenue Street	4	22-May-26	28-May-26	Not Started	41
CON-3940	Remove Existing Electrical Manhole - 54th Avenue Street	4	12-May-26	15-May-26	Not Started	41
CON-4300	Install Pedestrian Ramps With Truncated Domes - 54th Avenue Street	4	29-May-26	03-Jun-26	Not Started	41
CON-4410	Install 7" Concrete Sidewalk - 54th Avenue Street	5	04-Jun-26	10-Jun-26	Not Started	41
CON-9050	Install Furniture & Milling Work (Owner Provided & Installed) -4th Floor	5	30-Jul-26	05-Aug-26	Not Started	41
CON-5910	Install Furniture & Milling Work (Contractor Provided & Installed) -3rd Floor	5	22-Jul-26	28-Jul-26	Not Started	42
CON-6030	Install Signages-3rd Floor	5	29-Jul-26	04-Aug-26	Not Started	42
CON-1940	Install Plumbing Risers-5th Floor	1	06-Mar-26	06-Mar-26	Not Started	42
CON-3910	Install Grounding System -1st Floor	5	27-Apr-26	01-May-26	Not Started	42
CON-1790	Install Mechanical Piping Risers-5th Floor	2	04-Mar-26	05-Mar-26	Not Started	42
SUB-1780	Prepare & Submit Initial Underground Coordination Drawings	50	15-Oct-24	26-Dec-24	Not Started	42
SUB-2330	Prepare & Submit Remedial Closure Report	3	27-Jul-26	29-Jul-26	Not Started	42
CON-3850	Remove Existing Steel Faced Curb - 54th Avenue Street	3	06-May-26	08-May-26	Not Started	42
CON-9040	Install Furniture & Milling Work (Owner Provided & Installed) -3rd Floor	5	22-Jul-26	28-Jul-26	Not Started	42
CON-5710	Install Furniture & Milling Work (Contractor Provided & Installed) -2nd Floor	5	14-Jul-26	20-Jul-26	Not Started	43
CON-5820	Install Signages-2nd Floor	5	21-Jul-26	27-Jul-26	Not Started	43
CON-9030	Install Furniture & Milling Work (Owner Provided & Installed) -2nd Floor	5	14-Jul-26	20-Jul-26	Not Started	43
CON-1850	Rough-in Hot Water Piping-2nd Floor	7	02-Mar-26	10-Mar-26	Not Started	44
CON-2130	Rough-in Hot Water Piping-3rd Floor	7	11-Mar-26	19-Mar-26	Not Started	44
CON-2260	Rough-in Hot Water Piping-4th Floor	7	20-Mar-26	30-Mar-26	Not Started	44
CON-2440	Rough-in Hot Water Piping-5th Floor	7	31-Mar-26	08-Apr-26	Not Started	44

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-2910	Layout -1st Floor	3	07-Apr-26	09-Apr-26	Not Started	44
CON-3080	Install Top & Bottom Track -1st Floor	4	10-Apr-26	15-Apr-26	Not Started	44
CON-3240	Install Wall Steel Studs & Framing -1st Floor	5	16-Apr-26	22-Apr-26	Not Started	44
MIL-1220	Layout Finish	0		09-Apr-26	Not Started	44
MIL-1250	Top & Bottom Track Finish	0		15-Apr-26	Not Started	44
SUB-2270	Prepare & Submit Final Underground Coordination Drawings	37	17-Jan-25	11-Mar-25	Not Started	44
CON-3090	Install CMU Walls -1st Floor	3	10-Apr-26	14-Apr-26	Not Started	45
CON-3550	Install Cable Ladder - 3rd Floor IDF Room	5	22-Apr-26	28-Apr-26	Not Started	45
I-1020	Masonry Inspection	32	02-Mar-26	14-Apr-26	Not Started	45
CON-3970	Install VAV Boxes & Sound Attenuator Devices-1st Floor	5	16-Apr-26	22-Apr-26	Not Started	46
CON-3980	Install VAV Boxes & Sound Attenuator Devices-2nd Floor	5	19-Mar-26	25-Mar-26	Not Started	46
CON-4140	Install VAV Boxes & Sound Attenuator Devices-3rd Floor	5	26-Mar-26	01-Apr-26	Not Started	46
CON-4220	Install VAV Boxes & Sound Attenuator Devices-4th Floor	5	02-Apr-26	08-Apr-26	Not Started	46
CON-4330	Install VAV Boxes & Sound Attenuator Devices-5th Floor	5	09-Apr-26	15-Apr-26	Not Started	46
CON-5570	Install Plumbing Fixtures -2nd Floor	7	06-Jul-26	14-Jul-26	Not Started	46
CON-5730	Install Plumbing Fixtures -3rd Floor	7	15-Jul-26	23-Jul-26	Not Started	46
CON-5930	Install Plumbing Fixtures -4th Floor	7	24-Jul-26	03-Aug-26	Not Started	46
CON-6090	Install Plumbing Fixtures -5th Floor	7	04-Aug-26	12-Aug-26	Not Started	46
CON-4890	F/R/P Concrete Pads -Fuel Oil Room	2	01-Jun-26	02-Jun-26	Not Started	47
MIL-1680	Emergency Generator Final Sign-off	0		07-Aug-26	Not Started	49
PER-2640	Obtain Emergency Generator Permit	5	03-Aug-26	07-Aug-26	Not Started	49
CON-99247	Install Laboratory Equipment -3rd Floor	4	14-Jul-26	17-Jul-26	Not Started	49
CON-1750	F/R/P Concrete Columns -Bulkhead	3	05-Mar-26	09-Mar-26	Not Started	50
CON-2060	Install Hoist Beam-Bulkhead	1	12-Mar-26	12-Mar-26	Not Started	50
CON-1980	F/R/P Bulkhead Slab -Bulkhead	2	10-Mar-26	11-Mar-26	Not Started	50
CON-1180	Spray Fireproofing - 1st Floor	5	03-Mar-26	09-Mar-26	Not Started	50
CON-1220	Spray Fireproofing - 2nd Floor	5	10-Mar-26	16-Mar-26	Not Started	50
CON-2520	Install Voice Rack - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26	Not Started	50
CON-2530	Install Data Rack - 2nd Floor -IDF Room	10	27-Mar-26	09-Apr-26	Not Started	50
CON-2760	Install IPDVS Equipment Rack - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26	Not Started	50
CON-2770	Install Ladder Rack Cable Tray - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26	Not Started	50
MIL-2782	Submission of Operations and Maintenance Manuals	0		01-Jun-27	Not Started	51
CON-1420	Layout -2nd Floor	3	23-Feb-26	25-Feb-26	Not Started	52
CON-1520	Install Top & Bottom Track-2nd Floor	4	26-Feb-26	03-Mar-26	Not Started	52
CON-1640	Install Wall Steel Studs & Framing-2nd Floor	5	04-Mar-26	10-Mar-26	Not Started	52
CON-1650	Install Top & Bottom Track-3rd Floor	4	04-Mar-26	09-Mar-26	Not Started	52
CON-1910	Install Top & Bottom Track-4th Floor	4	10-Mar-26	13-Mar-26	Not Started	52
CON-2010	Install Wall Steel Studs & Framing-4th Floor	5	16-Mar-26	20-Mar-26	Not Started	52
CON-2200	Install Wall Steel Studs & Framing-5th Floor	5	23-Mar-26	27-Mar-26	Not Started	52
CON-2310	Install Ceiling Hangers & Supports-2nd Floor	4	16-Mar-26	19-Mar-26	Not Started	52
MIL-1140	Layout Start	0	23-Feb-26		Not Started	52
MIL-1160	Top & Bottom Track Start	0	26-Feb-26		Not Started	52
MIL-2612	Start Suspended Ceiling Grid	0	16-Mar-26		Not Started	52
CON-1530	Layout -3rd Floor	3	26-Feb-26	02-Mar-26	Not Started	53
CON-2020	Install Top & Bottom Track-5th Floor	4	16-Mar-26	19-Mar-26	Not Started	53
CON-4900	Rough-in Fuel Oil Piping -Fuel Oil Room	3	01-Jun-26	03-Jun-26	Not Started	54

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-5200	Rough-in Fuel Oil Vent Piping -Fuel Oil Room	4	09-Jun-26	12-Jun-26	Not Started	54
CON-5020	Rough-in Fuel Oil Fill Piping -Fuel Oil Room	3	04-Jun-26	08-Jun-26	Not Started	54
CON-1670	Layout -4th Floor	3	03-Mar-26	05-Mar-26	Not Started	54
CON-2390	Install Ceiling Hangers & Supports-3rd Floor	4	20-Mar-26	25-Mar-26	Not Started	54
CON-4500	Install SSDS Control Panel -1st Floor	5	07-May-26	13-May-26	Not Started	54
CON-1300	Spray Fireproofing - 3rd Floor	5	17-Mar-26	23-Mar-26	Not Started	55
CON-1390	Spray Fireproofing - 4th Floor	5	24-Mar-26	30-Mar-26	Not Started	55
CON-1730	Spray Fireproofing - 5th Floor	3	31-Mar-26	02-Apr-26	Not Started	55
CON-2120	Install Air Cooled Chiller CH-1 -Roof Floor	7	17-Mar-26	25-Mar-26	Not Started	56
CON-3520	Install Ceiling Hangers & Supports -1st Floor	4	15-Apr-26	20-Apr-26	Not Started	56
CON-1900	Install Wall Steel Studs & Framing-3rd Floor	5	10-Mar-26	16-Mar-26	Not Started	56
CON-1930	Layout -5th Floor	3	06-Mar-26	10-Mar-26	Not Started	56
MIL-1350	Electrical Rough-ins Finish	0		06-May-26	Not Started	57
CON-2550	Install Ceiling Hangers & Supports-4th Floor	4	26-Mar-26	31-Mar-26	Not Started	58
CON-5160	Install Fuel Oil Transfer Duplex Pump (FOP-1 & 2) -1st Floor	4	08-Jun-26	11-Jun-26	Not Started	59
CON-2850	Install Electric Unit Heaters -2nd Floor	5	16-Apr-26	22-Apr-26	Not Started	59
CON-3130	Install Electric Unit Heaters -3rd Floor	5	23-Apr-26	29-Apr-26	Not Started	59
CON-3420	Install Electric Unit Heaters -4th Floor	5	30-Apr-26	06-May-26	Not Started	59
CON-3640	Install Electric Unit Heaters -5th Floor	3	07-May-26	11-May-26	Not Started	59
CON-4990	Install Fuel Oil Storage Tank (FOT-1) - Fuel Oil Room	3	03-Jun-26	05-Jun-26	Not Started	59
CON-3150	Install Convector Heater CV - Mechanical Work - 2nd Floor	5	23-Apr-26	29-Apr-26	Not Started	59
CON-3450	Install Air Conditioning Unit AC - Mechanical Work - 2nd Floor	4	30-Apr-26	05-May-26	Not Started	59
I-1110	Fuel-Oil Storage & Fuel Oil Piping Systems Inspection	9	01-Jun-26	11-Jun-26	Not Started	59
CON-2620	Install Ceiling Hangers & Supports-5th Floor	4	01-Apr-26	06-Apr-26	Not Started	60
CON-2670	Install Wiring Devices -2nd Floor	7	06-Apr-26	14-Apr-26	Not Started	60
CON-3660	Install Wiring Devices -5th Floor	8	05-May-26	14-May-26	Not Started	60
CON-3280	Install Wiring Devices -4th Floor	7	24-Apr-26	04-May-26	Not Started	60
CON-2930	Install Wiring Devices -3rd Floor	7	15-Apr-26	23-Apr-26	Not Started	60
CON-2650	Install Data Rack - 4th Floor IDF Room	7	06-Apr-26	14-Apr-26	Not Started	61
CON-3290	Low Voltage Wires Pulling-5th Floor	6	23-Apr-26	30-Apr-26	Not Started	61
CON-2940	Low Voltage Wires Pulling-4th Floor	6	15-Apr-26	22-Apr-26	Not Started	61
CON-2690	Low Voltage Wires Pulling -3rd Floor	6	06-Apr-26	13-Apr-26	Not Started	61
APP-2330	Review & Approve Remedial Closure Report	21	30-Jul-26	19-Aug-26	Not Started	61
APP-2270	Review & Approve Final Foundations Coordination Drawings	21	12-Mar-25	01-Apr-25	Not Started	62
CON-2780	Install BACnet Data Cabinet - 2nd Floor -IDF Room	8	10-Apr-26	21-Apr-26	Not Started	62
CON-4560	Install Pavement Marking - 54th Avenue Street	3	11-Jun-26	15-Jun-26	Not Started	62
CON-4580	Remove Traffic Control Devices - 54th Avenue Street	3	16-Jun-26	18-Jun-26	Not Started	62
APP-1230	Review & Approve Initial Underground Coordination Drawings	21	27-Dec-24	16-Jan-25	Not Started	63
PRO-1570	Procure & Deliver Precast Sandwich Panels	112	30-Sep-25	19-Jan-26	Not Started	64
PRO-2040	Procure & Deliver VAV Units	170	30-Sep-25	18-Mar-26	Not Started	64
CON-4400	Install 4" Concrete Sidewalk - 54th Avenue Street	5	04-Jun-26	10-Jun-26	Not Started	65
CON-99347	Install Lightning Protection System - Roof Floor	6	05-Mar-26	12-Mar-26	Not Started	65
CON-1860	Rough-in Hot Glycol Piping-2nd Floor	7	02-Mar-26	10-Mar-26	Not Started	66
CON-2140	Rough-in Hot Glycol Piping-3rd Floor	7	11-Mar-26	19-Mar-26	Not Started	66
CON-2270	Rough-in Hot Glycol Piping-4th Floor	7	20-Mar-26	30-Mar-26	Not Started	66

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-2450	Rough-in Hot Glycol Piping-5th Floor	7	31-Mar-26	08-Apr-26	Not Started	66
PRO-1590	Procure & Deliver Steel Columns	120	02-Jun-25	29-Sep-25	Not Started	66
MIL-2992	Finish Fuel-Oil Storage & Fuel Oil Piping Systems Inspection	0		11-Jun-26	Not Started	67
CON-2350	Install Air Cooled Chiller CH-2 -Roof Floor	7	26-Mar-26	03-Apr-26	Not Started	69
CON-2820	Install Cable Ladder - 4th Floor IDF Room	5	13-Apr-26	17-Apr-26	Not Started	70
CON-2660	Install Voice Rack - 4th Floor IDF Room	5	06-Apr-26	10-Apr-26	Not Started	70
CON-7970	Coordinate With CON-ED For Gas Service	7	16-Apr-26	24-Apr-26	Not Started	70
CON-5790	Install Main Grounding Bus Bar - Electric Service Room	4	03-Jun-26	08-Jun-26	Not Started	70
CON-7990	Gas Authorization	5	24-Jun-26	30-Jun-26	Not Started	71
CON-8000	Pink Slip	5	01-Jul-26	08-Jul-26	Not Started	71
PRO-1150	Procure & Deliver Gypsum Board	150	30-Sep-25	26-Feb-26	Not Started	73
MIL-1150	Masonry Walls Start	0	23-Feb-26		Not Started	74
CON-1430	Install Unit Masonry Mock-Up	1	23-Feb-26	23-Feb-26	Not Started	74
CON-1470	Approve Unit Masonry Mock-Up	4	24-Feb-26	27-Feb-26	Not Started	74
CON-99307	Install Steel Stairs - 4th Floor	4	23-Feb-26	26-Feb-26	Not Started	74
CON-99317	Install Steel Stairs - 5th Floor	3	27-Feb-26	03-Mar-26	Not Started	74
PRO-1030	Procure & Deliver Mechanical Ducts	70	30-Sep-25	08-Dec-25	Not Started	76
CON-1540	Install Trusses - 5th Floor	2	26-Feb-26	27-Feb-26	Not Started	76
CON-4650	Install 3 Way Roof Manifold -Roof	5	23-Jun-26	29-Jun-26	Not Started	77
CON-99277	Install Steel Stairs -1st Floor	7	28-Jan-26	05-Feb-26	Not Started	77
CON-99287	Install Steel Stairs -2nd Floor	3	06-Feb-26	10-Feb-26	Not Started	77
CON-99297	Install Steel Stairs- 3rd Floor	4	11-Feb-26	17-Feb-26	Not Started	77
CON-1770	Install Roof Drains & Clean outs -Roof Floor	5	26-Feb-26	04-Mar-26	Not Started	79
CON-2230	Install Emergency Generator -Bulkhead	7	19-Mar-26	27-Mar-26	Not Started	79
CON-2070	Install Roof Drains & Clean outs - Mechanical Work - Roof Bulkhead	5	05-Mar-26	11-Mar-26	Not Started	79
CON-2190	Install Electric Unit Heater EUH - Mechanical Work - Roof Bulkhead	5	12-Mar-26	18-Mar-26	Not Started	79
CON-1570	Install CMU Walls -2nd Floor	3	02-Mar-26	04-Mar-26	Not Started	80
CON-1660	Install CMU Walls -3rd Floor	3	05-Mar-26	09-Mar-26	Not Started	80
CON-1920	Install CMU Walls -4th Floor	3	10-Mar-26	12-Mar-26	Not Started	80
CON-2030	Install CMU Walls -5th Floor	3	13-Mar-26	17-Mar-26	Not Started	80
MIL-2932	Start Masonry Inspection	0	05-Mar-26		Not Started	80
CON-3610	Install Floor Drains & Clean-outs -5th Floor	5	13-Feb-26	20-Feb-26	Not Started	82
PRO-1020	Procure & Deliver Mechanical Piping	70	30-Sep-25	08-Dec-25	Not Started	83
CON-4020	Install Filter Fabric -Roof Floor	3	07-May-26	11-May-26	Not Started	84
MIL-1170	Finish Concrete Work	0		11-Mar-26	Not Started	84
CON-1360	Install Trusses - 4th Floor	3	10-Feb-26	12-Feb-26	Not Started	84
MIL-1280	Main Roofing Finish	0		15-May-26	Not Started	85
PRO-1380	Procure & Deliver Roof Dunnage	100	30-Sep-25	07-Jan-26	Not Started	85
CON-4210	Install Concrete Pavers -Roof Floor	4	12-May-26	15-May-26	Not Started	85
CON-4050	Plumbing Piping Insulation -2nd Floor	5	07-May-26	13-May-26	Not Started	86
CON-4190	Plumbing Piping Insulation -3rd Floor	5	14-May-26	20-May-26	Not Started	86
CON-4390	Plumbing Piping Insulation -4th Floor	5	21-May-26	28-May-26	Not Started	86
CON-4530	Plumbing Piping Insulation -5th Floor	5	29-May-26	04-Jun-26	Not Started	86
CON-1460	F/R/P Piers - 5th Floor	5	23-Feb-26	27-Feb-26	Not Started	86
CON-1620	Install Dunnage - 5th Floor	8	02-Mar-26	11-Mar-26	Not Started	86
CON-3960	Install Concrete Pavers -5th Floor Roof	3	11-May-26	13-May-26	Not Started	87
CON-3820	Install Filter Fabric -5th Floor Roof	3	06-May-26	08-May-26	Not Started	87
CON-2100	Install Low Voltage Risers-5th Floor	3	13-Mar-26	17-Mar-26	Not Started	87

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
MIL-1310	5th Floor Roofing Finish	0		13-May-26	Not Started	87
CON-1710	Install Power Risers-2nd Floor	2	02-Mar-26	03-Mar-26	Not Started	87
CON-1820	Install Power Risers-3rd Floor	2	04-Mar-26	05-Mar-26	Not Started	87
CON-1960	Install Power Risers-4th Floor	2	06-Mar-26	09-Mar-26	Not Started	87
CON-2050	Install Power Risers-5th Floor	3	10-Mar-26	12-Mar-26	Not Started	87
CON-99337	Install Lightning Protection system -5th Floor	3	13-Mar-26	17-Mar-26	Not Started	87
CON-3700	Install Drainage -5th Floor Roof	3	30-Apr-26	04-May-26	Not Started	88
CON-1800	Install Low Voltage Risers-2nd Floor	2	04-Mar-26	05-Mar-26	Not Started	88
CON-1950	Install Low Voltage Risers-3rd Floor	2	06-Mar-26	09-Mar-26	Not Started	88
CON-2040	Install Low Voltage Risers-4th Floor	2	10-Mar-26	11-Mar-26	Not Started	88
CON-3200	Plumbing Pressure Testing -2nd Floor	5	28-Apr-26	04-May-26	Not Started	88
CON-3360	Plumbing Pressure Testing -3rd Floor	5	05-May-26	11-May-26	Not Started	88
CON-3560	Plumbing Pressure Testing -4th Floor	5	12-May-26	18-May-26	Not Started	88
CON-3530	Install Floor Drains & Clean-outs -4th Floor	5	28-Jan-26	03-Feb-26	Not Started	89
CON-4470	Install Wiring Devices -1st Floor	7	15-May-26	26-May-26	Not Started	90
CON-3590	Plumbing Pressure Testing -5th Floor	5	14-May-26	20-May-26	Not Started	91
CON-1260	Install Trusses - 3rd Floor	3	22-Jan-26	26-Jan-26	Not Started	94
CON-3400	Install Hot Water Circulation Pump -5th Floor	5	04-May-26	08-May-26	Not Started	94
CON-3410	Install Electric Hot Water Heater (EWH-1) -5th Floor	5	04-May-26	08-May-26	Not Started	94
CON-3320	Install Floor Drains & Clean-outs -3rd Floor	5	08-Jan-26	14-Jan-26	Not Started	97
CON-99327	Install Lightning Protection System-1st Floor	2	03-Dec-25	04-Dec-25	Not Started	97
CON-1090	Install Trusses -1st Floor	3	16-Dec-25	18-Dec-25	Not Started	98
CON-3270	Install Temporary Standpipe	9	29-Dec-25	09-Jan-26	Not Started	100
CON-3110	Install IPDVS Equipment Rack - 4th Floor IDF Room	5	20-Apr-26	24-Apr-26	Not Started	101
CON-2840	Install Main Sound Rack - 34th Floor IDF Room	5	13-Apr-26	17-Apr-26	Not Started	101
PRO-1290	Procure & Deliver Plumbing Pumps	250	30-Sep-25	06-Jun-26	Not Started	103
PRO-1990	Procure & Deliver Gas Meter Rig	60	25-Apr-26	23-Jun-26	Not Started	103
CON-1190	Install Trusses -2nd Floor	4	02-Jan-26	07-Jan-26	Not Started	103
CON-3160	Install Floor Drains & Clean-outs -2nd Floor	5	19-Dec-25	26-Dec-25	Not Started	104
PRO-1010	Procure & Deliver Furnitures	130	30-Sep-25	06-Feb-26	Not Started	104
CON-2810	Install Grounding Bars - 4th Floor IDF Room	5	06-Apr-26	10-Apr-26	Not Started	106
SUB-3710	Prepare & Submit AHU for Public Assemblies Sapces Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	106
SUB-3720	Prepare & Submit AHU for Public Assemblies Sapces Product Data	81	15-Oct-24	11-Feb-25	Not Started	106
SUB-1700	Prepare & Submit Roof Dunnage	81	05-Mar-25	27-Jun-25	Not Started	107
CON-1280	Install Elevator Hoist Pad	5	20-Jan-26	26-Jan-26	Not Started	110
CON-1320	Erect Material Hoist	5	27-Jan-26	02-Feb-26	Not Started	110
CON-1160	Hoist Material Design	10	29-Dec-25	12-Jan-26	Not Started	110
PRO-2010	Procure & Deliver Steel Stairs Components	120	30-Sep-25	27-Jan-26	Not Started	110
CON-2410	Install Storefront System-West Elevation	5	30-Mar-26	03-Apr-26	Not Started	115
SUB-1710	Prepare & Submit Chillers Product Data	71	15-Oct-24	28-Jan-25	Not Started	116
SUB-1950	Prepare & Submit Structure Steel Drawings	71	15-Oct-24	28-Jan-25	Not Started	117
MIL-2572	Place Steel Mill Order	0	20-Feb-25		Not Started	117
CON-2360	Install Smoke Purge Fan SPF - Mechanical Work - Roof Bulkhead	3	26-Mar-26	30-Mar-26	Not Started	119
CON-8390	Install Sidewalk Sheds -South Elevation	4	29-Dec-25	02-Jan-26	Not Started	120
CON-8400	Install Sidewalk Sheds -East Elevation	4	29-Dec-25	02-Jan-26	Not Started	120
MIL-1720	Start Sidewalk Bridge Installations	0	29-Dec-25		Not Started	120
PRO-1200	Procure & Deliver Elevator Machine	112	30-Sep-25	19-Jan-26	Not Started	122
CON-2000	Install SSDS Risers -SSDS System -5th Floor	1	09-Mar-26	09-Mar-26	Not Started	122

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
PRO-1250	Procure & Deliver Plumbing Pipes	60	30-Sep-25	28-Nov-25	Not Started	131
CON-2570	Field Testing of Windows (5%)	5	06-Apr-26	10-Apr-26	Not Started	131
MIL-1820	Crane Mobilization-Steel Installation Finish	0		12-Mar-26	Not Started	131
MIL-2622	Deliveries of all owner-furnished equipment and/or materials	0		06-Feb-26	Not Started	137
PRO-2020	Procure & Deliver Flagpole	60	30-Sep-25	28-Nov-25	Not Started	137
PRO-1090	Procure & Deliver Fire Sprinklers	100	30-Sep-25	07-Jan-26	Not Started	139
SUB-1200	Prepare & Submit Planting Schedule	81	15-Oct-24	11-Feb-25	Not Started	144
PRO-1050	Procure & Deliver Electrical Equipment	130	30-Sep-25	06-Feb-26	Not Started	144
SUB-1850	Prepare & Submit Record Documents	81	15-Oct-24	11-Feb-25	Not Started	144
SUB-2080	Prepare & Submit Waste Handling Equipment	81	15-Oct-24	11-Feb-25	Not Started	144
SUB-2160	Prepare & Submit Overcurrent Protective Devices Data	81	15-Oct-24	11-Feb-25	Not Started	144
SUB-3230	Prepare & Submit Shop Equipment Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	144
SUB-3240	Prepare & Submit Shop Equipment Product Data	81	15-Oct-24	11-Feb-25	Not Started	144
SUB-3300	Prepare & Submit Certification of Tests	81	15-Oct-24	11-Feb-25	Not Started	144
SUB-3310	Prepare & Submit Domestic Water Sterilization Plan	81	15-Oct-24	11-Feb-25	Not Started	144
SUB-3320	Prepare & Submit Tags, Charts & Identifications Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	144
SUB-3330	Prepare & Submit Tags, Charts & Identifications Product Data	81	15-Oct-24	11-Feb-25	Not Started	144
SUB-3340	Prepare & Submit Micselianeous Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	144
SUB-4080	Prepare & Submit Green School Submittal	81	15-Oct-24	11-Feb-25	Not Started	144
MIL-2762	Green Schools Compliance Submission	0		04-Mar-25	Not Started	145
PRO-1560	Procure & Deliver Gymnasium Equipment	180	30-Sep-25	28-Mar-26	Not Started	148
PRO-1160	Procure & Deliver Floorings	80	30-Sep-25	18-Dec-25	Not Started	150
SUB-3380	Prepare & Submit Schedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	81	15-Oct-24	11-Feb-25	Not Started	150
SUB-3400	Prepare & Submit Hydronic Specialities Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	150
SUB-3410	Prepare & Submit Hydronic Specialities Product Data	81	15-Oct-24	11-Feb-25	Not Started	150
SUB-3420	Prepare & Submit Water Treatment Firm	81	15-Oct-24	11-Feb-25	Not Started	150
SUB-3430	Prepare & Submit Chemical Products Product Data	81	15-Oct-24	11-Feb-25	Not Started	150
SUB-3610	Prepare & Submit Air Filters Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	150
SUB-3620	Prepare & Submit Air Filters Product Data	81	15-Oct-24	11-Feb-25	Not Started	150
SUB-3630	Prepare & Submit Air Filters Maintenance Data & Materials	81	15-Oct-24	11-Feb-25	Not Started	150
SUB-3730	Prepare & Submit AHU for Public Assemblies Sapces Maintenance Data & Materials	81	15-Oct-24	11-Feb-25	Not Started	150
SUB-3740	Prepare & Submit Control Systems Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	150
SUB-3750	Prepare & Submit Truck Network Cable Schematic Diagram	81	15-Oct-24	11-Feb-25	Not Started	150
PRO-1410	Procure & Deliver Door Frames	70	30-Sep-25	08-Dec-25	Not Started	153
SUB-1900	Prepare & Submit Chain Link Fences & Gates Drawings	81	15-Oct-24	11-Feb-25	Not Started	153
SUB-1960	Prepare & Submit Metal Deck Product Data	81	15-Oct-24	11-Feb-25	Not Started	153
SUB-2370	Prepare & Submit Ornamenta Metal Shop Drawings	81	15-Oct-24	11-Feb-25	Not Started	153
SUB-2930	Prepare & Submit Ornamenta Metal Product Data	81	15-Oct-24	11-Feb-25	Not Started	153
SUB-2340	Prepare & Submit Tree Protection Plan	71	15-Oct-24	28-Jan-25	Not Started	154
APP-3710	Review & Approve AHU for Public Assemblies Sapces Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	154
APP-3720	Review & Approve AHU for Public Assemblies	21	12-Feb-25	04-Mar-25	Not Started	154

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
	Submit Product Data					
SUB-1290	Prepare & Submit Gas Vapor Barrier Submittal & Inspection Schedule	81	15-Oct-24	11-Feb-25	Not Started	156
CON-1250	Approval of Hoist Design	7	13-Jan-26	19-Jan-26	Not Started	157
SUB-2140	Prepare & Submit Switch & Panel Boards	81	15-Oct-24	11-Feb-25	Not Started	157
APP-1810	Review & Approve Roof Dunnage	21	28-Jun-25	18-Jul-25	Not Started	158
PRO-1600	Procure & Deliver Trusses	60	30-Sep-25	28-Nov-25	Not Started	159
SUB-1720	Prepare & Submit Air Handling Units Product Data	71	15-Oct-24	28-Jan-25	Not Started	160
SUB-1970	Prepare & Submit Prefabricated Expansion Joint Covers	81	15-Oct-24	11-Feb-25	Not Started	161
PRO-1470	Procure & Deliver Cabinet Heaters	126	30-Sep-25	02-Feb-26	Not Started	163
SUB-1740	Prepare & Submit Emergency Generator System Product Data	71	15-Oct-24	28-Jan-25	Not Started	163
SUB-1140	Prepare & Submit Perimeter Foundation Insulation Product Data	81	15-Oct-24	11-Feb-25	Not Started	164
SUB-2980	Prepare & Submit Aluminum Framed Entrances & Storefronts Shop Drawings	81	15-Oct-24	11-Feb-25	Not Started	165
SUB-2990	Prepare & Submit Aluminum Framed Entrances & Storefronts Product Data	81	15-Oct-24	11-Feb-25	Not Started	165
PRO-1000	Procure & Deliver Kitchen Equipment	180	30-Sep-25	28-Mar-26	Not Started	166
CON-8040	CON-ED Work For Temporary Electrical Power	10	20-Oct-25	31-Oct-25	Not Started	166
CON-8050	Available Temporary Electrical Power For Testing MEP Equipment	0		31-Oct-25	Not Started	166
SUB-1420	Prepare & Submit Electrical Shop Drawings	81	15-Oct-24	11-Feb-25	Not Started	168
APP-1820	Review & Approve Chillers Product Data	21	29-Jan-25	18-Feb-25	Not Started	168
PRO-1170	Procure & Deliver Acosutical Ceiling Tiles	120	30-Sep-25	27-Jan-26	Not Started	169
CON-7750	Install Field Offices	5	08-Oct-25	15-Oct-25	Not Started	169
APP-1950	Review & Approve Structure Steel Drawings	21	29-Jan-25	18-Feb-25	Not Started	169
PRO-1630	Procure & Deliver Wood Flooring	120	30-Sep-25	27-Jan-26	Not Started	170
PRO-1640	Procure & Deliver Concrete Floating Floor Assembly	120	30-Sep-25	27-Jan-26	Not Started	170
CON-4920	Install Floor Drains & Clean-outs -1st Floor	5	27-Nov-25	04-Dec-25	Not Started	173
SUB-1610	Prepare & Submit Baseline Schedule	52	15-Oct-24	30-Dec-24	Not Started	173
PRO-1070	Procure & Deliver Wood Doors	50	30-Sep-25	18-Nov-25	Not Started	173
SUB-2050	Prepare & Submit Stationary Metal Wall Louvers	73	15-Oct-24	30-Jan-25	Not Started	173
SUB-1670	Prepare & Submit Aluminum Projected Windows	71	15-Oct-24	28-Jan-25	Not Started	175
CON-1150	Install Steel Canopy Framing -2nd Floor	5	29-Dec-25	05-Jan-26	Not Started	177
SUB-1190	Prepare & Submit Formwork Shop Drawings	81	15-Oct-24	11-Feb-25	Not Started	180
PRO-1420	Procure & Deliver Painting	70	30-Sep-25	08-Dec-25	Not Started	184
PRO-1210	Procure & Deliver Signs	70	30-Sep-25	08-Dec-25	Not Started	185
PRO-1450	Procure & Deliver Playground Equipment	60	09-Dec-25	06-Feb-26	Not Started	185
CON-9000	Protection & Restoration the adjacent Properties to Original Condition	263	30-Sep-25	19-Oct-26	Not Started	186
SUB-3070	Prepare & Submit Special Coating Samples	81	15-Oct-24	11-Feb-25	Not Started	188
SUB-3080	Prepare & Submit Special Coating Product Data	81	15-Oct-24	11-Feb-25	Not Started	188
SUB-3680	Prepare & Submit Variable Air Terminals Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	188
SUB-3690	Prepare & Submit Variable Air Terminals Product Data	81	15-Oct-24	11-Feb-25	Not Started	188
SUB-3700	Prepare & Submit Variable Air Terminals Maintenance Data & Materials	81	15-Oct-24	11-Feb-25	Not Started	188
PRE-2610	Prepare & Submit FDNY Fuel Permit	10	06-Oct-25	20-Oct-25	Not Started	191
PRO-2030	Procure & Deliver Bleachers	130	30-Sep-25	06-Feb-26	Not Started	193
SUB-1470	Prepare & Submit Gypsum Board	81	15-Oct-24	11-Feb-25	Not Started	195
SUB-1570	Prepare & Submit QCP	30	15-Oct-24	26-Nov-24	Not Started	195
SUB-1540	Prepare & Submit Mechanical Ducts	81	15-Oct-24	11-Feb-25	Not Started	196

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
SUB-3350	Prepare & Submit Valves (HVAC) Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	196
SUB-3360	Prepare & Submit Valves (HVAC) Product Data	81	15-Oct-24	11-Feb-25	Not Started	196
SUB-3640	Prepare & Submit Duct Accessories Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	196
PRO-1360	Procure & Deliver Metal Panel Ceilings	120	30-Sep-25	27-Jan-26	Not Started	198
SUB-1920	Prepare & Submit Precast Architectural Concrete	71	15-Oct-24	28-Jan-25	Not Started	198
CLO-1300	Provide Training	10	09-Sep-26	22-Sep-26	Not Started	198
PRO-2050	Procure & Deliver Furnitures (Owner Responsibility)	130	30-Sep-25	06-Feb-26	Not Started	199
SUB-1280	Prepare & Submit SSDS Geotextile	40	15-Oct-24	11-Dec-24	Not Started	200
SUB-3370	Prepare & Submit Piping Insulation Schedule Listing Items	81	15-Oct-24	11-Feb-25	Not Started	200
PRO-1140	Procure & Deliver Lighting Fixtures	60	30-Sep-25	28-Nov-25	Not Started	201
APP-1520	Review & Approve Planting Schedule	21	12-Feb-25	04-Mar-25	Not Started	209
PRO-1110	Procure & Deliver Fire Detectors & Alarms	60	30-Sep-25	28-Nov-25	Not Started	209
APP-1860	Review & Approve Record Documents	21	12-Feb-25	04-Mar-25	Not Started	209
APP-2070	Review & Approve Waste Handling Equipment	21	12-Feb-25	04-Mar-25	Not Started	209
APP-2150	Review & Approve Overcurrent Protective Devices Data	21	12-Feb-25	04-Mar-25	Not Started	209
APP-3230	Review & Approve Shop Equipment Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	209
APP-3240	Review & Approve Shop Equipment Product Data	21	12-Feb-25	04-Mar-25	Not Started	209
APP-3300	Review & Approve Certification of Tests	21	12-Feb-25	04-Mar-25	Not Started	209
APP-3310	Review & Approve Domestic Water Sterilization Plan	21	12-Feb-25	04-Mar-25	Not Started	209
APP-3320	Review & Approve Tags, Charts & Identifications Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	209
APP-3330	Review & Approve Tags, Charts & Identifications Product Data	21	12-Feb-25	04-Mar-25	Not Started	209
APP-3340	Review & Approve Micselianeous Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	209
APP-4080	Review & Approve Green School Submittal	21	12-Feb-25	04-Mar-25	Not Started	209
SUB-1560	Prepare & Submit Erosion Control and Sedimentation Plan	7	15-Oct-24	23-Oct-24	Not Started	211
SUB-1350	Prepare & Submit Site Safety Plan	2	15-Oct-24	16-Oct-24	Not Started	214
SUB-1300	Prepare & Submit Existing Conditions Survey	10	15-Oct-24	28-Oct-24	Not Started	215
SUB-1400	Prepare & Submit Sustainable Materials	10	15-Oct-24	28-Oct-24	Not Started	215
SUB-1430	Prepare & Submit Plumbing Shop Drawings	81	15-Oct-24	11-Feb-25	Not Started	215
SUB-1530	Prepare & Submit Furniture	81	15-Oct-24	11-Feb-25	Not Started	215
SUB-2110	Prepare & Submit Manufactured Wood Casework	81	15-Oct-24	11-Feb-25	Not Started	215
SUB-3110	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals	81	15-Oct-24	11-Feb-25	Not Started	215
SUB-3120	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	81	15-Oct-24	11-Feb-25	Not Started	215
SUB-3130	Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	81	15-Oct-24	11-Feb-25	Not Started	215
SUB-3160	Prepare & Submit Metal Storage Shelving Samples	81	15-Oct-24	11-Feb-25	Not Started	215
SUB-3170	Prepare & Submit Metal Storage Shelving Shop drawings	81	15-Oct-24	11-Feb-25	Not Started	215
APP-3380	Review & Approve chedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)	21	12-Feb-25	04-Mar-25	Not Started	217
APP-3400	Review & Approve Hydronic Specialities Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	217
APP-3410	Review & Approve Hydronic Specialities Product Data	21	12-Feb-25	04-Mar-25	Not Started	217

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
APP-3420	Review & Approve Water Treatment Firm	21	12-Feb-25	04-Mar-25	Not Started	217
APP-3430	Review & Approve Chemical Products Product Data	21	12-Feb-25	04-Mar-25	Not Started	217
APP-3610	Review & Approve Air Filters Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	217
APP-3620	Review & Approve Air Filters Product Data	21	12-Feb-25	04-Mar-25	Not Started	217
APP-3630	Review & Approve Air Filters Maintenance Data & Materials	21	12-Feb-25	04-Mar-25	Not Started	217
APP-3730	Review & Approve AHU for Public Assemblies Sapces Maintenance Data & Materials	21	12-Feb-25	04-Mar-25	Not Started	217
APP-3740	Review & Approve Control Systems Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	217
APP-3750	Review & Approve Truck Network Cable Schematic Diagram	21	12-Feb-25	04-Mar-25	Not Started	217
SUB-1750	Prepare & Submit Switch Gears Product Data	20	15-Oct-24	12-Nov-24	Not Started	218
SUB-1210	Prepare & Submit Site Furnishings Shop Drawings	15	15-Oct-24	04-Nov-24	Not Started	219
SUB-1370	Prepare & Submit Photo Submission - Temporary Fence	15	15-Oct-24	04-Nov-24	Not Started	219
PRO-1310	Procure & Deliver Telecommunication System	60	30-Sep-25	28-Nov-25	Not Started	219
PRO-1330	Procure & Deliver Cameras	60	30-Sep-25	28-Nov-25	Not Started	219
PRO-1500	Procure & Deliver Boilers	84	30-Sep-25	22-Dec-25	Not Started	219
MIL-2802	Provision of Training Schedules (30 days prior to start of Training)	0	10-Aug-26		Not Started	219
SUB-4060	Prepare & Submit Steel Stairs Shop Drawings	81	15-Oct-24	11-Feb-25	Not Started	219
SUB-4070	Prepare & Submit Steel Stairs Product Data	81	15-Oct-24	11-Feb-25	Not Started	219
SUB-1550	Prepare & Submit Mechanical Piping	60	15-Oct-24	10-Jan-25	Not Started	221
APP-1900	Review & Approve Chain Link Fences & Gates Drawings	21	12-Feb-25	04-Mar-25	Not Started	222
APP-1960	Review & Approve Metal Deck Product Data	21	12-Feb-25	04-Mar-25	Not Started	222
APP-2370	Review & Approve Ornamenta Metal Shop Drawings	21	12-Feb-25	04-Mar-25	Not Started	222
APP-2930	Review & Approve Ornamenta Metal Product Data	21	12-Feb-25	04-Mar-25	Not Started	222
APP-2340	Review & Approve Tree Protection Plan	21	29-Jan-25	18-Feb-25	Not Started	223
APP-1580	Review & Approve Gas Vapor Barrier Submittal & Inspection Schedule	21	12-Feb-25	04-Mar-25	Not Started	225
APP-2130	Review & Approve Switch & Panel Boards	21	12-Feb-25	04-Mar-25	Not Started	226
SUB-1590	Prepare & Submit Electrical Equipment, Conduits, and Cables	20	15-Oct-24	12-Nov-24	Not Started	229
SUB-1180	Prepare & Submit Concrete Reinforcement	30	15-Oct-24	26-Nov-24	Not Started	231
SUB-1450	Prepare & Submit Concrete Shop Drawings	30	15-Oct-24	26-Nov-24	Not Started	231
SUB-1580	Prepare & Submit Concrete Mix Design	30	15-Oct-24	26-Nov-24	Not Started	231
APP-1300	Review & Approve Air Handling Units Product Data	21	29-Jan-25	18-Feb-25	Not Started	231
PRE-2590	Meeting With SCA to Review The Permit Requirements	14	30-Sep-24	18-Oct-24	Not Started	231
APP-1970	Review & Approve Prefabricated Expansion Joint Covers	21	12-Feb-25	04-Mar-25	Not Started	232
SUB-3280	Prepare & Submit Valves Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	233
SUB-3290	Prepare & Submit Valves Product Data	81	15-Oct-24	11-Feb-25	Not Started	233
APP-1070	Review & Approve Emergency Generator System Product Data	21	29-Jan-25	18-Feb-25	Not Started	234
PRO-1530	Procure & Deliver Hydraulic Vertical Wheelchair Lift	90	30-Sep-25	28-Dec-25	Not Started	234
APP-1470	Review & Approve Perimeter Foundation Insulation Product Data	21	12-Feb-25	04-Mar-25	Not Started	237
SUB-1440	Prepare & Submit Sprinkler System Shop Drawings	81	15-Oct-24	11-Feb-25	Not Started	237
SUB-1460	Prepare & Submit Elevator Machine	71	15-Oct-24	28-Jan-25	Not Started	237
SUB-3090	Prepare & Submit Flagpole Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	237
SUB-3100	Prepare & Submit Flagpole Product Data	81	15-Oct-24	11-Feb-25	Not Started	237

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
APP-2980	Review & Approve Aluminum Framed Entrances & Storefronts Shop Drawings	21	12-Feb-25	04-Mar-25	Not Started	238
APP-2990	Review & Approve Aluminum Framed Entrances & Storefronts Product Data	21	12-Feb-25	04-Mar-25	Not Started	238
SUB-1880	Prepare & Submit Foundation Product Data	5	15-Oct-24	21-Oct-24	Not Started	240
MIL-2542	Complete Subcontractor 'Buyout'	0		11-Oct-24	Not Started	240
APP-1650	Review & Approve Electrical Shop Drawings	21	12-Feb-25	04-Mar-25	Not Started	241
CON-8030	Procurement From CON-ED For Temporary Electrical Power	20	30-Sep-25	19-Oct-25	Not Started	241
PRO-1190	Procure & Deliver Toilet Accessories	100	30-Sep-25	07-Jan-26	Not Started	244
PRO-1060	Procure & Deliver Plumbing Fixtures	100	30-Sep-25	07-Jan-26	Not Started	244
PRO-1280	Procure & Deliver Fire Protection Pumps	70	30-Sep-25	08-Dec-25	Not Started	244
SUB-1770	Prepare & Submit Gymnasium Equipment	81	15-Oct-24	11-Feb-25	Not Started	244
SUB-1480	Prepare & Submit Floorings	81	15-Oct-24	11-Feb-25	Not Started	246
PRO-1660	Procure & Deliver Auditorium Television Studio Dimming System	90	30-Sep-25	28-Dec-25	Not Started	246
SUB-1100	Prepare & Submit Door & Frame Corners Samples	81	15-Oct-24	11-Feb-25	Not Started	247
APP-1320	Review & Approve Stationary Metal Wall Louvers	21	31-Jan-25	20-Feb-25	Not Started	250
SUB-3060	Prepare & Submit Graffiti Resistant Coating Product Data	81	15-Oct-24	11-Feb-25	Not Started	250
APP-1240	Review & Approve Baseline Schedule	21	31-Dec-24	20-Jan-25	Not Started	252
APP-1310	Review & Approve Aluminum Projected Windows	21	29-Jan-25	18-Feb-25	Not Started	252
SUB-3000	Prepare & Submit Thresholds, Weatherstripping and Seals Color Samples	81	15-Oct-24	11-Feb-25	Not Started	253
SUB-3010	Prepare & Submit Thresholds, Weatherstripping and Seals Product Data	81	15-Oct-24	11-Feb-25	Not Started	253
SUB-3020	Prepare & Submit Miscellaneous Glazing Samples	81	15-Oct-24	11-Feb-25	Not Started	253
SUB-3030	Prepare & Submit Miscellaneous Glazing Product Data	81	15-Oct-24	11-Feb-25	Not Started	253
SUB-3040	Prepare & Submit Fire Rated Glazing Samples	81	15-Oct-24	11-Feb-25	Not Started	253
SUB-3050	Prepare & Submit Fire Rated Glazing Product Data	81	15-Oct-24	11-Feb-25	Not Started	253
SUB-3140	Prepare & Submit Wire Mesh Work Samples	81	15-Oct-24	11-Feb-25	Not Started	253
SUB-3150	Prepare & Submit Wire Mesh Work Shop drawings	81	15-Oct-24	11-Feb-25	Not Started	253
SUB-2090	Prepare & Submit Domestic Equipment	81	15-Oct-24	11-Feb-25	Not Started	256
SUB-2010	Prepare & Submit Wood Flooring	81	15-Oct-24	11-Feb-25	Not Started	259
SUB-2120	Prepare & Submit Concrete Floating Floor Assembly	81	15-Oct-24	11-Feb-25	Not Started	259
SUB-3930	Prepare & Submit Fiber Optic Cabling system Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	259
SUB-3940	Prepare & Submit Fiber Optic Cabling system Product Data	81	15-Oct-24	11-Feb-25	Not Started	259
SUB-3950	Prepare & Submit Fiber Optic Cabling system Samples	81	15-Oct-24	11-Feb-25	Not Started	259
APP-1510	Review & Approve Formwork Shop Drawings	21	12-Feb-25	04-Mar-25	Not Started	260
SUB-1620	Prepare & Submit Wood Doors	81	15-Oct-24	11-Feb-25	Not Started	261
PRO-1270	Procure & Deliver Mechanical Pumps	70	30-Sep-25	08-Dec-25	Not Started	262
SUB-1650	Prepare & Submit Kitchen Equipment	71	15-Oct-24	28-Jan-25	Not Started	266
SUB-1940	Prepare & Submit Cast Stone Product Data	81	15-Oct-24	11-Feb-25	Not Started	268
SUB-1090	Prepare & Submit Painting	81	15-Oct-24	11-Feb-25	Not Started	269
SUB-1660	Prepare & Submit Signs	81	15-Oct-24	11-Feb-25	Not Started	270
APP-3070	Review & Approve Special Coating Samples	21	12-Feb-25	04-Mar-25	Not Started	273
APP-3080	Review & Approve Special Coating Product Data	21	12-Feb-25	04-Mar-25	Not Started	273
APP-3680	Review & Approve Variable Air Terminals Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	273

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
APP-3690	Review & Approve Variable Air Terminals Product Data	21	12-Feb-25	04-Mar-25	Not Started	273
APP-3700	Review & Approve Variable Air Terminals Maintenance Data & Materials	21	12-Feb-25	04-Mar-25	Not Started	273
SUB-1330	Prepare & Submit Temporary Ventilation Plan	81	15-Oct-24	11-Feb-25	Not Started	274
SUB-1340	Prepare & Submit Construction Indoor Air Quality Management Plan	81	15-Oct-24	11-Feb-25	Not Started	274
SUB-1040	Prepare & Submit Hangers & Supports	40	15-Oct-24	11-Dec-24	Not Started	275
SUB-1760	Prepare & Submit Unit Cabinet Heaters	60	15-Oct-24	10-Jan-25	Not Started	275
SUB-1150	Prepare & Submit Crystalline Waterproofing Product Data	81	15-Oct-24	11-Feb-25	Not Started	276
SUB-2260	Prepare & Submit Air Outlets & Inlets	81	15-Oct-24	11-Feb-25	Not Started	276
PRO-1620	Procure & Deliver Security Screens & Barriers	60	30-Sep-25	28-Nov-25	Not Started	276
SUB-3250	Prepare & Submit Bleachers Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	276
SUB-3260	Prepare & Submit Bleachers Product Data	81	15-Oct-24	11-Feb-25	Not Started	276
SUB-3270	Prepare & Submit Bleachers Manufacturer's Warranty	81	15-Oct-24	11-Feb-25	Not Started	276
SUB-1490	Prepare & Submit Acosutical Ceiling Tiles	60	15-Oct-24	10-Jan-25	Not Started	279
PRE-2620	Review & Approve FDNY Fuel Permit	21	21-Oct-25	10-Nov-25	Not Started	280
SUB-1130	Prepare & Submit Roofing Membrane Product Data	81	15-Oct-24	11-Feb-25	Not Started	282
APP-1680	Review & Approve Gypsum Board	21	12-Feb-25	04-Mar-25	Not Started	282
SUB-1120	Prepare & Submit Flashing & Sheet Metal Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	283
SUB-1980	Prepare & Submit Self Adhering Sheet Air Barriers	81	15-Oct-24	11-Feb-25	Not Started	283
SUB-3900	Prepare & Submit Lightning Protection Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	284
SUB-3920	Prepare & Submit Lightning Protection Test Reports	81	15-Oct-24	11-Feb-25	Not Started	284
APP-1730	Review & Approve Mechanical Ducts	21	12-Feb-25	04-Mar-25	Not Started	285
APP-3350	Review & Approve Valves (HVAC) Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	285
APP-3360	Review & Approve Valves (HVAC) Product Data	21	12-Feb-25	04-Mar-25	Not Started	285
APP-3640	Review & Approve Duct Accessories Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	285
SUB-1640	Prepare & Submit Fire Detectors & Alarms	81	15-Oct-24	11-Feb-25	Not Started	286
APP-1130	Review & Approve QCP	21	27-Nov-24	17-Dec-24	Not Started	286
APP-1920	Review & Approve Precast Architectural Concrete	21	29-Jan-25	18-Feb-25	Not Started	287
SUB-1860	Prepare & Submit Environmental Site Assessment Reports	81	15-Oct-24	11-Feb-25	Not Started	290
SUB-1520	Prepare & Submit Lighting Fixtures	71	15-Oct-24	28-Jan-25	Not Started	291
APP-1200	Review & Approve SSDS Geotextile	21	12-Dec-24	01-Jan-25	Not Started	292
APP-3370	Review & Approve Piping Insulation Schedule Listing Items	21	12-Feb-25	04-Mar-25	Not Started	292
SUB-1020	Prepare & Submit Pressure Gages	40	15-Oct-24	11-Dec-24	Not Started	293
SUB-1680	Prepare & Submit Telecommunication System Drawings	81	15-Oct-24	11-Feb-25	Not Started	294
SUB-1690	Prepare & Submit Internet Protocol Digital Video Surveillance System using Digital Cameras	71	15-Oct-24	28-Jan-25	Not Started	294
SUB-3480	Prepare & Submit Plate Heat Exchanger Maintenance Data	81	15-Oct-24	11-Feb-25	Not Started	294
SUB-3490	Prepare & Submit Plate Heat Exchanger Product Data	81	15-Oct-24	11-Feb-25	Not Started	294
SUB-3760	Prepare & Submit Lighting Control Devices Shop Drawing	71	15-Oct-24	28-Jan-25	Not Started	294
SUB-3770	Prepare & Submit Lighting Control Devices Product Data	71	15-Oct-24	28-Jan-25	Not Started	294
SUB-3780	Prepare & Submit Lighting Control Devices Warranty	71	15-Oct-24	28-Jan-25	Not Started	294

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
SUB-2170	Prepare & Submit Gas Pipes	81	15-Oct-24	11-Feb-25	Not Started	296
SUB-1870	Prepare & Submit Selective Removals & Demoloition	81	15-Oct-24	11-Feb-25	Not Started	298
SUB-3390	Prepare & Submit Schedules Showing Manfacturers's Product Number Duct Work Insulation	81	15-Oct-24	11-Feb-25	Not Started	298
SUB-1380	Prepare & Submit Heating Plan	81	15-Oct-24	11-Feb-25	Not Started	300
SUB-1730	Prepare & Submit Boilers	71	15-Oct-24	28-Jan-25	Not Started	304
SUB-3440	Prepare & Submit Detail of Gag for the Safety Relief Valves	71	15-Oct-24	28-Jan-25	Not Started	304
SUB-3450	Prepare & Submit Boiler Accessories Maintenance Data	71	15-Oct-24	28-Jan-25	Not Started	304
SUB-2130	Prepare & Submit Hydraulic Vertical Wheelchair Lifts	81	15-Oct-24	11-Feb-25	Not Started	305
SUB-3180	Prepare & Submit Mirrors Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	305
SUB-3190	Prepare & Submit Mirrors Product Data	81	15-Oct-24	11-Feb-25	Not Started	305
SUB-3200	Prepare & Submit Mirrors Mastic Compatibility Test Reports & Certifications	81	15-Oct-24	11-Feb-25	Not Started	305
SUB-1390	Prepare & Submit Sample Classroom Materials	81	15-Oct-24	11-Feb-25	Not Started	308
APP-1020	Review & Approve Erosion Control and Sedimentation Plan	21	24-Oct-24	13-Nov-24	Not Started	308
SUB-1160	Prepare & Submit Suspension Assembly Shop Drawings	81	15-Oct-24	11-Feb-25	Not Started	309
SUB-1050	Prepare & Submit Fire & Jockey Pumps	81	15-Oct-24	11-Feb-25	Not Started	311
SUB-1500	Prepare & Submit Toilet Accessories	81	15-Oct-24	11-Feb-25	Not Started	311
SUB-1600	Prepare & Submit Plumbing Fixtures	81	15-Oct-24	11-Feb-25	Not Started	311
SUB-1630	Prepare & Submit Fire Protection Shop Drawings	81	15-Oct-24	11-Feb-25	Not Started	311
SUB-3210	Prepare & Submit Grab Bars Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	311
SUB-3220	Prepare & Submit Grab Bars Product Data	81	15-Oct-24	11-Feb-25	Not Started	311
APP-1660	Review & Approve Plumbing Shop Drawings	21	12-Feb-25	04-Mar-25	Not Started	312
APP-1000	Review & Approve Site Safety Plan	21	17-Oct-24	06-Nov-24	Not Started	313
APP-1720	Review & Approve Furniture	21	12-Feb-25	04-Mar-25	Not Started	313
APP-2100	Review & Approve Manufactured Wood Casework	21	12-Feb-25	04-Mar-25	Not Started	313
SUB-2150	Prepare & Submit Auditorium & Television Studio Dimming System Product Data	81	15-Oct-24	11-Feb-25	Not Started	313
APP-3110	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals	21	12-Feb-25	04-Mar-25	Not Started	313
APP-3120	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings	21	12-Feb-25	04-Mar-25	Not Started	313
APP-3130	Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples	21	12-Feb-25	04-Mar-25	Not Started	313
APP-3160	Review & Approve Metal Storage Shelving Samples	21	12-Feb-25	04-Mar-25	Not Started	313
APP-3170	Review & Approve Metal Storage Shelving Shop drawings	21	12-Feb-25	04-Mar-25	Not Started	313
SUB-2040	Prepare & Submit Fire Extinguishers & Cabinets	81	15-Oct-24	11-Feb-25	Not Started	314
APP-1030	Review & Approve Existing Conditions Survey	21	29-Oct-24	18-Nov-24	Not Started	315
APP-1040	Review & Approve Sustainable Materials	21	29-Oct-24	18-Nov-24	Not Started	315
SUB-1260	Prepare & Submit Steel Curb Facing Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	316
APP-1090	Review & Approve Switch Gears Product Data	21	13-Nov-24	03-Dec-24	Not Started	317
APP-4060	Review & Approve Steel Stairs Shop Drawings	21	12-Feb-25	04-Mar-25	Not Started	319
APP-4070	Review & Approve Steel Stairs Product Data	21	12-Feb-25	04-Mar-25	Not Started	319
SUB-1220	Prepare & Submit Playgroung Equipment Shop Drawings	81	15-Oct-24	11-Feb-25	Not Started	320

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
SUB-1910	Prepare & Submit Outdoor Game Equipment	81	15-Oct-24	11-Feb-25	Not Started	320
SUB-1010	Prepare & Submit Thermometers	40	15-Oct-24	11-Dec-24	Not Started	321
APP-1050	Review & Approve Site Furnishings Shop Drawings	21	05-Nov-24	25-Nov-24	Not Started	321
APP-1060	Review & Approve Photo Submission - Temporary Fence	21	05-Nov-24	25-Nov-24	Not Started	321
SUB-2250	Prepare & Submit Temperature Control System	81	15-Oct-24	11-Feb-25	Not Started	321
SUB-3850	Prepare & Submit Enclosed Switches Product Data	81	15-Oct-24	11-Feb-25	Not Started	321
SUB-3860	Prepare & Submit Enclosed Switches Test Reports	81	15-Oct-24	11-Feb-25	Not Started	321
SUB-1080	Prepare & Submit Door Hardware Submittal	81	15-Oct-24	11-Feb-25	Not Started	323
SUB-1110	Prepare & Submit Roof Drains & Clean Outs	81	15-Oct-24	11-Feb-25	Not Started	323
SUB-1990	Prepare & Submit Metal Plate Wall Panels	81	15-Oct-24	11-Feb-25	Not Started	323
APP-1280	Review & Approve Mechanical Piping	21	11-Jan-25	31-Jan-25	Not Started	324
SUB-3960	Prepare & Submit Sound, Intercome & Security System Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	326
SUB-3970	Prepare & Submit Sound, Intercome & Security System Programming Code and Password for the System	81	15-Oct-24	11-Feb-25	Not Started	326
SUB-3980	Prepare & Submit Sound, Intercome & Security System Warranty	81	15-Oct-24	11-Feb-25	Not Started	326
SUB-4010	Prepare & Submit Self Corrective Clock System Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	326
SUB-4020	Prepare & Submit Self Corrective Clock System Product Data	81	15-Oct-24	11-Feb-25	Not Started	326
SUB-4030	Prepare & Submit Self Corrective Clock System Field Test Reports	81	15-Oct-24	11-Feb-25	Not Started	326
MIL-2922	Start Pre -Cast Concrete Inspection	0	25-Mar-26		Not Started	330
SUB-1930	Prepare & Submit Unit Masonry Product Data	71	15-Oct-24	28-Jan-25	Not Started	331
APP-1080	Review & Approve Electrical Equipment, Conduits, and Cables	21	13-Nov-24	03-Dec-24	Not Started	332
SUB-3790	Prepare & Submit Surge Protective Devices Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	332
SUB-3800	Prepare & Submit Surge Protective Devices Product Data	81	15-Oct-24	11-Feb-25	Not Started	332
SUB-3810	Prepare & Submit Surge Protective Devices Warranty	81	15-Oct-24	11-Feb-25	Not Started	332
SUB-2920	Prepare & Submit Documentation of Proper Disposal	81	15-Oct-24	11-Feb-25	Not Started	333
SUB-3820	Prepare & Submit Service Entrance Equipment Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	333
SUB-3830	Prepare & Submit Service Entrance Equipment Product Data	81	15-Oct-24	11-Feb-25	Not Started	333
SUB-3840	Prepare & Submit Service Entrance Equipment Warranty	81	15-Oct-24	11-Feb-25	Not Started	333
SUB-2000	Prepare & Submit Security Screens & Barriers	81	15-Oct-24	11-Feb-25	Not Started	334
SUB-1070	Prepare & Submit Ceramic Tiles Product Data	81	15-Oct-24	11-Feb-25	Not Started	335
MIL-1660	Start Security Guard Services (30 Days From NTP)	0	30-Oct-24		Not Started	335
SUB-1840	Prepare & Submit Supplemental Comissioning Requirements	81	15-Oct-24	11-Feb-25	Not Started	335
APP-1100	Review & Approve Concrete Reinforcement	21	27-Nov-24	17-Dec-24	Not Started	337
APP-1110	Review & Approve Concrete Shop Drawings	21	27-Nov-24	17-Dec-24	Not Started	337
APP-1140	Review & Approve Concrete Mix Design	21	27-Nov-24	17-Dec-24	Not Started	337
SUB-3580	Prepare & Submit Centrifugal Fans Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	338
SUB-3590	Prepare & Submit Centrifugal Fans Product Data	81	15-Oct-24	11-Feb-25	Not Started	338
SUB-3600	Prepare & Submit Centrifugal Fans Maintenance Data & Materials	81	15-Oct-24	11-Feb-25	Not Started	338
SUB-2180	Prepare & Submit Water Heaters	81	15-Oct-24	11-Feb-25	Not Started	339
APP-3280	Review & Approve Valves Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	340

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
APP-3290	Review & Approve Valves Product Data	21	12-Feb-25	04-Mar-25	Not Started	340
SUB-1310	Prepare & Submit Training Outline & Schedule	81	15-Oct-24	11-Feb-25	Not Started	341
SUB-2230	Prepare & Submit Natural Gas Leak Detection Equipment	81	15-Oct-24	11-Feb-25	Not Started	341
SUB-3540	Prepare & Submit Fan Coils Units Maintenance Data & Materials	81	15-Oct-24	11-Feb-25	Not Started	342
SUB-3550	Prepare & Submit Fan Coils Units Shop Drawings	81	15-Oct-24	11-Feb-25	Not Started	342
SUB-1250	Prepare & Submit Concrete Curbs & Pavements Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	343
SUB-1030	Prepare & Submit Floor Drains	40	15-Oct-24	11-Dec-24	Not Started	344
SUB-3520	Prepare & Submit Convectors Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	344
SUB-3530	Prepare & Submit Convectors Product Data	81	15-Oct-24	11-Feb-25	Not Started	344
SUB-1240	Prepare & Submit Catch Basin Shop Drawings	81	15-Oct-24	11-Feb-25	Not Started	345
APP-1210	Review & Approve Elevator Machine	21	29-Jan-25	18-Feb-25	Not Started	345
APP-3090	Review & Approve Flagpole Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	346
APP-3100	Review & Approve Flagpole Product Data	21	12-Feb-25	04-Mar-25	Not Started	346
APP-1670	Review & Approve Sprinkler System Shop Drawings	21	12-Feb-25	04-Mar-25	Not Started	348
SUB-1890	Prepare & Submit Trench Drains Product Data	81	15-Oct-24	11-Feb-25	Not Started	348
APP-1010	Review & Approve Foundation Product Data	21	22-Oct-24	11-Nov-24	Not Started	350
SUB-3460	Prepare & Submit Breeching Chimney Connectors and Chimneys Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	351
SUB-3470	Prepare & Submit Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	81	15-Oct-24	11-Feb-25	Not Started	351
SUB-3650	Prepare & Submit Damper Assemblies Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	351
SUB-3660	Prepare & Submit Damper Assemblies Product Data	81	15-Oct-24	11-Feb-25	Not Started	351
SUB-3670	Prepare & Submit Damper Assemblies Maintenance Data & Materials	81	15-Oct-24	11-Feb-25	Not Started	351
SUB-3870	Prepare & Submit Motors, Motor Control Centers and Starters Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	351
SUB-3880	Prepare & Submit Motors, Motor Control Centers and Starters Product Data	81	15-Oct-24	11-Feb-25	Not Started	351
SUB-3890	Prepare & Submit Motors, Motor Control Centers and Starters Field Test Reports	81	15-Oct-24	11-Feb-25	Not Started	351
SUB-1270	Prepare & Submit Asphaltic Concrete Paving	81	15-Oct-24	11-Feb-25	Not Started	357
APP-1840	Review & Approve Gymnasium Equipment	21	12-Feb-25	04-Mar-25	Not Started	357
APP-1690	Review & Approve Floorings	21	12-Feb-25	04-Mar-25	Not Started	359
SUB-2210	Prepare & Submit Emergency Generator System Accessories	71	15-Oct-24	28-Jan-25	Not Started	359
APP-1430	Review & Approve Door & Frame Corners Samples	21	12-Feb-25	04-Mar-25	Not Started	362
SUB-2960	Prepare & Submit Coiling Doors, Grilles and Shutters Shop Drawings	81	15-Oct-24	11-Feb-25	Not Started	364
SUB-2970	Prepare & Submit Coiling Doors, Grilles and Shutters Product Data	81	15-Oct-24	11-Feb-25	Not Started	364
SUB-4040	Prepare & Submit Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	81	15-Oct-24	11-Feb-25	Not Started	364
APP-3060	Review & Approve Graffiti Resistant Coating Product Data	21	12-Feb-25	04-Mar-25	Not Started	365
SUB-2190	Prepare & Submit Pumping Apparatus & Tanks	81	15-Oct-24	11-Feb-25	Not Started	366
SUB-1510	Prepare & Submit Millwork	81	15-Oct-24	11-Feb-25	Not Started	369
SUB-3500	Prepare & Submit Coils Maintenance Data	81	15-Oct-24	11-Feb-25	Not Started	369
SUB-3510	Prepare & Submit Coils Certifications	81	15-Oct-24	11-Feb-25	Not Started	369
SUB-3990	Prepare & Submit Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	81	15-Oct-24	11-Feb-25	Not Started	369
SUB-4000	Prepare & Submit Projection and Interactive Whiteboard Systems Wiring diagram	81	15-Oct-24	11-Feb-25	Not Started	369

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
CON-8020	Scheduling With CON-ED For Temporary Electrical Power	7	22-Nov-24	03-Dec-24	Not Started	371
CON-8010	Coordination With CON-ED For Temporary Electrical Power	10	07-Nov-24	21-Nov-24	Not Started	371
SUB-2220	Prepare & Submit Fuel Storage Equipment	81	15-Oct-24	11-Feb-25	Not Started	371
APP-3000	Review & Approve Thresholds, Weatherstripping and Seals Color Samples	21	12-Feb-25	04-Mar-25	Not Started	371
APP-3010	Review & Approve Thresholds, Weatherstripping and Seals Product Data	21	12-Feb-25	04-Mar-25	Not Started	371
APP-3020	Review & Approve Miscellaneous Glazing Samples	21	12-Feb-25	04-Mar-25	Not Started	371
APP-3030	Review & Approve Miscellaneous Glazing Product Data	21	12-Feb-25	04-Mar-25	Not Started	371
APP-3040	Review & Approve Fire Rated Glazing Samples	21	12-Feb-25	04-Mar-25	Not Started	371
APP-3050	Review & Approve Fire Rated Glazing Product Data	21	12-Feb-25	04-Mar-25	Not Started	371
APP-3140	Review & Approve Wire Mesh Work Samples	21	12-Feb-25	04-Mar-25	Not Started	371
APP-3150	Review & Approve Miscellaneous Glazing Shop drawings	21	12-Feb-25	04-Mar-25	Not Started	371
SUB-3560	Prepare & Submit Door Air Curtains Shop Drawing	81	15-Oct-24	11-Feb-25	Not Started	372
SUB-3570	Prepare & Submit Door Air Curtains Product Data	81	15-Oct-24	11-Feb-25	Not Started	372
SUB-2020	Prepare & Submit Visual Display Boards	81	15-Oct-24	11-Feb-25	Not Started	373
SUB-2030	Prepare & Submit Metal Lockers	81	15-Oct-24	11-Feb-25	Not Started	373
SUB-2200	Prepare & Submit HVAC Pumps	81	15-Oct-24	11-Feb-25	Not Started	374
APP-2080	Review & Approve Domestic Equipment	21	12-Feb-25	04-Mar-25	Not Started	375
SUB-1060	Prepare & Submit Interior Signage Shop Drawings	81	15-Oct-24	11-Feb-25	Not Started	377
SUB-1170	Prepare & Submit Certification of Material	81	15-Oct-24	11-Feb-25	Not Started	379
APP-2010	Review & Approve Wood Flooring	21	12-Feb-25	04-Mar-25	Not Started	379
APP-2110	Review & Approve Concrete Floating Floor Assembly	21	12-Feb-25	04-Mar-25	Not Started	379
APP-3930	Review & Approve Fiber Optic Cabling system Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	379
APP-3940	Review & Approve Fiber Optic Cabling system Product Data	21	12-Feb-25	04-Mar-25	Not Started	379
APP-3950	Review & Approve Fiber Optic Cabling system Samples	21	12-Feb-25	04-Mar-25	Not Started	379
APP-1750	Review & Approve Wood Doors	21	12-Feb-25	04-Mar-25	Not Started	382
SUB-1320	Prepare & Submit Product Substitutions	82	15-Oct-24	12-Feb-25	Not Started	384
SUB-2060	Prepare & Submit Library Equipment	81	15-Oct-24	11-Feb-25	Not Started	388
SUB-2100	Prepare & Submit Laboratory Equipment	81	15-Oct-24	11-Feb-25	Not Started	388
APP-1780	Review & Approve Kitchen Equipment	21	29-Jan-25	18-Feb-25	Not Started	389
SUB-1230	Prepare & Submit Ductile Iron Pipes	37	15-Oct-24	06-Dec-24	Not Started	391
APP-1940	Review & Approve Cast Stone Product Data	21	12-Feb-25	04-Mar-25	Not Started	392
SUB-1000	Prepare & Submit Split Heat Pump System - SUB	60	15-Oct-24	10-Jan-25	Not Started	393
APP-1420	Review & Approve Painting	21	12-Feb-25	04-Mar-25	Not Started	393
SUB-2070	Prepare & Submit Platform Curtains & Auditorium Window Curtains	81	15-Oct-24	11-Feb-25	Not Started	393
APP-1790	Review & Approve Signs	21	12-Feb-25	04-Mar-25	Not Started	394
APP-1600	Review & Approve Temporary Ventilation Plan	21	12-Feb-25	04-Mar-25	Not Started	400
APP-1610	Review & Approve Construction Indoor Air Quality Management Plan	21	12-Feb-25	04-Mar-25	Not Started	400
APP-3250	Review & Approve Bleachers Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	402
APP-3260	Review & Approve Bleachers Product Data	21	12-Feb-25	04-Mar-25	Not Started	402
APP-3270	Review & Approve Bleachers Manufacturer's Warranty	21	12-Feb-25	04-Mar-25	Not Started	402
APP-1480	Review & Approve Crystalline Waterproofing Product Data	21	12-Feb-25	04-Mar-25	Not Started	404

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
SUB-1360	Prepare & Submit CWM Plan	81	15-Oct-24	11-Feb-25	Not Started	404
APP-1290	Review & Approve Unit Cabinet Heaters	21	11-Jan-25	31-Jan-25	Not Started	404
APP-2250	Review & Approve Air Outlets & Inlets	21	12-Feb-25	04-Mar-25	Not Started	404
APP-1190	Review & Approve Hangers & Supports	21	12-Dec-24	01-Jan-25	Not Started	405
APP-1270	Review & Approve Acosutical Ceiling Tiles	21	11-Jan-25	31-Jan-25	Not Started	410
APP-1460	Review & Approve Roofing Membrane Product Data	21	12-Feb-25	04-Mar-25	Not Started	412
APP-1450	Review & Approve Flashing & Sheet Metal Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	413
APP-1980	Review & Approve Self Adhering Sheet Air Barriers	21	12-Feb-25	04-Mar-25	Not Started	413
APP-3900	Review & Approve Lightning Protection Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	414
APP-3920	Review & Approve Lightning Protection Test Reports	21	12-Feb-25	04-Mar-25	Not Started	414
APP-1770	Review & Approve Fire Detectors & Alarms	21	12-Feb-25	04-Mar-25	Not Started	418
APP-1870	Review & Approve Environmental Site Assessment Reports	21	12-Feb-25	04-Mar-25	Not Started	422
APP-1120	Review & Approve Lighting Fixtures	21	29-Jan-25	18-Feb-25	Not Started	424
APP-1800	Review & Approve Telecommunication System Drawings	21	12-Feb-25	04-Mar-25	Not Started	428
APP-1220	Review & Approve Internet Protocol Digital Video Surveillance System using Digital Cameras	35	29-Jan-25	04-Mar-25	Not Started	428
APP-3480	Review & Approve Plate Heat Exchanger Maintenance Data	21	12-Feb-25	04-Mar-25	Not Started	428
APP-3490	Review & Approve Plate Heat Exchanger Product Data	21	12-Feb-25	04-Mar-25	Not Started	428
APP-3760	Review & Approve Lighting Control Devices Shop Drawing	21	29-Jan-25	18-Feb-25	Not Started	428
APP-3770	Review & Approve Lighting Control Devices Product Data	21	29-Jan-25	18-Feb-25	Not Started	428
APP-3780	Review & Approve Lighting Control Devices Warranty	21	29-Jan-25	18-Feb-25	Not Started	428
MIL-2912	Start Concrete Cast In Place Inspection	0	28-Oct-25		Not Started	430
APP-1170	Review & Approve Pressure Gages	21	12-Dec-24	01-Jan-25	Not Started	432
APP-2160	Review & Approve Gas Pipes	21	12-Feb-25	04-Mar-25	Not Started	432
APP-1880	Review & Approve Selective Removals & Demoloition	21	12-Feb-25	04-Mar-25	Not Started	434
APP-3390	Review & Approve chedules Showing Manfacturers's Product Number Duct Work Insulation	21	12-Feb-25	04-Mar-25	Not Started	434
APP-1630	Review & Approve Heating Plan	21	12-Feb-25	04-Mar-25	Not Started	436
APP-1830	Review & Approve Boilers	21	29-Jan-25	18-Feb-25	Not Started	442
APP-3440	Review & Approve Detail of Gag for the Safety Relief Valves	21	29-Jan-25	18-Feb-25	Not Started	442
APP-3450	Review & Approve Boiler Accessories Maintenance Data	21	29-Jan-25	18-Feb-25	Not Started	442
APP-2120	Review & Approve Hydraulic Vertical Wheelchair Lifts	21	12-Feb-25	04-Mar-25	Not Started	443
APP-3180	Review & Approve Mirrors Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	443
APP-3190	Review & Approve Mirrors Product Data	21	12-Feb-25	04-Mar-25	Not Started	443
APP-3200	Review & Approve Mirrors Mastic Compatibility Test Reports & Certifications	21	12-Feb-25	04-Mar-25	Not Started	443
PRE-2600	Prepare & Submit Permit Waiver Requests to SCA Chief Project Officer	5	30-Sep-24	04-Oct-24	Not Started	445
CON-7960	Obtain Gas Meter Layout From CON-ED	5	07-Oct-24	11-Oct-24	Not Started	445
APP-1640	Review & Approve Sample Classroom Materials	21	12-Feb-25	04-Mar-25	Not Started	448
APP-1490	Review & Approve Suspension Assembly Shop Drawings	21	12-Feb-25	04-Mar-25	Not Started	449
APP-1380	Review & Approve Fire & Jockey Pumps	21	12-Feb-25	04-Mar-25	Not Started	453
APP-1700	Review & Approve Toilet Accessories	21	12-Feb-25	04-Mar-25	Not Started	453

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
APP-1740	Review & Approve Plumbing Fixtures	21	12-Feb-25	04-Mar-25	Not Started	453
APP-1760	Review & Approve Fire Protection Shop Drawings	21	12-Feb-25	04-Mar-25	Not Started	453
APP-3210	Review & Approve Grab Bars Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	453
APP-3220	Review & Approve Grab Bars Product Data	21	12-Feb-25	04-Mar-25	Not Started	453
APP-2140	Review & Approve Auditorium & Television Studio Dimming System Product Data	21	12-Feb-25	04-Mar-25	Not Started	455
APP-2040	Review & Approve Fire Extinguishers & Cabinets	21	12-Feb-25	04-Mar-25	Not Started	456
APP-1560	Review & Approve Steel Curb Facing Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	460
APP-1530	Review & Approve Playgroung Equipment Shop Drawings	21	12-Feb-25	04-Mar-25	Not Started	464
APP-1910	Review & Approve Outdoor Game Equipment	21	12-Feb-25	04-Mar-25	Not Started	464
APP-2240	Review & Approve Temperature Control System	21	12-Feb-25	04-Mar-25	Not Started	467
APP-3850	Review & Approve Enclosed Switches Product Data	21	12-Feb-25	04-Mar-25	Not Started	468
APP-3860	Review & Approve Enclosed Switches Test Reports	21	12-Feb-25	04-Mar-25	Not Started	468
APP-1160	Review & Approve Thermometers	21	12-Dec-24	01-Jan-25	Not Started	470
APP-1410	Review & Approve Door Hardware Submittal	21	12-Feb-25	04-Mar-25	Not Started	470
APP-1440	Review & Approve Roof Drains & Clean Outs	21	12-Feb-25	04-Mar-25	Not Started	470
APP-1990	Review & Approve Metal Plate Wall Panels	21	12-Feb-25	04-Mar-25	Not Started	470
APP-3960	Review & Approve Sound, Intercome & Security System Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	475
APP-3970	Review & Approve Sound, Intercome & Security System Programming Code and Password for the System	21	12-Feb-25	04-Mar-25	Not Started	475
APP-3980	Review & Approve Sound, Intercome & Security System warranty	21	12-Feb-25	04-Mar-25	Not Started	475
APP-4010	Review & Approve Self Corrective Clock System Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	475
APP-4020	Review & Approve Self Corrective Clock System Product Data	21	12-Feb-25	04-Mar-25	Not Started	475
APP-4030	Review & Approve Self Corrective Clock System Field Test Reports	21	12-Feb-25	04-Mar-25	Not Started	475
APP-1930	Review & Approve Unit Masonry Product Data	21	29-Jan-25	18-Feb-25	Not Started	481
APP-3790	Review & Approve Surge Protective Devices Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	483
APP-3800	Review & Approve Surge Protective Devices Product Data	21	12-Feb-25	04-Mar-25	Not Started	483
APP-3810	Review & Approve Surge Protective Devices Warranty	21	12-Feb-25	04-Mar-25	Not Started	483
APP-2920	Review & Approve Documentation of Proper Disposal	21	12-Feb-25	04-Mar-25	Not Started	484
APP-3820	Review & Approve Service Entrance Equipment Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	484
APP-3830	Review & Approve Service Entrance Equipment Product Data	21	12-Feb-25	04-Mar-25	Not Started	484
APP-3840	Review & Approve Service Entrance Equipment Warranty	21	12-Feb-25	04-Mar-25	Not Started	484
APP-2000	Review & Approve Security Screens & Barriers	21	12-Feb-25	04-Mar-25	Not Started	485
APP-1400	Review & Approve Ceramic Tiles Product Data	21	12-Feb-25	04-Mar-25	Not Started	488
APP-1850	Review & Approve Supplemental Comissioning Requirements	21	12-Feb-25	04-Mar-25	Not Started	488
APP-3580	Review & Approve Centrifugal Fans Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	491
APP-3590	Review & Approve Centrifugal Fans Product Data	21	12-Feb-25	04-Mar-25	Not Started	491
APP-3600	Review & Approve Centrifugal Fans Maintenance Data & Materials	21	12-Feb-25	04-Mar-25	Not Started	491
APP-2170	Review & Approve Water Heaters	21	12-Feb-25	04-Mar-25	Not Started	495
APP-1590	Review & Approve Training Outline & Schedule	21	12-Feb-25	04-Mar-25	Not Started	497

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
APP-2220	Review & Approve Natural Gas Leak Detection Equipment	21	12-Feb-25	04-Mar-25	Not Started	497
APP-3540	Review & Approve Fan Coils Units Maintenance Data & Materials	21	12-Feb-25	04-Mar-25	Not Started	498
APP-3550	Review & Approve Fan Coils Units Shop Drawings	21	12-Feb-25	04-Mar-25	Not Started	498
APP-1550	Review & Approve Concrete Curbs & Pavements Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	499
APP-3520	Review & Approve Convectors Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	502
APP-3530	Review & Approve Convectors Product Data	21	12-Feb-25	04-Mar-25	Not Started	502
APP-1180	Review & Approve Floor Drains	21	12-Dec-24	01-Jan-25	Not Started	503
APP-1540	Review & Approve Catch Basin Shop Drawings	21	12-Feb-25	04-Mar-25	Not Started	503
APP-1890	Review & Approve Trench Drains Prodcut Data	21	12-Feb-25	04-Mar-25	Not Started	509
APP-3460	Review & Approve Breeching Chimney Connectors and Chimneys Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	512
APP-3470	Review & Approve Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys	21	12-Feb-25	04-Mar-25	Not Started	512
APP-3650	Review & Approve Damper Assemblies Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	512
APP-3660	Review & Approve Damper Assemblies Product Data	21	12-Feb-25	04-Mar-25	Not Started	512
APP-3670	Review & Approve Damper Assemblies Maintenance Data & Materials	21	12-Feb-25	04-Mar-25	Not Started	512
APP-3870	Review & Approve Motors, Motor Control Centers and Starters Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	512
APP-3880	Review & Approve Motors, Motor Control Centers and Starters Product Data	21	12-Feb-25	04-Mar-25	Not Started	512
APP-3890	Review & Approve Motors, Motor Control Centers and Starters Field Test Reports	21	12-Feb-25	04-Mar-25	Not Started	512
PRO-1480	Procure & Deliver Chillers	170	30-Sep-25	18-Mar-26	Not Started	515
APP-1570	Review & Approve Asphaltic Concrete Paving	21	12-Feb-25	04-Mar-25	Not Started	520
APP-2200	Review & Approve Emergency Generator System Accessories	21	29-Jan-25	18-Feb-25	Not Started	524
APP-2960	Review & Approve Coiling Doors, Grilles and Shutters Shop Drawings	21	12-Feb-25	04-Mar-25	Not Started	531
APP-2970	Review & Approve Coiling Doors, Grilles and ShuttersProduct Data	21	12-Feb-25	04-Mar-25	Not Started	531
APP-4040	Review & Approve Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings	21	12-Feb-25	04-Mar-25	Not Started	531
APP-2180	Review & Approve Pumping Apparatus & Tanks	21	12-Feb-25	04-Mar-25	Not Started	533
SUB-1410	Prepare & Submit Submittal Schedule	60	15-Oct-24	10-Jan-25	Not Started	534
APP-1710	Review & Approve Millwork	21	12-Feb-25	04-Mar-25	Not Started	538
APP-3500	Review & Approve Coils Maintenance Data	21	12-Feb-25	04-Mar-25	Not Started	538
APP-3510	Review & Approve Coils Certifications	21	12-Feb-25	04-Mar-25	Not Started	538
APP-3990	Review & Approve Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts	21	12-Feb-25	04-Mar-25	Not Started	538
APP-4000	Review & Approve Projection and Interactive Whiteboard Systems Wiring diagram	21	12-Feb-25	04-Mar-25	Not Started	538
APP-2210	Review & Approve Fuel Storage Equipment	21	12-Feb-25	04-Mar-25	Not Started	540
APP-3560	Review & Approve Door Air Curtains Shop Drawing	21	12-Feb-25	04-Mar-25	Not Started	541
APP-3570	Review & Approve Door Air Curtains Product Data	21	12-Feb-25	04-Mar-25	Not Started	541
APP-2020	Review & Approve Visual Display Boards	21	12-Feb-25	04-Mar-25	Not Started	544
APP-2030	Review & Approve Metal Lockers	21	12-Feb-25	04-Mar-25	Not Started	544
APP-2190	Review & Approve HVAC Pumps	21	12-Feb-25	04-Mar-25	Not Started	545
APP-1390	Review & Approve Interior Signage Shop Drawings	21	12-Feb-25	04-Mar-25	Not Started	548
APP-1500	Review & Approve Certification of Material	21	12-Feb-25	04-Mar-25	Not Started	552

Total Float Report

Activity ID	Activity Name	Original Duration	Start	Finish	Activity Status	Total Float
APP-2260	Review & Approve Product Substitutions	21	13-Feb-25	05-Mar-25	Not Started	559
APP-2050	Review & Approve Library Equipment	21	12-Feb-25	04-Mar-25	Not Started	565
APP-2090	Review & Approve Laboratory Equipment	21	12-Feb-25	04-Mar-25	Not Started	565
APP-1150	Review & Approve Ductile Iron Pipes	21	07-Dec-24	27-Dec-24	Not Started	572
APP-2060	Review & Approve Platform Curtains & Auditorium Window Curtains	21	12-Feb-25	04-Mar-25	Not Started	572
APP-1250	Review & Approve Split Heat Pump System - SUB	21	11-Jan-25	31-Jan-25	Not Started	573
APP-1620	Review & Approve CWM Plan	21	12-Feb-25	04-Mar-25	Not Started	588
SUB-2360	Prepare & Submit Adjacent Property and Structures Protection & Monitoring Plan	81	15-Oct-24	11-Feb-25	Not Started	593
APP-1260	Review & Approve Submittal Schedule	21	11-Jan-25	31-Jan-25	Not Started	807
APP-2360	Review & Approve Adjacent Property and Structures Protection & Monitoring Plan	21	12-Feb-25	04-Mar-25	Not Started	894

APPENDIX 14
Schedule Log

Scheduling/Leveling Report - 2025-03-21 16:14:13 - PM.EXE
==========

Default Project.....P026453.BL01
Use scheduling options from.....P026453.BL01

Projects:
P026453.BL01.....New Building PS/IS 341Q - Baseline Schedule Rev 01

Scheduling/Leveling Settings:

General

Scheduling .....Yes
Leveling .....No
Ignore relationships to and from other projects .....No
Make open-ended activities critical .....No
Use Expected Finish Dates .....Yes
Schedule automatically when a change affects dates .....Yes
Level resources during scheduling .....No
Recalculate assignment costs after scheduling .....No
When scheduling progressed activities use .....Retained Logic
Calculate start-to-start lag from .....Early Start
Define critical activities as .....Longest Path
Compute Total Float As .....Finish Float
Calculate float based on finish date of .....Each project
Calendar for scheduling Relationship Lag .....Predecessor Activity Calendar

Advanced

Calculate multiple float paths.....Yes
Calculate multiple float paths using.....Total Float
Number of paths to calculate.....10

Statistics:

Projects.....1
Activities.....1329
Not Started.....1329
In Progress.....0
Completed.....0
Relationships.....3266

```
        # Activities with Constraint.....................................6
                Project:        P026453.BL01    Activity:       MIL-1510        TCO
                Project:        P026453.BL01    Activity:       MIL-1550
Substantial Completion
                Project:        P026453.BL01    Activity:       MIL-1560
Final Completion
                Project:        P026453.BL01    Activity:       MIL-1600        MDF
Work Finish
                Project:        P026453.BL01    Activity:       MIL-1610        IDF
Work Finish
                Project:        P026453.BL01    Activity:       MIL-1620
IPDVS Work Finish

Errors:
-------
Warnings:
---------
        Activities without predecessors.................................1
                Project:        P026453.BL01    Activity:       MIL-1000        NTP

        Activities without successors...................................1
                Project:        P026453.BL01    Activity:       MIL-1560
Final Completion

        Out-of-sequence activities......................................0

        Activities with Actual Dates > Data Date........................0

        Milestone Activities with invalid relationships.................0

        Finish milestone and predecessors have different calendars.......16
                Project:        P026453.BL01    Activity:       CLO-1180
Sprinkler/Domestic Booster Pumps Sign-offs
                Project:        P026453.BL01    Activity:       MIL-1510        TCO
                Project:        P026453.BL01    Activity:       MIL-1510        TCO
                Project:        P026453.BL01    Activity:       MIL-1510        TCO
                Project:        P026453.BL01    Activity:       MIL-1510        TCO
                Project:        P026453.BL01    Activity:       MIL-1550
Substantial Completion
                Project:        P026453.BL01    Activity:       MIL-1560
Final Completion
                Project:        P026453.BL01    Activity:       MIL-1560
Final Completion
                Project:        P026453.BL01    Activity:       MIL-1640
Provide Complete Set of Approved Coordination Drawings
                Project:        P026453.BL01    Activity:       MIL-1640
Provide Complete Set of Approved Coordination Drawings
                Project:        P026453.BL01    Activity:       MIL-1640
Provide Complete Set of Approved Coordination Drawings
                Project:        P026453.BL01    Activity:       MIL-1640
```

Provide Complete Set of Approved Coordination Drawings
Project: P026453.BL01 Activity: MIL-1640
Provide Complete Set of Approved Coordination Drawings
Project: P026453.BL01 Activity: MIL-1640
Provide Complete Set of Approved Coordination Drawings
Project: P026453.BL01 Activity: MIL-2622
Deliveries of all owner-furnished equipment and/or materials
Project: P026453.BL01 Activity: MIL-2762
Green Schools Compliance Submission

Scheduling/Leveling Results:

Projects Scheduled/Leveled.....1
Activities Scheduled/Leveled.....1329
Relationships with other projects.....1
Data Date.....30-Sep-24
Earliest Early Start Date.....30-Sep-24
Latest Early Finish Date.....15-Aug-27
Number of float paths.....10
Exceptions:

Critical Activities.....163
Project: P026453.BL01 Activity: CLO-1030
Pre-Final Clean-Out
Project: P026453.BL01 Activity: CLO-1040
Pre-TCO Inspection
Project: P026453.BL01 Activity: CLO-1050
Pre-Substantial Punchlist
Project: P026453.BL01 Activity: CLO-1060
Prepare & Submit O&M Manuals
Project: P026453.BL01 Activity: CLO-1070
Prepare & Submit As-Built Drawings
Project: P026453.BL01 Activity: CLO-1080
Final Inspection
Project: P026453.BL01 Activity: CLO-1090
Final Clean Out
Project: P026453.BL01 Activity: CLO-1100
Demobilization
Project: P026453.BL01 Activity: CLO-1110
Pre-TCO Punchlist
Project: P026453.BL01 Activity: CON-1000
Mobilization
Project: P026453.BL01 Activity: CON-1020
Install 60 Dry MILS Liquid Boot -1st Floor
Project: P026453.BL01 Activity: CON-1040
F/R/P Concrete Walls & Beams -1st Floor
Project: P026453.BL01 Activity: CON-1050
Install Underground Conduits & Wires -1st Floor
Project: P026453.BL01 Activity: CON-1060
Backfilling & Compaction -1st Floor

Project: P026453.BL01 Activity: CON-1070
F/R/P SOG -1st Floor
Project: P026453.BL01 Activity: CON-1100
Install Framing Beams -1st Floor
Project: P026453.BL01 Activity: CON-1110
Install Metal Deck Slab -2nd Floor
Project: P026453.BL01 Activity: CON-1170
Install Steel Columns -2nd Floor
Project: P026453.BL01 Activity: CON-1200
Install Framing Beams -2nd Floor
Project: P026453.BL01 Activity: CON-1210
Install Metal Deck Slab - 3rd Floor
Project: P026453.BL01 Activity: CON-1240
Install Steel Columns - 3rd Floor
Project: P026453.BL01 Activity: CON-1270
Install Framing Beams - 3rd Floor
Project: P026453.BL01 Activity: CON-1290
Install Metal Deck Slab - 4th Floor
Project: P026453.BL01 Activity: CON-1330
Install Steel Columns - 4th Floor
Project: P026453.BL01 Activity: CON-1370
Install Framing Beams - 4th Floor
Project: P026453.BL01 Activity: CON-1380
Install Metal Deck Slab - 5th Floor
Project: P026453.BL01 Activity: CON-1440
Install Steel Columns - 5th Floor
Project: P026453.BL01 Activity: CON-1550
Install Framing Beams - 5th Floor
Project: P026453.BL01 Activity: CON-1720
Install Metal Deck Slab -Roof Floor
Project: P026453.BL01 Activity: CON-1830
Install Insulated Precast Concrete Sandwich Panel - Mock Up
Project: P026453.BL01 Activity: CON-1990
Approve Insulated Precast Concrete Sandwich Panel - Mock Up
Project: P026453.BL01 Activity: CON-2110
Install & Windows Mock-Up
Project: P026453.BL01 Activity: CON-2210
Approve Windows Mock-Up
Project: P026453.BL01 Activity: CON-2220
Install Storefront System Mock-Up
Project: P026453.BL01 Activity: CON-2240
Approve Storefront System Mock-Up
Project: P026453.BL01 Activity: CON-2380
Install Insulated Precast Concrete Sandwich Panel - West Elevation
Project: P026453.BL01 Activity: CON-2420
Install Insulated Precast Concrete Sandwich Panel - South Elevation
Project: P026453.BL01 Activity: CON-2590
Install Windows - South Elevation
Project: P026453.BL01 Activity: CON-2600
Install Storefront System- South Elevation

Project: P026453.BL01 Activity: CON-2610
Install Insulated Precast Concrete Sandwich Panel - East Elevation
Project: P026453.BL01 Activity: CON-2730
Install Insulated Precast Concrete Sandwich Panel - North Elevation
Project: P026453.BL01 Activity: CON-2920 Pour
Sloped Concrete Fill -5th Floor Roof
Project: P026453.BL01 Activity: CON-2980
Install Windows - East Elevation
Project: P026453.BL01 Activity: CON-2990
Install Storefront System- East Elevation
Project: P026453.BL01 Activity: CON-3010 Pour
Sloped Concrete Fill -Roof Floor
Project: P026453.BL01 Activity: CON-3210
Install Fluid-Applied Protected Membrane Mock-Up
Project: P026453.BL01 Activity: CON-3220
Dismantle Sidewalk Sheds- South Elevation
Project: P026453.BL01 Activity: CON-3300
Approve Fluid-Applied Protected Membrane Mock-Up
Project: P026453.BL01 Activity: CON-3370
Field Testing of Windows (90%)
Project: P026453.BL01 Activity: CON-3430
Install Hot Fluid Applied Membrane -Roof Floor
Project: P026453.BL01 Activity: CON-3440
Install Hot Fluid Applied Membrane -5th Floor Roof
Project: P026453.BL01 Activity: CON-3580
Install 6" Thick Rigid Insulation -5th Floor Roof
Project: P026453.BL01 Activity: CON-3600
Install Drainage Panels- Roof Floor
Project: P026453.BL01 Activity: CON-3630
Dismantle Sidewalk Sheds- East Elevation
Project: P026453.BL01 Activity: CON-3710 Roof
Flood Test -5th Floor Roof
Project: P026453.BL01 Activity: CON-3730
Install 6" Thick Rigid Insulation -Roof Floor
Project: P026453.BL01 Activity: CON-3780
Install Traffic Control Devices - 54th Avenue Street
Project: P026453.BL01 Activity: CON-3840 Roof
Flood Test -Roof Floor
Project: P026453.BL01 Activity: CON-3870
Install Traffic Control Devices - 2nd Street
Project: P026453.BL01 Activity: CON-3900
Remove Existing Sidewalk - 2nd Street
Project: P026453.BL01 Activity: CON-3950
Install Pedestrian Ramps With Truncated Domes - 2nd Street
Project: P026453.BL01 Activity: CON-4030
Install Gypsum Board Walls-2nd Floor
Project: P026453.BL01 Activity: CON-4040
Install Walls GWB-Mockup Room
Project: P026453.BL01 Activity: CON-4090
Remove Existing Steel Faced Curb - 2nd Street

Project: P026453.BL01 Activity: CON-4160
Install New Steel Faced Curb - 2nd Street
Project: P026453.BL01 Activity: CON-4260
Install Door Frames-Mockup Room
Project: P026453.BL01 Activity: CON-4310
Install 7'' Concrete Sidewalk - 2nd Street
Project: P026453.BL01 Activity: CON-4370
Install Gypsum Board Ceiling -2nd Floor
Project: P026453.BL01 Activity: CON-4380
Install Doors & Hardware-Mockup Room
Project: P026453.BL01 Activity: CON-4420
Remove Traffic Control Devices - 2nd Street
Project: P026453.BL01 Activity: CON-4480
Paint First coat -Mockup Room
Project: P026453.BL01 Activity: CON-4630
Install Gypsum Board Ceiling-3rd Floor
Project: P026453.BL01 Activity: CON-4640
Flooring Finishes-Mockup Room
Project: P026453.BL01 Activity: CON-4660
Excavation - Drainage Work - Building Perimeter
Project: P026453.BL01 Activity: CON-4740
Install Flood Barrier Wall - Drainage Work - Building Perimeter
Project: P026453.BL01 Activity: CON-4750
Paint Second coat-Mockup Room
Project: P026453.BL01 Activity: CON-4830
Install First Coat Painting-2nd Floor
Project: P026453.BL01 Activity: CON-4860
Install Drilled Caisson Supported Ventilation Structure - Drainage Work - Building Perimeter
Project: P026453.BL01 Activity: CON-4930
Install Furniture & Signs -Mockup Room
Project: P026453.BL01 Activity: CON-4980
Install 4'' & 6'' & 10'' & 12'' DIP - Drainage Work - Building Perimeter
Project: P026453.BL01 Activity: CON-5110
Install First Coat Painting-3rd Floor
Project: P026453.BL01 Activity: CON-5120
Install Door Frames & Doors-2nd Floor
Project: P026453.BL01 Activity: CON-5190
Install Catch Basin - Drainage Work - Building Perimeter
Project: P026453.BL01 Activity: CON-5290
Install Storm Inlet With Hood & Storm Hood - Drainage Work - Building Perimeter
Project: P026453.BL01 Activity: CON-5350
Install Door Frames & Doors-3rd Floor
Project: P026453.BL01 Activity: CON-5360
Install Flooring Tiles-2nd Floor
Project: P026453.BL01 Activity: CON-5400
Install Trench Drain - Drainage Work - Building Perimeter
Project: P026453.BL01 Activity: CON-5470
Install Flush Concrete Curb - Playground Area & Fences - Building Perimeter
Project: P026453.BL01 Activity: CON-5520

Install Acoustical Ceiling Tiles-4th Floor
Project: P026453.BL01 Activity: CON-5550
Install Flooring Tiles-3rd Floor
Project: P026453.BL01 Activity: CON-5560
Install Final Coat Painting-2nd Floor
Project: P026453.BL01 Activity: CON-5600
Install Concrete Pavement Pedestrian Ramp With Painted Black Handrails - Playground Area & Fences - Building Perimeter
Project: P026453.BL01 Activity: CON-5650
Install Playground Rubber Tile Safety Surface - Playground Area & Fences - Building Perimeter
Project: P026453.BL01 Activity: CON-5670
Install Acoustical Ceiling Tiles-5th Floor
Project: P026453.BL01 Activity: CON-5700
Install Final Coat Painting-3rd Floor
Project: P026453.BL01 Activity: CON-5800
Install Painted Asphalt Pavement & Painted Games On Asphalt Surface - Playground Area & Fences - Building Perimeter
Project: P026453.BL01 Activity: CON-5850
Install Colored Athletic Wearing Surface Color - Playground Area & Fences - Building Perimeter
Project: P026453.BL01 Activity: CON-5900
Install Final Coat Painting-4th Floor
Project: P026453.BL01 Activity: CON-5990
Install Playground Equipment - Playground Area & Fences - Building Perimeter
Project: P026453.BL01 Activity: CON-6060
Install Final Coat Painting -5th Floor
Project: P026453.BL01 Activity: CON-6140
Install Basketball Hoop - Playground Area & Fences - Building Perimeter
Project: P026453.BL01 Activity: CON-6170
Install Final Coat Painting-1st Floor
Project: P026453.BL01 Activity: CON-6190
Install Wrought Iron Fence Double Gate - Playground Area - Building Perimeter
Project: P026453.BL01 Activity: CON-6270
Install Chain Link Fence - Playground Area & Fences - Building Perimeter
Project: P026453.BL01 Activity: CON-6300
Install Furniture & Milling Work (Contractor Provided & Installed) -1st Floor
Project: P026453.BL01 Activity: CON-6320
Install Cafeteria Equipment-1st Floor
Project: P026453.BL01 Activity: CON-6370
Install Signages-1st Floor
Project: P026453.BL01 Activity: CON-9120 Soli Sampling
Project: P026453.BL01 Activity: CON-9140 Excavation
Project: P026453.BL01 Activity: CON-9160
Excavate for Footings - Playground Area & Fences - Building Perimeter
Project: P026453.BL01 Activity: CON-9170
Install 8" Combined Water Service (2nd Street)- Drainage Work - Building Perimeter
Project: P026453.BL01 Activity: CON-9180

Install 6" Fire Water Service (54th Avenue Street)- Drainage Work - Building Perimeter
Project: P026453.BL01 Activity: CON-9190
F/R/P Playground Equipment Footings - Playground Area & Fences - Building Perimeter
Project: P026453.BL01 Activity: CON-9777
Install Liquid Ultrashield G-1000 -1st Floor
Project: P026453.BL01 Activity: CON-98787
Install Steel Columns -1st Floor
Project: P026453.BL01 Activity: CON-9888
Install Liquid Boot VI-20 Geomembrane -1st Floor
Project: P026453.BL01 Activity: CON-98947
Install 4" slotted schedule 80 PVC Piping -1st Floor
Project: P026453.BL01 Activity: CON-9898
Install Gas Permeable Aggregate -1st Floor
Project: P026453.BL01 Activity: CON-99237
Install Flag Pole - South Elevation
Project: P026453.BL01 Activity: MIL-1000 NTP
Project: P026453.BL01 Activity: MIL-1060
Mobilization Start
Project: P026453.BL01 Activity: MIL-1120
Metal Decking Start
Project: P026453.BL01 Activity: MIL-1200 Main
Roofing Start
Project: P026453.BL01 Activity: MIL-1230 5th
Floor Roofing Start
Project: P026453.BL01 Activity: MIL-1340 BLDG
Tight
Project: P026453.BL01 Activity: MIL-1360
Start Mockup Room Work
Project: P026453.BL01 Activity: MIL-1420
Finish Mockup Room
Project: P026453.BL01 Activity: MIL-1430
Start Architecture Finishes
Project: P026453.BL01 Activity: MIL-1440
Start Gypsum Board
Project: P026453.BL01 Activity: MIL-1470
Finish Site Work
Project: P026453.BL01 Activity: MIL-1510 TCO
Project: P026453.BL01 Activity: MIL-1550
Substantial Completion
Project: P026453.BL01 Activity: MIL-1560
Final Completion
Project: P026453.BL01 Activity: MIL-1710
Complete Mobilization
Project: P026453.BL01 Activity: MIL-1730
Sidewalk Sheds Dismantle Complete
Project: P026453.BL01 Activity: MIL-1810
Crane Mobilization-Steel Installation start
Project: P026453.BL01 Activity: MIL-1830
Crane Mobilization-Precast Sandwich Panels Installation Start

Project: P026453.BL01 Activity: MIL-1840
Crane Mobilization-Precast Sandwich Panels Installation Finish
Project: P026453.BL01 Activity: MIL-1850
Construction Start
Project: P026453.BL01 Activity: MIL-2522 Site
Access
Project: P026453.BL01 Activity: MIL-2532
Submit Complete Permit Application
Project: P026453.BL01 Activity: MIL-2582
Start Concrete Placement
Project: P026453.BL01 Activity: MIL-2672
Finish Painting
Project: P026453.BL01 Activity: MIL-2702
Finish Concrete Work
Project: P026453.BL01 Activity: MIL-2812
Start Foundation
Project: P026453.BL01 Activity: MIL-2842
Issuance of Builders Pavement Permit
Project: P026453.BL01 Activity: MIL-2852
Issuance of Permit to Enter (PTE)
Project: P026453.BL01 Activity: MIL-2862
Issuance of NYPA Permit
Project: P026453.BL01 Activity: MIL-2872
Issuance of Construction Fences Permit
Project: P026453.BL01 Activity: MIL-2882
Issuance of Sidewalk Shed Permits
Project: P026453.BL01 Activity: MIL-2892
Issuance of CCD1
Project: P026453.BL01 Activity: MIL-2902
Issuance of DOB Permit & Insurance
Project: P026453.BL01 Activity: MIL-2912
Start Concrete Cast In Place Inspection
Project: P026453.BL01 Activity: MIL-2922
Start Pre -Cast Concrete Inspection
Project: P026453.BL01 Activity: PRE-1460
Obtain Construction Fences Permit
Project: P026453.BL01 Activity: PRE-1660 DOB
Permit & Insurance
Project: P026453.BL01 Activity: PRE-2540 SCA
Work Notification
Project: P026453.BL01 Activity: PRE-2550
Obtain CCD1
Project: P026453.BL01 Activity: PRE-2570
Obtain Sidewalk Shed Permits
Project: P026453.BL01 Activity: PRE-2630
Obtain Builders Pavement Permit
Project: P026453.BL01 Activity: PRE-2640
Obtain Excavation & Shoring Permit
Project: P026453.BL01 Activity: PRE-2650
Obtain Permit to Enter (PTE) Amtrak

Project: P026453.BL01 Activity: PRE-2660 Obtain NYPA Permit

Activities with unsatisfied constraints.....0

Activities with unsatisfied relationships.....0

Activities with external dates.....0

Activities that are not on any float paths.....1178

Project: P026453.BL01 Activity: APP-1000 Review & Approve Site Safety Plan

Project: P026453.BL01 Activity: APP-1010 Review & Approve Foundation Product Data

Project: P026453.BL01 Activity: APP-1020 Review & Approve Erosion Control and Sedimentation Plan

Project: P026453.BL01 Activity: APP-1030 Review & Approve Existing Conditions Survey

Project: P026453.BL01 Activity: APP-1040 Review & Approve Sustainable Materials

Project: P026453.BL01 Activity: APP-1050 Review & Approve Site Furnishings Shop Drawings

Project: P026453.BL01 Activity: APP-1060 Review & Approve Photo Submission - Temporary Fence

Project: P026453.BL01 Activity: APP-1070 Review & Approve Emergency Generator System Product Data

Project: P026453.BL01 Activity: APP-1080 Review & Approve Electrical Equipment, Conduits, and Cables

Project: P026453.BL01 Activity: APP-1090 Review & Approve Switch Gears Product Data

Project: P026453.BL01 Activity: APP-1100 Review & Approve Concrete Reinforcement

Project: P026453.BL01 Activity: APP-1110 Review & Approve Concrete Shop Drawings

Project: P026453.BL01 Activity: APP-1120 Review & Approve Lighting Fixtures

Project: P026453.BL01 Activity: APP-1130 Review & Approve QCP

Project: P026453.BL01 Activity: APP-1140 Review & Approve Concrete Mix Design

Project: P026453.BL01 Activity: APP-1150 Review & Approve Ductile Iron Pipes

Project: P026453.BL01 Activity: APP-1160 Review & Approve Thermometers

Project: P026453.BL01 Activity: APP-1170 Review & Approve Pressure Gages

Project: P026453.BL01 Activity: APP-1180 Review & Approve Floor Drains

Project: P026453.BL01 Activity: APP-1190 Review & Approve Hangers & Supports

Project: P026453.BL01 Activity: APP-1200
Review & Approve SSDS Geotextile
Project: P026453.BL01 Activity: APP-1210
Review & Approve Elevator Machine
Project: P026453.BL01 Activity: APP-1220
Review & Approve Internet Protocol Digital Video Surveillance System using Digital Cameras
Project: P026453.BL01 Activity: APP-1230
Review & Approve Initial Underground Coordination Drawings
Project: P026453.BL01 Activity: APP-1240
Review & Approve Baseline Schedule
Project: P026453.BL01 Activity: APP-1250
Review & Approve Split Heat Pump System - SUB
Project: P026453.BL01 Activity: APP-1260
Review & Approve Submittal Schedule
Project: P026453.BL01 Activity: APP-1270
Review & Approve Acosutical Ceiling Tiles
Project: P026453.BL01 Activity: APP-1280
Review & Approve Mechanical Piping
Project: P026453.BL01 Activity: APP-1290
Review & Approve Unit Cabinet Heaters
Project: P026453.BL01 Activity: APP-1300
Review & Approve Air Handling Units Product Data
Project: P026453.BL01 Activity: APP-1310
Review & Approve Aluminum Projected Windows
Project: P026453.BL01 Activity: APP-1320
Review & Approve Stationary Metal Wall Louvers
Project: P026453.BL01 Activity: APP-1330
Review & Approve Initial 1st Floor Coordination Drawings
Project: P026453.BL01 Activity: APP-1340
Review & Approve Initial 2nd Floor Coordination Drawings
Project: P026453.BL01 Activity: APP-1350
Review & Approve Initial 3rd Floor Coordination Drawings
Project: P026453.BL01 Activity: APP-1360
Review & Approve Initial 4th Floor Coordination Drawings
Project: P026453.BL01 Activity: APP-1370
Review & Approve Initial 5th Floor Coordination Drawings
Project: P026453.BL01 Activity: APP-1380
Review & Approve Fire & Jockey Pumps
Project: P026453.BL01 Activity: APP-1390
Review & Approve Interior Signage Shop Drawings
Project: P026453.BL01 Activity: APP-1400
Review & Approve Ceramic Tiles Product Data
Project: P026453.BL01 Activity: APP-1410
Review & Approve Door Hardware Submittal
Project: P026453.BL01 Activity: APP-1420
Review & Approve Painting
Project: P026453.BL01 Activity: APP-1430
Review & Approve Door & Frame Corners Samples
Project: P026453.BL01 Activity: APP-1440

Review & Approve Roof Drains & Clean Outs
Project: P026453.BL01 Activity: APP-1450
Review & Approve Flashing & Sheet Metal Shop Drawing
Project: P026453.BL01 Activity: APP-1460
Review & Approve Roofing Membrane Product Data
Project: P026453.BL01 Activity: APP-1470
Review & Approve Perimeter Foundation Insulation Product Data
Project: P026453.BL01 Activity: APP-1480
Review & Approve Crystalline Waterproofing Product Data
Project: P026453.BL01 Activity: APP-1490
Review & Approve Suspension Assembly Shop Drawings
Project: P026453.BL01 Activity: APP-1500
Review & Approve Certification of Material
Project: P026453.BL01 Activity: APP-1510
Review & Approve Formwork Shop Drawings
Project: P026453.BL01 Activity: APP-1520
Review & Approve Planting Schedule
Project: P026453.BL01 Activity: APP-1530
Review & Approve Playgroung Equipment Shop Drawings
Project: P026453.BL01 Activity: APP-1540
Review & Approve Catch Basin Shop Drawings
Project: P026453.BL01 Activity: APP-1550
Review & Approve Concrete Curbs & Pavements Shop Drawing
Project: P026453.BL01 Activity: APP-1560
Review & Approve Steel Curb Facing Shop Drawing
Project: P026453.BL01 Activity: APP-1570
Review & Approve Asphaltic Concrete Paving
Project: P026453.BL01 Activity: APP-1580
Review & Approve Gas Vapor Barrier Submittal & Inspection Schedule
Project: P026453.BL01 Activity: APP-1590
Review & Approve Training Outline & Schedule
Project: P026453.BL01 Activity: APP-1600
Review & Approve Temporary Ventilation Plan
Project: P026453.BL01 Activity: APP-1610
Review & Approve Construction Indoor Air Quality Management Plan
Project: P026453.BL01 Activity: APP-1620
Review & Approve CWM Plan
Project: P026453.BL01 Activity: APP-1630
Review & Approve Heating Plan
Project: P026453.BL01 Activity: APP-1640
Review & Approve Sample Classroom Materials
Project: P026453.BL01 Activity: APP-1650
Review & Approve Electrical Shop Drawings
Project: P026453.BL01 Activity: APP-1660
Review & Approve Plumbing Shop Drawings
Project: P026453.BL01 Activity: APP-1670
Review & Approve Sprinkler System Shop Drawings
Project: P026453.BL01 Activity: APP-1680
Review & Approve Gypsum Board
Project: P026453.BL01 Activity: APP-1690

Review & Approve Floorings
Project: P026453.BL01 Activity: APP-1700
Review & Approve Toilet Accessories
Project: P026453.BL01 Activity: APP-1710
Review & Approve Millwork
Project: P026453.BL01 Activity: APP-1720
Review & Approve Furniture
Project: P026453.BL01 Activity: APP-1730
Review & Approve Mechanical Ducts
Project: P026453.BL01 Activity: APP-1740
Review & Approve Plumbing Fixtures
Project: P026453.BL01 Activity: APP-1750
Review & Approve Wood Doors
Project: P026453.BL01 Activity: APP-1760
Review & Approve Fire Protection Shop Drawings
Project: P026453.BL01 Activity: APP-1770
Review & Approve Fire Detectors & Alarms
Project: P026453.BL01 Activity: APP-1780
Review & Approve Kitchen Equipment
Project: P026453.BL01 Activity: APP-1790
Review & Approve Signs
Project: P026453.BL01 Activity: APP-1800
Review & Approve Telecommunication System Drawings
Project: P026453.BL01 Activity: APP-1810
Review & Approve Roof Dunnage
Project: P026453.BL01 Activity: APP-1820
Review & Approve Chillers Product Data
Project: P026453.BL01 Activity: APP-1830
Review & Approve Boilers
Project: P026453.BL01 Activity: APP-1840
Review & Approve Gymnasium Equipment
Project: P026453.BL01 Activity: APP-1850
Review & Approve Supplemental Comissioning Requirements
Project: P026453.BL01 Activity: APP-1860
Review & Approve Record Documents
Project: P026453.BL01 Activity: APP-1870
Review & Approve Environmental Site Assessment Reports
Project: P026453.BL01 Activity: APP-1880
Review & Approve Selective Removals & Demoloition
Project: P026453.BL01 Activity: APP-1890
Review & Approve Trench Drains Prodcut Data
Project: P026453.BL01 Activity: APP-1900
Review & Approve Chain Link Fences & Gates Drawings
Project: P026453.BL01 Activity: APP-1910
Review & Approve Outdoor Game Equipment
Project: P026453.BL01 Activity: APP-1920
Review & Approve Precast Architectural Concrete
Project: P026453.BL01 Activity: APP-1930
Review & Approve Unit Masonry Product Data
Project: P026453.BL01 Activity: APP-1940

Review & Approve Cast Stone Product Data
Project: P026453.BL01 Activity: APP-1950
Review & Approve Structure Steel Drawings
Project: P026453.BL01 Activity: APP-1960
Review & Approve Metal Deck Product Data
Project: P026453.BL01 Activity: APP-1970
Review & Approve Prefabricated Expansion Joint Covers
Project: P026453.BL01 Activity: APP-1980
Review & Approve Self Adhering Sheet Air Barriers
Project: P026453.BL01 Activity: APP-1990
Review & Approve Metal Plate Wall Panels
Project: P026453.BL01 Activity: APP-2000
Review & Approve Security Screens & Barriers
Project: P026453.BL01 Activity: APP-2010
Review & Approve Wood Flooring
Project: P026453.BL01 Activity: APP-2020
Review & Approve Visual Display Boards
Project: P026453.BL01 Activity: APP-2030
Review & Approve Metal Lockers
Project: P026453.BL01 Activity: APP-2040
Review & Approve Fire Extinguishers & Cabinets
Project: P026453.BL01 Activity: APP-2050
Review & Approve Library Equipment
Project: P026453.BL01 Activity: APP-2060
Review & Approve Platform Curtains & Auditorium Window Curtains
Project: P026453.BL01 Activity: APP-2070
Review & Approve Waste Handling Equipment
Project: P026453.BL01 Activity: APP-2080
Review & Approve Domestic Equipment
Project: P026453.BL01 Activity: APP-2090
Review & Approve Laboratory Equipment
Project: P026453.BL01 Activity: APP-2100
Review & Approve Manufactured Wood Casework
Project: P026453.BL01 Activity: APP-2110
Review & Approve Concrete Floating Floor Assembly
Project: P026453.BL01 Activity: APP-2120
Review & Approve Hydraulic Vertical Wheelchair Lifts
Project: P026453.BL01 Activity: APP-2130
Review & Approve Switch & Panel Boards
Project: P026453.BL01 Activity: APP-2140
Review & Approve Auditorium & Television Studio Dimming System Product Data
Project: P026453.BL01 Activity: APP-2150
Review & Approve Overcurrent Protective Devices Data
Project: P026453.BL01 Activity: APP-2160
Review & Approve Gas Pipes
Project: P026453.BL01 Activity: APP-2170
Review & Approve Water Heaters
Project: P026453.BL01 Activity: APP-2180
Review & Approve Pumping Apparatus & Tanks
Project: P026453.BL01 Activity: APP-2190

Review & Approve HVAC Pumps
Project: P026453.BL01 Activity: APP-2200
Review & Approve Emergency Generator System Accessories
Project: P026453.BL01 Activity: APP-2210
Review & Approve Fuel Storage Equipment
Project: P026453.BL01 Activity: APP-2220
Review & Approve Natural Gas Leak Detection Equipment
Project: P026453.BL01 Activity: APP-2240
Review & Approve Temperature Control System
Project: P026453.BL01 Activity: APP-2250
Review & Approve Air Outlets & Inlets
Project: P026453.BL01 Activity: APP-2260
Review & Approve Product Substitutions
Project: P026453.BL01 Activity: APP-2270
Review & Approve Final Foundations Coordination Drawings
Project: P026453.BL01 Activity: APP-2280
Review & Approve Final 1st Floor Coordination Drawings
Project: P026453.BL01 Activity: APP-2290
Review & Approve Final 2nd Floor Coordination Drawings
Project: P026453.BL01 Activity: APP-2300
Review & Approve Final 3rd Floor Coordination Drawings
Project: P026453.BL01 Activity: APP-2310
Review & Approve Final 4th Floor Coordination Drawings
Project: P026453.BL01 Activity: APP-2320
Review & Approve Final 5th Floor Coordination Drawings
Project: P026453.BL01 Activity: APP-2330
Review & Approve Remedial Closure Report
Project: P026453.BL01 Activity: APP-2340
Review & Approve Tree Protection Plan
Project: P026453.BL01 Activity: APP-2360
Review & Approve Adjacent Property and Structures Protection & Monitoring Plan
Project: P026453.BL01 Activity: APP-2370
Review & Approve Ornamenta Metal Shop Drawings
Project: P026453.BL01 Activity: APP-2900
Review & Approve Excavated Material Disposal Plan
Project: P026453.BL01 Activity: APP-2910
Review & Approve Backfill & Resue Plan
Project: P026453.BL01 Activity: APP-2920
Review & Approve Documentation of Proper Disposal
Project: P026453.BL01 Activity: APP-2930
Review & Approve Ornamenta Metal Product Data
Project: P026453.BL01 Activity: APP-2960
Review & Approve Coiling Doors, Grilles and Shutters Shop Drawings
Project: P026453.BL01 Activity: APP-2970
Review & Approve Coiling Doors, Grilles and ShuttersProduct Data
Project: P026453.BL01 Activity: APP-2980
Review & Approve Aluminum Framed Entrances & Storefronts Shop Drawings
Project: P026453.BL01 Activity: APP-2990
Review & Approve Aluminum Framed Entrances & Storefronts Product Data
Project: P026453.BL01 Activity: APP-3000

Review & Approve Thresholds, Weatherstripping and Seals Color Samples
Project: P026453.BL01 Activity: APP-3010
Review & Approve Thresholds, Weatherstripping and Seals Product Data
Project: P026453.BL01 Activity: APP-3020
Review & Approve Miscellaneous Glazing Samples
Project: P026453.BL01 Activity: APP-3030
Review & Approve Miscellaneous Glazing Product Data
Project: P026453.BL01 Activity: APP-3040
Review & Approve Fire Rated Glazing Samples
Project: P026453.BL01 Activity: APP-3050
Review & Approve Fire Rated Glazing Product Data
Project: P026453.BL01 Activity: APP-3060
Review & Approve Graffiti Resistant Coating Product Data
Project: P026453.BL01 Activity: APP-3070
Review & Approve Special Coating Samples
Project: P026453.BL01 Activity: APP-3080
Review & Approve Special Coating Product Data
Project: P026453.BL01 Activity: APP-3090
Review & Approve Flagpole Shop Drawing
Project: P026453.BL01 Activity: APP-3100
Review & Approve Flagpole Product Data
Project: P026453.BL01 Activity: APP-3110
Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals
Project: P026453.BL01 Activity: APP-3120
Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings
Project: P026453.BL01 Activity: APP-3130
Review & Approve Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples
Project: P026453.BL01 Activity: APP-3140
Review & Approve Wire Mesh Work Samples
Project: P026453.BL01 Activity: APP-3150
Review & Approve Miscellaneous Glazing Shop drawings
Project: P026453.BL01 Activity: APP-3160
Review & Approve Metal Storage Shelving Samples
Project: P026453.BL01 Activity: APP-3170
Review & Approve Metal Storage Shelving Shop drawings
Project: P026453.BL01 Activity: APP-3180
Review & Approve Mirrors Shop Drawing
Project: P026453.BL01 Activity: APP-3190
Review & Approve Mirrors Product Data
Project: P026453.BL01 Activity: APP-3200
Review & Approve Mirrors Mastic Compatibility Test Reports & Certifications
Project: P026453.BL01 Activity: APP-3210
Review & Approve Grab Bars Shop Drawing
Project: P026453.BL01 Activity: APP-3220
Review & Approve Grab Bars Product Data
Project: P026453.BL01 Activity: APP-3230
Review & Approve Shop Equipment Shop Drawing

Project: P026453.BL01 Activity: APP-3240
Review & Approve Shop Equipment Product Data
Project: P026453.BL01 Activity: APP-3250
Review & Approve Bleachers Shop Drawing
Project: P026453.BL01 Activity: APP-3260
Review & Approve Bleachers Product Data
Project: P026453.BL01 Activity: APP-3270
Review & Approve Bleachers Manufacturer's Warranty
Project: P026453.BL01 Activity: APP-3280
Review & Approve Valves Shop Drawing
Project: P026453.BL01 Activity: APP-3290
Review & Approve Valves Product Data
Project: P026453.BL01 Activity: APP-3300
Review & Approve Certification of Tests
Project: P026453.BL01 Activity: APP-3310
Review & Approve Domestic Water Sterilization Plan
Project: P026453.BL01 Activity: APP-3320
Review & Approve Tags, Charts & Identifications Shop Drawing
Project: P026453.BL01 Activity: APP-3330
Review & Approve Tags, Charts & Identifications Product Data
Project: P026453.BL01 Activity: APP-3340
Review & Approve Micselianeous Shop Drawing
Project: P026453.BL01 Activity: APP-3350
Review & Approve Valves (HVAC) Shop Drawing
Project: P026453.BL01 Activity: APP-3360
Review & Approve Valves (HVAC) Product Data
Project: P026453.BL01 Activity: APP-3370
Review & Approve Piping Insulation Schedule Listing Items
Project: P026453.BL01 Activity: APP-3380
Review & Approve chedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)
Project: P026453.BL01 Activity: APP-3390
Review & Approve chedules Showing Manfacturers's Product Number Duct Work Insulation
Project: P026453.BL01 Activity: APP-3400
Review & Approve Hydronic Specialities Shop Drawing
Project: P026453.BL01 Activity: APP-3410
Review & Approve Hydronic Specialities Product Data
Project: P026453.BL01 Activity: APP-3420
Review & Approve Water Treatment Firm
Project: P026453.BL01 Activity: APP-3430
Review & Approve Chemical Products Product Data
Project: P026453.BL01 Activity: APP-3440
Review & Approve Detail of Gag for the Safety Relief Valves
Project: P026453.BL01 Activity: APP-3450
Review & Approve Boiler Accessories Maintenance Data
Project: P026453.BL01 Activity: APP-3460
Review & Approve Breeching Chimney Connectors and Chimneys Shop Drawing
Project: P026453.BL01 Activity: APP-3470
Review & Approve Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys

Project: P026453.BL01 Activity: APP-3480
Review & Approve Plate Heat Exchanger Maintenance Data
Project: P026453.BL01 Activity: APP-3490
Review & Approve Plate Heat Exchanger Product Data
Project: P026453.BL01 Activity: APP-3500
Review & Approve Coils Maintenance Data
Project: P026453.BL01 Activity: APP-3510
Review & Approve Coils Certifications
Project: P026453.BL01 Activity: APP-3520
Review & Approve Convectors Shop Drawing
Project: P026453.BL01 Activity: APP-3530
Review & Approve Convectors Product Data
Project: P026453.BL01 Activity: APP-3540
Review & Approve Fan Coils Units Maintenance Data & Materials
Project: P026453.BL01 Activity: APP-3550
Review & Approve Fan Coils Units Shop Drawings
Project: P026453.BL01 Activity: APP-3560
Review & Approve Door Air Curtains Shop Drawing
Project: P026453.BL01 Activity: APP-3570
Review & Approve Door Air Curtains Product Data
Project: P026453.BL01 Activity: APP-3580
Review & Approve Centrifugal Fans Shop Drawing
Project: P026453.BL01 Activity: APP-3590
Review & Approve Centrifugal Fans Product Data
Project: P026453.BL01 Activity: APP-3600
Review & Approve Centrifugal Fans Maintenance Data & Materials
Project: P026453.BL01 Activity: APP-3610
Review & Approve Air Filters Shop Drawing
Project: P026453.BL01 Activity: APP-3620
Review & Approve Air Filters Product Data
Project: P026453.BL01 Activity: APP-3630
Review & Approve Air Filters Maintenance Data & Materials
Project: P026453.BL01 Activity: APP-3640
Review & Approve Duct Accessories Shop Drawing
Project: P026453.BL01 Activity: APP-3650
Review & Approve Damper Assemblies Shop Drawing
Project: P026453.BL01 Activity: APP-3660
Review & Approve Damper Assemblies Product Data
Project: P026453.BL01 Activity: APP-3670
Review & Approve Damper Assemblies Maintenance Data & Materials
Project: P026453.BL01 Activity: APP-3680
Review & Approve Variable Air Terminals Shop Drawing
Project: P026453.BL01 Activity: APP-3690
Review & Approve Variable Air Terminals Product Data
Project: P026453.BL01 Activity: APP-3700
Review & Approve Variable Air Terminals Maintenance Data & Materials
Project: P026453.BL01 Activity: APP-3710
Review & Approve AHU for Public Assemblies Sapces Shop Drawing
Project: P026453.BL01 Activity: APP-3720
Review & Approve AHU for Public Assemblies Sapces Product Data

Project: P026453.BL01 Activity: APP-3730
Review & Approve AHU for Public Assemblies Sapces Maintenance Data & Materials
Project: P026453.BL01 Activity: APP-3740
Review & Approve Control Systems Shop Drawing
Project: P026453.BL01 Activity: APP-3750
Review & Approve Truck Network Cable Schematic Diagram
Project: P026453.BL01 Activity: APP-3760
Review & Approve Lighting Control Devices Shop Drawing
Project: P026453.BL01 Activity: APP-3770
Review & Approve Lighting Control Devices Product Data
Project: P026453.BL01 Activity: APP-3780
Review & Approve Lighting Control Devices Warranty
Project: P026453.BL01 Activity: APP-3790
Review & Approve Surge Protective Devices Shop Drawing
Project: P026453.BL01 Activity: APP-3800
Review & Approve Surge Protective Devices Product Data
Project: P026453.BL01 Activity: APP-3810
Review & Approve Surge Protective Devices Warranty
Project: P026453.BL01 Activity: APP-3820
Review & Approve Service Entrance Equipment Shop Drawing
Project: P026453.BL01 Activity: APP-3830
Review & Approve Service Entrance Equipment Product Data
Project: P026453.BL01 Activity: APP-3840
Review & Approve Service Entrance Equipment Warranty
Project: P026453.BL01 Activity: APP-3850
Review & Approve Enclosed Switches Product Data
Project: P026453.BL01 Activity: APP-3860
Review & Approve Enclosed Switches Test Reports
Project: P026453.BL01 Activity: APP-3870
Review & Approve Motors, Motor Control Centers and Starters Shop Drawing
Project: P026453.BL01 Activity: APP-3880
Review & Approve Motors, Motor Control Centers and Starters Product Data
Project: P026453.BL01 Activity: APP-3890
Review & Approve Motors, Motor Control Centers and Starters Field Test Reports
Project: P026453.BL01 Activity: APP-3900
Review & Approve Lightning Protection Shop Drawing
Project: P026453.BL01 Activity: APP-3920
Review & Approve Lightning Protection Test Reports
Project: P026453.BL01 Activity: APP-3930
Review & Approve Fiber Optic Cabling system Shop Drawing
Project: P026453.BL01 Activity: APP-3940
Review & Approve Fiber Optic Cabling system Product Data
Project: P026453.BL01 Activity: APP-3950
Review & Approve Fiber Optic Cabling system Samples
Project: P026453.BL01 Activity: APP-3960
Review & Approve Sound, Intercome & Security System Shop Drawing
Project: P026453.BL01 Activity: APP-3970
Review & Approve Sound, Intercome & Security System Programming Code and Password for the System
Project: P026453.BL01 Activity: APP-3980

Review & Approve Sound, Intercome & Security System warranty
Project: P026453.BL01 Activity: APP-3990
Review & Approve Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts
Project: P026453.BL01 Activity: APP-4000
Review & Approve Projection and Interactive Whiteboard Systems Wiring diagram
Project: P026453.BL01 Activity: APP-4010
Review & Approve Self Corrective Clock System Shop Drawing
Project: P026453.BL01 Activity: APP-4020
Review & Approve Self Corrective Clock System Product Data
Project: P026453.BL01 Activity: APP-4030
Review & Approve Self Corrective Clock System Field Test Reports
Project: P026453.BL01 Activity: APP-4040
Review & Approve Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings
Project: P026453.BL01 Activity: APP-4050
Review & Approve Soil Sampling Plan
Project: P026453.BL01 Activity: APP-4060
Review & Approve Steel Stairs Shop Drawings
Project: P026453.BL01 Activity: APP-4070
Review & Approve Steel Stairs Product Data
Project: P026453.BL01 Activity: APP-4080
Review & Approve Green School Submittal
Project: P026453.BL01 Activity: CLO-1000
Elevator Testing & Commissioning
Project: P026453.BL01 Activity: CLO-1010 HVAC Flush-Out
Project: P026453.BL01 Activity: CLO-1020
Electrical System Testing & Commissioning
Project: P026453.BL01 Activity: CLO-1140 SSDS System Testing & Commissioning
Project: P026453.BL01 Activity: CLO-1150 FDNY Inspection
Project: P026453.BL01 Activity: CLO-1160
Sprinkler/Domestic Booster Pumps Testing & Commissioning
Project: P026453.BL01 Activity: CLO-1170
Sprinkler/Domestic Booster Pumps Inspection
Project: P026453.BL01 Activity: CLO-1180
Sprinkler/Domestic Booster Pumps Sign-offs
Project: P026453.BL01 Activity: CLO-1190
Pre-Elevator Test Inspection
Project: P026453.BL01 Activity: CLO-1200
Elevator DOB Inspection
Project: P026453.BL01 Activity: CLO-1220
Emergency Generator Electric Load Test
Project: P026453.BL01 Activity: CLO-1230 Air Handling Unit Testing & Commissioning
Project: P026453.BL01 Activity: CLO-1240
Elevator Sump Pump Testing & Commissioning
Project: P026453.BL01 Activity: CLO-1250

Emergency Generator Testing & Commissioning
Project: P026453.BL01 Activity: CLO-1260 HVAC Split System Testing & Commissioning
Project: P026453.BL01 Activity: CLO-1270 Water Heater Testing & Commissioning
Project: P026453.BL01 Activity: CLO-1280 Fire Alarm Testing & Commissioning
Project: P026453.BL01 Activity: CLO-1290 Glycol System Testing & Commissioning
Project: P026453.BL01 Activity: CLO-1300 Provide Training
Project: P026453.BL01 Activity: CON-1010 Install Construction Signs
Project: P026453.BL01 Activity: CON-1030 Install Construction Fences
Project: P026453.BL01 Activity: CON-1080 Install Erosion Control Devices
Project: P026453.BL01 Activity: CON-1090 Install Trusses -1st Floor
Project: P026453.BL01 Activity: CON-1120 Install Firestopping Mock-Up
Project: P026453.BL01 Activity: CON-1130 Install MEP Hangers & Sleeves- 2nd Floor
Project: P026453.BL01 Activity: CON-1140 Approve Firestopping Mock-Up
Project: P026453.BL01 Activity: CON-1150 Install Steel Canopy Framing -2nd Floor
Project: P026453.BL01 Activity: CON-1160 Hoist Material Design
Project: P026453.BL01 Activity: CON-1180 Spray Fireproofing - 1st Floor
Project: P026453.BL01 Activity: CON-1190 Install Trusses -2nd Floor
Project: P026453.BL01 Activity: CON-1220 Spray Fireproofing - 2nd Floor
Project: P026453.BL01 Activity: CON-1230 Install MEP Hangers & Sleeves-3rd Floor
Project: P026453.BL01 Activity: CON-1250 Approval of Hoist Design
Project: P026453.BL01 Activity: CON-1260 Install Trusses - 3rd Floor
Project: P026453.BL01 Activity: CON-1280 Install Elevator Hoist Pad
Project: P026453.BL01 Activity: CON-1300 Spray Fireproofing - 3rd Floor
Project: P026453.BL01 Activity: CON-1310 Install MEP Hangers & Sleeves-4th Floor
Project: P026453.BL01 Activity: CON-1320 Erect Material Hoist
Project: P026453.BL01 Activity: CON-1360

Install Trusses - 4th Floor
Project: P026453.BL01 Activity: CON-1390
Spray Fireproofing - 4th Floor
Project: P026453.BL01 Activity: CON-1400
Install MEP Hangers & Sleeves-5th Floor
Project: P026453.BL01 Activity: CON-1420
Layout -2nd Floor
Project: P026453.BL01 Activity: CON-1430
Install Unit Masonry Mock-Up
Project: P026453.BL01 Activity: CON-1460
F/R/P Piers - 5th Floor
Project: P026453.BL01 Activity: CON-1470
Approve Unit Masonry Mock-Up
Project: P026453.BL01 Activity: CON-1490
Install Duct Risers -3rd Floor
Project: P026453.BL01 Activity: CON-1500
Install Mechanical Piping Risers-2nd Floor
Project: P026453.BL01 Activity: CON-1510 Duct
Leak Test -2nd Floor
Project: P026453.BL01 Activity: CON-1520
Install Top & Bottom Track-2nd Floor
Project: P026453.BL01 Activity: CON-1530
Layout -3rd Floor
Project: P026453.BL01 Activity: CON-1540
Install Trusses - 5th Floor
Project: P026453.BL01 Activity: CON-1560
Install Duct Risers -4th Floor
Project: P026453.BL01 Activity: CON-1570
Install CMU Walls -2nd Floor
Project: P026453.BL01 Activity: CON-1580
Install Plumbing Risers -2nd Floor
Project: P026453.BL01 Activity: CON-1590
Install Mechanical Piping Risers -3rd Floor
Project: P026453.BL01 Activity: CON-1600 Duct
Leak Test -3rd Floor
Project: P026453.BL01 Activity: CON-1610
Install MEP Hangers & Sleeves-Roof Floor
Project: P026453.BL01 Activity: CON-1620
Install Dunnage - 5th Floor
Project: P026453.BL01 Activity: CON-1630
Install Duct Risers-5th Floor
Project: P026453.BL01 Activity: CON-1640
Install Wall Steel Studs & Framing-2nd Floor
Project: P026453.BL01 Activity: CON-1650
Install Top & Bottom Track-3rd Floor
Project: P026453.BL01 Activity: CON-1660
Install CMU Walls -3rd Floor
Project: P026453.BL01 Activity: CON-1670
Layout -4th Floor
Project: P026453.BL01 Activity: CON-1680

Install Plumbing Risers -3rd Floor
Project: P026453.BL01 Activity: CON-1690
Install Mechanical Piping Risers -4th Floor
Project: P026453.BL01 Activity: CON-1700 Duct
Leak Test -4th Floor
Project: P026453.BL01 Activity: CON-1710
Install Power Risers-2nd Floor
Project: P026453.BL01 Activity: CON-1730
Spray Fireproofing - 5th Floor
Project: P026453.BL01 Activity: CON-1740
Install SSDS Risers -SSDS System -2nd Floor
Project: P026453.BL01 Activity: CON-1750
F/R/P Concrete Columns -Bulkhead
Project: P026453.BL01 Activity: CON-1760
Install Dunnage-Roof Floor
Project: P026453.BL01 Activity: CON-1770
Install Roof Drains & Clean outs -Roof Floor
Project: P026453.BL01 Activity: CON-1780
Install Plumbing Risers -4th Floor
Project: P026453.BL01 Activity: CON-1790
Install Mechanical Piping Risers-5th Floor
Project: P026453.BL01 Activity: CON-1800
Install Low Voltage Risers-2nd Floor
Project: P026453.BL01 Activity: CON-1810 Duct
Leak Test -5th Floor
Project: P026453.BL01 Activity: CON-1820
Install Power Risers-3rd Floor
Project: P026453.BL01 Activity: CON-1840
Install SSDS Risers -SSDS System -3rd Floor
Project: P026453.BL01 Activity: CON-1850
Rough-in Hot Water Piping-2nd Floor
Project: P026453.BL01 Activity: CON-1860
Rough-in Hot Glycol Piping-2nd Floor
Project: P026453.BL01 Activity: CON-1870
Rough-in Chilled Glycol Piping-2nd Floor
Project: P026453.BL01 Activity: CON-1890
Rough-in Duct Work -3rd Floor
Project: P026453.BL01 Activity: CON-1900
Install Wall Steel Studs & Framing-3rd Floor
Project: P026453.BL01 Activity: CON-1910
Install Top & Bottom Track-4th Floor
Project: P026453.BL01 Activity: CON-1920
Install CMU Walls -4th Floor
Project: P026453.BL01 Activity: CON-1930
Layout -5th Floor
Project: P026453.BL01 Activity: CON-1940
Install Plumbing Risers-5th Floor
Project: P026453.BL01 Activity: CON-1950
Install Low Voltage Risers-3rd Floor
Project: P026453.BL01 Activity: CON-1960

Install Power Risers-4th Floor
Project: P026453.BL01 Activity: CON-1970
Install SSDS Risers -SSDS System -4th Floor
Project: P026453.BL01 Activity: CON-1980
F/R/P Bulkhead Slab -Bulkhead
Project: P026453.BL01 Activity: CON-2000
Install SSDS Risers -SSDS System -5th Floor
Project: P026453.BL01 Activity: CON-2010
Install Wall Steel Studs & Framing-4th Floor
Project: P026453.BL01 Activity: CON-2020
Install Top & Bottom Track-5th Floor
Project: P026453.BL01 Activity: CON-2030
Install CMU Walls -5th Floor
Project: P026453.BL01 Activity: CON-2040
Install Low Voltage Risers-4th Floor
Project: P026453.BL01 Activity: CON-2050
Install Power Risers-5th Floor
Project: P026453.BL01 Activity: CON-2060
Install Hoist Beam-Bulkhead
Project: P026453.BL01 Activity: CON-2070
Install Roof Drains & Clean outs - Mechanical Work - Roof Bulkhead
Project: P026453.BL01 Activity: CON-2090
Install Elevator Controller #1 -Elevator Machine Room
Project: P026453.BL01 Activity: CON-2100
Install Low Voltage Risers-5th Floor
Project: P026453.BL01 Activity: CON-2120
Install Air Cooled Chiller CH-1 -Roof Floor
Project: P026453.BL01 Activity: CON-2130
Rough-in Hot Water Piping-3rd Floor
Project: P026453.BL01 Activity: CON-2140
Rough-in Hot Glycol Piping-3rd Floor
Project: P026453.BL01 Activity: CON-2150
Rough-in Chilled Glycol Piping-3rd Floor
Project: P026453.BL01 Activity: CON-2160
Rough-in Refrigerant Piping-3rd Floor
Project: P026453.BL01 Activity: CON-2170
Rough-in Duct Work -4th Floor
Project: P026453.BL01 Activity: CON-2190
Install Electric Unit Heater EUH - Mechanical Work - Roof Bulkhead
Project: P026453.BL01 Activity: CON-2200
Install Wall Steel Studs & Framing-5th Floor
Project: P026453.BL01 Activity: CON-2230
Install Emergency Generator -Bulkhead
Project: P026453.BL01 Activity: CON-2250
Install Air Handling Unit AHU-1 -Roof Floor
Project: P026453.BL01 Activity: CON-2260
Rough-in Hot Water Piping-4th Floor
Project: P026453.BL01 Activity: CON-2270
Rough-in Hot Glycol Piping-4th Floor
Project: P026453.BL01 Activity: CON-2280

Rough-in Chilled Glycol Piping-4th Floor
Project: P026453.BL01 Activity: CON-2290
Rough-in Refrigerant Piping-4th Floor
Project: P026453.BL01 Activity: CON-2300
Rough-in Duct Work-5th Floor
Project: P026453.BL01 Activity: CON-2310
Install Ceiling Hangers & Supports-2nd Floor
Project: P026453.BL01 Activity: CON-2320
Rough-in Power Conduits-3rd Floor
Project: P026453.BL01 Activity: CON-2340
Power Wires Pulling -2nd Floor
Project: P026453.BL01 Activity: CON-2350
Install Air Cooled Chiller CH-2 -Roof Floor
Project: P026453.BL01 Activity: CON-2360
Install Smoke Purge Fan SPF - Mechanical Work - Roof Bulkhead
Project: P026453.BL01 Activity: CON-2370
Install Elevator Controller #2 -Elevator Machine Room
Project: P026453.BL01 Activity: CON-2390
Install Ceiling Hangers & Supports-3rd Floor
Project: P026453.BL01 Activity: CON-2400
Install Windows -West Elevation
Project: P026453.BL01 Activity: CON-2410
Install Storefront System-West Elevation
Project: P026453.BL01 Activity: CON-2430
Install Air Handling Unit AHU-2 -Roof Floor
Project: P026453.BL01 Activity: CON-2440
Rough-in Hot Water Piping-5th Floor
Project: P026453.BL01 Activity: CON-2450
Rough-in Hot Glycol Piping-5th Floor
Project: P026453.BL01 Activity: CON-2460
Rough-in Chilled Glycol Piping-5th Floor
Project: P026453.BL01 Activity: CON-2470
Rough-in Refrigerant Piping-5th Floor
Project: P026453.BL01 Activity: CON-2480
Rough-in Power Conduits-4th Floor
Project: P026453.BL01 Activity: CON-2490 Low
Voltage Wires Pulling -2nd Floor
Project: P026453.BL01 Activity: CON-2500
Rough-in Low-Voltage Conduits-3rd Floor
Project: P026453.BL01 Activity: CON-2510
Power Wires Pulling-3rd Floor
Project: P026453.BL01 Activity: CON-2520
Install Voice Rack - 2nd Floor -IDF Room
Project: P026453.BL01 Activity: CON-2530
Install Data Rack - 2nd Floor -IDF Room
Project: P026453.BL01 Activity: CON-2550
Install Ceiling Hangers & Supports-4th Floor
Project: P026453.BL01 Activity: CON-2560
Install Air Handling Unit AHU-3 -Roof Floor
Project: P026453.BL01 Activity: CON-2570

Field Testing of Windows (5%)
Project: P026453.BL01 Activity: CON-2580
Install Power Panels -Elevator Machine Room
Project: P026453.BL01 Activity: CON-2600
Install Storefront System- South Elevation
Project: P026453.BL01 Activity: CON-2620
Install Ceiling Hangers & Supports-5th Floor
Project: P026453.BL01 Activity: CON-2630
Rough-in Gas Risers -2nd Floor
Project: P026453.BL01 Activity: CON-2650
Install Data Rack - 4th Floor IDF Room
Project: P026453.BL01 Activity: CON-2660
Install Voice Rack - 4th Floor IDF Room
Project: P026453.BL01 Activity: CON-2670
Install Wiring Devices -2nd Floor
Project: P026453.BL01 Activity: CON-2680
Rough-in Power Conduits -5th Floor
Project: P026453.BL01 Activity: CON-2690 Low
Voltage Wires Pulling -3rd Floor
Project: P026453.BL01 Activity: CON-2700
Rough-in Low-Voltage Conduits-4th Floor
Project: P026453.BL01 Activity: CON-2710
Power Wires Pulling-4th Floor
Project: P026453.BL01 Activity: CON-2720
Install Air Handling Unit AHU-4 -Roof Floor
Project: P026453.BL01 Activity: CON-2740
Rough-in Domestic Water Piping -2nd Floor
Project: P026453.BL01 Activity: CON-2750
Rough-in Gas Risers-3rd Floor
Project: P026453.BL01 Activity: CON-2760
Install IPDVS Equipment Rack - 2nd Floor -IDF Room
Project: P026453.BL01 Activity: CON-2770
Install Ladder Rack Cable Tray - 2nd Floor -IDF Room
Project: P026453.BL01 Activity: CON-2780
Install BACnet Data Cabinet - 2nd Floor -IDF Room
Project: P026453.BL01 Activity: CON-2790
Rough-in Conduits & Wires-Elevator Machine Room
Project: P026453.BL01 Activity: CON-2810
Install Grounding Bars - 4th Floor IDF Room
Project: P026453.BL01 Activity: CON-2820
Install Cable Ladder - 4th Floor IDF Room
Project: P026453.BL01 Activity: CON-2830
Install IPDVS Equipment Rack - 3rd Floor IDF Room
Project: P026453.BL01 Activity: CON-2840
Install Main Sound Rack - 34th Floor IDF Room
Project: P026453.BL01 Activity: CON-2850
Install Electric Unit Heaters -2nd Floor
Project: P026453.BL01 Activity: CON-2860
Install Fume Hood Exhaust -Roof Floor
Project: P026453.BL01 Activity: CON-2870

Rough-in Sanitary & Vent Piping -2nd Floor
Project: P026453.BL01 Activity: CON-2880
Rough-in Domestic Water Piping -3rd Floor
Project: P026453.BL01 Activity: CON-2890
Rough-in Gas Risers -4th Floor
Project: P026453.BL01 Activity: CON-2900
Install Duct Risers-1st Floor
Project: P026453.BL01 Activity: CON-2910
Layout -1st Floor
Project: P026453.BL01 Activity: CON-2930
Install Wiring Devices -3rd Floor
Project: P026453.BL01 Activity: CON-2940 Low Voltage Wires Pulling-4th Floor
Project: P026453.BL01 Activity: CON-2950
Rough-in Low-Voltage Conduits-5th Floor
Project: P026453.BL01 Activity: CON-2960
Power Wires Pulling-5th Floor
Project: P026453.BL01 Activity: CON-2970
Field Testing of Windows (50%)
Project: P026453.BL01 Activity: CON-2990
Install Storefront System- East Elevation
Project: P026453.BL01 Activity: CON-3000
Install Smoke Purge Fan -Roof Floor
Project: P026453.BL01 Activity: CON-3020
Rough-in Storm Piping -2nd Floor
Project: P026453.BL01 Activity: CON-3030
Rough-in Sanitary & Vent Piping -3rd Floor
Project: P026453.BL01 Activity: CON-3040
Rough-in Domestic Water Piping -4th Floor
Project: P026453.BL01 Activity: CON-3050
Rough-in Gas Risers & Piping -5th Floor
Project: P026453.BL01 Activity: CON-3060
Install Mechanical Piping Risers-1st Floor
Project: P026453.BL01 Activity: CON-3070 Duct Leak Test -1st Floor
Project: P026453.BL01 Activity: CON-3080
Install Top & Bottom Track -1st Floor
Project: P026453.BL01 Activity: CON-3090
Install CMU Walls -1st Floor
Project: P026453.BL01 Activity: CON-3100
Install Elevator Cabinet (1) -Elevator Machine Room
Project: P026453.BL01 Activity: CON-3110
Install IPDVS Equipment Rack - 4th Floor IDF Room
Project: P026453.BL01 Activity: CON-3120
Rough-in Duct Work -1st Floor
Project: P026453.BL01 Activity: CON-3130
Install Electric Unit Heaters -3rd Floor
Project: P026453.BL01 Activity: CON-3140
Install Plumbing Risers -1st Floor
Project: P026453.BL01 Activity: CON-3150

Install Convector Heater CV - Mechanical Work - 2nd Floor
Project: P026453.BL01 Activity: CON-3160
Install Floor Drains & Clean-outs -2nd Floor
Project: P026453.BL01 Activity: CON-3170
Rough-in Storm Piping -3rd Floor
Project: P026453.BL01 Activity: CON-3180
Rough-in Sanitary & Vent Piping -4th Floor
Project: P026453.BL01 Activity: CON-3190
Rough-in Domestic Water Piping -5th Floor
Project: P026453.BL01 Activity: CON-3200
Plumbing Pressure Testing -2nd Floor
Project: P026453.BL01 Activity: CON-3220
Dismantle Sidewalk Sheds- South Elevation
Project: P026453.BL01 Activity: CON-3240
Install Wall Steel Studs & Framing -1st Floor
Project: P026453.BL01 Activity: CON-3260
Install Power Risers-1st Floor
Project: P026453.BL01 Activity: CON-3270
Install Temporary Standpipe
Project: P026453.BL01 Activity: CON-3280
Install Wiring Devices -4th Floor
Project: P026453.BL01 Activity: CON-3290 Low
Voltage Wires Pulling-5th Floor
Project: P026453.BL01 Activity: CON-3310
Install 4" Standpipe -2nd Floor
Project: P026453.BL01 Activity: CON-3320
Install Floor Drains & Clean-outs -3rd Floor
Project: P026453.BL01 Activity: CON-3330
Rough-in Storm Piping -4th Floor
Project: P026453.BL01 Activity: CON-3340
Rough-in Sanitary & Vent Piping -5th Floor
Project: P026453.BL01 Activity: CON-3350
Install Low Voltage Risers-1st Floor
Project: P026453.BL01 Activity: CON-3360
Plumbing Pressure Testing -3rd Floor
Project: P026453.BL01 Activity: CON-3380
Install Windows -North Elevation
Project: P026453.BL01 Activity: CON-3390
Install Storefront System-North Elevation
Project: P026453.BL01 Activity: CON-3400
Install Hot Water Circulation Pump -5th Floor
Project: P026453.BL01 Activity: CON-3410
Install Electric Hot Water Heater (EWH-1) -5th Floor
Project: P026453.BL01 Activity: CON-3420
Install Electric Unit Heaters -4th Floor
Project: P026453.BL01 Activity: CON-3440
Install Hot Fluid Applied Membrane -5th Floor Roof
Project: P026453.BL01 Activity: CON-3450
Install Air Conditioning Unit AC - Mechanical Work - 2nd Floor
Project: P026453.BL01 Activity: CON-3460

Rough-in Hot Water Piping-1st Floor
Project: P026453.BL01 Activity: CON-3470
Rough-in Hot Glycol Piping-1st Floor
Project: P026453.BL01 Activity: CON-3480
Rough-in Chilled Glycol Piping-1st Floor
Project: P026453.BL01 Activity: CON-3490
Rough-in Refrigerant Piping-1st Floor
Project: P026453.BL01 Activity: CON-3500
Rough-in Main Sprinkler Piping -2nd Floor
Project: P026453.BL01 Activity: CON-3510
Install 4" Standpipe -3rd Floor
Project: P026453.BL01 Activity: CON-3520
Install Ceiling Hangers & Supports -1st Floor
Project: P026453.BL01 Activity: CON-3530
Install Floor Drains & Clean-outs -4th Floor
Project: P026453.BL01 Activity: CON-3540
Rough-in Storm Piping -5th Floor
Project: P026453.BL01 Activity: CON-3550
Install Cable Ladder - 3rd Floor IDF Room
Project: P026453.BL01 Activity: CON-3560
Plumbing Pressure Testing -4th Floor
Project: P026453.BL01 Activity: CON-3580
Install 6" Thick Rigid Insulation -5th Floor Roof
Project: P026453.BL01 Activity: CON-3590
Plumbing Pressure Testing -5th Floor
Project: P026453.BL01 Activity: CON-3610
Install Floor Drains & Clean-outs -5th Floor
Project: P026453.BL01 Activity: CON-3620
Install Elevator Cabinet (2) -Elevator Machine Room
Project: P026453.BL01 Activity: CON-3640
Install Electric Unit Heaters -5th Floor
Project: P026453.BL01 Activity: CON-3650
Install 4" Standpipe -4th Floor
Project: P026453.BL01 Activity: CON-3660
Install Wiring Devices -5th Floor
Project: P026453.BL01 Activity: CON-3670
Rough-in Branch Sprinkler Piping -2nd Floor
Project: P026453.BL01 Activity: CON-3680
Rough-in Sprinkler Heads -2nd Floor
Project: P026453.BL01 Activity: CON-3690
Rough-in Main Sprinkler Piping-3rd Floor
Project: P026453.BL01 Activity: CON-3700
Install Drainage -5th Floor Roof
Project: P026453.BL01 Activity: CON-3710 Roof
Flood Test -5th Floor Roof
Project: P026453.BL01 Activity: CON-3720
Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -2nd
Floor
Project: P026453.BL01 Activity: CON-3750
Install Emergency Generator- Roof Floor

Project: P026453.BL01 Activity: CON-3760
Rough-in Power Conduits -1st Floor
Project: P026453.BL01 Activity: CON-3770
Install 4" Standpipe -5th Floor
Project: P026453.BL01 Activity: CON-3780
Install Traffic Control Devices - 54th Avenue Street
Project: P026453.BL01 Activity: CON-3790
Rough-in Branch Sprinkler Piping -3rd Floor
Project: P026453.BL01 Activity: CON-3800
Rough-in Sprinkler Heads -3rd Floor
Project: P026453.BL01 Activity: CON-3810
Rough-in Main Sprinkler Piping-4th Floor
Project: P026453.BL01 Activity: CON-3820
Install Filter Fabric -5th Floor Roof
Project: P026453.BL01 Activity: CON-3830
Sprinklers Air Testing-2nd Floor
Project: P026453.BL01 Activity: CON-3850
Remove Existing Steel Faced Curb - 54th Avenue Street
Project: P026453.BL01 Activity: CON-3860
Remove Existing Asphalt - 54th Avenue Street
Project: P026453.BL01 Activity: CON-3880
Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-3rd Floor
Project: P026453.BL01 Activity: CON-3890
Install 4" Standpipe -Roof
Project: P026453.BL01 Activity: CON-3910
Install Grounding System -1st Floor
Project: P026453.BL01 Activity: CON-3920
Rough-in Low-Voltage Conduits-1st Floor
Project: P026453.BL01 Activity: CON-3930
Power Wires Pulling-1st Floor
Project: P026453.BL01 Activity: CON-3940
Remove Existing Electrical Manhole - 54th Avenue Street
Project: P026453.BL01 Activity: CON-3960
Install Concrete Pavers -5th Floor Roof
Project: P026453.BL01 Activity: CON-3970
Install VAV Boxes & Sound Attenuator Devices- 1st Floor
Project: P026453.BL01 Activity: CON-3980
Install VAV Boxes & Sound Attenuator Devices-2nd Floor
Project: P026453.BL01 Activity: CON-3990
Rough-in Branch Sprinkler Piping -4th Floor
Project: P026453.BL01 Activity: CON-4000
Rough-in Sprinkler Heads -4th Floor
Project: P026453.BL01 Activity: CON-4010
Rough-in Main Sprinkler Piping -5th Floor
Project: P026453.BL01 Activity: CON-4020
Install Filter Fabric -Roof Floor
Project: P026453.BL01 Activity: CON-4050
Plumbing Piping Insulation -2nd Floor
Project: P026453.BL01 Activity: CON-4060

Sprinklers Air Testing-3rd Floor
Project: P026453.BL01 Activity: CON-4070
Install Duct Insulation -2nd Floor
Project: P026453.BL01 Activity: CON-4080
Install 5' Wide Silva Cells Under Concrete Pavement Strip - 54th Avenue Street
Project: P026453.BL01 Activity: CON-4100
Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet-4th Floor
Project: P026453.BL01 Activity: CON-4120
Install Project Connect Cabinet - 1st Floor MDF Room
Project: P026453.BL01 Activity: CON-4130
Install BACnet Data Cabinet- 1st Floor MDF Room
Project: P026453.BL01 Activity: CON-4140
Install VAV Boxes & Sound Attenuator Devices-3rd Floor
Project: P026453.BL01 Activity: CON-4150
Pavement Replacement - 54th Avenue Street
Project: P026453.BL01 Activity: CON-4170
Install 4'' Concrete Sidewalk - 2nd Street
Project: P026453.BL01 Activity: CON-4180 Low Voltage Wires Pulling -1st Floor
Project: P026453.BL01 Activity: CON-4190
Plumbing Piping Insulation -3rd Floor
Project: P026453.BL01 Activity: CON-4200 Tape Gypsum Board -2nd Floor
Project: P026453.BL01 Activity: CON-4210
Install Concrete Pavers -Roof Floor
Project: P026453.BL01 Activity: CON-4220
Install VAV Boxes & Sound Attenuator Devices-4th Floor
Project: P026453.BL01 Activity: CON-4230
Rough-in Branch Sprinkler Piping -5th Floor
Project: P026453.BL01 Activity: CON-4240
Rough-in Sprinkler Heads -5th Floor
Project: P026453.BL01 Activity: CON-4250
Rough-in Main Sprinkler Piping -Roof
Project: P026453.BL01 Activity: CON-4270
Install Gypsum Board Ceiling -Mockup Room
Project: P026453.BL01 Activity: CON-4280
Sprinklers Air Testing-4th Floor
Project: P026453.BL01 Activity: CON-4290
Install New Steel Faced Curb - 54th Avenue Street
Project: P026453.BL01 Activity: CON-4300
Install Pedestrian Ramps With Truncated Domes - 54th Avenue Street
Project: P026453.BL01 Activity: CON-4320
Install Duct Insulation -3rd Floor
Project: P026453.BL01 Activity: CON-4330
Install VAV Boxes & Sound Attenuator Devices-5th Floor
Project: P026453.BL01 Activity: CON-4340
Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -5th Floor
Project: P026453.BL01 Activity: CON-4350

Install Ceramic Wall Tiles at Corridor-2nd Floor
Project: P026453.BL01 Activity: CON-4360
Install Gypsum Board Walls-3rd Floor
Project: P026453.BL01 Activity: CON-4390
Plumbing Piping Insulation -4th Floor
Project: P026453.BL01 Activity: CON-4400
Install 4'' Concrete Sidewalk - 54th Avenue Street
Project: P026453.BL01 Activity: CON-4410
Install 7'' Concrete Sidewalk - 54th Avenue Street
Project: P026453.BL01 Activity: CON-4430
Rough-in Branch Sprinkler Piping -Roof
Project: P026453.BL01 Activity: CON-4440
Rough-in Sprinkler Heads -Roof
Project: P026453.BL01 Activity: CON-4450
Install Gypsum Board Walls-1st Floor
Project: P026453.BL01 Activity: CON-4460
Rough-in Gas Risers -1st Floor
Project: P026453.BL01 Activity: CON-4470
Install Wiring Devices -1st Floor
Project: P026453.BL01 Activity: CON-4490
Sprinklers Air Testing-5th Floor
Project: P026453.BL01 Activity: CON-4500
Install SSDS Control Panel -1st Floor
Project: P026453.BL01 Activity: CON-4530
Plumbing Piping Insulation -5th Floor
Project: P026453.BL01 Activity: CON-4540 Tape
Gypsum Board -3rd Floor
Project: P026453.BL01 Activity: CON-4560
Install Pavement Marking - 54th Avenue Street
Project: P026453.BL01 Activity: CON-4570
Install Duct Insulation -4th Floor
Project: P026453.BL01 Activity: CON-4580
Remove Traffic Control Devices - 54th Avenue Street
Project: P026453.BL01 Activity: CON-4590
Rough-in Domestic Water Piping-1st Floor
Project: P026453.BL01 Activity: CON-4600 Tape
Gypsum Board -1st Floor
Project: P026453.BL01 Activity: CON-4610
Install Ceramic Wall Tiles at Corridor-3rd Floor
Project: P026453.BL01 Activity: CON-4620
Install Gypsum Board Walls-4th Floor
Project: P026453.BL01 Activity: CON-4650
Install 3 Way Roof Manifold -Roof
Project: P026453.BL01 Activity: CON-4670
Install Exhaust Fans -1st Floor
Project: P026453.BL01 Activity: CON-4680
Install Ceramic Wall Tiles at Corridor -1st Floor
Project: P026453.BL01 Activity: CON-4690
Rough-in Sanitary & Vent Piping -1st Floor
Project: P026453.BL01 Activity: CON-4700

Install Firestopping-2nd Floor
Project: P026453.BL01 Activity: CON-4710
Install Duct Insulation -5th Floor
Project: P026453.BL01 Activity: CON-4720 Tape
Gypsum Board -4th Floor
Project: P026453.BL01 Activity: CON-4730
Rough-in Conduits & Wires - Electric Service Room
Project: P026453.BL01 Activity: CON-4760
Rough-in Storm Piping -1st Floor
Project: P026453.BL01 Activity: CON-4770
Install PBX - 1st Floor MDF Room
Project: P026453.BL01 Activity: CON-4800
Install Ceramic Wall Tiles at Corridor-4th Floor
Project: P026453.BL01 Activity: CON-4810
Install Gypsum Board Walls-5th Floor
Project: P026453.BL01 Activity: CON-4820
Install Gypsum Board Ceiling-4th Floor
Project: P026453.BL01 Activity: CON-4840
Install Duct Insulation -1st Floor
Project: P026453.BL01 Activity: CON-4850
Install Firestopping-3rd Floor
Project: P026453.BL01 Activity: CON-4870
Install Cabinet Unit Heaters With Fan CUH-1st Floor
Project: P026453.BL01 Activity: CON-4880
Install Motorized Fire/Smoke Damper FSD - Mechanical Work - 1st Floor
Project: P026453.BL01 Activity: CON-4890
F/R/P Concrete Pads -Fuel Oil Room
Project: P026453.BL01 Activity: CON-4900
Rough-in Fuel Oil Piping -Fuel Oil Room
Project: P026453.BL01 Activity: CON-4910
Install 4" Standpipe -1st Floor
Project: P026453.BL01 Activity: CON-4920
Install Floor Drains & Clean-outs -1st Floor
Project: P026453.BL01 Activity: CON-4940
Install Duplex Domestic Water Booster Pump System (BP-1&BP-2) -1st Floor
Project: P026453.BL01 Activity: CON-4950
Install Duplex Ejector Pump System (EJ-1&EJ-2) -1st Floor
Project: P026453.BL01 Activity: CON-4960
F/R/P Concrete Pad - Electric Service Room
Project: P026453.BL01 Activity: CON-4970 Tape
Gypsum Board -5th Floor
Project: P026453.BL01 Activity: CON-4990
Install Fuel Oil Storage Tank (FOT-1) - Fuel Oil Room
Project: P026453.BL01 Activity: CON-5000
Mockup Room Inspection & Punchlist
Project: P026453.BL01 Activity: CON-5010
Install Firestopping-4th Floor
Project: P026453.BL01 Activity: CON-5020
Rough-in Fuel Oil Fill Piping -Fuel Oil Room
Project: P026453.BL01 Activity: CON-5030

Rough-in Main Sprinkler Piping -1st Floor
Project: P026453.BL01 Activity: CON-5040
Dismantle Hoist
Project: P026453.BL01 Activity: CON-5050
Plumbing Pressure Testing -1st Floor
Project: P026453.BL01 Activity: CON-5060
Install Hot Glycol / Hot Water Cabinet Heater (CUH) -3rd Floor
Project: P026453.BL01 Activity: CON-5070
Install Electric Unit Heaters -1st Floor
Project: P026453.BL01 Activity: CON-5080
Install Ceramic Wall Tiles at Corridor-5th Floor
Project: P026453.BL01 Activity: CON-5090
Install Acoustical Ceiling Tiles-2nd Floor
Project: P026453.BL01 Activity: CON-5100
Install Gypsum Board Ceiling-5th Floor
Project: P026453.BL01 Activity: CON-5150
Install Air Conditioning Unit AC - Mechanical Work - 1st Floor
Project: P026453.BL01 Activity: CON-5160
Install Fuel Oil Transfer Duplex Pump (FOP-1 & 2) -1st Floor
Project: P026453.BL01 Activity: CON-5170
Demolish Hoist Pad
Project: P026453.BL01 Activity: CON-5180
Install Service Switchboard "SS-A"- Electric Service Room
Project: P026453.BL01 Activity: CON-5200
Rough-in Fuel Oil Vent Piping -Fuel Oil Room
Project: P026453.BL01 Activity: CON-5210
Plumbing Piping Insulation -1st Floor
Project: P026453.BL01 Activity: CON-5220
Install Firestopping-5th Floor
Project: P026453.BL01 Activity: CON-5230
Rough-in Branch Sprinkler Piping -1st Floor
Project: P026453.BL01 Activity: CON-5240
Rough-in Sprinkler Heads -1st Floor
Project: P026453.BL01 Activity: CON-5250
Hoist In-Fill
Project: P026453.BL01 Activity: CON-5260
Install Cabinet Unit Heater With Fan CUH -4th Floor
Project: P026453.BL01 Activity: CON-5270
Install Control Valve Assembly & Fire Hose Valve with Cap and Chain in Cabinet -1st Floor
Project: P026453.BL01 Activity: CON-5280
Install Convector Heater CV - Mechanical Work - 3rd Floor
Project: P026453.BL01 Activity: CON-5300
Install Grease Interceptors - 1st Floor
Project: P026453.BL01 Activity: CON-5320
Install Door Curtains DC - Mechanical Work - 1st Floor
Project: P026453.BL01 Activity: CON-5330
Install Acoustical Ceiling Tiles-3rd Floor
Project: P026453.BL01 Activity: CON-5340
Install First Coat Painting-4th Floor

Project: P026453.BL01 Activity: CON-5370
Install Lighting Fixtures -3rd Floor
Project: P026453.BL01 Activity: CON-5380
Install Generator Connections -Roof Floor
Project: P026453.BL01 Activity: CON-5390
Install Firestopping-1st Floor
Project: P026453.BL01 Activity: CON-5410
Sprinklers Air Testing-1st Floor
Project: P026453.BL01 Activity: CON-5420
Install Asphalt Pavement - Playground Area & Fences - Building Perimeter
Project: P026453.BL01 Activity: CON-5430
Install Hot Glycol / Hot Water Cabinet Heater (CUH) -5th Floor
Project: P026453.BL01 Activity: CON-5450
Install Air Conditioning Unit AC - Mechanical Work - 3rd Floor
Project: P026453.BL01 Activity: CON-5460
Install Convector Heater CV - Mechanical Work - 4th Floor
Project: P026453.BL01 Activity: CON-5480
Install Gypsum Board Ceiling -1st Floor
Project: P026453.BL01 Activity: CON-5490
Install Convector Heater CV - Mechanical Work - 1st Floor
Project: P026453.BL01 Activity: CON-5500
Install Fire alarm Sensors and Devises -3rd Floor
Project: P026453.BL01 Activity: CON-5510
Install Leak Detector - Electric Service Room
Project: P026453.BL01 Activity: CON-5530
Install First Coat Painting -5th Floor
Project: P026453.BL01 Activity: CON-5540
Install Door Frames & Doors-4th Floor
Project: P026453.BL01 Activity: CON-5570
Install Plumbing Fixtures -2nd Floor
Project: P026453.BL01 Activity: CON-5580
Install Lighting Fixtures -4th Floor
Project: P026453.BL01 Activity: CON-5590
Install Exhaust Fan EF - Mechanical Work - 5th Floor
Project: P026453.BL01 Activity: CON-5610
Install Sprinkler Booster Pump - Electric Service Room
Project: P026453.BL01 Activity: CON-5620
Install Air Conditioning Unit AC - Mechanical Work - 4th Floor
Project: P026453.BL01 Activity: CON-5630
Install Convector Heater CV - Mechanical Work - 5th Floor
Project: P026453.BL01 Activity: CON-5640
Install Fire Alarm Normal ATS - Electric Service Room
Project: P026453.BL01 Activity: CON-5660
Install Fire alarm Sensors and Devises -4th Floor
Project: P026453.BL01 Activity: CON-5680
Install Door Frames & Doors -5th Floor
Project: P026453.BL01 Activity: CON-5690
Install Flooring Tiles-4th Floor
Project: P026453.BL01 Activity: CON-5710
Install Furniture & Milling Work (Contractor Provided & Installed) -2nd Floor

Project: P026453.BL01 Activity: CON-5720
Install First Coat Painting-1st Floor
Project: P026453.BL01 Activity: CON-5730
Install Plumbing Fixtures -3rd Floor
Project: P026453.BL01 Activity: CON-5740
Install Lighting Fixtures -5th Floor
Project: P026453.BL01 Activity: CON-5760
Install Wood Floating Floor System -Gymnatorium
Project: P026453.BL01 Activity: CON-5770
Install Air Cooled Condensing Unit ACCU - Mechanical Work - 5th Floor
Project: P026453.BL01 Activity: CON-5780
Install Motorized Fire/Smoke Damper & Control Panel - Electric Service Room
Project: P026453.BL01 Activity: CON-5790
Install Main Grounding Bus Bar - Electric Service Room
Project: P026453.BL01 Activity: CON-5810
Install Wall Pads - Gymnatorium
Project: P026453.BL01 Activity: CON-5820
Install Signages-2nd Floor
Project: P026453.BL01 Activity: CON-5830
Install Fire alarm Sensors and Devises -5th Floor
Project: P026453.BL01 Activity: CON-5840
Install Electric Unit Heater EUH-6 - Electric Service Room
Project: P026453.BL01 Activity: CON-5860
Install Sprinkler Booster Pump (SBP-1) -1st Floor
Project: P026453.BL01 Activity: CON-5870
Install Metal Panel Ceiling & Metal Geometric Ceiling -1st Floor
Project: P026453.BL01 Activity: CON-5880
Install Acoustical Ceiling Tiles -1st Floor
Project: P026453.BL01 Activity: CON-5890
Install Flooring Tiles -5th Floor
Project: P026453.BL01 Activity: CON-5910
Install Furniture & Milling Work (Contractor Provided & Installed) -3rd Floor
Project: P026453.BL01 Activity: CON-5920
Install Door Frames & Doors-1st Floor
Project: P026453.BL01 Activity: CON-5930
Install Plumbing Fixtures -4th Floor
Project: P026453.BL01 Activity: CON-5940
Install Lighting Fixtures -1st Floor
Project: P026453.BL01 Activity: CON-5950
Install Fire alarm Sensors and Devises -1st Floor
Project: P026453.BL01 Activity: CON-5960
F/R/P Concert Pad -Boiler Room
Project: P026453.BL01 Activity: CON-5970
Install Retractable Basketball Goal Assembly -Gymnatorium
Project: P026453.BL01 Activity: CON-6000
Rough-in Conduits & Wires-Boiler Room
Project: P026453.BL01 Activity: CON-6020
Install 8" Acoustic Block Painted-Gymnatorium
Project: P026453.BL01 Activity: CON-6030
Install Signages-3rd Floor

Project: P026453.BL01 Activity: CON-6050
Install Boiler B-1-Boiler Room
Project: P026453.BL01 Activity: CON-6070
Install Furniture & Milling Work (Contractor Provided & Installed) -4th Floor
Project: P026453.BL01 Activity: CON-6080
Install Flooring Tiles-1st Floor
Project: P026453.BL01 Activity: CON-6090
Install Plumbing Fixtures -5th Floor
Project: P026453.BL01 Activity: CON-6100
Install Jockey Pump (JP-1) -1st Floor
Project: P026453.BL01 Activity: CON-6110
Install Boiler B-2-Boiler Room
Project: P026453.BL01 Activity: CON-6120
Install Air Separator Units (AS-1 , AS-2 & AS-3)
Project: P026453.BL01 Activity: CON-6130
Install Boiler Condensate ACID Neutralization Tubes -Boiler Room
Project: P026453.BL01 Activity: CON-6150
Install Furniture & Milling Work (Contractor Provided & Installed) -5th Floor
Project: P026453.BL01 Activity: CON-6160
Install Signages-4th Floor
Project: P026453.BL01 Activity: CON-6180
Install Plumbing Fixtures-1st Floor
Project: P026453.BL01 Activity: CON-6200
Install Expansion Tanks (ET-1 , ET-2 & ET-3)
Project: P026453.BL01 Activity: CON-6210
Install Glycol Make-up Units (GF-1 & GF-2 & GF-3)
Project: P026453.BL01 Activity: CON-6220
Install Reduced Pressure Zone (RPZ) Devices -Boiler Room
Project: P026453.BL01 Activity: CON-6230
Install Gym Equipment -Gymnatorium -Gymnatorium
Project: P026453.BL01 Activity: CON-6240
Install Fine Tube Radiator FTR - Gymnatorium
Project: P026453.BL01 Activity: CON-6250
Install Hydraulic Vertical Wheelchair Lift -Gymnatorium
Project: P026453.BL01 Activity: CON-6260
Install Heat Exchanger -Boiler Room
Project: P026453.BL01 Activity: CON-6280
Install Signages- 5th Floor
Project: P026453.BL01 Activity: CON-6290
Install Hot Glycol Units Heaters (UH-5-1, UH-5-2)
Project: P026453.BL01 Activity: CON-6310
Install Security Screens & Barriers-1st Floor
Project: P026453.BL01 Activity: CON-6330
Install Heat Pump Electric Hot Water Heater (HPWH#1&2)-Boiler Room
Project: P026453.BL01 Activity: CON-6340
Install Exhaust Fans -Boiler Room
Project: P026453.BL01 Activity: CON-6350
Install Primary Hot Water Pump (GHWP 1 to 3) -Boiler Room
Project: P026453.BL01 Activity: CON-6360
Install Primary Chilled Water Pump (GCHWP-1&2)-Boiler Room

Project: P026453.BL01 Activity: CON-6380
Install Food Service Equipment-1st Floor
Project: P026453.BL01 Activity: CON-6390
Install Auditorium Television Studio Dimming System -Gymnatorium
Project: P026453.BL01 Activity: CON-6400
Install Secondary Hot Water Pump(HWP-1&2)-Boiler Room
Project: P026453.BL01 Activity: CON-6410
Install Electric Unit Heater (EUH-3) - Boiler Room
Project: P026453.BL01 Activity: CON-6420
Install Branch Panels (BRPP) -Boiler Room
Project: P026453.BL01 Activity: CON-7740
Protection Of All Overhead & Underground Utilities
Project: P026453.BL01 Activity: CON-7750
Install Field Offices
Project: P026453.BL01 Activity: CON-7960
Obtain Gas Meter Layout From CON-ED
Project: P026453.BL01 Activity: CON-7970
Coordinate With CON-ED For Gas Service
Project: P026453.BL01 Activity: CON-7990 Gas
Authorization
Project: P026453.BL01 Activity: CON-8000 Pink
Slip
Project: P026453.BL01 Activity: CON-8010
Coordination With CON-ED For Temporary Electrical Power
Project: P026453.BL01 Activity: CON-8020
Scheduling With CON-ED For Temporary Electrical Power
Project: P026453.BL01 Activity: CON-8030
Procurement From CON-ED For Temporary Electrical Power
Project: P026453.BL01 Activity: CON-8040
CON-ED Work For Temporary Electrical Power
Project: P026453.BL01 Activity: CON-8050
Available Temporary Electrical Power For Testing MEP Equipment
Project: P026453.BL01 Activity: CON-8060
CON-ED - Switchgear Inspection
Project: P026453.BL01 Activity: CON-8070
CON-ED - Pull Power Cable to the Building
Project: P026453.BL01 Activity: CON-8080
CON-ED - Terminate Power Cables
Project: P026453.BL01 Activity: CON-8090
CON-ED - Energize to the Building
Project: P026453.BL01 Activity: CON-8390
Install Sidewalk Sheds -South Elevation
Project: P026453.BL01 Activity: CON-8400
Install Sidewalk Sheds -East Elevation
Project: P026453.BL01 Activity: CON-9000
Protection & Restoration the adjacent Properties to Original Condition
Project: P026453.BL01 Activity: CON-9010
Remove Steel Plate Protection over NYPA Easement - Playground Area & Fences -
Building Perimeter
Project: P026453.BL01 Activity: CON-9020

Install Furniture & Milling Work (Owner Provided & Installed) -1st Floor
Project: P026453.BL01 Activity: CON-9030
Install Furniture & Milling Work (Owner Provided & Installed) -2nd Floor
Project: P026453.BL01 Activity: CON-9040
Install Furniture & Milling Work (Owner Provided & Installed) -3rd Floor
Project: P026453.BL01 Activity: CON-9050
Install Furniture & Milling Work (Owner Provided & Installed) -4th Floor
Project: P026453.BL01 Activity: CON-9060
Install Furniture & Milling Work (Owner Provided & Installed) -5th Floor
Project: P026453.BL01 Activity: CON-9070
In-Wall Inspection-2nd Floor
Project: P026453.BL01 Activity: CON-9080
In-Wall Inspection -3rd Floor
Project: P026453.BL01 Activity: CON-9090
In-Wall Inspection -4th Floor
Project: P026453.BL01 Activity: CON-9100
In-Wall Inspections -5th Floor
Project: P026453.BL01 Activity: CON-9110
In-Wall Inspection -1st Floor
Project: P026453.BL01 Activity: CON-9130
Install Switch Gear - Electric Service Room
Project: P026453.BL01 Activity: CON-9150
Install LED Theatrical Lighting -Gymnatorium
Project: P026453.BL01 Activity: CON-9180
Install 6" Fire Water Service (54th Avenue Street)- Drainage Work - Building Perimeter
Project: P026453.BL01 Activity: CON-98797
Install Intrusion System Components-2nd Floor
Project: P026453.BL01 Activity: CON-98807
Install Intrusion System Components-3rd Floor
Project: P026453.BL01 Activity: CON-98817
Install Intrusion System Components-4th Floor
Project: P026453.BL01 Activity: CON-98827
Install Intrusion System Components -5th Floor
Project: P026453.BL01 Activity: CON-98837
Install Intrusion System Components-1st Floor
Project: P026453.BL01 Activity: CON-98847
Install Auxiliary System Components-2nd Floor
Project: P026453.BL01 Activity: CON-98857
Install Auxiliary System Components-3rd Floor
Project: P026453.BL01 Activity: CON-98867
Install Auxiliary System Components-4th Floor
Project: P026453.BL01 Activity: CON-98877
Install Auxiliary System Components -5th Floor
Project: P026453.BL01 Activity: CON-98887
Install Auxiliary System Components-1st Floor
Project: P026453.BL01 Activity: CON-98897
Install Sound Clock System Components-2nd Floor
Project: P026453.BL01 Activity: CON-98907
Install Sound Clock System Components-3rd Floor

Project: P026453.BL01 Activity: CON-98917
Install Sound Clock System Components-4th Floor
Project: P026453.BL01 Activity: CON-98927
Install Sound Clock System Components -5th Floor
Project: P026453.BL01 Activity: CON-98937
Install Sound Clock System Components-1st Floor
Project: P026453.BL01 Activity: CON-98947
Install 4" slotted schedule 80 PVC Piping -1st Floor
Project: P026453.BL01 Activity: CON-99157
Install Elevator Sump Pump -Elevator Machine Room
Project: P026453.BL01 Activity: CON-99167
Install Elevator Guide Rails -Elevator Machine Room
Project: P026453.BL01 Activity: CON-99217
Install Bleachers -Gymnatorium
Project: P026453.BL01 Activity: CON-99237
Install Flag Pole - South Elevation
Project: P026453.BL01 Activity: CON-99247
Install Laboratory Equipment -3rd Floor
Project: P026453.BL01 Activity: CON-99257
Subcontractor Buyout
Project: P026453.BL01 Activity: CON-99267
Install Rolling Doors-1st Floor
Project: P026453.BL01 Activity: CON-99277
Install Steel Stairs -1st Floor
Project: P026453.BL01 Activity: CON-99287
Install Steel Stairs -2nd Floor
Project: P026453.BL01 Activity: CON-99297
Install Steel Stairs- 3rd Floor
Project: P026453.BL01 Activity: CON-99307
Install Steel Stairs - 4th Floor
Project: P026453.BL01 Activity: CON-99317
Install Steel Stairs - 5th Floor
Project: P026453.BL01 Activity: CON-99327
Install Lightning Protection System-1st Floor
Project: P026453.BL01 Activity: CON-99337
Install Lightning Protection system -5th Floor
Project: P026453.BL01 Activity: CON-99347
Install Lightning Protection System - Roof Floor
Project: P026453.BL01 Activity: CON-99357
Install CMU Wall for Shaft -Elevator Machine Room
Project: P026453.BL01 Activity: I-1010 Concrete
Cast-IN-Place Inspection
Project: P026453.BL01 Activity: I-1020 Masonry
Inspection
Project: P026453.BL01 Activity: I-1040 Roofing
Flood Testing Inspection
Project: P026453.BL01 Activity: I-1080 Standpipe
System Inspection
Project: P026453.BL01 Activity: I-1100
Fire-Resistant Penetrations And Joints Inspection

Project: P026453.BL01 Activity: I-1110 Fuel-Oil Storage & Fuel Oil Piping Systems Inspection
Project: P026453.BL01 Activity: I-1120 Mechanical System Inspection
Project: P026453.BL01 Activity: I-1130 Fire Alarm Inspection
Project: P026453.BL01 Activity: I-1140 Structural Steel Inspection
Project: P026453.BL01 Activity: I-1150 Concrete Precast Inspection
Project: P026453.BL01 Activity: MIL-1030 Project Duration(From NTP till TCO)
Project: P026453.BL01 Activity: MIL-1040 Project Duration(From NTP till Substantial Completion)
Project: P026453.BL01 Activity: MIL-1060 Mobilization Start
Project: P026453.BL01 Activity: MIL-1120 Metal Decking Start
Project: P026453.BL01 Activity: MIL-1140 Layout Start
Project: P026453.BL01 Activity: MIL-1150 Masonry Walls Start
Project: P026453.BL01 Activity: MIL-1160 Top & Bottom Track Start
Project: P026453.BL01 Activity: MIL-1170 Finish Concrete Work
Project: P026453.BL01 Activity: MIL-1200 Main Roofing Start
Project: P026453.BL01 Activity: MIL-1210 Duct Rough-ins Start
Project: P026453.BL01 Activity: MIL-1220 Layout Finish
Project: P026453.BL01 Activity: MIL-1230 5th Floor Roofing Start
Project: P026453.BL01 Activity: MIL-1250 Top & Bottom Track Finish
Project: P026453.BL01 Activity: MIL-1260 Plumbing Rough-ins Start
Project: P026453.BL01 Activity: MIL-1270 Electrical Rough-ins Start
Project: P026453.BL01 Activity: MIL-1280 Main Roofing Finish
Project: P026453.BL01 Activity: MIL-1290 Duct Rough-ins Finish
Project: P026453.BL01 Activity: MIL-1300 Start Sprinkler Rough-ins
Project: P026453.BL01 Activity: MIL-1310 5th Floor Roofing Finish
Project: P026453.BL01 Activity: MIL-1320 Plumbing Rough-ins Finish

Project: P026453.BL01 Activity: MIL-1330
Finish Sprinkler Rough-ins
Project: P026453.BL01 Activity: MIL-1350
Electrical Rough-ins Finish
Project: P026453.BL01 Activity: MIL-1360
Start Mockup Room Work
Project: P026453.BL01 Activity: MIL-1380
Crane Mobilization-Mechanical Subcontractor
Project: P026453.BL01 Activity: MIL-1400
Start Site Work
Project: P026453.BL01 Activity: MIL-1410
Mockup Room Ready For Inspection
Project: P026453.BL01 Activity: MIL-1430
Start Architecture Finishes
Project: P026453.BL01 Activity: MIL-1440
Start Gypsum Board
Project: P026453.BL01 Activity: MIL-1450
Start 1st Coat Painting
Project: P026453.BL01 Activity: MIL-1460 Roof
Top Units Installations Start
Project: P026453.BL01 Activity: MIL-1480 Roof
Top Units Installations Finish
Project: P026453.BL01 Activity: MIL-1580
Window Installation Finish
Project: P026453.BL01 Activity: MIL-1600 MDF
Work Finish
Project: P026453.BL01 Activity: MIL-1640
Provide Complete Set of Approved Coordination Drawings
Project: P026453.BL01 Activity: MIL-1650 FDNY
Inspection Finish
Project: P026453.BL01 Activity: MIL-1660
Start Security Guard Services (30 Days From NTP)
Project: P026453.BL01 Activity: MIL-1670
Elevator Final Sign-off
Project: P026453.BL01 Activity: MIL-1680
Emergency Generator Final Sign-off
Project: P026453.BL01 Activity: MIL-1720
Start Sidewalk Bridge Installations
Project: P026453.BL01 Activity: MIL-1730
Sidewalk Sheds Dismantle Complete
Project: P026453.BL01 Activity: MIL-1740
Start Windows
Project: P026453.BL01 Activity: MIL-1750
Start Firestopping
Project: P026453.BL01 Activity: MIL-1760
Start Elevator Work
Project: P026453.BL01 Activity: MIL-1770
Project Duration(From NTP till Final Completion)
Project: P026453.BL01 Activity: MIL-1810
Crane Mobilization-Steel Installation start

Project: P026453.BL01 Activity: MIL-1820
Crane Mobilization-Steel Installation Finish
Project: P026453.BL01 Activity: MIL-1830
Crane Mobilization-Precast Sandwich Panels Installation Start
Project: P026453.BL01 Activity: MIL-1840
Crane Mobilization-Precast Sandwich Panels Installation Finish
Project: P026453.BL01 Activity: MIL-2532
Submit Complete Permit Application
Project: P026453.BL01 Activity: MIL-2542
Complete Subcontractor ‘Buyout’
Project: P026453.BL01 Activity: MIL-2562
Start Below Grade Plumbing and Other Utilities
Project: P026453.BL01 Activity: MIL-2572
Place Steel Mill Order
Project: P026453.BL01 Activity: MIL-2582
Start Concrete Placement
Project: P026453.BL01 Activity: MIL-2592 P&D
- Connection to Roof Drains
Project: P026453.BL01 Activity: MIL-2602
Start Mechanical Distribution Lines
Project: P026453.BL01 Activity: MIL-2612
Start Suspended Ceiling Grid
Project: P026453.BL01 Activity: MIL-2622
Deliveries of all owner-furnished equipment and/or materials
Project: P026453.BL01 Activity: MIL-2632
Finish HVAC
Project: P026453.BL01 Activity: MIL-2642
Finish Fire Alarm Signoff
Project: P026453.BL01 Activity: MIL-2652
Finish Mechanical and Electrical System Commissioning
Project: P026453.BL01 Activity: MIL-2662
Finishes and Ceiling Complete
Project: P026453.BL01 Activity: MIL-2692
Building HVAC Flush-out
Project: P026453.BL01 Activity: MIL-2712
Start Low Voltage
Project: P026453.BL01 Activity: MIL-2722
Start Kitchen
Project: P026453.BL01 Activity: MIL-2732
Start Mechanical and Electrical System Commissioning
Project: P026453.BL01 Activity: MIL-2742
Permanent Power Available
Project: P026453.BL01 Activity: MIL-2762
Green Schools Compliance Submission
Project: P026453.BL01 Activity: MIL-2772
Performance test for all mechanical equipment and low voltage systems
Project: P026453.BL01 Activity: MIL-2782
Submission of Operations and Maintenance Manuals
Project: P026453.BL01 Activity: MIL-2792
Commissioning for all mechanical equipment and low voltage systems

Project: P026453.BL01 Activity: MIL-2802
Provision of Training Schedules (30 days prior to start of Training)
Project: P026453.BL01 Activity: MIL-2812
Start Foundation
Project: P026453.BL01 Activity: MIL-2822
Elevator Ready for Testing
Project: P026453.BL01 Activity: MIL-2832
Issuance of Excavation & Shoring Permit
Project: P026453.BL01 Activity: MIL-2842
Issuance of Builders Pavement Permit
Project: P026453.BL01 Activity: MIL-2852
Issuance of Permit to Enter (PTE)
Project: P026453.BL01 Activity: MIL-2862
Issuance of NYPA Permit
Project: P026453.BL01 Activity: MIL-2872
Issuance of Construction Fences Permit
Project: P026453.BL01 Activity: MIL-2882
Issuance of Sidewalk Shed Permits
Project: P026453.BL01 Activity: MIL-2892
Issuance of CCD1
Project: P026453.BL01 Activity: MIL-2902
Issuance of DOB Permit & Insurance
Project: P026453.BL01 Activity: MIL-2912
Start Concrete Cast In Place Inspection
Project: P026453.BL01 Activity: MIL-2922
Start Pre -Cast Concrete Inspection
Project: P026453.BL01 Activity: MIL-2932
Start Masonry Inspection
Project: P026453.BL01 Activity: MIL-2942
Start In-Wall Inspection
Project: P026453.BL01 Activity: MIL-2952
Finish Standpipe System Inspection
Project: P026453.BL01 Activity: MIL-2962
Finish Fire Alarm Inspection
Project: P026453.BL01 Activity: MIL-2972
Finish Mechanical System Inspection
Project: P026453.BL01 Activity: MIL-2982
Finish Fire-Resistant Penetrations And Joints Inspection
Project: P026453.BL01 Activity: MIL-2992
Finish Fuel-Oil Storage & Fuel Oil Piping Systems Inspection
Project: P026453.BL01 Activity: PER-2640
Obtain Emergency Generator Permit
Project: P026453.BL01 Activity: PER-2650
Elevator Equipment Use Permit
Project: P026453.BL01 Activity: PRE-1460
Obtain Construction Fences Permit
Project: P026453.BL01 Activity: PRE-1660 DOB
Permit & Insurance
Project: P026453.BL01 Activity: PRE-2540 SCA
Work Notification

Project: P026453.BL01 Activity: PRE-2550 Obtain CCD1
Project: P026453.BL01 Activity: PRE-2570 Obtain Sidewalk Shed Permits
Project: P026453.BL01 Activity: PRE-2590 Meeting With SCA to Review The Permit Requirements
Project: P026453.BL01 Activity: PRE-2600 Prepare & Submit Permit Waiver Requests to SCA Chief Project Officer
Project: P026453.BL01 Activity: PRE-2610 Prepare & Submit FDNY Fuel Permit
Project: P026453.BL01 Activity: PRE-2620 Review & Approve FDNY Fuel Permit
Project: P026453.BL01 Activity: PRE-2630 Obtain Builders Pavement Permit
Project: P026453.BL01 Activity: PRE-2640 Obtain Excavation & Shoring Permit
Project: P026453.BL01 Activity: PRE-2650 Obtain Permit to Enter (PTE) Amtrak
Project: P026453.BL01 Activity: PRE-2660 Obtain NYPA Permit
Project: P026453.BL01 Activity: PRO-1000 Procure & Deliver Kitchen Equipment
Project: P026453.BL01 Activity: PRO-1010 Procure & Deliver Furnitures
Project: P026453.BL01 Activity: PRO-1020 Procure & Deliver Mechanical Piping
Project: P026453.BL01 Activity: PRO-1030 Procure & Deliver Mechanical Ducts
Project: P026453.BL01 Activity: PRO-1050 Procure & Deliver Electrical Equipment
Project: P026453.BL01 Activity: PRO-1060 Procure & Deliver Plumbing Fixtures
Project: P026453.BL01 Activity: PRO-1070 Procure & Deliver Wood Doors
Project: P026453.BL01 Activity: PRO-1090 Procure & Deliver Fire Sprinklers
Project: P026453.BL01 Activity: PRO-1110 Procure & Deliver Fire Detectors & Alarms
Project: P026453.BL01 Activity: PRO-1120 Procure & Deliver Erosion Control and Sedimentation Devices
Project: P026453.BL01 Activity: PRO-1140 Procure & Deliver Lighting Fixtures
Project: P026453.BL01 Activity: PRO-1150 Procure & Deliver Gypsum Board
Project: P026453.BL01 Activity: PRO-1160 Procure & Deliver Floorings
Project: P026453.BL01 Activity: PRO-1170 Procure & Deliver Acosutical Ceiling Tiles
Project: P026453.BL01 Activity: PRO-1190 Procure & Deliver Toilet Accessories

Project: P026453.BL01 Activity: PRO-1200
Procure & Deliver Elevator Machine
Project: P026453.BL01 Activity: PRO-1210
Procure & Deliver Signs
Project: P026453.BL01 Activity: PRO-1220
Procure & Deliver Windows & Storefronts
Project: P026453.BL01 Activity: PRO-1250
Procure & Deliver Plumbing Pipes
Project: P026453.BL01 Activity: PRO-1260
Procure & Deliver Electrical Wires & Conduits
Project: P026453.BL01 Activity: PRO-1270
Procure & Deliver Mechanical Pumps
Project: P026453.BL01 Activity: PRO-1280
Procure & Deliver Fire Protection Pumps
Project: P026453.BL01 Activity: PRO-1290
Procure & Deliver Plumbing Pumps
Project: P026453.BL01 Activity: PRO-1310
Procure & Deliver Telecommunication System
Project: P026453.BL01 Activity: PRO-1330
Procure & Deliver Cameras
Project: P026453.BL01 Activity: PRO-1360
Procure & Deliver Metal Panel Ceilings
Project: P026453.BL01 Activity: PRO-1380
Procure & Deliver Roof Dunnage
Project: P026453.BL01 Activity: PRO-1410
Procure & Deliver Door Frames
Project: P026453.BL01 Activity: PRO-1420
Procure & Deliver Painting
Project: P026453.BL01 Activity: PRO-1450
Procure & Deliver Playground Equipment
Project: P026453.BL01 Activity: PRO-1470
Procure & Deliver Cabinet Heaters
Project: P026453.BL01 Activity: PRO-1480
Procure & Deliver Chillers
Project: P026453.BL01 Activity: PRO-1490
Procure & Deliver Air Handling Units
Project: P026453.BL01 Activity: PRO-1500
Procure & Deliver Boilers
Project: P026453.BL01 Activity: PRO-1510
Procure & Deliver Emergency Generator
Project: P026453.BL01 Activity: PRO-1520
Procure & Deliver Switch Gears
Project: P026453.BL01 Activity: PRO-1530
Procure & Deliver Hydraulic Vertical Wheelchair Lift
Project: P026453.BL01 Activity: PRO-1560
Procure & Deliver Gymnasium Equipment
Project: P026453.BL01 Activity: PRO-1570
Procure & Deliver Precast Sandwich Panels
Project: P026453.BL01 Activity: PRO-1580
Procure & Deliver Metal Deck

Project: P026453.BL01 Activity: PRO-1590
Procure & Deliver Steel Columns
Project: P026453.BL01 Activity: PRO-1600
Procure & Deliver Trusses
Project: P026453.BL01 Activity: PRO-1610
Procure & Deliver Prefabricated Expansion Joint Covers
Project: P026453.BL01 Activity: PRO-1620
Procure & Deliver Security Screens & Barriers
Project: P026453.BL01 Activity: PRO-1630
Procure & Deliver Wood Flooring
Project: P026453.BL01 Activity: PRO-1640
Procure & Deliver Concrete Floating Floor Assembly
Project: P026453.BL01 Activity: PRO-1660
Procure & Deliver Auditorium Television Studio Dimming System
Project: P026453.BL01 Activity: PRO-1990
Procure & Deliver Gas Meter Rig
Project: P026453.BL01 Activity: PRO-2000
Procure & Deliver Key Cutting Machine
Project: P026453.BL01 Activity: PRO-2010
Procure & Deliver Steel Stairs Components
Project: P026453.BL01 Activity: PRO-2020
Procure & Deliver Flagpole
Project: P026453.BL01 Activity: PRO-2030
Procure & Deliver Bleachers
Project: P026453.BL01 Activity: PRO-2040
Procure & Deliver VAV Units
Project: P026453.BL01 Activity: PRO-2050
Procure & Deliver Furnitures (Owner Responsibility)
Project: P026453.BL01 Activity: SUB-1000
Prepare & Submit Split Heat Pump System - SUB
Project: P026453.BL01 Activity: SUB-1010
Prepare & Submit Thermometers
Project: P026453.BL01 Activity: SUB-1020
Prepare & Submit Pressure Gages
Project: P026453.BL01 Activity: SUB-1030
Prepare & Submit Floor Drains
Project: P026453.BL01 Activity: SUB-1040
Prepare & Submit Hangers & Supports
Project: P026453.BL01 Activity: SUB-1050
Prepare & Submit Fire & Jockey Pumps
Project: P026453.BL01 Activity: SUB-1060
Prepare & Submit Interior Signage Shop Drawings
Project: P026453.BL01 Activity: SUB-1070
Prepare & Submit Ceramic Tiles Product Data
Project: P026453.BL01 Activity: SUB-1080
Prepare & Submit Door Hardware Submittal
Project: P026453.BL01 Activity: SUB-1090
Prepare & Submit Painting
Project: P026453.BL01 Activity: SUB-1100
Prepare & Submit Door & Frame Corners Samples

Project: P026453.BL01 Activity: SUB-1110
Prepare & Submit Roof Drains & Clean Outs
Project: P026453.BL01 Activity: SUB-1120
Prepare & Submit Flashing & Sheet Metal Shop Drawing
Project: P026453.BL01 Activity: SUB-1130
Prepare & Submit Roofing Membrane Product Data
Project: P026453.BL01 Activity: SUB-1140
Prepare & Submit Perimeter Foundation Insulation Product Data
Project: P026453.BL01 Activity: SUB-1150
Prepare & Submit Crystalline Waterproofing Product Data
Project: P026453.BL01 Activity: SUB-1160
Prepare & Submit Suspension Assembly Shop Drawings
Project: P026453.BL01 Activity: SUB-1170
Prepare & Submit Certification of Material
Project: P026453.BL01 Activity: SUB-1180
Prepare & Submit Concrete Reinforcement
Project: P026453.BL01 Activity: SUB-1190
Prepare & Submit Formwork Shop Drawings
Project: P026453.BL01 Activity: SUB-1200
Prepare & Submit Planting Schedule
Project: P026453.BL01 Activity: SUB-1210
Prepare & Submit Site Furnishings Shop Drawings
Project: P026453.BL01 Activity: SUB-1220
Prepare & Submit Playgroung Equipment Shop Drawings
Project: P026453.BL01 Activity: SUB-1230
Prepare & Submit Ductile Iron Pipes
Project: P026453.BL01 Activity: SUB-1240
Prepare & Submit Catch Basin Shop Drawings
Project: P026453.BL01 Activity: SUB-1250
Prepare & Submit Concrete Curbs & Pavements Shop Drawing
Project: P026453.BL01 Activity: SUB-1260
Prepare & Submit Steel Curb Facing Shop Drawing
Project: P026453.BL01 Activity: SUB-1270
Prepare & Submit Asphaltic Concrete Paving
Project: P026453.BL01 Activity: SUB-1280
Prepare & Submit SSDS Geotextile
Project: P026453.BL01 Activity: SUB-1290
Prepare & Submit Gas Vapor Barrier Submittal & Inspection Schedule
Project: P026453.BL01 Activity: SUB-1300
Prepare & Submit Existing Conditions Survey
Project: P026453.BL01 Activity: SUB-1310
Prepare & Submit Training Outline & Schedule
Project: P026453.BL01 Activity: SUB-1320
Prepare & Submit Product Substitutions
Project: P026453.BL01 Activity: SUB-1330
Prepare & Submit Temporary Ventilation Plan
Project: P026453.BL01 Activity: SUB-1340
Prepare & Submit Construction Indoor Air Quality Management Plan
Project: P026453.BL01 Activity: SUB-1350
Prepare & Submit Site Safety Plan

Project: P026453.BL01 Activity: SUB-1360
Prepare & Submit CWM Plan
Project: P026453.BL01 Activity: SUB-1370
Prepare & Submit Photo Submission - Temporary Fence
Project: P026453.BL01 Activity: SUB-1380
Prepare & Submit Heating Plan
Project: P026453.BL01 Activity: SUB-1390
Prepare & Submit Sample Classroom Materials
Project: P026453.BL01 Activity: SUB-1400
Prepare & Submit Sustainable Materials
Project: P026453.BL01 Activity: SUB-1410
Prepare & Submit Submittal Schedule
Project: P026453.BL01 Activity: SUB-1420
Prepare & Submit Electrical Shop Drawings
Project: P026453.BL01 Activity: SUB-1430
Prepare & Submit Plumbing Shop Drawings
Project: P026453.BL01 Activity: SUB-1440
Prepare & Submit Sprinkler System Shop Drawings
Project: P026453.BL01 Activity: SUB-1450
Prepare & Submit Concrete Shop Drawings
Project: P026453.BL01 Activity: SUB-1460
Prepare & Submit Elevator Machine
Project: P026453.BL01 Activity: SUB-1470
Prepare & Submit Gypsum Board
Project: P026453.BL01 Activity: SUB-1480
Prepare & Submit Floorings
Project: P026453.BL01 Activity: SUB-1490
Prepare & Submit Acosutical Ceiling Tiles
Project: P026453.BL01 Activity: SUB-1500
Prepare & Submit Toilet Accessories
Project: P026453.BL01 Activity: SUB-1510
Prepare & Submit Millwork
Project: P026453.BL01 Activity: SUB-1520
Prepare & Submit Lighting Fixtures
Project: P026453.BL01 Activity: SUB-1530
Prepare & Submit Furniture
Project: P026453.BL01 Activity: SUB-1540
Prepare & Submit Mechanical Ducts
Project: P026453.BL01 Activity: SUB-1550
Prepare & Submit Mechanical Piping
Project: P026453.BL01 Activity: SUB-1560
Prepare & Submit Erosion Control and Sedimentation Plan
Project: P026453.BL01 Activity: SUB-1570
Prepare & Submit QCP
Project: P026453.BL01 Activity: SUB-1580
Prepare & Submit Concrete Mix Design
Project: P026453.BL01 Activity: SUB-1590
Prepare & Submit Electrical Equipment, Conduits, and Cables
Project: P026453.BL01 Activity: SUB-1600
Prepare & Submit Plumbing Fixtures

Project: P026453.BL01 Activity: SUB-1610
Prepare & Submit Baseline Schedule
Project: P026453.BL01 Activity: SUB-1620
Prepare & Submit Wood Doors
Project: P026453.BL01 Activity: SUB-1630
Prepare & Submit Fire Protection Shop Drawings
Project: P026453.BL01 Activity: SUB-1640
Prepare & Submit Fire Detectors & Alarms
Project: P026453.BL01 Activity: SUB-1650
Prepare & Submit Kitchen Equipment
Project: P026453.BL01 Activity: SUB-1660
Prepare & Submit Signs
Project: P026453.BL01 Activity: SUB-1670
Prepare & Submit Aluminum Projected Windows
Project: P026453.BL01 Activity: SUB-1680
Prepare & Submit Telecommunication System Drawings
Project: P026453.BL01 Activity: SUB-1690
Prepare & Submit Internet Protocol Digital Video Surveillance System using Digital Cameras
Project: P026453.BL01 Activity: SUB-1700
Prepare & Submit Roof Dunnage
Project: P026453.BL01 Activity: SUB-1710
Prepare & Submit Chillers Product Data
Project: P026453.BL01 Activity: SUB-1720
Prepare & Submit Air Handling Units Product Data
Project: P026453.BL01 Activity: SUB-1730
Prepare & Submit Boilers
Project: P026453.BL01 Activity: SUB-1740
Prepare & Submit Emergency Generator System Product Data
Project: P026453.BL01 Activity: SUB-1750
Prepare & Submit Switch Gears Product Data
Project: P026453.BL01 Activity: SUB-1760
Prepare & Submit Unit Cabinet Heaters
Project: P026453.BL01 Activity: SUB-1770
Prepare & Submit Gymnasium Equipment
Project: P026453.BL01 Activity: SUB-1780
Prepare & Submit Initial Underground Coordination Drawings
Project: P026453.BL01 Activity: SUB-1790
Prepare & Submit Initial 1st Floor MEP Coordination Drawings
Project: P026453.BL01 Activity: SUB-1800
Prepare & Submit Initial 2nd Floor MEP Coordination Drawings
Project: P026453.BL01 Activity: SUB-1810
Prepare & Submit Initial 3rd Floor MEP Coordination Drawings
Project: P026453.BL01 Activity: SUB-1820
Prepare & Submit Initial 4th Floor MEP Coordination Drawings
Project: P026453.BL01 Activity: SUB-1830
Prepare & Submit Initial 5th Floor MEP Coordination Drawings
Project: P026453.BL01 Activity: SUB-1840
Prepare & Submit Supplemental Comissioning Requirements
Project: P026453.BL01 Activity: SUB-1850

Prepare & Submit Record Documents
Project: P026453.BL01 Activity: SUB-1860
Prepare & Submit Environmental Site Assessment Reports
Project: P026453.BL01 Activity: SUB-1870
Prepare & Submit Selective Removals & Demoloition
Project: P026453.BL01 Activity: SUB-1880
Prepare & Submit Foundation Product Data
Project: P026453.BL01 Activity: SUB-1890
Prepare & Submit Trench Drains Product Data
Project: P026453.BL01 Activity: SUB-1900
Prepare & Submit Chain Link Fences & Gates Drawings
Project: P026453.BL01 Activity: SUB-1910
Prepare & Submit Outdoor Game Equipment
Project: P026453.BL01 Activity: SUB-1920
Prepare & Submit Precast Architectural Concrete
Project: P026453.BL01 Activity: SUB-1930
Prepare & Submit Unit Masonry Product Data
Project: P026453.BL01 Activity: SUB-1940
Prepare & Submit Cast Stone Product Data
Project: P026453.BL01 Activity: SUB-1950
Prepare & Submit Structure Steel Drawings
Project: P026453.BL01 Activity: SUB-1960
Prepare & Submit Metal Deck Product Data
Project: P026453.BL01 Activity: SUB-1970
Prepare & Submit Prefabricated Expansion Joint Covers
Project: P026453.BL01 Activity: SUB-1980
Prepare & Submit Self Adhering Sheet Air Barriers
Project: P026453.BL01 Activity: SUB-1990
Prepare & Submit Metal Plate Wall Panels
Project: P026453.BL01 Activity: SUB-2000
Prepare & Submit Security Screens & Barriers
Project: P026453.BL01 Activity: SUB-2010
Prepare & Submit Wood Flooring
Project: P026453.BL01 Activity: SUB-2020
Prepare & Submit Visual Display Boards
Project: P026453.BL01 Activity: SUB-2030
Prepare & Submit Metal Lockers
Project: P026453.BL01 Activity: SUB-2040
Prepare & Submit Fire Extinguishers & Cabinets
Project: P026453.BL01 Activity: SUB-2050
Prepare & Submit Stationary Metal Wall Louvers
Project: P026453.BL01 Activity: SUB-2060
Prepare & Submit Library Equipment
Project: P026453.BL01 Activity: SUB-2070
Prepare & Submit Platform Curtains & Auditorium Window Curtains
Project: P026453.BL01 Activity: SUB-2080
Prepare & Submit Waste Handling Equipment
Project: P026453.BL01 Activity: SUB-2090
Prepare & Submit Domestic Equipment
Project: P026453.BL01 Activity: SUB-2100

Prepare & Submit Laboratory Equipment
Project: P026453.BL01 Activity: SUB-2110
Prepare & Submit Manufactured Wood Casework
Project: P026453.BL01 Activity: SUB-2120
Prepare & Submit Concrete Floating Floor Assembly
Project: P026453.BL01 Activity: SUB-2130
Prepare & Submit Hydraulic Vertical Wheelchair Lifts
Project: P026453.BL01 Activity: SUB-2140
Prepare & Submit Switch & Panel Boards
Project: P026453.BL01 Activity: SUB-2150
Prepare & Submit Auditorium & Television Studio Dimming System Product Data
Project: P026453.BL01 Activity: SUB-2160
Prepare & Submit Overcurrent Protective Devices Data
Project: P026453.BL01 Activity: SUB-2170
Prepare & Submit Gas Pipes
Project: P026453.BL01 Activity: SUB-2180
Prepare & Submit Water Heaters
Project: P026453.BL01 Activity: SUB-2190
Prepare & Submit Pumping Apparatus & Tanks
Project: P026453.BL01 Activity: SUB-2200
Prepare & Submit HVAC Pumps
Project: P026453.BL01 Activity: SUB-2210
Prepare & Submit Emergency Generator System Accessories
Project: P026453.BL01 Activity: SUB-2220
Prepare & Submit Fuel Storage Equipment
Project: P026453.BL01 Activity: SUB-2230
Prepare & Submit Natural Gas Leak Detection Equipment
Project: P026453.BL01 Activity: SUB-2250
Prepare & Submit Temperature Control System
Project: P026453.BL01 Activity: SUB-2260
Prepare & Submit Air Outlets & Inlets
Project: P026453.BL01 Activity: SUB-2270
Prepare & Submit Final Underground Coordination Drawings
Project: P026453.BL01 Activity: SUB-2280
Prepare & Submit Final 1st Floor Coordination Drawings
Project: P026453.BL01 Activity: SUB-2290
Prepare & Submit Final 2nd Floor Coordination Drawings
Project: P026453.BL01 Activity: SUB-2300
Prepare & Submit Final 3rd Floor Coordination Drawings
Project: P026453.BL01 Activity: SUB-2310
Prepare & Submit Final 4th Floor Coordination Drawings
Project: P026453.BL01 Activity: SUB-2320
Prepare & Submit Final 5th Floor Coordination Drawings
Project: P026453.BL01 Activity: SUB-2330
Prepare & Submit Remedial Closure Report
Project: P026453.BL01 Activity: SUB-2340
Prepare & Submit Tree Protection Plan
Project: P026453.BL01 Activity: SUB-2360
Prepare & Submit Adjacent Property and Structures Protection & Monitoring Plan
Project: P026453.BL01 Activity: SUB-2370

Prepare & Submit Ornamenta Metal Shop Drawings
Project: P026453.BL01 Activity: SUB-2900
Prepare & Submit Excavated Material Disposal Plan
Project: P026453.BL01 Activity: SUB-2910
Prepare & Submit Backfill & Resue Plan
Project: P026453.BL01 Activity: SUB-2920
Prepare & Submit Documentation of Proper Disposal
Project: P026453.BL01 Activity: SUB-2930
Prepare & Submit Ornamenta Metal Product Data
Project: P026453.BL01 Activity: SUB-2960
Prepare & Submit Coiling Doors, Grilles and Shutters Shop Drawings
Project: P026453.BL01 Activity: SUB-2970
Prepare & Submit Coiling Doors, Grilles and Shutters Product Data
Project: P026453.BL01 Activity: SUB-2980
Prepare & Submit Aluminum Framed Entrances & Storefronts Shop Drawings
Project: P026453.BL01 Activity: SUB-2990
Prepare & Submit Aluminum Framed Entrances & Storefronts Product Data
Project: P026453.BL01 Activity: SUB-3000
Prepare & Submit Thresholds, Weatherstripping and Seals Color Samples
Project: P026453.BL01 Activity: SUB-3010
Prepare & Submit Thresholds, Weatherstripping and Seals Product Data
Project: P026453.BL01 Activity: SUB-3020
Prepare & Submit Miscellaneous Glazing Samples
Project: P026453.BL01 Activity: SUB-3030
Prepare & Submit Miscellaneous Glazing Product Data
Project: P026453.BL01 Activity: SUB-3040
Prepare & Submit Fire Rated Glazing Samples
Project: P026453.BL01 Activity: SUB-3050
Prepare & Submit Fire Rated Glazing Product Data
Project: P026453.BL01 Activity: SUB-3060
Prepare & Submit Graffiti Resistant Coating Product Data
Project: P026453.BL01 Activity: SUB-3070
Prepare & Submit Special Coating Samples
Project: P026453.BL01 Activity: SUB-3080
Prepare & Submit Special Coating Product Data
Project: P026453.BL01 Activity: SUB-3090
Prepare & Submit Flagpole Shop Drawing
Project: P026453.BL01 Activity: SUB-3100
Prepare & Submit Flagpole Product Data
Project: P026453.BL01 Activity: SUB-3110
Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Sustainability Submittals
Project: P026453.BL01 Activity: SUB-3120
Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Shop Drawings
Project: P026453.BL01 Activity: SUB-3130
Prepare & Submit Bulletin Boards, Glazed Display Boards, Display Cabinets & Cases Samples
Project: P026453.BL01 Activity: SUB-3140
Prepare & Submit Wire Mesh Work Samples

Project: P026453.BL01 Activity: SUB-3150
Prepare & Submit Wire Mesh Work Shop drawings
Project: P026453.BL01 Activity: SUB-3160
Prepare & Submit Metal Storage Shelving Samples
Project: P026453.BL01 Activity: SUB-3170
Prepare & Submit Metal Storage Shelving Shop drawings
Project: P026453.BL01 Activity: SUB-3180
Prepare & Submit Mirrors Shop Drawing
Project: P026453.BL01 Activity: SUB-3190
Prepare & Submit Mirrors Product Data
Project: P026453.BL01 Activity: SUB-3200
Prepare & Submit Mirrors Mastic Compatibility Test Reports & Certifications
Project: P026453.BL01 Activity: SUB-3210
Prepare & Submit Grab Bars Shop Drawing
Project: P026453.BL01 Activity: SUB-3220
Prepare & Submit Grab Bars Product Data
Project: P026453.BL01 Activity: SUB-3230
Prepare & Submit Shop Equipment Shop Drawing
Project: P026453.BL01 Activity: SUB-3240
Prepare & Submit Shop Equipment Product Data
Project: P026453.BL01 Activity: SUB-3250
Prepare & Submit Bleachers Shop Drawing
Project: P026453.BL01 Activity: SUB-3260
Prepare & Submit Bleachers Product Data
Project: P026453.BL01 Activity: SUB-3270
Prepare & Submit Bleachers Manufacturer's Warranty
Project: P026453.BL01 Activity: SUB-3280
Prepare & Submit Valves Shop Drawing
Project: P026453.BL01 Activity: SUB-3290
Prepare & Submit Valves Product Data
Project: P026453.BL01 Activity: SUB-3300
Prepare & Submit Certification of Tests
Project: P026453.BL01 Activity: SUB-3310
Prepare & Submit Domestic Water Sterilization Plan
Project: P026453.BL01 Activity: SUB-3320
Prepare & Submit Tags, Charts & Identifications Shop Drawing
Project: P026453.BL01 Activity: SUB-3330
Prepare & Submit Tags, Charts & Identifications Product Data
Project: P026453.BL01 Activity: SUB-3340
Prepare & Submit Micselianeous Shop Drawing
Project: P026453.BL01 Activity: SUB-3350
Prepare & Submit Valves (HVAC) Shop Drawing
Project: P026453.BL01 Activity: SUB-3360
Prepare & Submit Valves (HVAC) Product Data
Project: P026453.BL01 Activity: SUB-3370
Prepare & Submit Piping Insulation Schedule Listing Items
Project: P026453.BL01 Activity: SUB-3380
Prepare & Submit Schedules Showing Manfacturers's Product Number Equipment Insulation (HVAC)
Project: P026453.BL01 Activity: SUB-3390

Prepare & Submit Schedules Showing Manfacturers's Product Number Duct Work Insulation
Project: P026453.BL01 Activity: SUB-3400
Prepare & Submit Hydronic Specialities Shop Drawing
Project: P026453.BL01 Activity: SUB-3410
Prepare & Submit Hydronic Specialities Product Data
Project: P026453.BL01 Activity: SUB-3420
Prepare & Submit Water Treatment Firm
Project: P026453.BL01 Activity: SUB-3430
Prepare & Submit Chemical Products Product Data
Project: P026453.BL01 Activity: SUB-3440
Prepare & Submit Detail of Gag for the Safety Relief Valves
Project: P026453.BL01 Activity: SUB-3450
Prepare & Submit Boiler Accessories Maintenance Data
Project: P026453.BL01 Activity: SUB-3460
Prepare & Submit Breeching Chimney Connectors and Chimneys Shop Drawing
Project: P026453.BL01 Activity: SUB-3470
Prepare & Submit Manfacturer's 10 Years Warranty for Condensing Boilers Double Wall Metal Chimneys
Project: P026453.BL01 Activity: SUB-3480
Prepare & Submit Plate Heat Exchanger Maintenance Data
Project: P026453.BL01 Activity: SUB-3490
Prepare & Submit Plate Heat Exchanger Product Data
Project: P026453.BL01 Activity: SUB-3500
Prepare & Submit Coils Maintenance Data
Project: P026453.BL01 Activity: SUB-3510
Prepare & Submit Coils Certifications
Project: P026453.BL01 Activity: SUB-3520
Prepare & Submit Convectors Shop Drawing
Project: P026453.BL01 Activity: SUB-3530
Prepare & Submit Convectors Product Data
Project: P026453.BL01 Activity: SUB-3540
Prepare & Submit Fan Coils Units Maintenance Data & Materials
Project: P026453.BL01 Activity: SUB-3550
Prepare & Submit Fan Coils Units Shop Drawings
Project: P026453.BL01 Activity: SUB-3560
Prepare & Submit Door Air Curtains Shop Drawing
Project: P026453.BL01 Activity: SUB-3570
Prepare & Submit Door Air Curtains Product Data
Project: P026453.BL01 Activity: SUB-3580
Prepare & Submit Centrifugal Fans Shop Drawing
Project: P026453.BL01 Activity: SUB-3590
Prepare & Submit Centrifugal Fans Product Data
Project: P026453.BL01 Activity: SUB-3600
Prepare & Submit Centrifugal Fans Maintenance Data & Materials
Project: P026453.BL01 Activity: SUB-3610
Prepare & Submit Air Filters Shop Drawing
Project: P026453.BL01 Activity: SUB-3620
Prepare & Submit Air Filters Product Data
Project: P026453.BL01 Activity: SUB-3630

Prepare & Submit Air Filters Maintenance Data & Materials
Project: P026453.BL01 Activity: SUB-3640
Prepare & Submit Duct Accessories Shop Drawing
Project: P026453.BL01 Activity: SUB-3650
Prepare & Submit Damper Assemblies Shop Drawing
Project: P026453.BL01 Activity: SUB-3660
Prepare & Submit Damper Assemblies Product Data
Project: P026453.BL01 Activity: SUB-3670
Prepare & Submit Damper Assemblies Maintenance Data & Materials
Project: P026453.BL01 Activity: SUB-3680
Prepare & Submit Variable Air Terminals Shop Drawing
Project: P026453.BL01 Activity: SUB-3690
Prepare & Submit Variable Air Terminals Product Data
Project: P026453.BL01 Activity: SUB-3700
Prepare & Submit Variable Air Terminals Maintenance Data & Materials
Project: P026453.BL01 Activity: SUB-3710
Prepare & Submit AHU for Public Assemblies Sapces Shop Drawing
Project: P026453.BL01 Activity: SUB-3720
Prepare & Submit AHU for Public Assemblies Sapces Product Data
Project: P026453.BL01 Activity: SUB-3730
Prepare & Submit AHU for Public Assemblies Sapces Maintenance Data & Materials
Project: P026453.BL01 Activity: SUB-3740
Prepare & Submit Control Systems Shop Drawing
Project: P026453.BL01 Activity: SUB-3750
Prepare & Submit Truck Network Cable Schematic Diagram
Project: P026453.BL01 Activity: SUB-3760
Prepare & Submit Lighting Control Devices Shop Drawing
Project: P026453.BL01 Activity: SUB-3770
Prepare & Submit Lighting Control Devices Product Data
Project: P026453.BL01 Activity: SUB-3780
Prepare & Submit Lighting Control Devices Warranty
Project: P026453.BL01 Activity: SUB-3790
Prepare & Submit Surge Protective Devices Shop Drawing
Project: P026453.BL01 Activity: SUB-3800
Prepare & Submit Surge Protective Devices Product Data
Project: P026453.BL01 Activity: SUB-3810
Prepare & Submit Surge Protective Devices Warranty
Project: P026453.BL01 Activity: SUB-3820
Prepare & Submit Service Entrance Equipment Shop Drawing
Project: P026453.BL01 Activity: SUB-3830
Prepare & Submit Service Entrance Equipment Product Data
Project: P026453.BL01 Activity: SUB-3840
Prepare & Submit Service Entrance Equipment Warranty
Project: P026453.BL01 Activity: SUB-3850
Prepare & Submit Enclosed Switches Product Data
Project: P026453.BL01 Activity: SUB-3860
Prepare & Submit Enclosed Switches Test Reports
Project: P026453.BL01 Activity: SUB-3870
Prepare & Submit Motors, Motor Control Centers and Starters Shop Drawing
Project: P026453.BL01 Activity: SUB-3880

Prepare & Submit Motors, Motor Control Centers and Starters Product Data
Project: P026453.BL01 Activity: SUB-3890
Prepare & Submit Motors, Motor Control Centers and Starters Field Test Reports
Project: P026453.BL01 Activity: SUB-3900
Prepare & Submit Lightning Protection Shop Drawing
Project: P026453.BL01 Activity: SUB-3920
Prepare & Submit Lightning Protection Test Reports
Project: P026453.BL01 Activity: SUB-3930
Prepare & Submit Fiber Optic Cabling system Shop Drawing
Project: P026453.BL01 Activity: SUB-3940
Prepare & Submit Fiber Optic Cabling system Product Data
Project: P026453.BL01 Activity: SUB-3950
Prepare & Submit Fiber Optic Cabling system Samples
Project: P026453.BL01 Activity: SUB-3960
Prepare & Submit Sound, Intercome & Security System Shop Drawing
Project: P026453.BL01 Activity: SUB-3970
Prepare & Submit Sound, Intercome & Security System Programming Code and Password for the System
Project: P026453.BL01 Activity: SUB-3980
Prepare & Submit Sound, Intercome & Security System Warranty
Project: P026453.BL01 Activity: SUB-3990
Prepare & Submit Projection and Interactive Whiteboard Systems Shop Drawing and Catalog Cuts
Project: P026453.BL01 Activity: SUB-4000
Prepare & Submit Projection and Interactive Whiteboard Systems Wiring diagram
Project: P026453.BL01 Activity: SUB-4010
Prepare & Submit Self Corrective Clock System Shop Drawing
Project: P026453.BL01 Activity: SUB-4020
Prepare & Submit Self Corrective Clock System Product Data
Project: P026453.BL01 Activity: SUB-4030
Prepare & Submit Self Corrective Clock System Field Test Reports
Project: P026453.BL01 Activity: SUB-4040
Prepare & Submit Heat Trace Cable System Wiring Diagram, Dimensional and Descriptive Drawings
Project: P026453.BL01 Activity: SUB-4050
Prepare & Submit Soil Sampling Plan
Project: P026453.BL01 Activity: SUB-4060
Prepare & Submit Steel Stairs Shop Drawings
Project: P026453.BL01 Activity: SUB-4070
Prepare & Submit Steel Stairs Product Data
Project: P026453.BL01 Activity: SUB-4080
Prepare & Submit Green School Submittal
