


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
BROOKLYN ANIMAL CARE CENTER - SCHEDULE Update 23			68.86%	274	28-Jul-23 A	17-Dec-26	17-Dec-26	1	
CONTRACTUAL & NON CONTRACTUAL MILESTONES			68.99%	382	04-Aug-23 A	17-Dec-26	17-Dec-26	2	
ML1000	Notice to Proceed	100%	100%	0	04-Aug-23 A				PRO-01-1000, PRO-06-
ML1020	Project Duration	0%	53.3%	382	04-Aug-23 A	17-Dec-26	17-Dec-26	2	ML3000
ML3010	DDC Personnel Vacant Existing Property	100%	100%	0	04-Aug-23 A	09-Aug-24 A	01-Nov-25		ML3030
ML3030	DDC Personnel Vacant Existing Property Milestone	100%	100%	0		09-Aug-24 A			PRE-1050, PRE-1040A,
ML1010	Start Construction	100%	100%	0	12-Aug-24 A				CONS-FOUN-1010
ML2000	Substantial Completion 18-Sep-26	0%	0%	0		18-Sep-26*	18-Sep-26	0	CONS-CLOS-1000, COI
ML3000	Final Completion Certificate of Occupancy19-Nov-26	0%	0%	0		17-Dec-26*	17-Dec-26	2	
PROCUREMENT			81.78%	135	04-Aug-23 A	05-Jun-26	20-Jul-26	119	
DIVISION 1 - GENERAL REQUIREMENTS			98.36%	6	04-Aug-23 A	08-Dec-25	10-Nov-25	189	
GUARANTEES, WARRANTIES & BONDS			100%	0	04-Aug-23 A	31-Aug-23 A	01-Nov-25		
PRO-01-1160	Prepare and submit bonds and insurance	100%	100%	0	04-Aug-23 A	31-Aug-23 A	01-Nov-25		PRE-1080, PR0-01-100
SUBCONTRACTOR "BUYOUT"			100%	0	04-Aug-23 A	16-May-25 A	01-Nov-25		
PR0-01-1110	Submit asbestos abatement subcontractor	100%	100%	0	04-Aug-23 A	31-Aug-23 A	01-Nov-25		PR0-01-1150, PRO-02-1
PR0-01-1000	Submit electrical subcontractor	100%	100%	0	01-Sep-23 A	28-Sep-23 A	01-Nov-25		PR0-01-1120
PR0-01-1010	Submit mechanical subcontractor	100%	100%	0	01-Sep-23 A	21-Sep-23 A	01-Nov-25		PR0-01-1160
PR0-01-1020	Submit plumbing subcontractor	100%	100%	0	01-Sep-23 A	22-Sep-23 A	01-Nov-25		PR0-01-1130
PR0-01-1040	Submit painting subcontractor	100%	100%	0	01-Sep-23 A	10-Oct-24 A	01-Nov-25		PR0-01-1220
PR0-01-1060	Submit roofer subcontractor	100%	100%	0	01-Sep-23 A	09-Feb-24 A	01-Nov-25		PR0-01-1200
PR0-01-1070	Submit steel subcontractor	100%	100%	0	01-Sep-23 A	27-Sep-23 A	01-Nov-25		PR0-01-1170
PR0-01-1080	Submit carpenter subcontractor	100%	100%	0	01-Sep-23 A	26-Sep-23 A	01-Nov-25		PR0-01-1190
PR0-01-1100	Submit elevator subcontractor	100%	100%	0	01-Sep-23 A	12-Oct-23 A	01-Nov-25		PR0-01-1180
PR0-01-1150	Approve asbestos abatement subcontractor	100%	100%	0	01-Sep-23 A	16-Nov-23 A	01-Nov-25		CONS-MEP-1030
PR0-01-1230	Submit hvac subcontractor	100%	100%	0	01-Sep-23 A	21-Sep-23 A	01-Nov-25		PR0-01-1240
PR0-01-1160	Approve mechanical subcontractor	100%	100%	0	22-Sep-23 A	05-Dec-23 A	01-Nov-25		PRO-23-1000, PRO-23-
PR0-01-1240	Approve hvac subcontractor	100%	100%	0	22-Sep-23 A	12-Jan-24 A	01-Nov-25		PRO-23-1000, PRO-23-
PR0-01-1130	Approve plumbing subcontractor	100%	100%	0	25-Sep-23 A	12-Jan-24 A	01-Nov-25		PRO-21-1000, PRO-21-
PR0-01-1190	Approve carpenter subcontractor	100%	100%	0	27-Sep-23 A	22-Feb-24 A	01-Nov-25		PRO-06-1020, PRO-06-
PR0-01-1170	Approve steel subcontractor	100%	100%	0	28-Sep-23 A	28-Feb-24 A	01-Nov-25		PRO-05-1150, PRO-05-
PR0-01-1120	Approve electrical subcontractor	100%	100%	0	29-Sep-23 A	09-Nov-23 A	01-Nov-25		PRO-26-1050, PRO-26-
PR0-01-1180	Approve elevator subcontractor	100%	100%	0	13-Oct-23 A	16-Jan-24 A	01-Nov-25		PRO-14-1000, PRO-14-
PR0-01-1200	Approve roofer subcontractor	100%	100%	0	12-Feb-24 A	12-Mar-24 A	01-Nov-25		PR0-07-1090, PR0-07-1
PR0-01-1241	Submit Environomental Consultant	100%	100%	0	20-Feb-24 A	19-Mar-24 A	01-Nov-25		PR0-01-1242
PR0-01-1242	Rejected Environomental Consultant	100%	100%	0	20-Mar-24 A	20-Jun-24 A	01-Nov-25		PR0-01-1243
PR0-01-1243	Re-Submit Environomental Consultant	100%	100%	0	21-Mar-24 A	28-Jun-24 A	01-Nov-25		PR0-01-1244
PR0-01-1249	Submit Trucker for Contaminated Soils	100%	100%	0	02-Apr-24 A	02-Apr-24 A	01-Nov-25		PR0-01-1254
PR0-01-1254	Approve Trucker for Contaminated Soils	100%	100%	0	03-Apr-24 A	16-May-25 A	01-Nov-25		CONS-EB-6345
PR0-01-1244	Approve Environomental Consultant	100%	100%	0	01-Jul-24 A	14-Mar-25 A	01-Nov-25		PRO-02-1080
PR0-01-1220	Approve painting subcontractor	100%	100%	0	11-Oct-24 A	07-Apr-25 A	01-Nov-25		CONS-EB-2240
013216.10 - PROJECT SCHEDULES			100%	0	04-Aug-23 A	19-Jan-24 A	01-Nov-25		
PRO-01-1000	Prepare and submit preliminary schedule R0	100%	100%	0	04-Aug-23 A	01-Sep-23 A	01-Nov-25		PRO-01-1010, PRO-01-
PRO-01-1020	Review and approve preliminary schedule	100%	100%	0	05-Sep-23 A	07-Sep-23 A	01-Nov-25		PRO-01-1010
PRO-01-1001	Returned preliminary schedule R0	100%	100%	0	05-Sep-23 A	07-Sep-23 A	01-Nov-25		PRO-01-1002
PRO-01-1002	Re-submit baseline schedule R1	100%	100%	0	12-Sep-23 A	12-Sep-23 A	01-Nov-25		PRO-01-1003
PRO-01-1003	Returned preliminary schedule R1	100%	100%	0	13-Sep-23 A	13-Sep-23 A	01-Nov-25		PRO-01-1004
PRO-01-1004	Re-submit baseline schedule R2	100%	100%	0	14-Sep-23 A	02-Oct-23 A	01-Nov-25		PRO-01-1005
PRO-01-1005	Returned preliminary schedule R2	100%	100%	0	03-Oct-23 A	10-Oct-23 A	01-Nov-25		PRO-01-1006
PRO-01-1006	Re-submit baseline schedule R3	100%	100%	0	27-Oct-23 A	27-Oct-23 A	01-Nov-25		PRO-01-1007
PRO-01-1007	Returned preliminary schedule R3	100%	100%	0	30-Oct-23 A	10-Nov-23 A	01-Nov-25		PRO-01-1008

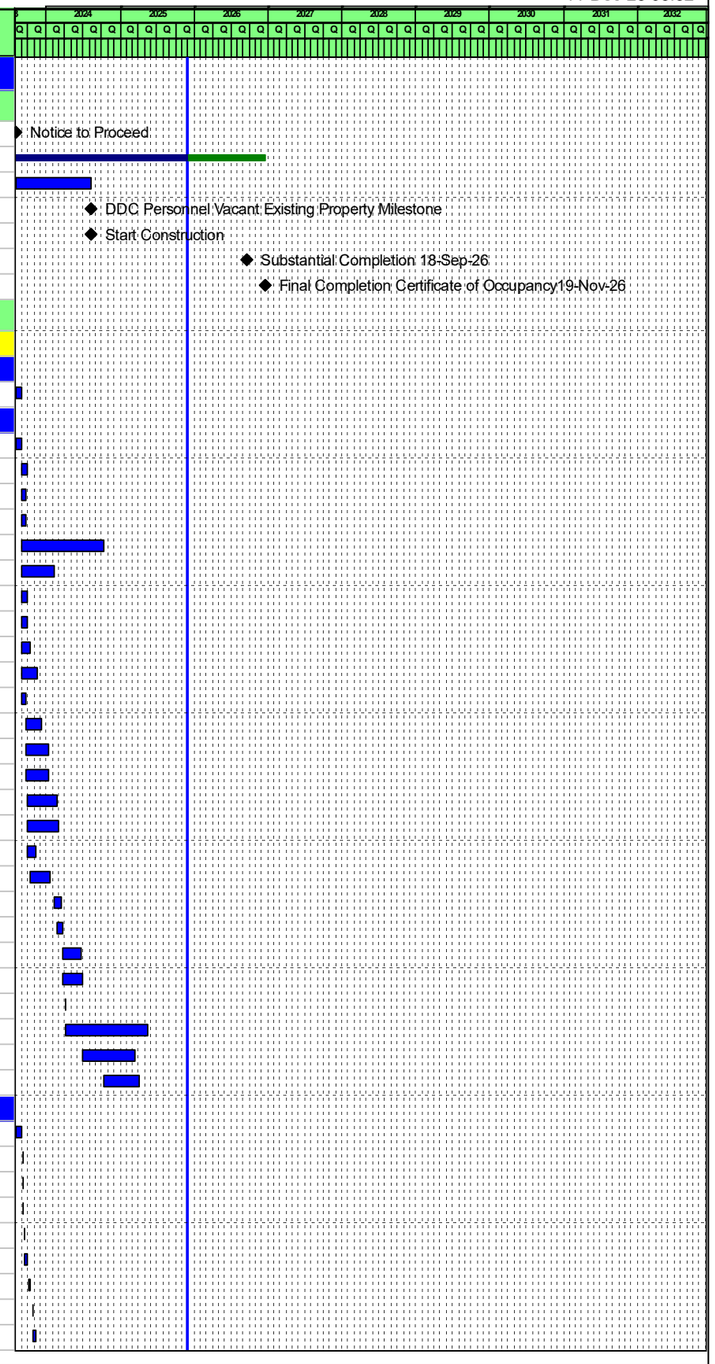


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PRO-01-1008	Re-submit baseline schedule R4	100%	100%	0	13-Nov-23 A	05-Dec-23 A	01-Nov-25		PRO-01-1010
PRO-01-1010	Prepare and submit baseline schedule R5	100%	100%	0	06-Dec-23 A	29-Dec-23 A	01-Nov-25		PRO-01-1030
PRO-01-1030	Review and approve baseline schedule R5	100%	100%	0	02-Jan-24 A	19-Jan-24 A	01-Nov-25		CONS-FOUN-1010
013526 - SAFETY REQUIREMENTS			100%	0	04-Aug-23 A	06-Sep-24 A	01-Nov-25		
PRO-01-1040	Prepare and submit safety program R0	100%	100%	0	04-Aug-23 A	30-Aug-23 A	01-Nov-25		PRO-01-1041
PRO-01-1185	Prepare and submit DDC Online safety program R0	100%	100%	0	04-Aug-23 A	03-Oct-23 A	01-Nov-25		PRO-01-1190
PRO-01-1041	Re-submit safety program R0	100%	100%	0	31-Aug-23 A	19-Apr-24 A	01-Nov-25		PRO-01-1042
PRO-01-1190	DDC Return Online safety program R0	100%	100%	0	04-Oct-23 A	19-Jan-24 A	01-Nov-25		PRO-01-1195
PRO-01-1195	Re-submit DDC Online safety program R1	100%	100%	0	22-Jan-24 A	02-Feb-24 A	01-Nov-25		PRO-01-1200
PRO-01-1200	DDC Return Online safety program R1	100%	100%	0	05-Feb-24 A	14-Mar-24 A	01-Nov-25		PRO-01-1205
PRO-01-1205	Re-submit DDC Online safety program R2	100%	100%	0	15-Mar-24 A	27-Mar-24 A	01-Nov-25		PRO-01-1210
PRO-01-1210	DDC Approve Online safety program R2	100%	100%	0	28-Mar-24 A	15-Apr-24 A	01-Nov-25		PRE-1080, PRE-1090, F
PRO-01-1211	DDC Advises not to resubmit Online safety program until JHAs' are approved	100%	100%	0	15-Apr-24 A	15-Apr-24 A	01-Nov-25		PRO-01-1212
PRO-01-1212	MPCC Submits revised JHAs' for approval	100%	100%	0	15-Apr-24 A	15-Apr-24 A	01-Nov-25		PRO-01-1213
PRO-01-1213	CM Returns revised JHAs' for resubmisson	100%	100%	0	16-Apr-24 A	23-Apr-24 A	01-Nov-25		PRO-01-1214
PRO-01-1042	Re-submit safety program R1	100%	100%	0	22-Apr-24 A	29-Apr-24 A	01-Nov-25		PRO-01-1050
PRO-01-1214	MPCC Re-Submits revised JHAs' for approval	100%	100%	0	24-Apr-24 A	29-Apr-24 A	01-Nov-25		PRO-01-1215
PRO-01-1215	CM Approves revised JHAs'	100%	100%	0	30-Apr-24 A	13-Jun-24 A	01-Nov-25		PRO-01-1220
PRO-01-1050	Review and approve safety program R1 (pred is PRO-01-1042)	100%	100%	0	30-Apr-24 A	15-Jul-24 A	01-Nov-25		PRE-1080
PRO-01-1220	Re-submit DDC Online safety program R3	100%	100%	0	14-Jun-24 A	14-Jun-24 A	01-Nov-25		PRO-01-1225
PRO-01-1225	DDC Returned Online safety program R3	100%	100%	0	17-Jun-24 A	19-Jul-24 A	01-Nov-25		PRE-1060, PRE-1080, F
PRO-01-1230	Re-submit DDC Online safety program R4	100%	100%	0	22-Jul-24 A	30-Aug-24 A	01-Nov-25		PRO-01-1235, CONS-S
PRO-01-1235	DDC Approve Online safety program R4	100%	100%	0	02-Sep-24 A	06-Sep-24 A	01-Nov-25		PRE-1060, PRE-1080, F
015000 - TEMPORARY FACILITIES, SERVICES AND CONTROLS			100%	0	04-Aug-23 A	18-Mar-24 A	01-Nov-25		
PRO-01-1080	Prepare and submit site plan (Fencing)	100%	100%	0	04-Aug-23 A	13-Sep-23 A	01-Nov-25		PRO-01-1090
PRO-01-1090	Review and approve site plan (Fencing)	100%	100%	0	14-Sep-23 A	18-Mar-24 A	01-Nov-25		PRE-1080, PRE-1170, C
017419 - CONSTRUCTION WASTE MANAGEMENT AND DISPOSAL			100%	0	04-Aug-23 A	08-Apr-24 A	01-Nov-25		
PRO-01-1140	Prepare and submit waste management plan R0	100%	100%	0	04-Aug-23 A	30-Aug-23 A	01-Nov-25		PRO-01-1141
PRO-01-1141	Review and approve waste management plan R0	100%	100%	0	31-Aug-23 A	27-Nov-23 A	01-Nov-25		PRO-01-1142
PRO-01-1142	Re-submit waste management plan R1	100%	100%	0	28-Nov-23 A	18-Mar-24 A	01-Nov-25		PRO-01-1150
PRO-01-1150	Approve waste management plan R0	100%	100%	0	19-Mar-24 A	08-Apr-24 A	01-Nov-25		PRE-1080
019117 BUILDING ENCLOSURE TESTING AGENT			97.45%	6	04-Aug-23 A	08-Dec-25	10-Nov-25	176	
PRO-01-1170	Prepare and submit Building Enclosure Testing Agent	100%	100%	0	04-Aug-23 A	18-Mar-24 A	01-Nov-25		PRO-01-1180
PRO-01-1180	Review and approve Building Enclosure Testing Agent	60%	60%	6	19-Mar-24 A	08-Dec-25	10-Nov-25	176	CONS-INSP-1005
DIVISION 2 - EXISTING CONDITIONS			100%	0	04-Aug-23 A	18-Apr-25 A	01-Nov-25		
026200 - ALLOWANCE FOR EXCAVATION AND DISPOSAL OF IMPACTED CONTAMINATED SOILS			100%	0	04-Aug-23 A	18-Apr-25 A	01-Nov-25		
PRO-02-1020	Prepare and submit material handling plan R0	100%	100%	0	04-Aug-23 A	27-Mar-24 A	01-Nov-25		PRO-02-1030, PRO-02-
PRO-02-1080	Prepare and submit excavation and disposal permits and certifications (impacted by Consultant approval)	100%	100%	0	04-Aug-23 A	28-Jan-25 A	01-Nov-25		PRO-02-1090, PRO-02-
PRO-02-1021	Returned material handling plan R0	100%	100%	0	28-Mar-24 A	15-May-24 A	01-Nov-25		PRO-02-1022
PRO-02-1022	Re-submit material handling plan R1	100%	100%	0	16-May-24 A	07-Jun-24 A	01-Nov-25		PRO-02-1030
PRO-02-1030	Review and approve material handling plan R1	100%	100%	0	10-Jun-24 A	12-Jul-24 A	01-Nov-25		CONS-EB-6545, CONS-
PRO-02-1081	Returned excavation and disposal permits and certifications R0	100%	100%	0	29-Jan-25 A	24-Feb-25 A	01-Nov-25		PRO-02-1082
PRO-02-1082	Re-submit excavation and disposal permits and certifications R1	100%	100%	0	25-Feb-25 A	25-Feb-25 A	01-Nov-25		PRO-02-1090
PRO-02-1090	Review and approve excavation and disposal permits and certifications R1 (tied to Site Clearing)	100%	100%	0	26-Feb-25 A	18-Apr-25 A	01-Nov-25		CONS-EB-1610, CONS-
DEMOLITION PLANS			100%	0	04-Aug-23 A	31-Aug-23 A	01-Nov-25		
PRE-1070	Preparation of Demolition Plans	100%	100%	0	04-Aug-23 A	15-Aug-23 A	01-Nov-25		PRE-1100
PRE-1100	Review Demolition Plans	100%	100%	0	16-Aug-23 A	24-Aug-23 A	01-Nov-25		PRE-1110
PRE-1110	Resubmit Demolition Plans	100%	100%	0	25-Aug-23 A	25-Aug-23 A	01-Nov-25		PRE-1140
PRE-1140	Approve Demolition Plans	100%	100%	0	28-Aug-23 A	31-Aug-23 A	01-Nov-25		PER-1030
028213 - ASBESTOS ABATEMENT			100%	0	31-Aug-23 A	13-Mar-24 A	01-Nov-25		
PRO-02-1120	Prepare and submit asbestos abatement work plan and schedules	100%	100%	0	31-Aug-23 A	31-Aug-23 A	01-Nov-25		PRO-02-1130

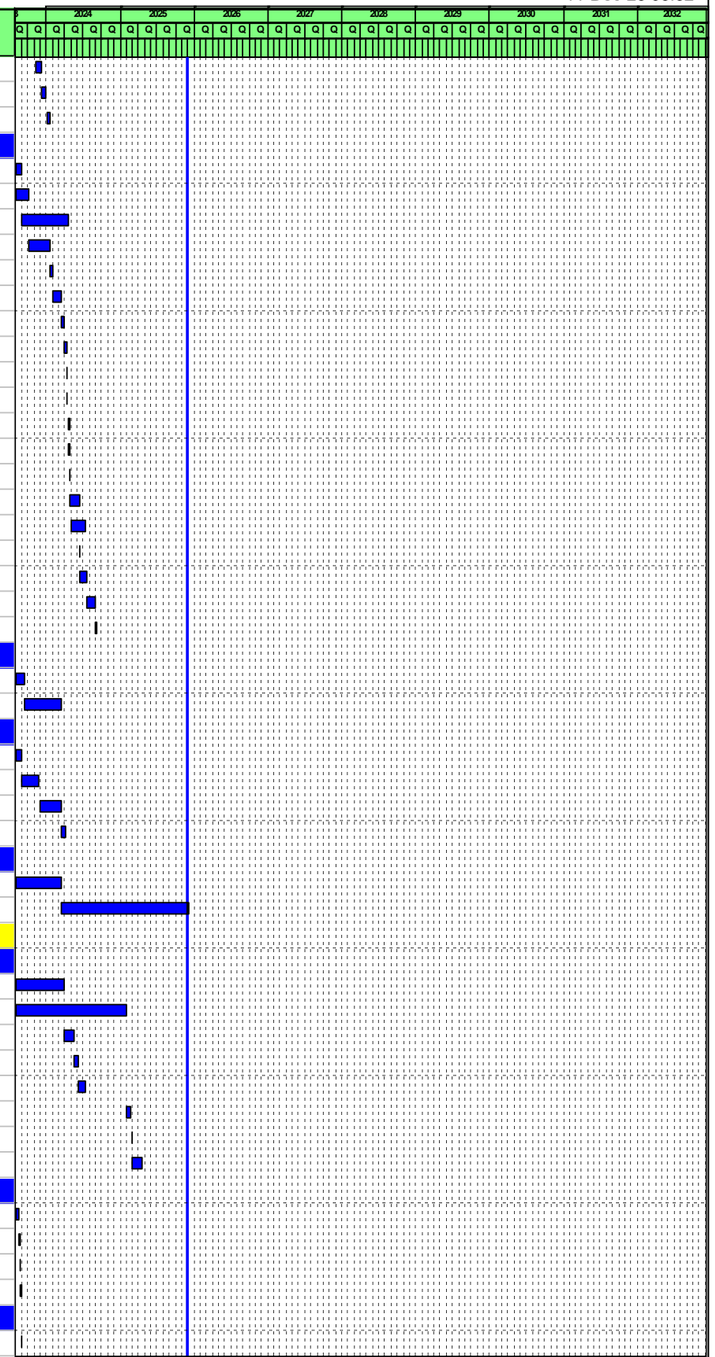


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PRO-02-1100	Prepare and submit asbestos abatement permits	100%	100%	0	31-Aug-23 A	15-Feb-24 A	01-Nov-25		PRO-02-1110
PRO-02-1130	Review and approve asbestos abatement work plan and schedules	100%	100%	0	01-Sep-23 A	06-Dec-23 A	01-Nov-25		ML1010, CONS-FOUN-
PRO-02-1110	Review and approve asbestos abatement permits	100%	100%	0	16-Feb-24 A	13-Mar-24 A	01-Nov-25		ML1010, CONS-FOUN-
DIVISION 3 - CONCRETE			90.94%	55	07-Aug-23 A	23-Feb-26	23-Jan-26	123	
033000 - CAST-IN-PLACE CONCRETE			100%	0	07-Aug-23 A	28-Apr-25 A	01-Nov-25		
PRO-03-1050	Prepare and submit Cip concrete product data	100%	100%	0	07-Aug-23 A	29-Aug-23 A	01-Nov-25		PRO-03-1090
PRO-03-1080	Prepare and submit concrete design mix	100%	100%	0	07-Aug-23 A	29-Aug-23 A	01-Nov-25		PRO-03-1120, PRO-04-
PRO-03-1090	Review and approve cip concrete product data	100%	100%	0	30-Aug-23 A	15-Nov-23 A	01-Nov-25		PRO-03-1000
PRO-03-1070	Prepare and submit cip reinforcement product data	100%	100%	0	30-Aug-23 A	15-Nov-23 A	01-Nov-25		PRO-03-1110
PRO-03-1120	Review and approve concrete design mix	100%	100%	0	30-Aug-23 A	15-Nov-23 A	01-Nov-25		PRO-03-1000, PRO-03-
PRO-03-1110	Review and approve cip reinforcement product data	100%	100%	0	15-Nov-23 A	15-Nov-23 A	01-Nov-25		PRO-03-1000
PRO-03-1040	Prepare and submit formwork shop drawings	100%	100%	0	02-Jan-24 A	29-Jan-24 A	01-Nov-25		PRO-03-1130
PRO-03-1060	Prepare and submit cip reinforcement shop drawings R0	100%	100%	0	12-Jan-24 A	12-Jan-24 A	01-Nov-25		PRO-03-1061
PRO-03-1061	Returned cip reinforcement shop drawings R0	100%	100%	0	15-Jan-24 A	23-Feb-24 A	01-Nov-25		PRO-03-1000, PRO-03-
PRO-03-1130	Review and approve formwork shop drawings	100%	100%	0	30-Jan-24 A	23-Feb-24 A	01-Nov-25		PRO-03-1010, PRO-03-
PRO-03-1062	Re-submit cip reinforcement shop drawings R1	100%	100%	0	26-Feb-24 A	27-Feb-24 A	01-Nov-25		PRO-03-1100, PRO-03-
PRO-03-1064	Returned cip reinforcement shop drawings R1	100%	100%	0	28-Feb-24 A	16-Sep-24 A	01-Nov-25		PRO-03-1065
PRO-03-1063	EOR Holding up review due to MEP Coordinaton of cip reinforcement shop drawings R1	100%	100%	0	03-Dec-24 A	03-Dec-24 A	01-Nov-25		PRO-03-1100, PRO-03-
PRO-03-1065	Re-submit cip reinforcement shop drawings R2	100%	100%	0	04-Dec-24 A	23-Dec-24 A	01-Nov-25		PRO-03-1100
PRO-03-1100	Review and approve cip reinforcement shop drawings R2	100%	100%	0	24-Dec-24 A	17-Mar-25 A	01-Nov-25		PRO-03-1000
PRO-03-1010	Fabrication and delivery of formwork	100%	100%	0	23-Apr-25 A	23-Apr-25 A	01-Nov-25		PRO-03-1270
PRO-03-1000	Fabrication and delivery of cip concrete	100%	100%	0	28-Apr-25 A	28-Apr-25 A	01-Nov-25		PRO-03-1270
033300 - ARCHITECTURAL CAST-IN-PLCE CONCRETE			0%	55	01-Dec-25	23-Feb-26	23-Jan-26	123	
PRO-03-1150	Prepare and submit architectural cip reinforcement shop drawings for Planters	0%	0%	20	01-Dec-25	30-Dec-25	01-Dec-25	123	PRO-03-1190
PRO-03-1160	Prepare and submit architectural cip mock-up for Planters	0%	0%	20	01-Dec-25	30-Dec-25	01-Dec-25	142	PRO-03-1200
PRO-03-1170	Prepare and submit architectural cip concrete product data for Planters	0%	0%	20	01-Dec-25	30-Dec-25	01-Dec-25	142	PRO-03-1210
PRO-03-1180	Prepare and submit architectural cip formwork shop drawings for Planters	0%	0%	20	01-Dec-25	30-Dec-25	01-Dec-25	142	PRO-03-1220
PRO-03-1190	Review and approve architectural cip reinforcement shop drawings for Planters	0%	0%	15	31-Dec-25	22-Jan-26	23-Dec-25	123	PRO-03-1230, PRO-03-
PRO-03-1200	Review and approve architectural cip mock-up for Planters	0%	0%	15	31-Dec-25	22-Jan-26	23-Dec-25	142	PRO-03-1230
PRO-03-1210	Review and approve architectural cip concrete product data for Planters	0%	0%	15	31-Dec-25	22-Jan-26	23-Dec-25	142	PRO-03-1230
PRO-03-1220	Review and approve architectural formwork shop drawings for Planters	0%	0%	15	31-Dec-25	22-Jan-26	23-Dec-25	142	PRO-03-1230
PRO-03-1140	Fabrication and delivery of concrete reinforcement for Planters	0%	0%	20	23-Jan-26	23-Feb-26	23-Jan-26	123	SITE-1120
PRO-03-1230	Fabrication and delivery of cip concrete for Planters	0%	0%	1	23-Jan-26	23-Jan-26	24-Dec-25	142	SITE-1120
033543 - POLISHED CONCRETE FINISHING			99.81%	1	01-Sep-23 A	01-Dec-25	03-Nov-25	147	
PRO-03-1240	Prepare and submit penetrating liquid hardener/densifier	100%	100%	0	01-Sep-23 A	02-Jun-25 A	01-Nov-25		PRO-03-1250
PRO-03-1270	Pre-installation conference for concrete	100%	100%	0	14-Apr-25 A	14-Apr-25 A	01-Nov-25		CONS-EB-1630
PRO-03-1250	Review and approve penetrating liquid hardener/densifier	100%	100%	0	03-Jun-25 A	16-Jun-25 A	01-Nov-25		PRO-03-1260
PRO-03-1260	Fabrication and delivery of penetrating liquid hardener/densifier	0%	0%	1	01-Dec-25	01-Dec-25	03-Nov-25	147	CONS-EB-1420
DIVISION 4 - MASONRY			100%	0	01-Sep-23 A	14-Oct-25 A	03-Nov-25		
04200 - UNIT MASONRY			100%	0	01-Sep-23 A	14-Oct-25 A	03-Nov-25		
PRO-04-1010	Prepare and submit cmu product data	100%	100%	0	01-Sep-23 A	06-Mar-24 A	01-Nov-25		PRO-04-1030, PRO-04-
PRO-04-1011	Returned cmu product data R0	100%	100%	0	07-Mar-24 A	12-Mar-24 A	01-Nov-25		PRO-04-1012
PRO-04-1012	Re-submit cmu product data R1	100%	100%	0	13-Mar-24 A	04-Apr-24 A	01-Nov-25		PRO-04-1030, PRO-04-
PRO-04-1013	Returned cmu product data R1	100%	100%	0	09-Apr-24 A	23-Apr-24 A	01-Nov-25		PRO-04-1014
PRO-04-1014	Re-submit cmu product data R2	100%	100%	0	24-Apr-24 A	06-Jun-24 A	01-Nov-25		PRO-04-1030
PRO-04-1030	Review and approve cmu product data R2	100%	100%	0	07-Jun-24 A	10-Jun-24 A	01-Nov-25		PRO-04-1050
PRO-04-1020	Prepare and submit cmu shop drawings R1	100%	100%	0	01-Apr-25 A	19-May-25 A	03-Nov-25		PRO-04-1040, PRO-04-
PRO-04-1021	Returned cmu shop drawings R1	100%	100%	0	21-May-25 A	02-Jun-25 A	03-Nov-25		PRO-04-1022
PRO-04-1022	Re-submit cmu shop drawings R2	100%	100%	0	03-Jun-25 A	10-Jul-25 A	03-Nov-25		PRO-04-1040
PRO-04-1040	Review and approve cmu shop drawings R2	100%	100%	0	11-Jul-25 A	15-Jul-25 A	03-Nov-25		PRO-04-1000
PRO-04-1000	Fabricate and deliver cmu	100%	100%	0	01-Oct-25 A	01-Oct-25 A	03-Nov-25		CONS-EB-1150, CONS-

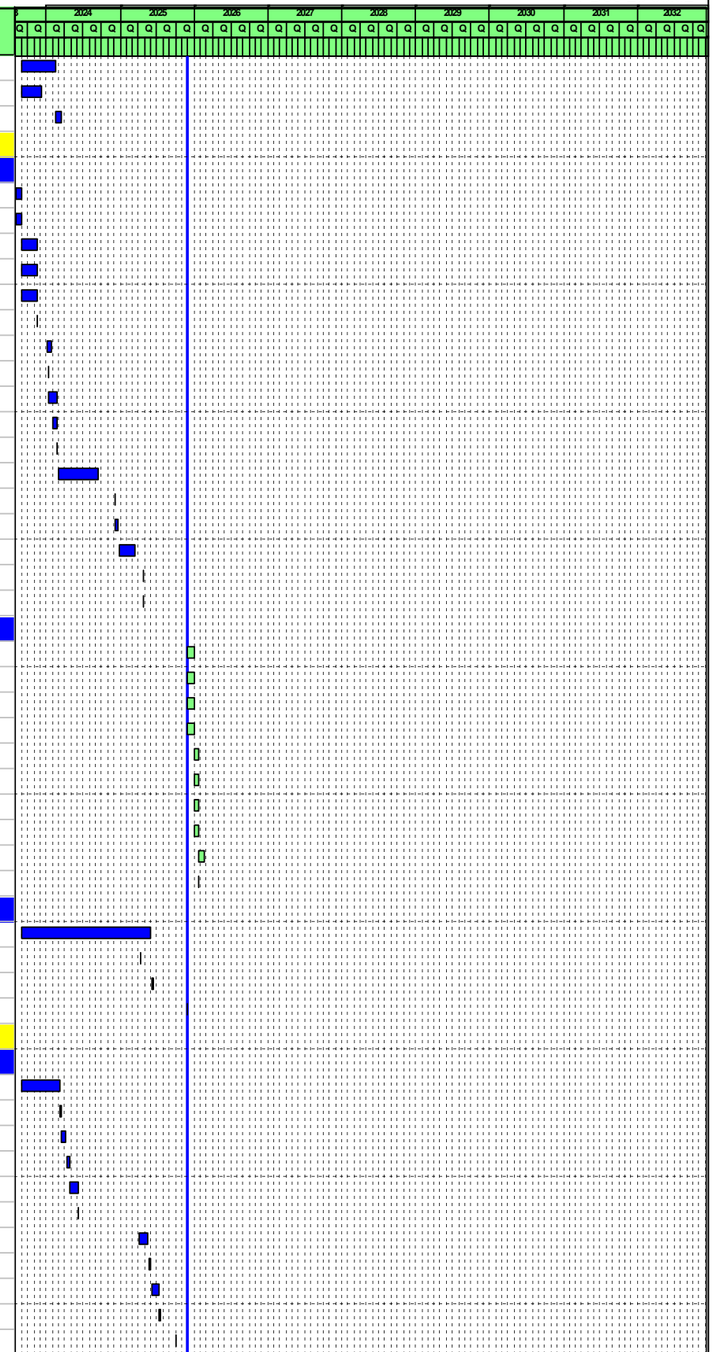


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PRO-04-1050	Prepare and submit cmu mock-up (Canceled not Required)	100%	100%	0	14-Oct-25 A	14-Oct-25 A	01-Nov-25		PRO-04-1060
PRO-04-1060	Review and approve cmu mock-up (Canceled not Required)	100%	100%	0	14-Oct-25 A	14-Oct-25 A	01-Nov-25		CONS-EB-1150
DIVISION 5 - METALS			97.04%	15	29-Sep-23 A	22-Dec-25	19-Dec-25	118	
051200 - STEEL STRUCTURAL FRAMING			100%	0	29-Sep-23 A	16-May-25 A	01-Nov-25		
PRO-05-1050	Prepare and submit steel structural framing shop drawings R0	100%	100%	0	29-Sep-23 A	01-Nov-23 A	01-Nov-25		PRO-05-1060, PRO-05-
PRO-05-1051	Returned steel structural framing shop drawings R0	100%	100%	0	02-Nov-23 A	21-Nov-23 A	01-Nov-25		PRO-05-1052, BULL#04
PRO-05-1052	Re-submit steel structural framing shop drawings R1 (Delayed due to Bulletin # 2)	100%	100%	0	03-Jun-24 A	14-Jun-24 A	01-Nov-25		PRO-05-1060, PRO-05-
PRO-05-1053	Returned steel structural framing shop drawings R1	100%	100%	0	17-Jun-24 A	03-Jul-24 A	01-Nov-25		PRO-05-1054
PRO-05-1054	Re-submit steel structural framing shop drawings R2 (pending Bulletibn # 2)	100%	100%	0	05-Jul-24 A	25-Jul-24 A	01-Nov-25		PRO-05-1060, PRO-05-
PRO-05-1055	Returned steel structural framing shop drawings R2	100%	100%	0	29-Jul-24 A	09-Aug-24 A	01-Nov-25		PRO-05-1056
PRO-05-1056	Re-submit steel structural framing shop drawings R3 (pending Bulletibn # 2)	100%	100%	0	12-Aug-24 A	27-Feb-25 A	01-Nov-25		PRO-05-1060, PRO-05-
PRO-05-1057	Returned steel structural framing shop drawings R3	100%	100%	0	28-Feb-25 A	18-Mar-25 A	01-Nov-25		PRO-05-1058
PRO-05-1058	Re-submit steel structural framing shop drawings R4 (including Bulletibn # 2)	100%	100%	0	19-Mar-25 A	06-May-25 A	01-Nov-25		PRO-05-1060
PRO-05-1060	Review and approve steel structural framing shop drawings R4	100%	100%	0	07-May-25 A	16-May-25 A	01-Nov-25		PRO-05-1000
053100 - STEEL DECK			100%	0	29-Sep-23 A	16-May-25 A	01-Nov-25		
PRO-05-1070	Prepare and submit steel deck shop drawings	100%	100%	0	29-Sep-23 A	06-May-25 A	01-Nov-25		PRO-05-1080
PRO-05-1080	Review and approve steel deck shop drawings	100%	100%	0	07-May-25 A	16-May-25 A	01-Nov-25		PRO-05-1010
055000 - MISCELLANEOUS METALS			100%	0	29-Sep-23 A	19-Apr-24 A	01-Nov-25		
RFI#32-10	Submit RFI # 32 Regarding assembling miscellaneous metals shop drawings	100%	100%	0	29-Sep-23 A	12-Dec-23 A	01-Nov-25		RFI#32-15
RFI#33-10	Submit RFI # 33 Regarding assembling miscellaneous metals shop drawings	100%	100%	0	29-Sep-23 A	13-Dec-23 A	01-Nov-25		RFI#33-15
RFI#32-15	Response to RFI # 32 Regarding assembling miscellaneous metals shop drawings	100%	100%	0	13-Dec-23 A	16-Jan-24 A	01-Nov-25		PRO-05-1090
RFI#33-15	Response to RFI # 33 Regarding assembling miscellaneous metals shop drawings	100%	100%	0	14-Dec-23 A	16-Jan-24 A	01-Nov-25		PRO-05-1090
PRO-05-1090	Prepare and submit assembling miscellaneous metals shop drawings	100%	100%	0	17-Jan-24 A	04-Apr-24 A	01-Nov-25		PRO-05-1100, PRO-05-
PRO-05-1100	Review and approve assembling miscellaneous metals shop drawings	100%	100%	0	12-Mar-24 A	19-Apr-24 A	01-Nov-25		PRO-05-1020
055113 - STEEL PAN STAIRS			100%	0	29-Sep-23 A	25-Apr-25 A	01-Nov-25		
PRO-05-1110	Prepare and submit steel stairs metal framing shop drawings R0	100%	100%	0	29-Sep-23 A	04-Apr-24 A	01-Nov-25		PRO-05-1111
PRO-05-1120	Prepare and submit steel stairs metal framing product data R0	100%	100%	0	29-Sep-23 A	04-Apr-24 A	01-Nov-25		PRO-05-1121
PRO-05-1111	Returned steel stairs metal framing shop drawings R0	100%	100%	0	05-Apr-24 A	19-Apr-24 A	01-Nov-25		PRO-05-1112
PRO-05-1121	Returned steel stairs metal framing product data R0	100%	100%	0	05-Apr-24 A	19-Apr-24 A	01-Nov-25		PRO-05-1122
PRO-05-1112	Re-submit steel stairs metal framing shop drawings R1	100%	100%	0	22-Apr-24 A	04-Jun-24 A	01-Nov-25		PRO-05-1113
PRO-05-1122	Re-submit steel stairs metal framing product data R1	100%	100%	0	22-Apr-24 A	04-Jun-24 A	01-Nov-25		PRO-05-1140, PRO-05-
PRO-05-1113	Returned steel stairs metal framing shop drawings R1	100%	100%	0	05-Jun-24 A	18-Jun-24 A	01-Nov-25		PRO-05-1114
PRO-05-1123	Returned steel stairs metal framing product data R1	100%	100%	0	05-Jun-24 A	18-Jun-24 A	01-Nov-25		PRO-05-1124
PRO-05-1114	Re-submit steel stairs metal framing shop drawings R2	100%	100%	0	19-Jun-24 A	07-Nov-24 A	01-Nov-25		PRO-05-1115
PRO-05-1124	Re-submit steel stairs metal framing product data R2	100%	100%	0	19-Jun-24 A	07-Nov-24 A	01-Nov-25		PRO-05-1140, PRO-05-
PRO-05-1115	Returned steel stairs metal framing shop drawings R2	100%	100%	0	08-Nov-24 A	22-Nov-24 A	01-Nov-25		PRO-05-1116
PRO-05-1125	Returned steel stairs metal framing product data R2	100%	100%	0	08-Nov-24 A	22-Nov-24 A	01-Nov-25		PRO-05-1126
PRO-05-1116	Re-submit steel stairs metal framing shop drawings R3	100%	100%	0	25-Nov-24 A	16-Apr-25 A	01-Nov-25		PRO-05-1130
PRO-05-1126	Re-submit steel stairs metal framing product data R3	100%	100%	0	25-Nov-24 A	16-Apr-25 A	01-Nov-25		PRO-05-1140
PRO-05-1130	Review and approve steel stairs metal framing shop drawings R3	100%	100%	0	17-Apr-25 A	25-Apr-25 A	01-Nov-25		PRO-05-1030
PRO-05-1140	Review and approve steel stairs metal framing product data R3	100%	100%	0	17-Apr-25 A	25-Apr-25 A	01-Nov-25		PRO-05-1030
057000 - ORNAMENTAL METALS			97.04%	15	29-Sep-23 A	22-Dec-25	19-Dec-25	40	
PRO-05-1150	Prepare and submit ornamental metals shop drawings R0	100%	100%	0	29-Sep-23 A	20-Mar-24 A	01-Nov-25		PRO-05-1180, PRO-05-
PRO-05-1160	Prepare and submit ornamental metals material data sheet R0	100%	100%	0	29-Sep-23 A	20-Mar-24 A	01-Nov-25		PRO-05-1190, PRO-05-
PRO-05-1170	Prepare and submit ornamental samples	100%	100%	0	29-Sep-23 A	09-May-24 A	27-Nov-25		PRO-05-1200
PRO-05-1151	Returned ornamental metals shop drawings R0	100%	100%	0	21-Mar-24 A	03-Apr-24 A	01-Nov-25		PRO-05-1152
PRO-05-1161	Returned ornamental material data sheet R0	100%	100%	0	21-Mar-24 A	03-Apr-24 A	01-Nov-25		PRO-05-1162
PRO-05-1152	Re-submit ornamental metals shop drawings R1	100%	100%	0	04-Apr-24 A	06-May-24 A	01-Nov-25		PRO-05-1180
PRO-05-1162	Re-submit ornamental metals material data sheet R1	100%	100%	0	04-Apr-24 A	06-May-24 A	01-Nov-25		PRO-05-1190
PRO-05-1180	Review and approve ornamental metals shop drawings	100%	100%	0	07-May-24 A	09-May-24 A	01-Nov-25		PRO-05-1040
PRO-05-1190	Review and approve ornamental material data sheet	100%	100%	0	07-May-24 A	09-May-24 A	01-Nov-25		PRO-05-1040

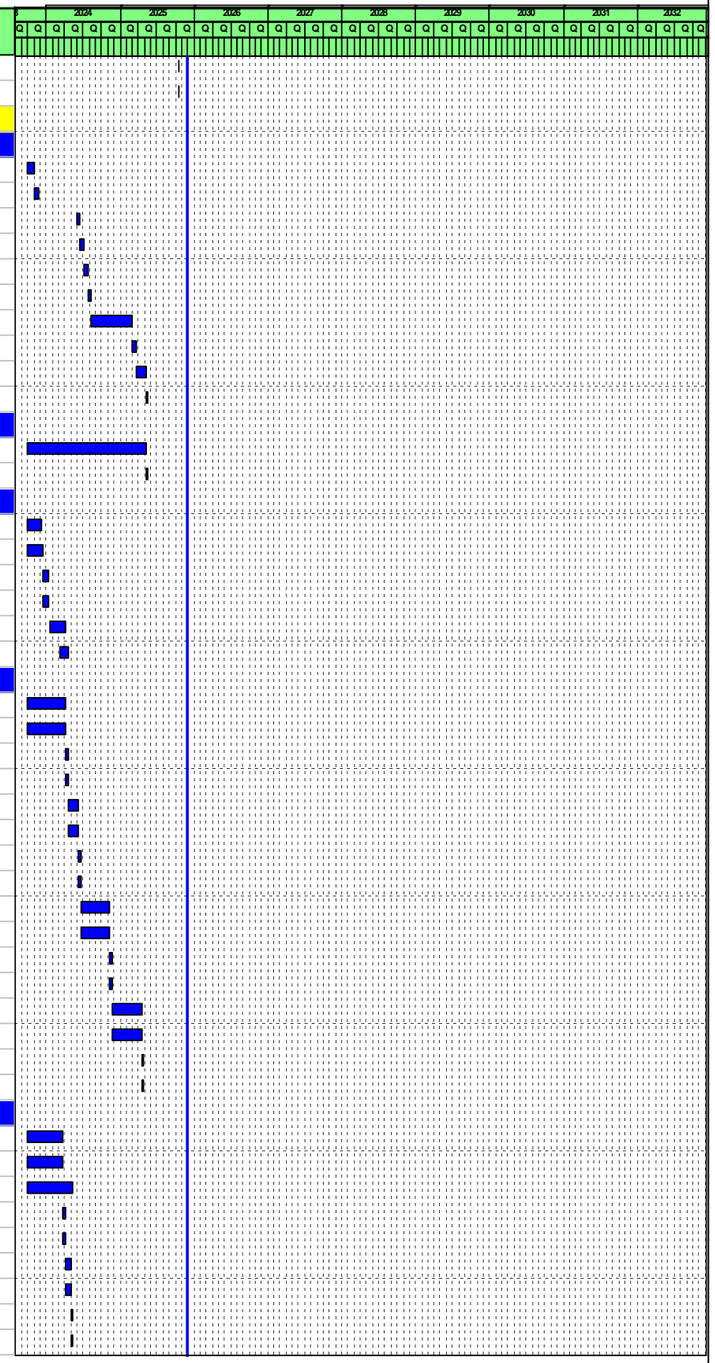


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PRO-05-1200	Review and approve ornamental samples	0%	0%	15	01-Dec-25	22-Dec-25	19-Dec-25	40	PRO-05-1040
DIVISION 6 - WOOD, PLASTICS AND COMPOSITES			89.13%	60	29-Sep-23 A	02-Mar-26	30-Jan-26	46	
062000 - CARPENTRY			89.13%	60	29-Sep-23 A	02-Mar-26	30-Jan-26	46	
PRO-06-1020	Prepare and submit rough carpentry	0%	0%	40	29-Sep-23 A	29-Jan-26	31-Dec-25	46	PRO-06-1030
PRO-06-1030	Review and approve rough carpentry	0%	0%	15	30-Jan-26	23-Feb-26	23-Jan-26	46	PRO-06-1000
PRO-06-1000	Fabrication and delivery of rough carpentry materials	0%	0%	5	24-Feb-26	02-Mar-26	30-Jan-26	46	CONS-EB-1350
064023 - ARCHITECTURAL WOODWORK			100%	0	29-Sep-23 A	04-Aug-25 A	01-Nov-25		
PRO-06-1040	Prepare and submit architectural woodwork shop drawings R0	100%	100%	0	29-Sep-23 A	10-May-24 A	01-Nov-25		PRO-06-1041
PRO-06-1050	Prepare and submit architectural woodwork samples	100%	100%	0	29-Sep-23 A	23-Jul-25 A	01-Nov-25		PRO-06-1080
PRO-06-1060	Prepare and submit architectural material data sheet	100%	100%	0	29-Sep-23 A	23-Jul-25 A	01-Nov-25		PRO-06-1090
PRO-06-1041	Returned architectural woodwork shop drawings R0	100%	100%	0	13-May-24 A	24-May-24 A	01-Nov-25		PRO-06-1042
PRO-06-1042	Re-submit architectural woodwork shop drawings R1	100%	100%	0	28-May-24 A	13-Aug-24 A	01-Nov-25		PRO-06-1070
PRO-06-1070	Review and approve architectural woodwork shop drawings R1	100%	100%	0	14-Aug-24 A	27-Aug-24 A	01-Nov-25		PRO-06-1010
PRO-06-1080	Review and approve architectural woodwork samples	100%	100%	0	24-Jul-25 A	04-Aug-25 A	01-Nov-25		PRO-06-1010
PRO-06-1090	Review and approve architectural material data sheet	100%	100%	0	24-Jul-25 A	04-Aug-25 A	01-Nov-25		PRO-06-1010
DIVISION 7 - THERMAL AND MOISTURE PROTECTION			98.99%	5	30-Nov-23 A	05-Dec-25	02-Dec-25	80	
071326 - SHEET MEMBRANE WATERPROOFING			100%	0	13-Mar-24 A	10-Apr-25 A	01-Nov-25		
PR0-07-1090	Prepare and submit sheet membrane waterproofing shop drawings	100%	100%	0	13-Mar-24 A	10-Apr-24 A	01-Nov-25		PR0-07-1110
PR0-07-1120	Prepare and submit sheet membrane waterproofing product data	100%	100%	0	13-Mar-24 A	10-Apr-24 A	01-Nov-25		PR0-07-1100
PR0-07-1100	Review and approve sheet membrane waterproofing product data	100%	100%	0	11-Apr-24 A	12-Apr-24 A	01-Nov-25		PRO-07-1000
PR0-07-1110	Review and approve sheet membrane waterproofing shop drawings	100%	100%	0	11-Apr-24 A	12-Apr-24 A	01-Nov-25		PRO-07-1000
PR0-07-1140	Prepare and submit sheet membrane waterproofing sample	100%	100%	0	01-Aug-24 A	05-Aug-24 A	01-Nov-25		PR0-07-1130
PR0-07-1130	Review and approve sheet membrane waterproofing sample	100%	100%	0	06-Aug-24 A	12-Aug-24 A	01-Nov-25		PRO-07-1000
PRO-07-1000	Fabrication and delivery of sheet membrane waterproofing material	100%	100%	0	01-Apr-25 A	10-Apr-25 A	01-Nov-25		CONS-EB-1250
071616 - CRYSTALLINE WATERPROOFING			98.58%	5	01-Jul-24 A	05-Dec-25	07-Nov-25	80	
PR0-07-1180	Prepare and submit crystalline waterproofing product data	100%	100%	0	01-Jul-24 A	05-Jul-24 A	01-Nov-25		PR0-07-1170
PR0-07-1170	Review and approve crystalline waterproofing product data	100%	100%	0	08-Jul-24 A	09-Jul-24 A	01-Nov-25		PR0-07-1010
PR0-07-1160	Prepare and submit crystalline waterproofing shop drawings	100%	100%	0	01-Apr-25 A	16-Apr-25 A	01-Nov-25		PR0-07-1150
PR0-07-1150	Review and approve crystalline waterproofing shop drawings	100%	100%	0	16-Apr-25 A	16-Apr-25 A	01-Nov-25		PR0-07-1010
PR0-07-1010	Fabrication and delivery of crystalline waterproofing material	0%	0%	5	01-Dec-25	05-Dec-25	07-Nov-25	80	CONS-EB-1250
072100 - THERMAL INSULATION			100%	0	01-Mar-24 A	21-May-25 A	01-Nov-25		
PR0-07-1200	Prepare and submit thermal insulation product data	100%	100%	0	01-Mar-24 A	02-Apr-24 A	01-Nov-25		PR0-07-1190
PR0-07-1190	Review and approve thermal insulation product data	100%	100%	0	03-Apr-24 A	10-Apr-24 A	01-Nov-25		PR0-07-1020
PR0-07-1020	Fabrication and delivery of thermal insulation material	100%	100%	0	11-Apr-25 A	21-May-25 A	01-Nov-25		CONS-EB-1250
072700 - VAPOR PERMEABLE AIR BARRIER LIQUID MEMBRANE			100%	0	13-Mar-24 A	18-Nov-25 A	07-Nov-25		
PR0-07-1220	Prepare and submit vapor permeable air barrier liquid membrane shop drawings	100%	100%	0	13-Mar-24 A	10-Apr-24 A	01-Nov-25		PR0-07-1210
PR0-07-1240	Prepare and submit vapor permeable air barrier liquid membrane product data	100%	100%	0	13-Mar-24 A	10-Apr-24 A	01-Nov-25		PR0-07-1230
PR0-07-1210	Review and approve vapor permeable air barrier liquid membrane shop drawings	100%	100%	0	11-Apr-24 A	12-Apr-24 A	01-Nov-25		PR0-07-1030
PR0-07-1230	Review and approve vapor permeable air barrier liquid membrane product data	100%	100%	0	11-Apr-24 A	12-Apr-24 A	01-Nov-25		PR0-07-1030
PR0-07-1030	Fabrication and delivery of vapor permeable air barrier liquid membrane material	100%	100%	0	03-Nov-25 A	18-Nov-25 A	07-Nov-25		CONS-EB-1250
075423 - THERMOPLASTIC POLYOLEFIN (TPO) ROOFING			98.79%	5	01-Mar-24 A	05-Dec-25	07-Nov-25	80	
PR0-07-1280	Prepare and submit tpo product data	100%	100%	0	01-Mar-24 A	04-Apr-24 A	01-Nov-25		PR0-07-1270
PR0-07-1270	Review and approve tpo product data	100%	100%	0	05-Apr-24 A	18-Apr-24 A	01-Nov-25		PR0-07-1040
PR0-07-1260	Prepare and submit tpo shop drawings R0	100%	100%	0	01-May-24 A	10-May-24 A	01-Nov-25		PR0-07-1250, PR0-07-1
PR0-07-1261	Returned tpo shop drawings R0	100%	100%	0	13-May-24 A	22-May-24 A	01-Nov-25		PR0-07-1262
PR0-07-1262	Re-submit tpo shop drawings R1	100%	100%	0	23-May-24 A	10-Jun-24 A	01-Nov-25		PR0-07-1250
PR0-07-1250	Review and approve tpo shop drawings R1	100%	100%	0	11-Jun-24 A	11-Jun-24 A	01-Nov-25		PR0-07-1040
PR0-07-1040	Fabrication and delivery of tpo roofing material	0%	0%	5	01-Dec-25	05-Dec-25	07-Nov-25	80	CONS-EB-1250, CONS-
076200 - SHEET METAL FLASHING			98.72%	5	13-Mar-24 A	05-Dec-25	07-Nov-25	80	
PR0-07-1300	Prepare and submit sheet metal flashing shop drawings	100%	100%	0	13-Mar-24 A	10-Apr-24 A	01-Nov-25		PR0-07-1290
PR0-07-1320	Prepare and submit sheet metal flashing product data	100%	100%	0	13-Mar-24 A	10-Apr-24 A	01-Nov-25		PR0-07-1310

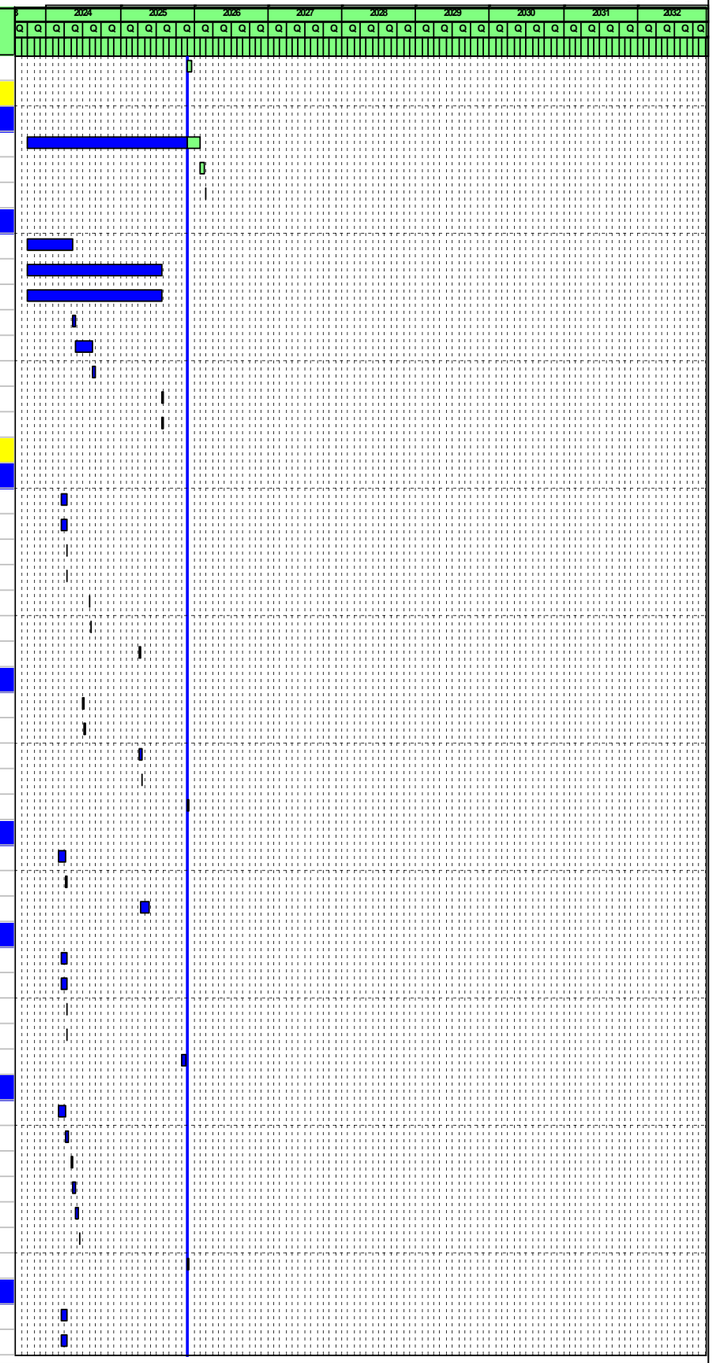


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PR0-07-1290	Review and approve sheet metal flashing shop drawings	100%	100%	0	11-Apr-24 A	23-Apr-24 A	01-Nov-25		PR0-07-1050
PR0-07-1310	Review and approve sheet metal flashing product data	100%	100%	0	11-Apr-24 A	23-Apr-24 A	01-Nov-25		PR0-07-1050
PR0-07-1050	Fabrication and delivery of sheet metal flashing material	0%	0%	5	01-Dec-25	05-Dec-25	07-Nov-25	80	CONS-EB-1250
077100 – ROOF SPECIALTIES AND ACCESSORIES			100%	0	01-Apr-25 A	18-Nov-25 A	07-Nov-25		
PR0-07-1340	Prepare and submit roof specialties and accessories product data	100%	100%	0	01-Apr-25 A	22-Apr-25 A	01-Nov-25		PR0-07-1330
PR0-07-1330	Review and approve roof specialties and accessories product data	100%	100%	0	23-Apr-25 A	13-May-25 A	01-Nov-25		PR0-07-1060
PR0-07-1060	Fabrication and delivery of roof specialties and accessories material	100%	100%	0	03-Nov-25 A	18-Nov-25 A	07-Nov-25		CONS-EB-1250
078413 - FIRESTOPPING/SMOKE SEALS			100%	0	30-Nov-23 A	18-Nov-25 A	02-Dec-25		
PR0-07-1380	Prepare and submit firestopping/smoke seals product data	100%	100%	0	30-Nov-23 A	17-Dec-24 A	01-Nov-25		PR0-07-1360, PR0-07-1
PR0-07-1360	Review and approve firestopping/smoke seals product data	100%	100%	0	17-Dec-24 A	17-Dec-24 A	01-Nov-25		PR0-07-1350
PR0-07-1070	Fabrication and delivery of firestopping/smoke seals	100%	100%	0	03-Nov-25 A	18-Nov-25 A	02-Dec-25		CONS-EB-1250
PR0-07-1350	Prepare and submit firestopping/smoke seals mock-up	100%	100%	0	03-Nov-25 A	12-Nov-25 A	07-Nov-25		PR0-07-1370
PR0-07-1370	Review and approve firestopping/smoke seals mock-up	100%	100%	0	03-Nov-25 A	12-Nov-25 A	01-Dec-25		PR0-07-1070
079200 - JOINT SEALERS			99.8%	1	30-Nov-23 A	01-Dec-25	03-Nov-25	84	
PR0-07-1400	Prepare and submit joint sealers product data	100%	100%	0	30-Nov-23 A	18-Feb-25 A	01-Nov-25		PR0-07-1390
PR0-07-1390	Review and approve joint sealer product data	100%	100%	0	19-Feb-25 A	27-Feb-25 A	01-Nov-25		PR0-07-1080
PR0-07-1080	Fabrication and delivery of joint sealer material	0%	0%	1	01-Dec-25	01-Dec-25	03-Nov-25	84	CONS-EB-1250
DIVISION 8 - OPENINGS			100%	0	01-Sep-23 A	30-Sep-25 A	01-Nov-25		
081113 - STEEL DOORS AND FRAMES			100%	0	01-Sep-23 A	07-May-25 A	01-Nov-25		
PR0-08-1020	Prepare and submit steel doors and frames shop drawings R0	100%	100%	0	01-Sep-23 A	17-Apr-24 A	01-Nov-25		PR0-08-1021
PR0-08-1040	Prepare and submit steel doors and frames product data R0	100%	100%	0	01-Sep-23 A	17-Apr-24 A	01-Nov-25		PR0-08-1041
PR0-08-1021	Returned steel doors and frames shop drawings R0	100%	100%	0	18-Apr-24 A	02-May-24 A	01-Nov-25		PR0-08-1022
PR0-08-1041	Returned steel doors and frames product data R0	100%	100%	0	18-Apr-24 A	02-May-24 A	01-Nov-25		PR0-08-1042
PR0-08-1022	Re-submit steel doors and frames shop drawings R1	100%	100%	0	03-May-24 A	05-Sep-24 A	01-Nov-25		PR0-08-1010, PR0-08-1
PR0-08-1042	Re-submit steel doors and frames product data R1	100%	100%	0	03-May-24 A	05-Sep-24 A	01-Nov-25		PR0-08-1030
PR0-08-1023	Returned steel doors and frames shop drawings R1	100%	100%	0	06-May-24 A	17-Sep-24 A	01-Nov-25		PR0-08-1024
PR0-08-1043	Returned steel doors and frames product data R1	100%	100%	0	06-Sep-24 A	17-Sep-24 A	01-Nov-25		PR0-08-1044
PR0-08-1044	Re-submit steel doors and frames product data R2	100%	100%	0	18-Sep-24 A	17-Apr-25 A	01-Nov-25		PR0-08-1030
PR0-08-1024	Re-submit steel doors and frames shop drawings R2	100%	100%	0	18-Sep-24 A	17-Apr-25 A	01-Nov-25		PR0-08-1010
PR0-08-1010	Review and approve steel doors and frames shop drawings R2	100%	100%	0	18-Apr-25 A	07-May-25 A	01-Nov-25		PR0-08-1000
PR0-08-1030	Review and approve steel doors and frames product data R2	100%	100%	0	18-Apr-25 A	07-May-25 A	01-Nov-25		PR0-08-1000
083113 - ACCESS DOORS			100%	0	01-Sep-23 A	24-Feb-25 A	01-Nov-25		
PR0-08-1140	Prepare and submit access doors shop drawings R0	100%	100%	0	01-Sep-23 A	19-Dec-24 A	01-Nov-25		PR0-08-1130, PR0-08-1
PR0-08-1160	Prepare and submit access doors product data	100%	100%	0	01-Sep-23 A	19-Dec-24 A	01-Nov-25		PR0-08-1161
PR0-08-1161	Returned access doors product data R0	100%	100%	0	20-Dec-24 A	23-Dec-24 A	01-Nov-25		PR0-08-1162
PR0-08-1141	Returned access doors shop drawings R0	100%	100%	0	20-Dec-24 A	23-Dec-24 A	01-Nov-25		PR0-08-1142
PR0-08-1142	Re-submit access doors shop drawings R1	100%	100%	0	24-Dec-24 A	17-Feb-25 A	01-Nov-25		PR0-08-1130
PR0-08-1162	Re-submit access doors product data R1	100%	100%	0	24-Dec-24 A	17-Feb-25 A	01-Nov-25		PR0-08-1150
PR0-08-1130	Review and approve access doors shop drawings R1	100%	100%	0	18-Feb-25 A	24-Feb-25 A	01-Nov-25		PR0-08-1050
PR0-08-1150	Review and approve access doors product data R1	100%	100%	0	18-Feb-25 A	24-Feb-25 A	01-Nov-25		PR0-08-1050
084113 – ALUMINUM ENTRANCE AND STOREFRONT			100%	0	01-Sep-23 A	02-Oct-24 A	01-Nov-25		
PR0-08-1180	Prepare and submit aluminum entrance and storefront shop drawings	100%	100%	0	01-Sep-23 A	06-Feb-24 A	01-Nov-25		PR0-08-1170
PR0-08-1200	Prepare and submit aluminum entrance and storefront product data	100%	100%	0	01-Sep-23 A	21-Dec-23 A	01-Nov-25		PR0-08-1190
PR0-08-1190	Review and approve aluminum entrance and storefront product data	100%	100%	0	22-Dec-23 A	11-Jan-24 A	01-Nov-25		PR0-08-1060
PR0-08-1170	Review and approve aluminum entrance and storefront shop drawings	100%	100%	0	07-Feb-24 A	02-Oct-24 A	01-Nov-25		PR0-08-1060
084413 - GLAZED ALUMINUM CURTAIN WALLS			100%	0	01-Sep-23 A	26-Sep-25 A	01-Nov-25		
PR0-08-1220	Prepare and submit aluminum entrance and storefront shop drawings R0	100%	100%	0	01-Sep-23 A	06-Feb-24 A	01-Nov-25		PR0-08-1221
PR0-08-1240	Prepare and submit aluminum entrance and storefront product data R0	100%	100%	0	01-Sep-23 A	21-Dec-23 A	01-Nov-25		PR0-08-1230
PR0-08-1230	Review and approve aluminum entrance and storefront product data R0	100%	100%	0	22-Dec-23 A	11-Jan-24 A	01-Nov-25		PR0-08-1070
PR0-08-1221	Returned aluminum entrance and storefront shop drawings R1	100%	100%	0	07-Feb-24 A	23-Feb-24 A	01-Nov-25		PR0-08-1222
PR0-08-1222	Re-submit aluminum entrance and storefront Shop Drawings R1	100%	100%	0	26-Feb-24 A	29-Mar-24 A	01-Nov-25		PR0-08-1210, PR0-08-1

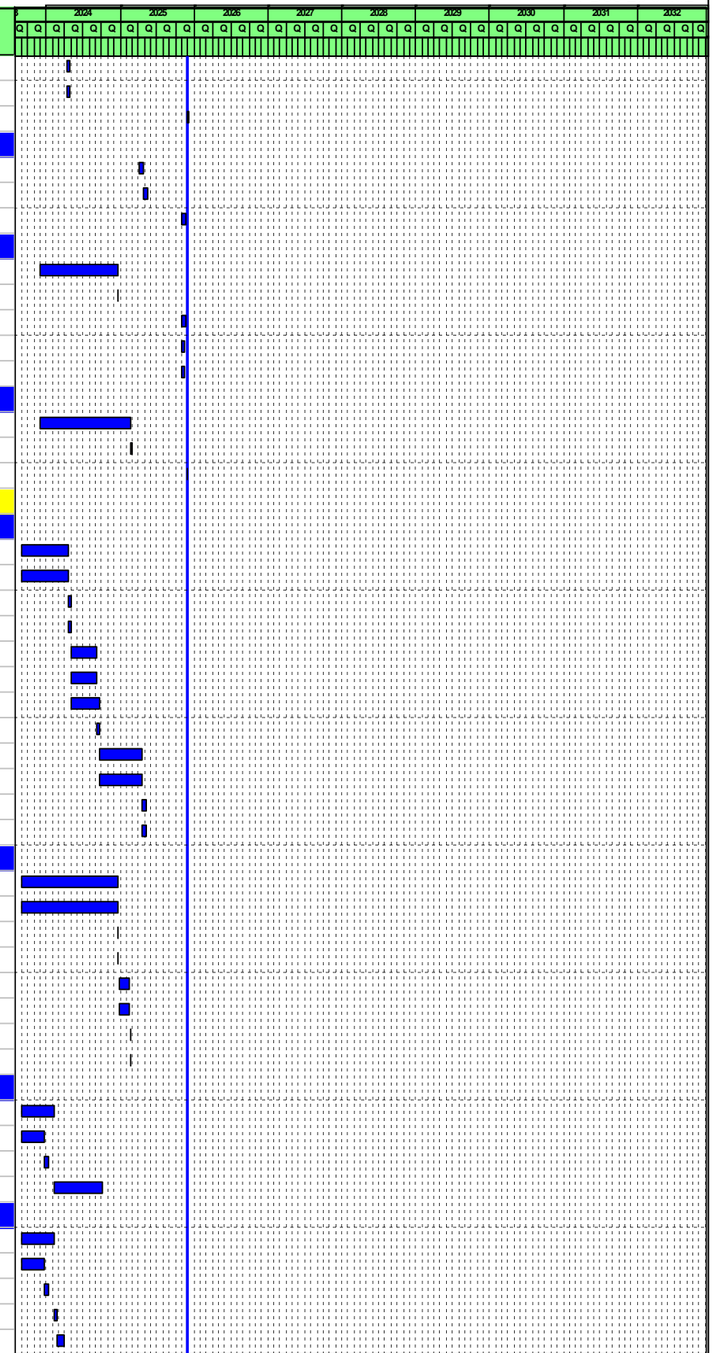


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PR0-08-1223	Returned aluminum entrance and storefront shop drawings R1	100%	100%	0	26-Feb-24 A	29-Apr-24 A	01-Nov-25		PR0-08-1224
PR0-08-1224	Re-submit aluminum entrance and storefront Shop Drawings R2	100%	100%	0	30-Apr-24 A	10-Oct-24 A	01-Nov-25		PR0-08-1225
PR0-08-1225	Returned aluminum entrance and storefront shop drawings R2	100%	100%	0	11-Oct-24 A	30-Oct-24 A	01-Nov-25		PR0-08-1226
PR0-08-1226	Re-submit aluminum entrance and storefront Shop Drawings R3	100%	100%	0	31-Oct-24 A	05-Jun-25 A	01-Nov-25		PR0-08-1227
PR0-08-1227	Returned aluminum entrance and storefront shop drawings R3	100%	100%	0	06-Jun-25 A	30-Jun-25 A	01-Nov-25		PR0-08-1228
PR0-08-1228	Re-submit aluminum entrance and storefront Shop Drawings R4	100%	100%	0	01-Jul-25 A	10-Sep-25 A	01-Nov-25		PR0-08-1210
PR0-08-1210	Review and approve aluminum entrance and storefront shop drawings R4	100%	100%	0	11-Sep-25 A	26-Sep-25 A	01-Nov-25		PR0-08-1070
085113 - ALUMINUM WINDOWS			100%	0	01-Sep-23 A	20-Feb-25 A	01-Nov-25		
PR0-08-1280	Prepare and submit aluminum windows product data	100%	100%	0	01-Sep-23 A	21-Dec-23 A	01-Nov-25		PR0-08-1270
PR0-08-1260	Prepare and submit aluminum windows shop drawings Rev.0	100%	100%	0	01-Sep-23 A	06-Feb-24 A	01-Nov-25		PR0-08-1261
PR0-08-1261	Returned aluminum windows shop drawings Rev.0	100%	100%	0	05-Sep-23 A	23-Feb-24 A	01-Nov-25		PR0-08-1262
PR0-08-1270	Review and approve aluminum windows product data	100%	100%	0	22-Dec-23 A	11-Jan-24 A	01-Nov-25		PR0-08-1080
PR0-08-1262	Re-submit aluminum windows shop drawings Rev.1	100%	100%	0	26-Feb-24 A	26-Jul-24 A	01-Nov-25		PR0-08-1250
PR0-08-1250	Review and approve aluminum windows shop drawings Rev.1	100%	100%	0	29-Jul-24 A	20-Feb-25 A	01-Nov-25		PR0-08-1080
086300 - METAL-FRAMED SKYLIGHTS			100%	0	01-Sep-23 A	11-Jan-24 A	01-Nov-25		
PR0-08-1300	Prepare and submit metal-framed skylights shop drawings	100%	100%	0	01-Sep-23 A	21-Dec-23 A	01-Nov-25		PR0-08-1290
PR0-08-1320	Prepare and submit metal-framed skylights product data	100%	100%	0	01-Sep-23 A	21-Dec-23 A	01-Nov-25		PR0-08-1310
PR0-08-1290	Review and approve metal-framed skylights shop drawings	100%	100%	0	22-Dec-23 A	11-Jan-24 A	01-Nov-25		PR0-08-1090, PR0-08-1
PR0-08-1310	Review and approve metal-framed skylights product data	100%	100%	0	22-Dec-23 A	11-Jan-24 A	01-Nov-25		PR0-08-1090, PR0-08-1
087100 - DOOR HARDWARE			100%	0	01-Sep-23 A	06-May-24 A	01-Nov-25		
PR0-08-1340	Prepare and submit door hardware shop drawings R0	100%	100%	0	01-Sep-23 A	19-Feb-24 A	01-Nov-25		PR0-08-1341
PR0-08-1360	Prepare and submit door hardware product data R0	100%	100%	0	01-Sep-23 A	19-Feb-24 A	01-Nov-25		PR0-08-1361
PR0-08-1341	Returned door hardware shop drawings R0	100%	100%	0	20-Feb-24 A	25-Mar-24 A	01-Nov-25		PR0-08-1342
PR0-08-1361	Returned door hardware product data R0	100%	100%	0	20-Feb-24 A	25-Mar-24 A	01-Nov-25		PR0-08-1362
PR0-08-1342	Re-submit door hardware shop drawings R1	100%	100%	0	26-Mar-24 A	15-Apr-24 A	01-Nov-25		PR0-08-1330
PR0-08-1362	Re-submit door hardware product data R1	100%	100%	0	26-Mar-24 A	15-Apr-24 A	01-Nov-25		PR0-08-1350
PR0-08-1330	Review and approve door hardware shop drawings R1	100%	100%	0	16-Apr-24 A	06-May-24 A	01-Nov-25		PR0-08-1100
PR0-08-1350	Review and approve door hardware product data R1	100%	100%	0	16-Apr-24 A	06-May-24 A	01-Nov-25		PR0-08-1100
088000 - GLASS AND GLAZING			100%	0	01-Sep-23 A	30-Sep-25 A	01-Nov-25		
PR0-08-1380	Prepare and submit glass and glazing shop drawings	100%	100%	0	01-Sep-23 A	22-May-25 A	01-Nov-25		PR0-08-1370
PR0-08-1400	Prepare and submit glass and glazing product data	100%	100%	0	01-Sep-23 A	22-May-25 A	01-Nov-25		PR0-08-1390
PR0-08-1370	Review and approve glass and glazing shop drawings	100%	100%	0	23-May-25 A	30-Sep-25 A	01-Nov-25		PR0-08-1110
PR0-08-1390	Review and approve glass and glazing product data	100%	100%	0	23-May-25 A	11-Jul-25 A	01-Nov-25		PR0-08-1110
089000 - LOUVERS			100%	0	01-Sep-23 A	01-Sep-23 A	01-Nov-25		
PR0-08-1120	Fabrication and delivery of louvers (not Applicable no Louvers in Contract)	100%	100%	0	01-Sep-23 A	01-Sep-23 A	01-Nov-25		CONS-EB-1350
PR0-08-1410	Review and approve louvers shop drawings (not Applicable no Louvers in Contract)	100%	100%	0	01-Sep-23 A	01-Sep-23 A	01-Nov-25		PR0-08-1120
PR0-08-1420	Prepare and submit louvers shop drawings (not Applicable no Louvers in Contract)	100%	100%	0	01-Sep-23 A	01-Sep-23 A	01-Nov-25		PR0-08-1410
PR0-08-1430	Review and approve louvers product data (not Applicable no Louvers in Contract)	100%	100%	0	01-Sep-23 A	01-Sep-23 A	01-Nov-25		PR0-08-1120
PR0-08-1440	Prepare and submit louvers product data (not Applicable no Louvers in Contract)	100%	100%	0	01-Sep-23 A	01-Sep-23 A	01-Nov-25		PR0-08-1430
DIVISION 9 - FINISHES			89.32%	66	01-Sep-23 A	10-Mar-26	10-Feb-26	82	
092313 - SEAMLESS ABSORPTIVE PLASTER			89.32%	66	01-Sep-23 A	10-Mar-26	10-Feb-26	66	
PR0-09-1080	Prepare and submit plaster product data	50%	50%	50	01-Sep-23 A	13-Feb-26	15-Jan-26	66	PR0-09-1070
PR0-09-1070	Review and approve plaster product data	0%	0%	15	17-Feb-26	09-Mar-26	09-Feb-26	66	PR0-09-1000
PR0-09-1000	Fabrication and delivery of plaster material	0%	0%	1	10-Mar-26	10-Mar-26	10-Feb-26	66	CONS-EB-2240
092900 - GYPSUM DRYWALL			99.82%	1	01-Sep-23 A	01-Dec-25	03-Nov-25	104	
PR0-09-1100	Prepare and submit gypsum drywall product data	100%	100%	0	01-Sep-23 A	09-Sep-24 A	01-Nov-25		PR0-09-1090
PR0-09-1090	Review and approve gypsum drywall product data	100%	100%	0	10-Sep-24 A	17-Sep-24 A	01-Nov-25		PR0-09-1010
PR0-09-1010	Fabrication and delivery of gypsum drywall	0%	0%	1	01-Dec-25	01-Dec-25	03-Nov-25	104	CONS-EB-2190
095113 - ACOUSTICAL PANEL CEILINGS			98.22%	10	01-Sep-23 A	12-Dec-25	14-Nov-25	110	
PR0-09-1120	Prepare and submit acoustical panel ceilings product data	100%	100%	0	01-Sep-23 A	16-May-25 A	01-Nov-25		PR0-09-1110
PR0-09-1110	Review and approve acoustical panel ceilings product data	100%	100%	0	19-May-25 A	27-May-25 A	01-Nov-25		PR0-09-1020

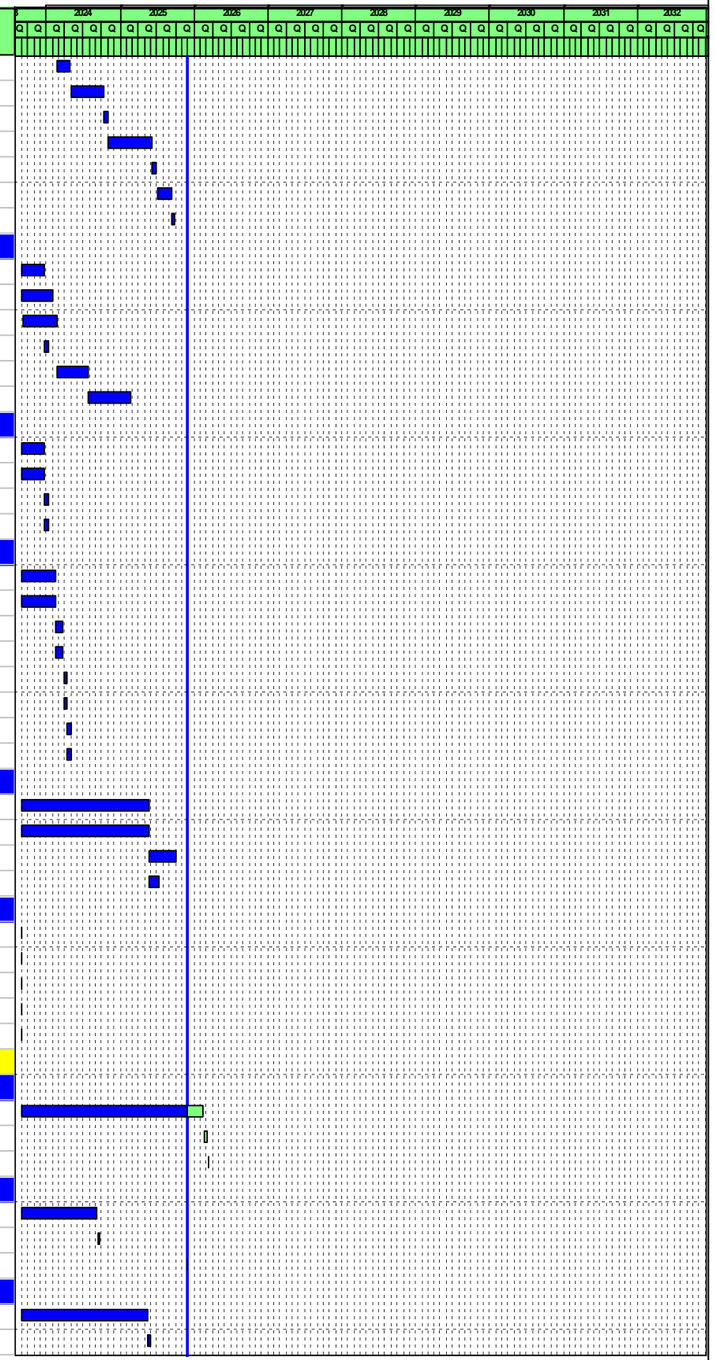


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PR0-09-1020	Fabrication and delivery of acoustical panel ceilings	0%	0%	10	01-Dec-25	12-Dec-25	14-Nov-25	110	CONS-EB-2210
096516 - RESILIENT SHEET FLOORING			99.82%	1	01-Sep-23 A	01-Dec-25	03-Nov-25	138	
PR0-09-1140	Prepare and submit Resilient sheet flooring product data	100%	100%	0	01-Sep-23 A	01-Jul-25 A	01-Nov-25		PR0-09-1130
PR0-09-1130	Review and approve Resilient sheet flooring product data	100%	100%	0	02-Jul-25 A	03-Jul-25 A	01-Nov-25		PR0-09-1030
PR0-09-1030	Fabrication and delivery of Resilient sheet flooring	0%	0%	1	01-Dec-25	01-Dec-25	03-Nov-25	138	CONS-EB-2280, CONS-
096623 - RESINOUS MATRIX TERRAZO FLOORING			89.32%	66	01-Sep-23 A	10-Mar-26	10-Feb-26	65	
PR0-09-1160	Prepare and submit terrazzo flooring product data	50%	50%	50	01-Sep-23 A	13-Feb-26	15-Jan-26	65	PR0-09-1150
PR0-09-1150	Review and approve terrazzo flooring product data	0%	0%	15	17-Feb-26	09-Mar-26	09-Feb-26	65	PR0-09-1040
PR0-09-1040	Fabrication and delivery of terrazzo flooring materials	0%	0%	1	10-Mar-26	10-Mar-26	10-Feb-26	65	CONS-EB-2220
096723 - RESINOUS FLOORING			99.82%	1	01-Sep-23 A	01-Dec-25	03-Nov-25	147	
PR0-09-1180	Prepare and submit resinous flooring product data	100%	100%	0	01-Sep-23 A	06-May-25 A	01-Nov-25		PR0-09-1170
PR0-09-1170	Review and approve resinous flooring product data	100%	100%	0	07-May-25 A	21-May-25 A	01-Nov-25		PR0-09-1050
PR0-09-1050	Fabrication and delivery of resinous flooring materials	0%	0%	1	01-Dec-25	01-Dec-25	03-Nov-25	147	CONS-EB-1420
099000 - PAINTING AND FINISHING			98.22%	10	01-Sep-23 A	12-Dec-25	14-Nov-25	122	
PR0-09-1200	Prepare and submit painting and finishing product data	100%	100%	0	01-Sep-23 A	22-Jul-25 A	01-Nov-25		PR0-09-1190
PR0-09-1190	Review and approve painting and finishing product data	100%	100%	0	23-Jul-25 A	30-Sep-25 A	01-Nov-25		PR0-09-1060
PR0-09-1060	Fabrication and delivery of paint	0%	0%	10	01-Dec-25	12-Dec-25	14-Nov-25	122	CONS-EB-2240
099600 - HIGH PERFORMANCE COATINGS			98.22%	10	01-Sep-23 A	12-Dec-25	14-Nov-25	138	
PR0-09-1210	Prepare and submit high performance coatings product data R0	100%	100%	0	01-Sep-23 A	22-Jul-25 A	01-Nov-25		PR0-09-1220, PR0-09-1
PR0-09-1211	Returned high performance coatings product data R0	100%	100%	0	23-Jul-25 A	07-Aug-25 A	01-Nov-25		PR0-09-1212
PR0-09-1212	Re-submit high performance coatings product data R1	100%	100%	0	08-Aug-25 A	15-Sep-25 A	01-Nov-25		PR0-09-1220
PR0-09-1220	Review and approve high performance coatings product data R1	100%	100%	0	16-Sep-25 A	30-Sep-25 A	01-Nov-25		PR0-09-1230
PR0-09-1230	Fabrication and delivery of coating material	0%	0%	10	01-Dec-25	12-Dec-25	14-Nov-25	138	CONS-EB-1420
DIVISION 10 - SPECIALTIES			88.04%	75	01-Sep-23 A	24-Mar-26	20-Jul-26	113	
101400 - SIGNAGE			88.04%	75	01-Sep-23 A	24-Mar-26	20-Jul-26	113	
PRO-10-1000	Prepare and submit signage sample	0%	80%	50	01-Sep-23 A	13-Feb-26	12-Jun-26	113	PRO-10-1020
PRO-10-1010	Prepare and submit signage product data	0%	80%	50	01-Sep-23 A	13-Feb-26	12-Jun-26	113	PRO-10-1030
PRO-10-1040	Prepare and submit signage shop drawings	0%	80%	50	01-Sep-23 A	13-Feb-26	12-Jun-26	113	PRO-10-1050
PRO-10-1020	Review and approve signage sample	0%	0%	15	17-Feb-26	09-Mar-26	03-Jul-26	113	PR0-10-1460
PRO-10-1030	Review and approve signage product data	0%	0%	15	17-Feb-26	09-Mar-26	03-Jul-26	113	PR0-10-1460
PRO-10-1050	Review and approve signage shop drawings	0%	0%	15	17-Feb-26	09-Mar-26	03-Jul-26	113	PR0-10-1460
PR0-10-1460	Fabrication and delivery of signage	0%	0%	10	10-Mar-26	24-Mar-26	20-Jul-26	113	CONS-EB-1580
102113 - TOILET PARTITIONS			96.5%	20	01-Sep-23 A	30-Dec-25	01-Dec-25	157	
PRO-10-1060	Prepare and submit toilet partitions sample	100%	100%	0	01-Sep-23 A	17-Dec-24 A	01-Nov-25		PRO-10-1090
PRO-10-1070	Prepare and submit toilet partitions product data	100%	100%	0	01-Sep-23 A	31-Oct-24 A	01-Nov-25		PRO-10-1100
PRO-10-1080	Prepare and submit toilet partitions shop drawings	100%	100%	0	01-Sep-23 A	31-Oct-24 A	01-Nov-25		PRO-10-1110
PRO-10-1100	Review and approve toilet partitions product data	100%	100%	0	01-Nov-24 A	07-Nov-24 A	01-Nov-25		PR0-10-1470
PRO-10-1110	Review and approve toilet partitions shop drawings	100%	100%	0	01-Nov-24 A	07-Nov-24 A	01-Nov-25		PR0-10-1470
PRO-10-1090	Review and approve toilet partitions sample	100%	100%	0	18-Dec-24 A	03-Jan-25 A	01-Nov-25		PR0-10-1470
PR0-10-1470	Fabrication and delivery of toilet partitions	0%	0%	20	01-Dec-25	30-Dec-25	01-Dec-25	157	CONS-EB-1380, CONS-
102219 - INTERIOR GLASS PARTITIONS			100%	0	01-Sep-23 A	30-Sep-25 A	01-Nov-25		
PRO-10-1120	Prepare and submit interior glass partitions sample	100%	100%	0	01-Sep-23 A	08-Apr-24 A	01-Nov-25		PRO-10-1150
PRO-10-1130	Prepare and submit interior glass partitions product data R0	100%	100%	0	01-Sep-23 A	20-Dec-23 A	01-Nov-25		PRO-10-1131
PRO-10-1140	Prepare and submit interior glass partitions shop drawings Rev.0	100%	100%	0	01-Sep-23 A	06-Feb-24 A	01-Nov-25		PRO-10-1170, PRO-10-1
PRO-10-1131	Returned interior glass partitions product data R0	100%	100%	0	21-Dec-23 A	13-Mar-24 A	01-Nov-25		PRO-10-1132
PRO-10-1141	Returned interior glass partitions shop drawings Rev.0	100%	100%	0	07-Feb-24 A	23-Feb-24 A	01-Nov-25		PRO-10-1142
PRO-10-1142	Re-submit interior glass partitions shop drawings rev.1	100%	100%	0	26-Feb-24 A	04-Apr-24 A	01-Nov-25		PRO-10-1143
PRO-10-1132	Re-submit interior glass partitions product data R1	100%	100%	0	14-Mar-24 A	04-Apr-24 A	01-Nov-25		PRO-10-1133
PRO-10-1133	Returned interior glass partitions product data R1	100%	100%	0	05-Apr-24 A	22-Apr-24 A	01-Nov-25		PRO-10-1134
PRO-10-1143	Returned interior glass partitions shop drawings Rev.1	100%	100%	0	05-Apr-24 A	22-Apr-24 A	01-Nov-25		PRO-10-1144
PRO-10-1150	Review and approve interior glass partitions sample	100%	100%	0	09-Apr-24 A	22-Apr-24 A	01-Nov-25		PR0-10-1480

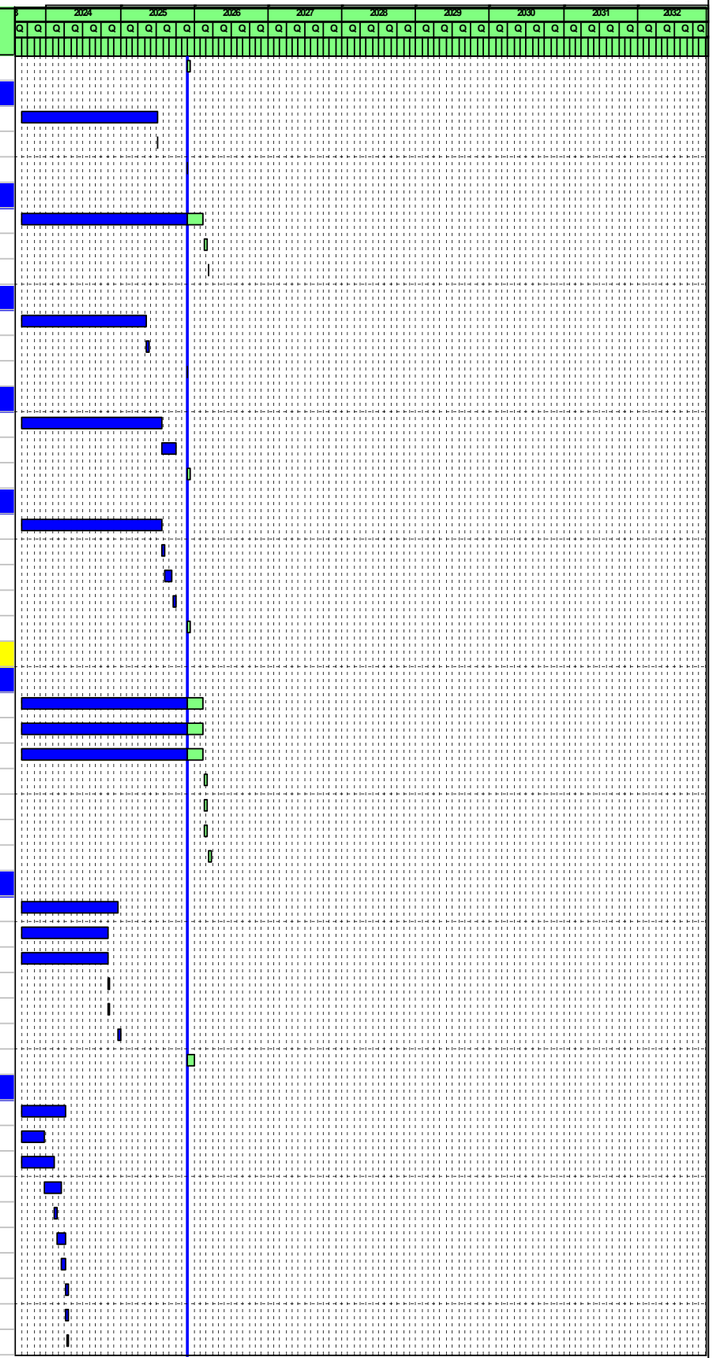


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PRO-10-1134	Re-submit interior glass partitions product data R2	100%	100%	0	23-Apr-24 A	02-Jun-25 A	01-Nov-25		PRO-10-1160
PRO-10-1144	Re-submit interior glass partitions shop drawings rev.2	100%	100%	0	23-Apr-24 A	30-Jun-25 A	01-Nov-25		PRO-10-1170
PRO-10-1170	Review and approve interior glass partitions shop drawings Rev.2	100%	100%	0	25-Apr-25 A	30-Sep-25 A	01-Nov-25		PR0-10-1480
PRO-10-1160	Review and approve interior glass partitions product data R2	100%	100%	0	03-Jun-25 A	01-Jul-25 A	01-Nov-25		PR0-10-1480
102623 - PROTECTIVE WALL COVERING			90.2%	60	01-Sep-23 A	02-Mar-26	30-Jan-26	80	
PRO-10-1190	Prepare and submit protective wall covering product data	50%	50%	25	01-Sep-23 A	07-Jan-26	08-Dec-25	80	PRO-10-1220
PRO-10-1200	Prepare and submit protective wall covering shop drawings	50%	50%	25	01-Sep-23 A	07-Jan-26	08-Dec-25	80	PRO-10-1230
PRO-10-1220	Review and approve protective wall covering product data	0%	0%	15	08-Jan-26	29-Jan-26	31-Dec-25	80	PR0-10-1490
PRO-10-1230	Review and approve protective wall covering shop drawings	0%	0%	15	08-Jan-26	29-Jan-26	31-Dec-25	80	PR0-10-1490
PR0-10-1490	Fabrication and delivery of protective wall covering	0%	0%	20	30-Jan-26	02-Mar-26	30-Jan-26	80	CONS-EB-2260
102813 - TOILET ACCESSORIES			98.22%	10	01-Sep-23 A	12-Dec-25	14-Nov-25	167	
PRO-10-1240	Prepare and submit protective toilet accessories product data	100%	100%	0	01-Sep-23 A	31-Oct-24 A	01-Nov-25		PRO-10-1260
PRO-10-1260	Review and approve protective toilet accessories product data	100%	100%	0	01-Nov-24 A	04-Nov-24 A	01-Nov-25		PR0-10-1500
PR0-10-1500	Fabrication and delivery of protective toilet accessories	0%	0%	10	01-Dec-25	12-Dec-25	14-Nov-25	167	CONS-EB-1380, CONS-
104416 - FIRE EXTINGUISHERS AND CABINETS			98.22%	10	01-Sep-23 A	12-Dec-25	14-Nov-25	146	
PRO-10-1270	Prepare and submit fire extinguishers and cabinets product data	100%	100%	0	01-Sep-23 A	31-Oct-24 A	01-Nov-25		PRO-10-1280
PRO-10-1280	Review and approve fire extinguishers and cabinets product data	100%	100%	0	01-Nov-24 A	04-Nov-24 A	01-Nov-25		PR0-10-1510
PR0-10-1510	Fabrication and delivery of fire extinguishers and cabinets	0%	0%	10	01-Dec-25	12-Dec-25	14-Nov-25	146	CONS-EB-1580, CONS-
109000 - MISCELLANEOUS SPECIALTIES			92.46%	45	01-Sep-23 A	06-Feb-26	08-Jan-26	132	
PRO-10-1290	Prepare and submit miscellaneous specialties product data	50%	50%	25	01-Sep-23 A	07-Jan-26	08-Dec-25	132	PRO-10-1310
PRO-10-1310	Review and approve miscellaneous specialties product data	0%	0%	15	08-Jan-26	29-Jan-26	31-Dec-25	132	PR0-10-1520
PR0-10-1520	Fabrication and delivery of miscellaneous specialties	0%	0%	5	30-Jan-26	06-Feb-26	08-Jan-26	132	CONS-EB-1380, CONS-
DIVISION 11 - EQUIPMENT			100%	0	01-Sep-23 A	16-May-25 A	01-Nov-25		
113100 - APPLIANCES			100%	0	01-Sep-23 A	13-Jun-24 A	01-Nov-25		
PRO-11-1000	Prepare and submit appliances catalog cuts	100%	100%	0	01-Sep-23 A	29-May-24 A	01-Nov-25		PRO-11-1010, PRO-11-1
PRO-11-1010	Review and approve appliances catalog cuts	100%	100%	0	07-Feb-24 A	13-Jun-24 A	01-Nov-25		PR0-11-1020
114000 - FOOD EQUIPMENT			100%	0	01-Sep-23 A	16-May-25 A	01-Nov-25		
PRO-11-1040	Prepare and submit food service equipment	100%	100%	0	01-Sep-23 A	01-May-25 A	01-Nov-25		PRO-11-1050, PRO-11-1
PRO-11-1050	Review and approve food service equipment	100%	100%	0	02-May-25 A	16-May-25 A	01-Nov-25		PR0-11-1030
DIVISION 12 - FURNISHINGS			98.22%	10	01-Sep-23 A	12-Dec-25	14-Nov-25	135	
124813 - ENTRANCE FLOOR MATS AND FRAMES			98.22%	10	01-Sep-23 A	12-Dec-25	14-Nov-25	60	
PRO-12-1050	Prepare and submit entrance floor mats and frame product data	100%	100%	0	01-Sep-23 A	09-Sep-24 A	01-Nov-25		PRO-12-1010
PRO-12-1010	Review and approve entrance floor mats and frame product data	100%	100%	0	10-Sep-24 A	10-Sep-24 A	01-Nov-25		PR0-12-1020
PR0-12-1020	Fabrication and delivery of entrance floor mats and frames	0%	0%	10	01-Dec-25	12-Dec-25	14-Nov-25	60	CONS-EB-1160
129313 - BICYCLE RACKS			100%	0	01-Sep-23 A	26-Nov-24 A	01-Nov-25		
PRO-12-1030	Prepare and submit bicycle racks product data	100%	100%	0	01-Sep-23 A	21-Oct-24 A	01-Nov-25		PRO-12-1040
PRO-12-1040	Review and approve bicycle racks product data	100%	100%	0	21-Oct-24 A	21-Oct-24 A	01-Nov-25		PR0-12-1000
PR0-12-1000	Fabrication and delivery of bicycle racks	100%	100%	0	22-Oct-24 A	26-Nov-24 A	01-Nov-25		SITE-1100
DIVISION 13 - SPECIAL CONSTRUCTION			93.24%	40	01-Sep-23 A	29-Jan-26	31-Dec-25	40	
134900 - X-RAY PROTECTION			93.24%	40	01-Sep-23 A	29-Jan-26	31-Dec-25	40	
PR0-13-1010	Prepare and submit x-ray protection product data	50%	50%	25	01-Sep-23 A	07-Jan-26	08-Dec-25	40	PR0-13-1030
PR0-13-1020	Prepare and submit x-ray protection shop drawings	50%	50%	25	01-Sep-23 A	07-Jan-26	08-Dec-25	40	PR0-13-1040
PR0-13-1030	Review and approve x-ray protection product data	0%	0%	15	08-Jan-26	29-Jan-26	31-Dec-25	40	PR0-13-1000
PR0-13-1040	Review and approve x-ray protection shop drawings	0%	0%	15	08-Jan-26	29-Jan-26	31-Dec-25	40	PR0-13-1000
DIVISION 14 - CONVEYING EQUIPMENT			100%	0	16-Oct-23 A	12-Mar-24 A	01-Nov-25		
142400 - HYDRAULIC PASSENGER ELEVATOR			100%	0	16-Oct-23 A	12-Mar-24 A	01-Nov-25		
PRO-14-1000	Prepare and submit hydraulic passenger elevator product data R0	100%	100%	0	16-Oct-23 A	26-Oct-23 A	01-Nov-25		PRO-14-1020, PRO-14-
PRO-14-1010	Prepare and submit hydraulic passenger elevator shop drawings R0	100%	100%	0	16-Oct-23 A	23-Oct-23 A	01-Nov-25		PRO-14-1030, PRO-14-
PRO-14-1011	Return hydraulic passenger elevator shop drawings R0	100%	100%	0	24-Oct-23 A	21-Nov-23 A	01-Nov-25		PRO-14-1012
PRO-14-1001	Return hydraulic passenger elevator product data R0	100%	100%	0	27-Oct-23 A	21-Nov-23 A	01-Nov-25		PRO-14-1002
PRO-14-1002	Re-submit hydraulic passenger elevator product data R1	100%	100%	0	22-Nov-23 A	23-Feb-24 A	01-Nov-25		PRO-14-1020

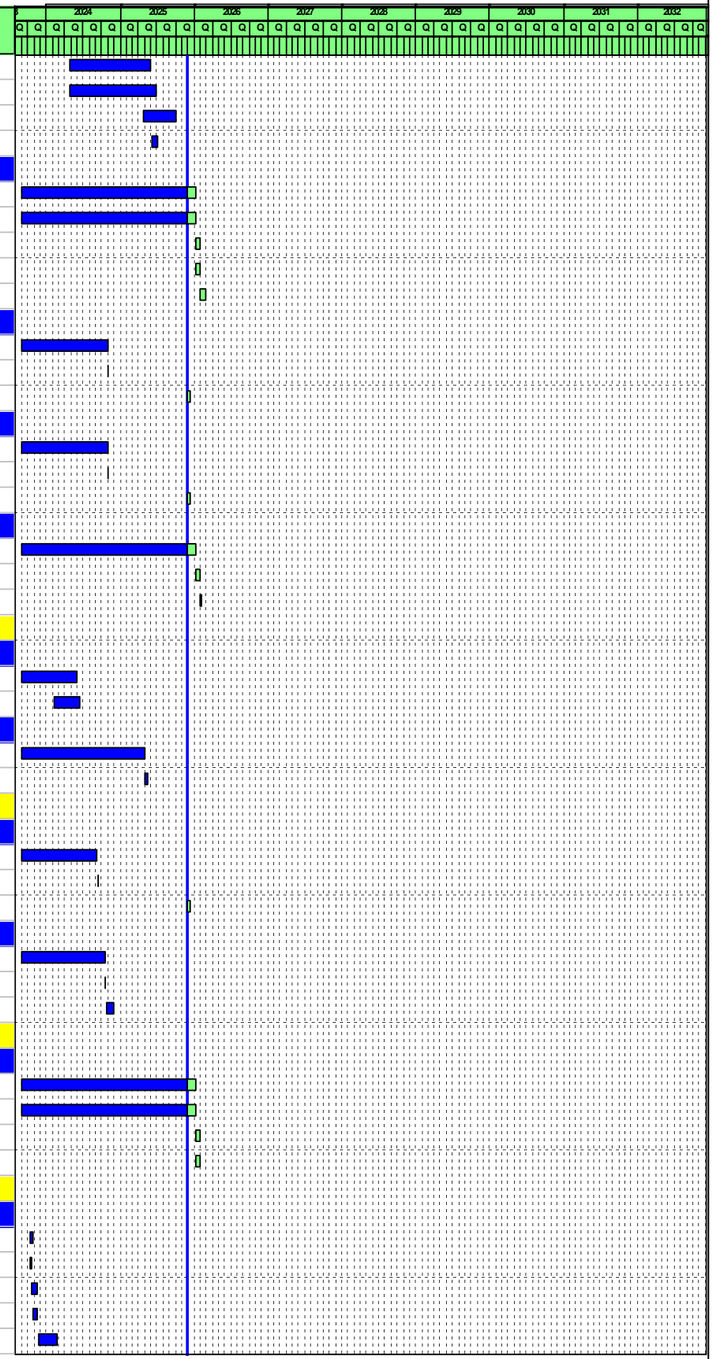


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PRO-14-1012	Re-submit hydraulic passenger elevator shop drawings R1	100%	100%	0	22-Nov-23 A	23-Feb-24 A	01-Nov-25		PRO-14-1030
PRO-14-1020	Review and approve hydraulic passenger elevator product data R1	100%	100%	0	26-Feb-24 A	12-Mar-24 A	01-Nov-25		PR0-14-1040, CONS-CI
PRO-14-1030	Review and approve hydraulic passenger elevator shop drawings R1	100%	100%	0	26-Feb-24 A	12-Mar-24 A	01-Nov-25		PR0-14-1040, CONS-CI
DIVISION 21 - FIRE SUPPRESSION			95.81%	22	26-Sep-23 A	02-Jan-26	16-Dec-25	64	
210800 - Cx FOR FIRE SUPPRESSION SYSTEMS			99.7%	2	26-Sep-23 A	02-Dec-25	16-Dec-25	83	
PRO-21-1000	Prepare and submit fire suppression system product data	100%	100%	0	26-Sep-23 A	27-Oct-25 A	24-Nov-25		PRO-21-1020
PRO-21-1010	Prepare and submit fire suppression system shop drawings Rev.0	100%	100%	0	26-Sep-23 A	11-Nov-24 A	01-Nov-25		PRO-21-1030, PRO-10-
PRO-10-1011	Returned fire suppression system shop drawings Rev.0	100%	100%	0	12-Nov-24 A	26-Nov-24 A	01-Nov-25		PRO-21-1012
PRO-21-1012	Re-submit fire suppression system shop drawings Rev.1	100%	100%	0	27-Nov-24 A	07-Oct-25 A	01-Nov-25		PRO-21-1030
PRO-21-1030	Review and approve fire suppression system shop drawings Rev.1	100%	100%	0	08-Oct-25 A	27-Oct-25 A	01-Nov-25		PR0-21-1080, PRO-1-1C
PRO-21-1020	Review and approve fire suppression system product data	90%	90%	2	28-Oct-25 A	02-Dec-25	16-Dec-25	83	PR0-21-1080, CONS-CI
211200 - FIRE STANDPIPE AND AUTOMATIC SPRINKLER SYSTEM			95.81%	22	26-Sep-23 A	02-Jan-26	03-Dec-25	64	
PRO-21-1040	Prepare and submit fire standpipe/automatic sprinkler system product data	100%	100%	0	26-Sep-23 A	19-Feb-24 A	01-Nov-25		PRO-21-1060
PRO-21-1050	Prepare and submit fire standpipe/automatic sprinkler system shop drawings R0	100%	100%	0	26-Sep-23 A	18-Sep-24 A	01-Nov-25		PRO-21-1070, PRO-21-
PRO-21-1060	Review and approve fire standpipe/automatic sprinkler system product data	90%	90%	2	20-Feb-24 A	02-Dec-25	04-Nov-25	64	PR0-21-1090, CONS-CI
PRO-21-1051	Returned fire standpipe/automatic sprinkler system shop drawings R0	100%	100%	0	19-Sep-24 A	26-Nov-24 A	01-Nov-25		PRO-21-1052
PRO-21-1052	Re-submit fire standpipe/automatic sprinkler system shop drawings R1	100%	100%	0	27-Nov-24 A	07-Oct-25 A	01-Nov-25		PRO-21-1070
PRO-21-1070	Review and approve fire standpipe/automatic sprinkler system shop drawings	100%	100%	0	08-Oct-25 A	27-Oct-25 A	01-Nov-25		PR0-21-1090, PRO-1-1C
PR0-21-1090	Fabrication and delivery of fire standpipe/automatic sprinkler system	0%	0%	20	02-Dec-25	02-Jan-26	03-Dec-25	64	CONS-EB-6130
DIVISION 22 - PLUMBING			87.54%	70	26-Sep-23 A	18-Mar-26	10-Mar-26	102	
220514 - PLUMBING MOTORS AND MOTOR CONTROLLERS			100%	0	26-Sep-23 A	27-Oct-25 A	31-Dec-25		
PRO-22-1020	Prepare and submit motors and motor controllers product data	100%	100%	0	26-Sep-23 A	08-Oct-25 A	08-Dec-25		PRO-22-1040
PRO-22-1030	Prepare and submit motors and motor controllers shop drawings	100%	100%	0	26-Sep-23 A	08-Oct-25 A	08-Dec-25		PRO-22-1050
PRO-22-1040	Review and approve motors and motor controllers product data	100%	100%	0	09-Oct-25 A	27-Oct-25 A	31-Dec-25		PR0-22-1370, CONS-CI
PRO-22-1050	Review and approve motors and motor controllers shop drawings	100%	100%	0	09-Oct-25 A	27-Oct-25 A	31-Dec-25		PR0-22-1370, CONS-CI
220523 - GENERAL DUTY VALVES FOR PLUMBING PIPING			100%	0	26-Sep-23 A	13-May-25 A	01-Nov-25		
PRO-22-1060	Prepare and submit duty valves product data	100%	100%	0	26-Sep-23 A	06-Nov-23 A	01-Nov-25		PRO-22-1080
PRO-22-1070	Prepare and submit duty valves shop drawings	100%	100%	0	26-Sep-23 A	06-Nov-23 A	01-Nov-25		PRO-22-1090
PRO-22-1080	Review and approve duty valves product data	100%	100%	0	07-Nov-23 A	05-Dec-23 A	01-Nov-25		PR0-22-1380, CONS-CI
PRO-22-1090	Review and approve duty valves shop drawings	100%	100%	0	07-Nov-23 A	05-Dec-23 A	01-Nov-25		PR0-22-1380, CONS-CI
PR0-22-1380	Fabrication and delivery of valves for plumbing piping	100%	100%	0	06-Dec-23 A	13-May-25 A	01-Nov-25		CONS-EB-1670, CONS-
220711 - PLUMBING INSULATION			93.01%	37	26-Sep-23 A	26-Jan-26	26-Dec-25	39	
PRO-22-1100	Prepare and submit plumbing insulation product data	80%	80%	12	26-Sep-23 A	17-Dec-25	18-Nov-25	39	PRO-22-1120
PRO-22-1110	Prepare and submit plumbing insulation shop drawings	80%	80%	12	26-Sep-23 A	17-Dec-25	18-Nov-25	39	PRO-22-1130
PRO-22-1120	Review and approve plumbing insulation product data	0%	0%	15	18-Dec-25	09-Jan-26	10-Dec-25	39	PR0-22-1390, CONS-CI
PRO-22-1130	Review and approve plumbing insulation shop drawings	0%	0%	15	18-Dec-25	09-Jan-26	10-Dec-25	39	PR0-22-1390, CONS-CI
PR0-22-1390	Fabrication and delivery of plumbing insulation	0%	0%	10	12-Jan-26	26-Jan-26	26-Dec-25	39	CONS-EB-6540
221000 - FUEL GAS SYSTEMS			100%	0	26-Sep-23 A	23-Jun-25 A	03-Nov-25		
PRO-22-1140	Prepare and submit fuel gas systems product data	100%	100%	0	26-Sep-23 A	23-Jun-25 A	01-Nov-25		PRO-22-1160
PRO-22-1150	Prepare and submit fuel gas systems shop drawings	100%	100%	0	26-Sep-23 A	23-Jun-25 A	03-Nov-25		PRO-22-1170
PRO-22-1160	Review and approve fuel gas systems product data	100%	100%	0	23-Jun-25 A	23-Jun-25 A	03-Nov-25		PR0-22-1400, CONS-CI
PRO-22-1170	Review and approve fuel gas systems shop drawings	100%	100%	0	23-Jun-25 A	23-Jun-25 A	03-Nov-25		PR0-22-1400, PRO-1-1C
221100 - WATER DISTRIBUTION PIPING			100%	0	26-Sep-23 A	30-Oct-25 A	14-Nov-25		
PRO-22-1180	Prepare and submit water distribution piping product data	100%	100%	0	26-Sep-23 A	02-Oct-25 A	01-Nov-25		PRO-22-1200, PRO-22-
PRO-22-1190	Prepare and submit water distribution piping shop drawings (Delayed by Bulletins)	100%	100%	0	26-Sep-23 A	28-Jul-25 A	01-Nov-25		PRO-22-1210, PRO-22-
PRO-22-1200	Review and approve water distribution piping product data	100%	100%	0	27-Nov-23 A	14-Oct-25 A	01-Nov-25		PR0-22-1410, CONS-CI
PRO-22-1210	Review and approve water distribution piping shop drawings	100%	100%	0	27-Nov-23 A	10-Sep-25 A	01-Nov-25		PR0-22-1410, PRO-1-1C
PR0-22-1410	Fabrication and delivery of water distribution piping	100%	100%	0	27-Oct-25 A	30-Oct-25 A	14-Nov-25		CONS-EB-6370
221300 - SANITARY, WASTE AND STORM DRAINAGE			100%	0	26-Sep-23 A	13-May-25 A	01-Nov-25		
PRO-22-1220	Prepare and submit sanitary, p&d product data R0	100%	100%	0	26-Sep-23 A	03-Nov-23 A	01-Nov-25		PRO-22-1240, PRO-22-
PRO-22-1230	Prepare and submit sanitary, p&d shop drawings (Delayed by Bulletins)	100%	100%	0	26-Sep-23 A	06-Dec-24 A	01-Nov-25		PRO-22-1250

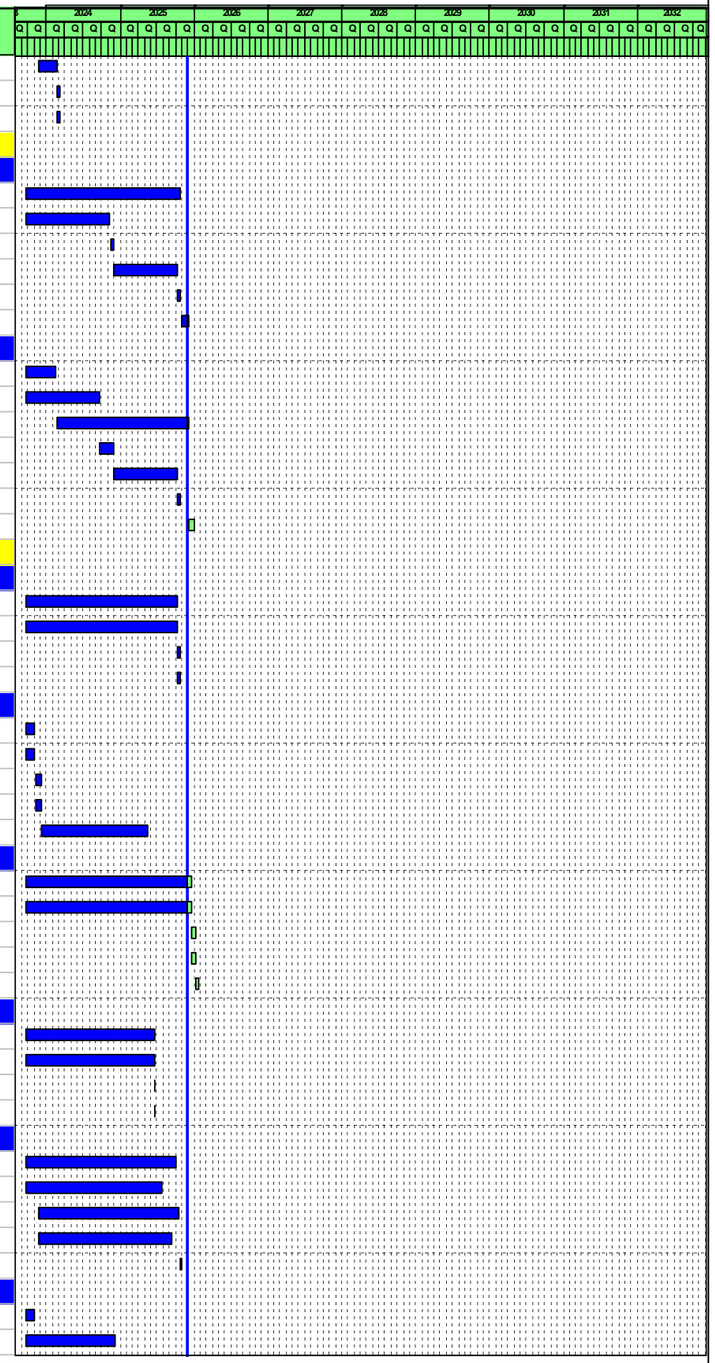

Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PRO-22-1221	Returned sanitary, p&d product data R0	100%	100%	0	07-Nov-23 A	21-Nov-23 A	01-Nov-25		PRO-22-1222
PRO-22-1222	Re-submit sanitary, p&d product data R1	100%	100%	0	22-Nov-23 A	05-Dec-23 A	01-Nov-25		PRO-22-1240
PRO-22-1240	Review and approve sanitary, p&d product data R1	100%	100%	0	06-Dec-23 A	10-Jan-24 A	01-Nov-25		PR0-22-1420, CONS-CI
PRO-22-1250	Review and approve sanitary, p&d shop drawings	100%	100%	0	09-Dec-24 A	24-Jan-25 A	01-Nov-25		PR0-22-1420, PRO-1-1C
PR0-22-1420	Fabrication and delivery of pipe, fittings, drains, cleanouts, valves, traps, grease & sand interceptor	100%	100%	0	01-May-25 A	13-May-25 A	01-Nov-25		CONS-EB-1670
223000 - PLUMBING EQUIPMENT AND ACCESSORIES			87.54%	70	26-Sep-23 A	18-Mar-26	10-Mar-26	82	
PRO-22-1260	Prepare and submit plumbing equipment and accessories product data R0	100%	100%	0	26-Sep-23 A	06-Nov-23 A	01-Nov-25		PRO-22-1261
PRO-22-1270	Prepare and submit equipment and accessories shop drawings R0	100%	100%	0	26-Sep-23 A	06-Nov-23 A	01-Nov-25		PRO-22-1271
PRO-22-1261	Return equipment and accessories product data R0	100%	100%	0	07-Nov-23 A	10-Nov-23 A	01-Nov-25		PRO-22-1262
PRO-22-1271	Return equipment and accessories shop drawings R0	100%	100%	0	07-Nov-23 A	10-Nov-23 A	01-Nov-25		PRO-22-1272
PRO-22-1262	Re-submit plumbing equipment and accessories product data R1	100%	100%	0	13-Nov-23 A	01-Feb-24 A	01-Nov-25		PRO-22-1263
PRO-22-1272	Re-submit equipment and accessories shop drawings R1	100%	100%	0	13-Nov-23 A	01-Feb-24 A	01-Nov-25		PRO-22-1373
PRO-22-1263	Return equipment and accessories product data R1	100%	100%	0	02-Feb-24 A	21-Feb-24 A	01-Nov-25		PRO-22-1264
PRO-22-1373	Return equipment and accessories shop drawings R1	100%	100%	0	02-Feb-24 A	21-Feb-24 A	01-Nov-25		PRO-22-1374
PRO-22-1264	Re-submit plumbing equipment and accessories product data R2	100%	100%	0	22-Feb-24 A	08-Mar-24 A	01-Nov-25		PRO-22-1280, PRO-22-'
PRO-22-1374	Re-submit equipment and accessories shop drawings R2	100%	100%	0	22-Feb-24 A	08-Mar-24 A	01-Nov-25		PRO-22-1375
PRO-22-1265	Return equipment and accessories product data R2	100%	100%	0	11-Mar-24 A	14-Mar-24 A	01-Nov-25		PRO-22-1266
PRO-22-1375	Return equipment and accessories shop drawings R2	100%	100%	0	11-Mar-24 A	14-Mar-24 A	01-Nov-25		PRO-22-1376
PRO-22-1266	Re-submit plumbing equipment and accessories product data R3	100%	100%	0	15-Mar-24 A	20-Nov-25 A	14-Nov-25		PRO-22-1280
PRO-22-1376	Re-submit equipment and accessories shop drawings R3	100%	100%	0	15-Mar-24 A	20-Nov-25 A	14-Nov-25		PRO-22-1290
PRO-22-1280	Review and approve equipment and accessories product data R3	33%	33%	10	21-Nov-25 A	16-Dec-25	08-Dec-25	82	PR0-22-1430, CONS-CI
PRO-22-1290	Review and approve equipment and accessories shop drawings R3	33%	33%	10	21-Nov-25 A	16-Dec-25	08-Dec-25	82	PR0-22-1430, CONS-CI
PR0-22-1430	Fabrication and delivery of plumbing equipment and accessories	0%	0%	60	16-Dec-25	18-Mar-26	10-Mar-26	82	CONS-EB-3400
224000 - PLUMBING FIXTURES			88.33%	65	26-Sep-23 A	09-Mar-26	09-Feb-26	107	
PRO-22-1300	Prepare and submit plumbing fixtures product data R0	100%	100%	0	26-Sep-23 A	18-Jan-24 A	01-Nov-25		PRO-22-1301
PRO-22-1301	Returned plumbing fixtures product data R0	100%	100%	0	19-Jan-24 A	13-Feb-24 A	01-Nov-25		PRO-22-1302
PRO-22-1302	Re-submit plumbing fixtures product data R1	100%	100%	0	14-Feb-24 A	23-Apr-24 A	01-Nov-25		PRO-22-1303
PRO-22-1303	Returned plumbing fixtures product data R1	100%	100%	0	24-Apr-24 A	06-May-24 A	01-Nov-25		PRO-22-1304
PRO-22-1304	Re-submit plumbing fixtures product data R2	100%	100%	0	07-May-24 A	30-Jul-24 A	01-Nov-25		PRO-22-1320, PRO-22-'
PRO-22-1305	Returned plumbing fixtures product data R2	100%	100%	0	31-Jul-24 A	19-Aug-24 A	01-Nov-25		PRO-22-1306
PRO-22-1306	Re-submit plumbing fixtures product data R3	50%	50%	10	20-Aug-24 A	12-Dec-25	14-Nov-25	107	PRO-22-1320
PRO-22-1320	Review and approve plumbing fixtures product data R3	0%	0%	15	16-Dec-25	07-Jan-26	08-Dec-25	107	PR0-22-1440, CONS-CI
PR0-22-1440	Fabrication and delivery of plumbing fixtures	0%	0%	40	08-Jan-26	09-Mar-26	09-Feb-26	107	CONS-EB-6295, CONS-
227000 - MEDICAL GAS SYSTEM			93.36%	35	26-Sep-23 A	22-Jan-26	23-Dec-25	71	
PRO-22-1330	Prepare and submit medical gas system product data R0	100%	100%	0	26-Sep-23 A	24-Feb-25 A	01-Nov-25		PRO-22-1331
PRO-22-1340	Prepare and submit medical gas system shop drawings	50%	50%	20	26-Sep-23 A	30-Dec-25	01-Dec-25	71	PRO-22-1360
PRO-22-1331	Returned medical gas system product data R0	100%	100%	0	25-Feb-25 A	11-Mar-25 A	01-Nov-25		PRO-22-1332
PRO-22-1332	Re-submit medical gas system product data R1	25%	25%	15	12-Mar-25 A	22-Dec-25	24-Nov-25	76	PRO-22-1350
PRO-22-1350	Review and approve medical gas system product data R1	0%	0%	15	23-Dec-25	14-Jan-26	16-Dec-25	76	PR0-22-1450, CONS-CI
PRO-22-1360	Review and approve medical gas system shop drawings	0%	0%	15	31-Dec-25	22-Jan-26	23-Dec-25	71	PR0-22-1450, PRO-1-1C
DIVISION 23 - HEATING, VENTILATING AND AIR CONDITIONING			90.77%	50	30-Aug-23 A	13-Feb-26	16-Dec-25	138	
230513 - HVAC MOTORS			100%	0	01-Sep-23 A	20-May-25 A	01-Nov-25		
PRO-23-1000	Prepare and submit hvac motor product data R0	100%	100%	0	01-Sep-23 A	01-Sep-23 A	01-Nov-25		PRO-23-1020, PRO-23-'
PRO-23-1010	Prepare and submit hvac motor shop drawings R0	100%	100%	0	01-Sep-23 A	01-Sep-23 A	01-Nov-25		PRO-23-1030, PRO-23-'
PRO-23-1001	Return hvac motor product data R0	100%	100%	0	05-Sep-23 A	15-Sep-23 A	01-Nov-25		PRO-23-1002
PRO-23-1011	Return hvac motor shop drawings R0	100%	100%	0	05-Sep-23 A	15-Sep-23 A	01-Nov-25		PRO-23-1012
PRO-23-1002	Re-submit hvac motor product data R1	100%	100%	0	18-Sep-23 A	01-May-25 A	01-Nov-25		PRO-23-1020
PRO-23-1012	Re-submit hvac motor shop drawings R1	100%	100%	0	18-Sep-23 A	01-May-25 A	01-Nov-25		PRO-23-1030
PRO-23-1020	Review and approve hvac motor product data R1	100%	100%	0	02-May-25 A	20-May-25 A	01-Nov-25		CONS-EB-1320, CONS-
PRO-23-1030	Review and approve hvac motor shop drawings R1	100%	100%	0	02-May-25 A	20-May-25 A	01-Nov-25		CONS-EB-1320, CONS-
230514 - VARIABLE FREQUENCY DRIVES (VFD)			100%	0	25-Sep-23 A	25-Sep-23 A	01-Nov-25		

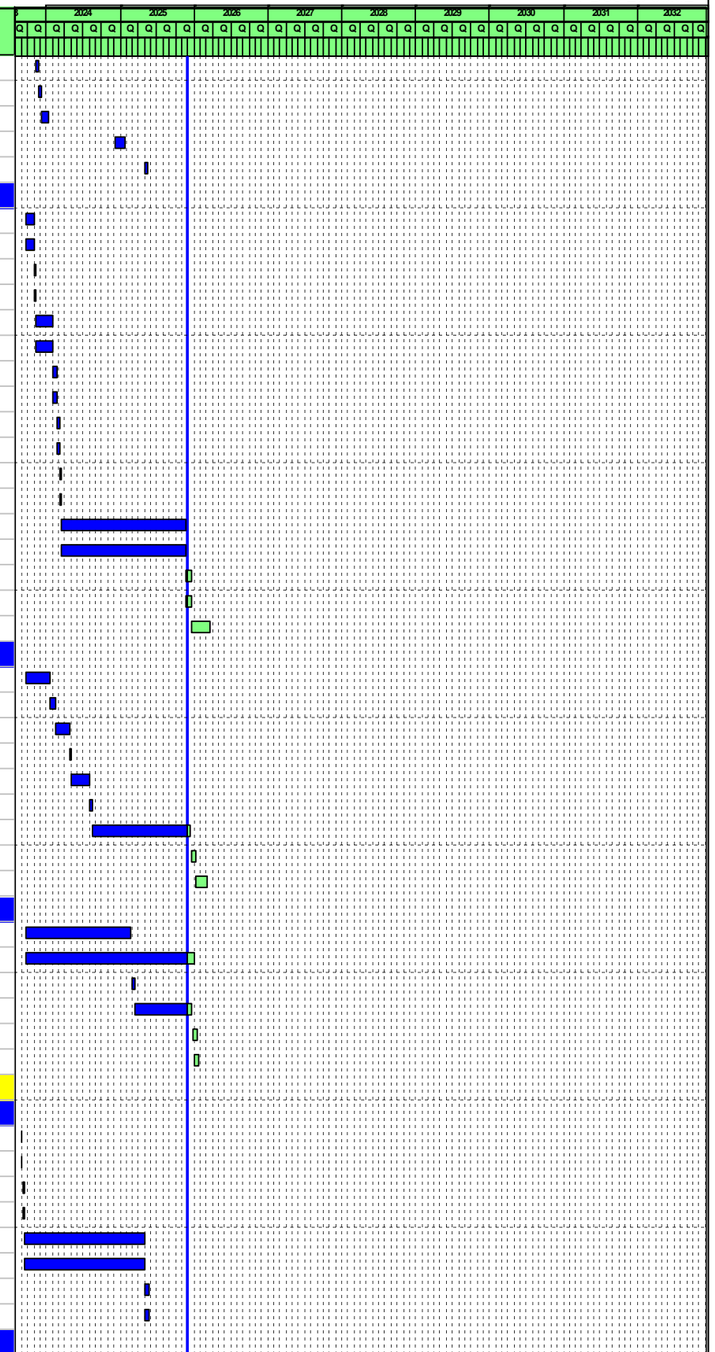


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PRO-23-1060	Review and approve hvac vfd product data (Not in Scope)	100%	100%	0	25-Sep-23 A	25-Sep-23 A	01-Nov-25		PR0-23-1430, CONS-CL
PRO-23-1040	Prepare and submit hvac vfd product data (Not in Scope)	100%	100%	0	25-Sep-23 A	25-Sep-23 A	01-Nov-25		PRO-23-1060
PRO-23-1070	Review and approve hvac vfd shop drawings (Not in Scope)	100%	100%	0	25-Sep-23 A	25-Sep-23 A	01-Nov-25		PR0-23-1430, CONS-CL
PRO-23-1050	Prepare and submit hvac vfd shop drawings (Not in Scope)	100%	100%	0	25-Sep-23 A	25-Sep-23 A	01-Nov-25		PRO-23-1070
230548 - VIBRATION & SEISMIC CONTROL FOR HVAC			90.77%	50	25-Sep-23 A	13-Feb-26	08-Dec-25	35	
PRO-23-1080	Prepare and submit vibration & seismic control for hvac product data R0	100%	100%	0	25-Sep-23 A	19-Dec-23 A	01-Nov-25		PRO-23-1081
PRO-23-1090	Prepare and submit vibration & seismic control for hvac shop drawings R0	100%	100%	0	25-Sep-23 A	19-Dec-23 A	01-Nov-25		PRO-23-1091
PRO-23-1081	Return vibration & seismic control for hvac product data R0	100%	100%	0	20-Dec-23 A	21-Feb-24 A	01-Nov-25		PRO-23-1082
PRO-23-1091	Return vibration & seismic control for hvac shop drawings R0	100%	100%	0	20-Dec-23 A	21-Feb-24 A	01-Nov-25		PRO-23-1092
PRO-23-1082	Re-submit vibration & seismic control for hvac product data R1	100%	100%	0	22-Feb-24 A	27-Jun-25 A	01-Nov-25		PRO-23-1100, PRO-23-
PRO-23-1092	Re- submit vibration & seismic control for hvac shop drawings R1	100%	100%	0	22-Feb-24 A	27-Jun-25 A	01-Nov-25		PRO-23-1110, PRO-23-1
PRO-23-1093	Return vibration & seismic control for hvac shop drawings R1	100%	100%	0	30-Jun-25 A	15-Jul-25 A	01-Nov-25		PRO-23-1094, RFI#234-
PRO-23-1083	Return vibration & seismic control for hvac product data R1	100%	100%	0	30-Jun-25 A	15-Jul-25 A	01-Nov-25		PRO-23-1084, RFI#234-
RFI#234-10	Submit RFI # 234 Regarding Mechanical Rails	100%	100%	0	19-Nov-25 A	19-Nov-25 A			RFI#234-20
RFI#234-20	Response to RFI # 234 Regarding Mechanical Rails	50%	50%	5	20-Nov-25 A	05-Dec-25		35	PRO-23-1084, PRO-23-
PRO-23-1094	Re- submit vibration & seismic control for hvac shop drawings R2	0%	0%	20	08-Dec-25	07-Jan-26	03-Nov-25	35	PRO-23-1110
PRO-23-1084	Re- submit vibration & seismic control for hvac product data R2	0%	0%	20	08-Dec-25	07-Jan-26	03-Nov-25	35	PRO-23-1100
PRO-23-1100	Review and approve vibration & seismic control for hvac product data R2	0%	0%	15	08-Jan-26	29-Jan-26	24-Nov-25	35	PR0-23-1440, CONS-CL
PRO-23-1110	Review and approve vibration & seismic control for hvac shop drawings R2	0%	0%	15	08-Jan-26	29-Jan-26	24-Nov-25	35	PR0-23-1440, CONS-CL
PR0-23-1440	Fabrication and delivery of vibration & seismic control for hvac	0%	0%	10	30-Jan-26	13-Feb-26	08-Dec-25	35	CONS-EB-6230
230593 - TESTING, ADJUSTING & BALANCING FOR HVAC			100%	0	25-Sep-23 A	09-Oct-25 A	01-Nov-25		
PRO-23-1130	Prepare and submit testing, adjusting & balancing procedures for hvac	100%	100%	0	25-Sep-23 A	22-Sep-25 A	01-Nov-25		PRO-23-1150
PRO-23-1150	Review and approve testing, adjusting & balancing procedures for hvac	100%	100%	0	23-Sep-25 A	09-Oct-25 A	01-Nov-25		CONS-TEST-1005, CON
230700 - HVAC INSULATION			98.01%	10	20-Dec-23 A	12-Dec-25	14-Nov-25	75	
PRO-23-1160	Prepare and submit hvac piping insulation product data	100%	100%	0	20-Dec-23 A	26-Feb-24 A	01-Nov-25		PRO-23-1180, PRO-23-
PRO-23-1170	Prepare and submit hvac piping insulation shop drawings	100%	100%	0	20-Dec-23 A	26-Feb-24 A	01-Nov-25		PRO-23-1190, PRO-23-
PRO-23-1180	Review and approve hvac piping insulation product data	100%	100%	0	21-Dec-23 A	04-Mar-24 A	01-Nov-25		PR0-23-1450, CONS-CL
PRO-23-1190	Review and approve hvac piping insulation shop drawings	100%	100%	0	21-Dec-23 A	04-Mar-24 A	01-Nov-25		PR0-23-1450, CONS-CL
PR0-23-1450	Fabrication and delivery of hvac piping insulation	0%	0%	10	01-Dec-25	12-Dec-25	14-Nov-25	75	CONS-EB-6230
230900 - INSTRUMENTATION & CONTROL FOR HVAC			100%	0	25-Sep-23 A	29-Jan-25 A	01-Nov-25		
PRO-23-1200	Prepare and submit instrumentation & control for hvac product data R0	100%	100%	0	25-Sep-23 A	07-Dec-23 A	01-Nov-25		PRO-23-1201
PRO-23-1210	Prepare and submit instrumentation & control for hvac shop drawings R0	100%	100%	0	25-Sep-23 A	07-Dec-23 A	01-Nov-25		PRO-23-1230, PRO-23-
PRO-23-1240	Prepare and submit instrumentation & control for hvac coordination drawings	100%	100%	0	25-Sep-23 A	13-Jan-25 A	01-Nov-25		PRO-23-1250
PRO-23-1201	Returned instrumentation & control for hvac product data R0	100%	100%	0	08-Dec-23 A	04-Mar-24 A	01-Nov-25		PRO-23-1202
PRO-23-1211	Returned instrumentation & control for hvac shop drawings R0	100%	100%	0	08-Dec-23 A	08-Mar-24 A	01-Nov-25		PRO-23-1212
PRO-23-1202	Re-submit instrumentation & control for hvac product data R1	100%	100%	0	05-Mar-24 A	21-Jun-24 A	01-Nov-25		PRO-23-1220, PRO-23-
PRO-23-1212	Re-submit instrumentation & control for hvac shop drawings R1	100%	100%	0	11-Mar-24 A	21-Jun-24 A	01-Nov-25		PRO-23-1230
PRO-23-1203	Returned instrumentation & control for hvac product data R1	100%	100%	0	24-Jun-24 A	08-Jul-24 A	01-Nov-25		PRO-23-1204
PRO-23-1213	Returned instrumentation & control for hvac shop drawings R1	100%	100%	0	24-Jun-24 A	08-Jul-24 A	01-Nov-25		PRO-23-1214
PRO-23-1204	Re-submit instrumentation & control for hvac product data R2	100%	100%	0	09-Jul-24 A	11-Dec-24 A	01-Nov-25		PRO-23-1220
PRO-23-1214	Re-submit instrumentation & control for hvac shop drawings R2	100%	100%	0	09-Jul-24 A	11-Dec-24 A	01-Nov-25		PRO-23-1230
PRO-23-1220	Review and approve instrumentation & control for hvac product data R2	100%	100%	0	12-Dec-24 A	29-Jan-25 A	01-Nov-25		PR0-23-1460, CONS-CL
PRO-23-1230	Review and approve instrumentation & control for hvac shop drawings R2	100%	100%	0	12-Dec-24 A	29-Jan-25 A	01-Nov-25		PR0-23-1460, PRO-1-1C
PRO-23-1250	Review and approve instrumentation & control for hvac coordination drawings	100%	100%	0	12-Dec-24 A	29-Jan-25 A	01-Nov-25		PR0-23-1460, CONS-CL
232113 - PIPING AND ACCESSORIES			98.01%	10	25-Sep-23 A	12-Dec-25	14-Nov-25	75	
PRO-23-1260	Prepare and submit piping and accessories product data R0	100%	100%	0	25-Sep-23 A	02-Nov-23 A	01-Nov-25		PRO-23-1280, PRO-23-
PRO-23-1270	Prepare and submit piping and accessories shop drawings R0	100%	100%	0	25-Sep-23 A	02-Nov-23 A	01-Nov-25		PRO-23-1290, PRO-23-
PRO-23-1261	Return piping and accessories product data R0	100%	100%	0	03-Nov-23 A	05-Dec-23 A	01-Nov-25		PRO-23-1262
PRO-23-1271	Return piping and accessories shop drawings R0	100%	100%	0	03-Nov-23 A	05-Dec-23 A	01-Nov-25		PRO-23-1272
PRO-23-1262	Re-submit piping and accessories product data R1	100%	100%	0	06-Dec-23 A	02-May-24 A	01-Nov-25		PRO-23-1280
PRO-23-1272	Re-submit piping and accessories shop drawings R1	100%	100%	0	06-Dec-23 A	02-May-24 A	01-Nov-25		PRO-23-1290

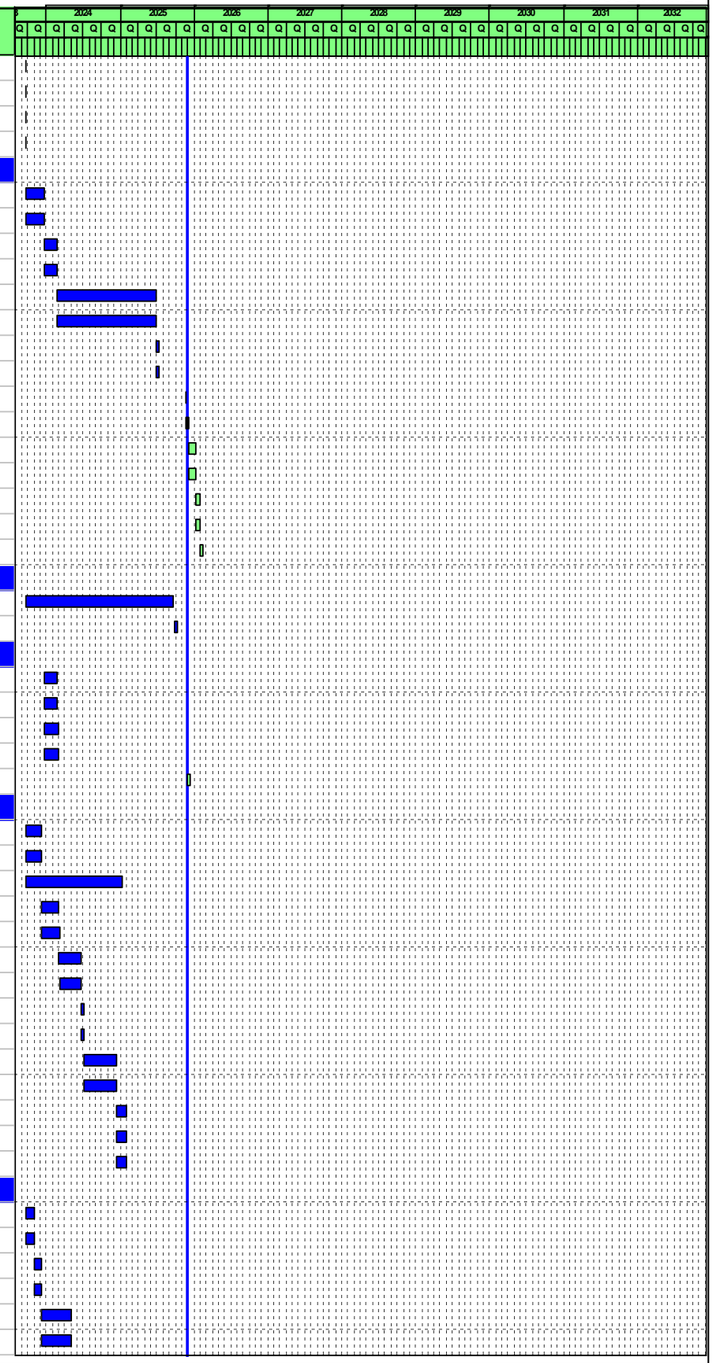


Remaining Level of Effort ◆ Milestone
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PRO-23-1280	Review and approve piping and accessories product data	100%	100%	0	03-May-24 A	13-May-24 A	01-Nov-25		PR0-23-1470, CONS-CI
PRO-23-1290	Review and approve piping and accessories shop drawings	100%	100%	0	03-May-24 A	13-May-24 A	01-Nov-25		PR0-23-1470, PRO-1-1C
PR0-23-1470	Fabrication and delivery of piping and accessories	0%	0%	10	01-Dec-25	12-Dec-25	14-Nov-25	75	CONS-EB-6230
233113 - METAL DUCTS			94.25%	30	30-Aug-23 A	14-Jan-26	16-Dec-25	55	
PRO-23-1300	Prepare and submit hvac ductwork product data R0	100%	100%	0	30-Aug-23 A	30-Aug-23 A	01-Nov-25		PRO-23-1320, PRO-23-
PRO-23-1310	Prepare and submit hvac ductwork shop drawings R0	100%	100%	0	30-Aug-23 A	30-Aug-23 A	01-Nov-25		PRO-23-1330, PRO-23-
PRO-23-1301	Return hvac ductwork product data R0	100%	100%	0	31-Aug-23 A	15-Sep-23 A	01-Nov-25		PRO-23-1302
PRO-23-1311	Return hvac ductwork shop drawings R0	100%	100%	0	31-Aug-23 A	15-Sep-23 A	01-Nov-25		PRO-23-1312
PRO-23-1302	Re-submit hvac ductwork product data R1	100%	100%	0	18-Sep-23 A	05-Apr-24 A	01-Nov-25		PRO-23-1320
PRO-23-1312	Re-submit hvac ductwork shop drawings R1	100%	100%	0	18-Sep-23 A	10-Jan-24 A	01-Nov-25		PRO-23-1330
PRO-23-1330	Review and approve hvac ductwork shop drawings R1	100%	100%	0	11-Jan-24 A	26-Apr-24 A	01-Nov-25		PR0-23-1480, CONS-CI
PRO-23-1320	Review and approve hvac ductwork product data R1	100%	100%	0	08-Apr-24 A	26-Apr-24 A	01-Nov-25		PR0-23-1480, PRO-1-1C
RFI#157-10	Submit RFI # 157 Regarding Sound Attenuators do not fit in Ductlayout	100%	100%	0	23-Apr-25 A	23-Apr-25 A	01-Nov-25		RFI#157-15
RFI#157-15	Response to RFI # 157 Regarding Sound Attenuators do not fit in Ductlayout	100%	100%	0	24-Apr-25 A	28-May-25 A	01-Nov-25		RFI#157-20
RFI#157-20	Re-submit hvac ductwork shop drawings per RFI # 157 Regarding Sound Attenuators do not fit in Ductlayout	100%	100%	0	29-May-25 A	29-Jul-25 A	01-Nov-25		RFI#157-25
RFI#157-25	Approve hvac ductwork shop drawings per RFI # 157 Regarding Sound Attenuators do not fit in Ductlayout	100%	100%	0	30-May-25 A	31-Jul-25 A	01-Nov-25		PR0-23-1480, PR0-23-1
PR0-23-1480	Fabrication and delivery of hvac ductwork	0%	0%	30	01-Dec-25	14-Jan-26	16-Dec-25	55	CONS-EB-6230
233117 - ACOUSTICAL TREATMENT			94.25%	30	25-Sep-23 A	14-Jan-26	16-Dec-25	90	
PRO-23-1340	Prepare and submit acoustical treatment product data	100%	100%	0	25-Sep-23 A	23-Oct-23 A	01-Nov-25		PRO-23-1360
PRO-23-1360	Review and approve acoustical treatment product data	100%	100%	0	24-Oct-23 A	10-Nov-23 A	01-Nov-25		PR0-23-1490
PR0-23-1490	Fabrication and delivery of acoustical treatment	0%	0%	30	01-Dec-25	14-Jan-26	16-Dec-25	90	CONS-EB-2210
233713 - DIFFUSERS, REGISTERS & GRILLES			98.01%	10	13-Sep-23 A	12-Dec-25	14-Nov-25	178	
PRO-23-1370	Prepare and submit diffusers, registers & grilles product data R0	100%	100%	0	13-Sep-23 A	13-Sep-23 A	01-Nov-25		PRO-23-1371
PRO-23-1371	Returned diffusers, registers & grilles product data R0	100%	100%	0	14-Sep-23 A	21-Jun-24 A	01-Nov-25		PR0-23-1500, CONS-CI
PRO-23-1372	Re-submit diffusers, registers & grilles product data R1	100%	100%	0	24-Jun-24 A	28-Jun-24 A	01-Nov-25		PRO-23-1380
PRO-23-1380	Review and approve diffusers, registers & grilles product data R1	100%	100%	0	01-Jul-24 A	10-Jul-24 A	01-Nov-25		PR0-23-1500, CONS-CI
PR0-23-1500	Fabrication and delivery of diffusers, registers & grilles	0%	0%	10	01-Dec-25	12-Dec-25	14-Nov-25	178	CONS-EB-2400, CONS-
236450 - HVAC EQUIPMENTS			100%	0	25-Sep-23 A	22-Nov-24 A	01-Nov-25		
PRO-23-1390	Prepare and submit hvac equipment product data	100%	100%	0	25-Sep-23 A	16-Jan-24 A	01-Nov-25		PRO-23-1410
PRO-23-1400	Prepare and submit hvac equipment shop drawings	100%	100%	0	25-Sep-23 A	16-Jan-24 A	01-Nov-25		PRO-23-1420
PRO-23-1410	Review and approve hvac equipment product data	100%	100%	0	17-Jan-24 A	29-Feb-24 A	01-Nov-25		PR0-23-1510, CONS-CI
PRO-23-1420	Review and approve hvac equipment shop drawings	100%	100%	0	17-Jan-24 A	29-Feb-24 A	01-Nov-25		PR0-23-1510, CONS-CI
PRO-23-1421	USEPA Phase out R410A Replacement Units to be Redesigned for R454B	100%	100%	0	17-Jan-24 A	03-Sep-24 A	01-Nov-25		PRO-23-1422
PRO-23-1422	Re-submit hvac equipment shop drawings Rev.1	100%	100%	0	04-Sep-24 A	04-Sep-24 A	01-Nov-25		PRO-23-1423
PRO-23-1423	Review and approve hvac equipment shop drawings Rev.1	100%	100%	0	05-Sep-24 A	22-Nov-24 A	01-Nov-25		PR0-23-1510, CONS-CI
DIVISION 26 - ELECTRICAL			93.36%	35	25-Sep-23 A	22-Jan-26	15-Jan-26	132	
260519 - ELECTRICAL MATERIALS AND METHODS			93.36%	35	25-Sep-23 A	22-Jan-26	15-Jan-26	46	
PRO-26-1020	Prepare and submit raceways, wires, cables, switches & wiring devices shop drawings	100%	100%	0	25-Sep-23 A	26-Sep-23 A	01-Nov-25		PRO-26-1040, PRO-26-
PRO-26-1021	Return raceways, wires, cables, switches & wiring devices shop drawings R0	100%	100%	0	27-Sep-23 A	06-Oct-23 A	01-Nov-25		PRO-26-1022
PRO-26-1022	Re-submit raceways, wires, cables, switches & wiring devices shop drawings R1	50%	80%	10	09-Oct-23 A	12-Dec-25	08-Dec-25	46	PRO-26-1040
PRO-26-1040	Review and approve raceways, wires, cables, switches & wiring devices shop drawings	0%	0%	15	16-Dec-25	07-Jan-26	31-Dec-25	46	PR0-26-1490, PRO-1-1C
PR0-26-1490	Fabrication and delivery of raceways, wires, cables, switches & wiring devices	0%	0%	10	08-Jan-26	22-Jan-26	15-Jan-26	46	CONS-EB-6210, CONS-
260533 - DIMMING SYSTEMS FOR SPECIALTY LIGHTING FIXTURES			95.16%	25	25-Sep-23 A	07-Jan-26	08-Dec-25	142	
PRO-26-1050	Prepare and submit dimming systems for specialty lighting fixtures shop drawings	100%	100%	0	25-Sep-23 A	15-Aug-25 A	01-Nov-25		PRO-26-1060
PRO-26-1070	Prepare and submit dimming systems for specialty lighting fixtures product data	100%	100%	0	25-Sep-23 A	15-Aug-25 A	01-Nov-25		PRO-26-1080
PRO-26-1060	Review and approve dimming systems for specialty lighting fixtures shop drawings	100%	100%	0	18-Aug-25 A	02-Sep-25 A	01-Nov-25		PR0-26-1500, PRO-1-1C
PRO-26-1080	Review and approve dimming systems for specialty lighting fixtures product data	100%	100%	0	18-Aug-25 A	02-Sep-25 A	01-Nov-25		PR0-26-1500, CONS-CI
PR0-26-1500	Fabrication and delivery of dimming systems for specialty lighting fixtures	0%	0%	25	01-Dec-25	07-Jan-26	08-Dec-25	142	CONS-EB-2170
262400 - ELECTRICAL SERVICE SYSTEM			100%	0	25-Sep-23 A	31-Mar-25 A	01-Nov-25		
PRO-26-1090	Prepare and submit distribution switchboard shop drawings R0	100%	100%	0	25-Sep-23 A	04-Dec-23 A	01-Nov-25		PRO-26-1110, PRO-26-1
PRO-26-1100	Prepare and submit distribution switchboard product data R0	100%	100%	0	25-Sep-23 A	04-Dec-23 A	01-Nov-25		PRO-26-1120, PRO-26-

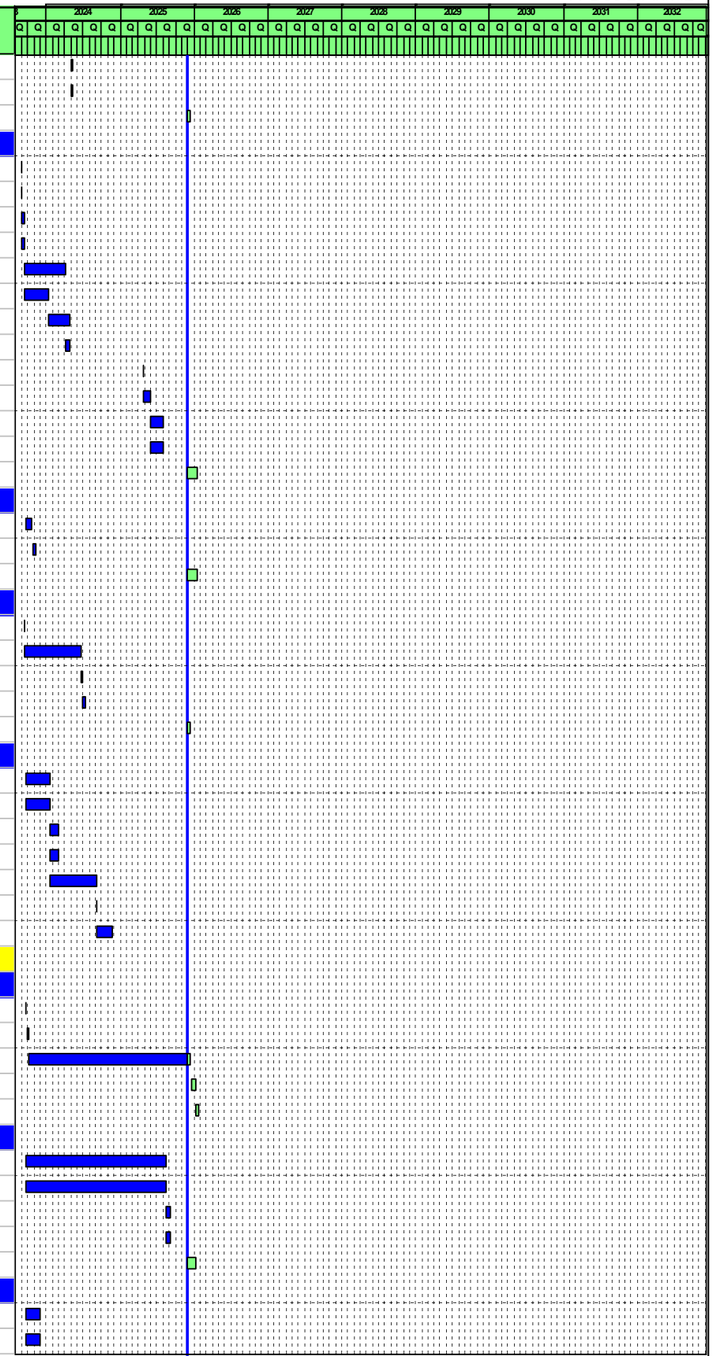


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PRO-26-1091	Return distribution switchboard shop drawings R0	100%	100%	0	05-Dec-23 A	10-Jan-24 A	01-Nov-25		PRO-26-1092
PRO-26-1101	Return distribution switchboard product data R0	100%	100%	0	05-Dec-23 A	10-Jan-24 A	01-Nov-25		PRO-26-1102, PRO-26-1
PRO-26-1101A	Con Ed Field Visit Determines POE must be Redesigned	100%	100%	0	11-Jan-24 A	03-Oct-24 A	01-Nov-25		PRO-26-1101B, BULL#1
PRO-26-1101B	DDC to redesign Electrical Closet & Switchgear Location	100%	100%	0	04-Oct-24 A	23-Jan-25 A	01-Nov-25		PRO-26-1102, PRO-26-1
PRO-26-1092	Re-submit distribution switchboard shop drawings R1	100%	100%	0	24-Jan-25 A	18-Mar-25 A	01-Nov-25		PRO-26-1110
PRO-26-1102	Re-submit distribution switchboard product data R1	100%	100%	0	24-Jan-25 A	18-Mar-25 A	01-Nov-25		PRO-26-1120
PRO-26-1110	Review and approve distribution switchboard shop drawings R1	100%	100%	0	19-Mar-25 A	31-Mar-25 A	01-Nov-25		PR0-26-1510, PRO-1-10
PRO-26-1120	Review and approve distribution switchboard product data R1	100%	100%	0	19-Mar-25 A	31-Mar-25 A	01-Nov-25		PR0-26-1510, CONS-CL
262416 - ELECTRICAL DISTRIBUTION SYSTEM			100%	0	25-Sep-23 A	21-Dec-23 A	01-Nov-25		
PRO-26-1130	Prepare and submit panel board & transformers shop drawings	100%	100%	0	25-Sep-23 A	04-Dec-23 A	01-Nov-25		PRO-26-1150
PRO-26-1140	Prepare and submit panel board & transformers product data	100%	100%	0	25-Sep-23 A	04-Dec-23 A	01-Nov-25		PRO-26-1160
PRO-26-1150	Review and approve panel board & transformers shop drawings	100%	100%	0	05-Dec-23 A	21-Dec-23 A	01-Nov-25		PR0-26-1520, PRO-1-10
PRO-26-1160	Review and approve panel board & transformers product data	100%	100%	0	05-Dec-23 A	21-Dec-23 A	01-Nov-25		PR0-26-1520, CONS-CL
262923 - ELECTRICAL POWER EQUIPMENT			100%	0	25-Sep-23 A	02-Jan-24 A	01-Nov-25		
PRO-26-1170	Prepare and submit disconnect switches & motor controllers shop drawings	100%	100%	0	25-Sep-23 A	04-Dec-23 A	01-Nov-25		PRO-26-1190
PRO-26-1180	Prepare and submit disconnect switches & motor controllers product data	100%	100%	0	25-Sep-23 A	04-Dec-23 A	01-Nov-25		PRO-26-1200
PRO-26-1190	Review and approve disconnect switches & motor controllers shop drawings	100%	100%	0	05-Dec-23 A	02-Jan-24 A	01-Nov-25		PR0-26-1530, CONS-CL
PRO-26-1200	Review and approve disconnect switches & motor controllers product data	100%	100%	0	05-Dec-23 A	02-Jan-24 A	01-Nov-25		PR0-26-1530, CONS-CL
263214 - EMERGENCY POWER SYSTEM GASEOUS TYPE ENGINE			100%	0	25-Sep-23 A	14-Jun-24 A	01-Nov-25		
PRO-26-1210	Prepare and submit ats shop drawings	100%	100%	0	25-Sep-23 A	02-Jan-24 A	01-Nov-25		PRO-26-1230
PRO-26-1220	Prepare and submit ats product data	100%	100%	0	25-Sep-23 A	02-Jan-24 A	01-Nov-25		PRO-26-1240
PRO-26-1250	Prepare and submit emergency generator shop drawings	100%	100%	0	25-Sep-23 A	02-Jan-24 A	01-Nov-25		PRO-26-1270, PRO-26-1
PRO-26-1260	Prepare and submit emergency generator product data	100%	100%	0	25-Sep-23 A	02-Jan-24 A	01-Nov-25		PRO-26-1261
PRO-26-1230	Review and approve ats shop drawings	100%	100%	0	03-Jan-24 A	05-Feb-24 A	01-Nov-25		PR0-26-1540
PRO-26-1240	Review and approve ats product data	100%	100%	0	03-Jan-24 A	05-Feb-24 A	01-Nov-25		PR0-26-1540
PRO-26-1251	Returned emergency generator shop drawings R0	100%	100%	0	03-Jan-24 A	05-Feb-24 A	01-Nov-25		PRO-26-1252, RFI#51-1
PRO-26-1261	Returned emergency generator product data R0	100%	100%	0	03-Jan-24 A	05-Feb-24 A	01-Nov-25		PRO-26-1262, RFI#51-1
RFI#51-10	Submit RFI # 52 Regarding Overcurrent Protection for Generator	100%	100%	0	06-Feb-24 A	15-Mar-24 A	01-Nov-25		RFI#51-20
RFI#51-20	Response to RFI # 52 Regarding Overcurrent Protection for Generator	100%	100%	0	18-Mar-24 A	29-Mar-24 A	01-Nov-25		PRO-26-1262, PRO-26-1
PRO-26-1252	Re-submit emergency generator shop drawings R1	100%	100%	0	01-Apr-24 A	20-May-24 A	01-Nov-25		PRO-26-1270
PRO-26-1262	Re-submit emergency generator product data R1	100%	100%	0	01-Apr-24 A	20-May-24 A	01-Nov-25		PRO-26-1280
PRO-26-1270	Review and approve emergency generator shop drawings	100%	100%	0	21-May-24 A	14-Jun-24 A	01-Nov-25		PR0-26-1550, CONS-CL
PRO-26-1280	Review and approve emergency generator product data	100%	100%	0	21-May-24 A	14-Jun-24 A	01-Nov-25		PR0-26-1550, CONS-CL
264100 - LIGHTING PROTECTION SYSTEM			96.09%	20	25-Sep-23 A	30-Dec-25	01-Dec-25	127	
PRO-26-1290	Prepare and submit lighting protection system shop drawings R0	100%	100%	0	25-Sep-23 A	22-Feb-24 A	01-Nov-25		PRO-26-1310, PRO-26-1
PRO-26-1300	Prepare and submit lighting protection system product data R0	100%	100%	0	25-Sep-23 A	22-Feb-24 A	01-Nov-25		PRO-26-1320, PRO-26-1
PRO-26-1483	Returned lighting protection system shop drawings R0	100%	100%	0	23-Feb-24 A	12-Apr-24 A	01-Nov-25		PRO-26-1292
PRO-26-1301	Returned lighting protection system product data R0	100%	100%	0	23-Feb-24 A	12-Apr-24 A	01-Nov-25		PRO-26-1302
PRO-26-1292	Re-submit lighting protection system shop drawings R1	100%	100%	0	15-Apr-24 A	10-May-24 A	01-Nov-25		PRO-26-1320
PRO-26-1302	Re-submit lighting protection system product data R1	100%	100%	0	15-Apr-24 A	10-May-24 A	01-Nov-25		PRO-26-1310
PRO-26-1310	Review and approve lighting protection system shop drawings R1	100%	100%	0	13-May-24 A	13-May-24 A	01-Nov-25		PR0-26-1560, PRO-1-10
PRO-26-1320	Review and approve lighting protection system product data R1	100%	100%	0	13-May-24 A	13-May-24 A	01-Nov-25		PR0-26-1560, CONS-CL
PR0-26-1560	Fabrication and delivery of lighting protection system	0%	0%	20	01-Dec-25	30-Dec-25	01-Dec-25	127	CONS-EB-6410
264313 - SURGE PROTECTION DEVICES (SPD)			96.09%	20	30-Nov-23 A	30-Dec-25	01-Dec-25	61	
PRO-26-1330	Prepare and submit Surge Protection shop drawings R0	100%	100%	0	30-Nov-23 A	04-Dec-23 A	01-Nov-25		PRO-26-1331
PRO-26-1340	Prepare and submit Surge Protection product data R0	100%	100%	0	30-Nov-23 A	04-Dec-23 A	01-Nov-25		PRO-26-1341
PRO-26-1331	Approve Surge Protection shop drawings R0	100%	100%	0	05-Dec-23 A	21-Dec-23 A	01-Nov-25		PR0-26-1570
PRO-26-1341	Approve Surge Protection product data R0	100%	100%	0	05-Dec-23 A	21-Dec-23 A	01-Nov-25		PR0-26-1570
PR0-26-1570	Fabrication and delivery of Surge Protection	0%	0%	20	01-Dec-25	30-Dec-25	01-Dec-25	61	CONS-EB-6345
265000 - NON ARCHITECTURAL LIGHTING FIXTURES			100%	0	30-Nov-23 A	03-Jan-24 A	01-Nov-25		
PRO-26-1370	Prepare and submit non architectural lighting fixtures shop drawings	100%	100%	0	30-Nov-23 A	20-Dec-23 A	01-Nov-25		PRO-26-1390

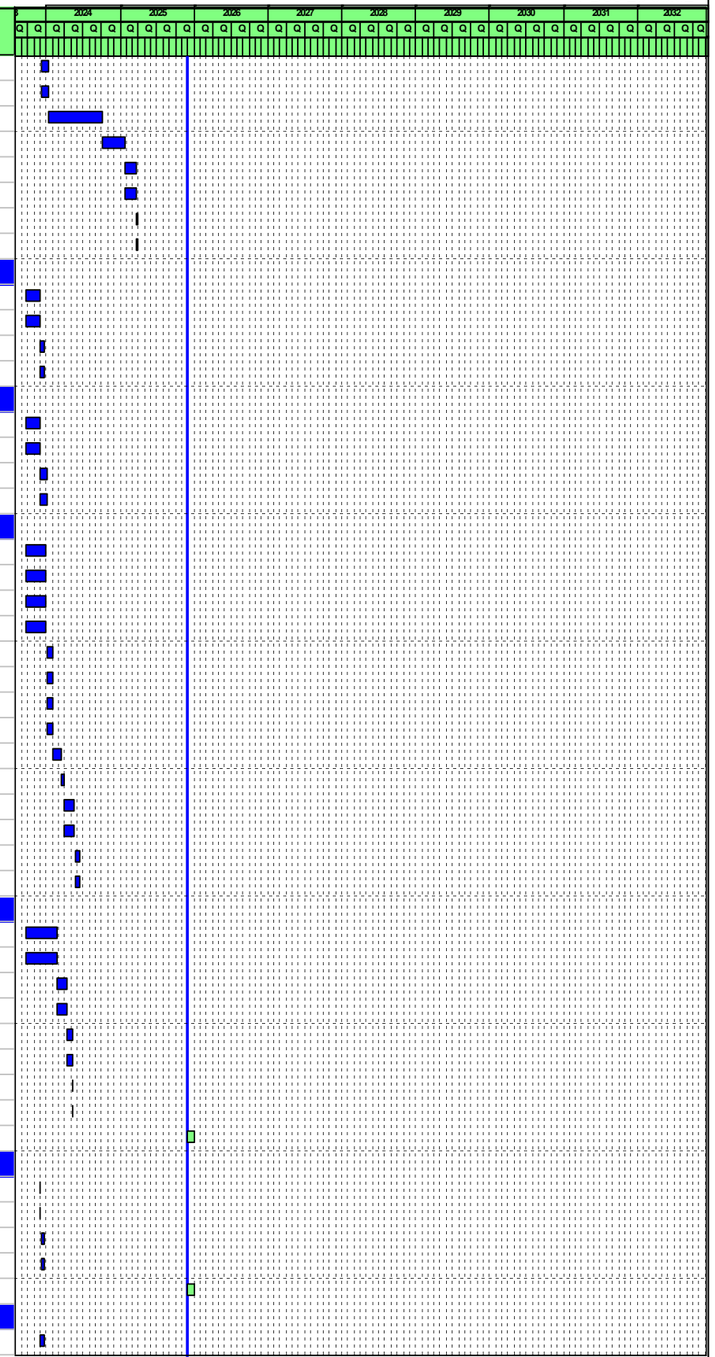


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PRO-26-1380	Prepare and submit non architectural lighting fixtures product data	100%	100%	0	30-Nov-23 A	20-Dec-23 A	01-Nov-25		PRO-26-1400
PRO-26-1390	Review and approve non architectural lighting fixtures shop drawings	100%	100%	0	21-Dec-23 A	03-Jan-24 A	01-Nov-25		PR0-26-1580, CONS-Cl
PRO-26-1400	Review and approve non architectural lighting fixtures product data	100%	100%	0	21-Dec-23 A	03-Jan-24 A	01-Nov-25		PR0-26-1580, CONS-Cl
265100 - ARCHITECTURAL LIGHTING FIXTURES			100%	0	30-Nov-23 A	31-Jul-25 A	01-Nov-25		
PRO-26-1410	Prepare and submit architectural lighting fixtures shop drawings R0	100%	100%	0	30-Nov-23 A	19-Dec-23 A	01-Nov-25		PRO-26-1411
PRO-26-1420	Prepare and submit architectural lighting fixtures product data R0	100%	100%	0	30-Nov-23 A	19-Dec-23 A	01-Nov-25		PRO-26-1421
PRO-26-1411	Return architectural lighting fixtures shop drawings R0	100%	100%	0	20-Dec-23 A	04-Mar-24 A	01-Nov-25		PRO-26-1412
PRO-26-1421	Return architectural lighting fixtures product data R0	100%	100%	0	20-Dec-23 A	04-Mar-24 A	01-Nov-25		PRO-26-1422
PRO-26-1412	Re-submit architectural lighting fixtures shop drawings R1	100%	100%	0	05-Mar-24 A	26-Jun-24 A	01-Nov-25		PRO-26-1413
PRO-26-1422	Re-submit architectural lighting fixtures product data R1	100%	100%	0	05-Mar-24 A	26-Jun-24 A	01-Nov-25		PRO-26-1423
PRO-26-1413	Return architectural lighting fixtures shop drawings R1	100%	100%	0	27-Jun-24 A	28-Aug-24 A	01-Nov-25		PRO-26-1414
PRO-26-1423	Return architectural lighting fixtures product data R1	100%	100%	0	27-Jun-24 A	28-Aug-24 A	01-Nov-25		PRO-26-1424
PRO-26-1414	Re-submit architectural lighting fixtures shop drawings R2	100%	100%	0	29-Aug-24 A	05-Nov-24 A	01-Nov-25		PRO-26-1415
PRO-26-1424	Re-submit architectural lighting fixtures product data R2	100%	100%	0	29-Aug-24 A	05-Nov-24 A	01-Nov-25		PRO-26-1425
PRO-26-1425	Return architectural lighting fixtures product data R2	100%	100%	0	05-Nov-24 A	19-Nov-24 A	01-Nov-25		PRO-26-1426
PRO-26-1415	Return architectural lighting fixtures shop drawings R2	100%	100%	0	06-Nov-24 A	19-Nov-24 A	01-Nov-25		PRO-26-1416
PRO-26-1416	Re-submit architectural lighting fixtures shop drawings R3	100%	100%	0	20-Nov-24 A	27-Dec-24 A	01-Nov-25		PRO-26-1417
PRO-26-1426	Re-submit architectural lighting fixtures product data R3	100%	100%	0	20-Nov-24 A	27-Dec-24 A	01-Nov-25		PRO-26-1427
PRO-26-1417	Return architectural lighting fixtures shop drawings R3	100%	100%	0	27-Dec-24 A	16-Jan-25 A	01-Nov-25		PRO-26-1418
PRO-26-1427	Return architectural lighting fixtures product data R3	100%	100%	0	27-Dec-24 A	16-Jan-25 A	01-Nov-25		PRO-26-1428
PRO-26-1418	Re-submit architectural lighting fixtures shop drawings R4	100%	100%	0	17-Jan-25 A	25-Feb-25 A	01-Nov-25		PRO-26-1430, PRO-26-
PRO-26-1428	Re-submit architectural lighting fixtures product data R4	100%	100%	0	17-Jan-25 A	25-Feb-25 A	01-Nov-25		PRO-26-1440, PRO-26-
PRO-26-1429	Return architectural lighting fixtures product data R4	100%	100%	0	26-Feb-25 A	24-Mar-25 A	01-Nov-25		PRO-26-1429a
PRO-26-1419	Return architectural lighting fixtures shop drawings R4	100%	100%	0	26-Feb-25 A	24-Mar-25 A	01-Nov-25		PRO-26-1419a
PRO-26-1429a	Re-submit architectural lighting fixtures product data R5	100%	100%	0	25-Mar-25 A	15-May-25 A	01-Nov-25		PRO-26-1440, PRO-26-
PRO-26-1419a	Re-submit architectural lighting fixtures shop drawings R5	100%	100%	0	25-Mar-25 A	15-May-25 A	01-Nov-25		PRO-26-1440, PRO-26-
PRO-26-1429c	Return architectural lighting fixtures product data R5	100%	100%	0	16-May-25 A	22-May-25 A	01-Nov-25		PRO-26-1429d
PRO-26-1419b	Return architectural lighting fixtures shop drawings R5	100%	100%	0	16-May-25 A	22-May-25 A	01-Nov-25		PRO-26-1419c
PRO-26-1429d	Re-submit architectural lighting fixtures product data R6	100%	100%	0	23-May-25 A	03-Jul-25 A	01-Nov-25		PRO-26-1440
PRO-26-1419c	Re-submit architectural lighting fixtures shop drawings R6	100%	100%	0	23-May-25 A	03-Jul-25 A	01-Nov-25		PRO-26-1430
PRO-26-1430	Review and approve architectural lighting fixtures shop drawings R6	100%	100%	0	07-Jul-25 A	31-Jul-25 A	01-Nov-25		PR0-26-1590, CONS-Cl
PRO-26-1440	Review and approve architectural lighting fixtures product data R6	100%	100%	0	07-Jul-25 A	31-Jul-25 A	01-Nov-25		PR0-26-1590, CONS-Cl
266000 - ACCESS DOORS			94.62%	28	30-Nov-23 A	12-Jan-26	11-Dec-25	67	
PRO-26-1450	Prepare and submit access doors shop drawings	0%	84%	8	30-Nov-23 A	10-Dec-25	12-Nov-25	67	PRO-26-1470
PRO-26-1460	Prepare and submit access doors product data	0%	84%	8	30-Nov-23 A	10-Dec-25	12-Nov-25	67	PRO-26-1480
PRO-26-1470	Review and approve access doors shop drawings	0%	0%	15	11-Dec-25	05-Jan-26	04-Dec-25	67	PR0-26-1600
PRO-26-1480	Review and approve access doors product data	0%	0%	15	11-Dec-25	05-Jan-26	04-Dec-25	67	PR0-26-1600
PR0-26-1600	Fabrication and delivery of access doors	0%	0%	5	06-Jan-26	12-Jan-26	11-Dec-25	67	CONS-EB-6240
DIVISION 27 - COMMUNICATOINS (not in Contract)			100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		
270526 - GROUNDING AND BONDING FOR COMMUNICATION SYSTEMS (not in Contract)			100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		
PR0-27-1200	Fabrication and delivery of comm grounding and bonding	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		CONS-EB-6040
PRO-27-1020	Review and approve comm grounding and bonding shop drawings	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PR0-27-1200, CONS-Cl
PRO-27-1000	Prepare and submit comm grounding and bonding shop drawings (not in Contract)	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PRO-27-1020
PRO-27-1030	Review and approve comm grounding and bonding product data	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PR0-27-1200, CONS-Cl
PRO-27-1010	Prepare and submit comm grounding and bonding product data (not in Contract)	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PRO-27-1030
270528.33 - CONDUIT AND BACKBOXES FOR COMMUNICATION SYSTEMS (not in Contract)			100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		
PR0-27-1210	Fabrication and delivery of comm conduit and backboxes	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		CONS-EB-6210
PRO-27-1060	Review and approve comm conduit and backboxes shop drawings	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PR0-27-1210, CONS-Cl
PRO-27-1040	Prepare and submit comm conduit and backboxes shop drawings (not in Contract)	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PRO-27-1060
PRO-27-1070	Review and approve comm conduit and backboxes product data	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PR0-27-1210, CONS-Cl
PRO-27-1050	Prepare and submit comm conduit and backboxes product data (not in Contract)	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PRO-27-1070

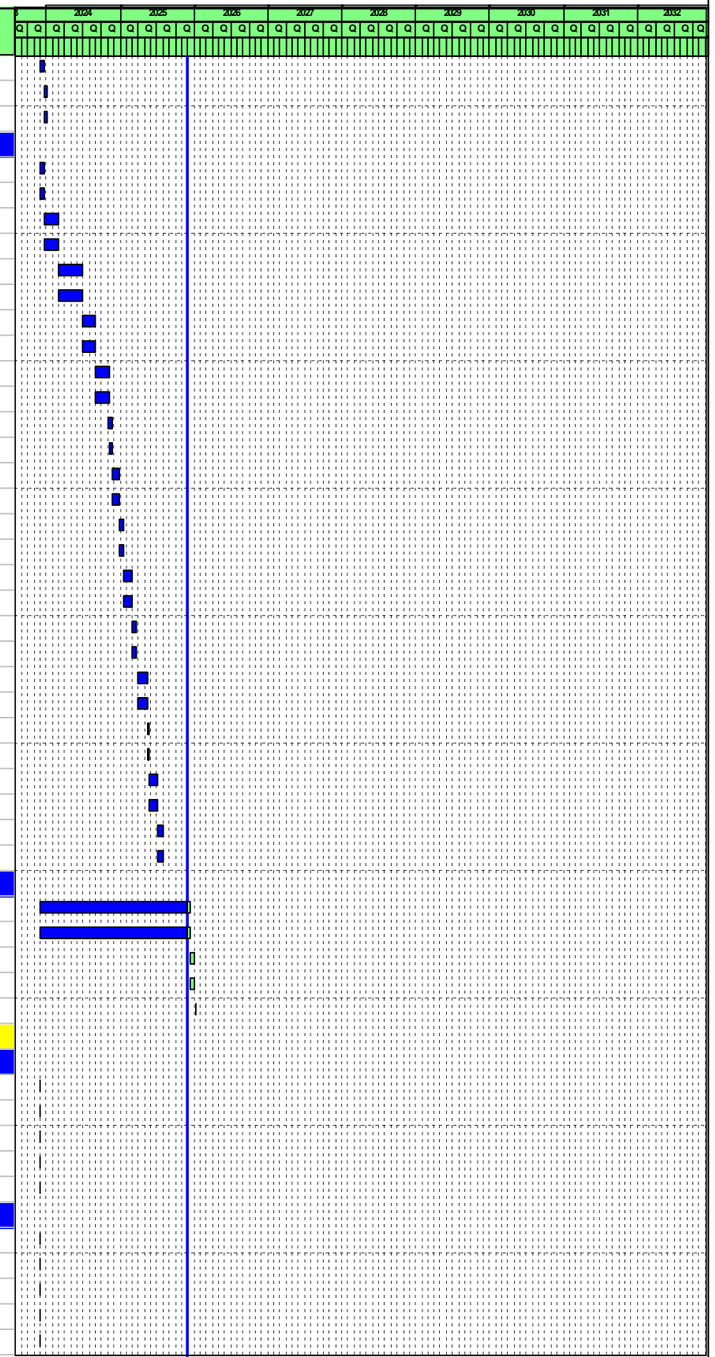


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
270529 - HANGERS AND SUPPORTS FOR COMMUNICATION SYSTEMS (not in Contract)			100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		
PR0-27-1220	Fabrication and delivery of comm hangers and supports	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		CONS-EB-6210
PRO-27-1100	Review and approve comm hangers and supports shop drawings	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PR0-27-1220, CONS-CI
PRO-27-1080	Prepare and submit comm hangers and supports shop drawings (not in Contract)	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PRO-27-1100
PRO-27-1110	Review and approve comm hangers and supports product data	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PR0-27-1220, CONS-CI
PRO-27-1090	Prepare and submit comm hangers and supports product data (not in Contract)	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PRO-27-1110
270536 - CABLE TRAYS FOR COMMUNICATION SYSTEMS (not in Contract)			100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		
PR0-27-1230	Fabrication and delivery of comm cable trays	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		CONS-EB-6210
PRO-27-1140	Review and approve comm cable trays shop drawings	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PR0-27-1230, CONS-CI
PRO-27-1120	Prepare and submit comm cable trays shop drawings (not in Contract)	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PRO-27-1140
PRO-27-1150	Review and approve comm cable trays product data	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PR0-27-1230, CONS-CI
PRO-27-1130	Prepare and submit comm cable trays product data (not in Contract)	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PRO-27-1150
270537 - FIRESTOPPING FOR COMMUNICATION SYSTEMS (not in Contract)			100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		
PR0-27-1240	Fabrication and delivery of comm firestopping devices	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		CONS-EB-2290
PRO-27-1180	Review and approve comm firestopping devices shop drawings	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PR0-27-1240, CONS-CI
PRO-27-1160	Prepare and submit comm firestopping devices shop drawings (not in Contract)	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PRO-27-1180
PRO-27-1190	Review and approve comm firestopping devices product data	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PR0-27-1240, CONS-CI
PRO-27-1170	Prepare and submit comm firestopping devices product data (not in Contract)	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PRO-27-1190
DIVISION 28 - ELECTRONIC SAFETY AND SECURITY			100%	0	02-Oct-23 A	21-Feb-24 A	01-Nov-25		
280000 - ELECTRONIC SAFETY AND SECURITY			100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		
PRO-28-1000	Prepare and submit electronic safety and security shop drawings and product data (Not in Contract)	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PRO-28-1010
PRO-28-1010	Review and approve safety and security shop drawings and product data (Not in Contract)	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PRO-1-1015, PRO-1-10
280513 - ELECTRONIC SECURITY CONDUCTORS AND CABLING			100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		
PR0-28-1000	Fabrication and delivery of security conductors and cabling materials (Not in Contract)	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		CONS-EB-6050
PRO-28-1110	Review and approve security conductors and cabling shop drawings (Not in Contract)	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PR0-28-1000, CONS-CI
PRO-28-1090	Prepare and submit security conductors and cabling shop drawings (Not in Contract)	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PRO-28-1110
PRO-28-1120	Review and approve security conductors and cabling product data (Not in Contract)	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PR0-28-1000, CONS-CI
PRO-28-1100	Prepare and submit security conductors and cabling product data (Not in Contract)	100%	100%	0	30-Nov-23 A	30-Nov-23 A	01-Nov-25		PRO-28-1120
283110 - FIRE ALARM SYSTEM			100%	0	02-Oct-23 A	21-Feb-24 A	01-Nov-25		
PRO-28-1130	Prepare and submit fire alarm system shop drawings R0	100%	100%	0	02-Oct-23 A	18-Oct-23 A	01-Nov-25		PRO-28-1150, PRO-28-
PRO-28-1140	Prepare and submit fire alarm system product data R0	100%	100%	0	02-Oct-23 A	18-Oct-23 A	01-Nov-25		PRO-28-1160, PRO-28-
PRO-28-1131	Return fire alarm system shop drawings R0	100%	100%	0	19-Oct-23 A	05-Dec-23 A	01-Nov-25		PRO-28-1132, RFI#34-1
PRO-28-1141	Return fire alarm system product data R0	100%	100%	0	19-Oct-23 A	05-Dec-23 A	01-Nov-25		PRO-28-1142, RFI#34-1
RFI#34-10	Submit RFI # 34 Regarding fire alarm system	100%	100%	0	06-Dec-23 A	13-Dec-23 A	01-Nov-25		RFI#34-15
RFI#34-15	Response to RFI # 34 Regarding fire alarm system	100%	100%	0	14-Dec-23 A	10-Jan-24 A	01-Nov-25		PRO-28-1132, PRO-28-
PRO-28-1132	Re-submit fire alarm system shop drawings R1	100%	100%	0	11-Jan-24 A	17-Jan-24 A	01-Nov-25		PRO-28-1150
PRO-28-1142	Re-submit fire alarm system product data R1	100%	100%	0	11-Jan-24 A	17-Jan-24 A	01-Nov-25		PRO-28-1160
PRO-28-1150	Review and approve fire alarm system shop drawings R1	100%	100%	0	18-Jan-24 A	21-Feb-24 A	01-Nov-25		PR0-28-1010, CONS-CI
PRO-28-1160	Review and approve fire alarm system product data R1	100%	100%	0	18-Jan-24 A	21-Feb-24 A	01-Nov-25		PR0-28-1010, CONS-CI
DIVISION 31 - EARTHWORK			100%	0	04-Aug-23 A	14-Mar-25 A	01-Nov-25		
310000 - EARTHWORK			100%	0	15-Jan-24 A	16-Jul-24 A	01-Nov-25		
PRO-31-1000	Prepare and submit excavation	100%	100%	0	15-Jan-24 A	24-Jun-24 A	01-Nov-25		PRO-31-1010
PRO-31-1010	Review and approve excavation	100%	100%	0	25-Jun-24 A	16-Jul-24 A	01-Nov-25		CONS-EB-1610, CONS-
310000 - DEWATERING			100%	0	20-Jun-24 A	16-Jul-24 A	01-Nov-25		
PRO-31-1170	Prepare and submit Dewatering Plan	100%	100%	0	20-Jun-24 A	20-Jun-24 A	01-Nov-25		PRO-31-1180
PRO-31-1180	Review and approve Dewatering Plan	100%	100%	0	21-Jun-24 A	16-Jul-24 A	01-Nov-25		CONS-EB-1620
310913 - MONITORING OF ADJACENT STRUCTURES			100%	0	04-Aug-23 A	10-Jan-24 A	01-Nov-25		
PRO-31-1020	Prepare and submit monitoring and vibration plan for adjacent structures	100%	100%	0	04-Aug-23 A	29-Dec-23 A	01-Nov-25		PRO-31-1030
PRO-31-1030	Review and approve monitoring and vibration plan for adjacent structures	100%	100%	0	02-Jan-24 A	10-Jan-24 A	01-Nov-25		CONS-EB-1610, PRE-1
311000 - SITE CLEARING, REMOVALS AND PREPARATION			100%	0	04-Aug-23 A	31-Aug-23 A	01-Nov-25		
PRO-31-1040	Prepare and submit selective removals & demolition plan	100%	100%	0	04-Aug-23 A	15-Aug-23 A	01-Nov-25		PRO-31-1050

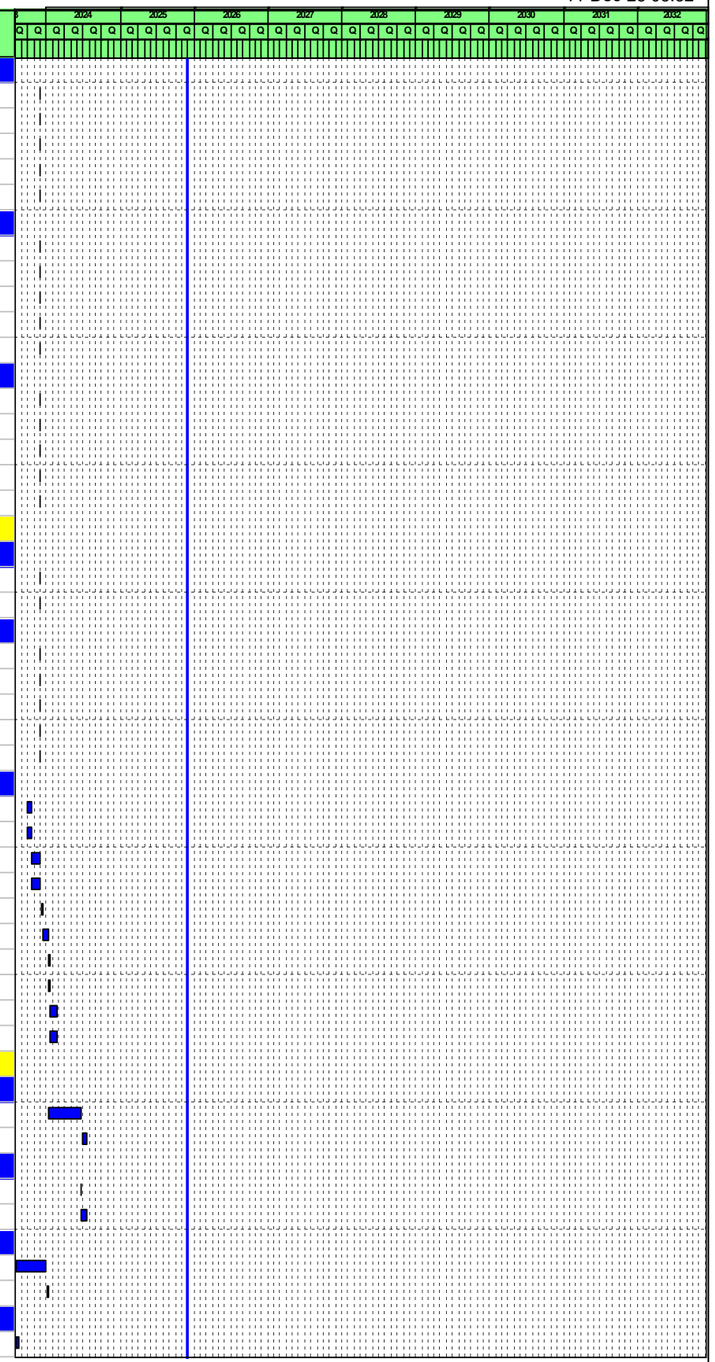


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PRO-31-1050	Review and approve selective removals & demolition plan	100%	100%	0	16-Aug-23 A	31-Aug-23 A	01-Nov-25		CONS-ARCH-1040
312020 - GROUND IMPROVEMENT			100%	0	01-Sep-23 A	05-Mar-25 A	01-Nov-25		
PRO-31-1060	Prepare and submit Ground Improvements Plans and Calcs R0	100%	100%	0	01-Sep-23 A	17-Oct-23 A	01-Nov-25		PRO-31-1061
PRO-31-1061	Return Ground Improvements Plans and Calcs R0	100%	100%	0	18-Oct-23 A	20-Oct-23 A	01-Nov-25		PRO-31-1062
PRO-31-1062	Re-submit Ground Improvements Plans and Calcs R1	100%	100%	0	23-Oct-23 A	07-Dec-23 A	01-Nov-25		PRO-31-1063
PRO-31-1063	Return Ground Improvements Plans and Calcs R1	100%	100%	0	08-Dec-23 A	04-Jan-24 A	01-Nov-25		PRO-31-1064
PRO-31-1064	Re-submit Ground Improvements Plans and Calcs R2	100%	100%	0	05-Jan-24 A	07-Mar-24 A	01-Nov-25		PRO-31-1070
PRO-31-1070	Review and approve Ground Improvements Plans and Calcs R2	100%	100%	0	08-Mar-24 A	25-Mar-24 A	01-Nov-25		PRO-31-1110
PRO-31-1110	Fabrication and delivery of cement grout mix for Ground Improvements	100%	100%	0	03-Mar-25 A	05-Mar-25 A	01-Nov-25		CONS-EB-1060
312500 - SOIL EROSION AND SEDIMENTATION CONTROL			100%	0	01-Sep-23 A	17-May-24 A	01-Nov-25		
PRO-31-1120	Prepare and submit soil erosion and sedimentation control plan R0	100%	100%	0	01-Sep-23 A	05-Jan-24 A	01-Nov-25		PRO-31-1140, PRO-31-1
PRO-31-1121	Returned soil erosion and sedimentation control plan R0	100%	100%	0	08-Jan-24 A	05-Mar-24 A	01-Nov-25		PRO-31-1122
PRO-31-1122	Re-submit soil erosion and sedimentation control plan R1	100%	100%	0	06-Mar-24 A	25-Mar-24 A	01-Nov-25		PRO-31-1123
PRO-31-1123	Returned soil erosion and sedimentation control plan R1	100%	100%	0	22-Mar-24 A	12-Apr-24 A	01-Nov-25		PRO-31-1124
PRO-31-1124	Re-submit soil erosion and sedimentation control plan R2	100%	100%	0	15-Apr-24 A	07-May-24 A	01-Nov-25		PRO-31-1130
PRO-31-1130	Review and approve soil erosion and sedimentation control plan R2	100%	100%	0	08-May-24 A	17-May-24 A	01-Nov-25		CONS-EB-1610
315000 - EXCAVATION SUPPORT			100%	0	15-Jan-24 A	14-Mar-25 A	01-Nov-25		
PRO-31-1140	Prepare and submit earthwork/support of excavation R0	100%	100%	0	15-Jan-24 A	26-Feb-24 A	01-Nov-25		PRO-31-1141
PRO-31-1141	Returned earthwork/support of excavation R0	100%	100%	0	27-Feb-24 A	05-Mar-24 A	01-Nov-25		PRO-31-1142
PRO-31-1142	Re-submit earthwork/support of excavation R1	100%	100%	0	06-Mar-24 A	15-Mar-24 A	01-Nov-25		PRO-31-1143
PRO-31-1143	Returned earthwork/support of excavation R1	100%	100%	0	18-Mar-24 A	18-Mar-24 A	01-Nov-25		PRO-31-1144
PRO-31-1144	Re-submit earthwork/support of excavation R2	100%	100%	0	19-Mar-24 A	26-Mar-24 A	01-Nov-25		PRO-31-1145
PRO-31-1145	Returned earthwork/support of excavation R2	100%	100%	0	27-Mar-24 A	24-Apr-24 A	01-Nov-25		PRO-31-1146
PRO-31-1146	Re-submit earthwork/support of excavation R3	100%	100%	0	25-Apr-24 A	01-May-24 A	01-Nov-25		PRO-31-1147
PRO-31-1147	Returned earthwork/support of excavation R3	100%	100%	0	02-May-24 A	21-May-24 A	01-Nov-25		PRO-31-1148
PRO-31-1148	Re-submit earthwork/support of excavation R4	100%	100%	0	22-May-24 A	30-May-24 A	01-Nov-25		PRO-31-1150
PRO-31-1150	Review and approve earthwork/support of excavation R4	100%	100%	0	31-May-24 A	17-Jun-24 A	01-Nov-25		PRO-31-1160
PRO-31-1160	Fabrication and delivery of soe	100%	100%	0	03-Mar-25 A	14-Mar-25 A	01-Nov-25		CONS-EB-1610
DIVISION 32 - EXTERIOR IMPROVEMENTS			67.89%	105	02-Jan-25 A	06-May-26	09-Apr-26	63	
321216 - ASPHALTIC PAVING			72.62%	69	24-Mar-25 A	16-Mar-26	13-Feb-26	99	
PRO-32-1000	Prepare and submit asphaltic concrete paving product data	50%	50%	49	24-Mar-25 A	12-Feb-26	14-Jan-26	99	PRO-32-1010
PRO-32-1010	Review and approve asphaltic concrete paving product data	0%	0%	15	13-Feb-26	06-Mar-26	06-Feb-26	99	PRO-32-1100
PRO-32-1100	Fabrication and delivery of asphaltic concrete paving	0%	0%	5	09-Mar-26	16-Mar-26	13-Feb-26	99	SITE-1110, SITE-1120
321315 - CONCRETE AND PAVEMENTS			100%	0	02-Jan-25 A	04-Mar-25 A	01-Nov-25		
PRO-32-1020	Prepare and submit concrete curbs and pavements product data	100%	100%	0	02-Jan-25 A	27-Jan-25 A	01-Nov-25		PRO-32-1030
PRO-32-1030	Review and approve concrete curbs and pavements product data	100%	100%	0	28-Jan-25 A	29-Jan-25 A	01-Nov-25		PRO-32-1110
PRO-32-1110	Fabrication and delivery of concrete for curbs and pavements	100%	100%	0	26-Feb-25 A	04-Mar-25 A	01-Nov-25		SITE-1110, SITE-1120
321713 - PARKING BUMPERS			0%	105	01-Dec-25	06-May-26	09-Apr-26	63	
PRO-32-1040	Prepare and submit parking bumpers product data	0%	0%	80	01-Dec-25	31-Mar-26	03-Mar-26	63	PRO-32-1050
PRO-32-1050	Review and approve parking bumpers product data	0%	0%	15	01-Apr-26	22-Apr-26	25-Mar-26	63	PRO-32-1120
PRO-32-1120	Fabrication and delivery of parking bumpers	0%	0%	10	23-Apr-26	06-May-26	09-Apr-26	63	SITE-1110, SITE-1120
329000 - PLANTING			0%	55	01-Dec-25	23-Feb-26	23-Jan-26	113	
PRO-32-1060	Prepare and submit landscaping product data	0%	0%	30	01-Dec-25	14-Jan-26	16-Dec-25	113	PRO-32-1070
PRO-32-1070	Review and approve landscaping product data	0%	0%	15	15-Jan-26	06-Feb-26	08-Jan-26	113	PRO-32-1130
PRO-32-1130	Fabrication and delivery of landscaping materials	0%	0%	10	09-Feb-26	23-Feb-26	23-Jan-26	113	SITE-1110, SITE-1120
329200 - TURF AND GRASSES			0%	105	01-Dec-25	06-May-26	09-Apr-26	63	
PRO-32-1080	Prepare and submit turf and grasses product data	0%	0%	80	01-Dec-25	31-Mar-26	03-Mar-26	63	PRO-32-1090
PRO-32-1090	Review and approve turf and grasses product data	0%	0%	15	01-Apr-26	22-Apr-26	25-Mar-26	63	PRO-32-1140
PRO-32-1140	Fabrication and delivery of turf and grasses materials	0%	0%	10	23-Apr-26	06-May-26	09-Apr-26	63	SITE-1110, SITE-1120
DIVISION 33 - SITE UTILITIES			97.62%	10	01-Mar-24 A	12-Dec-25	14-Nov-25	158	
334000 - STORM DRAINAGE UTILITIES			97.62%	10	01-Mar-24 A	12-Dec-25	14-Nov-25	158	

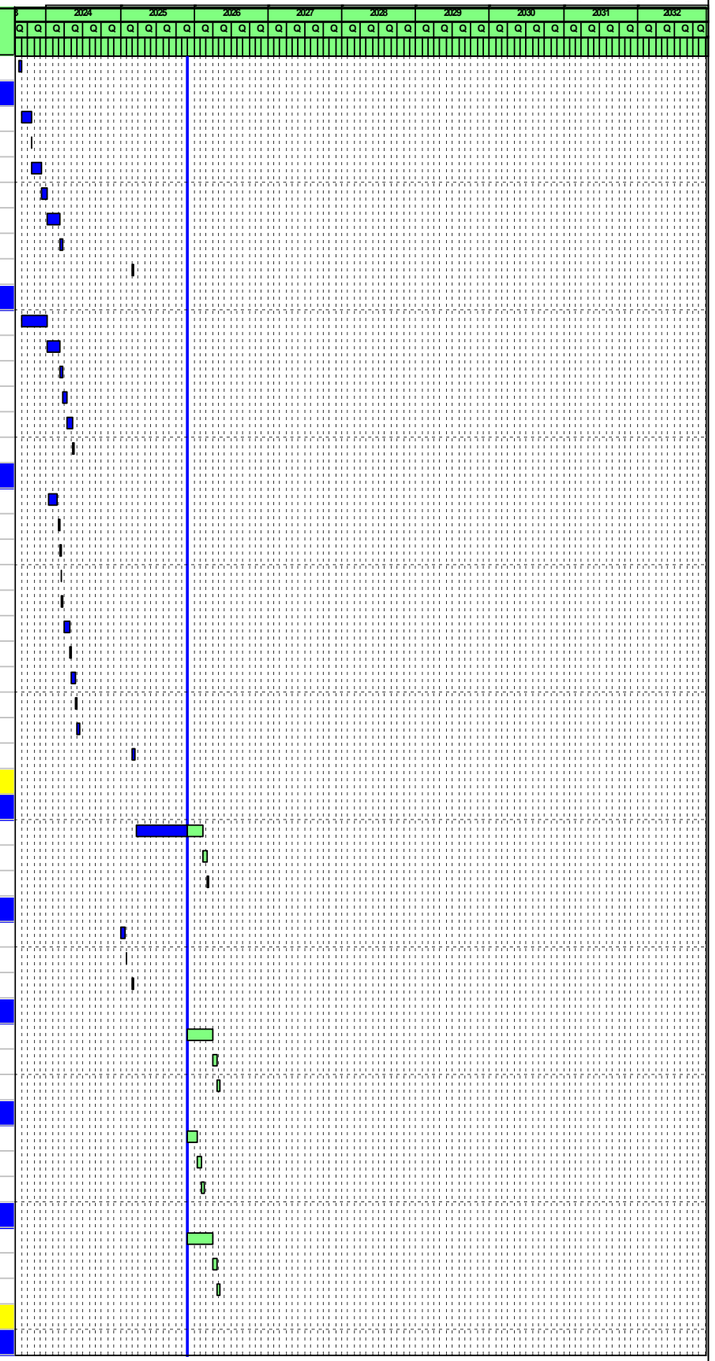

Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PRO-33-1020	Prepare and submit storm drainage utilities product data R0	100%	100%	0	01-Mar-24 A	12-Mar-24 A	01-Nov-25		PRO-33-1030
PRO-33-1040	Prepare and submit storm drainage utilities shop drawings R0	100%	100%	0	01-Mar-24 A	12-Mar-24 A	01-Nov-25		PRO-33-1050
PRO-33-1030	Returned storm drainage utilities product data R0	100%	100%	0	15-Mar-24 A	28-Mar-24 A	01-Nov-25		PRO-33-1000, BULL#08
PRO-33-1050	Returned storm drainage utilities shop drawings R0	100%	100%	0	15-Mar-24 A	28-Mar-24 A	01-Nov-25		PRO-33-1000, BULL#08
PRO-33-1060	Re-submit storm drainage utilities product data R1 per Bulletin	100%	100%	0	20-Nov-24 A	31-Jan-25 A	01-Nov-25		PRO-33-1061
PRO-33-1070	Re-submit storm drainage utilities shop drawings R1 per Bulletin	100%	100%	0	20-Nov-24 A	31-Jan-25 A	01-Nov-25		PRO-33-1081
PRO-33-1061	Returned storm drainage utilities product data R1 per Bulletin	100%	100%	0	03-Feb-25 A	13-Feb-25 A	01-Nov-25		PRO-33-1062
PRO-33-1081	Returned storm drainage utilities shop drawings R1 per Bulletin	100%	100%	0	03-Feb-25 A	13-Feb-25 A	01-Nov-25		PRO-33-1082
PRO-33-1062	Re-submit storm drainage utilities product data R2 per Bulletin	100%	100%	0	14-Feb-25 A	10-Jul-25 A	01-Nov-25		PRO-33-1080
PRO-33-1082	Re-submit storm drainage utilities shop drawings R2 per Bulletin	100%	100%	0	14-Feb-25 A	10-Jul-25 A	01-Nov-25		PRO-33-1090
PRO-33-1080	Review and approve storm drainage utilities product data R2 per Bulletin	100%	100%	0	11-Jul-25 A	31-Jul-25 A	01-Nov-25		PRO-33-1000
PRO-33-1090	Review and approve storm drainage utilities shop drawings R2 per Bulletin	100%	100%	0	11-Jul-25 A	31-Jul-25 A	01-Nov-25		PRO-33-1000
PRO-33-1000	Fabrication and delivery of storm drainage materials	0%	0%	10	01-Dec-25	12-Dec-25	14-Nov-25	158	SITE-1110
DIVISION 48 - ELECTRICAL POWER GENERATION			79.82%	85	31-Oct-23 A	08-Apr-26	10-Mar-26	42	
481400 - SOLAR ENERGY ELECTRICAL POWER GENERATION SYSTEM			79.82%	85	31-Oct-23 A	08-Apr-26	10-Mar-26	42	
RFI#104-10	Submit RFI # 104 regarding PV System Clarification	100%	100%	0	31-Oct-23 A	01-Nov-24 A	01-Nov-25		RFI#104-15
RFI#104-15	Response to RFI # 104 regarding PV System Clarification	100%	100%	0	04-Nov-24 A	20-Nov-24 A	01-Nov-25		PRO-48-1000
PRO-48-1000	Prepare and submit pv system product data R0	100%	100%	0	21-Nov-24 A	05-Dec-24 A	01-Nov-25		PRO-48-1001
PRO-48-1001	Returned pv system product data R0	100%	100%	0	06-Dec-24 A	11-Dec-24 A	01-Nov-25		PRO-48-1002
PRO-48-1002	Re-submit pv system product data R1	100%	100%	0	12-Dec-24 A	10-Jan-25 A	01-Nov-25		PRO-48-1020
PRO-48-1020	Review and approve pv system product data R1	100%	100%	0	13-Jan-25 A	27-Jan-25 A	01-Nov-25		PRO-48-1040, RFI#123-
RFI#123-10	Submit RFI # 123 regarding PV System is Obsolete	100%	100%	0	28-Jan-25 A	28-Jan-25 A	01-Nov-25		RFI#123-15
RFI#123-15	Response to RFI # 123 regarding PV System is Obsolete	100%	100%	0	29-Jan-25 A	11-Feb-25 A	01-Nov-25		PRO-48-1010, RFI#123-
RFI#123-25	DDC Obtain DCAS Approval for Alternate PV System	50%	50%	10	12-Feb-25 A	12-Dec-25	14-Nov-25	42	PRO-48-1010
PRO-48-1010	Prepare and submit pv system shop drawings	0%	0%	60	16-Dec-25	17-Mar-26	17-Feb-26	42	PRO-48-1030
PRO-48-1030	Review and approve pv system shop drawings	0%	0%	15	18-Mar-26	08-Apr-26	10-Mar-26	42	PRO-48-1040
LONG LEAD ITEMS			76.15%	125	25-Sep-23 A	05-Jun-26	07-May-26	42	
PR0-23-1430	Fabrication and delivery of hvac vfd (Not in Scope)	100%	100%	0	25-Sep-23 A	25-Sep-23 A	30-Jan-26		CONS-EB-1320
PR0-23-1510	Fabrication and delivery of hvac equipment	91%	91%	18	01-Mar-24 A	26-Dec-25	26-Dec-25	122	CONS-EB-1320
PR0-14-1040	Fabrication and delivery of hydraulic passenger elevator equipment	36%	36.25%	51	11-Nov-24 A	17-Feb-26	29-Dec-25	46	CONS-EB-1335, CONS-
PR0-26-1550	Fabrication and delivery of emergency generator	77%	76.82%	51	21-Mar-25 A	17-Feb-26	17-Feb-26	89	CONS-EB-1320
PR0-11-1020	Fabrication and delivery of appliances materials	50%	50%	20	07-Apr-25 A	30-Dec-25	01-Dec-25	132	CONS-EB-3400
PR0-08-1000	Fabrication and delivery of steel doors and frames	100%	100%	0	21-Apr-25 A	02-Sep-25 A	01-Nov-25		CONS-EB-1160
PRO-05-1030	Fabrication and delivery of steel stairs metal framing material	100%	100%	0	28-Apr-25 A	15-Oct-25 A	01-Nov-25		CONS-EB-1160
PR0-08-1050	Fabrication and delivery of access doors	100%	100%	0	02-May-25 A	26-Jun-25 A	01-Nov-25		CONS-EB-2300
PRO-05-1000	Fabrication and delivery of steel structural framing	100%	100%	0	08-May-25 A	10-Nov-25 A	30-Jan-26		CONS-EB-1190
PRO-05-1020	Fabrication and delivery of miscellaneous metals	100%	100%	0	28-May-25 A	14-Oct-25 A	01-Nov-25		CONS-EB-1190, CONS-
PR0-08-1060	Fabrication and delivery of aluminum entrance and storefront	28%	28%	72	25-Jul-25 A	19-Mar-26	25-Mar-26	34	CONS-EB-1350, CONS-
PR0-26-1510	Fabrication and delivery of distribution switchboards	80%	79.55%	27	02-Sep-25 A	09-Jan-26	09-Jan-26	54	CONS-EB-6345
PR0-26-1520	Fabrication and delivery of panel board & transformers	80%	79.55%	27	02-Sep-25 A	09-Jan-26	09-Jan-26	54	CONS-EB-6345
PR0-26-1540	Fabrication and delivery of ats	100%	100%	0	02-Sep-25 A	22-Oct-25 A	01-Nov-25		CONS-EB-1320
PR0-08-1070	Fabrication and delivery of interior glazing	40%	40%	60	29-Sep-25 A	02-Mar-26	01-Apr-26	72	CONS-EB-1910
PR0-26-1580	Fabrication and delivery of non architectural lighting fixtures	50%	63.64%	40	01-Oct-25 A	29-Jan-26	16-Apr-26	95	CONS-EB-2170, CONS-
PR0-26-1590	Fabrication and delivery of architectural lighting fixtures	50%	63.64%	40	01-Oct-25 A	29-Jan-26	16-Apr-26	95	CONS-EB-1990, CONS-
PRO-06-1010	Fabrication and delivery of architectural woodwork materials	0%	0%	40	01-Dec-25	29-Jan-26	31-Dec-25	100	CONS-EB-2260
PRO-05-1010	Fabrication and delivery of steel deck	0%	0%	60	01-Dec-25	02-Mar-26	30-Jan-26	92	CONS-EB-1195
PR0-08-1080	Fabrication and delivery of aluminum windows	0%	0%	60	01-Dec-25	02-Mar-26	30-Jan-26	46	CONS-EB-1350, CONS-
PR0-08-1100	Fabrication and delivery of door hardware	0%	0%	40	01-Dec-25	29-Jan-26	31-Dec-25	82	CONS-EB-2200
PR0-08-1110	Fabrication and delivery of glass and glazing	0%	0%	100	01-Dec-25	29-Apr-26	01-Apr-26	27	CONS-EB-1860
PR0-10-1480	Fabrication and delivery of interior glass partitions	0%	0%	30	01-Dec-25	14-Jan-26	16-Dec-25	92	CONS-EB-1390
PR0-11-1030	Fabrication and delivery of food service equipments	0%	0%	60	01-Dec-25	02-Mar-26	30-Jan-26	92	CONS-EB-3400

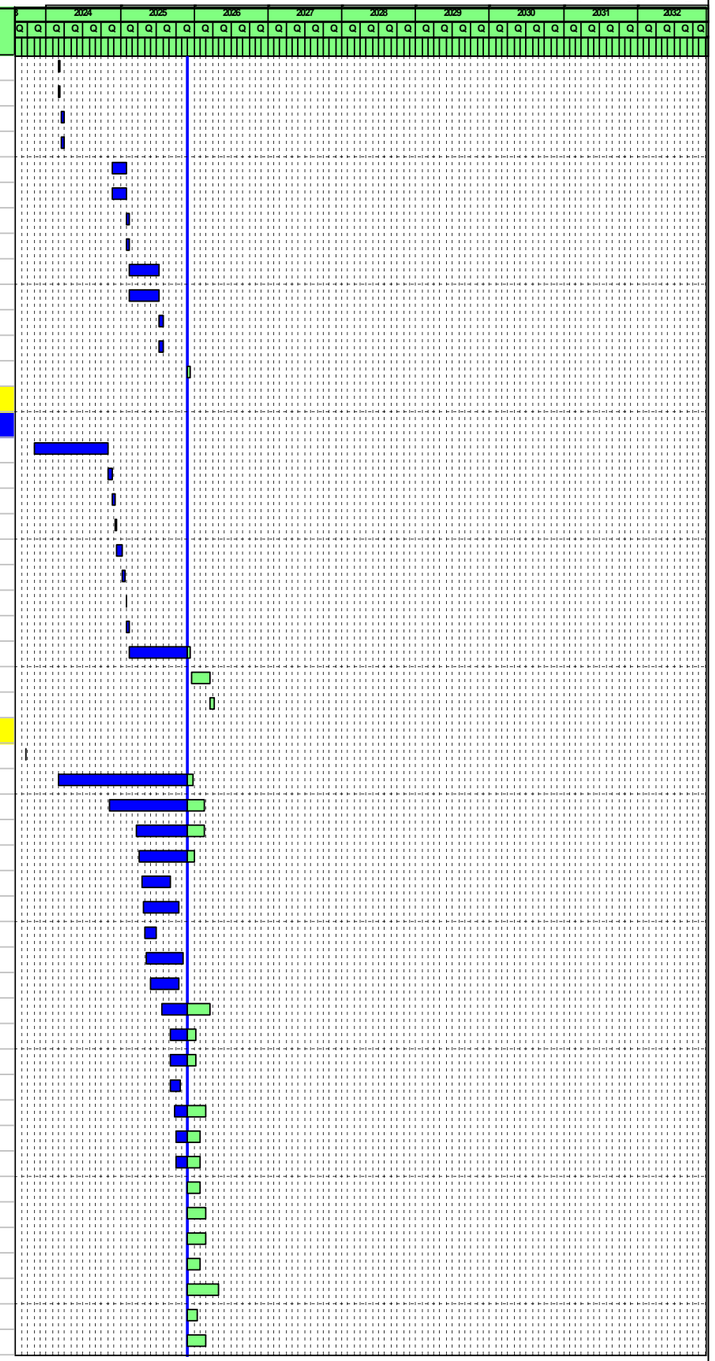


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PR0-22-1370	Fabrication and delivery of motors and motor controllers (Are located within the pumping units)	0%	0%	60	01-Dec-25	02-Mar-26	01-Apr-26	84	CONS-EB-6350
PR0-22-1400	Fabrication and delivery of gas systems	0%	0%	60	01-Dec-25	02-Mar-26	02-Feb-26	101	CONS-EB-6360
PR0-23-1460	Fabrication and delivery of instrumentation & control for hvac	0%	0%	60	01-Dec-25	02-Mar-26	30-Jan-26	80	CONS-EB-1320
PR0-26-1530	Fabrication and delivery of disconnect switches & motor controllers	0%	0%	30	01-Dec-25	14-Jan-26	16-Dec-25	51	CONS-EB-6345
PR0-28-1010	Fabrication and delivery of fire alarm system	0%	0%	40	01-Dec-25	29-Jan-26	31-Dec-25	121	CONS-EB-2180, CONS-
PR0-21-1080	Fabrication and delivery of Fire Pump	0%	0%	60	02-Dec-25	04-Mar-26	18-Mar-26	83	CONS-EB-6350
PR0-08-1090	Field Measure & Fabricate/ delivery of metal-framed skylights @ Training Room 238	0%	0%	65	19-Dec-25	27-Mar-26	27-Mar-26	37	CONS-EB-6600
PR0-08-1445	Field Measure & Fabricate/ delivery of metal-framed skylights @ Stair 1	0%	0%	65	19-Dec-25	27-Mar-26	27-Mar-26	37	CONS-EB-6600
PRO-05-1040	Fabrication and delivery of ornamental metals materials	0%	0%	60	23-Dec-25	24-Mar-26	23-Mar-26	40	CONS-EB-2300
PR0-22-1450	Fabrication and delivery of medical gas system	0%	0%	60	23-Jan-26	22-Apr-26	25-Mar-26	71	CONS-EB-6375
PR0-13-1000	Fabrication and delivery of x-ray protection equipment	0%	0%	60	30-Jan-26	29-Apr-26	01-Apr-26	40	CONS-EB-2260
PRO-48-1040	Fabrication and delivery of solar panels system	0%	0%	40	09-Apr-26	05-Jun-26	07-May-26	42	CONS-EB-2020
BULLETINS/CHANGE ORDERS			78.74%	149	04-Aug-23 A	10-Jul-26	18-Sep-26	46	
BULLETIN # 1 HVAC Ductwork Mechanical Bulkhead			95.37%	25	04-Aug-23 A	11-Feb-26	26-Dec-25	125	
BULL#1-10	Issue Bulletin # 1 hvac ductwork Mechanical Bulkhead	100%	100%	0	04-Aug-23 A	12-Sep-23 A	01-Nov-25		BULL#1-15
BULL#1-15	Prepare Cost Proposal for Bulletin # 1 hvac ductwork Mechanical Bulkhead	100%	100%	0	13-Sep-23 A	04-Mar-24 A	01-Nov-25		BULL#1-20, PR0-07-126
BULL#1-20	Negotiate Cost Proposal for Bulletin # 1 hvac ductwork Mechanical Bulkhead	100%	100%	0	05-Mar-24 A	29-Apr-25 A	01-Nov-25		PR0-23-1480
BULL#1-25	Install Bulletin #1 Rooftop Duct Supports	0%	0%	10	06-Jan-26	20-Jan-26	03-Dec-25	125	BULL#1-30
BULL#1-30	Install Bulletin #1 Pitch Pockets at Rooftop Duct Supports	0%	0%	5	21-Jan-26	27-Jan-26	10-Dec-25	125	BULL#1-35
BULL#1-35	Install Bulletin #1 Rooftop Ductwork	0%	0%	5	28-Jan-26	03-Feb-26	18-Dec-25	125	BULL#1-40
BULL#1-40	Insulate Bulletin #1 Rooftop Ductwork	0%	0%	5	05-Feb-26	11-Feb-26	26-Dec-25	125	CONS-EB-6430
BULLETIN # 2 CIP Reinforcement Pit , Shift Grid Lines,Chase Walls,Shaft Plumbing Risers			92.33%	50	07-Aug-23 A	29-Apr-26	27-Feb-26	95	
BULL#2-10	Issue Bulletin # 2 for CIP Reinforcement Pit , Shift Grid Lines,Chase Walls,Shaft Plumbing Risers	100%	100%	0	07-Aug-23 A	12-Jan-24 A	01-Nov-25		BULL#2-15, PRO-05-10
BULL#2-22	TYLin Directive to Proceed with Bulletin # 2 for CIP Pit , Shift Grid Lines,Chase Walls,Shaft Plumbing Risers	100%	100%	0	13-Jan-24 A	19-Mar-25 A	01-Nov-25		BULL#2-25
BULL#2-15	Submit Cost for Bulletin # 2 for CIP Reinforcement Pit , Shift Grid Lines,Chase Walls,Shaft Plumbing Risers	100%	100%	0	15-Jan-24 A	03-Jul-24 A	01-Nov-25		BULL#2-20, PRO-05-10
BULL#2-20	Negotiate Cost Proposal for Bulletin # 2 for CIP Reinforcement Pit , Shift Grid Lines,Chase Walls,Shaft Plun	100%	100%	0	05-Jul-24 A	07-Nov-25 A	01-Nov-25		ML2000
BULL#2-25	Excavate for Bulletin #2 Fur/Hair Interceptor Pits	100%	100%	0	12-Jun-25 A	12-Jun-25 A	01-Nov-25		BULL#2-30
BULL#2-30	Formwork/Rebar for Bulletin #2 Fur/Hair Interceptor Pits	100%	100%	0	13-Jun-25 A	13-Jun-25 A	01-Nov-25		BULL#2-35
BULL#2-35	Pour/Cure for Bulletin #2 Fur/Hair Interceptor Pits	100%	100%	0	16-Jun-25 A	24-Jun-25 A	01-Nov-25		BULL#2-40
BULL#2-40	Waterproof at Bulletin #2 Fur/Hair Interceptor Pits	100%	100%	0	26-Jun-25 A	26-Jun-25 A	01-Nov-25		CONS-EB-1650
BULL#2-45	Drill/Dowel Slab for Bulletin #2 Chase Walls	0%	0%	4	17-Feb-26	20-Feb-26	05-Feb-26	31	BULL#2-50, CONS-EB-2
BULL#2-50	Construct CMU for Bulletin #2 Chase Walls	0%	0%	15	09-Apr-26	29-Apr-26	27-Feb-26	0	CONS-EB-2050, CONS-
BULLETIN # 3 BPP and Street Tree Plans			100%	0	01-May-24 A	18-Nov-24 A	01-Nov-25		
BULL#03-10	Issue Bulletin # 3 BPP and Street tree Plans	100%	100%	0	01-May-24 A	01-May-24 A	01-Nov-25		BULL#08-15, BULL#03-
BULL#03-12	Await Further Redesign & DOT Approval of BPP Bulletin # 3 BPP and Street tree Plans (changed to Bulletin	100%	100%	0	02-May-24 A	18-Nov-24 A	01-Nov-25		BULL#08-15, BULL#08-
BULLETIN # 4 Structural Elevations & Foundation			84.92%	27	07-May-24 A	09-Jan-26	10-Dec-25	168	
BULL#04-10	Issue Bulletin # 4 Structural Elevations & Foundation	100%	100%	0	07-May-24 A	07-May-24 A	01-Nov-25		BULL#04-15, BULL#04-
BULL#04-15	Submit Cost for Bulletin # 4 Structural Elevations & Foundation	100%	100%	0	08-May-24 A	28-Oct-24 A	01-Nov-25		BULL#04-20
BULL#04-25	Revise Coordination Drawings for Underground Plumbing	100%	100%	0	15-May-24 A	11-Jun-24 A	01-Nov-25		PRO-22-1230
BULL#04-20	Negotiate Cost Proposal for Bulletin # 4 Structural Elevations & Foundation	10%	10%	27	29-Oct-24 A	09-Jan-26	10-Dec-25	168	ML2000
BULLETIN # 5 Revisons to ATS Room			86.43%	30	07-May-24 A	14-Jan-26	16-Dec-25	0	
BULL#05-10	Issue Bulletin # 5 Masonry Revisons to ATS Room	100%	100%	0	07-May-24 A	03-Jul-24 A	01-Nov-25		BULL#05-15, BULL#05-
BULL#05-15	Submit Cost for Bulletin # 5 Masonry Revisons to ATS Room	100%	100%	0	05-Jul-24 A	20-Dec-24 A	01-Nov-25		BULL#05-20
BULL#05-25	Revise Coordination Drawings for ATS Room	100%	100%	0	10-Jul-24 A	18-Nov-24 A	01-Nov-25		PRO-26-1022, PRO-04-
BULL#05-20	Negotiate Cost Proposal for Bulletin # 5 Masonry Revisons to ATS Room	0%	0%	30	23-Dec-24 A	14-Jan-26	16-Dec-25	0	PRO-04-1020
BULLETIN # 6 Shear Wall and Foundation Changes			92.06%	30	07-May-24 A	14-Jan-26	16-Dec-25	165	
BULL#06-10	Issue Bulletin # 6 Shear Wall and Foundation Changes	100%	100%	0	07-May-24 A	25-Jul-24 A	01-Nov-25		BULL#06-15, BULL#06-
BULL#06-15	Submit Cost for Bulletin # 6 Shear Wall and Foundation Changes	100%	100%	0	26-Jul-24 A	27-Jan-25 A	01-Nov-25		BULL#06-20
BULL#06-25	Submit RFI #86 for Additional Discrepancies in Bulletin #6	100%	100%	0	26-Jul-24 A	29-Jul-24 A	01-Nov-25		BULL#06-30
BULL#06-30	Bulletin #6 Rev 1 Issued	100%	100%	0	30-Jul-24 A	08-Aug-24 A	01-Nov-25		PRO-22-1230, PRO-26-
BULL#06-35	CM to issue directive to proceed with Bulletin #6 work	100%	95%	1	09-Aug-24 A	01-Dec-25	03-Nov-25	0	BULL#06-20, BULL#06-

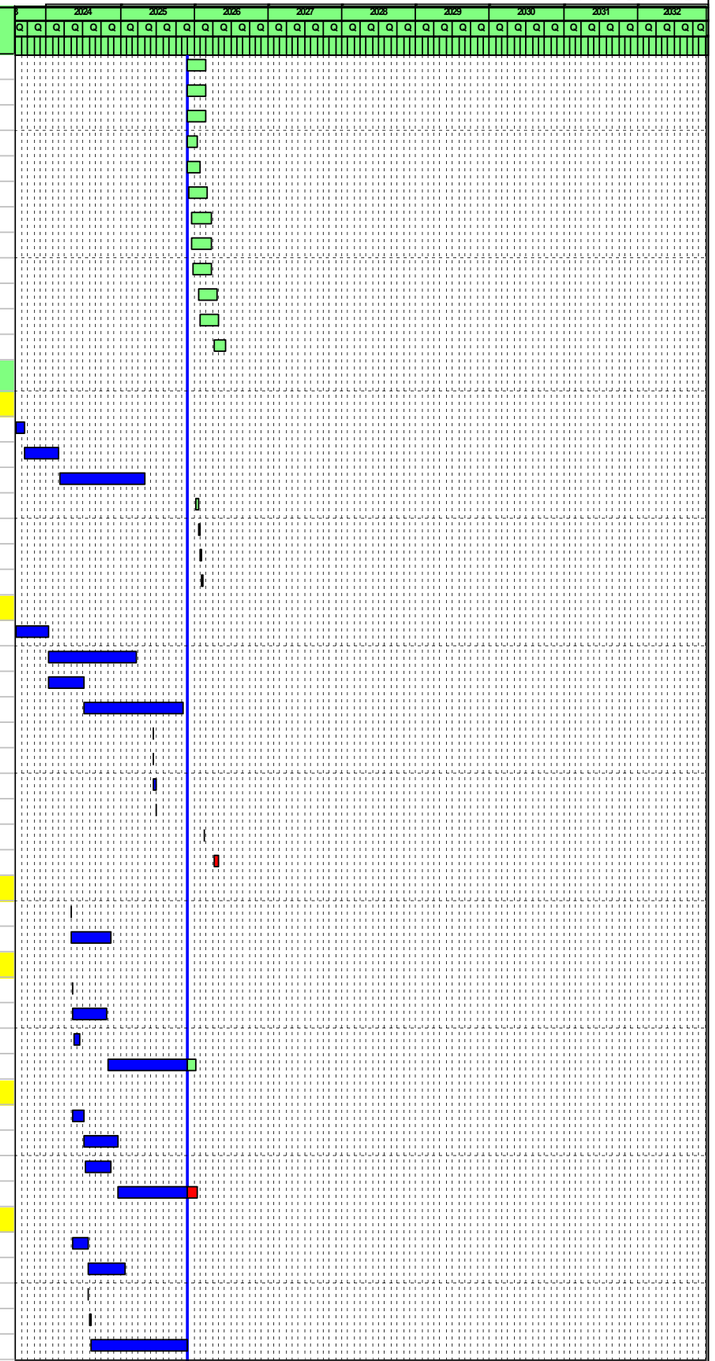


Remaining Level of Effort ◆ ◆ Milestone
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
BULL#06-20	Negotiate Cost Proposal for Bulletin # 6 Shear Wall and Foundation Changes	0%	0%	30	28-Jan-25 A	14-Jan-26	16-Dec-25	165	ML2000
BULL#06-40	Add 3'-10 to W-6 Wall per Bulletin #6,	100%	100%	0	28-Aug-25 A	28-Aug-25 A	03-Nov-25		CONS-EB-5950
BULL#06-45	Move CB-3 off slab edge per Bulletin #6,	100%	100%	0	28-Aug-25 A	28-Aug-25 A	01-Nov-25		CONS-EB-1850
BULLETIN # 7 Additional Skylight			80.23%	96	18-Nov-24 A	23-Apr-26	23-Apr-26	99	
BULL#07-05	Issue Bulletin # 7 Additional Skylight on Steel	100%	100%	0	18-Nov-24 A	18-Nov-24 A	01-Nov-25		BULL#07-10
BULL#07-10	Submit Cost for Bulletin # 7 Additional Skylight	100%	100%	0	19-Nov-24 A	04-Jun-25 A	01-Nov-25		BULL#07-15, BULL#07-
BULL#07-25	Prepare shop drawings for Bulletin #7 added skylight steel	100%	100%	0	06-May-25 A	06-May-25 A	01-Nov-25		BULL#07-30
BULL#07-30	Review/Approve shop drawings for Bulletin #7 added skylight steel	100%	100%	0	07-May-25 A	16-May-25 A	01-Nov-25		BULL#07-35, BULL#07-
BULL#07-15	DDC review and negotiate change order for Bulletin #7 additional skylight steel	0%	0%	20	05-Jun-25 A	30-Dec-25	01-Dec-25	165	BULL#07-20
BULL#07-35	Fabricate Bulletin #7 skylight support steel	100%	100%	0	01-Oct-25 A	31-Oct-25 A	01-Nov-25		CONS-EB-6270, BULL#
BULL#07-40	Erect Bulletin #7 skylight support steel	100%	100%	0	10-Nov-25 A	13-Nov-25 A	23-Dec-25		CONS-EB-6600
BULL#07-45	Additional formwork and embed plates per Bulletin #7	0%	0%	5	01-Dec-25	05-Dec-25	21-Nov-25	163	CONS-EB-1130
BULL#07-20	DDC issue change order for Bulletin #7	0%	0%	10	31-Dec-25	14-Jan-26	16-Dec-25	165	ML2000
BULL#07-50	Add 5'-4 exterior cavity wall per Bulletin #7	0%	0%	5	16-Mar-26	20-Mar-26	05-Mar-26	54	CONS-EB-1890
BULL#07-55	Add stepped flashing at skylight per Bulletin #7, SK-016	0%	0%	5	13-Apr-26	20-Apr-26	20-Apr-26	87	BULL#07-60
BULL#07-60	Paint Bulletin #7 Skylight Steel	0%	0%	3	20-Apr-26	23-Apr-26	23-Apr-26	87	CONS-INSP-1010
BULLETIN # 8 BPP and Street Tree Plans			73.35%	149	29-Mar-24 A	10-Jul-26	18-Sep-26	46	
BULL#08-10	DDC to issued Bulletin # 3 & changed to Bulletin # 8 for revised site Connecton plan for storm drainage utiliti	100%	100%	0	29-Mar-24 A	19-Nov-24 A	01-Nov-25		PRO-33-1060, PRO-33-
BULL#08-15	Submit Cost for Bulletin # 8 BPP and Street tree Plans	0%	83.33%	10	20-Nov-24 A	12-Dec-25	14-Nov-25	90	BULL#08-20
BULL#08-25	Bulletin #8 DDC provide utility letter to Relocate Utility Pole (changed to Bulletin # 8)	100%	100%	0	01-Aug-25 A	29-Aug-25 A	01-Nov-25		BULL#08-30
BULL#08-20	Negotiate Cost Proposal for Bulletin # 8 BPP and Street tree Plans	0%	0%	30	16-Dec-25	29-Jan-26	31-Dec-25	90	SITE-1120, SITE-1070
BULL#08-30	Bulletin # 8 BPP Drawings - Install new Sidewalks	0%	0%	15	21-May-26	12-Jun-26	19-Aug-26	46	BULL#08-40
BULL#08-40	Mill and Repave three streets per Bulletin # 8	0%	0%	20	15-Jun-26	10-Jul-26	18-Sep-26	46	ML2000
BULLETIN # 9 Dog Turf Changes			77.96%	110	05-Mar-24 A	14-May-26	16-Apr-26	70	
BULL#09-55	TY Lin to Issue Direction to Proceed for Bulletin # 9 Dog Turf Redesign	100%	100%	0	05-Mar-24 A	03-Jun-25 A	01-Nov-25		BULL#09-35
BULL#09-05	Issue Bulletin # 9 Dog Turf Redesign	100%	100%	0	20-Dec-24 A	20-Dec-24 A	01-Nov-25		BULL#09-10, BULL#09-
BULL#09-10	Submit Cost for Bulletin # 9 Dog Turf Redesign	0%	0%	40	23-Dec-24 A	29-Jan-26	31-Dec-25	70	BULL#09-20
BULL#09-25	Prepare shop drawings for Bulletin #9 dropped slabs for redesigned dog turf	100%	100%	0	20-Feb-25 A	20-Feb-25 A	01-Nov-25		BULL#09-30
BULL#09-30	Review/Approve shop drawings for Bulletin #9 dropped slabs for redesigned dog turf	100%	100%	0	21-Feb-25 A	04-Mar-25 A	01-Nov-25		BULL#09-35, BULL#09-
BULL#09-35	Fabricate Bulletin #9 dropped slabs Rebar	100%	100%	0	02-Sep-25 A	29-Sep-25 A	01-Nov-25		CONS-EB-1730, BULL#
BULL#09-60	Added formwork and rebar to lower 2nd floor slab depressions for Bulletin # 9 Dog Turf	100%	100%	0	01-Oct-25 A	02-Oct-25 A	01-Nov-25		CONS-EB-1730
BULL#09-20	DDC review and negotiate change order for Bulletin # 9 Dog Turf Redesign	0%	0%	20	30-Jan-26	02-Mar-26	30-Jan-26	70	BULL#09-15
BULL#09-15	DDC issue change order for Bulletin # 9 Dog Turf	0%	0%	10	03-Mar-26	17-Mar-26	17-Feb-26	70	ML2000, BULL#09-65
BULL#09-65	Fabricate/Deliver pedestal system for dog turf per Bulletin #9.	0%	0%	40	18-Mar-26	14-May-26	16-Apr-26	70	CONS-EB-6330
BULLETIN # 10 Con Edison Service Changes			93.49%	20	04-Oct-24 A	30-Dec-25	01-Dec-25	155	
BULL#10-05	Issue Bulletin # 10 for Con Ed Service Changes	100%	100%	0	04-Oct-24 A	14-Jan-25 A	01-Nov-25		BULL#10-10
BULL#10-10	MEP Re-coordination for Con Ed Service Changes	100%	100%	0	15-Jan-25 A	23-May-25 A	01-Nov-25		BULL#10-15
BULL#10-15	Submit Cost for Bulletin # 10 Con Edison Service Changes	100%	100%	0	26-May-25 A	26-Jun-25 A	01-Nov-25		BULL#10-20
BULL#10-20	DDC review and negotiate change order for Bulletin # 10 Con Edison Service Changes	0%	0%	20	27-Jun-25 A	30-Dec-25	01-Dec-25	155	PRO-1-1070
BULLETIN # 11 New Foundation @ Grid Line 1			97.06%	8	31-Jan-25 A	10-Dec-25	12-Nov-25	187	
RFI#124-10	Submit RFI # 124 regarding Retaining Wall at Property Line Grid Line 1	100%	100%	0	31-Jan-25 A	31-Jan-25 A	01-Nov-25		RFI#124-15
RFI#124-15	Response to RFI # 124 regarding Retaining Wall at Property Line Grid Line 1	100%	100%	0	03-Feb-25 A	04-Feb-25 A	01-Nov-25		RFI#124-20
RFI#124-20	DDC Negotiate Access Agreement with Hotel regarding Retaining Wall at Property Line Grid Line 1	100%	100%	0	05-Feb-25 A	12-Feb-25 A	01-Nov-25		BULL#11-05, RFI#135-1
BULL#11-05	Issue Bulletin # 11 New Foundation @ Grid Line 1	100%	100%	0	13-Feb-25 A	24-Feb-25 A	01-Nov-25		BULL#11-10, BULL#11-
BULL#11-10	Submit Cost for Bulletin # 11 New Foundation @ Grid Line 1	100%	100%	0	25-Feb-25 A	13-May-25 A	01-Nov-25		BULL#11-15
BULL#11-12	TYLIN Issue Directive to proceed with Bulletin # 11 New Foundation @ Grid Line 1	100%	100%	0	25-Feb-25 A	19-Mar-25 A	01-Nov-25		BULL#11-20, CONS-EB-
BULL#11-20	Revise Ground Improvement Shop Drawings for 11 New Foundation @ Grid Line 1	100%	100%	0	27-Feb-25 A	06-Mar-25 A	01-Nov-25		BULL#11-25
BULL#11-25	Approve Ground Improvement Shop Drawings for 11 New Foundation @ Grid Line 1	100%	100%	0	07-Mar-25 A	18-Mar-25 A	01-Nov-25		CONS-EB-1060
BULL#11-15	DDC review and negotiate change order for Bulletin # 11 New Foundation @ Grid Line 1	60%	60%	8	14-May-25 A	10-Dec-25	12-Nov-25	187	ML2000
BULLETIN # 12 for Pergola Foundation Design			93.86%	22	20-Feb-25 A	02-Jan-26	03-Dec-25	173	
RFI#135-10	Submit RFI # 135 regarding unforeseen retaining Wall Condition @ Hotel Property Line	100%	100%	0	20-Feb-25 A	20-Feb-25 A	01-Nov-25		RFI#135-15

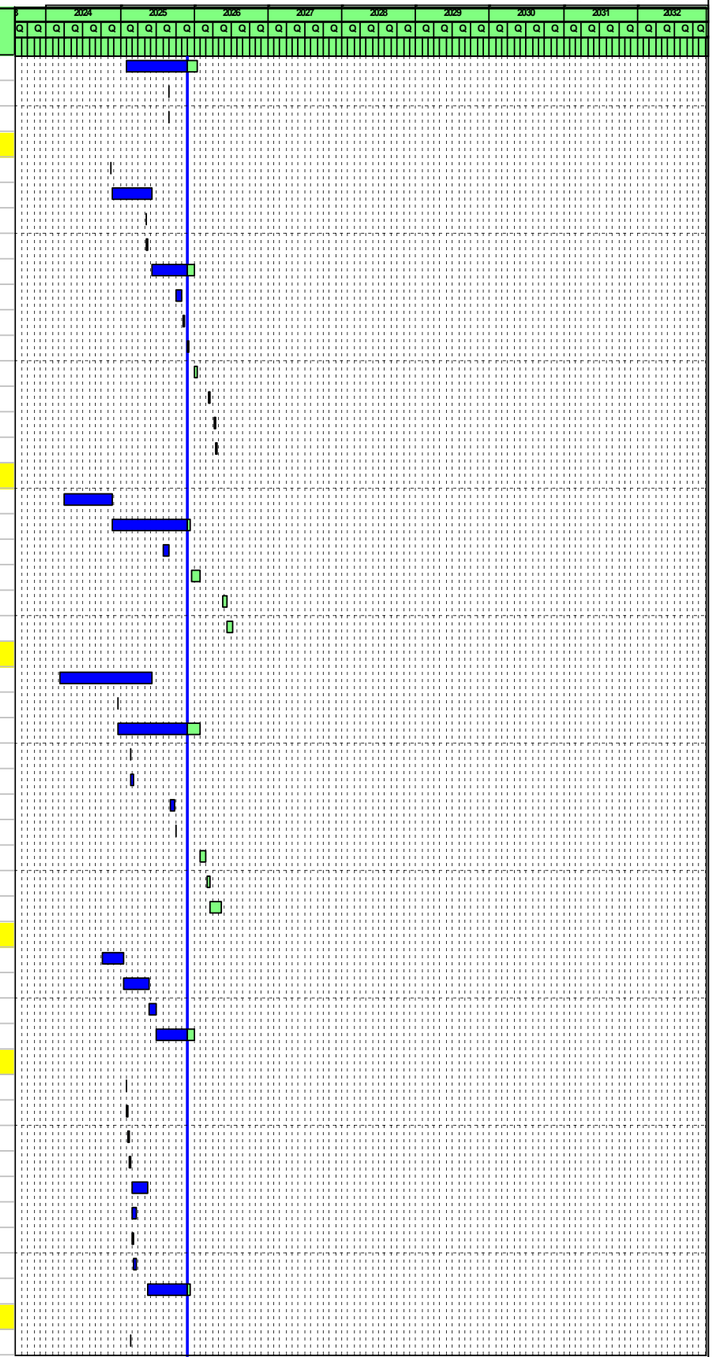


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
RFI#135-15	Response to RFI # 135 regarding unforeseen retaining Wall Condition @ Hotel Property Line	100%	100%	0	21-Feb-25 A	25-Feb-25 A	01-Nov-25		BULL#12-10
BULL#12-10	DDC Prepare Bulletin # 12 for Pergola Foundation Design	100%	100%	0	26-Feb-25 A	13-Mar-25 A	01-Nov-25		BULL#12-15
BULL#12-15	CM to Issue Direction to Proceed with Bulletin # 12 for Pergola Foundation Design	100%	100%	0	05-Mar-25 A	25-Apr-25 A	01-Nov-25		BULL#12-20, CONS-EB
BULL#12-20	Submit Cost for Bulletin # 12 for Pergola Foundation Design	90%	90%	2	28-Apr-25 A	02-Dec-25	04-Nov-25	173	BULL#12-25
BULL#12-25	DDC review and negotiate change order for Bulletin # 12 for Pergola Foundation Design	0%	0%	20	03-Dec-25	02-Jan-26	03-Dec-25	173	ML2000
BULLETIN # 13 for Gas Redesign			84.02%	27	04-Aug-23 A	09-Jan-26	10-Dec-25	168	
PRO-221395	AE Notifies MPCC of Reroute Point of Entry Gas Redesign from Neighbor's Driveway	100%	100%	0	04-Aug-23 A	02-May-25 A	01-Nov-25		PRO-221400
BULL#13-10	DDC Prepare Bulletin # 13 for Gas Redesign	100%	100%	0	31-Mar-25 A	31-Mar-25 A	01-Nov-25		BULL#13-15
BULL#13-15	CM to Issue Direction to Proceed with Bulletin # 13 for Gas Redesign	0%	0%	2	01-Apr-25 A	02-Dec-25	04-Nov-25	101	BULL#13-20, PRO-22-1
PRO-221400	National Grid Point of Entry Gas Redesign	100%	100%	0	02-May-25 A	13-Jun-25 A	01-Nov-25		PRO-221405
PRO-221405	National Grid Fabricate Amended Gas Supply Bends	100%	100%	0	16-Jun-25 A	22-Jul-25 A	01-Nov-25		BULL#13-45
BULL#13-45	Install Amended Gas Supply Bends	100%	100%	0	23-Jul-25 A	23-Jul-25 A	01-Nov-25		CONS-EB-6510, CONS-
BULL#13-20	Submit Cost for Bulletin # 13 for Gas Redesign	0%	0%	5	03-Dec-25	09-Dec-25	11-Nov-25	168	BULL#13-25
BULL#13-25	DDC review and negotiate change order for Bulletin # 13 for Gas Redesign	0%	0%	20	10-Dec-25	09-Jan-26	10-Dec-25	168	ML2000
BULLETIN # 14 Added Spec 054000			99.42%	1	23-Jul-25 A	01-Dec-25	16-Dec-25	49	
BULL#14-10	Prepare & Submit Cold Form Framing Shop Drawings R0	100%	100%	0	23-Jul-25 A	23-Jul-25 A	01-Nov-25		BULL#14-15
BULL#14-05	DDC Issues Bulletin # 14 Spec 054000	100%	100%	0	23-Jul-25 A	23-Jul-25 A	01-Nov-25		BULL#14-10
BULL#14-15	Return Cold Form Framing Shop Drawings R0	100%	100%	0	24-Jul-25 A	27-Aug-25 A	01-Nov-25		BULL#14-20
BULL#14-20	Re-Submit Cold Form Framing Shop Drawings R1	100%	100%	0	28-Aug-25 A	13-Nov-25 A	01-Dec-25		BULL#14-25
BULL#14-25	Approve Cold Form Framing Shop Drawings R1	90%	90%	1	14-Nov-25 A	01-Dec-25	16-Dec-25	49	CONS-EB-6565, CONS-
BULLETIN # 15 Increase of Scope of CMU Mockup to Include Foundation & Slabs			100%	0	14-Aug-25 A	14-Oct-25 A	01-Nov-25		
BULL#15-10	CM to Issue NOD to Proceed with Bulletin # 15	100%	100%	0	14-Aug-25 A	14-Aug-25 A	01-Nov-25		BULL#15-15, BULL#15-
BULL#15-05	DDC Issues Bulletin # 15 15 Increase of Scope of CMU Mockup to Include Foundation & Slabs	100%	100%	0	14-Aug-25 A	14-Aug-25 A	01-Nov-25		BULL#15-10
BULL#15-15	Contractor to Hire Engineer to Design Foundation for Mockup	100%	100%	0	15-Aug-25 A	27-Aug-25 A	01-Nov-25		BULL#15-20
BULL#15-20	Submit Design Foundation for Mockup	100%	100%	0	28-Aug-25 A	13-Oct-25 A	01-Nov-25		BULL#15-30
BULL#15-30	Approve Design Foundation for Mockup	100%	100%	0	14-Oct-25 A	14-Oct-25 A	01-Nov-25		PRO-04-1050
PRE-CONSTRUCTION			100%	0	04-Aug-23 A	03-Apr-25 A	01-Nov-25		
PERMITTING AND LICENSING AGREEMENTS			100%	0	04-Aug-23 A	03-Apr-25 A	01-Nov-25		
PER-1010	Procure fence permit	100%	100%	0	04-Aug-23 A	18-Sep-23 A	01-Nov-25		PRE-1090, PRE-1095
PER-1020	Procure dot permit	100%	100%	0	04-Aug-23 A	31-Oct-23 A	01-Nov-25		ML1010, CONS-FOUN-
ML3020	DDC Obtain Licensing Agreement with Existing Property (90 ccd)	100%	100%	0	04-Aug-23 A	29-Nov-24 A	01-Nov-25		CONS-FOUN-1020, PRE
PER-1020a	DOT Denies Permit Renewals Due to Delays until Demo Permit is Issued	100%	100%	0	01-Nov-23 A	17-Jul-24 A	01-Nov-25		PER-1020b
PER-1020b	Re-apply and obtain DOT Permits	100%	100%	0	18-Jul-24 A	09-Aug-24 A	01-Nov-25		PRE-1170
PER-1030	Obtain Demolition permit	100%	100%	0	04-Oct-24 A	25-Oct-24 A	01-Nov-25		PER-1000, CONS-ARCI
PER-1040	Apply for Plumbing permit	100%	100%	0	06-Jan-25 A	21-Jan-25 A	01-Nov-25		CONS-EB-1620
PER-1000	Apply DOB for building permit	100%	100%	0	13-Feb-25 A	05-Mar-25 A	01-Nov-25		CONS-EB-6100
PER-1035	Apply for excavation permit	100%	100%	0	13-Feb-25 A	05-Mar-25 A	01-Nov-25		CONS-EB-1620
PER-1050	Apply for Foundation /Concrete permit	100%	100%	0	13-Feb-25 A	05-Mar-25 A	01-Nov-25		CONS-EB-1630, CONS-
PER-1045	Apply for SOE permit	100%	100%	0	06-Mar-25 A	03-Apr-25 A	01-Nov-25		CONS-EB-1060
MOBILIZATION			100%	0	01-Aug-24 A	07-Feb-25 A	01-Nov-25		
PRE-1045	Owner terminate account Gas to Existing Building (Exact Date Unknown)	100%	100%	0	01-Aug-24 A	01-Aug-24 A	01-Nov-25		PRE-1046
PRE-1046	Owner pay final bill Gas to Existing Building (Exact Date Unknown)	100%	100%	0	01-Aug-24 A	01-Aug-24 A	01-Nov-25		PRE-1047
PRE-1047	Owner provide demo letter about Gas to Existing Building	100%	100%	0	02-Aug-24 A	08-Aug-24 A	01-Nov-25		PRE-1048
PRE-1048	Owner/Contractor schedule utility gas cut/cap to Existing Building	100%	100%	0	02-Aug-24 A	08-Aug-24 A	01-Nov-25		PRE-1050
PRE-1050	Gas Utility Cut/Cap to Existing Building	100%	100%	0	09-Aug-24 A	04-Sep-24 A	01-Nov-25		PER-1000, PER-1030, F
PRE-1170	Setup MPT	100%	100%	0	23-Aug-24 A	28-Aug-24 A	01-Nov-25		ML1010, PRE-1180
PRE-1090	Install Construction Fencing at Property Lines and Curbs	100%	100%	0	27-Aug-24 A	29-Aug-24 A	01-Nov-25		PRE-1080, CONS-FOUI
PRE-1190	Take Soil borings for Waste Characterization	100%	100%	0	27-Aug-24 A	28-Aug-24 A	01-Nov-25		PRE-1195
PRE-1180	Install project sign	100%	100%	0	28-Aug-24 A	28-Aug-24 A	01-Nov-25		PRE-1120
PRE-1195	Receive results for Soil Disposal	100%	100%	0	29-Aug-24 A	31-Dec-24 A	01-Nov-25		CONS-EB-1610, CONS-
PRE-1160	Furnish temporary toilets	100%	100%	0	02-Oct-24 A	02-Oct-24 A	01-Nov-25		CONS-EB-1060, CONS-

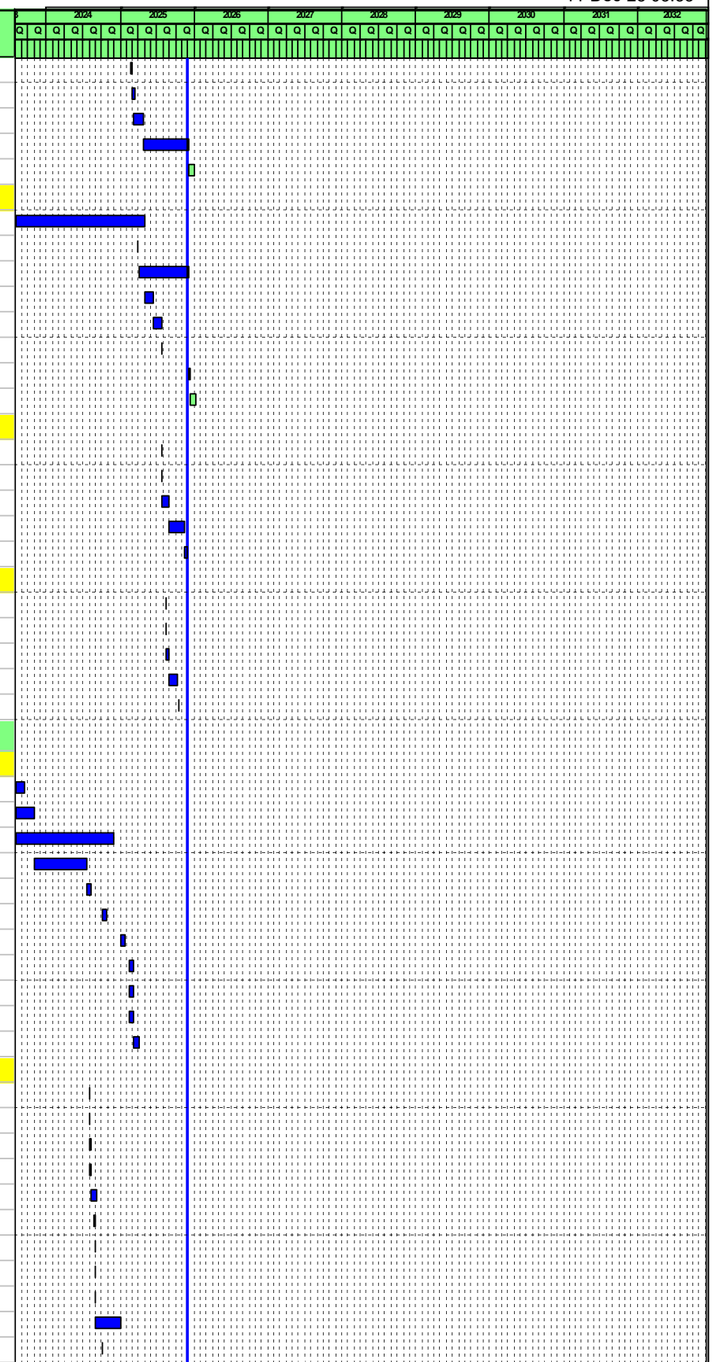


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PRE-1205	DDC to Obtain Waivers from Neighbors regarding vibrations Monitor Installation	100%	100%	0	25-Oct-24 A	19-Dec-24 A	01-Nov-25		PRE-1215, RFI#124-10
PRE-1080	Prepare site for field office setup	100%	100%	0	18-Nov-24 A	25-Nov-24 A	01-Nov-25		PRE-1120
PRE-1120	Field Office Setup	100%	100%	0	18-Nov-24 A	25-Nov-24 A	01-Nov-25		PRE-1130, PRE-1150
PRE-1095	Install additional fence at adjacent parking lots for pedestrian protection	100%	100%	0	03-Dec-24 A	03-Dec-24 A	01-Nov-25		CONS-ARCH-1040
PRE-1215	Install Vibrations & Displacement Monitors	100%	100%	0	20-Dec-24 A	30-Dec-24 A	01-Nov-25		CONS-ARCH-1040, RFI
PRE-1225	Install Add'l on 850 Shepard ave.Vibrations & Displacement Monitors	100%	100%	0	06-Feb-25 A	07-Feb-25 A	01-Nov-25		CONS-EB-1060
ENABLING UTILITIES			100%	0	20-May-24 A	19-Dec-24 A	01-Nov-25		
PRE-1055	Utility Survey Underground Sewer and Water to Existing Building	100%	100%	0	20-May-24 A	20-May-24 A	01-Nov-25		PRE-1060, PRO-31-117
PRE-1040A	DOHMH Terminate Electrical Service with Con Ed	100%	100%	0	01-Aug-24 A	07-Aug-24 A	01-Nov-25		PRE-1040B
PRE-1040B	DOHMH Pay Final Balance for Electrical Service	100%	100%	0	01-Aug-24 A	07-Aug-24 A	01-Nov-25		PRE-1040C
PRE-1040C	Open Case with Con Ed for Existing Service Disconnection	100%	100%	0	12-Aug-24 A	12-Aug-24 A	01-Nov-25		PRE-1040D
PRE-1040D	Con Ed Schedule Service Disconnection	100%	100%	0	13-Aug-24 A	30-Aug-24 A	01-Nov-25		PRE-1040E
PRE-1040E	Con Ed Service Disconnection	100%	100%	0	03-Sep-24 A	13-Sep-24 A	01-Nov-25		PER-1000, PER-1030, F
PRE-1130	Installation of temporary electrical service	100%	100%	0	11-Sep-24 A	19-Dec-24 A	01-Nov-25		CONS-EB-1140, CONS-
PRE-1060	Disconnect Water Service and Sewer to Existing Building	100%	100%	0	01-Oct-24 A	03-Oct-24 A	01-Nov-25		PER-1000, PER-1030, F
PRE-1150	Furnish temporary water	100%	100%	0	12-Dec-24 A	12-Dec-24 A	01-Nov-25		CONS-EB-1060, CONS-
CONSTRUCTION			65.63%	187	28-Jul-23 A	18-Aug-26	31-Jul-26	24	
SITE DEMOLITION			100%	0	23-Jan-24 A	12-Sep-25 A	01-Nov-25		
RFI#127-10	Submit RFI # 127 regarding Unforeseen Foundations at North Lot	100%	100%	0	23-Jan-24 A	23-Jan-25 A	01-Nov-25		RFI#127-15
RFI#119-10	Submit RFI # 119 regarding Unforeseen Foundations at North Lot	100%	100%	0	23-Jan-24 A	23-Jan-25 A	01-Nov-25		RFI#119-15
RFI#130-10	Submit RFI # 130 regarding Unforeseen Foundations at West Lot	100%	100%	0	06-Feb-24 A	06-Feb-25 A	01-Nov-25		RFI#130-15
RFI#131-10	Submit RFI # 131 regarding Unforeseen Foundations at West Lot	100%	100%	0	06-Feb-24 A	06-Feb-25 A	01-Nov-25		RFI#131-15
CONS-FOUN-1010	Perform Site Clearing & Miscellaneous Demolition	100%	100%	0	12-Aug-24 A	06-Feb-25 A	01-Nov-25		CONS-EB-1060, CONS-
RFI#127-15	Response to RFI # 127 regarding Unforeseen Foundations at North Lot	100%	100%	0	24-Jan-25 A	03-Feb-25 A	01-Nov-25		CONS-FOUN-1010, CO
RFI#119-15	Response to RFI # 119 regarding Unforeseen Foundations at North Lot	100%	100%	0	24-Jan-25 A	03-Feb-25 A	01-Nov-25		CONS-FOUN-1010, CO
RFI#130-15	Response to RFI # 130 regarding Unforeseen Foundations at West Lot	100%	100%	0	07-Feb-25 A	14-Feb-25 A	01-Nov-25		CONS-FOUN-1010, CO
RFI#131-15	Response to RFI # 131 regarding Unforeseen Foundations at West Lot	100%	100%	0	07-Feb-25 A	14-Feb-25 A	01-Nov-25		CONS-FOUN-1010, CO
CONS-FOUN-1020	Install Protection Barrier for 2nd Floor Slab Construction	100%	100%	0	08-Sep-25 A	12-Sep-25 A	01-Nov-25		CONS-EB-1730
ACM ABATEMENT			100%	0	28-Jul-23 A	23-May-25 A	01-Nov-25		
RFI#02-10	Submit RFI #2 clarify abatement scope	100%	100%	0	28-Jul-23 A	28-Jul-23 A	01-Nov-25		RFI#02-20
RFI#02-20	Response to RFI #2 regarding clarify abatement scope	100%	100%	0	31-Jul-23 A	28-Oct-23 A	01-Nov-25		RFI#02-30
CONS-DEMO-1000	ACM Ten day Notification Filings CCDs	100%	100%	0	12-Aug-24 A	22-Aug-24 A	01-Nov-25		CONS-MEP-1030
RFI#02-30	Remove RTUs' for abatement per RFI #2 regarding clarify abatement scope	100%	100%	0	15-Aug-24 A	01-Oct-24 A	01-Nov-25		CONS-MEP-1030
CONS-STOP-1000	Partial Stop Work Order Pending Approval of DDC Online Safety Program	100%	100%	0	06-Sep-24 A	06-Sep-24 A	01-Nov-25		PRO-01-1235
CONS-MEP-1030	ACM Abatement & HVAC Unit Removal	100%	100%	0	02-Oct-24 A	04-Oct-24 A	01-Nov-25		CONS-ARCH-1040, PEI
CONS-STOP-1010	Partial Stop Work Order Pending for Potential Concrete Redesign	100%	100%	0	19-May-25 A	23-May-25 A	01-Nov-25		CONS-EB-1690, CONS-
BUILDING DEMOLITION			100%	0	02-Jan-25 A	12-Feb-25 A	01-Nov-25		
CONS-ARCH-1040	Demolition of Existing Building	100%	100%	0	02-Jan-25 A	05-Feb-25 A	01-Nov-25		CONS-EB-1060, CONS-
CONS-ARCH-1045	Removal of Demoltion Debris of Existing Building	100%	100%	0	09-Jan-25 A	07-Feb-25 A	01-Nov-25		CONS-EB-1060, CONS-
CONS-ARCH-1055	Removal of Demoltion Debris of Existing Building	100%	100%	0	06-Feb-25 A	12-Feb-25 A	01-Nov-25		PER-1035, PER-1000, F
EXCAVATION			98.85%	1	11-Feb-25 A	01-Dec-25	03-Nov-25	154	
CONS-EB-1059	Remove & Dispose unforeseen Foundations	100%	100%	0	11-Feb-25 A	27-Feb-25 A	01-Nov-25		CONS-EB-1060
CONS-EB-1060	Install Ground Improvements	100%	100%	0	31-Mar-25 A	10-Apr-25 A	01-Nov-25		CONS-EB-1610, CONS-
CONS-EB-1610	Overexcavation 3 -4' below bottom of footings	100%	100%	0	31-Mar-25 A	10-Apr-25 A	01-Nov-25		CONS-EB-1620, CONS-
CONS-EB-1620	Excavate for underground Plumbing	100%	100%	0	14-May-25 A	10-Sep-25 A	01-Nov-25		CONS-EB-6250, CONS-
CONS-EB-6545	Dispose of Excavated Material (Stockpiled if nescessary)	80%	80%	1	20-May-25 A	01-Dec-25	03-Nov-25	154	SITE-1080
UNDERGROUND PLUMBING			100%	0	14-May-25 A	11-Sep-25 A	01-Nov-25		
PLUMBING			100%	0	14-May-25 A	11-Sep-25 A	01-Nov-25		
CONS-EB-1670	Install Underground plumbing of Building	100%	100%	0	14-May-25 A	11-Sep-25 A	01-Nov-25		CONS-EB-1660, CONS-
FOUNDATIONS			100%	0	15-Apr-25 A	17-Sep-25 A	01-Nov-25		
FOOTINGS			100%	0	15-Apr-25 A	09-Sep-25 A	01-Nov-25		

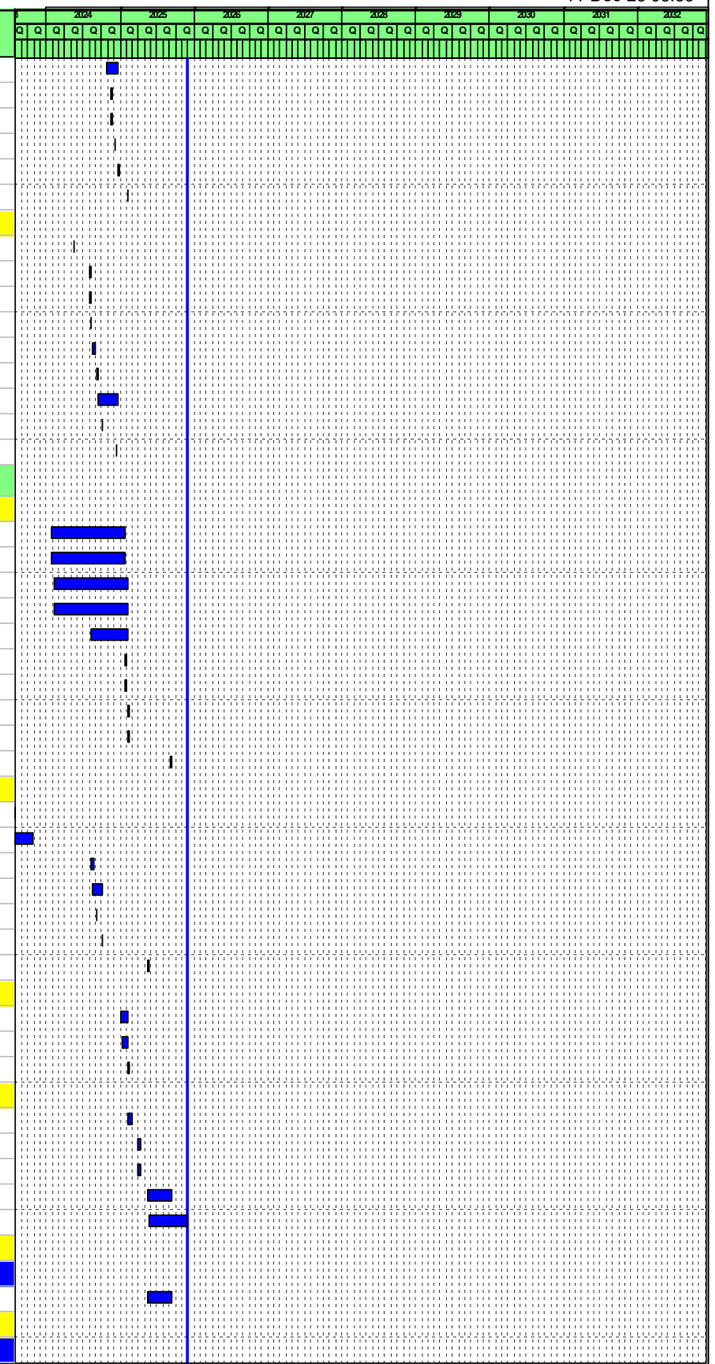


Remaining Level of Effort ◆ Milestone
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
CONS-EB-1630	Form/Rebar/Pour Concrete Footings	100%	100%	0	15-Apr-25 A	28-Aug-25 A	01-Nov-25		CONS-EB-1640, CONS-
BULL#04-35	Bulletin 4 Increased depth and size of footings	100%	100%	0	15-Apr-25 A	28-Aug-25 A	01-Nov-25		CONS-EB-1640
BULL#11-50	Bulletin # 11 Added 30 cy Concrete at footings, Columns & Walls	100%	100%	0	15-Apr-25 A	28-Aug-25 A	01-Nov-25		CONS-EB-1640, BULL#
CONS-EB-1635	Cure Concrete Footings	100%	100%	0	25-Apr-25 A	09-Sep-25 A	01-Nov-25		CONS-EB-1640, CONS-
WALLS			100%	0	25-Apr-25 A	08-Sep-25 A	01-Nov-25		
CONS-EB-1640	Form/Rebar/Pour Concrete Foundation Walls	100%	100%	0	25-Apr-25 A	28-Aug-25 A	01-Nov-25		CONS-EB-1650, CONS-
CONS-EB-1645	Cure Concrete Foundation Walls	100%	100%	0	01-May-25 A	08-Sep-25 A	01-Nov-25		CONS-EB-1660
BULL#04-45	Bulletin 4 Wall and Column amendments	100%	100%	0	01-May-25 A	28-Aug-25 A	01-Nov-25		CONS-EB-1650
BEAMS			100%	0	15-Apr-25 A	11-Sep-25 A	01-Nov-25		
CONS-EB-1650	Form/Rebar/Pour Grade Beams	100%	100%	0	15-Apr-25 A	25-Jul-25 A	01-Nov-25		CONS-EB-1660, CONS-
CONS-EB-6500	Cure Concrete Grade Beams	100%	100%	0	25-Apr-25 A	25-Jul-25 A	01-Nov-25		CONS-EB-1660, CONS-
CONS-EB-6510	Backfill area to allow pouring of slab on grade	100%	100%	0	28-Jul-25 A	11-Sep-25 A	01-Nov-25		CONS-EB-1660, CONS-
SLAB			100%	0	04-Aug-25 A	17-Sep-25 A	01-Nov-25		
CONS-EB-1660	Form/Rebar/PourSlab on Grade	100%	100%	0	04-Aug-25 A	12-Sep-25 A	01-Nov-25		CONS-EB-1900, CONS-
CONS-EB-1900	Cure Slab	100%	100%	0	14-Aug-25 A	17-Sep-25 A	01-Nov-25		CONS-EB-1150, CONS-
SUPERSTRUCTURE			41.74%	141	07-May-24 A	15-Jun-26	28-Jul-26	69	
SHEAR WALLS			100%	0	07-May-24 A	08-Sep-25 A	01-Nov-25		
CONS-EB-5900	Install Shear Walls Ground Floor	100%	100%	0	07-May-24 A	27-Aug-25 A	01-Nov-25		CONS-EB-5910, CONS-
CONS-EB-5890	Form Shear Walls Ground Floor	100%	100%	0	30-Apr-25 A	27-Aug-25 A	01-Nov-25		CONS-EB-5900
CONS-EB-5910	Pour Shear Walls Ground Floor	100%	100%	0	09-May-25 A	28-Aug-25 A	01-Nov-25		CONS-EB-5920, CONS-
CONS-EB-5920	Cure Shear Walls Ground Floor	100%	100%	0	10-May-25 A	08-Sep-25 A	01-Nov-25		CONS-EB-1730, CONS-
CONS-EB-5930	Strip Shear Walls Ground Floor	100%	100%	0	12-May-25 A	02-Sep-25 A	01-Nov-25		CONS-EB-1150, CONS-
COLUMNS			100%	0	29-Apr-25 A	24-Sep-25 A	01-Nov-25		
CONS-EB-1690	Form Concrete Columns Ground Floor	100%	100%	0	29-Apr-25 A	03-Sep-25 A	01-Nov-25		CONS-EB-1700, CONS-
CONS-EB-1700	Install Rebar Columns Ground Floor	100%	100%	0	01-May-25 A	03-Sep-25 A	01-Nov-25		CONS-EB-1710, CONS-
BULL#11-60	Bulletin # 11 Form/Rebar/Pour Additional 80CY Walls and Columns	100%	100%	0	05-May-25 A	04-Sep-25 A	01-Nov-25		CONS-EB-1660, CONS-
CONS-EB-1710	Pour Columns Ground Floor	100%	100%	0	09-May-25 A	04-Sep-25 A	01-Nov-25		CONS-EB-1720, CONS-
CONS-EB-1720	Cure Columns Ground Floor	100%	100%	0	09-May-25 A	24-Sep-25 A	01-Nov-25		CONS-EB-1730, CONS-
CONS-EB-1740	Strip Columns Ground Floor	100%	100%	0	12-May-25 A	15-Sep-25 A	01-Nov-25		CONS-EB-1150, CONS-
CMU			50.55%	45	25-Sep-25 A	06-Feb-26	29-Dec-25	128	
CONS-EB-1180	Install Form/Rebar for Concrete Stair 3	100%	100%	0	25-Sep-25 A	02-Oct-25 A	01-Nov-25		CONS-EB-1400, CONS-
CONS-EB-6490	Pour Concrete Stair 3	100%	100%	0	03-Oct-25 A	06-Oct-25 A	01-Nov-25		CONS-EB-1400
CONS-EB-1150	Install CMU, 1st Floor Column Line A-J & 1 to 17	20%	0%	25	30-Oct-25 A	07-Jan-26	27-Nov-25	0	CONS-EB-1190, CONS-
CONS-EB-1155	Install CMU, 1st Floor Column Line J to W & 1 to 17	0%	0%	20	08-Jan-26	06-Feb-26	29-Dec-25	0	CONS-EB-1190, CONS-
GROUND LEVEL TO 2ND FLOOR			58.49%	66	16-Sep-25 A	11-May-26	12-Mar-26	75	
SLAB			100%	0	16-Sep-25 A	16-Oct-25 A	01-Nov-25		
CONS-EB-1730	Form/Rebar/Pour Second Floor Concrete Slab	100%	100%	0	16-Sep-25 A	06-Oct-25 A	01-Nov-25		CONS-EB-1110, CONS-
CONS-EB-1110	Install Floor Drains, 2nd floor	100%	100%	0	01-Oct-25 A	03-Oct-25 A	01-Nov-25		CONS-EB-1760
CONS-EB-1850	Cure Slab	100%	100%	0	06-Oct-25 A	16-Oct-25 A	01-Nov-25		CONS-EB-1770, CONS-
SHEAR WALLS			100%	0	08-Oct-25 A	28-Oct-25 A	03-Nov-25		
CONS-EB-5940	Form Shear Walls 2nd Floor (added 2 days due to bulletin # 6)	100%	100%	0	08-Oct-25 A	21-Oct-25 A	01-Nov-25		CONS-EB-5950
CONS-EB-5950	Install Shear Walls 2nd Floor (added 2 days due to bulletin # 6)	100%	100%	0	10-Oct-25 A	22-Oct-25 A	03-Nov-25		CONS-EB-5960
CONS-EB-5960	Pour Shear Walls 2nd Floor	100%	100%	0	10-Oct-25 A	22-Oct-25 A	03-Nov-25		CONS-EB-5970
CONS-EB-5970	Cure Shear Walls 2nd Floor	100%	100%	0	23-Oct-25 A	28-Oct-25 A	03-Nov-25		CONS-EB-5980
CONS-EB-5980	Strip Shear Walls 2nd Floor	100%	100%	0	23-Oct-25 A	23-Oct-25 A	03-Nov-25		CONS-EB-1760
COLUMNS			100%	0	08-Oct-25 A	31-Oct-25 A	01-Nov-25		
CONS-EB-1770	Form Concrete Columns 2nd Floor	100%	100%	0	08-Oct-25 A	21-Oct-25 A	01-Nov-25		CONS-EB-1780
CONS-EB-1780	Install Rebar Columns 2nd Floor	100%	100%	0	10-Oct-25 A	22-Oct-25 A	01-Nov-25		CONS-EB-1790
CONS-EB-1790	Pour Columns 2nd Floor	100%	100%	0	10-Oct-25 A	22-Oct-25 A	01-Nov-25		CONS-EB-1800
CONS-EB-1800	Cure Columns 2nd Floor	100%	100%	0	23-Oct-25 A	31-Oct-25 A	01-Nov-25		CONS-EB-1810
CONS-EB-1810	Strip Columns 2nd Floor	100%	100%	0	23-Oct-25 A	23-Oct-25 A	01-Nov-25		CONS-EB-1760, CONS-

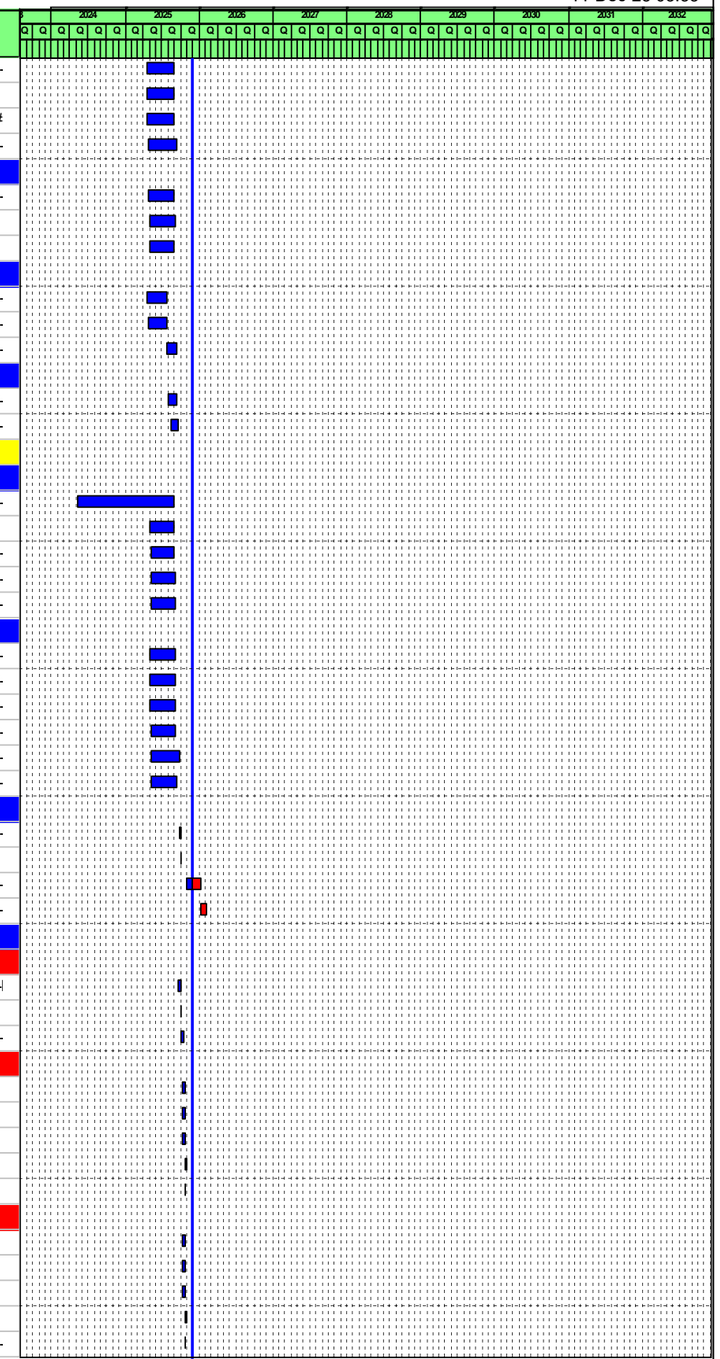


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
CMU			0%	63	09-Feb-26	11-May-26	12-Mar-26	70	
CONS-EB-6100	Install CMU, 2nd Floor Column Line A-J & 1 to 17	0%	0%	20	09-Feb-26	09-Mar-26	01-Dec-25	0	CONS-EB-1400, CONS-
CONS-EB-6280	Install CMU, 2nd Floor Column Line J to W & 1 to 17	0%	0%	20	10-Mar-26	08-Apr-26	31-Dec-25	0	CONS-EB-1400, CONS-
BULL#05-35	Install additional CMU ATS Room	0%	0%	3	07-May-26	11-May-26	12-Mar-26	70	CONS-EB-6555
2ND FLOOR TO ROOF			0%	141	30-Oct-25 A	15-Jun-26	28-Jul-26	69	
ROOFING			0%	141	30-Oct-25 A	15-Jun-26	28-Jul-26	69	
CONS-EB-1760	Form/Rebar/PourConcrete Roof Slab	100%	100%	0	30-Oct-25 A	18-Nov-25 A	13-Nov-25		CONS-EB-1130, CONS-
CONS-EB-1130	Install Roof Drains	100%	100%	0	17-Nov-25 A	17-Nov-25 A	28-Nov-25		SITE-1110
CONS-EB-6261	Architect Issues Sketch SK038 for Generator Rooftop Dunnage Steel	100%	100%	0	20-Nov-25 A	20-Nov-25 A			CONS-EB-6262
CONS-EB-6262	Submit Cost Proposal per Sketch SK038 for Generator Rooftop Dunnage Steel	100%	100%	0	21-Nov-25 A	25-Nov-25 A			CONS-EB-6263, CONS-
CONS-EB-6264	Submit Shop Drawings per Sketch SK038 for Generator Rooftop Dunnage Steel	100%	100%	0	21-Nov-25 A	25-Nov-25 A			CONS-EB-6265
CONS-EB-6263	DDC Negotiates C/O per Sketch SK038 for Generator Rooftop Dunnage Steel	0%	0%	10	26-Nov-25 A	12-Dec-25		60	CONS-EB-6610
CONS-EB-6265	Approve Shop Drawings per Sketch SK038 for Generator Rooftop Dunnage Steel	0%	0%	10	26-Nov-25 A	12-Dec-25		60	CONS-EB-6610
CONS-EB-1220	Install Solartubes	0%	0%	10	01-Dec-25	12-Dec-25	28-Nov-25	75	CONS-EB-1250, CONS-
CONS-EB-6610	Fabricate per Sketch SK038 for Generator Rooftop Dunnage Steel	0%	0%	10	16-Dec-25	30-Dec-25		60	CONS-EB-6270, CONS-
CONS-EB-6270	Install Rooftop Dunnage Steel	0%	0%	3	31-Dec-25	05-Jan-26	18-Nov-25	117	CONS-EB-1320, BULL#
CONS-EB-6410	Install Lighting protection system	0%	0%	15	31-Dec-25	22-Jan-26	23-Dec-25	127	CONS-EB-6315
CONS-EB-6620	Build Knee Wall at Rooftop Dunnage Steel	0%	0%	5	31-Dec-25	07-Jan-26		60	CONS-EB-1250
CONS-EB-1250	Install Main Roofing	0%	0%	18	16-Mar-26	08-Apr-26	29-Dec-25	18	CONS-EB-1320, CONS-
CONS-EB-6600	Install Skylight at Training 238	0%	0%	10	27-Mar-26	13-Apr-26	13-Apr-26	37	BULL#07-55, BULL#07-
CONS-EB-1320	Rig Rooftop Units and Generator	0%	0%	3	13-Apr-26	15-Apr-26	20-Feb-26	53	CONS-INSP-1005, CON
CONS-EB-6440	Install Rooftop Units Mechanical Connections	0%	0%	15	16-Apr-26	06-May-26	16-Mar-26	53	CONS-EB-6420, CONS-
CONS-EB-1510	Install Gutters and Rainchains	0%	0%	5	06-May-26	12-May-26	21-Jul-26	81	CONS-EB-1820
CONS-EB-6420	Install Rooftop Units Electrical Connections	0%	0%	15	07-May-26	29-May-26	06-Apr-26	53	CONS-EB-6430
CONS-EB-6555	ATS/Generator load bank testing	0%	0%	5	12-May-26	19-May-26	23-Mar-26	70	CONS-INSP-1010, CON
CONS-EB-1820	Install Roof Railings	0%	0%	5	14-May-26	20-May-26	28-Jul-26	81	CONS-CLOS-1000
CONS-EB-6430	Test Rooftop Units	0%	0%	5	01-Jun-26	05-Jun-26	21-Jul-26	53	CONS-TEST-1005, CON
CONS-EB-6550	Duct leakage testing	0%	0%	5	08-Jun-26	15-Jun-26	28-Jul-26	53	CONS-TEST-1005
BULKHEAD			3.06%	95	19-Nov-25 A	10-Apr-26	31-Dec-25	18	
CONS-EB-6640	Form, Rebar, Pour Bulkhead Walls and Columns	100%	100%	0	19-Nov-25 A	26-Nov-25 A			CONS-EB-6645
CONS-EB-6645	Form, Rebar, Pour Bulkhead Roof Slab	0%	0%	5	01-Dec-25	05-Dec-25		69	CONS-EB-6650, CONS-
CONS-EB-6650	Cure Bulkhead Concrete	0%	0%	7	06-Dec-25	12-Dec-25		108	CONS-EB-6655
CONS-EB-6655	Install Exterior CMU at Bulkhead	0%	0%	3	16-Dec-25	18-Dec-25		69	CONS-EB-6660
CONS-EB-6660	Install Interior CMU at Bulkhead	0%	0%	10	19-Dec-25	05-Jan-26		69	CONS-EB-6665
CONS-EB-6665	Install Exterior Brick at Bulkhead as Mockup	0%	0%	10	06-Jan-26	20-Jan-26		69	CONS-EB-1880
CONS-EB-6480	Install Bulkhead Roofing	0%	0%	2	09-Apr-26	10-Apr-26	31-Dec-25	18	CONS-EB-1320, CONS-
EXTERIOR ENCLOSURE			0%	156	17-Nov-25 A	22-Jul-26	20-Jul-26	39	
ELEVATION ESSEX STREET			0%	120	01-Dec-25	29-May-26	20-Jul-26	58	
CONS-EB-1230	Install Exterior relieving angles, mesh supports & artwork supports 1st Floor	0%	0%	8	01-Dec-25	10-Dec-25	26-Nov-25	37	CONS-EB-1240, CONS-
CONS-EB-5990	CMU Back Up Blocks Essex Street Elevation	0%	0%	15	11-Dec-25	05-Jan-26	18-Dec-25	37	CONS-EB-1350, CONS-
CONS-EB-6565	Install Cold Form Studs over windows Essex Street Elevation	0%	0%	5	19-Dec-25	26-Dec-25	23-Dec-25	37	CONS-EB-1240, CONS-
CONS-EB-6675	Install densglass/plywood sheathing Essex Street Elevation	0%	0%	5	29-Dec-25	05-Jan-26		49	CONS-EB-1240
CONS-EB-1240	Install Exterior Bricks Essex Street Elevation	0%	0%	15	06-Jan-26	27-Jan-26	15-Jan-26	49	CONS-EB-1350, CONS-
BULL#11-70	Bulletin # 11 Add 320 Exterior Brick to Essex Street Elevation	0%	0%	4	28-Jan-26	02-Feb-26	22-Jan-26	64	CONS-EB-1350
CONS-EB-1350	Install Windows and Storefronts Essex Street Elevation	0%	0%	5	20-Mar-26	26-Mar-26	01-Apr-26	34	CONS-EB-1840, CONS-
CONS-EB-6805	Install Metal framing for Exterior Stucco Soffits Essex Street Elevation	0%	0%	5	27-Mar-26	02-Apr-26		63	CONS-EB-6815, CONS-
CONS-EB-6815	Install Stucco for Exterior Stucco Soffits Essex Street Elevation	0%	0%	8	03-Apr-26	15-Apr-26		63	CONS-EB-6825, CONS-
CONS-EB-1400	Install Stairs 2 and 3 Exterior Essex Street Elevation	0%	0%	5	09-Apr-26	15-Apr-26	03-Jun-26	88	SITE-1120
CONS-EB-6825	Washdown Brick Essex Street Elevation	0%	0%	5	16-Apr-26	22-Apr-26		72	CONS-EB-6795
CONS-EB-1500	Install Exterior Architectural Mesh and Signage Essex Street Elevation	0%	0%	4	06-May-26	11-May-26	20-Jul-26	70	SITE-1120
CONS-EB-1390	Install Interior Storefronts and Glazing	0%	0%	5	22-May-26	29-May-26	15-Apr-26	7	CONS-EB-1860

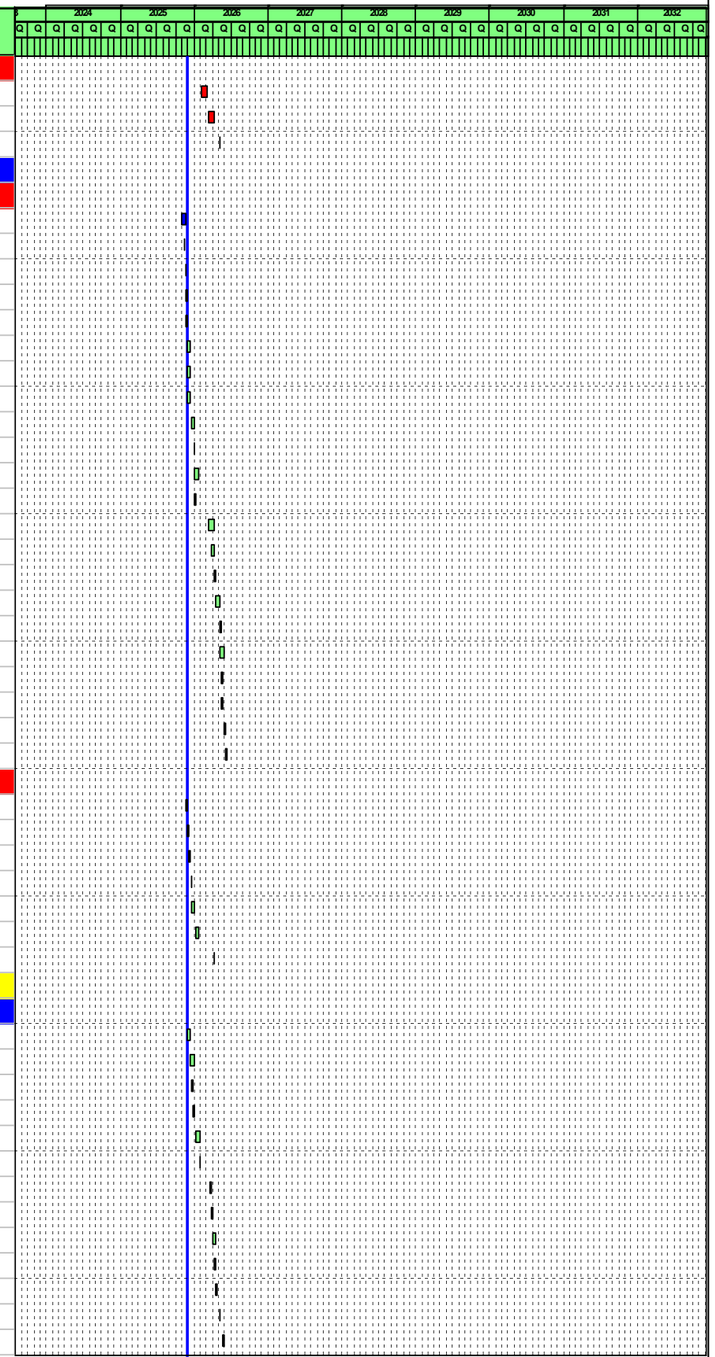


Remaining Level of Effort ◆ Milestone
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
ELEVATION LINDEN BLVD			0%	112	17-Nov-25 A	05-Jun-26	22-Apr-26	70	
CONS-EB-6000	CMU Back Up Block Linden Blvd Elevation	50%	50%	10	17-Nov-25 A	05-Jan-26	20-Jan-26	64	CONS-EB-6010, CONS-
CONS-EB-6575	Install Cold Form Studs over windows Linden Blvd Elevation	0%	0%	5	19-Dec-25	26-Dec-25	05-Jan-26	64	CONS-EB-1830, CONS-
CONS-EB-6685	Install densglass/plywood sheathing Linden Blvd Elevation	0%	0%	5	29-Dec-25	05-Jan-26		64	CONS-EB-1830
CONS-EB-1830	Install Exterior Bricks Linden Blvd Elevation	0%	0%	15	28-Jan-26	19-Feb-26	11-Feb-26	49	CONS-EB-1840, CONS-
CONS-EB-1840	Install Windows and Storefronts Linden Blvd Elevation	0%	0%	5	27-Mar-26	02-Apr-26	09-Apr-26	45	CONS-EB-1870, CONS-
CONS-EB-1870	Install Exterior Architectural Mesh and Signage Linden Blvd Elevation	0%	0%	5	03-Apr-26	10-Apr-26	16-Apr-26	108	CONS-CLOS-1000
CONS-EB-6775	Install Metal framing for Exterior Stucco Soffits Linden Blvd Elevation	0%	0%	5	03-Apr-26	10-Apr-26		66	CONS-EB-6785, CONS-
CONS-EB-6785	Install Stucco for Exterior Stucco Soffits Linden Blvd Elevation	0%	0%	8	16-Apr-26	27-Apr-26		63	CONS-EB-6795, CONS-
CONS-EB-6795	Washdown Brick Linden Blvd Elevation	0%	0%	5	28-Apr-26	04-May-26		69	CONS-EB-6765
CONS-EB-1860	Install Interior Storefronts and Glazing Linden Blvd Elevation	0%	0%	5	01-Jun-26	05-Jun-26	22-Apr-26	7	CONS-EB-1910
ELEVATION SHEEPHERD AVE			0%	135	17-Nov-25 A	09-Jul-26	29-Apr-26	47	
CONS-EB-6010	Install CMU Back Up Blocks Shepherd Avenue Elevation	67%	67%	5	17-Nov-25 A	26-Dec-25	11-Feb-26	77	CONS-EB-6020, CONS-
CONS-EB-6585	Install Cold Form Studs over windows Shepherd Avenue Elevation	0%	0%	5	19-Dec-25	26-Dec-25	03-Feb-26	79	CONS-EB-2190, CONS-
CONS-EB-6695	Install densglass/plywood sheathing Shepherd Avenue Elevation	0%	0%	5	29-Dec-25	05-Jan-26		79	CONS-EB-1880
CONS-EB-1880	Install Exterior Bricks Shepherd Avenue Elevation	0%	0%	15	20-Feb-26	13-Mar-26	26-Feb-26	49	CONS-EB-1890, CONS-
CONS-EB-1890	Install Windows and Storefronts Shepherd Avenue Elevation	0%	0%	5	23-Mar-26	27-Mar-26	13-Mar-26	54	CONS-EB-1920, CONS-
CONS-EB-1920	Install Exterior Architectural Mesh and Signage Shepherd Avenue Elevation	0%	0%	5	30-Mar-26	03-Apr-26	20-Mar-26	112	CONS-CLOS-1000
CONS-EB-1910	Install Interior Storefronts and Glazing Shepherd Avenue Elevation	0%	0%	5	08-Jun-26	15-Jun-26	29-Apr-26	7	CONS-EB-1960, CONS-
CONS-EB-6745	Install Metal framing for Exterior Stucco Soffits Shepherd Avenue Elevation	0%	0%	5	16-Jun-26	22-Jun-26		26	CONS-EB-6755, CONS-
CONS-EB-6755	Install Stucco for Exterior Stucco Soffits Shepherd Avenue Elevation	0%	0%	8	23-Jun-26	02-Jul-26		26	CONS-EB-6765, CONS-
CONS-EB-6765	Washdown Brick Shepherd Avenue Elevation	0%	0%	5	03-Jul-26	09-Jul-26		29	CONS-EB-6735
ELEVATION PARKING LOT			0%	138	26-Dec-25	22-Jul-26	06-May-26	39	
CONS-EB-6020	Install CMU Back Up Blocks Parking Lot Elevation	0%	0%	15	26-Dec-25	20-Jan-26	05-Mar-26	77	CONS-EB-1930, SITE-1
CONS-EB-6705	Install densglass/plywood sheathing Parking Lot Elevation	0%	0%	5	29-Dec-25	05-Jan-26		94	CONS-EB-1930
CONS-EB-6595	Install Cold Form Studs over windows Parking Lot Elevation	0%	0%	5	05-Jan-26	12-Jan-26	26-Feb-26	77	CONS-EB-2190, CONS-
CONS-EB-1930	Install Exterior Bricks Parking Lot Elevation	0%	0%	15	16-Mar-26	03-Apr-26	20-Mar-26	49	CONS-EB-1940, CONS-
CONS-EB-6520	Blow test & acceptance of Windows & Storefronts of building	0%	0%	2	27-Mar-26	30-Mar-26	03-Apr-26	34	CONS-EB-2190, CONS-
CONS-EB-1940	Install Windows and Storefronts Parking Lot Elevation	0%	0%	5	06-Apr-26	13-Apr-26	27-Mar-26	49	CONS-EB-1970, CONS-
CONS-EB-1970	Install Exterior Architectural Mesh and Signage Parking Lot Elevation	0%	0%	5	14-Apr-26	20-Apr-26	03-Apr-26	102	CONS-CLOS-1000
CONS-EB-1960	Install Interior Storefronts and Glazing Parking Lot Elevation	0%	0%	5	16-Jun-26	22-Jun-26	06-May-26	7	CONS-EB-2250, CONS-
CONS-EB-6715	Install Metal framing for Exterior Stucco Soffits Parking Lot Elevation	0%	0%	5	23-Jun-26	29-Jun-26		29	CONS-EB-6725
CONS-EB-6725	Install Stucco for Exterior Stucco Soffits Parking Lot Elevation	0%	0%	8	03-Jul-26	15-Jul-26		26	CONS-EB-6735
CONS-EB-6735	Washdown Brick Parking Lot Elevation	0%	0%	5	16-Jul-26	22-Jul-26		26	CONS-INSP-1005
PERGOLA WORK			61.08%	101	09-Jul-25 A	29-Jun-26	27-May-26	44	
BULL#12-40	Change CMU to Poured Wall Add'l 5 days per Bulletin # 12 work for Pergola Footings	100%	100%	0	09-Jul-25 A	15-Jul-25 A	01-Nov-25		CONS-EB-1190
CONS-EB-1090	Install Pergola Footings	100%	100%	0	11-Jul-25 A	21-Jul-25 A	01-Nov-25		CONS-EB-1150, CONS-
BULL#12-30	Install WF4 to WF3 Ad"l 2 days per Bulletin # 12 work for Pergola Footings	100%	100%	0	16-Jul-25 A	17-Jul-25 A	01-Nov-25		CONS-EB-1090, BULL#
BULL#12-35	Install Additional column depth 2 days per Bulletin # 12 work for Pergola Footings	100%	100%	0	22-Jul-25 A	23-Jul-25 A	01-Nov-25		CONS-EB-1090
CONS-EB-1190	Install Pergola and Canopy Steel	0%	0%	17	09-Feb-26	04-Mar-26	26-Feb-26	88	CONS-EB-1400, CONS-
CONS-EB-1195	Install Pergola Deck & Pour Stops	0%	0%	5	05-Mar-26	12-Mar-26	05-Mar-26	90	CONS-EB-1197
CONS-EB-1197	Install Rebar & Pour slab on Deck 2nd Floor	0%	0%	5	13-Mar-26	19-Mar-26	13-Mar-26	90	CONS-EB-1199
CONS-EB-1199	Install Pergola Polycarbonate Roof	0%	0%	5	20-Mar-26	26-Mar-26	20-Mar-26	95	CONS-EB-2020
CONS-EB-2020	Install PV Panel System at Pergola Roof	0%	0%	12	08-Jun-26	24-Jun-26	27-May-26	42	CONS-INSP-1005, ML2
CONS-EB-6630	Test PV Panel System at Pergola Roof	0%	0%	3	25-Jun-26	29-Jun-26		42	CONS-INSP-1005, ML2
INTERIOR WORK			0%	173	30-Oct-25 A	17-Aug-26	31-Jul-26	23	
1ST FLOOR			0%	166	30-Oct-25 A	05-Aug-26	31-Jul-26	29	
CONS-EB-1140	Install Overhead Plumbing Pipe, 1st Floor	10%	10%	18	30-Oct-25 A	26-Dec-25	01-Dec-25	58	CONS-EB-1170, CONS-
CONS-EB-1170	Install Plumbing Piping in Walls 1st Floor	40%	40%	6	30-Oct-25 A	26-Dec-25	01-Dec-25	58	CONS-EB-2190, PRO-1
CONS-EB-6210	Install Overhead Electrical, 1st Floor	20%	20%	16	03-Nov-25 A	22-Jan-26	17-Feb-26	46	CONS-EB-2190, CONS-
CONS-EB-6220	Install Electrical Rough-in in Walls 1st Floor	20%	20%	8	03-Nov-25 A	02-Mar-26	17-Feb-26	37	CONS-EB-2190, PRO-1

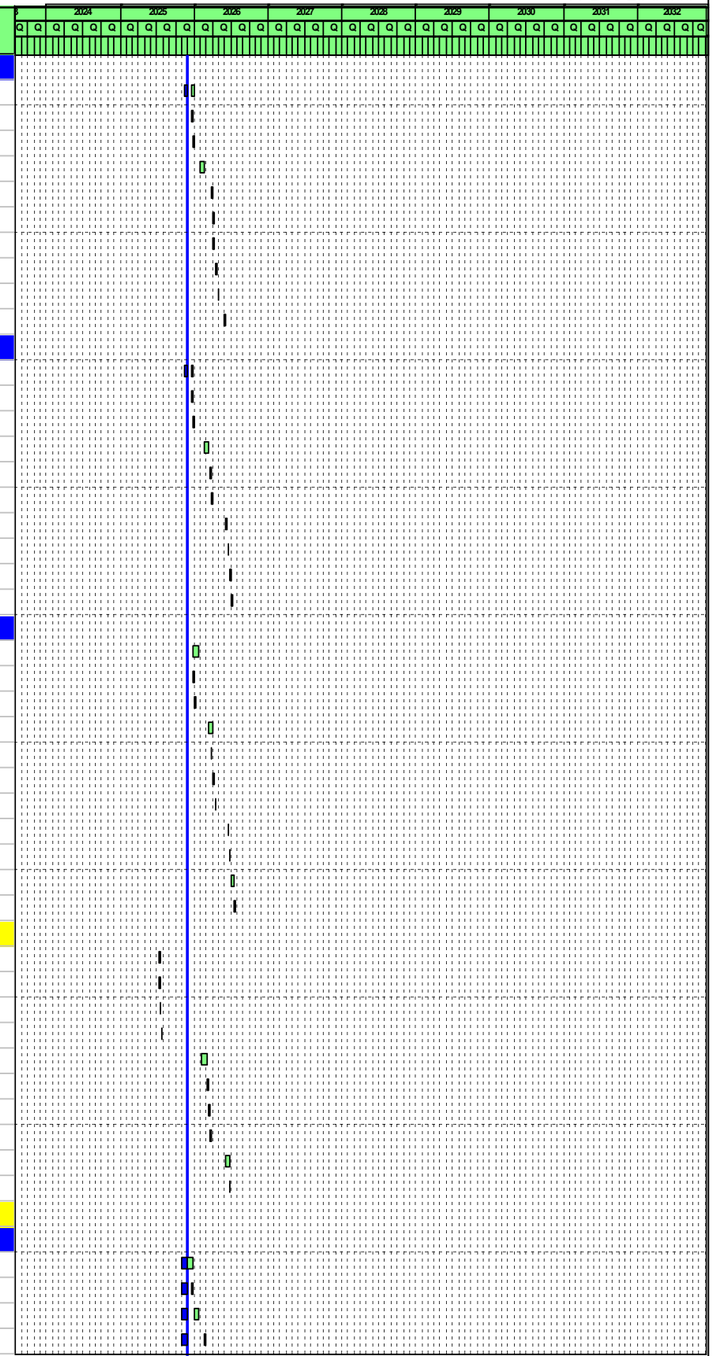

Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
CONS-EB-6130	Install Overhead Sprinkler Pipe, 1st Floor	0%	0%	20	02-Jan-26	02-Feb-26	05-Jan-26	64	CONS-EB-2190, CONS-
CONS-EB-6540	Leak test & insulate Plumbing piping walls 1st Floor	0%	0%	5	27-Jan-26	02-Feb-26	05-Jan-26	39	CONS-EB-2190, BULL#
CONS-EB-1160	Install Walls Framing and Door Frames, 1st Floor	0%	0%	15	09-Feb-26	02-Mar-26	21-Jan-26	25	CONS-EB-2300, CONS-
CONS-EB-6140	Install Sprinkler Piping thru Walls, 1st Floor	0%	0%	10	09-Feb-26	23-Feb-26	13-Jan-26	50	CONS-EB-2190, PRO-1·
CONS-EB-6230	Install Overhead Mechanical, 1st Floor	0%	0%	20	17-Feb-26	17-Mar-26	15-Jan-26	35	CONS-EB-6240, CONS-
CONS-EB-1310	Install Mechanical Unit Heaters System 1st Floor	0%	0%	15	03-Mar-26	24-Mar-26	12-Feb-26	25	CONS-INSP-1005, CON
CONS-EB-6240	Install Mechanical in Walls 1st Floor	0%	0%	10	03-Mar-26	17-Mar-26	15-Jan-26	35	CONS-EB-2190, PRO-1·
CONS-EB-1420	Install Polished Concrete Toppings 1st Floor	0%	0%	5	25-Mar-26	31-Mar-26	20-Feb-26	73	CONS-EB-1470
CONS-EB-2160	Spray Pryok ceilings 1st Floor	0%	0%	5	30-Apr-26	06-May-26	06-Mar-26	0	CONS-EB-2190, CONS-
BULL#05-30	Install additional CMU Bottle Fill Chase	0%	0%	5	30-Apr-26	06-May-26	06-Mar-26	0	CONS-EB-2190, BULL#
CONS-EB-2190	Install Gypsum Board wall and ceilings 1st Floor	0%	0%	10	07-May-26	21-May-26	08-Apr-26	0	CONS-EB-2210, CONS-
CONS-EB-2200	Install HM Doors and Door Hardware 1st Floor	0%	0%	10	22-May-26	05-Jun-26	22-Apr-26	7	CONS-EB-2240
CONS-EB-2290	Perform Tape & Spackle 1st floor	0%	0%	5	22-May-26	29-May-26	15-Apr-26	12	CONS-EB-2240, CONS-
CONS-EB-2300	Install Black Iron Grid	0%	0%	5	22-May-26	29-May-26	15-Apr-26	0	CONS-EB-2210
CONS-EB-2210	Install Acoustical Ceilings 1st Floor	0%	0%	5	01-Jun-26	05-Jun-26	22-Apr-26	0	CONS-EB-2240, CONS-
CONS-EB-2170	Install light fixtures and f/a devices 1st Floor	0%	0%	15	08-Jun-26	29-Jun-26	14-May-26	42	CONS-INSP-1005
CONS-EB-2220	Install Terrazzo and Epoxy Flooring 1st Floor	0%	0%	10	08-Jun-26	22-Jun-26	29-Apr-26	6	CONS-EB-2250, CONS-
CONS-EB-2230	Install Sprinkler Heads 1st Floor	0%	0%	7	08-Jun-26	17-Jun-26	01-May-26	0	CONS-EB-2240, CONS-
CONS-EB-1580	Install Fire Extinguishers and Signage 1st Floor	0%	0%	7	30-Jun-26	08-Jul-26	29-Jul-26	48	ML2000
CONS-EB-6040	Install Fire Alarm Devices and System 1st Floor	0%	0%	6	28-Jul-26	04-Aug-26	29-Jun-26	2	CONS-EB-6050, PRO-1·
CONS-EB-6050	Install Telecom Systems 1st Floor	0%	0%	7	28-Jul-26	05-Aug-26	30-Jun-26	16	CONS-INSP-1005, PRO
INTAKE/EXAM ROOMS			0%	6	18-Jun-26	25-Jun-26	12-May-26	57	
CONS-EB-2240	Interior Prime Paint Intake Rooms/Exam	0%	0%	1	18-Jun-26	18-Jun-26	04-May-26	0	CONS-EB-2250, CONS-
CONS-EB-2280	Install sheet vinyl flooring Intake Rooms/Exam	0%	0%	1	19-Jun-26	19-Jun-26	12-May-26	6	CONS-CLOS-1000, COI
CONS-EB-2260	Install Casework Intake Rooms/Exam	0%	0%	2	22-Jun-26	23-Jun-26	11-May-26	6	CONS-EB-2250
CONS-EB-2250	Install Interior Finish Paint Intake Rooms/Exam	0%	0%	1	24-Jun-26	24-Jun-26	07-May-26	6	CONS-EB-2270, CONS-
CONS-EB-2270	Install mechanical diffusersIntake Rooms/Exam	0%	0%	1	25-Jun-26	25-Jun-26	08-May-26	57	CONS-CLOS-1000
STORAGE ROOMS			0%	19	19-Jun-26	16-Jul-26	18-May-26	37	
CONS-EB-2370	Interior Prime Paint Storage Rooms	0%	0%	1	19-Jun-26	19-Jun-26	05-May-26	0	CONS-EB-2380, CONS-
CONS-EB-2410	Install sheet vinyl flooring Storage Rooms	0%	0%	1	22-Jun-26	22-Jun-26	12-May-26	6	CONS-CLOS-1000, COI
CONS-EB-2390	Install Casework Storage Rooms	0%	0%	2	23-Jun-26	24-Jun-26	11-May-26	6	CONS-EB-2380
CONS-EB-2380	Install Interior Finish Paint Storage Rooms	0%	0%	1	25-Jun-26	25-Jun-26	07-May-26	6	CONS-EB-2400, CONS-
CONS-EB-2400	Install mechanical diffusers Storage Rooms	0%	0%	1	16-Jul-26	16-Jul-26	18-May-26	37	CONS-EB-2530
EUTHANASIA ROOM			0%	18	22-Jun-26	16-Jul-26	18-May-26	37	
CONS-EB-2500	Interior Prime Paint Euthanasia Room	0%	0%	1	22-Jun-26	22-Jun-26	06-May-26	0	CONS-EB-2510, CONS-
CONS-EB-2540	Install sheet vinyl flooring Euthanasia Room	0%	0%	1	23-Jun-26	23-Jun-26	12-May-26	5	CONS-CLOS-1000, COI
CONS-EB-2520	Install Casework Euthanasia Room	0%	0%	2	24-Jun-26	25-Jun-26	11-May-26	5	CONS-EB-2510
CONS-EB-2510	Install Interior Finish Paint Euthanasia Room	0%	0%	1	26-Jun-26	26-Jun-26	07-May-26	5	CONS-EB-2530, CONS-
CONS-EB-2530	Install mechanical diffusers Euthanasia Room	0%	0%	1	16-Jul-26	16-Jul-26	18-May-26	37	CONS-EB-2660
BEHAVIOR ROOM			0%	17	23-Jun-26	16-Jul-26	18-May-26	37	
CONS-EB-2630	Interior Prime Paint Behavior Room	0%	0%	1	23-Jun-26	23-Jun-26	07-May-26	0	CONS-EB-2640, CONS-
CONS-EB-2670	Install sheet vinyl flooring Behavior Room	0%	0%	1	24-Jun-26	24-Jun-26	14-May-26	5	CONS-CLOS-1000, COI
CONS-EB-2650	Install Casework Behavior Room	0%	0%	2	25-Jun-26	26-Jun-26	12-May-26	5	CONS-EB-2640
CONS-EB-2640	Install Interior Finish Paint Behavior Room	0%	0%	1	29-Jun-26	29-Jun-26	08-May-26	5	CONS-EB-2660, CONS-
CONS-EB-2660	Install mechanical diffusers Behavior Room	0%	0%	1	16-Jul-26	16-Jul-26	18-May-26	37	CONS-EB-2790
CAT INTAKE			0%	16	24-Jun-26	16-Jul-26	18-May-26	37	
CONS-EB-2760	Interior Prime Paint Cat Intake	0%	0%	1	24-Jun-26	24-Jun-26	08-May-26	0	CONS-EB-2770, CONS-
CONS-EB-2770	Install Interior Finish Paint Cat Intake	0%	0%	1	30-Jun-26	30-Jun-26	11-May-26	5	CONS-EB-2780, CONS-
CONS-EB-2780	Install Casework Cat Intake	0%	0%	2	01-Jul-26	02-Jul-26	14-May-26	5	CONS-EB-2800
CONS-EB-2800	Install sheet vinyl flooring Cat Intake	0%	0%	1	03-Jul-26	03-Jul-26	15-May-26	5	CONS-EB-2930
CONS-EB-2790	Install mechanical diffusers Cat Intake	0%	0%	1	16-Jul-26	16-Jul-26	18-May-26	37	CONS-EB-2920

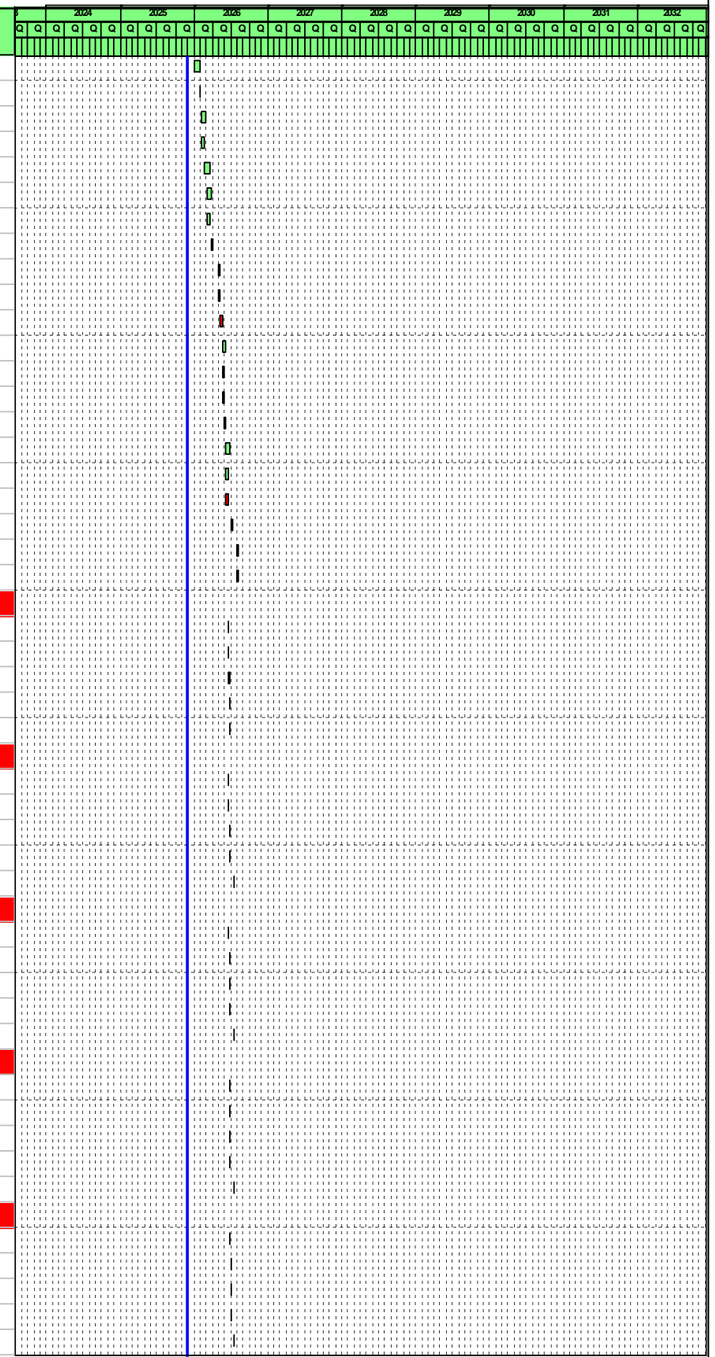


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
ADMISSIONS			0%	16	25-Jun-26	17-Jul-26	19-May-26	37	
CONS-EB-2890	Interior Prime Paint Admissions	0%	0%	1	25-Jun-26	25-Jun-26	11-May-26	0	CONS-EB-2900, CONS-
CONS-EB-2930	Install sheet vinyl flooring Admissions	0%	0%	1	06-Jul-26	06-Jul-26	18-May-26	5	CONS-CLOS-1000, COI
CONS-EB-2910	Install Casework Admissions	0%	0%	2	07-Jul-26	08-Jul-26	15-May-26	5	CONS-EB-2900
CONS-EB-2900	Install Interior Finish Paint Admissions	0%	0%	1	09-Jul-26	09-Jul-26	12-May-26	5	CONS-EB-2920, CONS-
CONS-EB-2920	Install mechanical diffusers Admissions	0%	0%	1	17-Jul-26	17-Jul-26	19-May-26	37	CONS-EB-1550
ADOPTIONS			0%	16	26-Jun-26	20-Jul-26	20-May-26	37	
CONS-EB-1450	Interior Prime Paint Adoptions	0%	0%	1	26-Jun-26	26-Jun-26	12-May-26	0	CONS-EB-1470, CONS-
CONS-EB-1570	Install sheet vinyl flooring Adoptions	0%	0%	1	29-Jun-26	29-Jun-26	19-May-26	11	CONS-EB-1580, CONS-
CONS-EB-1530	Install Casework Adoptions	0%	0%	2	30-Jun-26	01-Jul-26	18-May-26	11	CONS-EB-1470
CONS-EB-1470	Install Interior Finish Paint Adoptions	0%	0%	1	10-Jul-26	10-Jul-26	14-May-26	5	SITE-1110, CONS-EB-15
CONS-EB-1550	Install mechanical diffusers Adoptions	0%	0%	1	20-Jul-26	20-Jul-26	20-May-26	37	CONS-EB-3040, ML200
RECEPTION			0%	16	29-Jun-26	21-Jul-26	21-May-26	37	
CONS-EB-3010	Interior Prime Paint Reception	0%	0%	1	29-Jun-26	29-Jun-26	14-May-26	0	CONS-EB-3020, CONS-
CONS-EB-3050	Install sheet vinyl flooring Reception	0%	0%	1	30-Jun-26	30-Jun-26	20-May-26	11	CONS-CLOS-1000, COI
CONS-EB-3030	Install Casework Reception	0%	0%	2	01-Jul-26	02-Jul-26	19-May-26	11	CONS-EB-3020
CONS-EB-3020	Install Interior Finish Paint Reception	0%	0%	1	14-Jul-26	14-Jul-26	15-May-26	5	CONS-EB-3040, CONS-
CONS-EB-3040	Install mechanical diffusers Reception	0%	0%	1	21-Jul-26	21-Jul-26	21-May-26	37	CONS-EB-3160
WATER CLOSET/TOILETS			0%	15	01-Jun-26	22-Jun-26	06-May-26	47	
CONS-EB-6285	Install ceramic Tile Toilet 1st Floor	0%	0%	5	01-Jun-26	05-Jun-26	22-Apr-26	47	CONS-EB-6295
CONS-EB-6295	Install Plumbing Fixtures 1st Floor	0%	0%	5	08-Jun-26	15-Jun-26	29-Apr-26	47	CONS-CLOS-1000, COI
CONS-EB-6290	Install Partitions/Accessories/Trim 1st Floor	0%	0%	5	16-Jun-26	22-Jun-26	06-May-26	47	CONS-INSP-1005
ADMISSION COUNSELING			0%	16	30-Jun-26	22-Jul-26	22-May-26	37	
CONS-EB-3130	Interior Prime Paint Admission Counseling	0%	0%	1	30-Jun-26	30-Jun-26	15-May-26	0	CONS-EB-3140, CONS-
CONS-EB-3170	Install sheet vinyl flooring Admission Counseling	0%	0%	1	01-Jul-26	01-Jul-26	21-May-26	11	CONS-CLOS-1000, COI
CONS-EB-3150	Install Casework Admission Counseling	0%	0%	2	02-Jul-26	03-Jul-26	20-May-26	11	CONS-EB-3140
CONS-EB-3140	Install Interior Finish Paint Admission Counseling	0%	0%	1	15-Jul-26	15-Jul-26	18-May-26	5	CONS-EB-3160, CONS-
CONS-EB-3160	Install mechanical diffusers Admission Counseling	0%	0%	1	22-Jul-26	22-Jul-26	22-May-26	37	CONS-EB-3520
SERVER ROOM			0%	11	01-Jul-26	16-Jul-26	27-May-26	5	
CONS-EB-3250	Interior Prime Paint Server Room	0%	0%	1	01-Jul-26	01-Jul-26	18-May-26	0	CONS-EB-3260, CONS-
CONS-EB-3290	Install sheet vinyl flooring Server Room	0%	0%	1	02-Jul-26	02-Jul-26	20-May-26	8	CONS-CLOS-1000, COI
CONS-EB-3280	Install Racks Server Room	0%	0%	5	03-Jul-26	09-Jul-26	27-May-26	8	CONS-CLOS-1000, COI
CONS-EB-3260	Install Interior Finish Paint Server Room	0%	0%	1	16-Jul-26	16-Jul-26	19-May-26	5	CONS-EB-3380
FOOD PREP/KITCHEN			0%	11	02-Jul-26	17-Jul-26	28-May-26	5	
CONS-EB-3370	Interior Prime Paint Kitchen	0%	0%	1	02-Jul-26	02-Jul-26	19-May-26	0	CONS-EB-3380, CONS-
CONS-EB-3410	Install sheet vinyl flooring Kitchen	0%	0%	1	03-Jul-26	03-Jul-26	26-May-26	8	CONS-CLOS-1000, COI
CONS-EB-3390	Install Casework Kitchen	0%	0%	2	06-Jul-26	07-Jul-26	22-May-26	11	CONS-EB-3380
CONS-EB-3400	Install Sinks and Trim and Kitchen Equipment Kitchen	0%	0%	5	06-Jul-26	10-Jul-26	28-May-26	8	CONS-CLOS-1000, COI
CONS-EB-3380	Install Interior Finish Paint Kitchen	0%	0%	1	17-Jul-26	17-Jul-26	20-May-26	5	CONS-EB-3500
DOG SUPPORT			0%	14	03-Jul-26	23-Jul-26	27-May-26	37	
CONS-EB-3490	Interior Prime Paint Dog Support	0%	0%	1	03-Jul-26	03-Jul-26	20-May-26	0	CONS-EB-3500, CONS-
CONS-EB-3530	Install sheet vinyl flooring Dog Support	0%	0%	1	06-Jul-26	06-Jul-26	27-May-26	7	CONS-EB-3650, CONS-
CONS-EB-3510	Install Casework Dog Support	0%	0%	2	07-Jul-26	08-Jul-26	26-May-26	11	CONS-EB-3500
CONS-EB-3500	Install Interior Finish Paint Dog Support	0%	0%	1	20-Jul-26	20-Jul-26	21-May-26	5	CONS-EB-3520, CONS-
CONS-EB-3520	Install mechanical diffusers Dog Support	0%	0%	1	23-Jul-26	23-Jul-26	26-May-26	37	CONS-EB-2130
OXYGEN ROOM			0%	16	06-Jul-26	28-Jul-26	01-Jun-26	35	
CONS-EB-3610	Interior Prime Paint Oxygen Room	0%	0%	1	06-Jul-26	06-Jul-26	21-May-26	0	CONS-EB-3620, CONS-
CONS-EB-3650	Install sheet vinyl flooring Oxygen Room	0%	0%	1	07-Jul-26	07-Jul-26	28-May-26	7	CONS-CLOS-1000, COI
CONS-EB-3630	Install Casework Oxygen Room	0%	0%	2	08-Jul-26	09-Jul-26	27-May-26	7	CONS-EB-2120, CONS-
CONS-EB-3620	Install Interior Finish Paint Oxygen Room	0%	0%	1	21-Jul-26	21-Jul-26	22-May-26	5	CONS-EB-3640, CONS-
CONS-EB-3640	Install Oxygen Equipment Oxygen Room	0%	0%	5	22-Jul-26	28-Jul-26	01-Jun-26	35	CONS-CLOS-1000

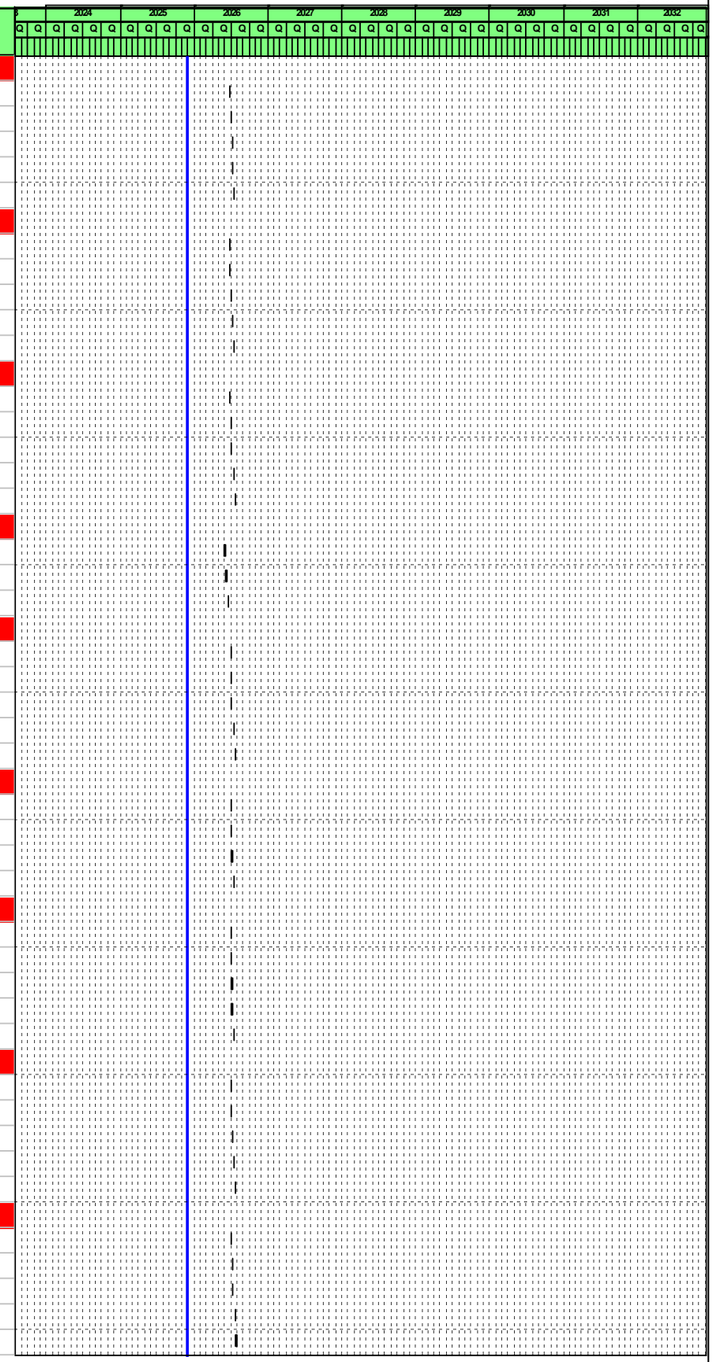


Remaining Level of Effort ◆ Milestone
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
SHOWERS			0%	15	01-Jun-26	22-Jun-26	06-May-26	47	
CONS-EB-1385	Install showers Base	0%	0%	5	01-Jun-26	05-Jun-26	22-Apr-26	47	CONS-EB-1375
CONS-EB-1375	Install ceramic Tile Shower	0%	0%	5	08-Jun-26	15-Jun-26	29-Apr-26	47	CONS-CLOS-1000, COI
CONS-EB-1380	Install Plumbing Trim/Accessories/Partitions	0%	0%	5	16-Jun-26	22-Jun-26	06-May-26	47	CONS-INSP-1005
FIRE PUMP ROOM			0%	31	01-Jun-26	15-Jul-26	01-Jun-26	24	
CONS-EB-6350	Install Fire Pump Equipment	0%	0%	2	01-Jun-26	02-Jun-26	17-Apr-26	24	CONS-EB-6355
CONS-EB-6355	Install Fire Pump Piping	0%	0%	19	03-Jun-26	30-Jun-26	15-May-26	24	CONS-EB-6390, CONS-
CONS-EB-6390	Pull & Terminate /Meggar Test Electrical Cable	0%	0%	5	01-Jul-26	07-Jul-26	22-May-26	24	CONS-EB-6385
CONS-EB-6300	Connect Fire Water Service Pipe	0%	0%	5	01-Jul-26	07-Jul-26	22-May-26	24	CONS-EB-6385
CONS-EB-6385	Preliminary Test Fire Water Pump	0%	0%	5	08-Jul-26	15-Jul-26	01-Jun-26	24	CONS-STAR-1150
GAS METER ROOM			0%	21	01-Jun-26	30-Jun-26	16-Jun-26	41	
CONS-EB-6360	Install new Gas Meter and Service	0%	0%	5	01-Jun-26	05-Jun-26	22-Apr-26	41	CONS-EB-6375
CONS-EB-6375	Install Weld Gas Piping	0%	0%	10	08-Jun-26	22-Jun-26	06-May-26	41	CONS-EB-6400
CONS-EB-6400	X-ray & Pressure Test Gas Piping	0%	0%	5	23-Jun-26	29-Jun-26	14-May-26	41	CONS-EB-6310
CONS-EB-6310	Energize Gas Service	0%	0%	1	30-Jun-26	30-Jun-26	16-Jun-26	41	CONS-INSP-1005, CON
WATER SERVICE ROOM			0%	21	01-Jun-26	30-Jun-26	15-May-26	32	
CONS-EB-6370	Install new RPZ & Water Rig	0%	0%	5	01-Jun-26	05-Jun-26	22-Apr-26	32	CONS-EB-6340
CONS-EB-6340	Install Domestic Water Piping from RPZ to Feed tank	0%	0%	10	08-Jun-26	22-Jun-26	06-May-26	32	CONS-EB-6365, CONS-
CONS-EB-6365	Install New Make-up Water Tank	0%	0%	2	23-Jun-26	24-Jun-26	08-May-26	32	CONS-EB-6380
CONS-EB-6380	Leak Test Water Pipe & Insulate	0%	0%	1	25-Jun-26	25-Jun-26	11-May-26	32	CONS-EB-6305
CONS-EB-6305	Connect Water Service Pipe	0%	0%	3	26-Jun-26	30-Jun-26	15-May-26	32	CONS-INSP-1000
DOG KENNELS			0%	15	01-Jun-26	22-Jun-26	18-Jun-26	30	
CONS-EB-6325	Install Dog Kennels	0%	0%	15	01-Jun-26	22-Jun-26	18-Jun-26	30	CONS-EB-6335
DOG RUNS			0%	30	23-Jun-26	04-Aug-26	31-Jul-26	30	
CONS-EB-6335	Install Dog Runs Fences and Gates	0%	0%	15	23-Jun-26	14-Jul-26	09-Jul-26	30	CONS-EB-6330
CONS-EB-6330	Install Dog Run Turf	0%	0%	15	15-Jul-26	04-Aug-26	31-Jul-26	30	CONS-CLOS-1000
ELECTRICAL SERVICE ROOM			0%	69	23-Jan-26	05-May-26	14-Jul-26	63	
CONS-EB-6345	Install Electrical Switchboards/Panelboards in Electrical Service Room	0%	0%	5	23-Jan-26	29-Jan-26	09-Apr-26	46	CONS-EB-6320, SITE-1
CONS-EB-6320	Install Conduit in Electrical Service Room	0%	0%	15	30-Jan-26	23-Feb-26	30-Apr-26	92	CONS-EB-6395, CONS-
CONS-EB-6395	Pull & Terminate /Meggar Test Electrical Cable in Electrical Service Room	0%	0%	15	24-Feb-26	17-Mar-26	22-May-26	92	CONS-EB-6315
CONS-EB-6315	Inspection & Energize Electrical Service	0%	0%	5	29-Apr-26	05-May-26	14-Jul-26	63	CONS-TEST-1000, CON
2ND FLOOR			0%	173	01-Dec-25	17-Aug-26	01-Jul-26	23	
CONS-EB-1200	Install Mechanical Overhead, 2nd Floor North	0%	0%	13	01-Dec-25	18-Dec-25	03-Dec-25	43	CONS-EB-1201
CONS-EB-1260	Install Framing 2nd Floor	0%	0%	15	01-Dec-25	22-Dec-25	05-Dec-25	56	CONS-EB-2010, CONS-
CONS-EB-6150	Install Electrical Overhead, 2nd Floor North	0%	0%	13	01-Dec-25	18-Dec-25	03-Dec-25	31	CONS-EB-6151
CONS-EB-6160	Install Sprinkler Overhead, 2nd Floor North	0%	0%	13	01-Dec-25	18-Dec-25	03-Dec-25	31	CONS-EB-6161
CONS-EB-6170	Install Plumbing Overhead, 2nd Floor North	0%	0%	13	01-Dec-25	18-Dec-25	03-Dec-25	31	CONS-EB-6171
CONS-EB-6180	Install Electrical in walls , 2nd Floor	0%	0%	20	19-Dec-25	20-Jan-26	05-Jan-26	92	CONS-EB-2030
CONS-EB-1201	Install Mechanical Overhead, 2nd Floor South	0%	0%	12	19-Dec-25	07-Jan-26	22-Dec-25	43	CONS-EB-2010, CONS-
CONS-EB-6151	Install Electrical Overhead, 2nd Floor South	0%	0%	12	19-Dec-25	07-Jan-26	22-Dec-25	31	CONS-EB-2010, CONS-
CONS-EB-6161	Install Sprinkler Overhead, 2nd Floor South	0%	0%	12	19-Dec-25	07-Jan-26	22-Dec-25	31	CONS-EB-2010, CONS-
CONS-EB-6171	Install Plumbing Overhead, 2nd Floor South	0%	0%	12	19-Dec-25	07-Jan-26	22-Dec-25	31	CONS-EB-2010, PRO-1
CONS-EB-2000	Install Mechanical Unit Heaters System 2nd Floor	0%	0%	15	23-Dec-25	14-Jan-26	30-Dec-25	152	CONS-INSP-1005, CON
CONS-EB-6190	Install Sprinkler piping walls , 2nd Floor	0%	0%	20	29-Dec-25	27-Jan-26	12-Jan-26	87	CONS-EB-2030
CONS-EB-6200	Install Mechanical piping walls , 2nd Floor	0%	0%	20	29-Dec-25	27-Jan-26	12-Jan-26	87	CONS-EB-2030, PRO-1
CONS-EB-2010	Install Plumbing piping walls , 2nd Floor	0%	0%	20	08-Jan-26	06-Feb-26	22-Jan-26	31	CONS-EB-2030, CONS-
CONS-EB-1990	Install light fixtures and f/a devices 2nd Floor	0%	0%	15	30-Jan-26	23-Feb-26	07-May-26	95	CONS-EB-2080
CONS-EB-6530	Leak test & insulate Plumbing piping walls 2nd Floor	0%	0%	5	09-Feb-26	13-Feb-26	29-Jan-26	31	CONS-EB-2030, BULL#
CONS-EB-1980	Install Spray Pryok ceilings 2nd Floor	0%	0%	5	15-May-26	21-May-26	10-Feb-26	10	CONS-EB-2030, CONS-
CONS-EB-2030	Install Gypsum Board wall and ceilings 2nd Floor	0%	0%	10	22-May-26	05-Jun-26	27-Apr-26	10	CONS-EB-2050, CONS-
CONS-EB-2040	Install HM Doors and Door Hardware 2nd Floor	0%	0%	10	08-Jun-26	22-Jun-26	11-May-26	10	CONS-EB-2100

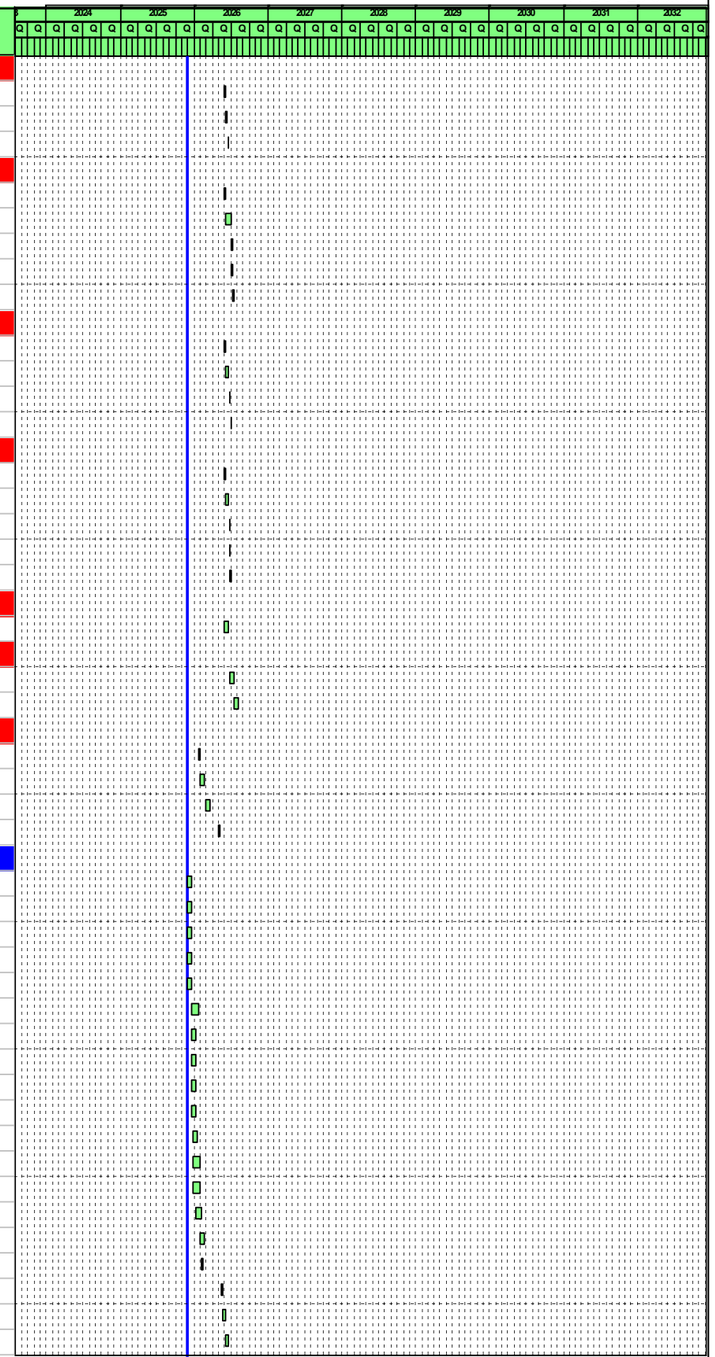


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
CONS-EB-2050	Install Acoustical Ceilings 2nd Floor	0%	0%	5	08-Jun-26	15-Jun-26	04-May-26	15	CONS-EB-2100, CONS-
CONS-EB-2060	Install Plumbing Fixtures 2nd Floor	0%	0%	7	08-Jun-26	17-Jun-26	06-May-26	50	CONS-INSP-1005
CONS-EB-2070	Install Polished Concrete Toppings 2nd Floor	0%	0%	5	16-Jun-26	22-Jun-26	11-May-26	25	CONS-EB-2110
CONS-EB-2080	Install Epoxy Resinous Flooring 2nd Floor	0%	0%	10	16-Jun-26	29-Jun-26	22-May-26	20	CONS-EB-2110
CONS-EB-2090	Install Sprinkler Heads 2nd Floor	0%	0%	5	16-Jun-26	22-Jun-26	11-May-26	35	ML2000, CONS-STAR-1
CONS-EB-2150	Install Fire Extinguishers and and Signage 2nd Floor	0%	0%	5	20-Jul-26	24-Jul-26	19-Jun-26	3	ML2000, CONS-EB-218
CONS-EB-2180	Install Fire Alarm Devices and System 2nd Floor	0%	0%	6	30-Jul-26	06-Aug-26	29-Jun-26	0	CONS-EB-2310, PRO-1
CONS-EB-2310	Install Telecom Systems 2nd Floor	0%	0%	8	30-Jul-26	10-Aug-26	01-Jul-26	13	CONS-INSP-1005, PRO
ADOPTION LOFTS			0%	15	07-Jul-26	28-Jul-26	12-Jun-26	35	
CONS-EB-2100	Interior Prime Paint Adoption Lofts	0%	0%	1	07-Jul-26	07-Jul-26	12-May-26	0	CONS-EB-2110, CONS-
CONS-EB-2140	Install sheet vinyl flooring Adoption Lofts	0%	0%	7	08-Jul-26	17-Jul-26	12-Jun-26	2	CONS-EB-2150, CONS-
CONS-EB-2120	Install Casework Adoption Lofts	0%	0%	5	20-Jul-26	24-Jul-26	02-Jun-26	2	CONS-EB-2130, CONS-
CONS-EB-2110	Install Interior Finish Paint Adoption Lofts	0%	0%	1	27-Jul-26	27-Jul-26	26-May-26	2	SITE-1110, CONS-EB-2
CONS-EB-2130	Install mechanical diffusers Adoption Lofts	0%	0%	1	28-Jul-26	28-Jul-26	27-May-26	35	ML2000
MEDICAL OFFICES			0%	6	08-Jul-26	16-Jul-26	20-May-26	37	
CONS-EB-4080	Interior Prime Paint Medical Offices	0%	0%	1	08-Jul-26	08-Jul-26	14-May-26	0	CONS-EB-4090, CONS-
CONS-EB-4120	Install sheet vinyl flooring Medical Offices	0%	0%	1	09-Jul-26	09-Jul-26	20-May-26	0	CONS-CLOS-1000, COI
CONS-EB-4100	Install Casework Medical Offices	0%	0%	2	10-Jul-26	14-Jul-26	19-May-26	0	CONS-EB-4090
CONS-EB-4090	Install Interior Finish Paint Medical Offices	0%	0%	1	15-Jul-26	15-Jul-26	15-May-26	0	CONS-EB-4110, CONS-
CONS-EB-4110	Install mechanical diffusers Medical Offices	0%	0%	1	16-Jul-26	16-Jul-26	18-May-26	37	CONS-EB-2400
CAT LOFTS 1 AND 2			0%	6	09-Jul-26	17-Jul-26	21-May-26	43	
CONS-EB-4190	Interior Prime Paint Cat Lofts	0%	0%	1	09-Jul-26	09-Jul-26	15-May-26	0	CONS-EB-4200, CONS-
CONS-EB-4230	Install sheet vinyl flooring Cat Lofts	0%	0%	1	10-Jul-26	10-Jul-26	21-May-26	0	CONS-CLOS-1000, COI
CONS-EB-4210	Install Casework Cat Lofts	0%	0%	2	14-Jul-26	15-Jul-26	20-May-26	0	CONS-EB-4200
CONS-EB-4200	Install Interior Finish Paint Cat Lofts	0%	0%	1	16-Jul-26	16-Jul-26	18-May-26	0	CONS-EB-4220, CONS-
CONS-EB-4220	Install mechanical diffusers Cat Lofts	0%	0%	1	17-Jul-26	17-Jul-26	19-May-26	43	CONS-CLOS-1000
WATER CLOSET/TOILETS			0%	15	08-Jun-26	29-Jun-26	19-May-26	42	
CONS-EB-6450	Install ceramic Tile Toilet 2nd Floor	0%	0%	5	08-Jun-26	15-Jun-26	04-May-26	42	CONS-EB-6460
CONS-EB-6460	Install Plumbing Fixtures 2nd Floor	0%	0%	5	16-Jun-26	22-Jun-26	11-May-26	42	CONS-CLOS-1000, COI
CONS-EB-6470	Install Partitions/Accessories/Trim 2nd Floor	0%	0%	5	23-Jun-26	29-Jun-26	19-May-26	42	CONS-INSP-1005
EXOTIC CAT SUPPORT ROOM			0%	6	10-Jul-26	20-Jul-26	22-May-26	42	
CONS-EB-4300	Interior Prime Paint Exotic Cat Support	0%	0%	1	10-Jul-26	10-Jul-26	18-May-26	0	CONS-EB-4310, CONS-
CONS-EB-4340	Install sheet vinyl flooring Exotic Cat Support	0%	0%	1	14-Jul-26	14-Jul-26	22-May-26	0	CONS-CLOS-1000, COI
CONS-EB-4320	Install Casework Exotic Cat Support	0%	0%	2	15-Jul-26	16-Jul-26	21-May-26	0	CONS-EB-4310
CONS-EB-4310	Install Interior Finish Paint Exotic Cat Support	0%	0%	1	17-Jul-26	17-Jul-26	19-May-26	0	CONS-EB-4330, CONS-
CONS-EB-4330	Install mechanical diffusers Exotic Cat Support	0%	0%	1	20-Jul-26	20-Jul-26	20-May-26	42	CONS-CLOS-1000
WARD ROOMS			0%	6	14-Jul-26	21-Jul-26	26-May-26	40	
CONS-EB-4410	Interior Prime Paint Ward Rooms	0%	0%	1	14-Jul-26	14-Jul-26	19-May-26	0	CONS-EB-4420, CONS-
CONS-EB-4450	Install sheet vinyl flooring Ward Rooms	0%	0%	1	15-Jul-26	15-Jul-26	26-May-26	0	CONS-CLOS-1000, COI
CONS-EB-4430	Install Casework Ward Rooms	0%	0%	2	16-Jul-26	17-Jul-26	22-May-26	0	CONS-EB-4420
CONS-EB-4420	Install Interior Finish Paint Ward Rooms	0%	0%	1	20-Jul-26	20-Jul-26	20-May-26	0	CONS-EB-4440, CONS-
CONS-EB-4440	Install mechanical diffusers Ward Rooms	0%	0%	1	21-Jul-26	21-Jul-26	21-May-26	40	CONS-CLOS-1000
TREATMENT ROOMS			0%	6	15-Jul-26	22-Jul-26	27-May-26	39	
CONS-EB-4520	Interior Prime Paint Treatment Rooms	0%	0%	1	15-Jul-26	15-Jul-26	20-May-26	0	CONS-EB-4530, CONS-
CONS-EB-4560	Install sheet vinyl flooring Treatment Rooms	0%	0%	1	16-Jul-26	16-Jul-26	27-May-26	0	CONS-CLOS-1000, COI
CONS-EB-4540	Install Casework Treatment Rooms	0%	0%	2	17-Jul-26	20-Jul-26	26-May-26	0	CONS-EB-4530
CONS-EB-4530	Install Interior Finish Paint Treatment Rooms	0%	0%	1	21-Jul-26	21-Jul-26	21-May-26	0	CONS-EB-4550, CONS-
CONS-EB-4550	Install mechanical diffusers Treatment Rooms	0%	0%	1	22-Jul-26	22-Jul-26	22-May-26	39	CONS-CLOS-1000
RECOVERY ROOMS			0%	10	16-Jul-26	29-Jul-26	03-Jun-26	34	
CONS-EB-4630	Interior Prime Paint Recovery Rooms	0%	0%	1	16-Jul-26	16-Jul-26	21-May-26	0	CONS-EB-4640, CONS-
CONS-EB-4670	Install sheet vinyl flooring Recovery Rooms	0%	0%	1	17-Jul-26	17-Jul-26	03-Jun-26	0	CONS-CLOS-1000, COI

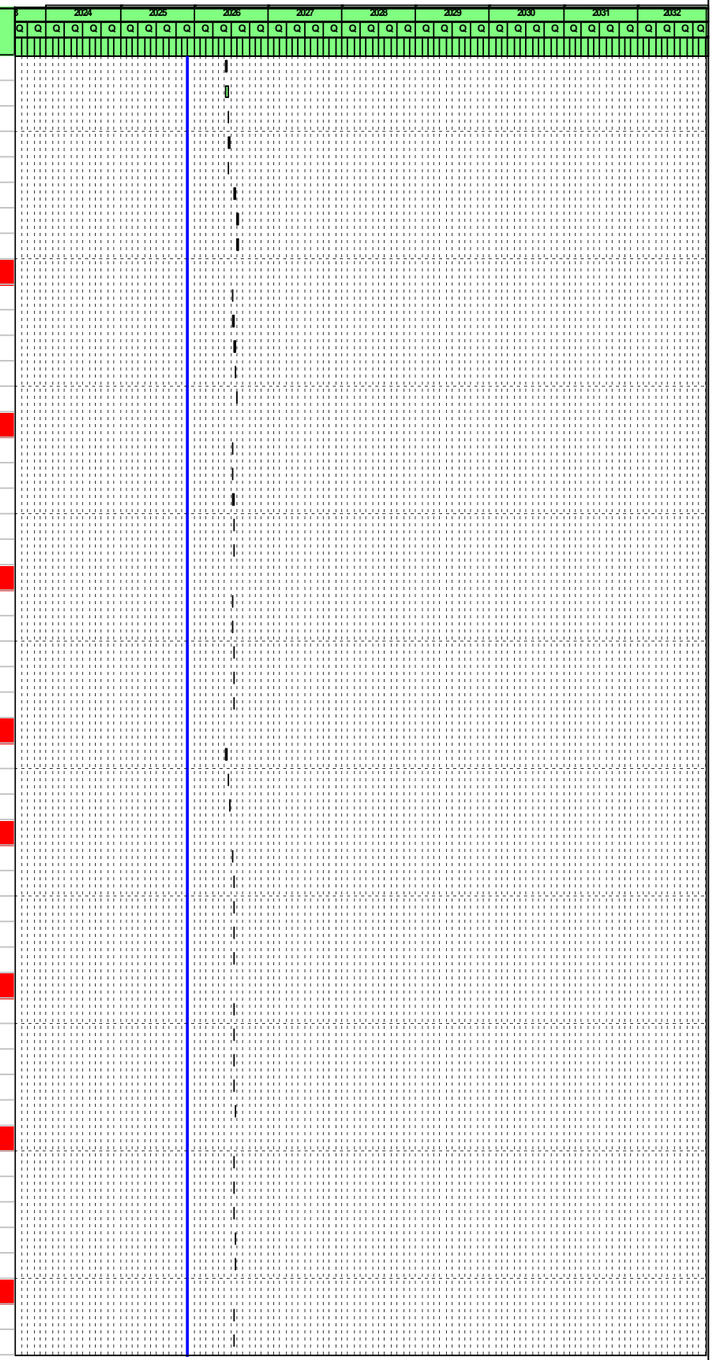


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
CONS-EB-4650	Install Casework Recovery Rooms	0%	0%	2	20-Jul-26	21-Jul-26	02-Jun-26	0	CONS-EB-4640
CONS-EB-4640	Install Interior Finish Recovery Rooms	0%	0%	5	22-Jul-26	28-Jul-26	29-May-26	0	CONS-EB-4660, CONS-
CONS-EB-4660	Install mechanical diffusers Recovery Rooms	0%	0%	1	29-Jul-26	29-Jul-26	01-Jun-26	34	CONS-CLOS-1000
LAUNDRY ROOM			0%	14	17-Jul-26	05-Aug-26	08-Jun-26	29	
CONS-EB-4740	Interior Prime Paint Laundry Room	0%	0%	1	17-Jul-26	17-Jul-26	22-May-26	4	CONS-EB-4750, CONS-
CONS-EB-4780	Install sheet vinyl flooring Laundry Room	0%	0%	1	20-Jul-26	20-Jul-26	04-Jun-26	4	CONS-CLOS-1000, COI
CONS-EB-4760	Install Casework Laundry Room	0%	0%	2	21-Jul-26	22-Jul-26	03-Jun-26	4	CONS-EB-4750
CONS-EB-4750	Install Interior Finish Paint Laundry Room	0%	0%	1	29-Jul-26	29-Jul-26	01-Jun-26	0	CONS-EB-4770, CONS-
CONS-EB-4770	Install Laundry Equipment Laundry Room	0%	0%	5	30-Jul-26	05-Aug-26	08-Jun-26	29	CONS-CLOS-1000
JANITOR ROOMS			0%	10	20-Jul-26	31-Jul-26	05-Jun-26	32	
CONS-EB-4850	Interior Prime Paint Janitor Rooms	0%	0%	1	20-Jul-26	20-Jul-26	26-May-26	26	CONS-EB-4860, CONS-
CONS-EB-4890	Install sheet vinyl flooring Janitor Rooms	0%	0%	1	21-Jul-26	21-Jul-26	05-Jun-26	26	CONS-CLOS-1000, COI
CONS-EB-4870	Install Casework Janitor Rooms	0%	0%	2	22-Jul-26	23-Jul-26	04-Jun-26	26	CONS-EB-4860
CONS-EB-4860	Install Interior Finish Paint Janitor Rooms	0%	0%	1	30-Jul-26	30-Jul-26	02-Jun-26	22	CONS-EB-4880, CONS-
CONS-EB-4880	Install mechanical diffusers Janitor Rooms	0%	0%	1	31-Jul-26	31-Jul-26	03-Jun-26	32	CONS-CLOS-1000
OFFICES			0%	10	21-Jul-26	03-Aug-26	08-Jun-26	31	
CONS-EB-4960	Interior Prime Paint Offices	0%	0%	1	21-Jul-26	21-Jul-26	27-May-26	26	CONS-EB-4970, CONS-
CONS-EB-5000	Install sheet vinyl flooring Offices	0%	0%	1	22-Jul-26	22-Jul-26	08-Jun-26	26	CONS-CLOS-1000, COI
CONS-EB-4980	Install Casework Offices	0%	0%	2	23-Jul-26	24-Jul-26	05-Jun-26	26	CONS-EB-4970
CONS-EB-4970	Install Interior Finish Paint Offices	0%	0%	1	31-Jul-26	31-Jul-26	03-Jun-26	22	CONS-EB-4990, CONS-
CONS-EB-4990	Install mechanical diffusers Offices	0%	0%	1	03-Aug-26	03-Aug-26	04-Jun-26	31	CONS-CLOS-1000
TRAINING ROOM			0%	10	22-Jul-26	04-Aug-26	09-Jun-26	30	
CONS-EB-5070	Interior Prime Paint Training Room	0%	0%	1	22-Jul-26	22-Jul-26	28-May-26	26	CONS-EB-5080, CONS-
CONS-EB-5110	Install sheet vinyl flooring Training Room	0%	0%	1	23-Jul-26	23-Jul-26	09-Jun-26	26	CONS-CLOS-1000, COI
CONS-EB-5090	Install Casework Training Room	0%	0%	2	24-Jul-26	27-Jul-26	08-Jun-26	26	CONS-EB-5080
CONS-EB-5080	Install Interior Finish Paint Training Room	0%	0%	1	03-Aug-26	03-Aug-26	04-Jun-26	22	CONS-EB-5100, CONS-
CONS-EB-5100	Install mechanical diffusers Training Room	0%	0%	1	04-Aug-26	04-Aug-26	05-Jun-26	30	CONS-CLOS-1000
CORRIDORS			0%	11	23-Jul-26	06-Aug-26	08-Jun-26	28	
CONS-EB-5180	Interior Prime Paint Corridors	0%	0%	1	23-Jul-26	23-Jul-26	29-May-26	26	CONS-EB-5190, CONS-
CONS-EB-5190	Install Interior Finish Paint Corridors	0%	0%	1	04-Aug-26	04-Aug-26	05-Jun-26	22	CONS-EB-5210, CONS-
CONS-EB-5220	Install sheet vinyl flooring Corridors	0%	0%	1	05-Aug-26	05-Aug-26	08-Jun-26	28	CONS-CLOS-1000, COI
CONS-EB-5210	Install mechanical diffusers Corridors	0%	0%	1	06-Aug-26	06-Aug-26	08-Jun-26	28	CONS-CLOS-1000
SERVER ROOM			0%	14	24-Jul-26	12-Aug-26	16-Jun-26	24	
CONS-EB-5290	Interior Prime Paint Server Room	0%	0%	1	24-Jul-26	24-Jul-26	01-Jun-26	26	CONS-EB-5300, CONS-
CONS-EB-5330	Install sheet vinyl flooring Server Room	0%	0%	1	27-Jul-26	27-Jul-26	12-Jun-26	26	CONS-CLOS-1000, COI
CONS-EB-5310	Install Casework Server Room	0%	0%	2	28-Jul-26	29-Jul-26	11-Jun-26	26	CONS-EB-5300
CONS-EB-5300	Install Interior Finish Paint Server Room	0%	0%	1	05-Aug-26	05-Aug-26	08-Jun-26	22	CONS-EB-5320, CONS-
CONS-EB-5320	Install Server Racks Server Room	0%	0%	5	06-Aug-26	12-Aug-26	16-Jun-26	24	CONS-CLOS-1000
LOCKER ROOM			0%	14	27-Jul-26	14-Aug-26	17-Jun-26	23	
CONS-EB-5400	Interior Prime Paint Locker Rooms	0%	0%	1	27-Jul-26	27-Jul-26	02-Jun-26	26	CONS-EB-5410, CONS-
CONS-EB-5440	Install sheet vinyl flooring Locker Rooms	0%	0%	1	28-Jul-26	28-Jul-26	15-Jun-26	26	CONS-CLOS-1000, COI
CONS-EB-5420	Install Casework Locker Rooms	0%	0%	2	29-Jul-26	30-Jul-26	12-Jun-26	26	CONS-EB-5410
CONS-EB-5410	Install Interior Finish Paint Locker Rooms	0%	0%	1	06-Aug-26	06-Aug-26	09-Jun-26	22	CONS-EB-5430, CONS-
CONS-EB-5430	Install Lockers in Locker Rooms	0%	0%	5	07-Aug-26	14-Aug-26	17-Jun-26	23	CONS-CLOS-1000
GREETING ROOM			0%	10	28-Jul-26	10-Aug-26	16-Jun-26	26	
CONS-EB-5510	Interior Prime Paint Greeting Rooms	0%	0%	1	28-Jul-26	28-Jul-26	03-Jun-26	26	CONS-EB-5520, CONS-
CONS-EB-5550	Install sheet vinyl flooring Greeting Rooms	0%	0%	1	29-Jul-26	29-Jul-26	16-Jun-26	26	CONS-CLOS-1000, COI
CONS-EB-5530	Install Casework Greeting Rooms	0%	0%	2	30-Jul-26	31-Jul-26	15-Jun-26	26	CONS-EB-5520
CONS-EB-5520	Install Interior Finish Paint Greeting Rooms	0%	0%	1	07-Aug-26	07-Aug-26	11-Jun-26	22	CONS-EB-5540, CONS-
CONS-EB-5540	Install mechanical diffusers Greeting Rooms	0%	0%	1	10-Aug-26	10-Aug-26	12-Jun-26	26	CONS-CLOS-1000
RABBIT ROOMS			0%	10	29-Jul-26	11-Aug-26	17-Jun-26	25	

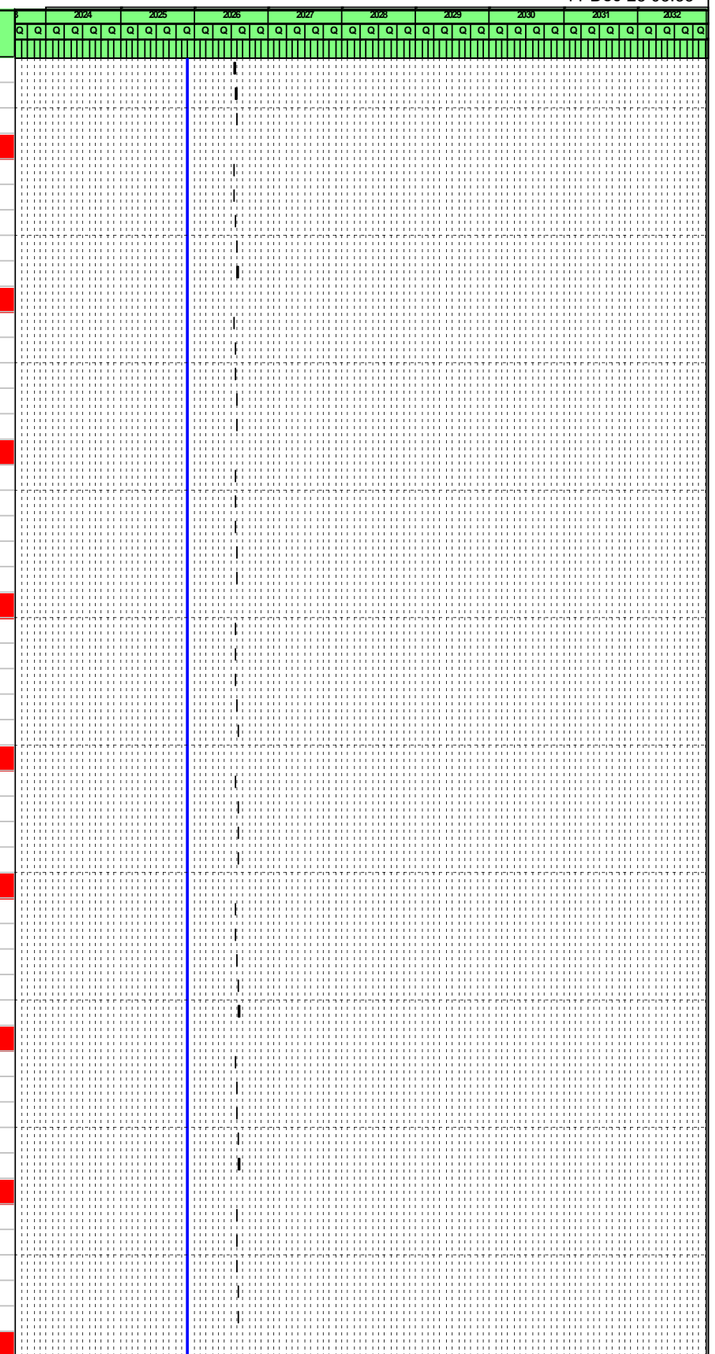


Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
CONS-EB-5620	Interior Prime Paint Rabbit Rooms	0%	0%	1	29-Jul-26	29-Jul-26	04-Jun-26	26	CONS-EB-5630, CONS-
CONS-EB-5660	Install sheet vinyl flooring Rabbit Rooms	0%	0%	1	30-Jul-26	30-Jul-26	17-Jun-26	26	CONS-CLOS-1000, COI
CONS-EB-5640	Install Casework Rabbit Rooms	0%	0%	2	31-Jul-26	03-Aug-26	16-Jun-26	26	CONS-EB-5630
CONS-EB-5630	Install Interior Finish Paint Rabbit Rooms	0%	0%	1	10-Aug-26	10-Aug-26	12-Jun-26	22	CONS-EB-5650, CONS-
CONS-EB-5650	Install mechanical diffusers Rabbit Rooms	0%	0%	1	11-Aug-26	11-Aug-26	15-Jun-26	25	CONS-CLOS-1000
OPEN OFFICES			0%	12	30-Jul-26	17-Aug-26	18-Jun-26	22	
CONS-EB-5730	Interior Prime Paint Open Offices	0%	0%	1	30-Jul-26	30-Jul-26	05-Jun-26	27	CONS-EB-5740, CONS-
CONS-EB-5740	Install Interior Finish Paint Open Offices	0%	0%	1	11-Aug-26	11-Aug-26	15-Jun-26	22	CONS-EB-5750, CONS-
CONS-EB-5750	Install Casework Open Offices	0%	0%	2	12-Aug-26	14-Aug-26	17-Jun-26	22	CONS-EB-5770
CONS-EB-5760	Install mechanical diffusers Open Offices	0%	0%	1	12-Aug-26	12-Aug-26	16-Jun-26	24	CONS-CLOS-1000
CONS-EB-5770	Install sheet vinyl flooring Open Offices	0%	0%	1	17-Aug-26	17-Aug-26	18-Jun-26	22	CONS-CLOS-1000
MEDICAL STORAGE			0%	10	31-Jul-26	14-Aug-26	19-Jun-26	23	
CONS-EB-5840	Interior Prime Paint Medical Storage	0%	0%	1	31-Jul-26	31-Jul-26	08-Jun-26	27	CONS-EB-5850, CONS-
CONS-EB-5880	Install sheet vinyl flooring Medical Storage	0%	0%	1	03-Aug-26	03-Aug-26	19-Jun-26	27	CONS-CLOS-1000, COI
CONS-EB-5860	Install Casework Medical Storage	0%	0%	2	04-Aug-26	05-Aug-26	18-Jun-26	27	CONS-EB-5850
CONS-EB-5850	Install Interior Finish PaintMedical Storage	0%	0%	1	12-Aug-26	12-Aug-26	16-Jun-26	23	CONS-EB-5870
CONS-EB-5870	Install mechanical diffusers Medical Storage	0%	0%	1	14-Aug-26	14-Aug-26	17-Jun-26	23	CONS-CLOS-1000
ELEVATORS			40.09%	130	23-Apr-25 A	15-Jun-26	01-Jun-26	37	
CONS-EB-6250	Excavate for Elevator Pit	100%	100%	0	23-Apr-25 A	24-Apr-25 A	01-Nov-25		CONS-EB-1280
CONS-EB-1280	Form/Rebar/Pour Elevator Pit	100%	100%	0	25-Apr-25 A	28-Apr-25 A	01-Nov-25		CONS-EB-1290
CONS-EB-1290	Install CMU Elevator Shaft	10%	10%	9	24-Nov-25 A	11-Dec-25	28-Nov-25	88	CONS-EB-1300
CONS-EB-1300	Install Elevator Rails	0%	0%	5	03-Mar-26	09-Mar-26	24-Feb-26	37	CONS-EB-1330
CONS-EB-1330	Install Elevator Platforms	0%	0%	10	10-Mar-26	24-Mar-26	10-Mar-26	37	CONS-EB-1335
CONS-EB-1335	Install Elevator Cab	0%	0%	10	25-Mar-26	08-Apr-26	25-Mar-26	37	CONS-EB-1340
CONS-EB-1340	Install Elevator Cab wiring & Terminations /Meggar Test	0%	0%	20	09-Apr-26	06-May-26	23-Apr-26	37	CONS-EB-1345
CONS-EB-1345	Install Elevator Cab Finishes & door Trim	0%	0%	10	07-May-26	21-May-26	07-May-26	37	CONS-EB-1355
CONS-EB-1355	Troubleshoot & Preliminary Testing of Elevator	0%	0%	5	22-May-26	29-May-26	15-May-26	37	CONS-INSP-1005, CON
CONS-EB-6260	Final Testing & sign-off of Elevator (Not in Scope)	0%	0%	10	01-Jun-26	15-Jun-26	01-Jun-26	37	CONS-TEST-1000
SITEWORK			0%	174	01-Dec-25	18-Aug-26	28-Jul-26	9	
SITE-1010	DEP Permit for Combined Sewer Connection	0%	0%	20	01-Dec-25	30-Dec-25	01-Dec-25	106	SITE-1050
SITE-1130	DEP Permit for wall & Fire Service Connection	0%	0%	20	08-Jan-26	06-Feb-26	22-Jan-26	81	SITE-1060
SITE-1050	Excavate at wall & Install Combined Sewer (Sanitary)	0%	0%	4	20-Jan-26	26-Jan-26	12-Mar-26	93	SITE-1070, SITE-1080, I
SITE-1000	DDC obtain new Con Edison electrical Service	0%	0%	40	30-Jan-26	31-Mar-26	08-Jun-26	46	SITE-1030, SITE-1020
SITE-1060	Excavate at wall & Install water & Fire Service	0%	0%	4	09-Feb-26	12-Feb-26	12-Mar-26	81	SITE-1070, SITE-1080, I
SITE-1020	Excavate at wall & Install Gas Service Con Edison	0%	0%	4	01-Apr-26	06-Apr-26	15-Jun-26	46	SITE-1070, SITE-1080, I
SITE-1030	Excavate at wall & Install Electric Service From Street by Con Edison	0%	0%	19	01-Apr-26	28-Apr-26	06-Jul-26	46	SITE-1040, SITE-1070, S
SITE-1040	Excavate at wall & Install Data Service Cable Company	0%	0%	4	01-Apr-26	06-Apr-26	15-Jun-26	46	SITE-1070, SITE-1080, I
SITE-1070	Install Site Grading and Site Concrete	0%	0%	15	08-Apr-26	28-Apr-26	06-Jul-26	46	SITE-1080, SITE-1090, S
SITE-1090	Install Site Lighting	0%	0%	15	08-Apr-26	28-Apr-26	06-Jul-26	46	SITE-1100
SITE-1080	Install Site Paving	0%	0%	5	29-Apr-26	05-May-26	14-Jul-26	56	CONS-EB-1500, CONS-
SITE-1100	Install Site Fences and Gates	0%	0%	15	29-Apr-26	20-May-26	28-Jul-26	46	SITE-1120, SITE-1120, E
SITE-1110	Install Drainage Mats and Turf	0%	0%	10	28-Jul-26	10-Aug-26	09-Jun-26	9	SITE-1120
SITE-1120	Install Landscaping	0%	0%	5	11-Aug-26	18-Aug-26	28-Jul-26	9	CONS-CLOS-1000, COI
CLOSEOUT			0%	274	03-Jun-24 A	17-Dec-26	17-Dec-26	1	
EQUIPMENT START-UP			0%	72	29-Apr-26	09-Jul-26	16-Jul-26	67	
CONS-STAR-1120	Perform Electrical Equipment Startup	0%	0%	2	29-Apr-26	30-Apr-26	08-Jul-26	134	CONS-PRE-1170
CONS-STAR-1170	Perform Generator Equipment Startup	0%	0%	2	12-May-26	13-May-26	18-Mar-26	124	CONS-PRE-1220
CONS-STAR-1160	Perform Elevator Equipment Startup	0%	0%	2	22-May-26	23-May-26	09-May-26	114	CONS-PRE-1210
CONS-STAR-1130	Perform HVAC Equipment Startup	0%	0%	2	01-Jun-26	02-Jun-26	16-Jul-26	96	CONS-PRE-1180
CONS-STAR-1140	Perform Plumbing Equipment Startup	0%	0%	2	30-Jun-26	01-Jul-26	17-Jun-26	72	CONS-PRE-1190
CONS-STAR-1150	Perform Sprinkler Equipment Startup	0%	0%	2	08-Jul-26	09-Jul-26	27-May-26	35	CONS-PRE-1200

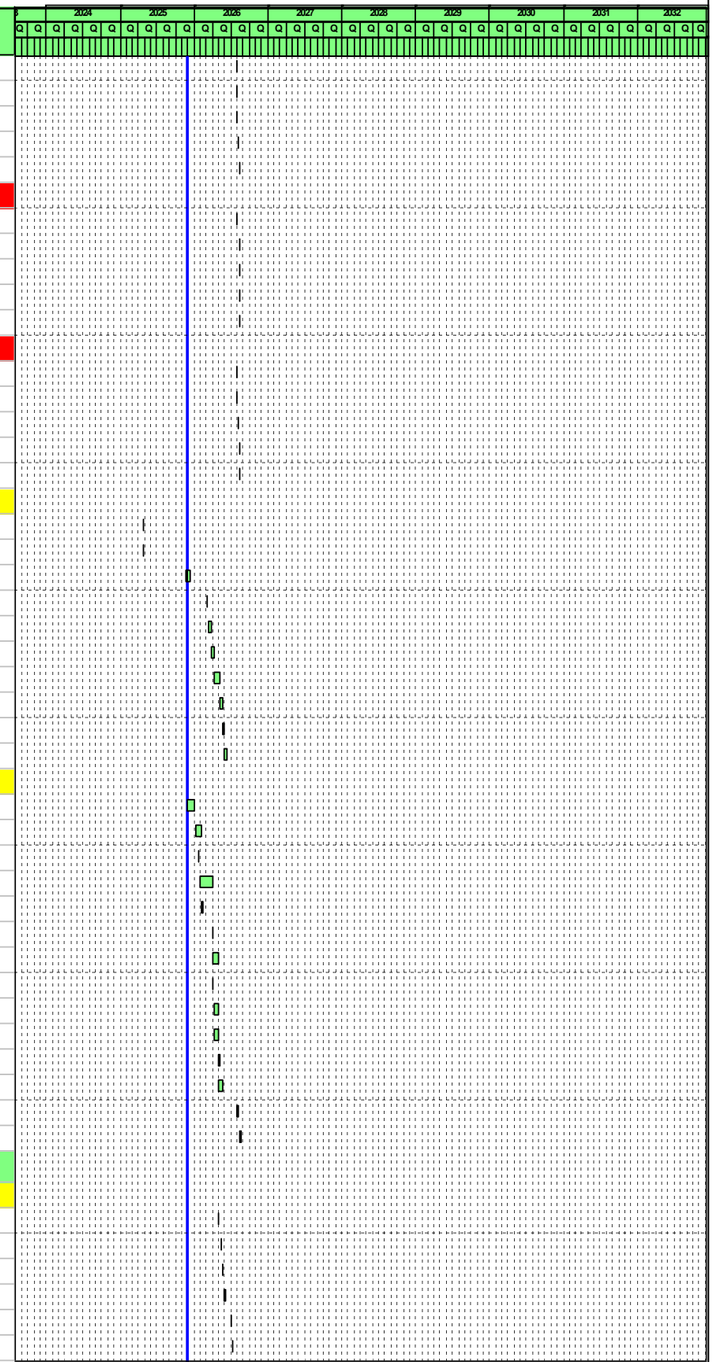

Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
PRE-FUNCTIONAL TESTING			0%	72	01-May-26	11-Jul-26	18-Jul-26	67	
CONS-PRE-1170	Perform Electrical Equipment Pre-Functional/Checklist	0%	0%	2	01-May-26	02-May-26	10-Jul-26	134	CONS-FUN-1000
CONS-PRE-1220	Perform Generator Equipment Pre-Functional/Checklist	0%	0%	2	14-May-26	15-May-26	20-Mar-26	124	CONS-FUN-1030
CONS-PRE-1210	Perform Elevator Equipment Pre-Functional/Checklist	0%	0%	2	24-May-26	25-May-26	11-May-26	114	CONS-FUN-1020
CONS-PRE-1180	Perform HVAC Equipment Pre-Functional/Checklist	0%	0%	2	03-Jun-26	04-Jun-26	18-Jul-26	96	CONS-FUN-1005
CONS-PRE-1190	Perform Plumbing Equipment Pre-Functional/Checklist	0%	0%	2	02-Jul-26	03-Jul-26	19-Jun-26	72	CONS-FUN-1010
CONS-PRE-1200	Perform Sprinkler Equipment Pre-Functional/Checklist	0%	0%	2	10-Jul-26	11-Jul-26	29-May-26	35	CONS-FUN-1015
FUNCTIONAL TESTING			0%	41	16-May-26	13-Jul-26	14-Aug-26	49	
CONS-FUN-1030	Perform Generator Equipment Functional	0%	0%	2	16-May-26	17-May-26	22-Mar-26	124	ML2000
CONS-FUN-1020	Perform Elevator Equipment Functional	0%	0%	2	26-May-26	27-May-26	13-May-26	114	ML2000
CONS-TEST-1005	HVAC Balancing	0%	0%	5	16-Jun-26	22-Jun-26	04-Aug-26	53	ML2000, CONS-FUN-10
CONS-FUN-1005	Perform HVAC Equipment Functional	0%	0%	10	23-Jun-26	02-Jul-26	14-Aug-26	78	ML2000
CONS-FUN-1000	Perform Electrical Equipment Functional	0%	0%	5	30-Jun-26	04-Jul-26	15-Jul-26	76	ML2000
CONS-FUN-1010	Perform Plumbing Equipment Functional	0%	0%	5	04-Jul-26	08-Jul-26	24-Jun-26	72	ML2000
CONS-FUN-1015	Perform Sprinkler Equipment Functional	0%	0%	2	12-Jul-26	13-Jul-26	31-May-26	35	CONS-INSP-1000
COMMISSIONING			93.48%	6	03-Jun-24 A	17-Aug-26	22-Jul-26	22	
CONS-COMM-1080	HVAC Commissioning (not Required)	100%	100%	0	03-Jun-24 A	03-Jun-24 A	01-Nov-25		ML2000
CONS-COMM-1110	Low Voltage System Commissioning (not Required)	100%	100%	0	03-Jun-24 A	03-Jun-24 A	01-Nov-25		ML2000
CONS-COMM-1120	Electrical Commissioning (not Required)	100%	100%	0	03-Jun-24 A	03-Jun-24 A	01-Nov-25		ML2000
CONS-COMM-1150	Solar System Commissioning (not Required)	100%	100%	0	03-Jun-24 A	03-Jun-24 A	01-Nov-25		ML2000
CONS-COMM-1115	Commissioning Fire Water Pump (not Required)	100%	100%	0	03-Jun-24 A	03-Jun-24 A	01-Nov-25		CONS-INSP-1000
CONS-COMM-1160	Building Envelope Testing (not Required)	100%	100%	0	03-Jun-24 A	03-Jun-24 A	01-Nov-25		CONS-INSP-1005
CONS-COMM-1170	Elevator Commissioning (not Required)	100%	100%	0	03-Jun-24 A	03-Jun-24 A	01-Nov-25		ML2000
CONS-TEST-1000	Fire Alarm Testing for First TCO	0%	0%	6	07-Aug-26	17-Aug-26	22-Jul-26	0	CONS-INSP-1000
TRAINING			0%	90	19-Sep-26	17-Dec-26	17-Dec-26	2	
CONS-CLOS-1020	Post-construction Close-out Perform Training (Electrical)	0%	0%	90	19-Sep-26	17-Dec-26	17-Dec-26	2	ML3000
CONS-CLOS-1080	Post-construction Close-out Perform Training (HVAC)	0%	0%	90	19-Sep-26	17-Dec-26	17-Dec-26	2	ML3000
CONS-CLOS-1090	Post-construction Close-out Perform Training Plumbing)	0%	0%	90	19-Sep-26	17-Dec-26	17-Dec-26	2	ML3000
CONS-CLOS-1100	Post-construction Close-out Perform Training (Sprinkler)	0%	0%	90	19-Sep-26	17-Dec-26	17-Dec-26	2	ML3000
CONS-CLOS-1110	Post-construction Close-out Perform Training (Elevator)	0%	0%	90	19-Sep-26	17-Dec-26	17-Dec-26	2	ML3000
019500 - BIM MODEL ASBUILT			0%	189	01-Dec-25	09-Sep-26	04-Aug-26	68	
BIM MODEL - FIRST LEVEL			0%	131	24-Feb-26	03-Sep-26	04-Aug-26	71	
PRO-1-1000	Prepare fire protection As-built Model - 1st level	0%	0%	20	24-Feb-26	24-Mar-26	12-Feb-26	120	CONS-CLOS-1000, COI
PRO-1-1020	Prepare HVAC As-built Model - 1st level	0%	0%	20	25-Mar-26	22-Apr-26	16-Mar-26	80	PRO-1-1010, PRO-1-11
PRO-1-1010	Prepare Plumbing As-built Model - 1st level	0%	0%	20	23-Apr-26	21-May-26	14-Apr-26	80	CONS-CLOS-1000, COI
PRO-1-1030	Prepare electrical As-built Model - 1st level	0%	0%	20	29-Apr-26	28-May-26	04-Aug-26	76	CONS-CLOS-1000, COI
PRO-1-1015	Prepare electronic safety and security work Asbuilt Model - 1st level	0%	0%	20	06-Aug-26	03-Sep-26	29-Jul-26	71	CONS-CLOS-1000, COI
BIM MODEL - SECOND LEVEL			0%	189	01-Dec-25	09-Sep-26	30-Jul-26	68	
PRO-1-1060	Prepare fire protection As-built Model- 2nd level	0%	0%	20	01-Dec-25	30-Dec-25	01-Dec-25	175	CONS-CLOS-1000, COI
PRO-1-1070	Prepare electrical coordination drawings all tradesAs-built Model - 2nd level	0%	0%	20	08-Jan-26	06-Feb-26	30-Jan-26	150	CONS-CLOS-1000, COI
PRO-1-1050	Prepare HVAC As-built Model - 2nd level	0%	0%	20	28-Jan-26	26-Feb-26	11-Feb-26	117	PRO-1-1040, PRO-1-11
PRO-1-1040	Prepare Plumbing As-built Model - 2nd level	0%	0%	20	27-Feb-26	27-Mar-26	13-Mar-26	117	CONS-CLOS-1000, COI
PRO-1-1035	Prepare electronic safety and security work As-built Model - 2nd level	0%	0%	20	11-Aug-26	09-Sep-26	30-Jul-26	68	CONS-CLOS-1000, COI
BIM MODEL - ROOF LEVEL			0%	110	01-Dec-25	14-May-26	23-Mar-26	147	
PRO-1-1100	Prepare fire protection As-built Model Roof level	0%	0%	20	01-Dec-25	30-Dec-25	01-Dec-25	175	CONS-CLOS-1000, COI
PRO-1-1110	Prepare electrical As-built Model - roof level	0%	0%	20	08-Jan-26	06-Feb-26	30-Jan-26	212	CONS-CLOS-1000, COI
PRO-1-1080	Prepare Plumbing As-built Model - roof level	0%	0%	20	23-Jan-26	23-Feb-26	23-Jan-26	140	CONS-CLOS-1000, COI
PRO-1-1090	Prepare HVAC As-built Model - roof level	0%	0%	20	16-Apr-26	14-May-26	23-Mar-26	85	CONS-CLOS-1000, COI
BMS ASBUILT			0%	20	11-Aug-26	09-Sep-26	04-Aug-26	68	
PRO-1-1120	Prepare BMS As-built	0%	0%	20	11-Aug-26	09-Sep-26	04-Aug-26	68	CONS-CLOS-1000, COI
O & M MANUALS			0%	90	19-Sep-26	17-Dec-26	17-Dec-26	2	

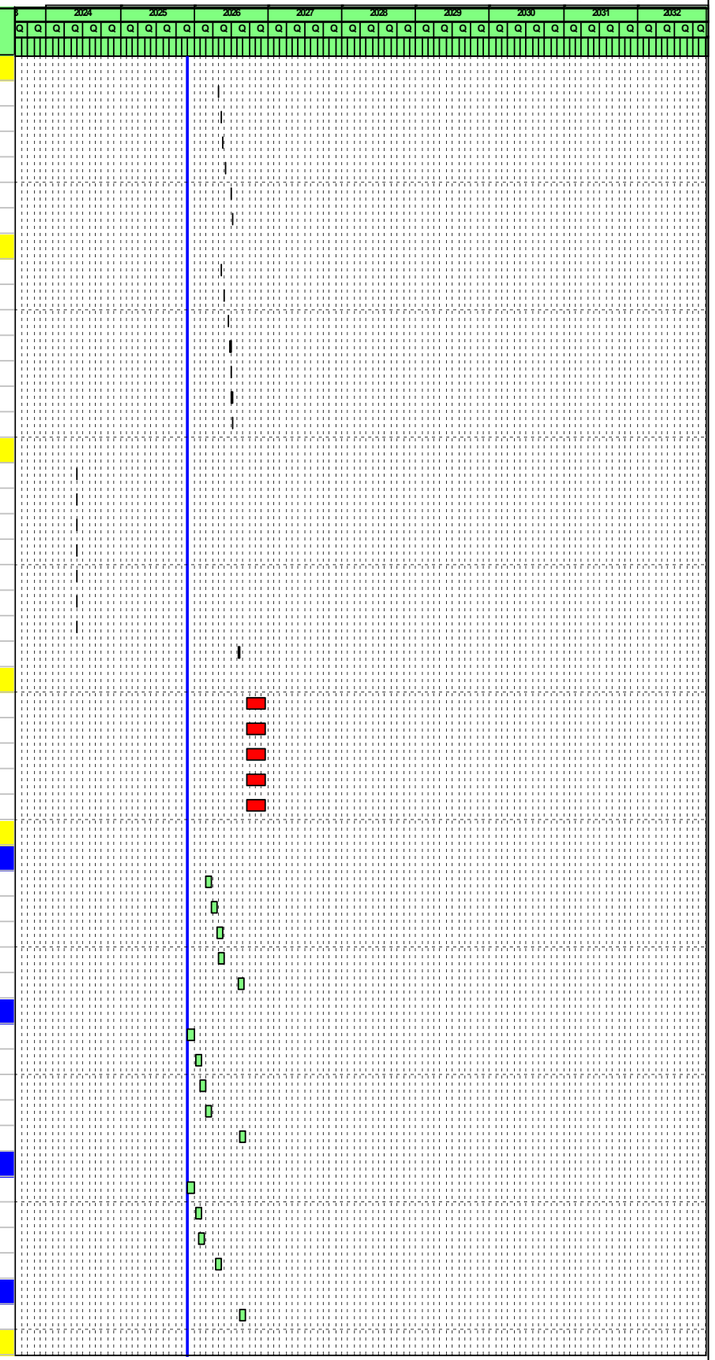

Activity ID	Activity Name	Physical % Complete	Duration % Complete	Remaining Duration	Start	Finish	Prev Update Early Finish	Total Float	Successors
CONS-CLOS-1010	Post-construction Close-out Documentation Plumbing O & M Manuals	0%	0%	90	19-Sep-26	17-Dec-26	17-Dec-26	2	ML3000
CONS-CLOS-1030	Post-construction Close-out Documentation Electrical O & M Manuals	0%	0%	90	19-Sep-26	17-Dec-26	17-Dec-26	2	ML3000
CONS-CLOS-1040	Post-construction Close-out Documentation HVAC O & M Manuals	0%	0%	90	19-Sep-26	17-Dec-26	17-Dec-26	2	ML3000
CONS-CLOS-1050	Post-construction Close-out Documentation BMS O & M Manuals	0%	0%	90	19-Sep-26	17-Dec-26	17-Dec-26	2	ML3000
CONS-CLOS-1060	Post-construction Close-out Documentation Fire Protection O & M Manuals	0%	0%	90	19-Sep-26	17-Dec-26	17-Dec-26	2	ML3000
CONS-CLOS-1070	Post-construction Close-out Documentation Elevator O & M Manuals	0%	0%	90	19-Sep-26	17-Dec-26	17-Dec-26	2	ML3000
REQUESTS/INSPECTIONS/PUNCH LIST			0%	26	11-Aug-26	18-Sep-26	17-Aug-26	62	
CONS-INSP-1005	Request Substantial completion	0%	0%	1	11-Aug-26	11-Aug-26	02-Jul-26	13	ML2000, CONS-INSP-1(
CONS-INSP-1000	FDNY Inspection for First TCO	0%	0%	10	18-Aug-26	31-Aug-26	29-Jul-26	0	CONS-INSP-1010
CONS-INSP-1010	Substantial completion Walk thru & Inspection	0%	0%	2	01-Sep-26	02-Sep-26	31-Jul-26	0	ML2000, CONS-INSP-1(
CONS-INSP-1015	Punch list for Final Completion being Granted	0%	0%	10	03-Sep-26	18-Sep-26	17-Aug-26	62	ML3000
CONS-INSP-1025	Punch list for Substantial completion Milestone	0%	0%	10	03-Sep-26	18-Sep-26		0	ML2000
ADMINISTATIVE/PAPERWORK CLOSEOUTS			0%	90	19-Sep-26	17-Dec-26	17-Dec-26	2	
CONS-CLOS-1000	Post-construction Close-out Documentation Warranties	0%	0%	90	19-Sep-26	17-Dec-26	17-Dec-26	2	ML3000

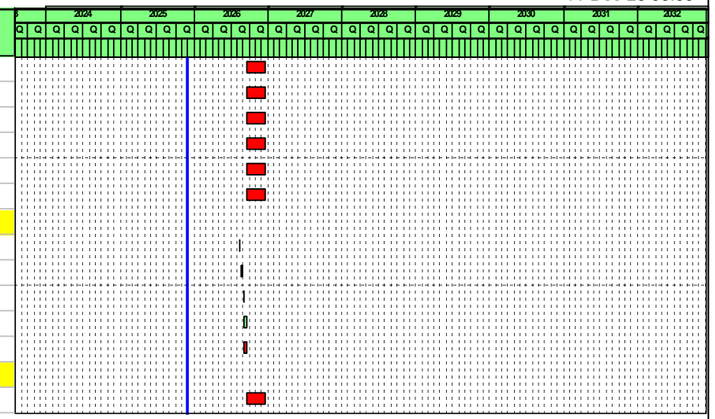

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone
