Name of Job:

Creedmoor Psychiatric Center
Inpatient Bed Expansion Renovations
79-25 Winchester Boulevard
Queens Village, NY
Project#47777-C

P-187 Job No.
S-006 Contract No.

All correspondence pertaining to this Agreement shall be forwarded in duplicate to the address shown opposite.

PRISMATIC
DEVELOPMENT CORPORATION
60 US HIGHWAY 46, FAIRFIELD, NJ 07004
(973) 882-1133 / (973) 882-1132 FAX

THIS AGREEMENT, made and executed this 13th day of August, 2025
by and between Elli NY Design Corp.
50-01 Metropolitan Avenue
Ridgewood, NY 11385
(718) 418-9002 / (718) 418-4629 fax
Lissette Olivo – lissette@ellicorp.com

hereinafter designated as the "Subcontractor", and PRISMATIC DEVELOPMENT CORPORATION, a Corporation organized and existing under the laws of the State of NJ, hereinafter designated as the "Contractor"

WITNESSETH

Whereas Prismatic Development Corporation is the General Contractor under a prime contract with The State of New York, Office of General Services under the terms of which Prismatic Development Corporation is obligated to construct the project therein described pursuant to the plans, specifications, addenda, amendments and prime contract documents pertaining thereto; and

Whereas, it is the intention of the parties hereto to enter into a subcontract agreement for a portion of the said work as hereinafter described: ARCHITECTURAL WOODWORK & SOLID PLASTIC FABRICATIONS.

NOW THEREFORE in consideration of a sum of TWO HUNDRED TWENTY FIVE THOUSAND ONE DOLLARS AND 64/100. ($225,001.64)

the Subcontractor hereby covenants and agrees to furnish all materials, labor, tools, equipment and services for, and perform and complete in place in a good, workmanlike substantial manner to the complete satisfaction of the Contractor, all the following described work and construction:

A) Elli NY Design Corp. hereby agrees as stated above to provide all necessary labor, materials, equipment and services required for a complete and safe installation of all work as described in Specification Section 064000 entitled "Architectural Woodwork", and Specification Section 066000 entitled "Solid Plastic Fabrications", as modified by Addendums and all as shown on the drawings as prepared by New York Office of General Services, Design & Construction, Hyman Hayes Associates, 800 Troy-Schenectady Road, Suite 103, Latham, NY 12110, Fellenzer Engineering LLP, 22 Mulberry Street, Suite 2A, Middletown, NY 10940.

SUB	CONT

Prismatic Development has very serious minority participation requirements for this project imposed by the State of New York, Office of General Services, as well as an internal moral commitment to embrace the spirit of the WBE/MBE/SDVOB Laws and Regulations. Accordingly Prismatic Development expects Elli NY Design Corp. to make the maximum good faith effort to include and employ both Women and Minority Business Enterprises wherever and whenever practical in fulfilling this order.

B) It is understood and agreed that this contract consists of and includes the following Contract Documents:

CONTRACT DOCUMENTS:

Addendum: No. 1 dated June 9, 2022
No. 2 dated June 22, 2022
No. 3 dated July 8, 2022

Numerous RFI's Responses dated from June 2, 2022 through July 8, 2022

Specifications: Project Manual dated February 15, 2022, includes all the Technical Specification Sections, Appendix and General Conditions.

Drawings: All labeled as Project No. 47103-C dated February 15, 2022, as Bid Documents.
G Drawings
L Drawings
A Drawings
FP Drawings
P Drawings
M Drawings
E Drawings

NOTE: This contract includes documents shown in NYSOGS Contract Number 47103-C and 47777-C. See also Paragraph T for additional documents included in this contract.

C) It is understood that the work of this contract includes but is not limited to the following items of work:
1. All work as described in Paragraph A above.

D) This contractor shall guarantee his work in accordance with the contract documents, codes, etc., and shall execute a guarantee form as part of this agreement.

E) The sequence, scheduling and installation of all items of work included in this agreement shall be performed in accordance with the documents and the directives of the Contractor's Project Superintendent.

F) It is understood and agreed that all shop drawings, samples and catalogs will begin to be submitted to this office within 10 days of execution of this contract.

G) It is understood and agreed that prior to any work commencement on site, this Subcontractor will supply proof of insurance coverage of types and with limits as specified in the Contract Documents.

H) It is understood and agreed that this Subcontractor will submit a complete payment breakdown prior to his first payment request, to be used for billing purposes each month.

I) This subcontractor shall cleanup all refuse, rubbish and debris caused by his workmen or resulting from work within and shall remove same from jobsite.

J) It is understood and agreed that this contract is exempt from Sales Tax. Certificate attached.

SUB	CONT

K) This Subcontractor shall coordinate his work with the work of all other trades and will be responsible to protect the work and equipment of other trades in addition to his own while performing his work.

L) It shall be the responsibility of this Subcontractor to repair and/or replace any defective material and/or workmanship in connection with his work and perform any Punchlist items of work that may be required to produce an acceptable job.

M) It is understood and agreed that certified payrolls (three copies) must be submitted each month along with your request for partial payment, certifying that wages contained therein are not less than those determined by the Secretary of Labor for each mechanic to the work he performed. All work to be performed with Union Labor and Prevailing Wage Rates. This will include two copies of the following forms; BDC25 Monthly Income Payments, BDC58 Contractor Monthly Payment Report, and BDC328 Monthly Utilization Plan, as well as EEO101 Workforce Utilization.

N) It is understood that prior to payments, evidence of payment to major subcontractors and materialmen will be supplied by this subcontractor.

O) It is understood and agreed that this subcontractor shall comply with all applicable Federal, State, and local laws, statues, rules and regulations related to Prevailing Wage and Equal Employment/Affirmative Action.

P) This subcontractor fully understands and agrees that any subcontractors to it performing portions of the work under this agreement subject to Article 13 of this subcontract will be fully bound to all the terms and conditions of the Contract Documents and this subcontract, including all General Contract Language pertaining to wage scale, Affirmative Action, payment of subs, suppliers, etc.

Q) It is understood and agreed that this subcontractor will submit a schedule of the dates on which all shop drawings, catalogs, etc., will be furnished, and dates showing the delivery of all such items. Such schedule shall be in compliance with the requirements set forth by the General Contractor and overall project schedule.

R) It is understood that the Subcontractor will comply with all particular items listed and be fully cognizant of special areas within, such as but not limited to Advertisement Information for Bids, Instructions to Bidders, Supplementary Instructions to Bidders, Proposal, Standard Construction Contract; Time Provisions, Labor Provisions, Partial and Final Payments, Miscellaneous Provisions, General Conditions, Prevailing Wage Rates/Labor Law 220; General Requirements, Equal Employment Opportunity, No Discrimination, Affirmative Action Programs, Minimum Wage Rates, Extra Work Orders, Shop Drawings, Catalog Cuts/Samples, Substitutions, Workmanship, Inspections & Rejections, Certifications, Safety Provisions, Daily Reports, Signs, Permits, Inspections, Warranties, Record Drawings, Temporary Utilities & Services, Progress Schedule, Safety Requirements, Hours of Work, Construction Staging & Phases, Maintenance of Traffic and Work Areas Protection, Schedules, Geotechnical Report, Bonds, Construction Schedules and Sequence, Permits, American Goods and Products Exemption of State Sales, Use Taxes and Federal Excise Taxes; Time of Completion; Work harmoniously in all respects with all parties; Approval of Subcontractor; Indemnify and Hold Harmless; Prohibited Procedure and Waste Materials Disposal; Quality Control and Testing; Table of Contents; Bid Submission Checklist; Sample of Forms to be Completed Upon Execution of Contract: Insurance, Integrity Affidavit, Disclosure Form, Form of Contract, Initial Project Workforce Report; Contract Components; The Owner, The Contractor, Time; Prosecution and Progress of Work, Subcontractors, Changes in Work, Insurance and Bonds, Suspension of the Work, Default and Termination, Substantial Completion and Final Acceptance and Completion, Liquidated Damages, Payment and Contract Completion, Protection of Persons and Property, Documents and Records, Risk of Loss and Indemnification, Claims and Dispute Resolution, Legal Relations and Miscellaneous Provisions, Warranties; Supplementary Conditions; Code of Ethics; Drawing List, Summary of Work; Allowances; Alternates; Unit Prices; Field Engineering; Change Order Procedure; Coordination; Cutting & Patching; Pre-Construction Conference; Project Meetings; Submittals; Schedules and Reports; Photographs; Testing Laboratory Service; Temporary Facilities; Storage and Protection; Products and Substitutions; Contract Closeout; Final Cleaning; Project Record Documents; Operations & Maintenance Data; Warranties & Bonds, comply with Project Labor Agreement. VOLUME 1 - PROCUREMENT AND CONTRACTING REQUIREMENTS GROUP - PROCUREMENT AND CONTRACTING REQUIREMENTS -

SUB	CONT

INTRODUCTORY – INFORMATION, Title Page (Cover) Certification Page, Table of Contents, List of Drawings, BIDDING REQUIREMENTS - Advertisement for Bids – PLA, Instructions to Bidders, Supplementary Instructions to Bidders – MWBE-EEO, Supplementary Instructions to Bidders – Total Bid, Supplementary Instructions to Bidders – Asbestos Projects, Supplementary Instructions to Bidders – Pre-Bid Site Visit, Supplementary Instructions to Bidders – Qualifications of Bidders, Supplementary Instructions to Bidders - Project Labor Agreement, Supplementary Instructions to Bidders - Condition of Award Use with PLA, Supplementary Instructions to Bidders – Mandatory Pre Bid Visit, Preliminary Project Schedule, Preliminary Project Schedule CP 003126 Existing Hazardous Material, Bid Form – PLA - With Service Contract, Bid Form - Service Contract – Elevators, Bid Form - Service Contract – HVAC, BDC 59P Project Labor Agreement List of Subcontractors, Form of Bid Bond – Bid Security, New York State Surety Bond, DCA-3 Offerer Disclosure of Prior Non-Responsibility Determinations. CONTRACTING REQUIREMENTS - General Conditions, Supplementary Conditions – Liquidated Damages, Supplementary Conditions – Warranty Extension, Supplementary Conditions – MWBE-EEO, Supplementary Conditions – License Requirements, Supplementary Conditions – Contractor's Supervision, Supplementary Conditions – Iran Divestment Act, Supplementary Conditions – Workers Compensation Supplementary Conditions – Vendor Responsibility, Supplementary Conditions - Encouraging Use of New York State Businesses, Supplementary Conditions - Project Labor Agreement Plan (PLA), Supplementary Conditions - Orders on Contract (Change Orders), Supplementary Conditions- State's Right to Perform Work, Elevator Maintenance Services Agreement, HVAC Systems & Equipment Maintenance Services Agreement, OMH Bid Submission Documentation and Forms. GENERAL REQUIREMENTS SUBGROUP - DIVISION 01 – GENERAL REQUIREMENTS - Summary of the Work, Interim Life Safety Measures, Allowances, Cost Computations, Administrative Requirements, Project Meetings Construction Progress Documentation, Submittals, Building Information, Model (BIM/REVIT) Protocol, Regulatory Requirements, Definitions, Mockup Requirements, Construction Facilities & Temporary Controls, Temporary Heat and Air Conditioning, Material and Personnel Hoists, Materials and Equipment, Removals Cutting and Patching, Pre-Occupancy Cleaning, Contract Closeout, Demonstration and Training, Video Training Programs, General Commissioning Requirements. APPENDIX - BDC 42 Submittal Transmittal, BDC 49 Contract Document Deviation Request Form BDC 59.1 Contractor's Proposal for Subcontractor Change (PLA), BDC 59.P Project Labor Agreement List of Subcontractors, BDC 187 Schedule of Values, BDC 328 Contractor's MWBE Utilization Plan, BDC 329 Contractor's List of Subcontractors – Suppliers, BDC 346 Field Inspection Report, BDC 387 Concealed Space Enclosure Inspection BDC 406 Summary of Special Inspections, BDC 406.1 Statement of Special Inspections, BIM Facility Asset Attribute Log Commissioning Sample Functional Test Form, Commissioning Sample Pre-Functional Form, Existing Hazardous Material Summary Report, List of Controlled Inspections, MR02 BID SCHEDULE, Project Labor Agreement, Sample Above Ceiling Concealed Space Inspection Check List, FF&E Room List, FF&E Equipment & Responsibilities. Article 10 of the NYC OGS General Conditions 007213 also applies relative to Change Orders.

S) It is understood and agreed that there are no exceptions to this contract unless otherwise noted below:

1. None.

T) It is clearly understood and agreed this contract includes but is not necessarily limited to the following:

Plans and specs complete.

Reviewed & agreed that this is a Unique Contract with different Front End Spec Sections for Project No. 47777-C.

Reviewed & agreed that this is a separate contract/separate administrative requirements; including separate billing procedures and certified payroll reporting/daily work reporting.

Security and Badging requirements will be used by all Subcontractors on this project.

Contract is contingent on OGS approval before, during and after execution.

All Subcontractors and Suppliers must cooperate and coordinate with Prismatic Development Corporation regarding the Phasing and Scheduling of the work including the use of the Hoist and hours of operation.

SUB	CONT

There will be Mockup Participation by everyone which will require expedited and quick delivery of materials for same.

Proof of Covid Vaccinations are required by everyone working on this site.

This Project also requires Temporary relocations and replacements and must be coordinated with Prismatic Development Corporation as identified on all G Drawings.

OGS-NY Contract 47777-C – "additional floors"

Includes responses to Pre-Award RFI's #1-21.

47777-C contract documents make reference to 47103-C contract documents for work included herein.

OGS Approval Letter 47777-C Three Bid Waiver dated 7/22/25 PDC received 8/12/25 – with markups on Elli Proposal Floors 4B & 5B only, attached.

Material SWAP provisions are following the OGS direction provided in C47103 – 1B55 attached.

No bond required.

Based on plans dated 3/17/25 and specs dated 1/24/25 including an update in 3/18/25.

Complying with Outline Bar Chart Schedule – Simple Guideline Bar Chart dated 4/21/25 for sequencing.

Complying & guided by baseline CPM Schedule dated 6/5/25. Subject to change by PDC and/or OGS.

Debris to be center piled at the direction of PDC Supervision for removal by others.

U) It is understood and agreed that this Subcontractor must utilize work site Laborers, Workers, and Mechanics who have been certified as having completed a 10 hour OSHA Course in Construction Safety and Health, complying with Labor Law 220-h. Workers are required to comply with local law 196, if it applies on this project, and carry their card as proof.

V) Reporting of Illegal Activity: During the terms of the contract, the Contractor agrees to report any observed or suspected illegal activity of its employees, agents or other third parties, to the Contracting Officer at (518) 474-0201, the Group Director, OGS Legal Services, the State Inspector General or other law enforcement agency. Failure to report criminal conduct associated with the contract awarded by the Office of General Services, will be considered a material breach of the contract and may provide grounds for disqualification of the subject Contractor or Subcontractor for award of future contracts.

W)

22.1 The Group Director, the Comptroller or their representatives shall have the right to examine all books, records, documents, and other data of the Contractor, subcontractors, material-men or suppliers relating to the bidding, pricing, or performance of this Contract or any change or modification thereto for the purpose of evaluating the accuracy, completeness, and currency of the cost or pricing data submitted. This right of examination shall extend to all documents necessary to permit adequate evaluation of the cost or pricing data submitted along with the computations and projections used therein.

SUB	CONT

22.2 The above materials shall be made available at the office of the Contractor, subcontractors, material-men or suppliers at all reasonable times for inspection, audit or reproduction until the expiration of six years from the date of the final certificate for the Contract.

22.3 If this Contract is completely or partially terminated, the records relating to the Work terminated shall be made available for a period of six years from the date of any resulting final settlement.

22.4 Records which relate to the Disputes Clause of this Contract or litigation or the settlement of claims arising out of the performance of this Contract shall be made available until such appeals, litigation or claims have been disposed of.

22.5 The Contractor shall insert a clause containing all of the provisions of Paragraphs 22.1 to 22.4 of these General Conditions in all Subcontracts or Purchase Orders issued hereunder.

22.6 The Contractor shall make available to the Contracting Officer, upon written request, all records required to be kept by this Contract or by Article 3-A of the Lien Law. The failure to provide said records upon the receipt of the written request shall bar any recovery for claimed extra or additional costs under this Contract.

EEO: Contractor will not discriminate against any employee or applicant for employment because of race, creed, color, national origin, sex, age, disability or marital status, will undertake or continue existing programs of affirmative action to ensure that minority ground members are afforded equipment employment opportunities without discrimination, and shall make and document its conscientious and active efforts to employ and utilize minority group members and women in its work force on state contracts. Contractor shall state in all solicitation or advertisements for employees that in the performance of the State contract all qualified applicants will be afforded equal employment opportunities without discrimination because of race, creed, color, national origin, sex, disability or marital status. At the request of the contracting agency, Contractor shall request each employment agency, labor union, or authorized representative will not discriminate on the basis of race, creed, color, national origin, sex, age, disability or marital status and that such union or representative will affirmatively cooperate in the implementation of Contractor's obligations herein. Contractor shall comply with the provisions of the Human Rights Law, all other State and Federal statutory and constitutional non-discrimination provisions. Contractor and subcontractors shall not discriminate against any employee or applicant for employment because of race, creed (religion), color, sex, national origin, sexual orientation, military status, age, disability, predisposing genetic characteristic, marital status, or domestic violence victim status, and shall also follow the requirements of the Human Rights Law with regard to non-discrimination on the basis of prior criminal conviction and prior arrest.

X) It is understood this contract is subject to Prismatic Development Corporation receiving the Owner executed contract and Notice to Proceed.

FURTHER, it is expressly understood and agreed by and between the parties hereto as follows:

1. EXECUTION: This Agreement is signed and executed by a legal representative of the Subcontractor, authorized to bind the Subcontractor, be it individual, partnership or corporation, to all the terms of this Agreement. Should this Agreement, because of the manner of execution, be not legally binding upon the Subcontractor for any reason whatsoever, all work performed under this Agreement shall be performed at the risk of the Subcontractor, and, should this Agreement be voided due to improper execution, the Subcontractor hereby agrees to waive all claims for compensation for work performed.

2. WAIVER: No provisions of this Agreement shall be held to be waived by the Contractor by reason of any act, whatsoever, or in any manner other than by an express waiver thereof, in writing, signed by the Contractor.

3. PLANS, SPECIFICATIONS, ETC.: The entire plans, specifications, addenda, amendments and prime contract documents, if any, as mentioned herein, are made and declared to be a part of this Agreement, and all work performed and materials, equipment and services furnished by the Subcontractor, under this Agreement, must and shall be in strict conformity to, and in full compliance with the provisions of the said plans, specifications, addenda, amendments and prime contract documents. The Subcontractor represents that he has thoroughly examined said plans, specifications, addenda, amendments and prime contract documents, and is fully familiar therewith. In the event of any dispute as to the meaning of any part of said plans, specifications, addenda, amendments and prime contract documents, the same shall be determined by the Contractor, which determination shall be final and binding on the Subcontractor.

4. RIGHTS, OPTIONS, RESPONSIBILITIES, ETC.: The Contractor hereto shall have the same relative rights, options and privileges under this Agreement, as against the Subcontractor hereto, as are secured to the Owner under said plans, specifications, addenda, amendments and prime contract

SUB	CONT

documents, and shall have the right to exercise the same towards the Subcontractor hereto, in the same manner as the said Owner may exercise like rights, options and privileges against the Contractor hereto under said plans, specifications, addenda, amendments and prime contract documents. The Contractor certifies that it has posted a 100 percent (100%) payment and performance surety bond with a responsible surety company guaranteeing, among other things, the payment of all labor and materials furnished in the prosecution of the work provided for in this contract. Accordingly, the Subcontractor does hereby agree that no Municipal or Mechanic's Lien or stop notice shall be filed or maintained against the project involved, whether against the lands or buildings and further agrees in the event that any Municipal or Mechanic's Liens or claims are filed by anyone in relation to the labor and material of the Subcontractor, the Subcontractor agrees, within two (2) days after notice from the Contractor, to institute proceedings for the discharge of such Municipal or Mechanic's Liens and to have the same discharged with five (5) days from the date of filing of the notice, and in the event of the failure of the Subcontractor so to do, the Contractor may cause such Municipal or Mechanic's Liens to be discharged and the expense thereof, including any deposit by the Contractor and the amount of any obligation assumed by the Contractor by bond, indemnify or otherwise, in and about such discharge, as well as its counsel fees in connection therewith, are to be charged to and paid by the Subcontractor. Subcontractor hereby waives and releases all lien or right of lien now existing or that may hereafter arise for work or labor performed or material furnished under this agreement under any lien laws upon the structure in which the Work is being or will be done, the land upon which the same is situated, and upon any money or moneys due or to become due to Contractor, and agrees if so required, to furnish a good and sufficient waiver of lien in form and substance satisfactory to Contractor from any or all persons and corporations furnishing labor or materials under Subcontractor, for the structure and the land upon which the same is situated. The Subcontractor, nevertheless shall have the right to seek payment from the Contractor and/or the bonding company. Further, all liabilities incurred, and obligations assumed, by the Contractor hereto under and by virtue of said plans, specifications, addenda, amendments and prime contract documents, shall, in turn, devolve upon, and be discharged by the Subcontractor hereto, so far as they arise in connection with the work, labor, services or materials to be furnished and delivered under this Agreement, including all general and special conditions, it being understood and agreed that the Subcontractor shall be accountable and responsible to the Contractor hereto in all respects and particulars, to the same extent and in the same manner as the Contractor is accountable and responsible to the said Owner under said plans, specifications, addenda, amendments and prime contract documents.

5. CLAIMS FOR EXTRAS: The Subcontractor shall not claim, and the Contractor shall not pay to the Subcontractor any additional sums of money over and above the amount as stipulated and set forth in this Agreement for any materials, workmen, equipment or services whatsoever to perform the work as specified herein, unless the legally authorized representatives of the Owner certify, in writing, to the Contractor that said claim is beyond the scope and intent of the plans, specifications, addenda, amendments and prime contract documents and the amount of compensation which will be paid by the Owner for said claim, and unless the authorized representative of the Contractor shall direct the Subcontractor, in writing, stipulating the scope of the extra work to be performed and the amount of compensation to be paid by the Contractor for said work, the Subcontractor shall not be entitled to any claim or recovery of any kind hereunder, unless the same shall first be allowed to the Contractor hereto by the Owner. Furthermore, it is specifically understood and agreed that the Contractor has the absolute right, with the approval of the Owner or its authorized representative, to substitute any material of whatever character, nature or description, in place of the specified in the contract documents, provided such material is "equal" to that specified in the plans and specifications which substituted material shall be incorporated into the project by the Subcontractor. Should such substitution result in any savings in cost to the Subcontractor, then and in that event, the Contractor shall be entitled to an equitable credit in a sum to be negotiated between the parties and the Subcontractor hereby agrees that the contract price shall be reduced accordingly. Should it appear that no savings in cost results from such substitution, then and in that event, such materials shall be incorporated into the project at no change in contract price.

6. DELAYS: The Subcontractor shall perform its work so as not to delay hinder or damage the work of others on the job site, and shall repair or pay for any and all damage as determined by the Contractor and shall keep up with the schedule of progress as set up by the Contractor and as may be corrected and modified by Contractor during the course of the work. Further, if the Subcontractor at any time during the progress of said work, neglects or refuses to supply sufficient tools, equipment, workmen, or materials, for any cause whatsoever, as determined by the Contractor, or delays its work and or the work of others as determined by the Contractor, the Contractor, may at its election, provide the same after three (3) days notice, in writing. If, after the service of three (3) day notice, the Subcontractor shall fail to return to work or continues to delay the work, in the opinion of the Contractor, then the said Contractor may complete the work, and the expense thereof as well as any other damages to which the Contractor may be entitled under Section 20 of this Agreement and without limitation thereto shall be deducted from any compensation due the Subcontractor under this Agreement. If the expense of completion exceeds the original contract price, then the Subcontractor shall be liable to the Contractor for such expense including the cost and expense, if any, of collection. The notice in writing herein referred to may be served personally on the Subcontractor or his Agent or mailed by certified mail to the office of the Subcontractor at the address above stated.

7. BONDS: Within five (5) days after the execution of this Agreement and prior to the commencement of work hereunder the Subcontractor shall furnish and deliver to the Contractor, at the Subcontractor's sole cost and expense, separate Performance and Payment Bonds each in the sum of 100% (100 percent) issued by a responsible Surety Company acceptable to the Contractor and approved by the Contractor as to form and substance. Should the Subcontractor fail, neglect or refuse to comply with the provisions of this paragraph, then and in that event, this Agreement, at the option of the Contractor may be cancelled on three (3) days notice in writing to the Subcontractor, who shall be held liable for such damages, if any, as the Contractor may suffer as a result thereof.

8. PROOF OF PAYMENT OF OBLIGATIONS: The Subcontractor, at any time or times prior to completion and acceptance of the project, and with 7 days after request by the Contractor, shall furnish the Contractor evidence in whatever form the Contractor may require that all obligations of persons or firms performing work and/or supplying materials, equipment or services to the Subcontractor as well as all Federal, State and local taxes and obligations of whatsoever kind and character charged to or incurred by the Subcontractor in the performance of his Subcontractor have been met, paid, satisfied or discharged. The Subcontractor at the request of the Contractor shall also be required to furnish to the Contractor a statement under oath setting forth the names and addresses of all persons or firms supplying labor, services, equipment or materials of any nature to the Subcontractor on this project with a clear indication of the amount of money still due and unpaid to such persons or firms.

9. RELEASES: The Subcontractor shall furnish and execute or cause to be executed within seven (7) days after request by the Contractor and in any form designated by the Contractor, releases and acknowledgments of payment from all persons or firms supplying materials or performing work, labor or services of any nature to the Subcontractor as well as releases, requisitions and acknowledgments of payment from the Subcontractor to the Contractor in such form as may be required by the Contractor whether under oath or otherwise.

10. INDEMNIFICATION/HOLD HARMLESS: To the fullest extent permitted by law, the Subcontractor agrees to indemnify, defend and hold harmless the Contractor, the owner, and any other party whom the Contractor has agreed to defend, indemnify and hold harmless, as well as each of their officers, directors, agents, employees and partners (hereafter collectively "Indemnitees") from any and all claims, suits, damages, liabilities, professional fees, including attorneys' fees, costs, court costs, expenses and disbursements related to death, personal injuries or property damage (including loss of use

SUB	CONT

thereof) brought against any of the Indemnitees by any person or entity, arising out of or in connection with or as a result or consequence of the performance of the Work of the Subcontractor, as well as any additional work, extra work or add-on work, whether or not caused in whole or in part by the Subcontractor or any person or entity employed, either directly or indirectly by the Subcontractor including any subcontractors thereof and their employees. The parties expressly agree that this indemnification agreement contemplates 1) full indemnity in the event of liability imposed against the Indemnitees without negligence; and 2) partial indemnity in the event of any actual negligence on the part of the Indemnitees either causing or contributing to the underlying claim which negligence is expressly excepted from the Subcontractor's obligation to indemnify. Attorneys' fees, court costs, expenses and disbursements shall be defined without limit to include those fees, costs, etc. incurred in defending the underlying claim and those fees, costs, etc. incurred in connection with the enforcement of this Subcontract Agreement. Indemnification under this Agreement shall operate whether or not Contractor has placed and maintained the insurance required under this agreement. The Subcontractor shall cause all subcontract agreements it enters into to include this indemnification clause so as to ensure that Contractor and all Indemnitees hereunder shall have the same protection from sub-subcontractors as is afforded by the Subcontractor.

11. RETAIN SUFFICIENT FUNDS: The Subcontractor hereby authorizes the Contractor to retain sufficient funds, in addition to retainage withheld until final completion and acceptance of the work, to satisfy any claims, debts, or obligations arising out of the work performed by the Subcontractor hereunder for the labor, materials or equipment supplied therefore of which the Contractor has knowledge. Said funds are to be released upon, receipt by the Contractor of sufficient evidence in whatever form the said Contractor may require that the claim, debt or obligation has been met, paid, satisfied or discharged, and the Contractor will be held harmless from any manner of debt, claim, dispute or lien arising out of the performance of this Subcontract.

12. NON-COMPLIANCE: The Contractor further reserves the right to withhold all or any part of partial payments, in addition to retained percentage withheld, until final completion, due to the Subcontractor, for non-compliance with any of the terms of this Agreement, and the same shall be withheld until such time as said non-compliance has been corrected to the satisfaction of the Contractor.

13. NON-ASSIGNABLE: This Agreement, or any part thereof, or any monies now due or which may hereafter become due, shall not be assigned, transferred, or sublet by the Subcontractor, nor shall the Contractor be liable to any assignee, transferee, or sublessee, without the written consent of the Contractor, and no such written consent shall release the Subcontractor from any obligation hereunder. The Subcontractor shall submit for the approval of the Contractor the name or names of all persons, companies, or corporations to whom it intends to sublet or subcontract any of its work, as well as copies of proposed contracts between the said Subcontractor and such persons, companies and corporations, and the Contractor reserves the right to disapprove of any such person, company or corporation for whatever reason it determines sufficient. The approval of the Contract Form and/or such person, company or corporation to whom the Subcontractor intends to sublet a part or parts of its contract, shall not under any circumstances constitute a contractual relationship between such party and the Contractor and no payment shall be made to the Subcontractor for any work performed by any such person, company or corporation who has not been approved in writing by the Contractor.

14. LABOR CONDITIONS: The Subcontractor agrees to comply with and conform to all labor conditions and practices prevalent in the area in which the work is to be performed, subject to all Federal and State laws, rules and regulations, and further agrees that only mechanics skilled in their trades shall be employed in the execution of the work to be performed under this Agreement. The Contractor, may at its option, require the Subcontractor to discharge any incompetent or undesirable employee and the Subcontractor hereby agrees to comply with such directive.

15. GENERAL CONTRACTORS RIGHT TO TERMINATE: If the Subcontractor neglects to carry out the Work in accordance with the Contract Documents and in a good and workmanlike manner, without delays, or fails to complete the Work by the Completion Date, or is in default in the performance of any term or condition of the Contract Documents, then the General Contractor may, at its option, without prejudice to any other right or remedy, terminate this Subcontract upon not less than three (3) days' written notice to the Subcontractor and its surety, if any. The General Contractor may then take possession of all materials, tools and equipment and employ such means as it deems necessary to complete the Work. In such case, the Subcontractor shall not be entitled to receive any further payment until the Work has been completed. If the unpaid balance of the Subcontract Sum exceeds the actual cost of completing the Work, including liquidated damages and all other recoverable damages, the excess shall be paid to the Subcontractor. If the actual cost exceeds the unpaid balance, the Subcontractor and/or its surety, if any, shall pay the difference to the General Contractor. This obligation shall survive the termination of the Subcontract. The General Contractor may also terminate this Subcontract at any time, in whole or in part, for its own conveniences and without cause, if the General Contractor determines it is in its own best interest to do so. In such case, the Subcontractor shall only be entitled to payment for that portion of the Work actually performed prior to said termination. In the event that a termination by the General Contractor of this Subcontract for cause is ultimately determined to be improper for any reason, it shall then be treated as termination for convenience as set forth hereinabove. In no event shall Subcontractor be entitled to recover profit with respect to work that is unperformed at the time of termination.

15A. GENERAL CONTRACTORS SPECIAL RIGHT TO TERMINATE: In the case of m/w/d/s/be Subcontract the Contractor reserves the right to terminate said Subcontract at any time during the course of the work that the Subcontractor loses its 'special' status, or if for any reason Contractor is unable to claim full credit for said special Subcontract under the terms of the Contract Documents, in this case Subcontractor will be entitled only to payment for work performed to the date of termination. In no event shall Subcontractor be entitled to recover profit with respect to work that is unperformed at the time of termination.

16. STORAGE OF MATERIALS: All materials on the job site to be used in the performance of the work under this Subcontract shall be stored by the Subcontractor in a safe, secure and proper manner and the Subcontractor shall assume full and absolute responsibility for the safety and protection of same. Any loss incurred shall be the responsibility of the Subcontractor, regardless of circumstances, and shall be replaced by the Subcontractor immediately upon notification by the Contractor, and at no additional cost to the Contractor regardless of whether payment for said materials has been made to the Subcontractor by the Contractor. Further, any materials or equipment delivered and stored on the job site by the Subcontractor or its subcontractors or suppliers, for incorporation into the work shall not be removed from the job site without the written consent of the Contractor. The Subcontractor shall not be entitled to requisition payment for such materials stored on the job site unless and until same is incorporated into the project and approved for payment by the Contractor. The responsibility of the Subcontractor for materials used by itself shall continue in full force and effect even after such materials are incorporated into the project and accepted by the owner. The acceptance of the project shall in no way be deemed to relieve the Subcontractor of his responsibility in connection with his workmanship or the quality of the materials, which shall survive the acceptance and continue in full force and effect as set forth in the prime contract documents to like extent as the responsibility of the Contractor continues to the Owner.

17. MATERIALS, SAMPLES, ETC.: Samples of all materials to be incorporated into the job and shop drawings, if required, shall be submitted to the Contractor as directed for approval within the time schedule called for by the Contractor. All materials, supplies or equipment to be furnished by

SUB	CONT
CH	TM

Subcontractor and installed or incorporated in the Work shall be free from the rights of vendors under conditional bills of sale, chattel mortgages or any other encumbrances of any kind and nature whatsoever, and upon delivery thereof at the site of the Work, title thereto shall pass immediately to the Owner, free from all liens and encumbrances and subject only to the right of the Subcontractor and/or Contractor to utilize the same in completing the Work. Subcontractor hereby warrants good title to all materials, supplies or equipment installed or incorporated in the Work.

18. PAYMENT OF TAXES: The Subcontractor agrees to assume all responsibility for the payment of any and all taxes of whatsoever kind and character including all Federal, State and Municipal taxes, withholdings and contributions whether measured by the salaries or wages of any of its employees or otherwise including but not limited to all sales and use taxes, if any, which taxes withholdings and contributions are all specifically included as part of the Subcontractor's price for the performance of this contract. The Subcontractor agrees to promptly pay all of such Federal, State and Municipal taxes, withholdings and contributions and to furnish documentary evidence of such payment to the Contractor whenever so requested. The Subcontractor further agrees to indemnify, save and hold harmless the Contractor for any claim or claims for payment which may be assessed against the Subcontractor under authority of the rules, statutes and laws of the Federal and State Governments under which the work described in this Agreement is to be performed. Further, for the work to be performed, the Subcontractor agrees (if not already qualified to make immediate application to become a registered employing unit under the Unemployment Compensation Act of the State where the work hereunder is to be performed for the duration of this Agreement and in every respect to comply with and conform to all the rules, regulations and laws of the United States of America and the State where the work hereunder is to be performed. If the Subcontractor is not required to pay or bear the burden or obtains a refund or drawback, in whole or in part of any Federal or State tax, duty, interest, or penalty which is included in the contract price pursuant to the terms of this Agreement then and in the event the contract price shall be correspondingly decreased. The Contractor shall be privileged to deduct the amount of such decreases from monies due or to become due to the Subcontractor including monies represented by the retainage. This provision shall survive the contract and should the Subcontractor receive any benefit or benefits from a refund, drawback, or tax waiver of any kind or character, Federal or State, subsequent to the final completion and acceptance of this Contract and the release of all retained monies, then and in that event the Subcontractor shall be obliged to pay to the Contractor within three (3) days after receipt of such refund, drawback, or tax waiver the amount thereof by mailing the same by registered mail to the principal office of the Contractor at 60 Route 46, Fairfield, New Jersey 07004.

19. INSURANCE POLICIES:

A. The Subcontractor shall take out pay for and carry policies of contingent liability insurance and general liability insurance which shall be in amounts and form as listed in Article B below in companies approved by and satisfactory to the Contractor, and the Subcontractor shall comply in all respects with the laws of the state where the work hereunder is to be performed, relating to compensation for accidental injuries or death suffered in the course of employment. Should the Subcontractor fail, neglect or refuse to comply with the provisions of this paragraph, then and in that event, the Contractor, at its opinion, may cancel and annul this Agreement holding the Subcontractor responsible for such damages as may be incurred thereby or, in the alternative, at its option may secure such insurance as may be necessary to meet its requirements, charging the cost thereof to the Subcontractor and reimbursing itself for such cost out of the funds due to the Subcontractor under the terms of its agreement.

B. Insurance Requirements

The Subcontractor shall purchase and maintain insurance of the following types of coverage and limits of liability:

Commercial General Liability (CGL) coverage with limits of Insurance of not less than $2,000,000 each occurrence and $4,000,000 Annual Aggregate.

a) If the CGL coverage contains a General Aggregate Limit, such General Aggregate shall apply separately to each project.
b) CGL coverage shall be written on ISO Occurrence form CG 00 01 10/01 or a substitute form providing equivalent coverage and shall cover liability arising from premises, operations, independent contractors, products-completed operations, residential projects (if applicable) and personal and advertising injury.
c) Contractor, Owner and all other parties who Contractor is required to name as additional insureds by any contract, shall be included as insureds on the CGL, using ISO Additional Insured Endorsement CG 20 10 (11 85) or a combination of CG 20 10 (10 01) & CG 20 37 (10 01), or an endorsement providing equivalent or broader coverage to the additional insureds. The coverage provided to the additional insureds under the policy issued to the Subcontractor shall be at least as broad as the coverage provided to the Subcontractor under the policy. Coverage for the additional insureds shall apply as primary and non-contributing insurance before any other insurance or self-insurance, including any deductible, maintained by, or provided to, the additional insureds.
d) Subcontractor shall maintain CGL coverage for itself and all additional insureds for the duration of the project and maintain Completed Operations coverage for itself and each additional insured for at least 3 years after completion of the Work.
e) CGL coverage shall not have exclusions for residential projects, territorial limitations, bodily injury to employees, work at heights or any other exclusion deemed unacceptable to the Contractor.

Automobile Liability

a) Business Auto Liability with limits of at least $2,000,000 each accident.
b) Business Auto coverage must include coverage for liability arising out of all owned, leased, hired and non-owned automobiles.
c) Contractor, Owner and all other parties required of the Contractor, shall be included as insureds on the auto policy.

Commercial Umbrella

a) Umbrella limits must be at least $10,000,000.
b) Umbrella coverage must include as insureds all entities that are additional insureds on the CGL.
c) Umbrella coverage for such additional insureds shall apply as primary and non-contributing insurance before any other insurance or self-insurance, including any deductible, maintained by, or provided to, the additional insured other than the CGL, Auto Liability and Employers Liability coverages maintained by the Subcontractor.
d) Umbrella coverage shall not have exclusions for residential projects, territorial limitations, bodily injury to employees, work at heights or any other exclusion deemed unacceptable to the Contractor.

Workers Compensation and Employers Liability

a) Employers Liability Insurance limits of at least $2,000,000 each accident for bodily injury by accident and $2,000,000 each employee for injury by disease.

SUB	CONT

b) Where applicable, U.S. Longshore and Harborworkers Compensation Act Endorsement shall be attached to the policy.
c) Where applicable, the Maritime Coverage Endorsement shall be attached to the policy.

Additional Marine/Specialty Insurance, if applicable

a) Pollution/Environmental Liability with limits of $2,000,000. per occurrence and $4,000,000. Aggregate, if applicable.
b) Marine Protection and Indemnity with limits of $1,000,000. per occurrence and $2,000,000. Aggregate, if applicable.
c) Collision Liability/Towers Liability with limits of $2,000,000. per occurrence and $4,000,000. Aggregate, if applicable.
d) Marine Pollution Liability with a limit of $1,000,000. per occurrence.

Waiver of Subrogation – Subcontractor waives all rights against Contractor, Owner and Architect and their agents, officers, directors and employees for recovery of damages to the extent these damages are covered by commercial general liability, commercial umbrella liability, business auto liability or workers compensation and employers liability insurance maintained per requirements stated above. Subcontractor's Workers Compensation policy has WAIVER OF OUR RIGHT TO RECOVER FROM OTHERS ENDORSEMENT with Contractor, Owner and Architect listed on SCHEDULE.

Notice of Cancellation – The required insurance policies shall contain a provision that coverage afforded under the policies will not be canceled or allowed to expire until at least 30 days prior written notice has been given to the Contractor.

The Subcontractor shall not sublet any part of its work without written approval from the Owner or Contractor. The Subcontractor shall not sublet any part of its work without assuming full responsibility for requiring similar insurance from its subcontractors and shall submit satisfactory evidence to that effect to the Contractor. Each such insurance policy of the sub-subcontractor, except the Workers Compensation Policy, shall include the Owner, the Contractor and all other parties who Contractor is required to name as additional insureds by any contract as an additional insured.

Prior to commencing the work, the Subcontractor shall submit to the Contractor a certificate of insurance, a copy of the Additional Insured Endorsement and a copy of the applicable Other Insurance clause that is part of the Subcontractor's Commercial General Liability Policy. A copy of the entire Commercial General Liability policy with all endorsements shall be submitted to the Contractor when requested.

20. TIME OF THE ESSENCE: Time of completion on the part of the Subcontractor is a most absolute consideration and is to be considered the essence of this Agreement. The Subcontractor shall commence work whenever so directed in writing by the Contractor and shall continue diligently to perform such work until completion or as may be directed by the Contractor in pursuance to its construction and progress schedule as may be corrected and modified by the Contractor during the course of the work. The Subcontractor shall commence work at such place or places as may be directed in writing by the Contractor and shall continue to pursue such continuity and progress schedule as may be determined by the Contractor as herein above indicated. Should the Subcontractor fail, neglect or refuse to maintain its schedule or work as required by the Contractor, causing a delay in the construction of the project as a result thereof then and in that event the Subcontractor shall be liable in damages to the Contractor for such delay, including but not necessarily limited to charges which may be incurred by the Contractor directly or indirectly under the terms of its Contract. The fact that the Contractor has furnished the Owner with a progress schedule at variance with the construction and progress schedule furnished or to be furnished to the Subcontractor shall in no way whatsoever be deemed evident as between the parties hereto and shall have no bearing whatsoever on the progress of the work to be performed by the Subcontractor as herein referred to. The Subcontractor shall perform his work solely in accordance with the construction and progress schedule furnished to him by the Contractor, which may be modified, corrected, changed, altered, or amended by the Contractor from time to time and by no other schedule whatsoever, it is distinctly understood that there shall be no right of recovery on the part of the Subcontractor against the Contractor for any damages caused by delays in the construction of the project irrespective of the cause or reasons therefore and irrespective of the fact that the Contractor may have changed, modified, corrected, altered or amended the construction or progress schedule from time to time, providing, however that where the progress of the job is unduly delayed for causes or reasons directly and solely attributable to the Contractor, then and in that event, the only remedy available to the Subcontractor for such delays shall be a reasonable extension of time to be described by the Contractor.

21. EXECUTION OF FORMS: The Subcontractor agrees to execute and deliver to the Contractor such form or forms as may be determined by the Contractor including but not necessarily limited to (1) certified copies of payrolls (2) Subcontractors Status Reports (3) Subcontractors Cost Reports (4) such other forms as the Contractor may determine voluntary in order to maintain an accurate record of costs and work progress until the final completion and acceptance thereof in addition to the execution and delivery of the forms herein referred to the Subcontractor may also be required upon the request of the Contractor to furnish such proof and documentation evidence as the Contractor may require in order to substantiate and corroborate the information contained in the forms aforementioned.

22. PAYMENT BREAKDOWN: The Subcontractor agrees to furnish the Contractor prior to starting of any work, a complete itemized breakdown of the contract price as set forth in this Agreement, satisfactory to and subject to the approval of the Contractor, for the purpose of preparing monthly progress payments. Said Contract Payment Breakdown, in satisfactory form, shall be furnished to the Contractor within five (5) days after the execution of this Contract, and the failure or neglect of the Subcontractor to do so may at the option of the Contractor result in (a) cancellation of this contract and the Subcontractor may become liable for such damages as the Contractor may sustain as a result of the Subcontractors failure to comply with the requirements herein sustained or (b) in the alternative no payment whatsoever shall become due and payable to the Subcontractor unless and until a satisfactory Contract Payment Breakdown has been furnished to the Contractor and approved by it.

23. RETAINAGE AND PAYMENTS: In consideration of the faithful performance by the Subcontractor, of the covenants and conditions in this Agreement, the Contractor agrees to make monthly partial payments of approximate estimates of the amount of work completed and materials, equipment and services furnished each month, less ~~10~~ percent retainage, unless the Subcontractor has provided a Performance & Payment Bond, then 5 percent applies to insure the faithful completion of this Agreement, on or about the 30th day of the ensuing month, provided, however, that all labor and material delivered to the job, and all taxes have been paid by the Subcontractor, and provided that the Contractor has on each such date been paid by the Owner. The reserve percentage is to be withheld by the Contractor until the said Contractor has received final completion, acceptance and payment by the Owner for the entire job. Further, the Subcontractor must submit said estimates to the field representative of the Contractor on or before the 25th day of each month of the month for which the estimate is submitted, for the approval of said field representative, before any said monthly partial payments shall be made. As a condition precedent to any payment due the Subcontractor, it shall deliver to the Contractor a release from all of its Subcontractors and Materialmen, in form satisfactory to the Contractor, as well as an affidavit as to all unpaid materialmen, labor, etc., incurred or to be incurred by the Subcontractor. Progress payments shall not be considered an acceptance of any work of the Subcontractor; the entire work being subject to final approval and inspection of the Contractor and the Owner upon completion, pursuant to the prime contract documents.

2.0

SUB	CONT

24. CONTRACT ACCEPTED IN NEW JERSEY: This contract shall not be binding upon the Contractor unless or until the same is actually accepted and signed by an executive officer authorized so to sign at the office of the Contractor located at 60 Route 46, Fairfield, New Jersey. As the project itself is in the City of New York and the contract between Contractor and Owner, which the Subcontractor is also bound to, is subject to the laws of the State of New York, accordingly the laws of the State of New York shall control this Subcontract Agreement.

25. SUBCONTRACTOR'S KNOWLEDGE: It is distinctly understood and declared by the Subcontractor that this Agreement is executed by the said Subcontractor for the consideration herein named, solely on the knowledge and information of the Subcontractor, derived from sources other than the Contractor, its agents or officers of the nature and information of the work to be performed and the means of access thereto. The Subcontractor herein declares that it has investigated all pertinent conditions relative to the performance of the work contained in this Agreement and having satisfied itself enters into the Agreement knowing the character, quantities and sources of materials to be used in performing the work, the labor conditions prevalent in the area in which the work is to be performed and has familiarized itself with all the data necessary to complete the work as stipulated in this Agreement.

26. SERVICE OF NOTICES: All notices which are required to be served under provisions of this Agreement may be served upon the designated authorized representative of the Subcontractor, or upon the Subcontractor, by mailing the same, addressed to the address appearing on the face of this Agreement.

27. CORRECTION OF DEFECTS: The Subcontractor shall, at the request of and in a manner acceptable to the Contractor, correct any defects due to faulty materials or workmanship which appears within a period of one year following final acceptance and completion of the project. The Subcontractor, upon receipt of notice in writing from the Contractor shall forthwith remove all materials and take down and remove and dismantle all condemned materials from the job site and rebuild all portions of the work which may be declared to be faulty or not in accordance with the plans, specifications, amendments, addenda and prime contract documents in all instances where the Contractor may be so advised by the Owner, or Architect, for which the work hereunder is to be performed. Under such circumstances, Subcontractor's rework, including the cost of all new materials and equipment, if necessary, shall be performed by such Subcontractor at no extra cost to the Contractor. The Subcontractor is completely responsible for all of its materials or installations for the duration of the entire job, until such time as it is formally and finally accepted by the Contractor and the Owner, in addition to the Subcontractor's duty of strict compliance with all of the other requirements of the prime contract documents relating to materials, installation and workmanship.

28. WARRANTEES AND GUARANTEES: All Subcontractor's, Manufacturers or Suppliers' warrantees and guarantees, expressed or implied, respecting any material or equipment used in or incorporated in the work, shall be deemed obtained by the Subcontractor for and in behalf of the Contractor, and the Subcontractor, if so directed by the Contractor, shall require such Manufacturers or Suppliers to execute such warrantees and guarantees in writing directly to the Contractor or Owner, as may be directed by the Contractor.

29. DEDUCTIONS FOR UNCORRECTED WORK: If the Contractor is required to allow an equitable deduction of the contract price to the Owner because it may be deemed inexpedient to correct any work not performed in accordance with the contract, then and in that event, the Contractor shall be privileged to make an equally equitable deduction from the amount due the Subcontractor for the failure to perform as aforementioned.

30. DEFINITIONS: Wherever the term "Contract Documents" or the term "Prime Contract Documents" appears in this Agreement, the same is intended to mean the Contract as well as all other documents, contracts and agreements executed or about to be executed by and between the Contractor and the Owner. A specimen copy of the contract, as well as other such documents, contracts and agreements herein referred to , is on file at the office of the Contractor and may be examined at all reasonable business hours.

31. COMPLETE AGREEMENT: This contract contains the complete agreement between the parties and may not be changed, amended or modified in any way except by agreement in writing between the parties hereto.

32. SUPERVISION AND DEVIATION: The Subcontractor agrees to give his personal attention to the work, labor and services to be performed under this Agreement and shall at all times maintain a competent supervisor at the job site subject to the approval of the Contractor to supervise the work on behalf of the Subcontractor. The Subcontractor shall immediately after execution of this Agreement, designate in writing, an official representative of the Subcontractor who will have full authority to act on any and all matters pertaining to the work to be performed under this Subcontract and whose acts shall be binding upon the Subcontractor to the fullest extent. Should the Contractor determine that the Subcontractor's supervisor is not satisfactory, for any reason whatsoever, then, and in that event, the Contractor has the unqualified right to direct the Subcontractor, in writing, to discharge such supervisor within seventy-two (72) hours and the Subcontractor does hereby agree to comply with such written directive and to furnish another supervisor who shall likewise be cloaked with full authority to act for and in behalf of the Subcontractor. Should the Subcontractor, through the direction of its supervisor or otherwise deviate in any way from the strict requirements of the plans, specifications, amendments, addenda or prime contract documents or make any installation or perform any work, labor or services contrary to the requirements of such plans, specifications, amendments, addenda or prime contract documents without first obtaining the written consent and approval of the Contractor, such deviation shall be at the sole peril and risk of such Subcontractor who may then be required to remedy such deviation or conflict to the complete satisfaction of the General Contractor and the Owner at no cost whatsoever to the General Contractor, which remedial work shall be done within a time schedule as may be directed by the General Contractor in order to preclude any dislocation of its production schedule.

33. SUBCONTRACTOR INSOLVENCY: In addition to the other rights as contained herein, if the Subcontractor should be adjudicated a bankrupt, insolvent or placed in receivership, or should proceedings be instituted by or against the Subcontractor for bankruptcy, insolvency, receivership, agreement of composition or assignment for the benefit of creditors, or if this subcontract or the interest of the subcontract hereunder passes to another by virtue of any court proceedings, writ of execution, levy, sale or by operation of law, the Contractor may, if the Contractor so elects at any time hereafter, terminate this subcontract upon giving to the Subcontractor or to any trustee, receiver, assignee or any other person in charge of or acting as custodian of the assets or property of the Subcontractor five (5) days notice in writing of the Contractor's intention to do so. Upon the giving of such notice, this subcontract shall end on the date fixed in such notice and the Contractor may take possession of the premises, and all the materials, tools and appliances thereon, and finish the work itself or through others by whatever method it deems expedient. In such event the Subcontractor shall not be entitled to receive any further payments until the work is finished. If the unpaid balance of the Subcontract price shall exceed the expenses of finishing the work, including compensation for additional managerial and administrative services, such excess shall be paid to the Subcontractor. If such expenses shall exceed such unpaid balance, the Subcontractor shall pay the difference to the Contractor.

34. CLEAN UP: The Subcontractor agrees to keep the job site clean of all rubbish, debris, scrap material and refuse caused or created by the Subcontractor and to remove same from the job site as soon as possible upon request of the Contractor, this also includes obligation of Subcontractor to

SUB	CONT
CH	

keep all buildings clean as herein indicated. Should the Subcontractor fail, refuse or neglect to clean up as directed within twenty-four (24) hours after notice from the Project Superintendent then, and in that event, the Contractor at its option may perform such clean up service and back-charge the same to the Subcontractor and reimburse itself for such back-charge from the next payment due to the Subcontractor. Furthermore, the Contractor at its option may cancel and annul this Agreement on failure of the Subcontractor to comply with the provisions of this paragraph.

35. COVENANT AGAINST CONTINGENT FEES: The Subcontractor covenants, warrants, and represents that he has not paid any fee, commission, bonus or other consideration to any person, persons, company or corporation for securing this subcontract, other than a fee, commission or consideration paid in the normal course of business to an established bona fide company engaged in such business or full time employee in the employ of the Subcontractor in its normal and usual course of business. Breach of this representation shall entitle the Contractor to deduct from the contract price the full amount of such fee, commission or other consideration, or at its option, the Contractor may cancel and annul this agreement holding the Subcontractor liable for such damages as it may sustain as a result thereof.

36. The Subcontractor agrees that it will not commence any action, whether at law or at equity, against the Contractor, or the sureties on the performance and/or payment bond, if any, given by the Contractor to the Owner because of any matter whatsoever arising out of the alleged breach of performance of this agreement, in the courts of any state other than the State of New York. It is further agreed that if any action shall be brought in the courts of the State of New York, such action shall be commenced only in the venue of the City of New York. The rights herein given the Contractor shall also be deemed for the direct benefit of the aforesaid sureties, if any, with the same force and effect as if they were parties herein. Any action must be brought within the time limited for the bringing of actions by the Contractor against the Owner as set forth in the General Contract Documents.

37. The Subcontractor shall conform to and comply with all Federal, State and local laws, rules and regulations concerning occupational health and safety including, without limitation, the requirements of the Contract Documents and the rules and regulations of the Occupational Safety & Health Act of 1970 and the Occupational Safety & Health Standards promulgated there under.

The Subcontractor further agrees to indemnify and hold the Contractor harmless from any and all costs, expenses, fines and penalties (including reasonable attorneys' fees) that may be incurred by the Contractor as the result of the Subcontractor's non-compliance with this subparagraph.

38. SPECIFIC CLAUSE FOR M/W/D/S/BE SUBCONTRACTORS:
A. Subcontractor agrees to immediately notify Contractor of any changes to it's status as a M/W/D/S/BE. Failure to do so will be a breach of this Subcontract Agreement.

B. Subcontractor has represented that it has been and currently is certified as an MBE, DBE, WBE, SBE, SDVOB or Emerging Business Enterprise under the program for certification applicable to and specifically identified in the plans, specifications, addenda, amendments and prime contract documents (the "Contract Documents"). Subcontractor has represented and agreed that it shall take all steps necessary to allow Contractor to comply with the Contract Documents with respect to MBE, DBE, WBE, SBE, SDVOB or Emerging Business Enterprise requirements of the Contract Documents, including providing all forms, reports, certifications or other requirements stated therein or applicable thereto. Subcontractor represents and agrees that it will perform its obligations in a manner that will allow Contractor to credit the Subcontractor's services, materials and/or equipment as applicable toward the achievement of goals for MBE, DBE, WBE, SBE, SDVOB or Emerging Business Enterprise requirements as stated in the Contract Documents or otherwise applicable. Subcontractor specifically represents and agrees that:

- it will provide and actual service other than acting as an intermediary between a supplier and a customer;
- it will perform a "commercially useful function" as defined in 49 CPR § 26.55 and/or NYC Local Law 1 (2013); and
- otherwise performs a valuable service that qualifies for counting toward goals stated in the Contract Documents.

Subcontractor agrees that it will be responsible for and will actually perform, manage and supervise the work covered by this Subcontract and agrees that it will not sub-subcontract a significantly greater portion of the work than would be expected on the basis of normal industry practices. Subcontractor certifies that it has the technical capability and adequate resources to perform the work covered by this Subcontract. Subcontractor agrees to prepare and submit all sub-tier subcontracts and material contracts to Contractor for approval. Contractor reserves the right to review and reject any and all sub-subcontracts, equipment leases and/or use of other Contractor's personnel entered into between Subcontractor and third parties that do not conform or comply with the provisions of this section, the terms of the Contract Documents or the requirements of the Owner. Neither the approval of nor the failure on the part of Contractor to reject such arrangements shall relieve the Subcontractor of any of its obligations under this agreement. In the event it is determined that the Subcontractor fails to qualify as a MBE, DBE, WBE, SBE, SDVOB or Emerging Business Enterprise and/or fails to perform its obligations in a manner that will allow Contractor to credit the Subcontractor's services, materials and/or equipment as applicable toward the achievement of goals for MBE, DBE, WBE, SB, SDVOB or Emerging Business Enterprise requirements as stated in the Contract Documents, such as by allowing its certification to lapse or be revoked or by failing to perform a "commercially useful function," or to otherwise comply with the Contract Documents or other requirements applicable to the Subcontractor's Work, the Contractor shall have the right to terminate the Subcontract, without penalty or liability, and Contractor may recover from Subcontractor any damages Contractor may suffer as a result of Subcontractor's failure to perform its obligations in a manner that will allow Contractor to credit the Subcontractor's services, materials and/or equipment as applicable toward the achievement of goals for MBE, DBE, WBE, SBE, SDVOB or Emerging Business Enterprise requirements as stated in the Contract Documents. Such remedy shall be in addition to any other remedy available to Contractor hereunder.

SUB	CONT
CH	

39. This Contract consists of the following pages: 1, 2, 3, 4, 5, 6, 7, 8, 9, 10, 11, 12, 13 "Supplemental Provision for non-MWBE Subcontract", and Attachment 1 "Outline Bar Chart Schedule" Attachment 2 "OGS Three Bid Waiver and Proposal".

WITNESS:

.....

SEAL

Elli NY Design Corp.
(Subcontractor)

By .....

Name & Title Lissette Olivo Chief Executive officer

Date 8/21/2025

WITNESS:

.....

SEAL

PRISMATIC DEVELOPMENT CORPORATION
(Contractor)

By Michael Vetri

Name & Title MICHAEL VETRI, V. PRES.

Date 9/2/25

SUB	CONT

SUPPLEMENTAL PROVISION FOR NON-MWBE SUBCONTRACT

Pursuant to the prime contract, Prismatic is required to employ good faith efforts to achieve 30% participation for minority and women-owned business enterprises ("MWBE"s & SDVOB) inclusive of 15% participation by minority-owned business enterprises ("MBE"s) and 15% participation by women-owned business enterprises ("WBE"s) (the "Goals"). Pursuant to the contract and the law Prismatic may be subject to severe penalties, including but not limited to, liquidated damages, direct damages, consequential damages and other sanctions that may negatively affect Prismatic's ability to conduct business with public entities.

Subcontractor agrees, in addition to any nondiscrimination provision of the prime contract and at no additional cost to Prismatic to fully comply and cooperate with Prismatic and the Owner in implementation of these Goals and all requirements of New York State Executive Law 15 –A and 5 NYCRR Parts 142-144 ("MWBE Regulations").

Subcontractor has represented to Prismatic that Subcontractor will meet the stated Goals by employing 30% MWBE & SDVOB subcontractors and/or suppliers, all of whom shall add value to the work and perform a commercially useful function as appropriate, inclusive of 15% MBE, 15% WBE and 6% SDVOB participation in Subcontractor's portion of the work. Subcontractor acknowledges that Prismatic has relied upon such representations in awarding this Subcontract to Subcontractor and that achievement of such Goals is an express condition of this Subcontract.

It shall be Subcontractor's obligation to submit acceptable utilization plans and programs and to demonstrate to the satisfaction of Prismatic, the Owner and any cognizant agency that Subcontractor has achieved such Goals with subcontractors and suppliers who will have added value to the project or will have performed a commercially useful function as applicable and in accordance with the MWBE & SDVOB Regulations.

If Subcontractor fails to achieve the stated Goals, it shall be the sole obligation of Subcontractor to demonstrate to the satisfaction of Prismatic, the Owner and any cognizant agency that Subcontractor has exercised good faith efforts, all in accordance with the MWBE & SDVOB Regulations.

The failure of the Subcontractor to achieve the stated Goals and/or to demonstrate to the satisfaction of Prismatic, the Owner and any cognizant agency that that it has exercised good faith efforts shall be a material breach of the Subcontract.

Subcontractor shall defend, indemnify and hold Prismatic harmless from any and all expenses, claims, penalties, liquidated damages or other consequences related to the failure by Subcontractor to achieve the stated Goals for MWBE, MBE, WBE & SDVOB participation and/or from the failure of Subcontractor to demonstrate to the satisfaction of Prismatic, the Owner and/or any cognizant entity that Subcontractor has exercised good faith efforts in accordance with the MWBE & SDVOB Regulations and Prismatic shall be permitted to withhold sufficient funds from progress payments to protect itself in such regard.

SUB	CONT

ATTACHMENT 1
OUTLINE BAR CHART SCHEDULE

See Next Page for Attachment

SUB	CONT


PRISMATIC DEVELOPMENT CORPORATION

4/21/2025

P187 CREEDMOOR PSYCH -Prelim SUMMARY SCHEDULE 3/24/25 UPDATED

FLIPPED VIEW

NOTE: dates are start dates - date we start renovation and date of the start of the 25 day check OGS check out

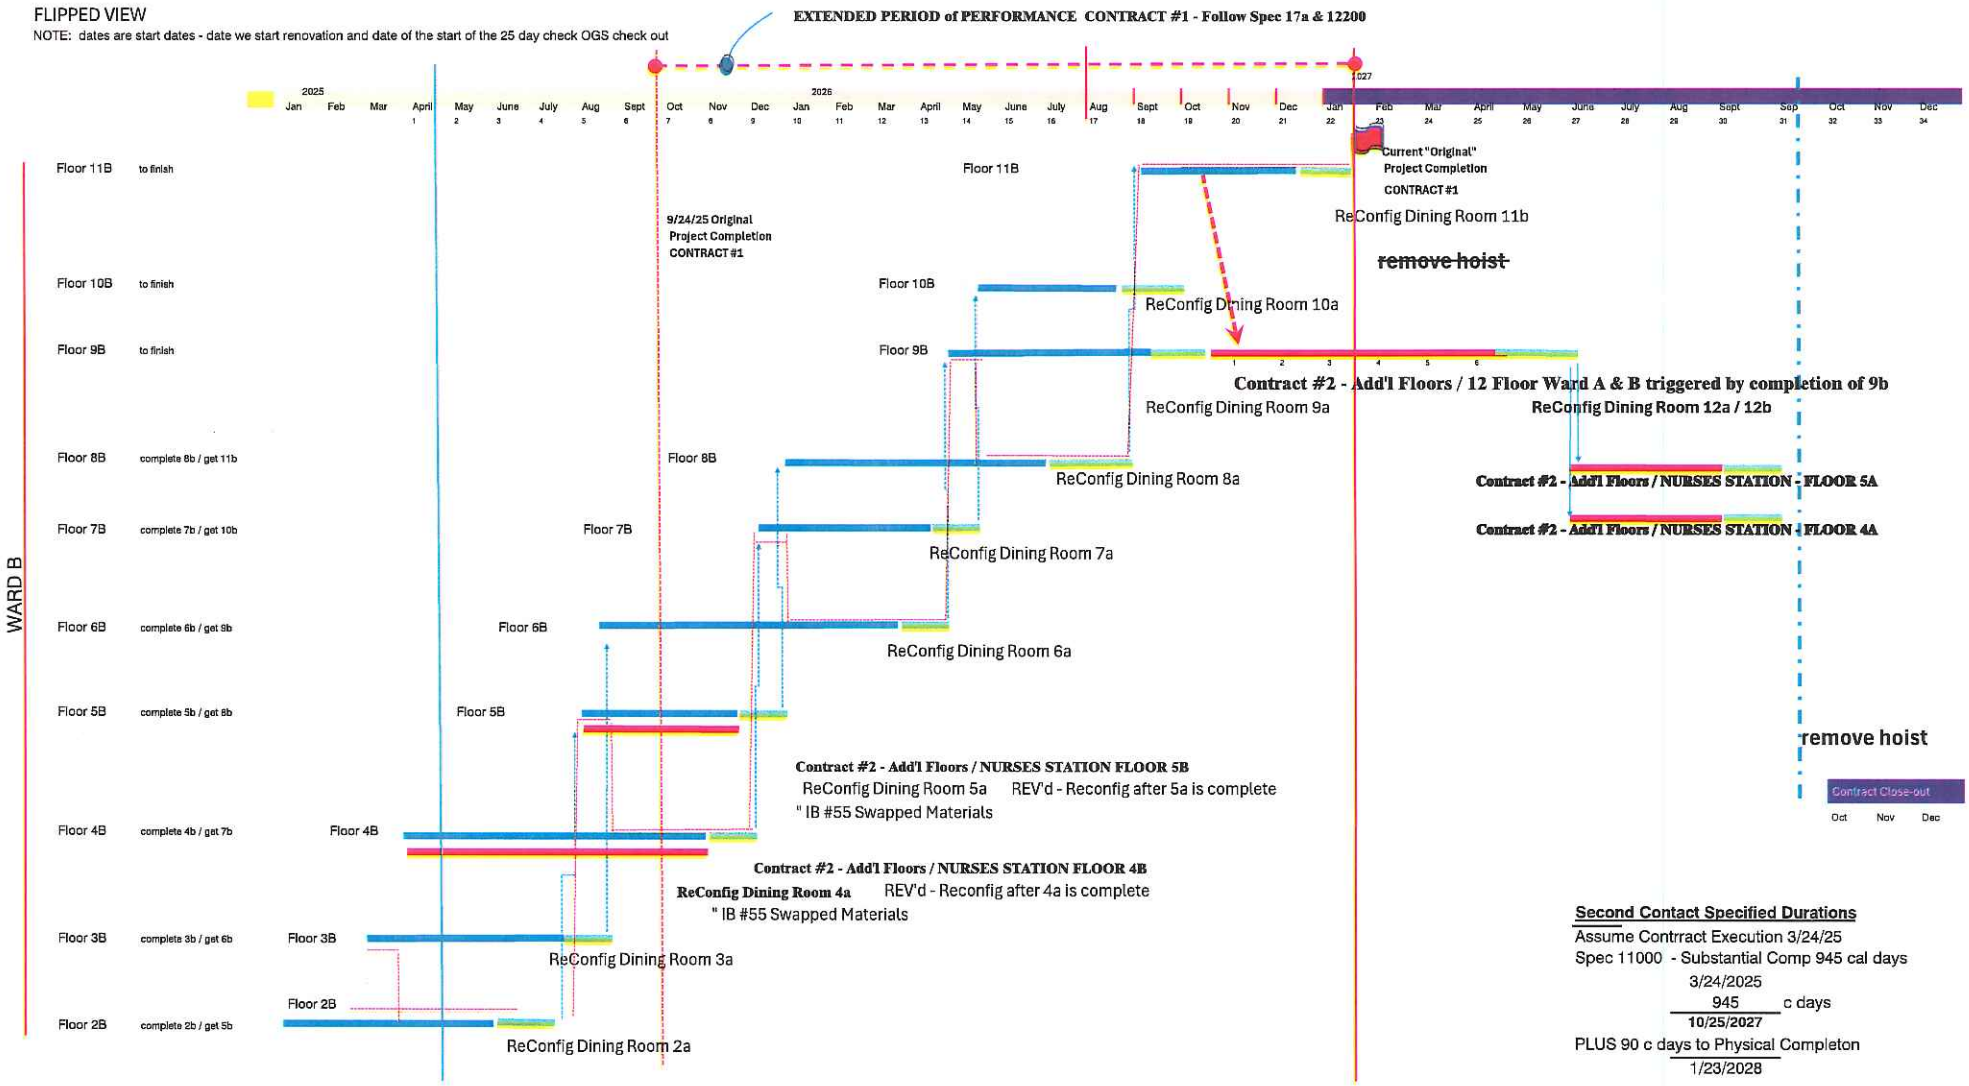

Second Contact Specified Durations

Assume Contrract Execution 3/24/25

Spec 11000 - Substantial Comp 945 cal days

3/24/2025

945 c days

10/25/2027

PLUS 90 c days to Physical Completon

1/23/2028

ATTACHMENT 2

OGS Approval Three Bid Waiver and Proposal

See Next Page for Attachment

SUB	CONT

Tom Zimmermann

From: Otto, Justin C (OGS) <Justin.Otto@ogs.ny.gov>
Sent: Tuesday, August 12, 2025 10:43 AM
To: Tom Zimmermann; Brian Troast
Cc: Prewitt, Nicole (OGS); Gaudio, Thomas (OGS); McLean, Nigel (OGS)
Subject: FW: 47777C - Creedmoor PC -Elli Design Corp. - Three Bid Waiver
Attachments: 47777-C Three Bid Waiver.pdf

Tom/Brian,

Below and attached find Elli approval sent to PDC on 7/31.

Thank you

Justin Otto, CCM
Senior Project Manager / EIC

Office of General Services | Design and Construction | Long Island Region
Creedmoor Psychiatric Center, Building #73 Basement,
80-45 Winchester Blvd, Queens Village, NY 11427
p.(718)-923-2980 c: (914) 419-5619
www.ogs.ny.gov | justin.otto@ogs.ny.gov

From: Bacchus, Bibi A (OGS) <Bibi.Bacchus@ogs.ny.gov>
Sent: Thursday, July 31, 2025 10:24 AM
To: rvg@prisdev.com
Cc: Otto, Justin C (OGS) <Justin.Otto@ogs.ny.gov>; McLean, Nigel (OGS) <Nigel.McLean@ogs.ny.gov>; Gaudio, Thomas (OGS) <Thomas.Gaudio@ogs.ny.gov>
Subject: RE: 47777C - Creedmoor PC -Elli Design Corp. - Three Bid Waiver

Good Morning,

Attached please find your firm approved three bid waiver request for the above noted contract.

Regards.

Bibi Bacchus
Regional Office Manager

Office of General Services | Design and Construction | Long Island Region
Creedmoor Psychiatric Center, Building #73 Basement,
80-45 Winchester Blvd, Queens Village, NY 11427
o. (718) 776-4441 | f. (718) 776-8088 bibi.bacchus@ogs.ny.gov
www.ogs.ny.gov

C04

NEW YORK STATE | Office of General Services

KATHY HOCHUL
Governor

JEANETTE M. MOY
Commissioner

07/30/2025

Prismatic Development Corporation
60 Us Highway 46
Fairfield, NJ 07004-3027

RE: Creedmoor PC
Inpatient Bed Expansion Renovations
Emergency Contract No. 47777-C

Mr. Zimmerman:

Your firm is hereby granted a waiver of 3 bids for the associated work included in the attached proposal dated 06/19/2025 in accordance with Supplemental Conditions Document 007304 Non-Emergency Cost Plus Percentage Fee Contract.

Elli Design Corp. is authorized to proceed with the work for a lump sum of 225,001.64. In addition, your firm is authorized a cost-plus fee of 21% on labor and material only in accordance with section 2.25.6.4 of the above noted supplemental conditions.

Sincerely,

for John Kochem
Director of Construction

cc: J. Hustedt, J. Otto, E. Gamache

NEW YORK STATE | **Office of General Services**

Design and Construction
Division of Construction, 34th Floor, Corning Tower
The Governor Nelson A. Rockefeller Empire State Plaza
Albany, New York 12242
Phone: (518) 474-0331

THREE BID WAIVER REQUEST

Project No.: 47777 C

Send completed form to the Division of Contract Management at the above address.

Project Description: *(Project Title, Facility Name and Address)*	Contractor:
Inpatient Bed Expansion Renovations ***Creedmoor Psychiatric Center*** ***80-45 Winchester Blvd*** ***Queens Village, NY 11427-2193***	***Prismatic Development Corporation***
	Date: ***July 22, 2025***

JUSTIFICATION

The reason the contractor cannot fulfill the contract requirements to obtain three (3) bids is:

Subcontractor is already on site for Contract 47103 in the same location. For the sake of continuity and limiting exposure to the Facility for extended down time on floors, it is in the best interest of the project and for the Client to have the same subcontractor demolish the balance of the 4th & 5th floors.

– OGS TO FIX

The description of subcontract work to be performed is:

PDC will have their subcontractor, Elli Design Corp, supply and install the millwork for the nursing station and bathrooms for Wards 4B & 5B as part of Contract 47777.

The company to perform the subcontract is:

Name: ***Elli Design Corp.*** Federal ID No.: ***13-3617169***

Address: ***50-01 Metropolitan Ave***
Ridgewood, NY

Phone: ***info@ellicorp.com***

The cost of the subcontractor work to be determined by one of the following methods:

☒ Approved subcontract amount of ***$225,001.64*** (Fixed Price)

☐ Cost plus fee of _____ %, Not to Exceed _____

☒ Other: *(Provide full description.)*

Contractor will be proceeding on a not to exceed basis with the understanding of their price submitted should follow contract 47777 and will be paid so accordingly.

☐ Subcontractor's proposal is attached.

NOTE: If this waiver is for rental, under no circumstances will the State pay more then 100% of the new purchase price as rental. The contractor shall advise the EIC if the rental cost is approaching the purchase price. In accordance with the contract these subcontract charges are to be accepted as a cost to the prime contract.

Recommended by:	Justin Otto	7/22/25	Approved by:		7-28-25
	Project Executive	Date		Regional Supervisor	Date

FOR CENTRAL OFFICE USE ONLY:

Approved by:	07/30/25	For Requests over $76,000:	John Kochem	
Emergency Coordinator	Date		Assistant Director, Division of Construction	Date

Subcontractor Reviewed by: _____ Vendor Responsibility Group _____ Date

Distribution: Regional Office # ___ EIC: ***Justin Otto***

91

E-FILE: V:\DesignAndConstr\Project Folder\05_SubContractorsSuppliers

ELLI NY DESIGN

50-01 Metropolitan Ave, Ridgewood, NY
Tel: 718-418-9002 | Fax. 718-418-4629
www.ellicorp.com | info@ellicorp.com

M/WBE CERTIFIED
NYC Small Business Services
THE PORT AUTHORITY OF NEW YORK & NEW JERSEY
SCA School Construction Authority

June 18th 2025,

Please note: This quote will only be valid for 90 days.

RE: Creedmoor Additional Wards Proposal

The following is our proposal for the Manufacturing and Installation of the Architectural Woodwork as per Drawings and Specifications Sections:

8/12/25 -
POTENTIAL MAT'L SWAP FROM FLOORS

INCLUDED: Ward B Floor 4th & 5th Floor

- Nurse Station Observation Desks
- Plam Cabinets and Solid Surface Countertops at Chart rooms, med rooms and exam rooms
- Solid Surface Windowsill in Med Room
- Solid Surface Staff vanity tops (4B only).
- Sliding Drawers in Chart rooms per IB#039.
- Updated hinges for cabinet doors per PCO#230R1

Excluding Corian shelves for all closets

10B & 11B - THEN REPLACE TO ACCOMODATE SCHEDULE -
* SCHEDULE NO ISSUE *

Total Material and fabrication cost for all above = $138,740.00
Field Labor: 2 carpenters for 30 days (480 hrs total) @ $118.57/hr = $56,913.60

Total for the above: $195,703.60
Overhead & Profit 15% = $29,348.04

8/12/25
PHONE CALL W/ MAHAYIA

BASE BID TOTAL: $ 225,001.64

PROJECT SPECIFIC EXCLUSIONS: *Vestibule Area N.I.C. | Caulking | Doors, Frames, & Associated Hardware | Electrical Closets | Dining room cabinets in 4 & 5 floors | Anything not listed or attached herein.*

STANDARD EXCLUSIONS: *Metal & Steel Work (Custom and/or Structural) | Doors, Frames, & Associated Hardware | Plumbing Fixtures | Appliances | Removal of Debris (Center-pile Only) | Glazing | Caulking | In-Wall Blocking | Overtime | NYC/NYS Taxes | Items not listed or attached herein.*

✓ 2 MOBS REQ'D

PHASING: *Pricing is based on single Installation | single Mobilization. If more than one phase is required. Elli NY Design will assess & recapture the proper additional costs at the appropriate time.*

NOT VALID - NO COST ADD

ESCALATIONS: *If delivery &/or installation extends beyond the agreed baseline schedule, Elli NY Design reserves the right to review and assess additional fees. These may cover increased raw material and labor costs, production schedule impacts, and storage-related expenses.*

Should you have any questions or uncertainty please contact the undersigned.
Elli NY Design Corp.
Peter Ligas
Senior Estimator.

AWI

New York & New Jersey Minority Supplier Development Council

An Equal Opportunity Employer

CREEDMOOR #47777-C (ADDED CONTRACT 4B & 5B)

FL/WARD	ROOM	ITEM DESCRIPTION	#47777-C REF DWGS	#47103-C REF DWGS
4B	MED ROOM	2 CORIAN SOLID SURFACE COUNTERS	A101.3	A201
		1 ADA & 1 WALL HUNG PLASTIC LAMINATE CABINETS	A101.3	A201
		1 CORIAN SOLID SURFACE WINDOWSILL	A101.3	A201
	EXAM ROOM	2 CORIAN SOLID SURFACE COUNTERS	A101.3	A201
		6 WALL HUNG, 1 ADA & 1 BASE PLASTIC LAMINATE CABINETS	A101.3	A201
	CHART ROOM	4 CORIAN SOLID SURFACE COUNTERS	A101.3	A201
		6 BASE CABINETS WITH DRAWERS, 4 WALL HUNG CABINETS	A101.3	A201
	NURSE STATION	1 OBSERVATION DESK	A101.3	A201
	STAFF BATHROOM	2 CORIAN SOLID SURFACE INTEGRAL BATHROOM VANITIES	A415	
5B	MED ROOM	2 CORIAN SOLID SURFACE COUNTERS	A101.3	A201
		1 ADA & 1 WALL HUNG PLASTIC LAMINATE CABINETS	A101.3	A201
		1 CORIAN SOLID SURFACE WINDOWSILL	A101.3	A201
	EXAM ROOM	2 CORIAN SOLID SURFACE COUNTERS	A101.3	A201
		6 WALL HUNG, 1 ADA & 1 BASE PLASTIC LAMINATE CABINETS	A101.3	A201
	CHART ROOM	4 CORIAN SOLID SURFACE COUNTERS	A101.3	A201
		6 BASE CABINETS WITH DRAWERS, 4 WALL HUNG CABINETS	A101.3	A201
	NURSE STATION	1 OBSERVATION DESK	A101.3	A201

NOTE: ABOVE BREAKDOWN OF ITEMS FOR 4B & 5B DOES NOT INCLUDE ANY CORIAN SHELF FOR CLOSETS

120 St. James Ave, 5th Floor
Boston, MA 02116
USA

July 22, 2025

Office of General Services | Design & Construction | Division of Construction
35th Floor, Corning Tower, ESP
Albany, NY 12242
Re: 47777-C Creedmoor Psychiatric Center

The accompanying bid proposal, submitted by Elli NY Design and dated June 18, 2025, of $225,001.64 is fair and reasonable based on following.

- The 47777-C scope calculates to $39.40/SF while the current contract value for 47103-C scope is $35.45/SF. This increase is warranted due to inflation, market conditions, and due to the incorporation of 47103-C change order scope that has been captured in the 47777-C scope.
- The field labor included in the proposal is fair and reasonable for the work requirements of the project site.

If you would like to discuss my review of the attached Bid Proposal, please contact me via email at austin.chaffee@jacobs.com or telephone at (508) 857-9479.

Sincerely,

Austin Chaffee

Digitally signed by Austin Chaffee
DN: C=US
E=austin.chaffee@jacobs.com, O=Jacobs, CN=Austin Chaffee
Reason: I am the author of this document
Date: 2025.07.22 09:35:56-04'00'

Austin Chaffee
Estimator
Jacobs

NEW YORK STATE OF OPPORTUNITY. Office of General Services

Design and Construction
AN ISO 9001:2015 CERTIFIED ORGANIZATION
Division of Construction, 34th Floor, Corning Tower
The Governor Nelson A. Rockefeller Empire State Plaza
Albany, New York 12242
Phone: (518) 474-0331

INFORMATION BULLETIN

Project No.: 47103

Project Description: *(Project Title, Facility Name and Address)* 47103 - Creedmoor PC, North Campus - Renovate Nurse Station, Clinical Areas & Shower Ro Queens, NY			Client Agency: OMH
IB No.: IB 055	Trades: ☒ C ☐ E ☐ H ☐ P Other ☐	Spec. Section:	Drawing No.: N/A
Brief Description: 10th and 11th Floors Material swap			
Issue Date: 4/14/2025	Issued By: Alex dOelsnitz	Affiliation: OGS Design & Construction	

Reason:
☒ Program Changer ☐ Omission ☐ Design Error ☐ Contractor Error ☐ Field Error ☐ Field Condition ☐ Document Clarification
☐ Material / Methods Substitution

Detailed Scope Description (include contract adds and deducts):
- Use all finishes and materials, including doors and hardware, already purchased for floors 10th and 11th (project 47103), on the 4th and 5th floors, (project 47777).

Justification for OSC:
The client, to save time in the current phasing construction schedule, suggested to use all finishes and materials already purchased for the 10th and 11th floor, (Project 47103) and use them in the 4th and 5th floor for project 47777.

Estimated Cost Impact: ☐ Additional Cost ☒ No Change ☐ Credit	Estimated Time Impact: ☐ YES ☒ NO

Attached Document Description:
N/A

BDC-43 Meeting Report and Discussion Record

NEW YORK STATE OF OPPORTUNITY. Office of General Services
Design & Construction

Project: 47777.0 - Creedmoor PC, Inpatient Bed Expn Rnvtn - BL1...

Status Date: 06.23.25 **Award Date:** 02.04.25

Meeting Log and Discussion of Activity Variance (5 Days) Noted By The Project Team For the Schedule Update

Schedule Section (WBS)	Activity Name	Activity ID	Comment About Variance	Comment Date
A0.00.SCH - Justin Kalinkewicz				
Milestones	02b BL1 Agreement	MLST.0-202	Baseline schedule w as agreed to on 06/16/25 by the Project Team. Attached is the baseline w ork plan. The next report w ill be posted on 07/28/25.	06.24.25
A1.R3.EIC.KD - Justin Otto				
Milestones	02b BL1 Agreement	MLST.0-202	Agreed	06.20.25
PDC - Tom Zimmermann				
Milestones	02b BL1 Agreement	MLST.0-202	Agree	06.17.25
Milestones	02b BL1 Agreement	MLST.0-202	Agree TZ / PDC 6/17/25	06.17.25

Baseline Agreement

NEW YORK STATE OF OPPORTUNITY | Office of General Services Design & Construction

Project: 47777.0 - Creedmoor PC, Inpatient Bed Expn Rnvtn - BL1...

It is agreed that the referenced Project Schedule defined by the following reports has been reviewed and is accepted for use in coordinating, scheduling, and monitoring the work of all related contracts

By acknowledging within the Project Work Plan software, OGS does not waive the terms and conditions set forth in the Contract Documents. In accordance with the General Conditions (Document 007213) any change in the Contract sum or time of completion requires an Order on Contract.

Refer to the following report for the specific dates.

Contract	Representative	Activity Name	Date
A0.00.SCH - Justin Kalinkewicz			
R1B5.47777.0	justin.kalinkew icz	02b BL1 Agreement	05.28.25 14
R1B5.47777.0	justin.kalinkew icz	02b BL1 Agreement	05.28.25 14
A1.R3.EIC.KD - Justin Otto			
R1B5.47777.0	justin.otto	02b BL1 Agreement	06.20.25 10
PDC - Tom Zimmermann			
R1B5.47777.C	Tom.Zimmermann	02b BL1 Agreement	06.17.25 19
R1B5.47777.C	Tom.Zimmermann	02b BL1 Agreement	06.17.25 19


CH

000a - Baseline Plan

New York State
Office of General Services
Design & Construction

Printed: 06.16.25 13:53

Activity Name	Activity ID	Critical	!RWP	!DRWG	Predecessors	BL Start	BL Est Dur	BL Est Wkr Days	BL Finish	Successors	Calendar	Activity Type	Primary Constra	Primary Constraint Date	Project ID	Act #	Primary Resource	Total Float
47777 - Creedmoor, Inpatient Bed Expn Rnvtn						03.24.25	660	2321	10.25.27		!05MGF08D.H					258		0
Milestones						03.24.25	660	0	10.25.27		!05MGF08D.H					9		0
Key Milestones						03.24.25	660	0	10.25.27		!05MGF08D.H					5		0
01a Awarded	MLST.0-200	☐	NoRWP	NA		03.24.25	0	0		MTG.0-100, MLST.0-202, MLST.0-212, 47777.C-2903, 47777.C-2905, 47777.C-2904	!05MGF08D.H	Start Milestone			R1B5.47777.0	1		
02b BL1 Agreement	MLST.0-202	☐	NoRWP	NA	MLST.0-200		0	0	05.08.25	MLST.0-218	!05MGF08D.H	Finish Milestone			R1B5.47777.0	1		
04C Ctr As-Sched SC	MLST.0-212	☐	NoRWP	NA	MLST.0-200, MLST.0-212		0	0	10.18.27	MLST.0-219, MLST.0-218	!05MGF08D.H	Finish Milestone			R1B5.47777.0	1		6
05a Project As-Sched SC	MLST.0-218	☐	NoRWP	NA	MLST.0-202, MLST.0-212		0	0	10.18.27	MLST.0-219	!05MGF08D.H	Finish Milestone			R1B5.47777.0	1		6
05b Project SC	MLST.0-219	☑	NoRWP	NA	MLST.0-212, MTG.0-100, MLST.0-218		0	0	10.25.27		!05MGF08D.H	Finish Milestone	Mandatc Finish	10.25.27	R1B5.47777.0	1		0
Contract Milestones						03.24.25	660	0	10.25.27		!05MGF08D.H					4		0
01a Awarded	MLST.0-200	☐	NoRWP	NA		03.24.25	0	0		MLST.0-202, MLST.0-212, MTG.0-100, 47777.C-2760	!05MGF08D.H	Start Milestone			R1B5.47777.C	1		
02b BL1 Agreement	MLST.0-202	☐	NoRWP	NA	MLST.0-200		0	0	05.08.25		!05MGF08D.H	Finish Milestone			R1B5.47777.C	1		
04C Ctr As-Sched SC	MLST.0-212	☐	NoRWP	NA	MLST.0-200, 47777.C-2823, 47777.C-2851		0	0	10.18.27	MLST.0-219, MLST.0-212	!05MGF08D.H	Finish Milestone			R1B5.47777.C	1		6
05b Contract SC	MLST.0-219	☑	NoRWP	NA	MLST.0-212, MTG.0-100		0	0	10.25.27		!05MGF08D.H	Finish Milestone	Mandatc Finish	10.25.27	R1B5.47777.C	1		0
Mob & Admin						03.24.25	654	645	10.18.27		!05MGF08D.H					75		6
Meetings						04.08.25	0	0	04.08.25		!05MGF08D.H					2		
Initial Scheduling Meeting (EIC/Ctr Training) (+15d)	MTG.0-100	☐	NoRWP	NA	MLST.0-200		0	0	04.08.25	MLST.0-219	!05MGF08D.H	Finish Milestone			R1B5.47777.C	1		
Initial Scheduling Meeting (EIC/Ctr Training) (+15d)	MTG.0-100	☐	NoRWP	NA	MLST.0-200		0	0	04.08.25	MLST.0-219	!05MGF08D.H	Finish Milestone			R1B5.47777.0	1		
Subcontractor Procurement/Approval						03.24.25	465	405	01.20.27		!05MGF08D.H					33		11
C47777 - Project Proceed / Adminstrative Set-Up	47777.C-2760	☐	NoRWP	NA	MLST.0-200	03.24.25	5	5	03.31.25	47777.C-100, 47777.C-2710, 47777.C-2711, 47777.C-2712, 47777.C-2714, 47777.C-2715, 47777.C-2716, 47777.C-2717, 47777.C-2718, 47777.C-2719, 47777.C-2720, 47777.C-2721, 47777.C-2722, 47777.C-2723, 47777.C-2724, 47777.C-2713	!05MGF08D.H	Resource Depender	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Solicit / Submit / OGS Approvel - Demolition Sub	47777.C-100	☐	NoRWP	NA	47777.C-2760	03.31.25	15	15	04.21.25	47777.C-2726	!05MGF08D.H	Resource Depender	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Solicit / Submit / OGS Approvel -Fire Protection Sub	47777.C-2721	☐	NoRWP	NA	47777.C-2760	04.02.25	15	15	04.23.25	47777.C-2731	!05MGF08D.H	Resource Depender	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Solicit / Submit / OGS Approvel -Plumbing Sub	47777.C-2722	☐	NoRWP	NA	47777.C-2760	04.02.25	15	15	04.23.25	47777.C-2737	!05MGF08D.H	Resource Depender	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Solicit / Submit / OGS Approvel -Mechanical Sub	47777.C-2723	☐	NoRWP	NA	47777.C-2760	04.02.25	15	15	04.23.25	47777.C-2733	!05MGF08D.H	Resource Depender	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Solicit / Submit / OGS Approvel -Electrical , Fire Alarm, Security Sub	47777.C-2724	☐	NoRWP	NA	47777.C-2760	04.02.25	15	15	04.23.25	47777.C-2730	!05MGF08D.H	Resource Depender	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55

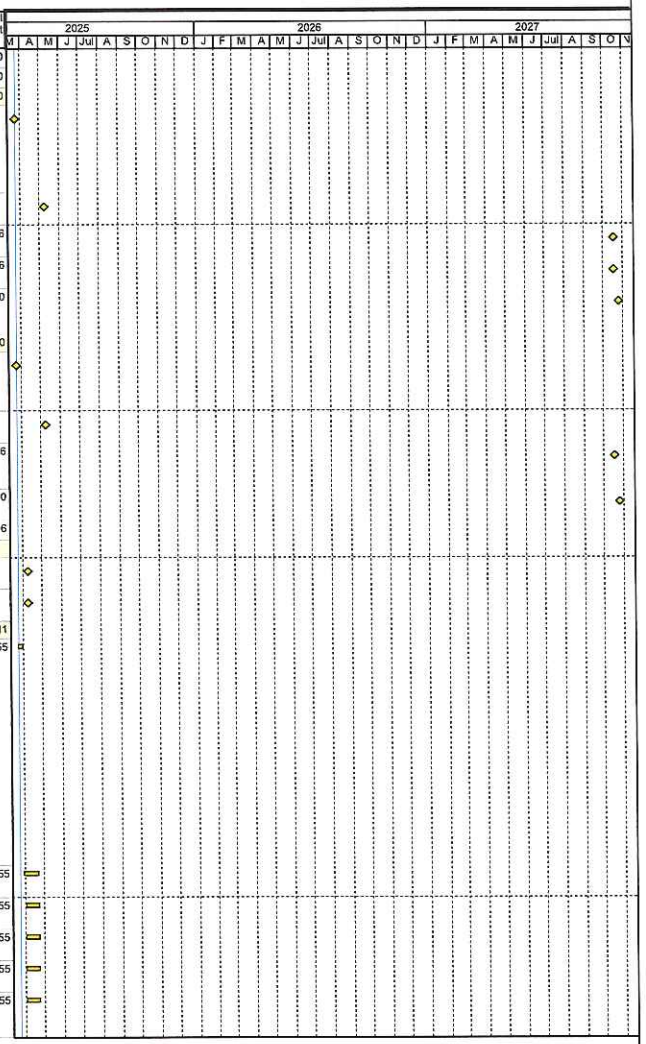

BL Baseline (Working) | BL Milestone | RWP Roofing | RWP PhyWork | RWP Heating | RWP WtrProofing | RWP Paving | RWP UGConduit | RWP Grubbing | RWP Seeding | RWP HVAC | RWP Stucco


- Filters: TASK filter: Excl WBS Summary Only.
- Data Date: 03.24.25
- Baseline:

000a - Baseline Plan

New York State
Office of General Services
Design & Construction

Printed: 06.16.25 13:53

Activity Name	Activity ID	Critical	!RWP	!DRWG	Predecessors	BL Start	BL Est Dur	BL Est Wkr Days	BL Finish	Successors	Calendar	Activity Type	Primary Constra	Primary Constraint Date	Project ID	Act #	Primary Resource	Total Float
C47777 - Solicit / Submit / OGS Approvel - Hollow Metal / Hardware Supplier	47777.C-2710		NoRWP	NA	47777.C-2760	04.11.25	15	15	05.02.25	47777.C-2725	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Solicit / Submit / OGS Approvel -Mtl Stub / GWB / Selection Installation Sub	47777.C-2717		NoRWP	NA	47777.C-2760	04.11.25	15	15	05.02.25	47777.C-2735	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Contract Admin - Demolition Sub	47777.C-2726		NoRWP	NA	47777.C-100	04.21.25	10	10	05.05.25	47777.C-2693, 47777.C-2875	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Contract Admin -Electrical , Fire Alarm, Security Sub	47777.C-2730		NoRWP	NA	47777.C-2724	04.23.25	10	10	05.07.25	47777.C-2697, 47777.C-2854	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Contract Admin - Fire Protection Sub	47777.C-2731		NoRWP	NA	47777.C-2721	04.23.25	10	10	05.07.25	47777.C-2698, 47777.C-2854	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Contract Admin -Mechanical Sub	47777.C-2733		NoRWP	NA	47777.C-2723	04.23.25	10	10	05.07.25	47777.C-2700, 47777.C-2854	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Contract Admin -Plumbing Sub	47777.C-2737		NoRWP	NA	47777.C-2722	04.23.25	10	10	05.07.25	47777.C-2704, 47777.C-2854	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Contract Admin - Hollow Metal / Hardware Supplier	47777.C-2725		NoRWP	NA	47777.C-2710	05.02.25	10	10	05.16.25	47777.C-2694	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Contract Admin -Mtl Stud / GWB / Selection Installation Sub	47777.C-2735		NoRWP	NA	47777.C-2717	05.02.25	10	10	05.16.25	47777.C-2702	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Solicit / Submit / OGS Approvel -Painting Sub	47777.C-2714		NoRWP	NA	47777.C-2760	05.05.25	15	15	05.27.25	47777.C-2736	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Solicit / Submit / OGS Approvel -Millwork Sub	47777.C-2715		NoRWP	NA	47777.C-2760	05.12.25	15	15	06.03.25	47777.C-2734	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Solicit / Submit / OGS Approvel -Wallcovering Supplier	47777.C-2716		NoRWP	NA	47777.C-2760	05.12.25	15	15	06.03.25	47777.C-2741	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Solicit / Submit / OGS Approvel -Alum & Glass Sub	47777.C-2711		NoRWP	NA	47777.C-2760	05.16.25	15	15	06.09.25	47777.C-2728	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Solicit / Submit / OGS Approvel -Caulking & Sealant Sub	47777.C-2720		NoRWP	NA	47777.C-2760	05.16.25	15	15	06.09.25	47777.C-2729	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Solicit / Submit / OGS Approvel -LVT Flooring Sub	47777.C-2719		NoRWP	NA	47777.C-2760	05.27.25	15	15	06.17.25	47777.C-2732	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Contract Admin -Painting Sub	47777.C-2736		NoRWP	NA	47777.C-2714	05.27.25	10	10	06.10.25	47777.C-2703	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Solicit / Submit / OGS Approvel -Toilet Access / Fire Cab Supplier	47777.C-2712		NoRWP	NA	47777.C-2760	05.30.25	15	15	06.20.25	47777.C-2739	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Solicit / Submit / OGS Approvel -Wall & Corner Protection Supplier	47777.C-2718		NoRWP	NA	47777.C-2760	05.30.25	15	15	06.20.25	47777.C-2740	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Contract Admin -Millwork Sub	47777.C-2734		NoRWP	NA	47777.C-2715	06.03.25	10	10	06.17.25	47777.C-2701	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Contract Admin -Wallcovering Supplier	47777.C-2741		NoRWP	NA	47777.C-2716	06.03.25	10	10	06.17.25	47777.C-2708	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Contract Admin -Alum & Glass Sub	47777.C-2728		NoRWP	NA	47777.C-2711	06.09.25	10	10	06.23.25	47777.C-2695	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Contract Admin -Caulking & Sealant Sub	47777.C-2729		NoRWP	NA	47777.C-2720	06.09.25	10	10	06.23.25	47777.C-2696	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Contract Admin -LVT Flooring Sub	47777.C-2732		NoRWP	NA	47777.C-2719	06.17.25	10	10	07.01.25	47777.C-2699	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Contract Admin -Toilet Access / Fire Cab Supplier	47777.C-2739		NoRWP	NA	47777.C-2712	06.20.25	10	10	07.07.25	47777.C-2706	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Contract Admin -Wall & Corner Protection Supplier	47777.C-2740		NoRWP	NA	47777.C-2718	06.20.25	10	10	07.07.25	47777.C-2707	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Solicit / Submit / OGS Approvel -Ceramic Tile Sub	47777.C-2713		NoRWP	NA	47777.C-2760	12.15.26	15	15	01.06.27	47777.C-2738	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 - Contract Admin -Ceramic Tile Sub	47777.C-2738		NoRWP	NA	47777.C-2713	01.07.27	10	10	01.20.27	47777.C-2705	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11

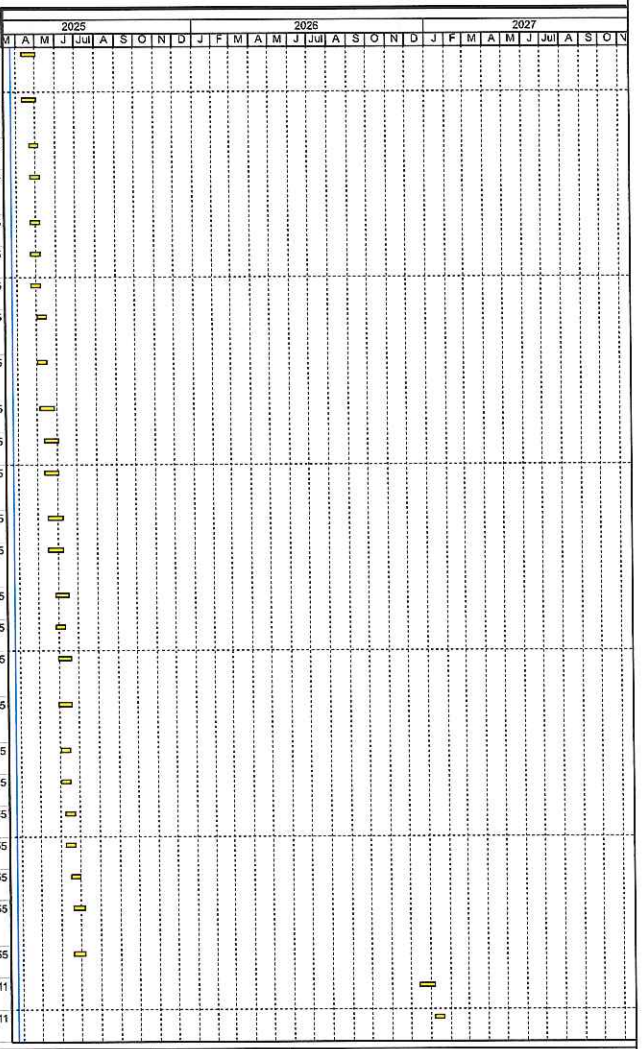

BL Baseline (Working)
BL Milestone
RWP Roofing
RWP PhyWork
RWP Heating
RWP WtrProofing
RWP Paving
RWP UGConduit
RWP Grubbing
RWP Seeding
RWP HVAC
RWP Stucco


- Filters: TASK filter: Excl WBS Summary Only.
- Data Date: 03.24.25
- Baseline:

000a - Baseline Plan

New York State
Office of General Services
Design & Construction

Printed: 06.16.25 13:53

Activity Name	Activity ID	Critical	!RWP	!DRWG	Predecessors	BL Start	BL Est Dur	BL Est Wkr Days	BL Finish	Successors	Calendar	Activity Type	Primary Constra	Primary Constraint Date	Project ID	Act #	Primary Resource	Total Float
Critical Submittals						05.05.25	445	160	02.03.27		!05MGF08D.H					16		11
C47777 - SD Submit - Review & Approve - Demolition Sub	47777.C-2693		NoRWP	NA	47777.C-2726	05.05.25	10	10	05.19.25	47777.C-2742	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - SD Submit - Review & Approve -Electrical , Fire Alarm, Security Sub	47777.C-2697		NoRWP	NA	47777.C-2730	05.07.25	10	10	05.21.25	47777.C-2754	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - SD Submit - Review & Approve -Fire Protection Sub	47777.C-2698		NoRWP	NA	47777.C-2731	05.07.25	10	10	05.21.25	47777.C-2753	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - SD Submit - Review & Approve -Mechanical Sub	47777.C-2700		NoRWP	NA	47777.C-2733	05.07.25	10	10	05.21.25	47777.C-2750	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - SD Submit - Review & Approvel -Plumbing Sub	47777.C-2704		NoRWP	NA	47777.C-2737	05.07.25	10	10	05.21.25	47777.C-2744	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - SD Submit - Review & Approve - Hollow Metal / Hardware Supplier	47777.C-2694		NoRWP	NA	47777.C-2725	05.16.25	10	10	06.02.25	47777.C-2755	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - SD Submit - Review & Approve -Mtl Stub / GWB / Selection Installation Sub	47777.C-2702		NoRWP	NA	47777.C-2735	05.16.25	10	10	06.02.25	47777.C-2749	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - SD Submit - Review & Approve -Painting Sub	47777.C-2703		NoRWP	NA	47777.C-2736	06.10.25	10	10	06.24.25	47777.C-2748	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - SD Submit - Review & Approve -Millwork Sub	47777.C-2701		NoRWP	NA	47777.C-2734	06.17.25	10	10	07.01.25	47777.C-2751	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - SD Submit - Review & Approvel -Wallcovering Supplier	47777.C-2708		NoRWP	NA	47777.C-2741	06.17.25	10	10	07.01.25	47777.C-2743	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - SD Submit - Review & Approve -Alum & Glass Sub	47777.C-2695		NoRWP	NA	47777.C-2728	06.23.25	10	10	07.08.25	47777.C-2757	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - SD Submit - Review & Approve -Caulking & Sealant Sub	47777.C-2696		NoRWP	NA	47777.C-2729	06.23.25	10	10	07.08.25	47777.C-2756	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - SD Submit - Review & Approve -LVT Flooring Sub	47777.C-2699		NoRWP	NA	47777.C-2732	07.01.25	10	10	07.16.25	47777.C-2752	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - SD Submit - Review & Approve -Toilet Access / Fire Cab Supplier	47777.C-2706		NoRWP	NA	47777.C-2739	07.07.25	10	10	07.21.25	47777.C-2746	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - SD Submit - Review & Approve -Wall & Corner Protection Supplier	47777.C-2707		NoRWP	NA	47777.C-2740	07.07.25	10	10	07.21.25	47777.C-2745	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - SD Submit - Review & Approve -Ceramic Tile Sub	47777.C-2705		NoRWP	NA	47777.C-2738	01.21.27	10	10	02.03.27	47777.C-2747	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
Critical Procurement						05.19.25	440	80	02.10.27		!05MGF08D.H					16		11
C47777 - Fabricate/Deliver - Demolition Sub Mat'l per IB55	47777.C-2742		NoRWP	NA	47777.C-2693	05.19.25	5	5	05.27.25	47777.C-2875	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Fabricate/Deliver - Plumbing Sub per IB55	47777.C-2744		NoRWP	NA	47777.C-2704	05.21.25	5	5	05.29.25	47777.C-2859, 47777.C-2854	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Fabricate/Deliver - Mechanical Sub per IB55	47777.C-2750		NoRWP	NA	47777.C-2700	05.21.25	5	5	05.29.25	47777.C-2854	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Fabricate/Deliver - Fire Protection Sub per IB55	47777.C-2753		NoRWP	NA	47777.C-2698	05.21.25	5	5	05.29.25	47777.C-2854	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Fabricate/Deliver - Electrical , Fire Alarm, Security Sub per IB55	47777.C-2754		NoRWP	NA	47777.C-2697	05.21.25	5	5	05.29.25	47777.C-2854	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Fabricate/Deliver - Mtl Stub / GWB / Selection Installation Sub per IB55	47777.C-2749		NoRWP	NA	47777.C-2702	06.02.25	5	5	06.09.25	47777.C-2858	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Fabricate/Deliver - Hollow Metal / Hardware Supplier per IB55	47777.C-2755		NoRWP	NA	47777.C-2694	06.02.25	5	5	06.09.25	47777.C-2603, 47777.C-2858	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Fabricate/Deliver - Painting Sub per IB55	47777.C-2748		NoRWP	NA	47777.C-2703	06.24.25	5	5	07.01.25	47777.C-2863	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Fabricate/Deliver - Wallcovering Supplier per IB55	47777.C-2743		NoRWP	NA	47777.C-2708	07.01.25	5	5	07.09.25	47777.C-2865	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Fabricate/Deliver - Millwork Sub per IB55	47777.C-2751		NoRWP	NA	47777.C-2701	07.01.25	5	5	07.09.25	47777.C-2865	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55

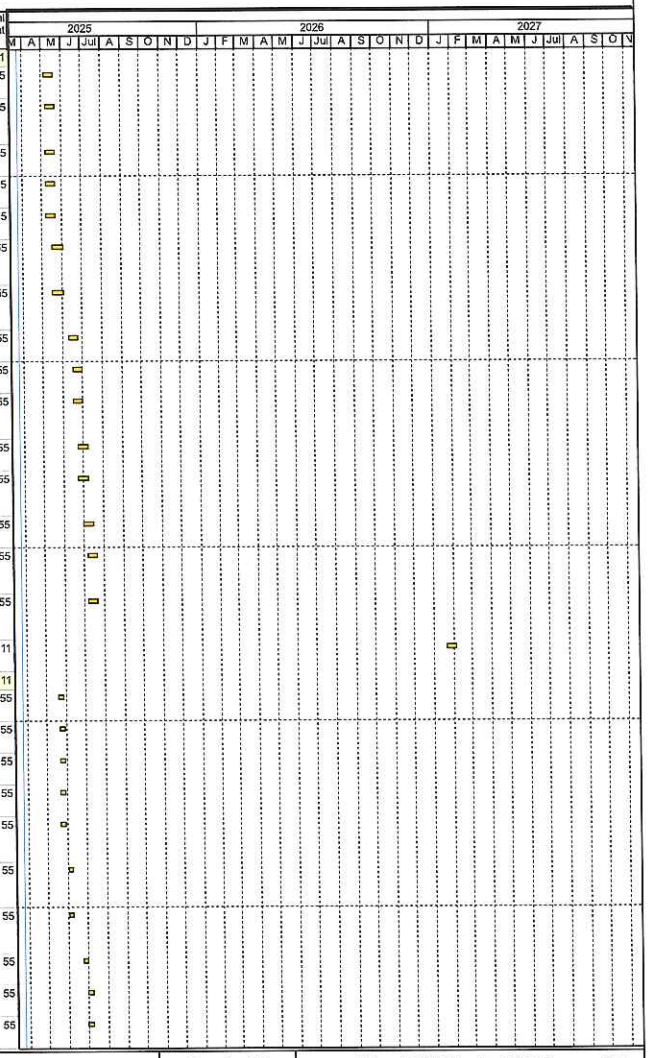

BL Baseline (Working)
BL Milestone
RWP Roofing
RWP PhyWork
RWP Heating
RWP WtrProofing
RWP Paving
RWP UGConduit
RWP Grubbing
RWP Seeding
RWP HVAC
RWP Stucco


- Filters: TASK filter: Excl WBS Summary Only.
- Data Date: 03.24.25
- Baseline:

000a - Baseline Plan

New York State
Office of General Services
Design & Construction

Printed: 06.16.25 13:53

Activity Name	Activity ID	Critical	!RWP	!DRWG	Predecessors	BL Start	BL Est Dur	BL Est Wkr Days	BL Finish	Successors	Calendar	Activity Type	Primary Constra	Primary Constraint Date	Project ID	Act #	Primary Resource	Total Float
C47777 - Fabricate/Deliver - Caulking & Sealant Sub per IB55	47777.C-2756	☐	NoRWP	NA	47777.C-2696	07.08.25	5	5	07.15.25	47777.C-2812, 47777.C-2867	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Fabricate/Deliver - Alum & Glass Sub per IB55	47777.C-2757	☐	NoRWP	NA	47777.C-2695	07.08.25	5	5	07.15.25	47777.C-2812, 47777.C-2867	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Fabricate/Deliver - LVT Flooring Sub per IB55	47777.C-2752	☐	NoRWP	NA	47777.C-2699	07.16.25	5	5	07.23.25	47777.C-2870	!05MGF08D.H	Resource Dependei	As Late As		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Fabricate/Deliver - Wall & Corner Protection Supplier per IB55	47777.C-2745	☐	NoRWP	NA	47777.C-2707	07.21.25	5	5	07.28.25	47777.C-2871	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Fabricate/Deliver - Toilet Access / Fire Cab Supplier per IB55	47777.C-2746	☐	NoRWP	NA	47777.C-2706	07.21.25	5	5	07.28.25	47777.C-2872	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - Fabricate/Deliver - Ceramic Tile Sub per IB55	47777.C-2747	☐	NoRWP	NA	47777.C-2705	02.04.27	5	5	02.10.27	47777.C-2667, 47777.C-2665, 47777.C-2666	!05MGF08D.H	Resource Dependei	As Late As Possible		R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
Mobilize						03.24.25	654	0	10.18.27		!05MGF08D.H					8		6
C47777- BASELINE Turnover 4B 3/24/25	47777.C-2903	☑	NoRWP	NA	MLST.0-200	03.24.25	0	0	03.24.25	47777.C-2875	!05MGF08D.H	Resource Dependei	Finish On or	03.24.25	R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	-1
C47777 - BASELINE Turnover flr 5b 7/9/25 from C47103 Update #26	47777.C-2905	☑	NoRWP	NA	MLST.0-200	07.09.25	0	0	07.09.25	47777.C-2876	!05MGF08D.H	Resource Dependei	Start On	07.09.25	R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	0
C47777 Floor 4B - COMPLETION / Obtain C47103 - 7B (11/26/25 update #26)	47777.C-2137	☐	NoRWP	N/A	47777.C-2134, 47777.C-2135, 47103.C-2136	09.10.25	0	0	09.10.25	47777.C-2858	!05MGF08D.H	Resource Dependei	Start On or Before	11.26.25	R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 Floor 5B - COMPLETION 5B / Obtain 8B (MS) (01/8/26 update #26)	47777.C-2902	☐	NoRWP	N/A	47777.C-2899, 47777.C-2901	10.21.25	0	0	10.21.25	47777.C-2658	!05MGF08D.H	Resource Dependei	Start On or Before	01.08.26	R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - Complete 9B C47103 // Get 12A & 12B C47777 (MS)	47777.C-2684	☐	NoRWP	n/a	47777.C-2904	10.14.26	0	0	10.14.26	47777.C-2656	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - BASELINE Turnover12th floor 10/14/26 for C47103 Update#26	47777.C-2904	☑	NoRWP	NA	MLST.0-200	10.14.26	0	0	10.14.26	47777.C-2684	!05MGF08D.H	Resource Dependei	Start On	10.14.26	R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	0
C47777 Floor 4A - COMPLETION / to C47103 Reconfigure Dining Room & Remove Hoist (MS)	47777.C-2823	☐	NoRWP	N/A	47777.C-2820, 47777.C-2822	10.15.27	0	0	10.15.27	MLST.0-212	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 Floor 5A - COMPLETION / to C47103 Reconfigure Dining Room & Remove Hoist (MS)	47777.C-2851	☐	NoRWP	N/A	47777.C-2848, 47777.C-2850	10.18.27	0	0	10.18.27	MLST.0-212	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
4th & 5th Floor Upgrades						05.27.25	102	166	10.20.25		!05MGF08D.H					51		54
4th FL - Mold, Demo & Removals						05.27.25	7	14	06.05.25		!05MGF08D.H					4		55
C47777 - 4B Demo Ceilings	47777.C-2875	☐	NoRWP	n/a	47777.C-2726, 47777.C-2742, 47777.C-2903	05.27.25	2	4	05.29.25	47777.C-2854, 47777.C-2855	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - 4B MEP & FP Cut, Cap, & Drop	47777.C-2854	☐	NoRWP	n/a	47777.C-2875, 47777.C-2737, 47777.C-2733, 47777.C-2731, 47777.C-2730, 47777.C-2750, 47777.C-2744, 47777.C-2753, 47777.C-2754	05.29.25	1	4	05.30.25	47777.C-2855	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - 4B Demo Balance - Clgs, Walls, & Floors	47777.C-2855	☐	NoRWP	n/a	47777.C-2854, 47777.C-2875	05.30.25	2	4	06.03.25	47777.C-2856	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - 4B VERIFY EXISTING MEP & FP Systems & Arrangements	47777.C-2856	☐	NoRWP	n/a	47777.C-2855	06.03.25	2	2	06.05.25	47777.C-2857	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
4th FL - Framing, MEP Rough & Drywall						06.05.25	23	33	07.09.25		!05MGF08D.H					8		55
C47777 - 4B Fire Proofing Touch-Up	47777.C-2857	☐	NoRWP	n/a	47777.C-2856	06.05.25	2	2	06.09.25	47777.C-2858	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - 4B Frame New Walls w/ Hollow Mtl Bucks & Frames	47777.C-2858	☐	NoRWP	n/a	47777.C-2857, 47777.C-2749, 47777.C-2755	06.09.25	3	9	06.12.25	47777.C-2859	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55

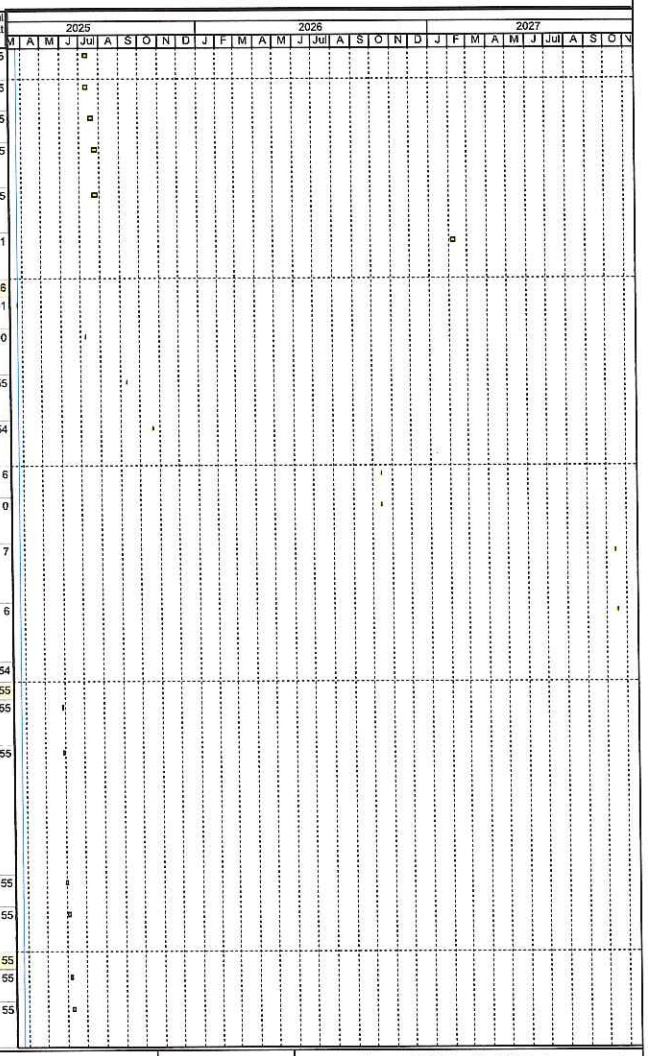

BL Baseline (Working) | BL Milestone | RWP Roofing | RWP PhyWork | RWP Heating | RWP WtrProofing | RWP Paving | RWP UGConduit | RWP Grubbing | RWP Seeding | RWP HVAC | RWP Stucco


- Filters: TASK filter: Excl WBS Summary Only.
- Data Date: 03.24.25
- Baseline:

000a - Baseline Plan

New York State
Office of General Services
Design & Construction

Printed: 06.16.25 13:53

Activity Name	Activity ID	Critical	!RWP	!DRWG	Predecessors	BL Start	BL Est Dur	BL Est Wkr Days	BL Finish	Successors	Calendar	Activity Type	Primary Constra	Primary Constraint Date	Project ID	Act #	Primary Resource	Total Float
C47777 - 4B MEP & FP Rough - Ceilings & Walls	47777.C-2859		NoRWP	n/a	47777.C-2858, 47777.C-2744	06.12.25	3	6	06.17.25	47777.C-2860	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - 4B Fire Stopping	47777.C-2860		NoRWP	n/a	47777.C-2859	06.17.25	2	2	06.19.25	47777.C-2861	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - 4B MEP & FP Inspectings / Testing	47777.C-2861		NoRWP	n/a	47777.C-2860	06.19.25	4	4	06.25.25	47777.C-2862	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - 4B GWB & T.S.Cigs & Walls	47777.C-2862		NoRWP	n/a	47777.C-2861	06.25.25	4	4	07.01.25	47777.C-2863	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - 4B Prime Paint	47777.C-2863		NoRWP	n/a	47777.C-2862, 47777.C-2748	07.01.25	1	2	07.02.25	47777.C-2864	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - 4B Install Ceiling Grid - Select Rooms	47777.C-2864		NoRWP	n/a	47777.C-2863	07.02.25	4	4	07.09.25	47777.C-2865	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
4th FL Finishes & Inspections						07.09.25	44	36	09.10.25		!05MGF08D.H					13		55
C47777 - 4B Install Millwork with Counters & Columns	47777.C-2865		NoRWP	n/a	47777.C-2864, 47777.C-2743, 47777.C-2751	07.09.25	2	4	07.11.25	47777.C-2866	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - 4B MEP Devices, Grills, Diffusers, Lights - In Ceilings	47777.C-2866		NoRWP	n/a	47777.C-2865	07.11.25	2	2	07.15.25	47777.C-2867	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - 4B Glass, Glazings, & Polycarb	47777.C-2867		NoRWP	n/a	47777.C-2866, 47777.C-2757, 47777.C-2756	07.15.25	3	9	07.18.25	47777.C-2868	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - 4B Acoustic Ciling Tiles w/ MEP & FP Devices	47777.C-2868		NoRWP	n/a	47777.C-2867	07.18.25	1	4	07.21.25	47777.C-2869	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - 4B Swing Doors / Install Hardware	47777.C-2869		NoRWP	n/a	47777.C-2868	07.21.25	2	2	07.23.25	47777.C-2870	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - 4B Vinyl Floor Tile (LVT) w/ base mold	47777.C-2870		NoRWP	n/a	47777.C-2869, 47777.C-2752	07.23.25	3	3	07.28.25	47777.C-2871, 47777.C-2873, 47777.C-2872	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - 4B Wall, Corner Guards & Bumpers	47777.C-2871		NoRWP	n/a	47777.C-2870, 47777.C-2745	07.28.25	2	2	07.30.25	47777.C-2874	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - 4B Misc Toilet & Bath Accessories, Fire Ext'grs, Misc	47777.C-2872		NoRWP	n/a	47777.C-2870, 47777.C-2746	07.28.25	2	2	07.30.25	47777.C-2874	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - 4B Finish Paint	47777.C-2873		NoRWP	n/a	47777.C-2870	07.28.25	2	2	07.30.25	47777.C-2874	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 - 4B Clean & Punchlist - Ready for Agency Review & Approval	47777.C-2874		NoRWP	n/a	47777.C-2871, 47777.C-2872, 47777.C-2873	07.30.25	2	2	08.01.25	47777.C-2134, 47777.C-2135	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 Floor 4B - Install Owner Furnished- Contractor Installed Items	47777.C-2134		NoRWP	NA	47777.C-2874	08.01.25	1	2	08.04.25	47103.C-2136, 47777.C-2137	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	56
C47777 Floor 4B-Final Furnishing, Owner Supplied Items, Misc	47777.C-2135		NoRWP	N/A	47777.C-2874	08.01.25	2	2	08.05.25	47103.C-2136, 47777.C-2137	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 Floor 4B - OGS/OMH FINAL INSPNs, FF & CLINICAL CLEANING (25wd)	47103.C-2136		NoRWP	N/A	47777.C-2134, 47777.C-2135	08.05.25	25	0	09.10.25	47777.C-2137	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Justin.Otto.A1.R3.E - J Otto	55
5th FL - Mold, Demo & Removals						07.09.25	7	16	07.17.25		!05MGF08D.H					5		54
C47777 - 5B Complete C47103 2B / Obtain 5B & Integrate into C47103 Shower Rm Work (MS)	47777.C-2875		NoRWP	n/a	47777.C-2905	07.09.25	0	0	07.09.25	47777.C-2877	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B Demo Ceilings	47777.C-2877		NoRWP	n/a	47777.C-2876	07.09.25	2	4	07.10.25	47777.C-2878, 47777.C-2879	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B MEP & FP Cut, Cap, & Drop	47777.C-2878		NoRWP	n/a	47777.C-2877	07.11.25	1	4	07.11.25	47777.C-2879	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B Demo Balance - Clgs, Walls, & Floors	47777.C-2879		NoRWP	n/a	47777.C-2877, 47777.C-2878	07.14.25	2	4	07.15.25	47777.C-2880	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B VERIFY EXISTING MEP & FP Systems & Arrangements	47777.C-2880		NoRWP	n/a	47777.C-2879	07.16.25	2	4	07.17.25	47777.C-2881	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
5th FL - Framing, MEP Rough & Drywall						07.18.25	22	31	08.18.25		!05MGF08D.H					8		54
C47777 - 5B Fire Proofing Touch-Up	47777.C-2881		NoRWP	n/a	47777.C-2880	07.18.25	2	2	07.21.25	47777.C-2882	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54

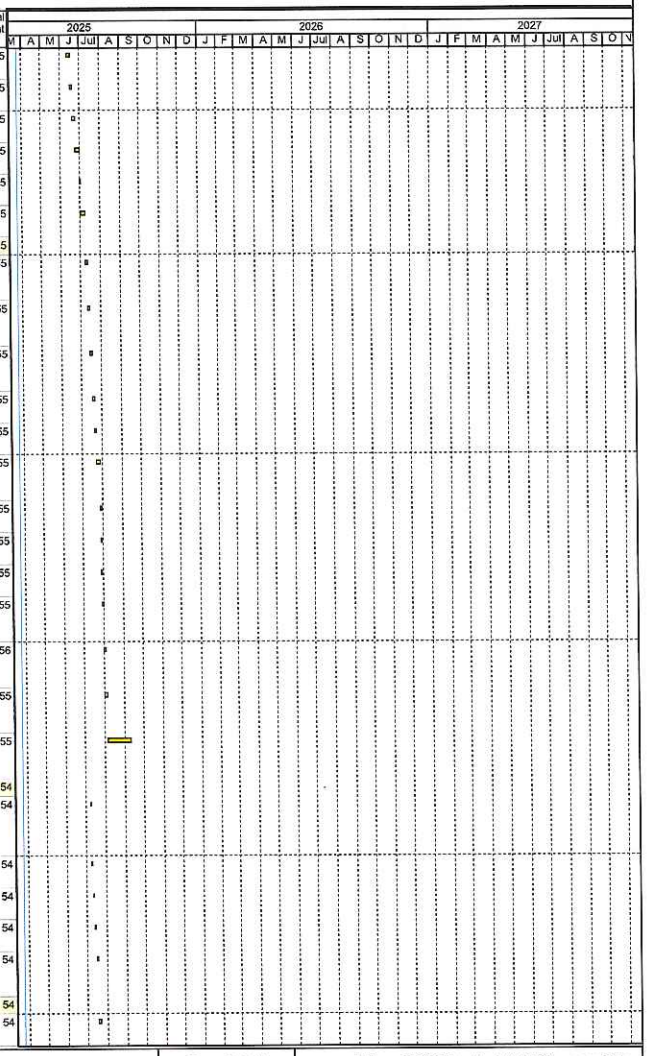

BL Baseline (Working)
BL Milestone
RWP Roofing
RWP PhyWork
RWP Heating
RWP WtrProofing
RWP Paving
RWP UGConduit
RWP Grubbing
RWP Seeding
RWP HVAC
RWP Stucco


- Filters: TASK filter: Excl WBS Summary Only.
- Data Date: 03.24.25
- Baseline:

000a - Baseline Plan

New York State
Office of General Services
Design & Construction

Printed: 06.16.25 13:53

Activity Name	Activity ID	Critica	!RWP	!DRWG	Predecessors	BL Start	BL Est Dur	BL Est Wkr Days	BL Finish	Successors	Calendar	Activity Type	Primary Constra	Primary Constraint Date	Project ID	Act #	Primary Resource	Total Float
C47777 - 5B Frame New Walls w/ Hollow Mtl Bucks & Frames	47777.C-2882		NoRWP	n/a	47777.C-2881	07.22.25	3	9	07.24.25	47777.C-2883	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B MEP & FP Rough - Ceilings & Walls	47777.C-2883		NoRWP	n/a	47777.C-2882	07.25.25	2	4	07.28.25	47777.C-2884	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B Fire Stopping	47777.C-2884		NoRWP	n/a	47777.C-2883	07.29.25	2	2	07.30.25	47777.C-2885	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B MEP & FP Inspectings / Testing	47777.C-2885		NoRWP	n/a	47777.C-2884	07.31.25	4	4	08.05.25	47777.C-2886	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B GWB & T.S.Clgs & Walls	47777.C-2886		NoRWP	n/a	47777.C-2885	08.06.25	4	4	08.11.25	47777.C-2887	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B Prime Paint	47777.C-2887		NoRWP	n/a	47777.C-2886	08.12.25	1	2	08.12.25	47777.C-2888	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B Install Ceiling Grid - Select Rooms	47777.C-2888		NoRWP	n/a	47777.C-2887	08.13.25	4	4	08.18.25	47777.C-2889	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
5th FL Finishes & Inspections						08.19.25	44	36	10.20.25		!05MGF08D.H					13		54
C47777 - 5B Install Millwork with Counters & Columns	47777.C-2889		NoRWP	n/a	47777.C-2888	08.19.25	2	4	08.20.25	47777.C-2890	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B MEP Devices, Grills, Diffusers, Lights - In Ceilings	47777.C-2890		NoRWP	n/a	47777.C-2889	08.21.25	2	4	08.22.25	47777.C-2891	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B Glass, Glazings, & Polycarb	47777.C-2891		NoRWP	n/a	47777.C-2890	08.25.25	3	9	08.27.25	47777.C-2892	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B Acoustic Ciling Tiles w/ MEP & FP Devices	47777.C-2892		NoRWP	n/a	47777.C-2891	08.28.25	1	4	08.28.25	47777.C-2893	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B Swing Doors / Install Hardware	47777.C-2893		NoRWP	n/a	47777.C-2892	08.29.25	2	2	09.02.25	47777.C-2894	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B Vinyl Floor Tile (LVT) w/ base mold	47777.C-2894		NoRWP	n/a	47777.C-2893	09.03.25	3	3	09.05.25	47777.C-2897, 47777.C-2896, 47777.C-2895	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B Wall, Corner Guards & Bumpers	47777.C-2895		NoRWP	n/a	47777.C-2894	09.08.25	2	2	09.09.25	47777.C-2898	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B Misc Toilet & Bath Accessories, Fire Ext'grs, Misc	47777.C-2896		NoRWP	n/a	47777.C-2894	09.08.25	2	2	09.09.25	47777.C-2898	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B Finish Paint	47777.C-2897		NoRWP	n/a	47777.C-2894	09.08.25	2	2	09.09.25	47777.C-2898	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 - 5B Clean & Punchlist - Ready for Agency Review & Approval	47777.C-2898		NoRWP	n/a	47777.C-2895, 47777.C-2896, 47777.C-2897	09.10.25	2	2	09.11.25	47777.C-2899, 47777.C-2900	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 Floor 5B - Install Owner Furnished- Contractor Installed Items	47777.C-2899		NoRWP	NA	47777.C-2898	09.12.25	1	2	09.12.25	47777.C-2902, 47777.C-2901, 47777.C-2901	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	55
C47777 Floor 5B-Final Furnishing, Owner Suppied Items, Misc	47777.C-2900		NoRWP	N/A	47777.C-2898	09.12.25	2	0	09.15.25	47777.C-2901	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	54
C47777 Floor 5B - OGS/OMH FINAL INSPNs, FF & CLINICAL CLEANING (25wd)	47777.C-2901		NoRWP	N/A	47777.C-2899, 47777.C-2899, 47777.C-2900	09.16.25	25	0	10.20.25	47777.C-2902	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Justin.Otto.A1.R3.E - J Otto	54
12th Floor Upgrades						10.14.26	184	1351	07.06.27		!05MGF08D.H					71		6
12th FL - Demo & Removals						10.14.26	51	400	12.24.26		!05MGF08D.H					19		21
C47777 - DEVELOP HOIST ACCESS TO 12th FLR	47777.C-2656		NoRWP	n/a	47777.C-2684	10.14.26	8	16	10.23.26	47777.C-2657	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12B Install Temporary Protections (Select Rooms & Lobby Core Area)	47777.C-2657		NoRWP	n/a	47777.C-2656	10.26.26	3	3	10.28.26	47777.C-2658	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12B Selective Demolition	47777.C-2658		NoRWP	n/a	47777.C-2657, 47777.C-2137, 47777.C-2902	10.29.26	10	80	11.11.26	47777.C-2685, 47777.C-2659, 47777.C-2765	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12B Overhead Mech'l Review & Corrd's based on previously Approved MEP& FP shop dwgs	47777.C-2659		NoRWP	n/a	47777.C-2658	11.12.26	5	20	11.18.26	47777.C-2660, 47777.C-2766	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	36
C47777 -12B IB# (unforseen mold) OGS Potential ID of Mold	47777.C-2685		NoRWP	n/a	47777.C-2658	11.12.26	2	2	11.13.26	47777.C-2686, 47777.C-2767	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6

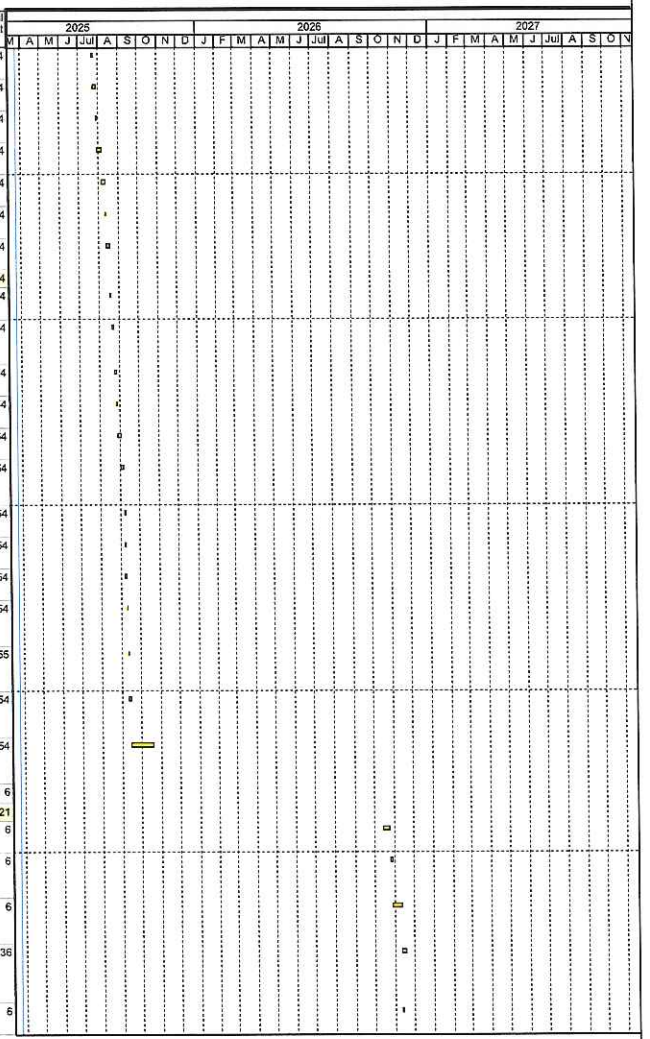

BL Baseline (Working) | BL Milestone | RWP Roofing | RWP PhyWork | RWP Heating | RWP WtrProofing | RWP Paving | RWP UGConduit | RWP Grubbing | RWP Seeding | RWP HVAC | RWP Stucco


- Filters: TASK filter: Excl WBS Summary Only.
- Data Date: 03.24.25
- Baseline:

000a - Baseline Plan

New York State
Office of General Services
Design & Construction

Printed: 06.16.25 13:53

Activity Name	Activity ID	Critical	!RWP	!DRWG	Predecessors	BL Start	BL Est Dur	BL Est Wkr Days	BL Finish	Successors	Calendar	Activity Type	Primary Constra	Primary Constraint Date	Project ID	Act #	Primary Resource	Total Float
C47777 -12A Selective Demolition	47777.C-2765		NoRWP	n/a	47777.C-2658	11.12.26	10	80	11.25.26	47777.C-2767, 47777.C-2766	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 -12B IB# (unforseen mold) PDC/Abatement Contr Mobilize For Abatement	47777.C-2686		NoRWP	n/a	47777.C-2685	11.16.26	1	1	11.16.26	47777.C-2687	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12B IB# (unforseen mold) PDC/Abate Sub - ABATEMENTS Identified Mold	47777.C-2687		NoRWP	n/a	47777.C-2686	11.17.26	10	50	12.01.26	47777.C-2688, 47777.C-2689	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12A Overhead Mech'l Review & Corrd's based on previously Approved MEP& FP shop dwgs	47777.C-2766		NoRWP	n/a	47777.C-2765, 47777.C-2659	11.27.26	5	25	12.03.26	47777.C-2774	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	36
C47777 -12A IB# (unforseen mold) OGS Potential ID of Mold	47777.C-2767		NoRWP	n/a	47777.C-2765, 47777.C-2685	11.27.26	2	1	11.30.26	47777.C-2768	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 -12A IB# (unforseen mold) PDC/Abatement Contr Mobilize For Abatement	47777.C-2768		NoRWP	n/a	47777.C-2767	12.01.26	1	1	12.01.26	47777.C-2769	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 -12B IB# (unforseen mold) PDC/Plumber proceed with Plumbing ((Floor Below)) REQUIRED?	47777.C-2688		NoRWP	n/a	47777.C-2687	12.02.26	1	1	12.02.26	47777.C-2690	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12B IB# (unforseen mold) OGS Identifies Metal Stub Replacement Scope	47777.C-2689		NoRWP	n/a	47777.C-2687	12.02.26	1	1	12.02.26	47777.C-2690	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12A IB# (unforseen mold) PDC/Abate Sub - ABATEMENTS Identified Mold	47777.C-2769		NoRWP	n/a	47777.C-2768	12.02.26	10	50	12.15.26	47777.C-2771, 47777.C-2770	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 -12B IB# (unforseen mold) PDC/JDT Replace Damaged Metal Studs	47777.C-2690		NoRWP	n/a	47777.C-2689, 47777.C-2688	12.03.26	1	4	12.03.26	47777.C-2662	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12B Frame Walls, Partitions, Hard Ceilings W/ HM Bucks & Windows	47777.C-2662		NoRWP	n/a	47777.C-2690	12.04.26	15	60	12.24.26	47777.C-2660, 47777.C-2661, 47777.C-2773	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12A IB# (unforseen mold) PDC/Plumber proceed with Plumbing ((Floor Below)) required?	47777.C-2770		NoRWP	n/a	47777.C-2769	12.16.26	1	0	12.16.26	47777.C-2772	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 -12A IB# (unforseen mold) OGS Identifies Metal Stub Replacement Scope	47777.C-2771		NoRWP	n/a	47777.C-2769	12.16.26	1	1	12.16.26	47777.C-2772	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 -12A IB# (unforseen mold) PDC/JDT Replace Damaged Metal Studs	47777.C-2772		NoRWP	n/a	47777.C-2771, 47777.C-2770	12.17.26	1	4	12.17.26	47777.C-2773	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
12th FL - Framing, MEP Rough & Drywall						12.28.26	60	416	03.22.27		!05MGF08D.H					17		6
C47777 -12B MEP & FP Rough-In .. OH & In-Wall ... Core & BR/BR Areas	47777.C-2660		NoRWP	n/a	47777.C-2659, 47777.C-2662	12.28.26	10	40	01.11.27	47777.C-2691, 47777.C-2663, 47777.C-2670, 47777.C-2774	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 -12B Install In-Wall Blocking	47777.C-2661		NoRWP	n/a	47777.C-2662	12.28.26	4	4	12.31.26	47777.C-2664	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	29
C47777 -12A Frame Walls, Partitions, Hard Ceilings W/ HM Bucks & Windows	47777.C-2773		NoRWP	n/a	47777.C-2772, 47777.C-2662	12.28.26	15	60	01.18.27	47777.C-2775, 47777.C-2774	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12B MEP & FP Rough In Acoust Ceiling Areas	47777.C-2670		NoRWP	n/a	47777.C-2660	01.12.27	10	40	01.25.27	47777.C-2663, 47777.C-2776	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 -12B Fire Proofing Touch-Up	47777.C-2691		NoRWP	n/a	47777.C-2660	01.12.27	5	10	01.18.27	47777.C-2663	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	16
C47777 -12A MEP & FP Rough-In .. OH & In-Wall ... Core & BR/BR Areas	47777.C-2774		NoRWP	n/a	47777.C-2766, 47777.C-2773, 47777.C-2660	01.19.27	10	40	02.01.27	47777.C-2776, 47777.C-2777, 47777.C-2778	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12A Install In-Wall Blocking	47777.C-2775		NoRWP	n/a	47777.C-2773	01.19.27	4	4	01.22.27	47777.C-2779	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	24
C47777 -12B MEP & FP Rough Inspections	47777.C-2663		NoRWP	n/a	47777.C-2660, 47777.C-2670, 47777.C-2691	01.26.27	2	2	01.27.27	47777.C-2664	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11

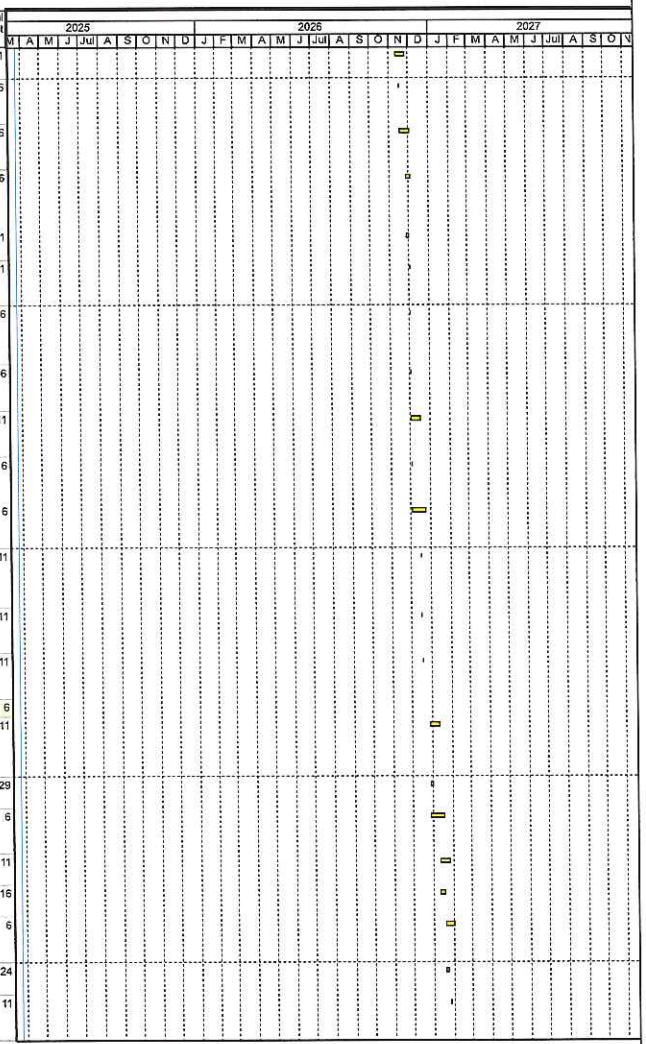

BL Baseline (Working) | BL Milestone | RWP Roofing | RWP PhyWork | RWP Heating | RWP WtrProofing | RWP Paving | RWP UGConduit | RWP Grubbing | RWP Seeding | RWP HVAC | RWP Stucco


- Filters: TASK filter: Excl WBS Summary Only.
- Data Date: 03.24.25
- Baseline:

000a - Baseline Plan

New York State
Office of General Services
Design & Construction

Printed: 06.16.25 13:53

Activity Name	Activity ID	Critica	!RWP	!DRWG	Predecessors	BL Start	BL Est Dur	BL Est Wkr Days	BL Finish	Successors	Calendar	Activity Type	Primary Constra	Primary Constraint Date	Project ID	Act #	Primary Resource	Total Float
C47777 -12B GWB w/ t+s - Walls & Select Ceilings	47777.C-2664		NoRWP	n/a	47777.C-2663, 47777.C-2661	01.28.27	10	40	02.10.27	47777.C-2665, 47777.C-2668, 47777.C-2673	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 -12A MEP & FP Rough in Acoust Ceiling Areas	47777.C-2776		NoRWP	n/a	47777.C-2774, 47777.C-2670	02.02.27	10	40	02.15.27	47777.C-2778	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12A Fire Proofing Touch-Up	47777.C-2777		NoRWP	n/a	47777.C-2774	02.02.27	5	10	02.08.27	47777.C-2778	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 -12B Shower Room - Install Backer Board	47777.C-2665		NoRWP	n/a	47777.C-2664, 47777.C-2747	02.11.27	3	12	02.15.27	47777.C-2666, 47777.C-2780	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 -12B Shower Rooms - Install Waterproofing System (w/ testing)	47777.C-2666		NoRWP	n/a	47777.C-2665, 47777.C-2747	02.16.27	10	30	03.01.27	47777.C-2667, 47777.C-2783	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 -12A MEP & FP Rough Inspections	47777.C-2778		NoRWP	n/a	47777.C-2774, 47777.C-2776, 47777.C-2777	02.16.27	2	2	02.17.27	47777.C-2779	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12A GWB w/ t+s - Walls & Select Ceilings	47777.C-2779		NoRWP	n/a	47777.C-2775, 47777.C-2778	02.18.27	10	40	03.03.27	47777.C-2782, 47777.C-2781, 47777.C-2780	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12A Shower Room - Install Backer Board	47777.C-2780		NoRWP	n/a	47777.C-2779, 47777.C-2665	03.04.27	3	12	03.08.27	47777.C-2783	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12A Shower Rooms - Install Waterproofing System (w/ testing)	47777.C-2783		NoRWP	n/a	47777.C-2780, 47777.C-2666	03.09.27	10	30	03.22.27	47777.C-2790	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
12th FL Finishes & Inspections						02.11.27	101	535	07.06.27		!05MGF08D.H					35		6
C47777 -12B Prime Paint Walls	47777.C-2668		NoRWP	n/a	47777.C-2664	02.11.27	5	10	02.17.27	47777.C-2669, 47777.C-2671, 47777.C-2781	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	25
C47777 -12B Nurses Station Millwork / Other Millwk	47777.C-2673		NoRWP	n/a	47777.C-2664	02.11.27	10	30	02.24.27	47777.C-2759, 47777.C-2674, 47777.C-2782	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	26
C47777 -12B Install Acoustical Ceiling Framng	47777.C-2669		NoRWP	n/a	47777.C-2668	02.18.27	4	4	02.23.27	47777.C-2677, 47777.C-2678, 47777.C-2784	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	25
C47777 -12B Swing Doors / Install Hardware	47777.C-2671		NoRWP	n/a	47777.C-2668	02.18.27	5	10	02.24.27	47777.C-2675, 47777.C-2785, 47777.C-2786	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	34
C47777 -12B Finish Mechanical	47777.C-2677		NoRWP	n/a	47777.C-2669	02.24.27	5	15	03.02.27	47777.C-2679	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	25
C47777 -12B Finish Sprinkler	47777.C-2678		NoRWP	n/a	47777.C-2669	02.24.27	5	15	03.02.27	47777.C-2679, 47777.C-2787	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	25
C47777 -12B Install Glass & Glazings	47777.C-2674		NoRWP	n/a	47777.C-2673	02.25.27	3	3	03.01.27	47777.C-2675, 47777.C-2788	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	31
C47777 -12B Install Finish LVT Flooring	47777.C-2759		NoRWP	n/a	47777.C-2673	02.25.27	8	24	03.08.27	47777.C-2675	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	26
C47777 -12B Shower Room Ceramic Tile Installations	47777.C-2667		NoRWP	n/a	47777.C-2666, 47777.C-2747	03.02.27	7	21	03.10.27	47777.C-2676, 47777.C-2790	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 -12A Prime Paint Walls	47777.C-2781		NoRWP	n/a	47777.C-2779, 47777.C-2668	03.04.27	5	10	03.10.27	47777.C-2785, 47777.C-2784	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	20
C47777 -12A Nurses Station Millwork / Other Millwk	47777.C-2782		NoRWP	n/a	47777.C-2779, 47777.C-2673	03.04.27	10	30	03.17.27	47777.C-2788, 47777.C-2789	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	21
C47777 -12B Finish Plumbing	47777.C-2676		NoRWP	n/a	47777.C-2667	03.11.27	8	24	03.22.27	47777.C-2680, 47777.C-2679, 47777.C-2791, 47777.C-2792	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 -12A Install Acoustical Ceiling Framng	47777.C-2784		NoRWP	n/a	47777.C-2781, 47777.C-2669	03.11.27	4	4	03.16.27	47777.C-2786, 47777.C-2787	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	20
C47777 -12A Swing Doors / Install Hardware	47777.C-2785		NoRWP	n/a	47777.C-2781, 47777.C-2671	03.11.27	5	10	03.17.27	47777.C-2793	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	29
C47777 -12A Finish Mechanical	47777.C-2786		NoRWP	n/a	47777.C-2784, 47777.C-2671	03.17.27	5	15	03.23.27	47777.C-2792	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	20
C47777 -12A Finish Sprinkler	47777.C-2787		NoRWP	n/a	47777.C-2784, 47777.C-2678	03.17.27	5	15	03.23.27	47777.C-2792	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	20
C47777 -12A Install Glass & Glazings	47777.C-2788		NoRWP	n/a	47777.C-2782, 47777.C-2674	03.18.27	3	3	03.22.27	47777.C-2793	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	26

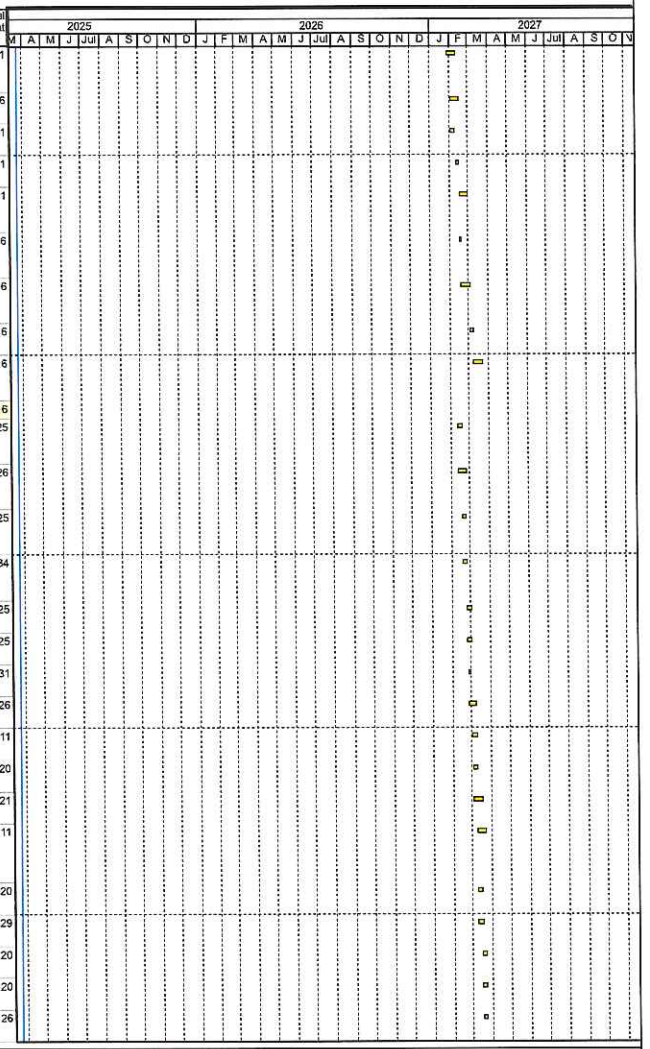

BL Baseline (Working) | BL Milestone | RWP Roofing | RWP PhyWork | RWP Heating | RWP WtrProofing | RWP Paving | RWP UGConduit | RWP Grubbing | RWP Seeding | RWP HVAC | RWP Stucco


- Filters: TASK filter: Excl WBS Summary Only.
- Data Date: 03.24.25
- Baseline:

000a - Baseline Plan

New York State
Office of General Services
Design & Construction

Printed: 06.16.25 13:53

Activity Name	Activity ID	Critica	!RWP	!DRWG	Predecessors	BL Start	BL Est Dur	BL Est Wkr Days	BL Finish	Successors	Calendar	Activity Type	Primary Constra	Primary Constraint Date	Project ID	Act #	Primary Resource	Total Float
C47777 -12A Install Finish LVT Flooring	47777.C-2789		NoRWP	n/a	47777.C-2782	03.18.27	8	24	03.29.27	47777.C-2793	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	21
C47777 -12B Install RCP Ceiling Tiles	47777.C-2679		NoRWP	n/a	47777.C-2677, 47777.C-2678, 47777.C-2676	03.23.27	5	20	03.29.27	47777.C-2675, 47777.C-2792	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 -12A Shower Room Ceramic Tile Installations	47777.C-2790		NoRWP	n/a	47777.C-2783, 47777.C-2667	03.23.27	7	21	03.31.27	47777.C-2791	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12B Finish Painting	47777.C-2675		NoRWP	n/a	47777.C-2671, 47777.C-2759, 47777.C-2679, 47777.C-2674	03.30.27	8	24	04.08.27	47777.C-2672, 47777.C-2793	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 -12A Finish Plumbing	47777.C-2791		NoRWP	n/a	47777.C-2790, 47777.C-2676	04.01.27	8	24	04.12.27	47777.C-2795, 47777.C-2792	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12B Install Handrails, Bump Rails	47777.C-2672		NoRWP	n/a	47777.C-2675	04.09.27	5	15	04.15.27	47777.C-2680, 47777.C-2794	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 -12A Install RCP Ceiling Tiles	47777.C-2792		NoRWP	n/a	47777.C-2786, 47777.C-2787, 47777.C-2791, 47777.C-2676, 47777.C-2679	04.13.27	5	15	04.19.27	47777.C-2793	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12B Install Toilet Rm Accessories / Misc Finishes	47777.C-2680		NoRWP	n/a	47777.C-2676, 47777.C-2672	04.16.27	10	30	04.29.27	47777.C-2681, 47777.C-2682, 47777.C-2795	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	11
C47777 -12A Finish Painting	47777.C-2793		NoRWP	n/a	47777.C-2785, 47777.C-2788, 47777.C-2789, 47777.C-2792, 47777.C-2675	04.20.27	8	24	04.29.27	47777.C-2794	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12B Final Inspections	47777.C-2681		NoRWP	n/a	47777.C-2680	04.30.27	5	10	05.06.27	47777.C-2683, 47777.C-2764	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	21
C47777 -12B Clean-up, Touch Up, & Punchlist,	47777.C-2682		NoRWP	n/a	47777.C-2680	04.30.27	5	20	05.06.27	47777.C-2683, 47777.C-2764	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	21
C47777 -12A Install Handrails, Bump Rails	47777.C-2794		NoRWP	n/a	47777.C-2793, 47777.C-2672	04.30.27	5	15	05.06.27	47777.C-2795	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12B OGS/OMH 25 day check-out, FFE & occupy	47777.C-2683		NoRWP	n/a	47777.C-2682, 47777.C-2681	05.07.27	25	0	06.11.27	47777.C-2764	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Justin.Otto.A1.R3.E - J Otto	21
C47777 -12A Install Toilet Rm Accessories / Misc Finishes	47777.C-2795		NoRWP	n/a	47777.C-2791, 47777.C-2794, 47777.C-2680	05.07.27	10	30	05.20.27	47777.C-2797, 47777.C-2796	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12A Final Inspections	47777.C-2796		NoRWP	n/a	47777.C-2795	05.21.27	5	10	05.27.27	47777.C-2798, 47777.C-2764	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12A Clean-up, Touch Up, & Punchlist,	47777.C-2797		NoRWP	n/a	47777.C-2795	05.21.27	5	10	05.27.27	47777.C-2798, 47777.C-2764	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 -12A OGS/OMH 25 day check-out, FFE & occupy	47777.C-2798		NoRWP	n/a	47777.C-2796, 47777.C-2797	05.28.27	25	0	07.02.27	47777.C-2764	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Justin.Otto.A1.R3.E - J Otto	6
C47777 - Complete 12A & 12B - Get 4A & 5A Nurses Stations (MS)	47777.C-2764		NoRWP	n/a	47777.C-2683, 47777.C-2798, 47777.C-2681, 47777.C-2797, 47777.C-2796, 47777.C-2682	07.06.27	0	0	07.06.27	47777.C-2824, 47777.C-2826	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
Final Tie-Ins & Inspections						07.06.27	73	159	10.15.27		!05MGF08D.H					52		6
4th, 5th, & 6th Floor Tie-Ins						07.06.27	73	159	10.15.27		!05MGF08D.H					52		6
C47777 - 4A Demo Ceilings	47103.C-2653		NoRWP	a101.3	47777.C-2824	07.06.27	2	4	07.07.27	47777.C-2799	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 4A Completed 12A & 12B / Obtain 4A (MS)	47777.C-2824		NoRWP	n/a	47777.C-2764	07.06.27	0	0	07.06.27	47103.C-2653	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 5A Demo Ceilings	47777.C-2825		NoRWP	n/a	47777.C-2826	07.06.27	2	4	07.07.27	47777.C-2828, 47777.C-2827	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 5A Completed 12A & 12B / Obtain 5A (MS)	47777.C-2826		NoRWP	n/a	47777.C-2764	07.06.27	0	0	07.06.27	47777.C-2825	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 4A MEP & FP Cut, Cap, & Drop	47777.C-2799		NoRWP	m,fp,p,e-	47103.C-2653	07.08.27	1	4	07.08.27	47777.C-2800	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7

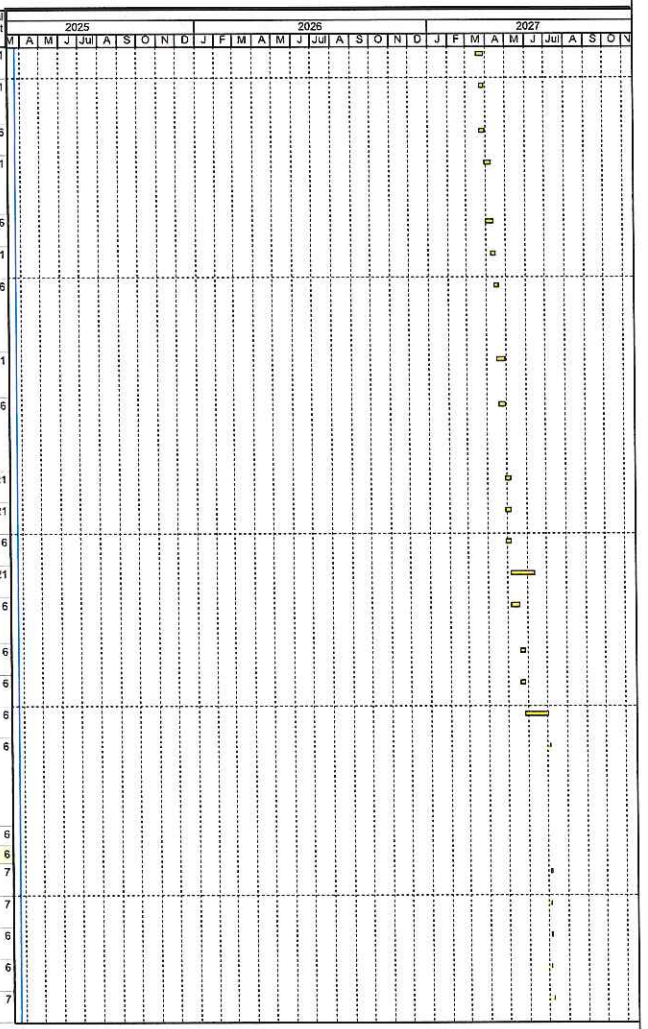

BL Baseline (Working) | BL Milestone | RWP Roofing | RWP PhyWork | RWP Heating | RWP WtrProofing | RWP Paving | RWP UGConduit | RWP Grubbing | RWP Seeding | RWP HVAC | RWP Stucco


- Filters: TASK filter: Excl WBS Summary Only.
- Data Date: 03.24.25
- Baseline:

000a - Baseline Plan

New York State
Office of General Services
Design & Construction

Printed: 06.16.25 13:53

Activity Name	Activity ID	Critica	!RWP	!DRWG	Predecessors	BL Start	BL Est Dur	BL Est Wkr Days	BL Finish	Successors	Calendar	Activity Type	Primary Constra	Primary Constraint Date	Project ID	Act #	Primary Resource	Total Float
C47777 - 5A MEP & FP Cut, Cap, & Drop	47777.C-2827		NoRWP	n/a	47777.C-2825	07.08.27	1	4	07.08.27	47777.C-2828	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 4A Demo Balance - Clgs, Walls, & Floors	47777.C-2800		NoRWP	a101.3	47777.C-2799	07.09.27	2	4	07.12.27	47777.C-2801	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 5A Demo Balance - Clgs, Walls, & Floors	47777.C-2828		NoRWP	n/a	47777.C-2825, 47777.C-2827	07.09.27	2	4	07.12.27	47777.C-2829	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 4A VERIFY EXISTING MEP & FP Systems & Arrangements	47777.C-2801		NoRWP	m,fp,p,e-	47777.C-2800	07.13.27	2	2	07.14.27	47777.C-2802	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 5A VERIFY EXISTING MEP & FP Systems & Arrangements	47777.C-2829		NoRWP	n/a	47777.C-2828	07.13.27	2	8	07.14.27	47777.C-2830	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 4A Fire Proofing Touch-Up	47777.C-2802		NoRWP	notes	47777.C-2801	07.15.27	2	2	07.16.27	47777.C-2803	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 5A Fire Proofing Touch-Up	47777.C-2830		NoRWP	n/a	47777.C-2829	07.15.27	2	2	07.16.27	47777.C-2831	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 4A Frame New Walls w/ Hollow Mtl Bucks & Frames	47777.C-2803		NoRWP	notes C47103	47777.C-2802, 47777.C-2755	07.19.27	2	4	07.20.27	47777.C-2804	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 5A Frame New Walls w/ Hollow Mtl Bucks & Frames	47777.C-2831		NoRWP	n/a	47777.C-2830	07.19.27	2	4	07.20.27	47777.C-2832	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 4A MEP & FP Rough - Ceilings & Walls	47777.C-2804		NoRWP	m,fp,p,e-	47777.C-2803	07.21.27	2	4	07.22.27	47777.C-2805	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 5A MEP & FP Rough - Ceilings & Walls	47777.C-2832		NoRWP	n/a	47777.C-2831	07.21.27	2	4	07.22.27	47777.C-2833	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 4A Fire Stopping	47777.C-2805		NoRWP	notes	47777.C-2804	07.23.27	2	2	07.26.27	47777.C-2806	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 5A Fire Stopping	47777.C-2833		NoRWP	n/a	47777.C-2832	07.23.27	2	2	07.26.27	47777.C-2834	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 4A MEP & FP Inspectings / Testing	47777.C-2806		NoRWP	notes	47777.C-2805	07.27.27	4	4	07.30.27	47777.C-2807	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 5A MEP & FP Inspectings / Testing	47777.C-2834		NoRWP	n/a	47777.C-2833	07.27.27	4	4	07.30.27	47777.C-2835	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 4A GWB & T.S.Clgs & Walls	47777.C-2807		NoRWP	notes C47103	47777.C-2806	08.02.27	4	4	08.05.27	47777.C-2808	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 5A GWB & T.S.Clgs & Walls	47777.C-2835		NoRWP	n/a	47777.C-2834	08.02.27	4	4	08.05.27	47777.C-2836	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 4A Prime Paint	47777.C-2808		NoRWP	a205	47777.C-2807	08.06.27	1	2	08.06.27	47777.C-2809	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 5A Prime Paint	47777.C-2836		NoRWP	n/a	47777.C-2835	08.06.27	1	2	08.06.27	47777.C-2837	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 4A Install Ceilng Grid - Select Rooms	47777.C-2809		NoRWP	a302	47777.C-2808	08.09.27	4	4	08.12.27	47777.C-2810	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 5A Install Ceiling Grid - Select Rooms	47777.C-2837		NoRWP	n/a	47777.C-2836	08.09.27	4	4	08.12.27	47777.C-2838	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 4A Install Millwork with Counters & Columns	47777.C-2810		NoRWP	notes C47103	47777.C-2809	08.13.27	2	4	08.16.27	47777.C-2811	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 5A Install Millwork with Counters & Columns	47777.C-2838		NoRWP	n/a	47777.C-2837	08.13.27	2	4	08.16.27	47777.C-2839	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 4A MEP Devices, Grills, Diffusers, Lights - In Ceilings	47777.C-2811		NoRWP	m,fp,p,e-	47777.C-2810	08.17.27	2	2	08.18.27	47777.C-2812	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 5A MEP Devices, Grills, Diffusers, Lights - In Ceilings	47777.C-2839		NoRWP	n/a	47777.C-2838	08.17.27	3	9	08.19.27	47777.C-2840	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 4A Glass. Glazings, & Polycarb	47777.C-2812		NoRWP	notes C47103	47777.C-2811, 47777.C-2756, 47777.C-2757	08.19.27	3	9	08.23.27	47777.C-2813	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 5A Glass. Glazings, & Polycarb	47777.C-2840		NoRWP	n/a	47777.C-2839	08.20.27	3	3	08.24.27	47777.C-2841	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 4A Acoustic Clng Tiles w/ MEP & FP Devices	47777.C-2813		NoRWP	notes C47103	47777.C-2812	08.24.27	1	4	08.24.27	47777.C-2814	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 4A Swing Doors / Install Hardware	47777.C-2814		NoRWP	a500.3	47777.C-2813	08.25.27	2	2	08.26.27	47777.C-2815	!05MGF08D.H	Resource Depender			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7

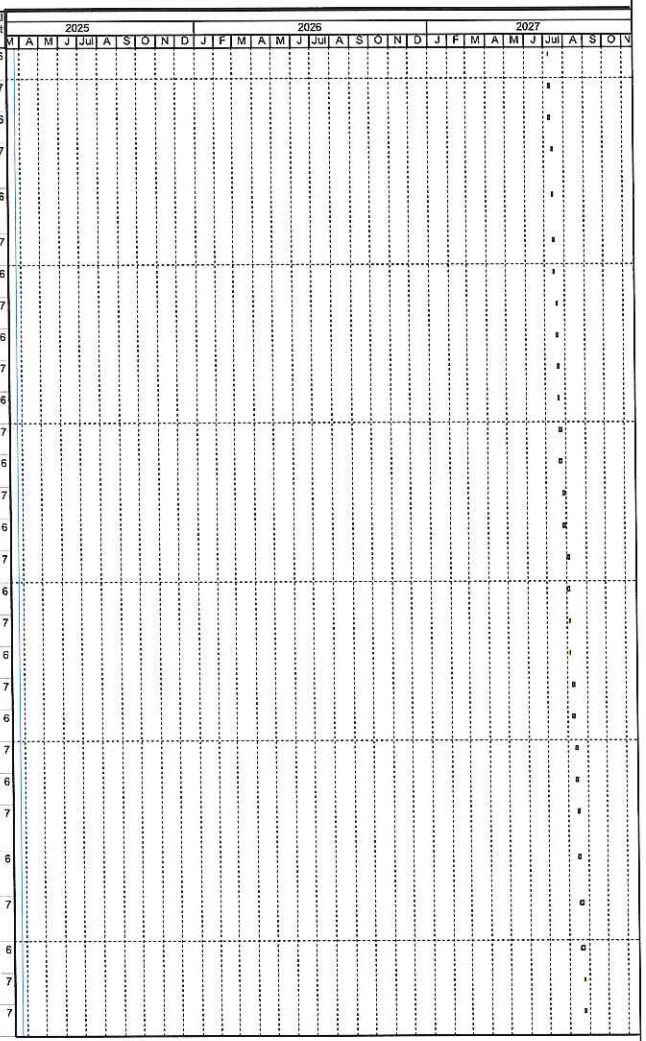

BL Baseline (Working) | BL Milestone | RWP Roofing | RWP PhyWork | RWP Heating | RWP WtrProofing | RWP Paving | RWP UGConduit | RWP Grubbing | RWP Seeding | RWP HVAC | RWP Stucco


- Filters: TASK filter: Excl WBS Summary Only.
- Data Date: 03.24.25
- Baseline:

000a - Baseline Plan

New York State
Office of General Services
Design & Construction

Printed: 06.16.25 13:53

Activity Name	Activity ID	Critical	!RWP	!DRWG	Predecessors	BL Start	BL Est Dur	BL Est Wkr Days	BL Finish	Successors	Calendar	Activity Type	Primary Constra	Primary Constraint Date	Project ID	Act #	Primary Resource	Total Float
C47777 - 5A Acoustic Ciling Tiles w/ MEP & FP Devices	47777.C-2841		NoRWP	n/a	47777.C-2840	08.25.27	1	4	08.25.27	47777.C-2842	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 5A Swing Doors / Install Hardware	47777.C-2842		NoRWP	n/a	47777.C-2841	08.26.27	2	2	08.27.27	47777.C-2843	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 4A Vinyl Floor Tile (LVT) w/ base mold	47777.C-2815		NoRWP	a902.2	47777.C-2814	08.27.27	3	3	08.31.27	47777.C-2816, 47777.C-2817, 47777.C-2818	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 5A Vinyl Floor Tile (LVT) w/ base mold	47777.C-2843		NoRWP	n/a	47777.C-2842	08.30.27	3	3	09.01.27	47777.C-2845, 47777.C-2844, 47777.C-2846	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 4A Wall, Corner Guards & Bumpers	47777.C-2816		NoRWP	a910.1	47777.C-2815	09.01.27	2	2	09.02.27	47777.C-2819	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 4A Misc Toilet & Bath Accessories, Fire Ext'grs, Misc	47777.C-2817		NoRWP	a910.1	47777.C-2815	09.01.27	2	2	09.02.27	47777.C-2819	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 4A Finish Paint	47777.C-2818		NoRWP	a910.1	47777.C-2815	09.01.27	2	2	09.02.27	47777.C-2819	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 5A Wall, Corner Guards & Bumpers	47777.C-2844		NoRWP	n/a	47777.C-2843	09.02.27	2	2	09.03.27	47777.C-2847	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 5A Misc Toilet & Bath Accessories, Fire Ext'grs, Misc	47777.C-2845		NoRWP	n/a	47777.C-2843	09.02.27	2	2	09.03.27	47777.C-2847	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 5A Finish Paint	47777.C-2846		NoRWP	n/a	47777.C-2843	09.02.27	2	2	09.03.27	47777.C-2847	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 - 4A Clean & Punchlist - Ready for Agency Review & Approval	47777.C-2819		NoRWP	notes	47777.C-2816, 47777.C-2817, 47777.C-2818	09.03.27	2	2	09.07.27	47777.C-2820, 47777.C-2821	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 - 5A Clean & Punchlist - Ready for Agency Review & Approval	47777.C-2847		NoRWP	n/a	47777.C-2844, 47777.C-2845, 47777.C-2846	09.07.27	2	2	09.08.27	47777.C-2848, 47777.C-2849	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 Floor 4A - Install Owner Furnished- Contractor Installed Items	47777.C-2820		NoRWP	NA	47777.C-2819	09.08.27	1	2	09.08.27	47777.C-2822, 47777.C-2823, 47777.C-2822	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	8
C47777 Floor 4A-Final Furnishing, Owner Suppied Items, Misc	47777.C-2821		NoRWP	N/A	47777.C-2819	09.08.27	2	2	09.09.27	47777.C-2822	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 Floor 5A - Install Owner Furnished- Contractor Installed Items	47777.C-2848		NoRWP	NA	47777.C-2847	09.09.27	1	2	09.09.27	47777.C-2851, 47777.C-2850, 47777.C-2850	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	7
C47777 Floor 5A-Final Furnishing, Owner Suppied Items, Misc	47777.C-2849		NoRWP	N/A	47777.C-2847	09.09.27	2	2	09.10.27	47777.C-2850	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Tom.Zimmermann.F - Tom Zimmermann	6
C47777 Floor 4A - OGS/OMH FINAL INSP'Ns, FF & CLINICAL CLEANING (25wd)	47777.C-2822		NoRWP	N/A	47777.C-2820, 47777.C-2821, 47777.C-2820	09.10.27	25	0	10.14.27	47777.C-2823	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Justin.Otto.A1.R3.E - J Otto	7
C47777 Floor 5A - OGS/OMH FINAL INSP'Ns, FF & CLINICAL CLEANING (25wd)	47777.C-2850		NoRWP	N/A	47777.C-2848, 47777.C-2848, 47777.C-2849	09.13.27	25	0	10.15.27	47777.C-2851	!05MGF08D.H	Resource Dependei			R1B5.47777.C	1	Justin.Otto.A1.R3.E - J Otto	6

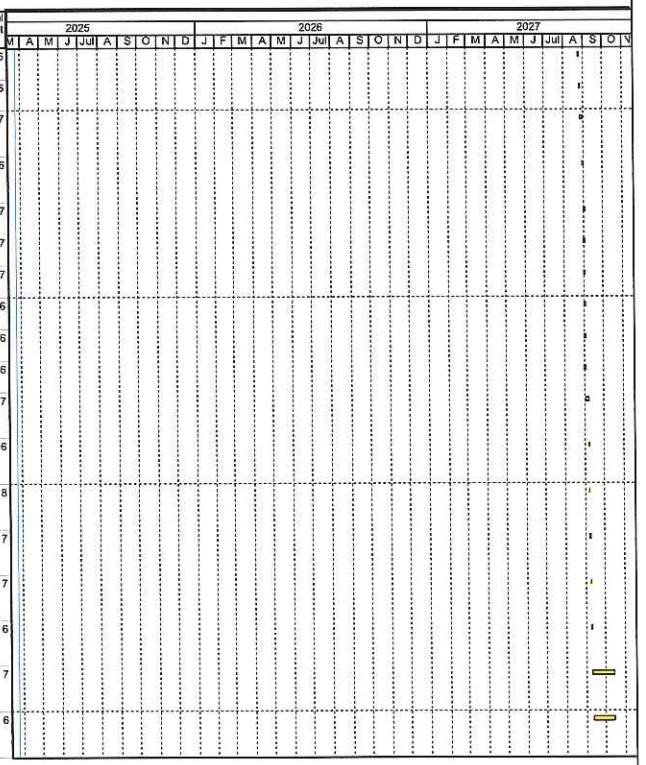

BL Baseline (Working) | RWP Roofing | RWP Heating | RWP Paving | RWP Grubbing | RWP HVAC
BL Milestone | RWP PhyWork | RWP WtrProofing | RWP UGConduit | RWP Seeding | RWP Stucco

- Filters: TASK filter: Excl WBS Summary Only.
- Data Date: 03.24.25
- Baseline:

Department of Taxation and Finance

New York State and Local Sales and Use Tax

Contractor Exempt Purchase Certificate

ST-120.1
(5/16)

To be used **only** by contractors who are registered with the Tax Department for sales tax purposes.

To vendors:
You must collect tax on any sale of taxable property or services unless the contractor gives you a properly completed exempt purchase certificate not later than 90 days after the property is sold or service is rendered. In addition, you must keep the certificate for at least three years, as explained in the instructions.

This form cannot be used to purchase motor fuel or diesel motor fuel exempt from tax.

To contractors and vendors: Read the instructions on pages 3 and 4 carefully before completing or accepting this certificate.

Name of seller			Name of purchasing contractor		
Elli NY Design Corp.			Prismatic Development Corporation		
Street address			Street address		
50-01 Metropolitan Avenue			60 US Highway 46		
City	State	ZIP code	City	State	ZIP code
Ridgewood	NY	11385	Fairfield	NJ	07004

1. I have been issued a New York State *Certificate of Authority*, 22-2433095 *(enter your sales tax identification number)*, to collect New York State and local sales and use tax, and that certificate has not expired or been suspended or revoked.

2. The tangible personal property or service being purchased will be used on the following project:

   Inpatient Bed Expansion Renovations, Creedmoor Psychiatric Center

   located at 80-45 Winchester Blvd., Queens Village, NY

   for and with State of NY, Office of General Services, Design & Construction

   pursuant to prime contract dated 03-24-2025.

3. These purchases are exempt from sales and use tax because:
   *(Mark an **X** in the appropriate box; for further explanation, see items A through P in the instructions on pages 3 and 4.)*

☒ **A.** The tangible personal property will be used in the above project to create a building or structure or to improve real property or to maintain, service, or repair a building, structure, or real property, owned by an organization exempt under Tax Law section 1116(a). (*For example, New York State government entities, United States governmental entities, United Nations and any international organization of which the United States is a member, certain posts or organizations of past or present members of the armed forces, and certain nonprofit organizations and Indian nations or tribes that have received New York State sales tax exempt organization status.)* The tangible personal property will become an integral component part of such building, structure, or real property.

☐ **B.** The tangible personal property is production machinery and equipment, and it will be incorporated into real property.

☐ **C.** The tangible personal property will be used:
- in an Internet data center when the property is to be incorporated as part of a capital improvement; or
- directly and predominantly in connection with telecommunications services for sale or Internet access services for sale; or
- directly and predominantly by a television or radio broadcaster in connection with producing or transmitting live or recorded programs.

☐ **D.** The tangible personal property, including production machinery and equipment, is for installation in the above project and will remain tangible personal property after installation.

☐ **E.** The tangible personal property will become an integral component part of a building, structure, or real property, used predominantly (more than 50%) either in the production phase of farming or in a commercial horse boarding operation, or in both.

Note: This certificate is not valid unless the purchaser completes the certification on page 2.

CH

☐ **F.** The machinery or equipment will be used directly and predominantly to control, prevent, or abate pollution or contaminants from manufacturing or industrial facilities.

☐ **G.** The tangible personal property is residential or commercial solar energy systems equipment. (**Note:** Item G purchases are exempt from the 4% New York State tax rate and from the 3/8% MCTD rate. Item G purchases may be exempt from local taxes. See instructions.)

☐ **H.** The tangible personal property will be used directly and exclusively in adding to, altering, or improving a qualifying tenant's leased premises for use as commercial office space in Eligible Area A or B as described in TSB-M-05(12)S, *Sales and Use Tax Exemptions on Certain Purchases of Tangible Personal Property and Services for Leased Commercial Office Space in Lower Manhattan*, provided that the tangible personal property becomes an integral component part of the building in which the leased premises are located, and where such property is purchased during the first year of the qualifying tenant's lease and delivered to the leased premises no later than 90 days after the end of that first year.

☐ **I.** The tangible personal property is machinery or equipment used directly and predominantly in loading, unloading, and handling cargo at a qualified marine terminal facility in New York City. This exemption does **not** apply to the local tax in New York City.

☐ **J.** The tangible personal property is commercial fuel cell systems equipment. (**Note:** Item J purchases are exempt from the 4% New York State tax rate and from the 3/8% MCTD rate. Item J purchases may be exempt from local taxes. See instructions.)

☒ **K.** The services are for the project described in line 2 on page 1 and will be resold. (This includes trash removal services in connection with repair services to real property.)

☐ **L.** The services are to install, maintain, service, or repair tangible personal property used in an Internet data center, for telecommunication or Internet access services, or for radio or television broadcast production or transmission.

☐ **M.** The services are to install, maintain, service, or repair tangible personal property that will be used predominantly either in farm production or in a commercial horse boarding operation, or in both provided such tangible personal property will become an integral component part of such structure, building, or real property.

☐ **N.** The services are to install residential or commercial solar energy systems equipment.

☐ **O.** The services are to install tangible personal property purchased during the first year of the qualifying tenant's lease and delivered to the leased premises no later than 90 days after the end of that first year, that will be used directly and exclusively in adding to, altering, or improving a qualifying tenant's leased premises for use as commercial office space in Eligible Area A or B as described in TSB-M-05(12)S.

☐ **P.** The services are to install or maintain commercial fuel cell systems equipment.

Caution: Contractors may **not** use this certificate to purchase services tax exempt unless the services are resold to customers in connection with a project. Construction equipment, tools, and supplies purchased or rented for use in completing a project but that do not become part of the finished project may not be purchased exempt from tax through the use of this certificate.

Certification: I certify that the above statements are true, complete, and correct, and that no material information has been omitted. I make these statements and issue this exemption certificate with the knowledge that this document provides evidence that state and local sales or use taxes do not apply to a transaction or transactions for which I tendered this document and that willfully issuing this document with the intent to evade any such tax may constitute a felony or other crime under New York State Law, punishable by a substantial fine and a possible jail sentence. I understand that this document is required to be filed with, and delivered to, the vendor as agent for the Tax Department for the purposes of Tax Law section 1838 and is deemed a document required to be filed with the Tax Department for the purpose of prosecution of offenses. I also understand that the Tax Department is authorized to investigate the validity of tax exclusions or exemptions claimed and the accuracy of any information entered on this document.

Type or print name and title of owner, partner, or authorized person of purchasing contractor	
Michael Diekhaus, CFO	
Signature of owner, partner, or authorized person of purchasing contractor Michael Diekhaus	Date prepared 8/13/25

Substantial penalties will result from misuse of this certificate.

CH

Instructions

Only a contractor who has a valid *Certificate of Authority* issued by the Tax Department may use this exempt purchase certificate. The contractor must present a properly completed certificate to the vendor to purchase tangible personal property, or to a subcontractor to purchase services tax exempt. This certificate is not valid unless all entries have been completed.

The contractor may use this certificate to claim an exemption from sales or use tax on tangible personal property or services that will be used in the manner specified in items A through Q below. The contractor may not use this certificate to purchase tangible personal property or services tax exempt on the basis that Form ST-124, *Certificate of Capital Improvement*, has been furnished by the project owner to the contractor.

The contractor must use a separate Form ST-120.1, *Contractor Exempt Purchase Certificate*, for each project.

Purchase orders showing an exemption from the sales or use tax based on this certificate must contain the address of the project where the property will be used, as well as the name and address of the project owners (see page 1 of this form). Invoices and sales or delivery slips must also contain this information (name and address of the project for which the exempt purchases will be used or where the exempt services will be rendered, as shown on page 1 of this form).

Use of the certificate

Note: Unless otherwise stated, the customer must furnish the contractor a properly completed Form ST-121, *Exempt Use Certificate*.

This certificate may be used by a contractor to claim exemption from tax only on purchases of **tangible personal property** that is:

A. Incorporated into real property under the terms of a contract entered into with an exempt organization that has furnished the contractor with a copy of Form ST-119.1, *Exempt Organization Exempt Purchase Certificate,* governmental purchase order, or voucher.

B. Production machinery or equipment that will be incorporated into real property.

C. Used in one of the following situations:

- Machinery, equipment, and other tangible personal property related to providing website services for sale to be installed in an Internet data center when the property is to be incorporated as part of a capital improvement. The customer must furnish the contractor a completed Form ST-121.5, *Exempt Use Certificate for Operators of Internet Data Centers (Web Hosting)*.
- Used directly and predominantly in the receiving, initiating, amplifying, processing, transmitting, re-transmitting, switching, or monitoring of switching of telecommunications services for sale, or Internet access service for sale.
- Machinery, equipment, and other tangible personal property (including parts, tools, and supplies) used by a television or radio broadcaster directly and predominantly in the production and post-production of live or recorded programs used by a broadcaster predominantly for broadcasting by the broadcaster either over-the-air or for transmission through a cable television or direct broadcast satellite system. (Examples of exempt machinery and equipment include cameras, lights, sets, costumes, and sound equipment.) This exemption also includes machinery, equipment, and other tangible personal property used by a broadcaster directly and predominantly to transmit live or recorded programs. (Examples of exempt machinery and equipment include amplifiers, transmitters, and antennas.)

D. Installed or placed in the project in such a way that it remains tangible personal property after installation. The contractor must collect tax from its customer when selling such tangible personal property or related services to the customer, unless the customer gives the contractor an appropriate and properly completed exemption certificate.

E. Going to become an integral component part of a structure, building, or real property used predominantly (more than 50%) either in the production phase of farming or in a commercial horse boarding operation, or in both, for which the customer has provided the contractor a completed Form ST-125, *Farmer's and Commercial Horse Boarding Operator's Exemption Certificate.*

F. Machinery or equipment used directly and predominantly to control, prevent, or abate pollution or contaminants from manufacturing or industrial facilities.

G. Residential or commercial solar energy systems equipment. *Residential solar energy systems equipment* means an arrangement or combination of components installed in a residence that utilizes solar radiation to produce energy designed to provide heating, cooling, hot water, and/or electricity. *Commercial solar energy systems equipment* means an arrangement or combination of components installed upon nonresidential premises that utilize solar radiation to produce energy designed to provide heating, cooling, hot water, or electricity. The exemption is allowed on the 4% New York State tax rate and where applicable, the ¾% MCTD rate. The exemption does not apply to local taxes unless the locality specifically enacts the exemption. The customer must furnish the contractor a completed Form ST-121 by completing the box marked *Other* (U.). For the definition of *residence* and for an exception relating to recreational equipment used for storage, as well as for other pertinent information, see TSB-M-05(11)S, *Sales and Use Tax Exemption for Residential Solar Energy Systems Equipment.* For the definition of *nonresidential premises*, as well as other pertinent information, see TSB-M-12(14)S, *Sales and Use Tax Exemption for the Sales and Installation of Commercial Solar Energy Systems Equipment.*

H. Delivered and used directly and exclusively in adding to, altering, or improving a qualifying tenant's leased premises for use as commercial office space in Eligible Area A or B as described in TSB-M-05(12)S, *Sales and Use Tax Exemptions on Certain Purchases of Tangible Personal Property and Services for Leased Commercial Office Space in Lower Manhattan*, provided that the tangible personal property becomes an integral component part of the building in which the leased premises are located, and where such property is purchased within the first year of the qualifying tenant's lease.

I. Machinery and equipment used at qualified marine terminal facilities located in New York City. The machinery and equipment must be used directly and predominantly in loading, unloading, and handling cargo at marine terminal facilities located in New York City that handled more than 350,000 twenty foot equivalent units (TEUs) in 2003. For purposes of this exemption, the term *TEU* means a unit of volume equivalent to the volume of a twenty-foot container. This exemption does **not** apply to the local tax in New York City.

J. Commercial fuel cell systems equipment. *Commercial fuel cell systems equipment* means an electric generating arrangement or combination of components that is installed upon nonresidential premises and utilizes solid oxide, molten carbonate, a proton exchange membrane, phosphoric acid, or a linear generator to provide heating, cooling, hot water, or electricity. The exemption is allowed on the 4% New York State tax rate and the ⅜% MCTD rate, if applicable. The exemption does not apply to local taxes unless the locality specifically enacts the exemption. The customer must furnish the contractor a completed Form ST-121 by completing the box marked *Other* (U.). See TSB-M-16(3)S, *Sales and Use Tax Exemptions Related to Commercial Fuel Cell Systems Equipment,* for more information.

K. For use in a project for an exempt HDFC that has furnished the contractor with a copy of the exemption letter issued to them by the Tax Department.

This certificate may also be used by a contractor to claim exemption from tax on the following **services**:

L. Installing tangible personal property, including production machinery and equipment, that does not become a part of the real property upon installation.

Repairing real property, when the services are for the project named on page 1 of this form and will be resold.

Trash removal services rendered in connection with repair services to real property, if the trash removal services will be resold.

Note: Purchases of services for resale can occur between prime contractors and subcontractors or between two subcontractors. The retail seller of the services, generally the prime contractor, must charge and collect tax on the contract price, unless the project owner gives the retail seller of the service a properly completed exemption certificate.

M. Installing, maintaining, servicing, or repairing tangible personal property used for Web hosting, telecommunication or Internet access services, or by a broadcaster (described in item C on page 3).

N. Installing, maintaining, servicing, or repairing tangible personal property that will be used predominantly either in farm production or in a commercial horse boarding operation, or in both (described in item E on page 3).

O. Installing qualifying residential or commercial solar energy systems equipment (described in item G on page 3).

P. Installing tangible personal property delivered to and used directly and exclusively in adding to, altering, or improving a qualifying tenant's leased premises for use as commercial office space in Eligible Area A or B as described in TSB-M-05(12)S, provided that the tangible personal property becomes an integral component part of the building in which the leased premises are located.

Q. Installing or maintaining commercial fuel cell systems equipment (described in item J above).

Misuse of this certificate

Misuse of this exemption certificate may subject you to serious civil and criminal sanctions in addition to the payment of any tax and interest due. These include:

- a penalty equal to 100% of the tax due;
- a $50 penalty for each fraudulent exemption certificate issued;
- criminal felony prosecution, punishable by a substantial fine and a possible jail sentence; and
- revocation of your *Certificate of Authority*, if you are required to be registered as a vendor. See TSB-M-09(17)S, *Amendments that Encourage Compliance with the Tax Law and Enhance the Tax Department's Enforcement Ability*, for more information.

To the seller

When making purchases that qualify for exemption from sales and use tax, the contractor must provide you with this exemption certificate with all entries completed to establish the right to the exemption.

As a New York State registered vendor, you may accept an exemption certificate in lieu of collecting tax and be protected from liability for the tax if the certificate is valid. The certificate will be considered valid if it is:

- accepted in good faith;
- in your possession within 90 days of the transaction; and
- properly completed (all required entries were made).

An exemption certificate is accepted in good faith when you have no knowledge that the exemption certificate is false or is fraudulently given, and you exercise reasonable ordinary due care. If you do not receive a properly completed certificate within 90 days after the delivery of the property or service, you will share with the purchaser the burden of proving the sale was exempt.

Failure to collect sales or use tax, as a result of accepting an improperly completed exemption certificate or receiving the certificate more than 90 days after the sale, will make you personally liable for the tax plus any penalty and interest charges due.

You must maintain a method of associating an invoice (or other source document) for an exempt sale with the exemption certificate you have on file from the purchaser. You must also keep this certificate at least three years after the due date of your sales tax return to which it relates, or the date the return was filed, if later.

Need help?



Visit our website at ***www.tax.ny.gov***

- get information and manage your taxes online
- check for new online services and features

Telephone assistance:	518-485-9863
To order forms and publications:	518-457-5431
Text Telephone (TTY) or TDD equipment users	Dial 7-1-1 for the New York Relay Service

Q1

Form **W-9**
(Rev. March 2024)
Department of the Treasury
Internal Revenue Service

Request for Taxpayer Identification Number and Certification

Go to *www.irs.gov/FormW9* for instructions and the latest information.

Give form to the requester. Do not send to the IRS.

Before you begin. For guidance related to the purpose of Form W-9, see *Purpose of Form*, below.

Print or type. See ***Specific Instructions*** on page 3.

1 Name of entity/individual. An entry is required. (For a sole proprietor or disregarded entity, enter the owner's name on line 1, and enter the business/disregarded entity's name on line 2.)

Elli NY Design Corp.

2 Business name/disregarded entity name, if different from above.

3a Check the appropriate box for federal tax classification of the entity/individual whose name is entered on line 1. Check only **one** of the following seven boxes.

☐ Individual/sole proprietor ☐ C corporation ☑ S corporation ☐ Partnership ☐ Trust/estate

☐ LLC. Enter the tax classification (C = C corporation, S = S corporation, P = Partnership) . . . .

Note: Check the "LLC" box above and, in the entry space, enter the appropriate code (C, S, or P) for the tax classification of the LLC, unless it is a disregarded entity. A disregarded entity should instead check the appropriate box for the tax classification of its owner.

☐ Other (see instructions)

4 Exemptions (codes apply only to certain entities, not individuals; see instructions on page 3):

Exempt payee code (if any)

Exemption from Foreign Account Tax Compliance Act (FATCA) reporting code (if any)

(Applies to accounts maintained outside the United States.)

3b If on line 3a you checked "Partnership" or "Trust/estate," or checked "LLC" and entered "P" as its tax classification, and you are providing this form to a partnership, trust, or estate in which you have an ownership interest, check this box if you have any foreign partners, owners, or beneficiaries. See instructions . . . . . ☐

5 Address (number, street, and apt. or suite no.). See instructions.

50-01 Metropolitan Ave

6 City, state, and ZIP code

Ridgewood, NY 11385

Requester's name and address (optional)

7 List account number(s) here (optional)

Part I Taxpayer Identification Number (TIN)

Enter your TIN in the appropriate box. The TIN provided must match the name given on line 1 to avoid backup withholding. For individuals, this is generally your social security number (SSN). However, for a resident alien, sole proprietor, or disregarded entity, see the instructions for Part I, later. For other entities, it is your employer identification number (EIN). If you do not have a number, see *How to get a TIN*, later.

Note: If the account is in more than one name, see the instructions for line 1. See also *What Name and Number To Give the Requester* for guidelines on whose number to enter.

Social security number

			–			–				

or

Employer identification number

1	3	–	3	6	1	7	1	6	9

Part II Certification

Under penalties of perjury, I certify that:

1. The number shown on this form is my correct taxpayer identification number (or I am waiting for a number to be issued to me); and
2. I am not subject to backup withholding because (a) I am exempt from backup withholding, or (b) I have not been notified by the Internal Revenue Service (IRS) that I am subject to backup withholding as a result of a failure to report all interest or dividends, or (c) the IRS has notified me that I am no longer subject to backup withholding; and
3. I am a U.S. citizen or other U.S. person (defined below); and
4. The FATCA code(s) entered on this form (if any) indicating that I am exempt from FATCA reporting is correct.

Certification instructions. You must cross out item 2 above if you have been notified by the IRS that you are currently subject to backup withholding because you have failed to report all interest and dividends on your tax return. For real estate transactions, item 2 does not apply. For mortgage interest paid, acquisition or abandonment of secured property, cancellation of debt, contributions to an individual retirement arrangement (IRA), and, generally, payments other than interest and dividends, you are not required to sign the certification, but you must provide your correct TIN. See the instructions for Part II, later.

Sign Here | **Signature of U.S. person** [signature] **Date** 4/30/2025

General Instructions

Section references are to the Internal Revenue Code unless otherwise noted.

Future developments. For the latest information about developments related to Form W-9 and its instructions, such as legislation enacted after they were published, go to *www.irs.gov/FormW9*.

What's New

Line 3a has been modified to clarify how a disregarded entity completes this line. An LLC that is a disregarded entity should check the appropriate box for the tax classification of its owner. Otherwise, it should check the "LLC" box and enter its appropriate tax classification.

New line 3b has been added to this form. A flow-through entity is required to complete this line to indicate that it has direct or indirect foreign partners, owners, or beneficiaries when it provides the Form W-9 to another flow-through entity in which it has an ownership interest. This change is intended to provide a flow-through entity with information regarding the status of its indirect foreign partners, owners, or beneficiaries, so that it can satisfy any applicable reporting requirements. For example, a partnership that has any indirect foreign partners may be required to complete Schedules K-2 and K-3. See the Partnership Instructions for Schedules K-2 and K-3 (Form 1065).

Purpose of Form

An individual or entity (Form W-9 requester) who is required to file an information return with the IRS is giving you this form because they
